

## Project Overview Report October 31, 2010

A total of 195 projects are currently in the MSBA's grant program. The following summary table provides the category (e.g., New Program, etc.) and the number of projects in each phase (e.g., Local Clearance, etc.):

	<b>Total</b>	<b>Local Clearance</b>	<b>Feasibility Study/ Schematic Design</b>	<b>Design Development</b>	<b>Construction</b>
<b>New Program</b>	121	34	46	18	25
<b>Waitlist</b>	13		2		11
<b>Green Repair</b>	39	9	14	13	1
<b>Closeout/Audit Complete</b>	22				
<b>Total</b>	195	43	62	31	37

The MSBA utilizes the Capital Pipeline Status chart to account for the ongoing status of all Districts in the pipeline. Activity for some of the key milestone activities are summarized in the table below with the numbers reported indicative of the category requirements. (For instance, enrollment certifications are not required for all projects, e.g., repairs, and Owner's Project Managers are not required for construction projects under \$1.5 million unless required by the MSBA.)

### Critical Prerequisites:

An agreed upon enrollment is a key prerequisite for the MSBA to commence a Feasibility Study with a District. In order to begin the enrollment projection process, a District must file enrollment information utilizing the MSBA's online enrollment projection.

After the MSBA and the District have agreed upon an enrollment to be used as the design basis and executed a Feasibility Study Agreement, the District procures consultants, starting with Owner's Project Manager. Currently, there are 40 Districts in the Capital Pipeline who still need to procure an Owner's Project Manager.

After a District has selected an Owner's Project Manager and executed a contract with that Owner's Project Manager, it is ready for the selection of a Designer utilizing either a local designer selection process for projects under \$5 million or the MSBA's Designer Selection Panel for those projects over \$5 million. Currently, there are 83 Districts in the Capital Pipeline who still need to procure a Designer.

	<b>District Action to complete</b>	<b>MSBA/ District Collaboration</b>	<b>Completed Activity this Period</b>	<b>Total Completed to Date</b>	<b>Total</b>
Enrollment	17	29	9	93	73,787 students
Owner's Project Manager	40	10	4	103	Over \$65 million in OPM fees
Designer	83	5	5	118	Over \$160 million in Designer Fees

## Owner's Project Managers

Since the September Board of Directors Meeting, the following Districts have completed the OPM selection process:

- Norton (High School)
- Peabody (Repair)
- Saugus (Repair)
- Williamsburg (Elementary School)

The schedule for the next OPM Review Panel meeting is shown below with the potential of 3 Districts submitting for review and approval.

Panel Date	District/School	Project Description Status	Estimated Project Cost
12/6/10	W. Springfield	Model School	\$50-\$85mil
12/6/10	Wilmington	Feasibility Study	\$65-\$75mil
12/6/10	Pittsfield	Feasibility Study	\$80-\$200mil

## Designers

Since the September Board of Directors meeting, the DSP has met twice resulting in 2 additional Districts completing the Designer selection process.

Panel Date	District/School	Status	Estimated Project Cost	# of Proposals Received	Top 3-Ranked Firms	Interviews Requested	First-Ranked Selection
10/5/10	So. Worcester Cnty Reg. Voc. PS – Bay Path RVTHS	Designer Selection	\$10m - \$40m	7	- Fletcher Thompson - HMFH Architects - Kaestle Boos	Yes	Kaestle Boos
10/5/10	Weston – Field School	Designer Selection	\$28m - \$32m	11	- Dore & Whittier - Flansburgh - Jonathan Levi Architects	Yes	TBD
10/19/10	Brookline – Heath School	Designer Selection	\$5m - \$6m	9	- Arrowstreet - Kaestle Boos - Maryann Thompson - Miller Dyer Spears	Yes	TBD
10/19/10	Springfield – Forest Park MS	Designer Selection	\$30m - \$33m	15	- Perkins Eastman - DRA - SMMA	Yes	TBD
10/19/10	Essex North Shore Agr. & Tech Sch.	Design Development	\$125m	3	- Design Part. /Cambridge - Fletcher Thompson - Mount Vernon Group	No	Design Part. /Cambridge

The following Districts are tentatively scheduled for upcoming DSP meetings:

- Weston – Field School – November 2 (interviews)
- Brookline – Heath School – November 2 (interviews)
- Springfield – Forest Park MS– November 16 (interviews)
- Lincoln – Lincoln School – December 7
- Norton – Norton High School – December 7
- Boston – Quincy Upper - TBD

## Commissioning

Since the September Board of Directors meeting, the MSBA has assigned Commissioning Consultants to an additional 4 projects as presented in the table below. The MSBA has executed 43 Commissioning Consultant contracts to date, totaling \$5.4 Million.

District	School	Estimated Const. Cost (millions)	Commissioning Consultant	Contract Amount
Ashland PS	David Mindess IS	\$1.90	Cannon Design	\$24,900
Rockport PS	Rockport HS	\$0.87	VP Consultants, LLC	\$21,000
Whittier Voc PS	Whittier Reg Voc HS	\$1.42	Cannon Design	\$36,200
Quabbin PS	Oakham Center ES	\$0.77	VP Consultants, LLC	\$18,500
<b>Total</b>		<b>\$4.96</b>	<b>Total</b>	<b>\$100,600</b>

Projects for which we are currently seeking proposals and/or negotiating Work Orders include:

District	School	Responses Due
North Attleborough PS	Joseph W Martin Jr ES	8/23/2010
Dartmouth PS	James M. Quinn ES	8/23/2010
Uxbridge PS	Uxbridge HS	9/17/2010
Marshfield PS	Gov Edward Winslow ES	11/4/2010

Projects that are currently in the queue for assignment of a Commissioning Consultant and for which contract documents are being drafted include:

District	School
Burlington PS	Marshall Simonds MS
Adams-Cheshire PS	Adams MS
Granby PS	Granby JHS / SHS
Maynard PS	Maynard HS
Norfolk County Agr PS	Norfolk County Agr HS
Somerville PS	E Somerville Community K-8
Essex N. Shore Agr Tech PS	Essex N. Shore Agr and Tech Institute
South Shore Reg Voc PS	South Shore Voc / Tech HS

Attached to the Project Status report are the following:

- Master District Status List
- SOI Status - Capital Pipeline: As indicated in the attached chart, Districts continue to make progress with their projects. The narrow solid bar indicates the number of Districts in each category as reported at the September Board meeting.
- Estimated Bid Schedule.
- Construction Status Report



# Massachusetts School Building Authority

No. of Projects: 213

## Master District Status List

Yellow = Wait List Project
Green = Green Repair
Red = Changes in last 60 days

District Name	School Name	Status	Preferred Schematic	OPM	Designer	Cx Authority	Procurement Status	CM/GC
Abington PS	Frolio JHS	Local Clearance - 07/08						
Acton PS	Douglas ES	Design Development	Repair	N/A	CBI Consulting Inc.			
Adams-Cheshire PS	Adams MS	Design Development	Addition/Renovation	URS Corporation	Tessier Associates		Undetermined	
Amherst-Pelham PS	Amherst Reg MS	Local Clearance						
Andover PS	Bancroft ES	Project Scope & Budget	New Construction	Town of Andover	Symmes Maini & McKee Associates			
Arlington PS	Thompson ES	Feasibility Study		PMA Consultants	HMFH Architects, Inc.			
Ashburnham-West PS	Briggs ES	Project Scope & Budget	New Construction	STV, Inc.	Lamoureux Pagano & Associates, Inc.			
Ashland PS	David Mindess IS	Closeout/Audit	Repair	Heery International, Inc	Gale Associates, Inc.	Cannon Design	DBB - Contract Awarded	Greenwood Industries
Assabet Valley PS	Assabet Valley Voc HS	Feasibility Study	Repair	Strategic Building Solutions, LLC	Design Partnership of Cambridge, Inc.			
Athol-Royalston PS	Riverbend ES	Local Clearance - Repair - 09						
Attleboro PS	A. Irvin Studley ES	Approved Project Vote Pending	Repair	Skanska USA Building, Inc.	Russo Barr Associates, Inc.			
Attleboro PS	Hill-Roberts ES	Approved Project Vote Pending	Repair	Skanska USA Building, Inc.	Russo Barr Associates, Inc.			
Attleboro PS	Hyman Fine ES	Approved Project Vote Pending	Repair	Skanska USA Building, Inc.	Russo Barr Associates, Inc.			
Attleboro PS	Attleboro HS	Approved Project Vote Pending	Repair	Skanska USA Building, Inc.	Russo Barr Associates, Inc.			
Auburn PS	Auburn MS	Local Clearance - 07/08						
Avon PS	Ralph D Butler ES	Closeout/Audit	Repair		Richard D. Kimball Company, Inc.		DBB - Contract Awarded	Automaitic Temperature Controls Inc.
Ayer PS	Ayer HS	Local Clearance - 09/10						
Bedford PS	Bedford HS	Closeout/Audit	Renovation	Peter Cox	Symmes Maini & McKee Associates		DBB - Contract Awarded	Brait Builders Construction
Bellingham PS	Bellingham Memorial MS	Local Clearance						
Belmont PS	Roger E Wellington ES	Construction	New Construction	PMA Consultants	Jonathan Levi Architects LLC	Strategic Building Solutions	CMR - CM Selected	Skanska USA Building, Inc.
Berlin-Boylston PS	Tahanto Reg HS	Design Development	New Construction	PMA Consultants	HMFH Architects, Inc.	Strategic Building Solutions		
Beverly PS	Beverly HS	Construction	Addition/Renovation	Heery International	Mount Vernon Group Architects, Inc.		DBB - Contract Awarded	CTA Construction Co.
Billerica PS	Parker ES	Construction	New Construction	Joslin, Lesser & Associates, Inc.	Symmes Maini & McKee Associates	Sebesta Blomberg & Associates	Undetermined	

# Master District Status List

Yellow = Wait List Project	
Green = Green Repair	Red = Changes in last 60 days

District Name	School Name	Status	Preferred Schematic	OPM	Designer	Cx Authority	Procurement Status	CM/GC
Billerica PS	Billerica Memorial HS	Local Clearance						
Boston PS	Dearborn MS	Local Clearance - 09/10						
Boston PS	Quincy Upper School	Designer Selection		City of Boston				
Boxford PS	Harry Lee Cole Primary	Local Clearance						
Braintree PS	Highlands	Project Scope & Budget	Repair					
Braintree PS	South MS	Closeout/Audit	Repair	Town Employee	Habeeb & Associates Architects, Inc.		DBB - Contract Awarded	Construction Dynamics
Braintree PS	Hollis ES	Project Scope & Budget	Repair					
Braintree PS	Archie T Morrison ES	Project Scope & Budget	Repair					
Braintree PS	Braintree HS	Project Scope & Budget	Repair					
Braintree PS	East MS	Project Scope & Budget	Repair					
Brookfield PS	Brookfield ES	Local Clearance						
Brookline PS	John D Runkle K-8	Construction	Addition/Renovation	Town of Brookline Building Department	Design Partnership of Cambridge, Inc.	Consulting Engineering Services, LLC	DBB - In Design	
Brookline PS	Heath K-8	Feasibility Study	Addition/Renovation	Town of Brookline Building Department	Miller Dyer Spears Inc.			
Burlington PS	Marshall Simonds MS	Design Development	Addition/Renovation	Construction Monitoring Services, Inc.	Knight, Bagge & Anderson, Inc.			
Burlington PS	Memorial ES	Construction	New Construction	Construction Monitoring Services, Inc.	Knight, Bagge & Anderson, Inc.	Consulting Engineering Services, LLC	DBB - Contract Awarded	CTA Construction Co. Inc.
Cape Cod Region Voc Tech PS	Cape Cod Regional Voc / Tech HS	Local Clearance	Repair					
Carlisle PS	Carlisle K-8	Design Development	Addition/Renovation	Daedalus Projects, Inc.	HMFH Architects, Inc.	Horizon Engineering Associates, LLP	DBB - In Design	
Chelmsford PS	McCarthy MS	Closeout/Audit					DBB - Contract Awarded	Multiple
Chelsea PS	Clark Avenue MS	Local Clearance - 07/08			Jacobs			
Chicopee PS	Chicopee Academy	Local Clearance - 09/10						
Concord-Carlisle PS	Concord Carlisle HS	Local Clearance - Repair - 09						
Conway PS	Conway Grammar ES	Design Development	Repair		Richardson Gorman Architects			
Danvers PS	Danvers HS	Construction	Addition/Renovation	Construction Monitoring Services, Inc.	DiNisco Design Partnership, Limited	Turner Facilities Management Solutions	DBB - In Design	Bacon Construction Co., Inc.
Dartmouth PS	James M. Quinn ES	Closeout/Audit	Repair		Russo Barr Associates, Inc.			
Dedham PS	Avery ES	Construction	New Construction	Construction Monitoring Services, Inc.	Dore & Whittier Architects, Inc.	WSP Flack + Kurtz	CMR - CM Selected	Consigli Construction Co
Dennis-Yarmouth PS	Ezra H Baker ES	OPM Selection	Repair					

# Master District Status List

Yellow = Wait List Project	
Green = Green Repair	Red = Changes in last 60 days

District Name	School Name	Status	Preferred Schematic	OPM	Designer	Cx Authority	Procurement Status	CM/GC
Douglas PS	Douglas IS	Preferred Schematic		Heery International, Inc	DiNisco Design Partnership, Limited			
Dracut PS	Dracut SHS	Preferred Schematic	Addition/Renovation	RF Walsh Collaborative Partners	Mount Vernon Group Architects, Inc.		Undetermined	
Duxbury PS	Chandler ES	Closeout/Audit	Repair	N/A	Gale Associates, Inc.		DBB - Contract Awarded	Built-up Roofing Systems LLC
Duxbury PS	Duxbury HS	Local Clearance - 09/10						
East Bridgewater PS	East Bridgewater HS	Preferred Schematic	Model School	RF Walsh Collaborative Partners - pending	Ai3 Architects LLC			
Essex North Shore Agr and Tech PS	Essex North Shore Agr and Tech School	Design Development	New Construction	PMA Consultants	Design Partnership of Cambridge, Inc.			
Fairhaven PS	Rogers ES	Feasibility Study		Daedalus Projects Inc	HMFH Architects, Inc.			
Fall River PS	Morton MS	OPM Selection						
Falmouth PS	Falmouth High School	Construction	Addition/Renovation	Gilbane Building Company	DiNisco Design Partnership, Limited		DBB - Contract Awarded	TLT Construction
Fitchburg PS	Goodrich K Center	Design Development	Repair	Compass Project Management, Inc.	BLW Engineers, Inc.			
Fitchburg PS	South Street ES	Design Development	Repair	Compass Project Management, Inc.	BLW Engineers, Inc.			
Fitchburg PS	Reingold ES	Design Development	Repair	Compass Project Management, Inc.	BLW Engineers, Inc.			
Fitchburg PS	Crocker ES	Local Clearance - 07/08						
Fitchburg PS	Memorial IS	Design Development	Repair	Compass Project Management, Inc.	BLW Engineers, Inc.			
Florida PS	Abbott Memorial K-8	Building Completion 2010	Repair		Dietz and Company		DBB - Contract Awarded	Waterman Excavating, Inc
Foxborough PS	Foxborough HS	Construction	Repair	Construction Monitoring Services, Inc.	Kaestle Boos Associates, Inc.	Consulting Engineering Services, LLC	DBB - Contract Awarded	CTA Construction Co.
Franklin PS	Franklin HS	Feasibility Study	Renovation	Daedalus Projects Inc.	Kaestle Boos Associates, Inc.			
Gardner PS	Waterford Street Primary	Local Clearance - 07/08						
Georgetown PS	Penn Brook IS	Local Clearance - 09/10						
Gloucester PS	West Parish ES	Local Clearance - 09/10						
Grafton PS	Grafton Memorial SHS	Design Development	New Construction	Joslin, Lesser & Associates, Inc.	Symmes Maini & McKee Associates	Horizon Engineering Associates, LLP	CMR - CM Selected	Dimeo Construction
Granby PS	Granby JHS / SHS	Approved Project Vote Pending	New Construction	Skanska USA Building, Inc.	Dore & Whittier Architects, Inc.			
Greater Lowell Voc Tec PS	Gr Lowell Regional Voc / Tech HS	OPM Selection						
Greenfield PS	Greenfield HS	OPM Selection						
Hadley PS	Hopkins Academy	Local Clearance						
Hadley PS	Hopkins Academy	Closeout/Audit			Kaestle Boos Associates, Inc.			

# Master District Status List

Yellow = Wait List Project	
Green = Green Repair	Red = Changes in last 60 days

District Name	School Name	Status	Preferred Schematic	OPM	Designer	Cx Authority	Procurement Status	CM/GC
Hamilton-Wenham PS	Cutler ES	Closeout/Audit	Repair	Municipal Building Consultants, Inc.	Richard D. Kimball Company, Inc.	Sebesta Blomberg & Associates	DBB - Contract Awarded	Thomas E. Snowden Inc.
Hampden-Wilbraham PS	Minnechaug Reg HS	Construction	Model School	ARCADIS U.S., Inc.	Mount Vernon Group Architects, Inc.	Horizon Engineering Associates, LLP	DBB - Contract Awarded	Fontaine Bros.
Hancock PS	Hancock ES	Design Development	Repair	N/A	Westall Architects			
Hanover PS	Hanover HS	Construction	New Construction	PMA Consultants	HMFH Architects, Inc.	Horizon Engineering Associates, LLP	DBB - Contract Awarded	Callahan, Inc
Harvard PS	Harvard ES	Local Clearance						
Haverhill PS	Haverhill HS	Construction						
Hingham PS	New Elementary School	Closeout/Audit	New Construction	Knight, Bagge & Anderson, Inc.	Ai3 Architects LLC		DBB - Contract Awarded	CTA Construction Co.
Holbrook PS	Holbrook JHS / SHS	OPM Selection						
Holyoke PS	Holyoke HS	Construction			Design Partnership of Cambridge, Inc.			
Hopedale PS	Memorial ES	Closeout/Audit	Repair		Gale Associates, Inc.		DBB - Contract Awarded	Greenwood Industries Inc.
Hopkinton PS	Center ES	Preferred Schematic	New Construction	Town of Hopkinton	Design Partnership of Cambridge, Inc.		Undetermined	
Hudson PS	John F Kennedy MS	Project Scope & Budget	New Construction	PMA Consultants	The Office of Michael Rosenfeld, Inc.			
Leicester PS	Leicester Memorial ES	Local Clearance						
Leicester PS	Leicester MS	Local Clearance						
Leominster PS	Leominster SHS	Design Development	Addition/Renovation	Daedalus Projects, Inc.	Lamoureux Pagano & Associates, Inc.	Horizon Engineering Associates, LLP		
Lincoln PS	Lincoln K-8	Designer Selection		Skanska USA Building, Inc.				
Littleton PS	Russell St ES	Closeout/Audit	Repair	Daedalus Projects, Inc.	Drummeay Rosane Anderson, Inc.	WSP Flack + Kurtz	DBB - Contract Awarded	Colantonio, Inc.
Longmeadow PS	Longmeadow HS	Construction	New Construction	Joslin, Lesser & Associates, Inc.	The Office of Michael Rosenfeld, Inc.	Foreman Building Commissioning, LP	CMR - CM Selected	Gilbane Building Company
Lowell PS	Charles W Morey ES	Closeout/Audit		Watermark			DBB - Contract Awarded	CTA Construction Co.
Lunenburg PS	Lunenburg HS	Local Clearance - 09/10						
Lynn PS	Thurgood Marshall MS	Local Clearance - 09/10						
Lynnfield PS	Lynnfield HS	Local Clearance - 09/10						
Malden PS	Malden HS	Construction	Renovation	URS Corporation	Flansburgh Associates, Inc.		CMR - CM Selected	Gilbane Building Company
Manchester Essex Regional PS	Manchester JHS / SHS	Closeout/Audit		Design Technique	Mount Vernon Group Architects, Inc.		DBB - Contract Awarded	TLT Construction
Marblehead PS	Glover Primary	Preferred Schematic	New Construction	Municipal Building Consultants, Inc.	JCJ Architecture + Interiors, PC		Undetermined	
Marblehead PS	Village IS	Building Completion 2010	Repair	Municipal Building Consultants, Inc.	Symmes Maini & McKee Associates	RDK Engineering	DBB - Contract Awarded	Groom Construction

# Master District Status List

Yellow = Wait List Project	
Green = Green Repair	Red = Changes in last 60 days

District Name	School Name	Status	Preferred Schematic	OPM	Designer	Cx Authority	Procurement Status	CM/GC
Marshfield PS	Gov Edward Winslow ES	Design Development	Repair	Vertex Construction Services	Knight, Bagge & Anderson, Inc.			
Maynard PS	Maynard HS	Approved Project Vote Pending	New Construction	Municipal Building Consultants, Inc.	Tappe Associates, Inc.		Undetermined	
Medway PS	Medway MS	Approved Project Vote Pending		Compass Project Management, Inc.	Knight, Bagge & Anderson, Inc.			
Methuen PS	Methuen HS	Design Development	Addition/Renovation	KBA/Trident	Finegold Alexander and Associates, Inc.	Environmental Health and Engineering	Undetermined	
Middleton PS	Howe-Manning IS	Construction	New Construction	RF Walsh Collaborative Partners	DiNisco Design Partnership, Limited	Foreman Building Commissioning, LP	DBB - Contract Awarded	CTA Construction Co.
Minuteman Voc Tech PS	Minuteman Reg HS	Local Clearance - 09/10						
Mount Greylock PS	Mt Greylock Reg HS	Construction	Repair	N/A	Hesnor Engineering & Barry Architects	Horizon Engineering Associates, LLP	DBB - Contract Awarded	Adams Plumbing & Heating
Narragansett PS	Templeton Center	Feasibility Study		Strategic Building Solutions, LLC	Symmes Maini & McKee Associates		Undetermined	
Nashoba PS	Pompositicut Primary	Construction	Addition/Renovation	Construction Monitoring Services, Inc.	Symmes Maini & McKee Associates	Strategic Building Solutions	DBB - Contract Awarded	Stella P.J. Construction Corp.
Nashoba Valley Tech PS	Nashoba Valley Tech HS	Approved Project Vote Pending	Repair					
Natick PS	Natick HS	Construction	Model School	RF Walsh Collaborative Partners	Ai3 Architects LLC	RFS Engineering	DBB - Contract Awarded	Brait Builders Corporation
Needham PS	Newman ES	Design Development	Repair	Town of Needham	Drumme Rosane Anderson, Inc.	RFS Engineering	CMR - CM Selected	Consigli Construction Co.
New Bedford PS	Abraham Lincoln	Building Completion 2010	New Construction	Daedalus Projects Inc	Mount Vernon Group Architects, Inc.	Sebesta Blomberg & Associates	DBB - Contract Awarded	CTA Construction Co.
New Bedford PS	John Hannigan ES	Local Clearance - 09/10						
New Bedford PS	Elizabeth Carter Brooks ES	Feasibility Study						
New Salem-Wendell PS	Swift River ES	Local Clearance						
Newburyport PS	Rupert A Nock MS	Local Clearance - 09/10						
Newton PS	Newton North HS	Building Completion 2010	New Construction	Turner Construction Company	Dore & Whittier Architects, Inc.		CMR - CM Selected	Dimeo Construction
Norfolk County Agr PS	Norfolk County Agr HS	Approved Project Vote Pending	Addition/Renovation	Compass Project Management, Inc	Turowski2 Architecture, Inc.			
Norfolk PS	Freeman-Centennial IS	Design Development	New Construction	Joslin, Lesser & Associates, Inc.	Flansburgh Associates, Inc.	WSP Flack + Kurtz	DBB - In Design	Fontaine Bros., Inc.
North Adams PS	Silvio O Conte MS	Feasibility Study		Strategic Building Solutions, LLC	Margo Jones Architects, Inc.			
North Attleborough PS	Falls ES	Local Clearance						
North Attleborough PS	Joseph W Martin Jr ES	Closeout/Audit	Repair		CBI Consulting Inc.		DBB - Contract Awarded	Eagle Rivet Roof Services Corporation
North Brookfield PS	North Brookfield ES	Local Clearance						
North Reading PS	North Reading HS	OPM Selection						
Northampton-Smith PS	Smith Vocational and Agricultural HS	Local Clearance - 09/10						



# Master District Status List

Yellow = Wait List Project	
Green = Green Repair	Red = Changes in last 60 days

District Name	School Name	Status	Preferred Schematic	OPM	Designer	Cx Authority	Procurement Status	CM/GC
Northeast Metro Voc PS	Northeast Metro Reg Voc HS	Local Clearance - 09/10						
Norton PS	Norton HS	Designer Selection		Pinck				
Norwood PS	Norwood HS	Construction	Model School	Compass Project Management, Inc.	Ai3 Architects LLC		DBB - Contract Awarded	Agostini Construction Company, Inc.
Old Colony Reg Voc Tech PS	Old Colony Regional Voc / Tech HS	Local Clearance - 09/10						
Orange PS	Dexter Park IS	Local Clearance - 09/10						
Oxford PS	Oxford MS	OPM Selection						
Palmer PS	Converse MS	Local Clearance						
Palmer PS	Old Mill Pond ES	Local Clearance						
Palmer PS	Palmer HS	Local Clearance						
Peabody PS	J Henry Higgins MS	Designer Selection	Repair	Daedalus				
Pittsfield PS	Taconic HS	OPM Selection						
Plymouth PS	Plymouth North HS	Construction	Model School	Ted Gentry Associates	Ai3 Architects LLC	Sebesta Blomberg & Associates	DBB - Contract Awarded	J&J Contractors Inc.
Quabbin PS	Quabbin Reg HS	Project Scope & Budget	Repair		LPBA Architects			
Quabbin PS	Oakham Center ES	Closeout/Audit	Repair		Russo Barr Associates, Inc.	VP Consultants, LLC	DBB - Contract Awarded	Cape Way Roofing
Quincy PS	Quincy High School	Building Completion 2010	New Construction	Tishman Construction Corporation of MA	Symmes Maini & McKee Associates		CMR - CM Selected	Gilbane Building Company
Quincy PS	Central MS	Feasibility Study	New Construction	Tishman Construction Corporation of MA	Ai3 Architects LLC			
Reading PS	Birch Meadow ES	Local Clearance						
Reading PS	J Warren Killam ES	Local Clearance						
Revere PS	Paul Revere ES	Building Completion 2010	New Construction	RF Walsh Collaborative Partners	Drummey Rosane Anderson, Inc.		DBB - Contract Awarded	Delulis Brothers Construction Company
Rochester PS	Rochester Memorial ES	Construction	Addition/Renovation	PMA Consultants	Flansburgh Associates, Inc.	Horizon Engineering Associates, LLP	CMR - CM Selected	Gilbane Building Company
Rockland PS	John W Rogers MS	Design Development	Addition/Renovation	Daedalus Projects Inc	Dore & Whittier Architects, Inc.	Consulting Engineering Services, LLC	CMR - CM Selected	Agostini Construction Company, Inc.
Rockport PS	Rockport ES	Design Development	Repair	N/A	Russo Barr Associates, Inc.			
Rockport PS	Rockport HS	Closeout/Audit	Repair		Russo Barr Associates, Inc.	VP Consultants, LLC	DBB - Contract Awarded	Feeley, McAnespie, Inc.
Salem PS	Saltonstall ES	Local Clearance	Repair					
Salem PS	Collins MS	Local Clearance	Repair					
Sandwich PS	Oak Ridge K-8	Local Clearance	Repair					

# Master District Status List

Yellow = Wait List Project	
Green = Green Repair	Red = Changes in last 60 days

District Name	School Name	Status	Preferred Schematic	OPM	Designer	Cx Authority	Procurement Status	CM/GC
Saugus PS	Belmonte Saugus MS	Designer Selection	Repair	Skanska				
Scituate PS	Wampanoag ES	Project Scope & Budget	Repair	Bargmann Hendrie + Archetype	Knight, Bagge & Anderson, Inc.			
Sharon PS	Sharon MS	Construction	Addition/Renovation	Daedalus Projects, Inc.	Kaestle Boos Associates, Inc.	Horizon Engineering Associates, LLP	CMR - CM Selected	Consigli Construction Co.
Shawsheen Valley Voc PS	Shawsheen Valley Voc / Tech HS	Design Development			Knight, Bagge & Anderson, Inc.			
Shrewsbury PS	Spring Street ES	Local Clearance						
Shrewsbury PS	Sherwood MS	Design Development	New Construction	PMA Consultants	Lamoureux Pagano & Associates, Inc.	RDK Engineering	CMR - CM Selected	Gilbane Building Company
Somerset PS	Somerset HS	Local Clearance - 09/10						
Somerville PS	E Somerville Community K-8	Project Scope & Budget	Renovation	City of Somerville	Maguire Group Inc.			
South Hadley PS	Plains ES	Local Clearance - 09/10						
South Shore Reg Voc PS	South Shore Voc / Tech HS	Design Development	Repair	Lincoln Consultants	Gale Associates, Inc.			
Southbridge PS	Southbridge HS	Design Development	New Construction	Joslin, Lesser & Associates, Inc.	Tappe Associates, Inc.	Environmental Health and Engineering	CMR - CM Selected	Consigli Construction Co.
Southeastern Reg Voc Tech PS	Southeastern Regional Voc / Tech HS	Feasibility Study		RF Walsh Collaborative Partners	Drummey Rosane Anderson, Inc.			
Southern Worcester Cty VT PS	Bay Path Regional Voc / Tech HS	Feasibility Study		Heery International, Inc	Kaestle Boos Associates, Inc.			
Southwick-Tolland	Woodland ES	Feasibility Study		Strategic Building Solutions, LLC	JCJ Architecture + Interiors, PC			
Spencer-E Brookfield PS	David Prouty HS	Local Clearance - Repair - 09						
Springfield PS	Forest Park Middle School	Preferred Schematic	Addition/Renovation	ARCADIS-U.S., Inc.				
Springfield PS	SCIPP Years 2 & 3	Designer Selection						
Springfield PS	Putnam Voc / Tech HS	Construction	New Construction	ARCADIS	Drummey Rosane Anderson, Inc.	Strategic Building Solutions	CMR - CM Selected	Consigli Construction Co.
Springfield PS	SCIPP Year 1	Closeout/Audit	Repair					
Stoneham PS	Stoneham MS	OPM Selection						
Sturbridge PS	Burgess ES	Construction	Addition/Renovation	Lamoureux Pagano & Associates, Inc.	Drummey Rosane Anderson, Inc.	Horizon Engineering Associates, LLP	DBB - Contract Awarded	Fontaine Bros.
Sudbury PS	Peter Noyes ES	Local Clearance						
Sutton PS	Sutton MS	Design Development	Addition/Renovation	Strategic Building Solutions	Flansburgh Associates, Inc.	RDK Engineering		
Tantasqua PS	Tantasqua Reg JHS	Local Clearance						
Taunton PS	Taunton HS	Construction	Addition/Renovation	Gilbane	Design Partnership of Cambridge, Inc.		DBB - Contract Awarded	Bacon-Agostini Construction Joint Venture
Tewksbury PS	Tewksbury Memorial HS	Construction	Model School	Heery International, Inc	Symmes Maini & McKee Associates	Sebesta Blomberg & Associates	DBB - Out to Bid	

# Master District Status List

Yellow = Wait List Project	
Green = Green Repair	Red = Changes in last 60 days

District Name	School Name	Status	Preferred Schematic	OPM	Designer	Cx Authority	Procurement Status	CM/GC
Tri County PS	Tri County Regional Voc / Tech HS	Project Scope & Budget	Repair		Richard D. Kimball Company, Inc.			
Uxbridge PS	Uxbridge HS	Design Development	New Construction	Joslin, Lesser & Associates, Inc.	Raymond Design Associates, Inc.		CMR - CM Selected	Shawmut Design and Construction
Wachusett PS	Mountview MS	Local Clearance - 09/10						
Wakefield PS	Galvin MS	Local Clearance - 09/10						
Wakefield PS	Wakefield Memorial HS	Approved Project Vote Pending	Addition/Renovation					
Walpole PS	Bird MS	Local Clearance						
Wayland PS	Wayland HS	Construction	New Construction	KV Associates	HMFH Architects, Inc.	WSP Flack + Kurtz	CMR - CM Selected	Shawmut Construction
Webster PS	Park Avenue ES	Local Clearance - 09/10						
Wellesley PS	Wellesley SHS	Construction	New Construction	Ryegate Inc	Symmes Maini & McKee Associates	RFS Engineering	CMR - CM Selected	Turner Construction
West Bridgewater PS	West Bridgewater JHS / SHS	Local Clearance - 09/10						
West Springfield PS	West Springfield HS	OPM Selection	Model School					
Westborough PS	Sarah W Gibbons MS	Local Clearance - Repair - 09						
Westfield PS	Southampton Road ES	Local Clearance	Repair					
Westfield PS	Highland School	Local Clearance	Repair					
Westfield PS	Abner Gibbs ES	OPM Selection						
Weston PS	Field ES School	Feasibility Study		Compass Project Management, Inc	Jonathan Levi Architects LLC			
Weston PS	Weston HS	Local Clearance						
Weston PS	Weston MS	Local Clearance						
Westport PS	Alice A Macomber ECC	Local Clearance						
Westport PS	Westport HS	Local Clearance						
Westport PS	Westport MS	Local Clearance						
Whitman-Hanson PS	Maquan ES	Local Clearance - 09/10						
Whittier Voc PS	Whittier Reg Voc HS	Closeout/Audit	Repair	Heery International	Gale Associates, Inc.	Cannon Design	DBB - Contract Awarded	Greenwood Industries
Williamsburg PS	Anne T Dunphy IS	Designer Selection		Arcadis				
Wilmington PS	Wilmington HS	OPM Selection						
Winchendon PS	Toy Town ES	Design Development	Repair		Hesnor Engineering Company			

# Master District Status List

Yellow = Wait List Project

Green = Green Repair


Red = Changes in last 60 days

District Name	School Name	Status	Preferred Schematic	OPM	Designer	Cx Authority	Procurement Status	CM/GC
Winchester PS	Lynch ES	Local Clearance						
Winchester PS	Winchester HS	Local Clearance - 09/10						
Winchester PS	Vinson-Owen ES	Project Scope & Budget	New Construction	RF Walsh Collaborative Partners	Tappe Associates, Inc.		Undetermined	
Winthrop PS	Winthrop Senior High	OPM Selection						
Woburn PS	Daniel L Joyce MS	Project Scope & Budget						
Woburn PS	Goodyear ES	Construction	New Construction	Municipal Building Consultants, Inc.	Tappe Associates, Inc.	Strategic Building Solutions	CMR - CM Selected	Gilbane Building Company
Woburn PS	John F Kennedy MS	Project Scope & Budget						
Worcester PS	North HS	Construction		Maguire Group Inc	City of Worcester		CMR - CM Selected	Gilbane Building Company

**No. of Projects: 213**

## Project Status November 17, 2010

New Program: 121  
 Waitlist: 13  
 Green Repair: 39  
 Closeout/Audit Complete: 22  
 Total Projects: 195

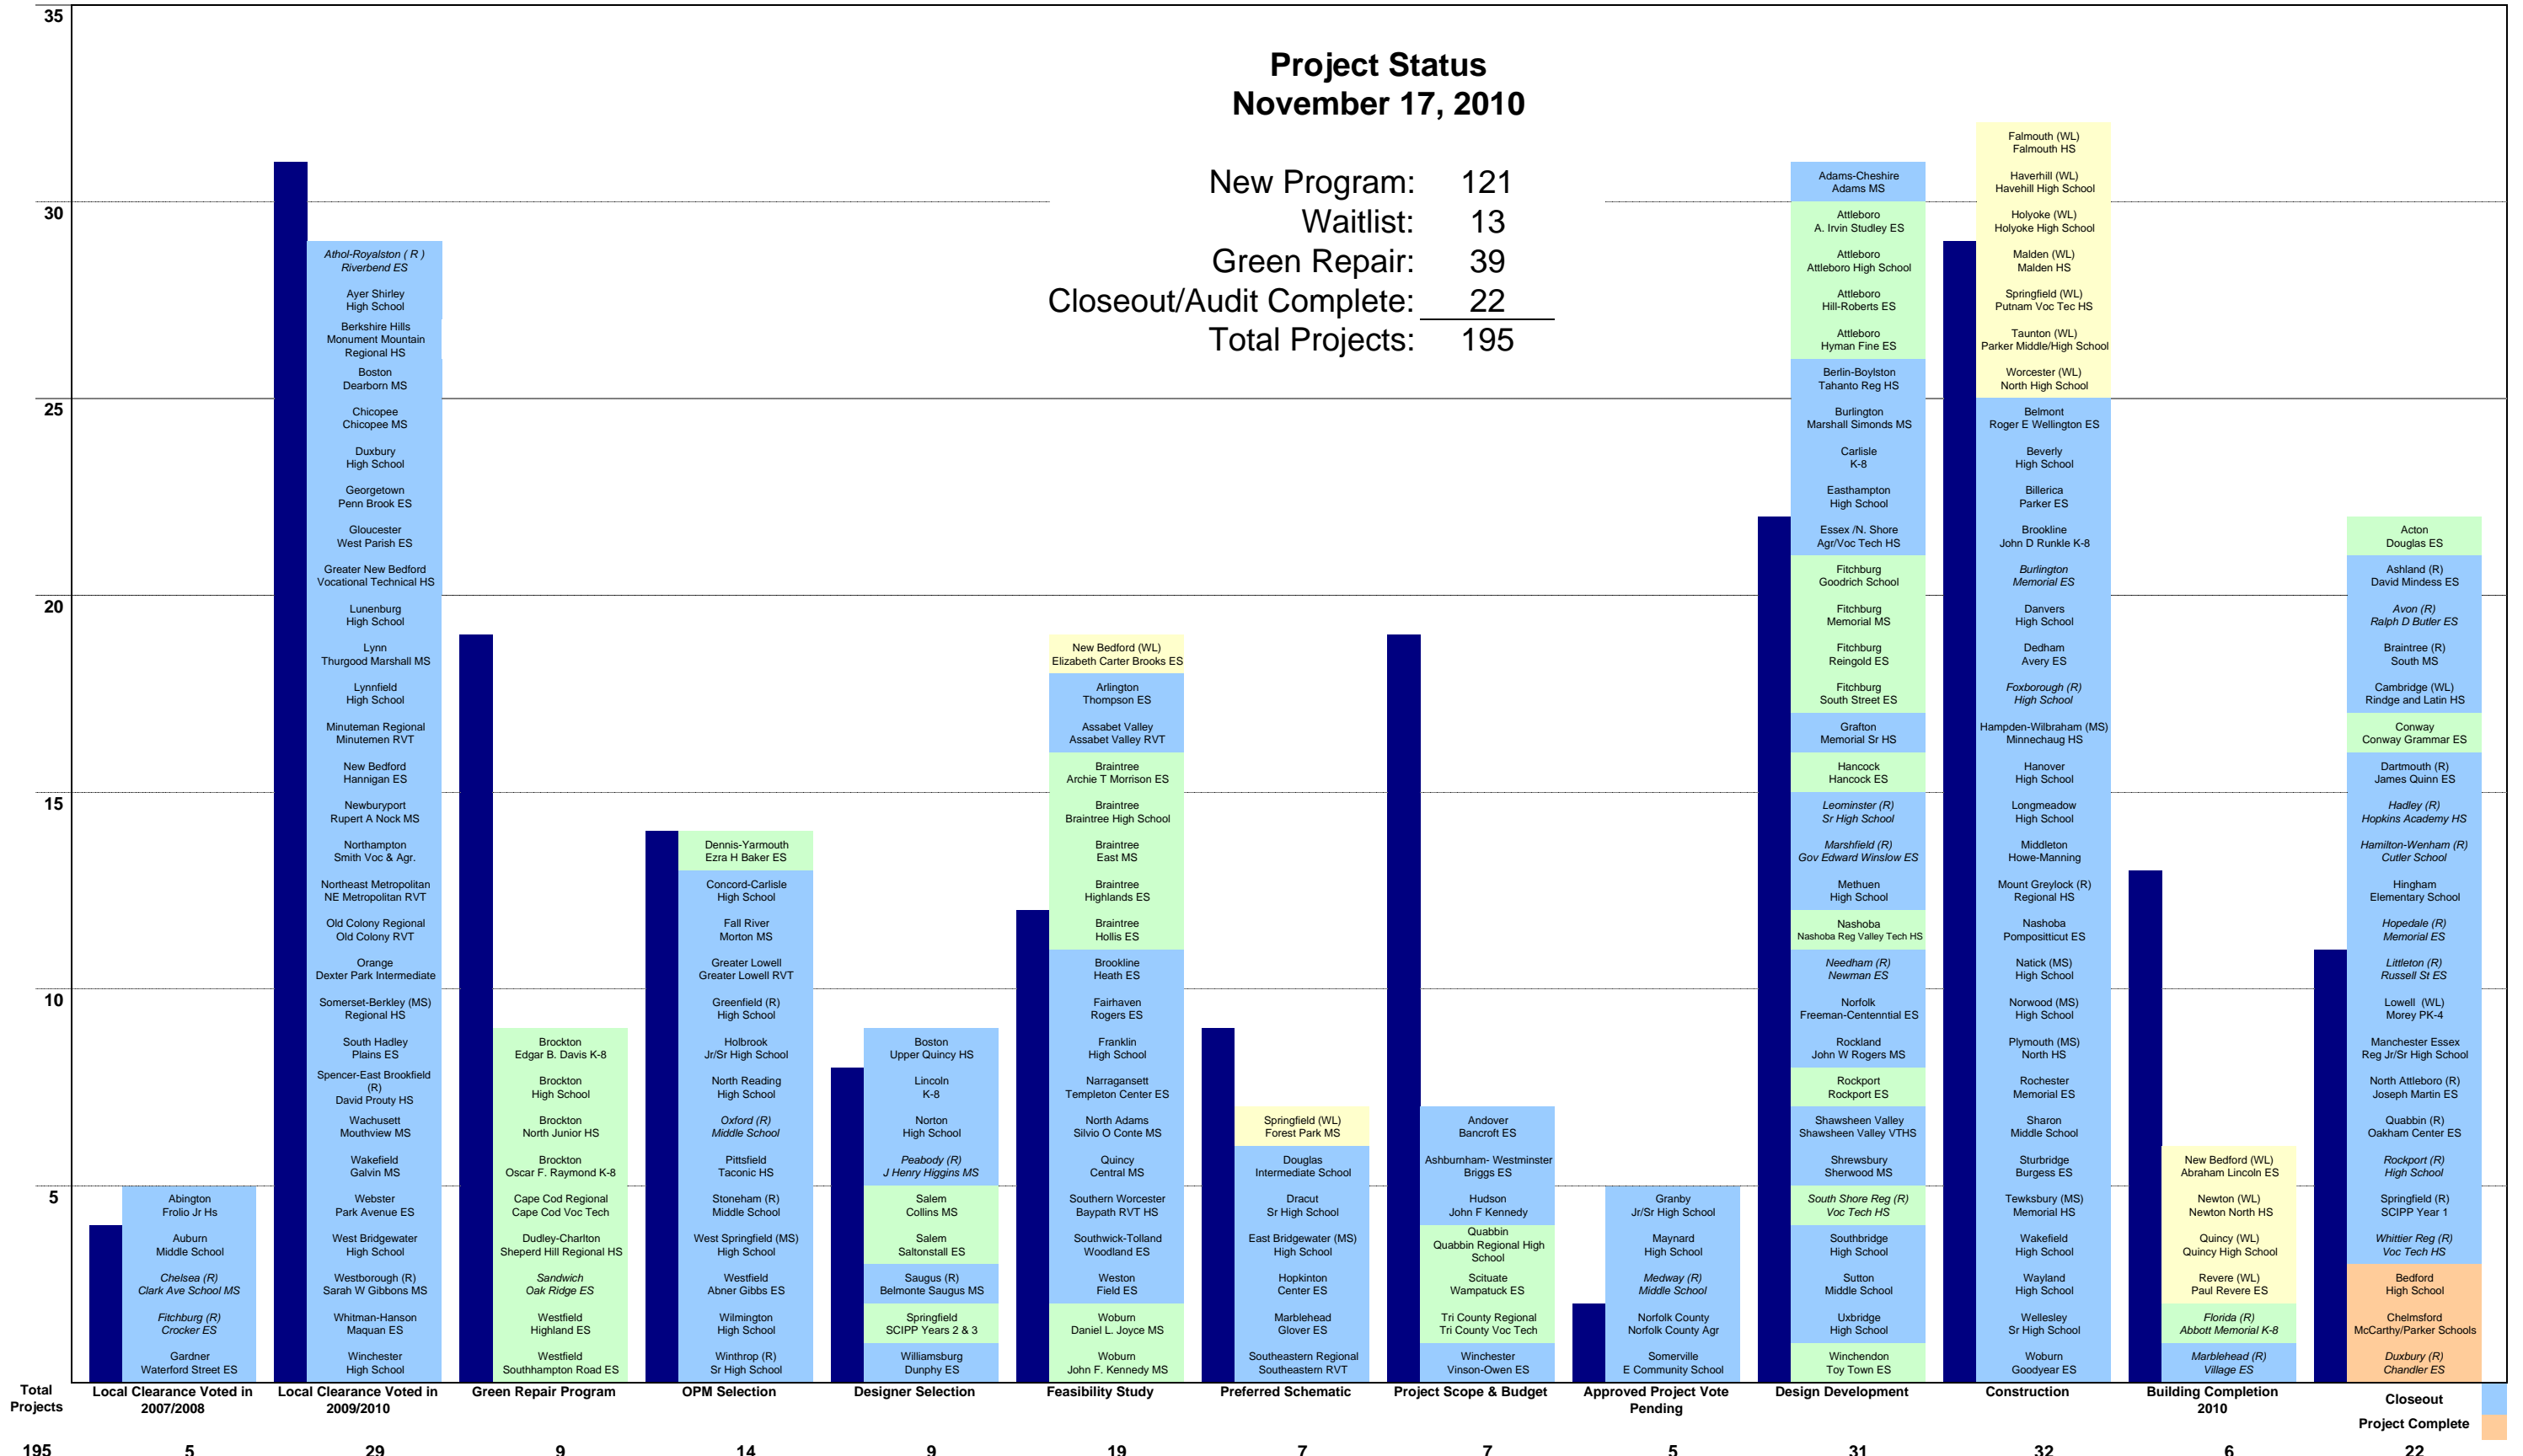

■ Capital Pipeline Status Presented at September 29, 2010 Board of Directors Meeting  
 (R) = Repair (MS) = Model School

■ Waitlist Projects  
■ Green Repair Projects

### 2010 Estimated Bid Dates

Note bid dates are **Estimates ONLY**. Please contact Districts for exact information.

Total Project Budget denotes total District costs and does not denote the basis of the MSBA Total Facilities Grant.

- Denotes bid phase in progress or complete
  - Denotes estimated bid dates

DISTRICT	DESIGN BASIS FOR ENROLLMENT	PROJECT BUDGET <small>Shown in Millions</small>	CONSTRUCTION BUDGET <small>Shown in Millions</small>	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC
<b>BURLINGTON</b>	500	\$27.1	\$22.2	Memorial ES New Construction: GC Bids rcv'd 1/28. NTP Issued 2/18.											
<b>*WELLESLEY</b>	1500	\$132.0	\$98.5	Senior HS New Construction: Filed-Sub Bids rcv'd 2/8, 2/9, 2/10. GMP Issued 3/25.											
<b>*WOBURN</b>	320	\$26.5	\$19.9	Goodyear ES New Construction: Filed-Sub Bids rcv'd 3/11. GMP Issued 3/24.											
<b>*SPRINGFIELD</b>	1440	\$125.0	\$101.5	Putnam Vo-Tech New Construction: Filed-Sub Bids rcv'd 3/11. GMP Issued 5/3.											
<b>MIDDLETON</b>	553	\$31.3	\$24.3	Howe-Manning ES New Construction: Filed-Sub Bids rcv'd 3/10. G.C. Bids rcv'd 3/26. NTP Issued 4/5.											
<b>PLYMOUTH</b>	1350	\$92.2	\$72.0	North HS New Construction: Filed Sub-Bids rcv'd 3/4. G.C. Bids rcv'd 3/30. NTP Issued 4/28.											
<b>*BELMONT</b>	575	\$40.0	\$28.7	Wellington ES New Construction: Filed Sub-Bids rcv'd 5/11. Non-Trade Bids rcv'd 5/20. GMP Issued 7/20.											
<b>QUABBIN</b>	291	\$0.8	\$0.7	OakHam Center ES: Filed-Sub Bids rcv'd 4/30/10. NTP Issued 5/11.											
<b>*ROCHESTER</b>	635	\$26.5	\$20.5	Memorial ES Addition / Renovation: Filed Sub-Bids rcv'd 5/5. GMP Issued 6/22.											
<b>FLORIDA</b>	115	\$0.5	\$0.4	Abbott Memorial: Filed Sub-Bids rcv'd 5/11. NTP Issued 5/17											
<b>HAMPDEN-WILBRAHAM</b>	1225	\$78.9	\$66.4	Minnechaug HS New Construction: Filed-Sub Bids rcv'd 6/15. G.C. Bids rcv'd 7/20. NTP Issued 7/27.											
<b>HAMILTON-WENHAM</b>	300	\$1.5	\$1.2	Cutler ES Repair: Filed-Sub Bids rcv'd 3/30. G.C. Bids rcv'd 4/8. NTP Issued 4/16.											
<b>*SHARON</b>	845	\$49.5	\$34.7	Middle School Addition / Renovation: Early Release Bid Package rcv'd 5/17. Filed-Sub Bids rcv'd 5/18. GMP Issued 9/14.											
<b>ASHLAND</b>	596	\$3.1	\$2.6	David Mindess ES Repair: Filed-Sub Bids rcv'd 4/26. G.C. Bids rcv'd 5/3. NTP Issued 6/17.											
<b>DARTMOUTH</b>	845	\$1.3	\$1.1	James Quinn ES Repair: G.C. Bids rcv'd 2/25. NTP Issued 3/31.											
<b>N. ATTLEBORO</b>	717	\$0.8	\$0.7	Joseph Martin ES Repair: Filed-Sub Bids rcv'd 4/23. NTP Issued 6/4.											
<b>ROCKPORT</b>	331	\$1.1	\$1.0	Rockport HS Repair: G.C. Bids rcv'd 2/26. NTP Issued 3/17.											
<b>MT GREYLOCK</b>	641	\$1.4	\$1.2	MT Greylock Regional H.S Repair: Filed-Sub Bids rcv'd 4/29. G.C. Bids rcv'd 5/6. NTP Issued 5/6.											
<b>WHITTIER REGIONAL</b>	1206	\$3.2	\$2.6	Regional VTHS Repair: Filed-Sub Bids rcv'd 3/31. G.C. Bids rcv'd 4/7. NTP Issued 5/19.											
<b>Subtotal</b>	<b>13,985</b>	<b>\$642.7</b>	<b>\$500.2</b>												

## 2010 Estimated Bid Dates

Note bid dates are **Estimates ONLY**. Please contact Districts for exact information.

Total Project Budget denotes total District costs and does not denote the basis of the MSBA Total Facilities Grant.

- Denotes bid phase in progress or complete
  - Denotes estimated bid dates


DISTRICT	DESIGN BASIS FOR ENROLLMENT	PROJECT BUDGET <small>Shown in Millions</small>	CONSTRUCTION BUDGET <small>Shown in Millions</small>	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC
<small>*Projects Considering the CM @ Risk Method</small>															
<b>*WAYLAND</b>	900	\$70.8	\$56.2					Wayland HS New Construction: Early Bid Packages rcv'd 6/30.							Filed-Sub Bid rcv'd 10/21. GMP Targeted for November.
<b>NATICK</b>	1300	\$89.0	\$70.8												Natick HS New Construction: Filed-Sub Bids rcv'd 9/1. NTP Issued 9/22. G.C. Bids rcv'd 8/18.
<b>NASHOBA</b>	600	\$37.8	\$28.8												Pompositticut ES Addition / Renovation: Filed-Sub Bids rcv'd 5/24. G.C. Bids rcv'd 6/7. NTP Issued 6/15.
<b>STURBRIDGE</b>	860	\$46.9	\$36.4												Burgess ES Addition/Renovation: Filed-Sub Bids rcv'd 7/14. G.C. Bids rcv'd 7/27. NTP Issued 8/5.
<b>NORFOLK</b>	585	\$37.5	\$28.9												Freeman-Centennial ES New Construction: Filed-Sub Bids rcv'd 10/20. G.C. Bids Due 11/3. NTP Targeted December.
<b>TEWKSBURY</b>	1100	\$84.2	\$65.9												Memorial HS (MS) New Construction: Filed-Sub Bids rcv'd 9/15. G.C. Bids rcv'd 10/6. NTP Issued 10/15.
<b>BILLERICA</b>	500	\$34	\$27.1												Parker ES New Construction: Filed-Sub Bids rcv'd 8/19. G.C. Bids rcv'd 9/2. NTP Issued 9/15.
<b>*SOUTHBRIDGE</b>	1050	\$76.5	\$60.1		Southbridge: CM@R Completed.										Southbridge HS New Construction: Early Site Package Bids rcv'd 8/24. Early Steel Package Bids rcv'd 10/15. Filed-Sub Bids Due 12/23/10. GMP Targeted January 2011.
<b>*DEDHAM</b>	310	\$23.4	\$19.9					Dedham: CM@R Completed.							Avery ES New Construction: Filed-Sub Bids Due 10/29. GMP Targeted November.
<b>DANVERS</b>	1000	\$79	\$62.7					Danvers High School Addition / Renovation: Early Bid Packages For Demo & Abatement Bids rcv'd 5/6. Swing Space Bids rcv'd 5/26.							Filed-Sub Bids rcv'd 10/7. G.C. Bids rcv'd 10/27. NTP Targeted November.
<b>BROOKLINE</b>	560	\$29.8	\$22.5												Runkle ES Addition / Renovation: Filed-Sub Bids rcv'd 9/23. G.C. Bids rcv'd 10/14. NTP Targeted November.
<b>*GRAFTON</b>	900	\$72.4	\$57.4												Grafton: CM@R Completed. Memorial HS New Construction: Early Foundation Package rcv'd 9/24. Early Steel Packages rcv'd 10/4. Early Site Packages Due 10/22. Filed-Sub Bids Due 12/17. GMP Targeted December.
<b>*ROCKLAND</b>	1525	\$86.2	\$66.5												Rockland: CM@R Completed. Rogers MS New Construction / HS Renovation: Early Site / Foundation Packages Due 11/4. Filed-Sub Bids Due 12/15. GMP Targeted December.
<b>SO. SHORE RVT</b>	595	\$3.2	\$2.6												Regional VTHS Repair: Filed-Sub & G.C. Bids Targeted December. NTP Targeted January 2011.
<b>ESSEX-NS</b>	1440	\$125	\$96.5												Essex North Shore HS New Construction.
<b>SHAWSHEEN</b>	1300	\$4.7	\$3.8												Shawsheen Voc Tech Repair: Filed Sub Due 11/10. G.C. Bids Due 11/17. NTP Targeted November.
<b>*NEEDHAM</b>	759	\$27.4	\$21.9												Newman ES Repair: Early Modular Foundation Work Bids rcv'd 5/7. Early Elec Duct Bank & Waterline Extension Work. Bids rcv'd 6/15. Filed-Sub Bids Due 12/7. GMP Targeted December.
<b>Subtotal</b>	<b>15,284</b>	<b>\$927.8</b>	<b>\$728.0</b>												
<b>GRAND TOTAL</b>	<b>29,269</b>	<b>\$1.57 B</b>	<b>\$1.23B</b>												
<b>Number of Construction-related Employment</b>			<b>6,141</b>												

### 2011 Estimated Bid Dates

Note bid dates are **Estimates ONLY**. Please contact Districts for exact information.

Total Project Budget denotes total District costs and does not denote the basis of the MSBA Total Facilities Grant.

- Denotes bid phase in progress or complete
  - Denotes estimated bid dates

DISTRICT	DESIGN BASIS FOR ENROLLMENT	PROJECT BUDGET <small>Shown in Millions</small>	CONSTRUCTION BUDGET <small>Shown in Millions</small>	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC
<small>*Projects Considering the CM @ Risk Method</small>															
<b>*SHREWSBURY</b>	900	\$47.3	\$37.0		Sherwood MS New Construction: Filed-Sub Bids Due 1/7. GMP Targeted February.										
<b>CARLISLE</b>	700	\$20.0	\$15.6	Carlisle ES Addition/Renovation: Filed-Sub Bids Due 1/14. G.C. Bids due 1/28. NTP Targeted February.											
<b>MARSHFIELD</b>	485	\$2.4	\$2.0	Marshfield Edward Winslow ES Repair: Filed-Sub Bids Due 1/6. G.C. Bids Due 1/20 NTP Targeted January.											
<b>BURLINGTON</b>	880	\$32.9	\$24.7	Marshall Simonds MS Addition/Renovation: Filed Sub and G.C Bids Targeted February to March. NTP Targeted April.											
<b>BERLIN / BOYLSTON</b>	560	\$44.0	\$34.2	Tahanto MS/HS New Construction: Filed-Sub and G.C. Bids Targeted April. NTP Targeted May.											
<b>*UXBRIDGE</b>	600	\$43.0	\$34.4	Uxbridge: CMR Complete											
<b>EASTHAMPTON</b>	510	\$43.7	\$33.5	Easthampton HS New Construction: Filed-Sub and G.C. Bids Targeted March to May. NTP Targeted June.											
<b>*LONGMEADOW</b>	1000	\$78.5	\$63.8	Longmeadow HS New Construction: Filed-Sub Bids Targeted 4/26. GMP Targeted May.											
<b>LEOMINSTER</b>	1805	\$45.9	\$32.7	Leominster HS Addition/Renovation: Filed-Sub and G.C. Bids Targeted March to May. NTP Targeted June.											
<b>SUTTON</b>	840	\$59.9	\$46.4	Sutton MS New Construction: Filed-Sub and G.C.Bids Targeted March to April. NTP Targeted June.											
<b>*ADAMS/CHESHIRE</b>	805	\$40.6	\$30.0	Hoosac Valley MHS Addition/Renovation: Filed-Sub and G.C.Bids Targeted June. GMP Targeted July.											
<b>METHUEN</b>	2075	\$99.1	\$74.9	Methuen HS Addition/Renovation: Filed-Sub and G.C. Bids Targeted November to December. NTP Targeted January 2012.											
<b>Subtotal</b>	<b>11,160</b>	<b>\$557.3</b>	<b>\$429.2</b>												
<b>GRAND TOTAL</b>	<b>11,160</b>	<b>\$557.3 M</b>	<b>\$429.2 M</b>												
<b>Number of Construction-related Employment</b>			<b>2,146</b>												



**Projects in Construction  
MSBA Grant Basis and Maximum Grant Amount**

New Program and Wait List Program Totals			39,013	6,991,216	2,152,133,542	\$1,732,743,782		\$1,157,183,941					
District	School	Grade	Projected Enroll	Proposed Square Footage	District Total Project Budget	MSBA Total Facility Grant Basis	Reimbursement Rate	Approximate Maximum Grant Amount	Project Type	CM-R/GC	Construction Start	Estimated Substantial Completion Date	Construction Status
<b>Capital Pipeline Projects in Construction</b>													
<b>New Program Totals</b>			<b>22,450</b>	<b>4,286,059</b>	<b>1,139,874,460</b>	<b>\$1,041,212,470</b>		<b>\$542,767,814</b>					
Ashland	David Mindess ES	3-5	628	96,000	\$2,384,021	\$2,173,515	48.68%	\$1,058,067	Design/Bid/Build	Greenwood Industries	22-Jun-10	27-Aug-10	New roof, skylight and ceiling tile replacement work is now complete. Punch list items remain and should be completed by the end of September.
Belmont	Roger E Wellington ES	K-5	575	88,203	\$40,664,431	\$31,000,050	40.00%	\$12,400,020	CM-R	Skanska	1-Mar-10	1-Jul-11	Concrete footings and walls are complete. Steel erection complete. Underslab utilities are being installed. Second floor slabs are being poured.
Beverly	Beverly HS	9-12	1,200	247,275	\$81,500,000	\$80,155,000	58.42%	\$46,826,551	Design/Bid/Build	CTA	6-Jan-09	16-Dec-11	Substantial Completion Dates: Phase 1A: New Academic Tower - Nov 18, 2010. Phase 1A: Auditorium/Music Rooms/Renovation Areas - Nov 18, 2010. Phase 1B: Locker Room/Upper Gym/Renovation Areas - substantially complete. Contractor working punch list. Phase 1C Existing Kitchen/Cafeteria/Renovation Areas: April, 2011. Phase 1D Field House/Renovated Areas: November 19, 2010. Phase 2 Existing Building Demolition/Site Work: December 16, 2011.
Billerica	Parker MS	K-5	500	89,093	\$34,007,436	\$31,565,064	55.69%	\$17,578,584	Design/Bid/Build	CTA	16-Sep-10	6-Sep-12	Pre-Phase 1 enabling work substantially complete. Notice to proceed issued to General contractor on 9/16/10.
Braintree	South MS	6-8	523	72,041	\$3,052,702	\$2,687,302	48.47%	\$1,302,535	Design/Bid/Build	Construction Dynamics	1-Apr-10	1-Oct-10	All construction has been completed with the exception of starting up the new boilers. This is scheduled to be accomplished prior to the need for heat in late October or early November 2010.
Burlington	Memorial ES	K-5	500	79,500	\$27,923,244	\$26,963,244	52.11%	\$14,050,546	Design/Bid/Build	CTA	8-Mar-10	11-Aug-11	The erection of structural steel is complete. The closing in of the exterior is on-going as is the installation of mechanical, plumbing and electrical work. Installation of metal stud walls and dry wall has begun.
Danvers	Danvers HS	9-12	1,000	249,792	\$79,843,732	\$74,694,239	56.11%	\$41,910,938	Design/Bid/Build	Bid ongoing	Oct-10	20-Aug-13	Abatement/Demo of links is now complete and graded. Infill of exterior walls from demo is on going and rerouting of electrical and tel/data is now complete.
Dartmouth	James Quinn ES	PK-5	925	122,000	\$1,358,304	\$1,358,304	47.64%	\$647,096	Design/Bid/Build	Advantage Glass, Inc.	6-Jun-10	30-Sep-10	Window replacement is over 95% complete. All academic areas are complete and remaining areas( Admin & Gym) will be complete by October 2010
Florida	Abbott Memorial K-8	K-8	115	23,241	\$490,347	\$487,829	60.76%	\$296,405	Design/Bid/Build	Waterman Excavating, Inc.	14-Jun-10	31-Aug-10	Waterproofing of foundation, installation of perimeter drain to mitigate water infiltration is complete. Punch list items that remain will be complete by 10/1/10.
Foxborough	Foxborough HS	9-12	885	218,500	\$19,993,200	\$19,037,185	49.31%	\$9,387,236	Design/Bid/Build	CTA	30-Mar-10	30-Dec-12	The building department toured the school on August 25th and signed off for the schools use. Boiler work continues and nearing completion for Oct 1st start-up. Roofing is 80% complete and will continue second shift and on Saturday to complete the metal edge trim on the completed areas. All site work curb cuts, handicap ramp and sidewalks are completed with only punch list work remaining.
Hamilton-Wenham	Cutler ES	K-5	298	45,000	\$1,429,720	\$1,429,720	42.58%	\$608,775	Design/Bid/Build	Thomas E. Snowden Inc.	6-Jun-10	31-Aug-10	HVAC replacement began in May and is 99% complete. Only Commissioning remains.
Hampden-Wilbraham	Minnechaug HS	9-12	1,225	231,467	\$78,986,658	\$76,796,379	61.73%	\$47,406,405	Design/Bid/Build	Fontaine Brothers	1-Aug-10	28-Jun-12	Site Contractor began clearing and grading the site. The General Contractor has secured the site.
Hanover	Hanover HS	9-12	800	156,000	\$59,953,688	\$59,484,384	47.21%	\$28,082,578	Design/Bid/Build	Callahan	1-Nov-09	1-May-12	Building slab on grade is complete. First floor framing underway. Exterior sheathing is 95% complete. Site work, drainage & utility installation is 95% complete. Brick facade installation underway. The project is approximately 55% complete.
Littleton	Russell Street ES	3-5	N/A	N/A	\$15,131,820	\$14,754,732	47.84%	\$7,058,664	Design/Bid/Build	Colantonio	25-Jun-09	30-Aug-10	The elevator is complete and elevator inspection is scheduled for the week of September 13th. All windows are installed. The project is substantially complete and 2 months ahead of schedule. Punch list remains and anticipated to be completed the second week of October.
Marblehead	Village ES	4-6	N/A	123,000	\$15,749,456	\$14,509,468	40.00%	\$5,803,787	Design/Bid/Build	Groom Construction	22-Dec-08	13-Aug-10	Construction on the project is now complete. Students and staff are using the building. Only minor punch list type work remains.
Middleton	Howe-Manning ES	4 - 6	553	83,500	\$31,392,734	\$30,114,849	51.47%	\$15,500,113	CM-R	CTA	22-Apr-10	13-Jan-12	Structural steel work has been completed. Mechanical, plumbing and electrical rough-in has begun.
Mount Greylock	Mount Greylock Reg HS	7-12	651	N/A	\$1,049,986	\$1,042,186	54.16%	\$564,448	Design/Bid/Build	Adams Plumbing & Heating	14-Jun-10	30-Sep-10	The heating system is approximately 80 % complete and will be completed prior to the need for heat.
					\$1,369,906	\$1,358,646	54.16%	\$735,843	Design/Bid/Build	Salco Construction	May-10	30-Sep-10	The renovations to the locker room areas are approximately 95% complete.
Nashoba	Pompositticut ES	K-2	600	98,030	\$37,829,870	\$35,640,351	50.85%	\$18,123,118	Design/Bid/Build	Stella P.J. Construction Corp.	16-Jun-10	12-Jun-12	Perimeter fencing, project layout, asbestos abatement and building demo completed during Phase 1A. Excavating for footings and concrete placement is underway.
Natick	Natick HS	9-12	1,300	254,095	\$88,987,414	\$82,016,562	52.63%	\$43,165,316	Design/Bid/Build	Brait Builders Corp.	15-Sep-10	15-Jun-13	Notice to proceed was issued to the General Contractor on 9/14/10. Mobilization and securing the site is complete.
North Attleboro	Joseph Martin ES	K-5	699	79,886	\$625,750	\$625,750	52.06%	\$325,765	Design/Bid/Build	Eagle Rivet Roof Services	14-Jun-10	1-Sep-10	Roof replacement is complete.
Norwood	Norwood HS	9-12	1,100	227,374	\$68,655,476	\$64,364,981	59.21%	\$38,110,505	Design/Bid/Build	Agostini	19-May-09	1-Jun-11	The project is approximately 67% complete. Sections C&D MEP rough-in continues. Interior wallboard and plaster is substantially complete. Ceiling grid and painting have begun. Tile flooring has begun in all toilet rooms. Sections A&B electrical finishes have begun. Site crews began construction of the east parking lot
Plymouth	Plymouth HS	9-12	1,350	267,357	\$92,249,040	\$79,420,894	58.24%	\$46,254,729	Design/Bid/Build	J&J Contractors	3-May-10	11-May-12	Contractor has mobilized and secured the site. Site work continues. Structural steel erection has begun
Quabbin	Oakham Center ES	PK-6	187	46,000	\$765,179	\$765,179	57.74%	\$441,814	Design/Bid/Build	Capeway Roofing	11-May-10	27-Aug-10	Roof and ceiling tile replacement projects are complete.
Rochester	Memorial ES	K-6	635	105,023	\$26,500,000	\$25,268,708	57.94%	\$14,640,689	CM-R	Gilbane	19-Apr-10	1-Sep-11	Phase 2 completed August 27- existing building turned back over to the town. Boiler room slab poured. Precast Bldg roof installation 50% complete. Interior framing 20% complete and MEP 35% complete. Site utilities 85% complete. Project is approximately 27% complete.
Rockport	Rockport MS/HS	6-12	598	117,184	\$1,006,384	\$1,006,384	41.10%	\$413,624	Design/Bid/Build	Feeley, McAnespie, Inc.	21-Jun-10	31-Aug-10	Roof replacement is on schedule and was completed Aug. 31st.
Sharon	Sharon MS	6-8	845	170,750	\$49,540,287	\$43,950,340	52.68%	\$23,153,039	CM-R	Consigli	1-Jun-10	22-Aug-11	All renovation work that could be accomplished to the existing school during the summer months has been accomplished. Students and staff are back in the existing building for this school year. Foundation work continues in front of the existing school building as does site work. Temporary driveways for dropping off and picking up students have been installed. Protective walkways separate the students from work area. All utilities such as telephone, electrical, gas and sewer have been connected.
Sturbridge	Burgess ES	K-6	860	129,300	\$46,926,630	\$41,844,754	57.92%	\$24,236,481	Design/Bid/Build	Fontaine Brothers	26-Aug-10	16-Oct-12	General Contractor mobilized, site secured.
Wayland	Wayland HS	9-12	900	154,171	\$70,800,000	\$62,500,000	40.00%	\$25,000,000	CM-R	Shawmut Design	28-Jun-10	1-Dec-11	Underground utilities are ongoing. Concrete footings and wall foundations are ongoing. Steel scheduled to arrive on October 7, 2010.
Wellesley	Wellesley HS	9-12	1,500	280,000	\$131,054,929	\$107,751,342	40.00%	\$43,100,537	CM-R	Turner	24-Aug-09	5-Mar-12	Concrete decking, exterior wall metal framing and sheathing continues. Brickwork ongoing at Bldg C. Mock-up window due w/e September 13, 2010. Balance of windows units due November, 2010.
Whittier Reg	Whittier Reg Voc Tech HS	9-12	1,178	365,000	\$2,147,762	\$2,069,360	66.18%	\$1,369,502	Design/Bid/Build	Greenwood Industries	28-Jun-10	15-Sep-10	Roof replacement was completed on September 15, 2010.

**Projects in Construction  
MSBA Grant Basis and Maximum Grant Amount**

District	School	Grade	Projected Enroll	Proposed Square Footage	District Total Project Budget	MSBA Total Facility Grant Basis	Reimbursement Rate	Approximate Maximum Grant Amount	Project Type	CM-R/GC	Construction Start	Estimated Substantial Completion Date	Construction Status
Woburn	Goodyear ES	K-5	320	67,277	\$26,504,354	\$24,375,769	54.21%	\$13,214,104	CM-R	Gilbane	24-Mar-10	15-Jul-11	Structural steel has been erected. Concrete slab and concrete floor decks have been poured. Mechanical, electrical, plumbing and fire protection trades work on-going.
<b>Wait List Projects in Construction</b>													
<b>Wait List Program Totals</b>			<b>16,563</b>	<b>2,705,157</b>	<b>1,012,259,082</b>	<b>\$691,531,312</b>		<b>\$614,416,127</b>					
Cambridge	Rindge & Latin HS	9-12	1,529	82,938	\$112,116,300	\$33,620,000	69.47%	<b>\$33,973,519</b>	Design/Bid/Build	W.T. Rich, Inc.	May-07	Jul-11	Phase 1A is complete with ongoing work in phase 1B as well as phase 2 which began in July 2010.
Falmouth	Falmouth HS	9-12	1,003	266,654	\$86,325,000	\$56,263,993	59.70%	\$33,589,604	Design/Bid/Build	TLT Construction	Jun-05	Nov-10	Project is approximately 95% complete at this time with Phase 2 completion scheduled for Fall 2010.
Haverhill	Haverhill HS	9-12	1,864	N/A	\$33,739,532	\$33,739,532	68.48%	\$23,104,832	Design/Bid/Build	CTA	Apr-04	Aug-11	Major work on building is complete. Remaining work consists of site and perimeter work which is ongoing. The locker replacement and painting is scheduled for Summer 2011.
Holyoke	Holyoke HS	9-12	1,252	N/A	\$22,738,000	\$15,964,800	90.00%	\$14,368,320	Design/Bid/Build	WJ Mountford	Mar-10	Sep-10	HVAC, windows and ADA upgrades are ongoing with an approximate completion date of September 2010.
Malden	Malden HS	9-12	1,720	365,271	\$77,033,447	\$77,072,181	90.00%	\$69,364,963	CM-R	Gilbane	8-Aug-10	Jun-12	This is a complete renovation of the existing high school. Work has been divided into nine (9) phases. The project is approximately 50 percent complete.
New Bedford	Abraham Lincoln ES	K-5	450	96,000	\$28,072,000	\$17,952,000	90.00%	<b>\$23,494,800</b>	Design/Bid/Build	CTA	1-Jun-09	Dec-10	Substantial completion date for Phase I, the new facility, achieved on schedule, August 16, 2010. Minor punchlist work remaining. FF&E installation complete. Substantial completion for Phase II, existing building demolition, is December 15, 2010. Abatement is complete. Demo of existing building began September 14, 2010.
Newton	Newton North HS	9-12	1,795	375,000	\$197,499,511	\$77,628,610	60.00%	<b>\$46,577,166</b>	CM-R	Dimeo Construction	Feb-08	Aug-10	The permanent certificate of occupancy was received in August. Phase II, demo and abatement of the existing building, has begun.
Quincy	Quincy HS	9-12	1,650	368,000	\$126,766,465	\$80,228,599	90.00%	<b>\$87,205,739</b>	CM-R	Gilbane	Jun-10	Oct-10	Construction has been completed. The school staff began moving into the building in August of this year. Only punch list work needs to be completed.
Revere	Paul Revere ES	K-5	350	57,500	\$17,409,000	\$10,752,500	90.00%	<b>\$16,152,185</b>	Design/Bid/Build	Delulis Brothers	Nov-10	Aug-10	The building has been completed. Furnishings, fixtures and equipment along with students and staff are in the building.
Springfield	Putnam Voc Tech HS	9-12	1,400	315,000	\$125,000,000	\$125,000,000	90.00%	\$112,500,000	CM-R	Consigli	18-May-10	Jul-12	Underslab utilities, footings and foundations are ongoing. Steel erection for Bldg A is scheduled to start on September 27, 2010.
Taunton	Parker MS	5-8	2,350	539,224	\$112,759,827	\$112,759,827	83.00%	\$93,590,656	Design/Bid/Build	Bacon-Agostini	Jul-10	Jan-12	Renovation of the existing High School continues and now stands at approximately 80% complete.
Worcester	North HS	9-12	1,200	239,570	\$72,800,000	\$50,549,270	90.00%	<b>\$60,494,343</b>	CM-R	Gilbane	24-Sep-08	Jul-11	Metal stud framing is 95% complete. Drywall installation is 85% complete. MEP rough-ins and fire suppression systems are ongoing. Interior masonry walls are 95% complete and exterior masonry is underway at the south and north elevations. The overall project is approximately 58% complete.

**Bold and italicized totals include an additional grant/loan amount to the Reimbursement Rate.**
