

# Project Overview Report

## July 28, 2010

Currently there are 197 projects in the capital pipeline. As of this report, 18 projects have been approved for final MSBA approved grants and with the fiscal year end will be removed from future reports. Of the remaining 179 projects, 10 are in Audit, 131 are active new program projects, 13 are active Waitlist projects and 35 are active Green Repair projects.

### Local Vote Authorization

Since the May Board Meeting:


Feasibility Funding Appropriated:

Concord-Carlisle, East Bridgewater, Minuteman Voc Tech  
North Reading, Norton, Somerville, Westfield

Project Funding Appropriated:

Florida, Foxboro, Longmeadow, Methuen, Quabbin  
Regional, Scituate, Uxbridge


Marblehead failed to obtain Authorization and Funding to continue with the Glover ES project, next vote currently scheduled for Fall 2010.

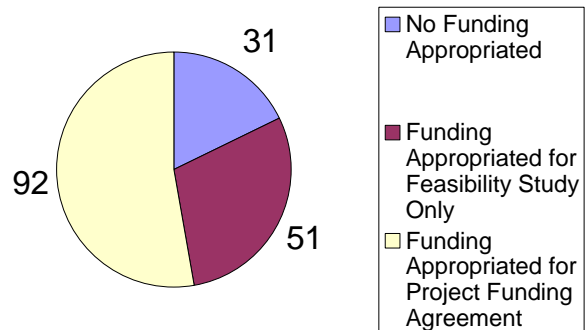

### Design Enrollment

Since the May Board Meeting:


- 4 districts completed prerequisites and are in collaboration with staff
- 4 districts executed enrollment certifications

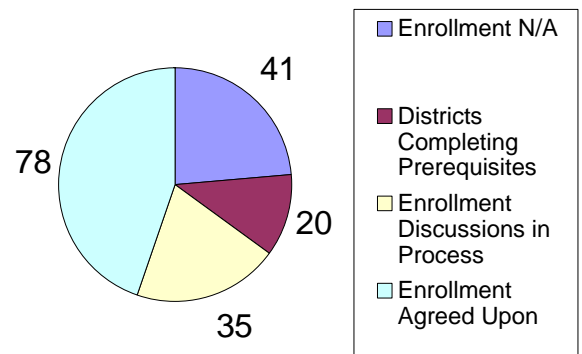

### Owner's Project Managers

Since the May Board Meeting the following Districts have completed the OPM selection process:

- North Adams– Silvio O. Conte MS – Feasibility Study (Strategic Building Solutions)

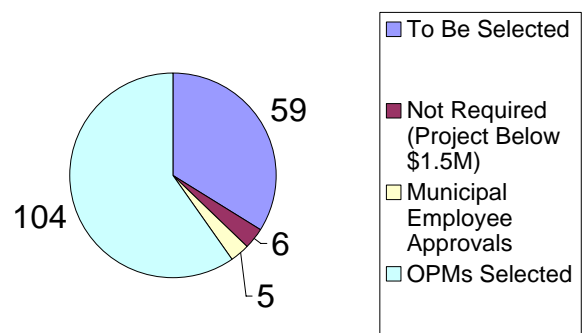

The schedule for the next meeting is shown with the potential of 1 District submitting for approval. Six additional Districts are completing the procurement process and will be scheduled for meetings.


Panel Date	District/School	Project Description Status	Estimated Project Cost
8/2/10	Weston / Field School	Feasibility Status	\$30-\$32 mil
9/13/10	City of Boston/ Quincy Upper School	Feasibility Study	TBD
9/13/10	E. Bridgewater/ HS	Model School	\$60-\$65mil
9/13/10	Lincoln K-8	Feasibility Study	\$30-\$45mil
9/13/10	Norton/ HS	Feasibility Study	\$15-\$20mil
9/13/10	Williamsburg/Helen E. James	Feasibility Study	\$6-\$10 mil
9/13/10	Winthrop/ Winthrop SR HS	Repair	\$10-\$45 mil

### Designers

Since the last Board of Directors Meeting the DSP has met 3 times resulting in 3 additional Districts completing the Designer selection process.

The following District's are tentatively scheduled for upcoming meetings:

- Assabet Valley Reg. Vocational School District– July 27
- Franklin High School Interviews – July 27
- The Southern Worcester County Regional Vocational School District (Baypath Regional Voc.) – September 21

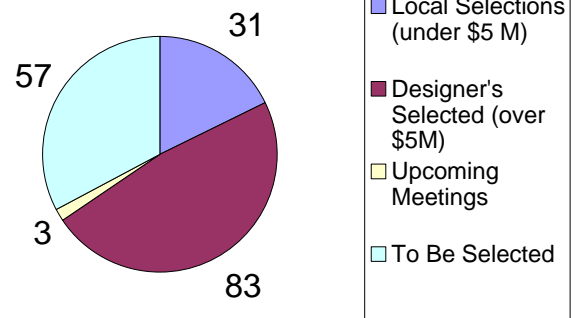

Since the last report to the Board, the Designer Selection Panel has met 3 times.

Panel Date	District/School	Status	Estimated Project Cost	# of Proposals Received	Top 3-Ranked Firms	Interviews Requested	First-Ranked Selection
6/15/2010	Norfolk County – Norfolk County Agricultural High School	Designer Selection	\$12m - \$15m	7	- Turowski2 - DRA - Kaestle Boos	No	Turowski2
6/15/2010	Southwick-Tolland RSD – Woodland ES	Designer Selection	\$10m- \$30m	6	- CGKV - JCJ - Margo Jones	Yes	TBD
6/15/2010	Informational Interviews – XChange Architects						
6/15/2010	Informational Interviews – Studio G Architects						
6/15/2010	Informational Interviews – The Gluck Architectural Collaborative, PC dba Peter Gluck and Partners						
6/29/2010	Southwick-Tolland RSD – Woodland ES	Designer Selection	\$10m- \$30m	6	- CGKV - JCJ - Margo Jones	Interviews Held	JCJ
6/29/2010	MSBA Green Repair Program	N/A	N/A	21	<i>The following firms were pre-qualified:</i> - Baker/Wohl - BLW Engineers - Bradley Architects	No	N/A

Panel Date	District/School	Status	Estimated Project Cost	# of Proposals Received	Top 3-Ranked Firms	Interviews Requested	First-Ranked Selection
					- BVH Integrated Svs - Cannon Design - CGKV Architects - CSS Architects - DiMarinisi & Wolfe - Durland Van Voorhis - Gale Associates - Habeeb & Associates - Hesnor Engineering - ICON architecture - Knight, Bagge & Anderson - LPBA/Architects - Reinhardt Associates - Richard D. Kimball - Russo Barr Associates - SED Associates - Tighe & Bond - Turowski2		
7/13/2010	Franklin PS – Franklin HS	Designer Selection	\$40m - \$60m	9	- CGKV - Design Partnership - Flansburgh - Kaestle Boos	Yes	TBD
7/13/2010	Southeastern RVSD- Southeastern RVTHS	Designer Selection	\$12m - \$20m	6	- DRA - Fletcher Thompson - Mount Vernon Group	No	DRA
7/13/2010	Informational Interviews – Bechtel Frank Erickson Architects, Inc.						
7/13/2010	Informational Interviews – The Robinson Green Beretta Corporation						
7/13/2010	Informational Interviews – Hesnor Engineering Company						

### Commissioning

To date, the MSBA has assigned Commissioning Consultants to thirty-two Districts as follows:

District	School	Estimated Const. Cost (millions)	Commissioning Consultant	Contract Amount
Hanover	Hanover HS	\$49.0	Horizon Engineering Associates, LLP	\$176,039
Marblehead	Village ES	\$15.8	RDK Engineering	\$112,108
Plymouth	Plymouth North HS	\$70.0	Sebesta Blomberg & Associates	\$224,480
Springfield	Putnam Voc. HS	\$100.0	Strategic Building Solutions	\$207,079
Belmont	Wellington ES	\$28.8	Strategic Building Solutions	\$90,149
Foxborough	Foxborough HS	\$16.3	Consulting Engineering Services, LLC	\$155,300
Littleton	Russell Street ES	\$11.0	WSP Flack + Kurtz	\$102,250
Middleton	Howe-Manning ES	\$24.0	Foreman Building Commissioning, LP	\$102,576
Wellesley	Wellesley HS	\$130.0	RFS Engineering	\$228,700
Brookline	John D Runkle K-8	\$22.5	Consulting Engineering Services, LLC	\$109,260

<b>District</b>	<b>School</b>	<b>Estimated Const. Cost (millions)</b>	<b>Commissioning Consultant</b>	<b>Contract Amount</b>
Burlington	Memorial ES	\$28.0	Consulting Engineering Services, LLC	\$74,500
Danvers PS	Danvers HS	\$62.7	Turner Facilities Management Solutions	\$185,278
Needham	Newman ES	\$21.9	RFS Engineering	\$93,530
Wayland	Wayland HS	\$59.7	WSP Flack + Kurtz	\$166,600
Hampden-Wilbraham	Minnechaug Reg HS	\$66.5	Horizon Engineering Associates, LLP	\$179,200
Woburn PS	Goodyear ES	\$19.9	Strategic Building Solutions	\$92,679
Nashoba PS	Pompositticut Primary	\$31.1	Strategic Building Solutions	\$119,052
Rochester PS	Rochester Mem. ES	\$26.5	Horizon Engineering Associates, LLP	\$104,870
Rockland PS	John W Rogers MS	\$66.5	Consulting Engineering Services, LLC	\$237,300
Natick PS	Natick HS	\$72.5	RFS Engineering	\$205,500
Sturbridge PS	Burgess ES	\$36.5	Horizon Engineering Associates, LLP	\$98,400
Billerica PS	Parker ES	\$27.0	Sebesta Blomberg & Associates	\$88,129
New Bedford PS	Abraham Lincoln	\$21.0	Sebesta Blomberg & Associates	\$90,800
Sharon PS	Sharon MS	\$35.8	Horizon Engineering Associates, LLP	\$126,900
Dedham PS	Avery ES	\$17.9	WSP Flack + Kurtz	\$69,750
Norfolk PS	Freeman-Centennial IS	\$28.9	WSP Flack + Kurtz	\$91,000
Grafton PS	Grafton Memorial SHS	\$57.4	Horizon Engineering Associates, LLP	\$155,800
Southbridge PS	Southbridge HS	\$60.1	Environmental Health & Engineering	\$219,800
Hamilton-Wenham PS	Cutler ES	\$1.2	Sebesta Blomberg & Associates	\$38,600
Carlisle PS	Carlisle K-8	\$15.6	Horizon Engineering Associates, LLP	\$107,130
Tewksbury PS	Tewksbury Memorial HS	\$65.9	Sebesta Blomberg & Associates	\$158,700
Shrewsbury PS	Sherwood MS	\$37.0	RDK Engineering	\$114,825
<b>Total</b>	<b>32</b>	<b>\$1,327.0</b>	<b>Total</b>	<b>\$4,326,284</b>

Projects for which we are currently seeking proposals and/or negotiating Work Orders include:

<b>District</b>	<b>School</b>	<b>Responses Received</b>
Mount Greylock PS	Mt Greylock Reg. HS	6/7/2010
Easthampton PS	Easthampton HS	6/7/2010
Longmeadow PS	Longmeadow HS	6/11/2010
Berlin-Boylston PS	Tahanto Reg HS	6/25/2010
Sutton PS	Sutton MS	6/25/2010

Projects that are currently in the queue for assignment and for which RFP documents are being drafted include:

<b>District</b>	<b>School</b>
Methuen PS	Methuen HS
Leominster PS	Leominster SHS
Andover PS	Bancroft ES

<b>District</b>	<b>School</b>
Burlington PS	Marshall Simonds MS
Uxbridge PS	Uxbridge HS

Attached to the Project Status report are the following:

- Master District Status List
- Capital Pipeline Status Chart - As indicated in the attached chart, Districts continue to make progress with their projects. The narrow solid bar indicates the number of Districts in each category as reported at the May Board meeting.
- Estimated Bid Dates
- Construction Status Report



# Massachusetts School Building Authority

No. of Projects: 174

## Master District Status List

Yellow = Wait List Project

Grey = Complete

Red = Changes in last 60 days

District Name	School Name	Status	Preferred Schematic	OPM	Designer	Cx Authority	Procurement Status	CM/GC
Abington PS	Frolio JHS	Local Clearance - 07/08						
Acton PS	Luther Conant ES	Complete	Repair		Universal Environmental Consultants		DBB - Contract Awarded	E.Amanti & Sons Inc.
Adams-Cheshire PS	Adams MS	Preferred Schematic		URS Corporation	Tessier Associates		Undetermined	
Andover PS	Bancroft ES	Preferred Schematic	New Construction	Town of Andover	Symmes Maini & McKee Associates			
Arlington PS	Thompson ES	Feasibility Study		PMA Consultants	HMFH Architects, Inc.			
Ashburnham-West PS	Briggs ES	Preferred Schematic		STV, Inc.	Lamoureux Pagano & Associates, Inc.			
Ashland PS	David Mindess IS	Construction		Heery International, Inc	Gale Associates, Inc.			
Assabet Valley PS	Assabet Valley Voc HS	Designer Selection		Strategic Building Solutions, LLC				
Athol-Royalston PS	Riverbend ES	Local Clearance - Repair - 09						
Attleboro PS	Attleboro HS	Complete	Repair	Skanska USA Building Inc.	Russo Barr Associates, Inc.		DBB - Contract Awarded	Gibson Roofs, Inc.
Auburn PS	Auburn MS	Local Clearance - 07/08						
Avon PS	Ralph D Butler ES	Closeout/Audit	Repair		Richard D. Kimball Company, Inc.		Undetermined	Automaitic Temperature Controls Inc.
Ayer PS	Ayer HS	Local Clearance - 09/10						
Bedford PS	Bedford HS	Closeout/Audit		Peter Cox	Symmes Maini & McKee Associates		DBB - Contract Awarded	Brait Builders Construction
Belmont PS	Roger E Wellington ES	Construction	New Construction	PMA Consultants	Jonathan Levi Architects LLC	Strategic Building Solutions	CMR - CM Selected	Skanska USA Building, Inc.
Berlin-Boylston PS	Tahanto Reg HS	Design Development	New Construction	PMA Consultants	HMFH Architects, Inc.			
Beverly PS	Beverly HS	Construction		Heery International	Mount Vernon Group Architects, Inc.		DBB - Contract Awarded	CTA Construction Co.
Billerica PS	Parker ES	Design Development	New Construction	Joslin, Lesser & Associates, Inc.	Symmes Maini & McKee Associates	Sebesta Blomberg & Associates	Undetermined	
Blue Hills Voc PS	Blue Hills Regional Voc / Tech HS	Complete	Repair		Habeeb & Associates Inc.		DBB - Contract Awarded	Silktown Roofing Inc.
Boston PS	Quincy Upper School	Local Clearance - 09/10						
Boston PS	Dearborn MS	Local Clearance - 09/10						
Braintree PS	South MS	Construction	Repair	Town Employee	Habeeb & Associates Architects, Inc.		DBB - Contract Awarded	Construction Dynamics
Brookline PS	Heath K-8	Local Clearance - 09/10						

# Master District Status List

Yellow = Wait List Project

Grey = Complete

Red = Changes in last 60 days

District Name	School Name	Status	Preferred Schematic	OPM	Designer	Cx Authority	Procurement Status	CM/GC
Brookline PS	John D Runkle K-8	Design Development	Addition/Renovation	Town of Brookline Building Department	Design Partnership of Cambridge, Inc.	Consulting Engineering Services, LLC	Undetermined	
Burlington PS	Marshall Simonds MS	Design Development	Addition/Renovation		Knight, Bagge & Anderson, Inc.			
Burlington PS	Memorial ES	Construction	New Construction	Construction Monitoring Services, Inc.	Knight, Bagge & Anderson, Inc.	Consulting Engineering Services, LLC	CMR - CM Selected	CTA Construction Co. Inc.
Cambridge PS	Cambridge Rindge and Latin HS	Closeout/Audit			HMFH Architects, Inc.		Undetermined	W.T. Rich, Inc.
Carlisle PS	Carlisle K-8	Design Development	Addition/Renovation	Daedalus Projects, Inc.	HMFH Architects, Inc.	Horizon Engineering Associates, LLP	DBB - In Design	
Carver PS	Gov John Carver ES	Removed from Capital Pipeline	Addition/Renovation	Daedalus Projects, Inc.	Design Partnership of Cambridge, Inc.			N/A
Chelmsford PS	McCarthy MS	Closeout/Audit					DBB - Contract Awarded	Multiple
Chelmsford PS	Chelmsford HS	Complete		Turner	Flansburgh Associates, Inc.		DBB - Contract Awarded	TLT Construction
Chelsea PS	Clark Avenue MS	Local Clearance - 07/08			Jacobs			
Chicopee PS	Chicopee Academy	Local Clearance - 09/10						
Concord PS	Thoreau ES	Complete		Construction Monitoring Services, Inc.	Symmes Maini & McKee Associates		DBB - Contract Awarded	J&J Contractors Inc.
Concord-Carlisle PS	Concord Carlisle HS	Local Clearance - Repair - 09						
Danvers PS	Danvers HS	Construction	Addition/Renovation	Construction Monitoring Services, Inc.	DiNisco Design Partnership, Limited	Turner Facilities Management Solutions	DBB - In Design	
Dartmouth PS	James M. Quinn ES	Construction			Russo Barr Associates, Inc.			
Dedham PS	Avery ES	Design Development	New Construction	Construction Monitoring Services, Inc.	Dore & Whittier Architects, Inc.	WSP Flack + Kurtz	CMR - Procurement Pending	Consigli
Douglas PS	Douglas IS	Feasibility Study		Heery International, Inc	DiNisco Design Partnership, Limited			
Dracut PS	Dracut SHS	Feasibility Study		RF Walsh Collaborative Partners	Mount Vernon Group Architects, Inc.		Undetermined	
Duxbury PS	Chandler ES	Closeout/Audit	Repair	N/A	Gale Associates, Inc.		DBB - Contract Awarded	Built-up Roofing Systems LLC
East Bridgewater PS	East Bridgewater HS	OPM Selection	Model School					
East Longmeadow PS	Meadow Brook Primary	Complete		N/A	N/A		DBB - Contract Awarded	Multiple
Easthampton PS	Easthampton HS	Design Development	New Construction	Strategic Building Solutions, LLC	Caolo & Bieniek Associates, Inc.		Undetermined	
Essex North Shore Agr and Tech PS	Essex North Shore Agr and Tech School	Design Development	New Construction	PMA Consultants				
Fairhaven PS	Rogers ES	Feasibility Study		Daedalus Projects Inc	HMFH Architects, Inc.			
Fall River PS	Morton MS	Local Clearance - 09/10						
Falmouth PS	Falmouth High School	Construction	Addition/Renovation	Gilbane Building Company	DiNisco Design Partnership, Limited		DBB - Contract Awarded	TLT Construction
Fitchburg PS	Crocker ES	OPM Selection						

# Master District Status List

Yellow = Wait List Project	
Grey = Complete	Red = Changes in last 60 days

District Name	School Name	Status	Preferred Schematic	OPM	Designer	Cx Authority	Procurement Status	CM/GC
Florida PS	Abbott Memorial K-8	Construction	Repair		Dietz and Company		DBB - Contract Awarded	Waterman Excavating, Inc
Foxborough PS	Foxborough HS	Construction	Repair	Construction Monitoring Services, Inc.	Kaestle Boos Associates, Inc.	Consulting Engineering Services, LLC	DBB - Contract Awarded	CTA Construction Co.
Franklin PS	Franklin HS	Feasibility Study		Daedalus Projects Inc.				
Gardner PS	Waterford Street Primary	Local Clearance - 07/08						
Georgetown PS	Penn Brook IS	Local Clearance - 09/10						
Gloucester PS	West Parish ES	Local Clearance - 09/10						
Grafton PS	Grafton Memorial SHS	Design Development	New Construction	Joslin, Lesser & Associates, Inc.	Symmes Maini & McKee Associates	Horizon Engineering Associates, LLP	CMR - CM Selected	Dimeo Construction
Granby PS	Granby JHS / SHS	Preferred Schematic	New Construction	Skanska USA Building Inc.	Dore & Whittier Architects, Inc.			
Greater Lowell Voc Tec PS	Gr Lowell Regional Voc / Tech HS	OPM Selection						
Greenfield PS	Greenfield HS	Local Clearance - Repair - 09						
Hadley PS	Hopkins Academy	Closeout/Audit			Kaestle Boos Associates, Inc.			
Hamilton-Wenham PS	Cutler ES	Construction	Repair	Municipal Building Consultants, Inc.	Richard D. Kimball Company, Inc.	Sebesta Blomberg & Associates	DBB - Contract Awarded	Thomas E. Snowden Inc.
Hampden-Wilbraham PS	Minnechaug Reg HS	Design Development	Model School	ARCADIS U.S., Inc.	Mount Vernon Group Architects, Inc.	Horizon Engineering Associates, LLP	DBB - Out to Bid	
Hancock PS	Hancock ES	Local Clearance - 09/10						
Hanover PS	Hanover HS	Construction	New Construction	PMA Consultants	HMFH Architects, Inc.	Horizon Engineering Associates, LLP	DBB - Contract Awarded	Callahan, Inc
Haverhill PS	Haverhill HS	Construction						
Hingham PS	New Elementary School	Closeout/Audit	New Construction	Knight, Bagge & Anderson, Inc.	Ai3 Architects LLC		DBB - Contract Awarded	CTA Construction Co.
Holbrook PS	Holbrook JHS / SHS	OPM Selection						
Holyoke PS	Holyoke HS	Construction			Design Partnership of Cambridge, Inc.			
Hopedale PS	Memorial ES	Closeout/Audit	Repair		Gale Associates, Inc.		Undetermined	Greenwood Industries Inc.
Hopkinton PS	Center ES	Preferred Schematic		Town of Hopkinton	Design Partnership of Cambridge, Inc.		Undetermined	
Hudson PS	John F Kennedy MS	Preferred Schematic	New Construction	PMA Consultants	The Office of Michael Rosenfeld, Inc.			
Lakeville PS	Assawompset ES	Complete	Repair				DBB - Contract Awarded	KPR Inc.
Leicester PS	Leicester Primary	Complete	Repair		Nault Architects		DBB - Contract Awarded	Rockwell Roofing Inc.
Leominster PS	Leominster SHS	Approved Project Vote Pending	Addition/Renovation	Daedalus Projects, Inc.	Lamoureux Pagano & Associates, Inc.			
Lincoln PS	Lincoln K-8	OPM Selection						



# Master District Status List

Yellow = Wait List Project

Grey = Complete

Red = Changes in last 60 days

District Name	School Name	Status	Preferred Schematic	OPM	Designer	Cx Authority	Procurement Status	CM/GC
Littleton PS	Russell St ES	Construction	Repair	Daedalus Projects, Inc.	Drumme Rosane Anderson, Inc.	WSP Flack + Kurtz	DBB - Contract Awarded	Colantonio, Inc.
Longmeadow PS	Longmeadow HS	Design Development	New Construction	Joslin, Lesser & Associates, Inc.	The Office of Michael Rosenfeld, Inc.		CMR - Procurement Pending	
Lowell PS	Charles W Morey ES	Closeout/Audit		Watermark			Undetermined	CTA Construction Co.
Lunenburg PS	Lunenburg HS	Local Clearance - 09/10						
Lynn PS	Thurgood Marshall MS	Local Clearance - 09/10						
Lynnfield PS	Lynnfield HS	Local Clearance - 09/10						
Malden PS	Malden HS	Construction	Renovation	URS Corporation	Flansburgh Associates, Inc.		CMR - CM Selected	Gilbane Building Company
Manchester Essex Regional PS	Manchester JHS / SHS	Closeout/Audit		Design Technique	Mount Vernon Group Architects, Inc.		Undetermined	TLT Construction
Marblehead PS	Glover Primary	Preferred Schematic	New Construction	Municipal Building Consultants, Inc.	JCJ Architecture + Interiors, PC		Undetermined	
Marblehead PS	Village IS	Construction	Repair	Municipal Building Consultants, Inc.	Symmes Maini & McKee Associates	RDK Engineering	DBB - Contract Awarded	Groom Construction
Marshfield PS	Gov Edward Winslow ES	Design Development	Repair	Vertex Construction Services	Knight, Bagge & Anderson, Inc.			
Maynard PS	Maynard HS	Preferred Schematic		Municipal Building Consultants, Inc.	Tappe Associates, Inc.		Undetermined	
Medford PS	Medford HS	Complete					DBB - Contract Awarded	
Medway PS	Medway MS	Feasibility Study		Compass Project Management, Inc.	Knight, Bagge & Anderson, Inc.			
Methuen PS	Methuen HS	Design Development	Addition/Renovation	KBA/Trident	Finegold Alexander and Associates, Inc.		Undetermined	
Middleton PS	Howe-Manning IS	Construction	New Construction	RF Walsh Collaborative Partners	DiNisco Design Partnership, Limited	Foreman Building Commissioning, LP	DBB - Contract Awarded	CTA Construction Co.
Milford PS	Stacy MS	Complete					DBB - Contract Awarded	Chapman Waterproofing Company
Minuteman Voc Tech PS	Minuteman Reg HS	Local Clearance - 09/10						
Mount Greylock PS	Mt Greylock Reg HS	Construction	Repair	N/A	Hesnor Engineering & Barry Architects	Horizon Engineering Associates, LLP	DBB - Contract Awarded	Adams Plumbing & Heating
Narragansett PS	Templeton Center	Feasibility Study		Strategic Building Solutions, LLC	Symmes Maini & McKee Associates		Undetermined	
Nashoba PS	Pompositicut Primary	Construction	Addition/Renovation	Construction Monitoring Services, Inc.	Symmes Maini & McKee Associates	Strategic Building Solutions	DBB - Contract Awarded	Stella P.J. Construction Corp.
Natick PS	Natick HS	Design Development		RF Walsh Collaborative Partners	Ai3 Architects LLC	RFS Engineering	DBB - In Design	
Needham PS	Newman ES	Design Development	Repair	Town of Needham	Drumme Rosane Anderson, Inc.	RFS Engineering	CMR - IG Application Pending	
New Bedford PS	Abraham Lincoln	Construction	New Construction	Daedalus Projects Inc	Mount Vernon Group Architects, Inc.	Sebesta Blomberg & Associates	DBB - Contract Awarded	CTA Construction Co.
New Bedford PS	Elizabeth Carter Brooks ES	Feasibility Study						
New Bedford PS	John Hannigan ES	Local Clearance - 09/10						

# Master District Status List

Yellow = Wait List Project

Grey = Complete

Red = Changes in last 60 days

District Name	School Name	Status	Preferred Schematic	OPM	Designer	Cx Authority	Procurement Status	CM/GC
Newburyport PS	Rupert A Nock MS	Local Clearance - 09/10						
Newton PS	Newton North HS	Construction		Turner Construction Company	Dore & Whittier Architects, Inc.		CMR - CM Selected	Dimeo Construction
Norfolk County Agr PS	Norfolk County Agr HS	Feasibility Study		Compass Project Management, Inc	Turowski2 Architecture, Inc.			
Norfolk PS	Freeman-Centennial IS	Design Development	New Construction	Joslin, Lesser & Associates, Inc.	Flansburgh Associates, Inc.	WSP Flack + Kurtz	DBB - In Design	
North Adams PS	Silvio O Conte MS	Designer Selection		Strategic Building Solutions, LLC				
North Attleborough PS	Joseph W Martin Jr ES	Construction			CBI Consultants, Inc.		Undetermined	Eagle Rivet Roof Services Corporation
North Reading PS	North Reading HS	Local Clearance - 09/10						
North Reading PS	L D Batchelder ES	Complete			Tappe Associates, Inc.		DBB - Contract Awarded	GVW, Inc.
Northampton-Smith PS	Smith Vocational and Agricultural HS	Local Clearance - 09/10						
Northborough PS	Lincoln Street ES	Complete					DBB - Contract Awarded	Wayne Roofing Inc.
Northeast Metro Voc PS	Northeast Metro Reg Voc HS	Local Clearance - 09/10						
Norton PS	Norton HS	OPM Selection						
Norwood PS	Norwood HS	Construction	Model School	Compass Project Management, Inc.	Ai3 Architects LLC		DBB - Contract Awarded	Agostini Construction Company, Inc.
Old Colony Reg Voc Tech PS	Old Colony Regional Voc / Tech HS	Local Clearance - 09/10						
Orange PS	Dexter Park IS	Local Clearance - 09/10						
Oxford PS	Oxford MS	OPM Selection						
Peabody PS	J Henry Higgins MS	OPM Selection						
Pittsfield PS	Taconic HS	OPM Selection						
Plymouth PS	Plymouth North HS	Construction	Model School	Ted Gentry Associates	Ai3 Architects LLC	Sebesta Blomberg & Associates	DBB - Contract Awarded	J&J Contractors Inc.
Quabbin PS	Oakham Center ES	Design Development	Repair		Russo Barr Associates, Inc.			
Quincy PS	Central MS	Feasibility Study		Tishman Construction Corporation of MA	Ai3 Architects LLC			
Quincy PS	Quincy High School	Construction	New Construction	Tishman Construction Corporation of MA	Symmes Maini & McKee Associates		CMR - CM Selected	Gilbane Building Company
Randolph PS	Martin E Young ES	Complete	Repair		CBI Consultants, Inc.		DBB - Contract Awarded	Gibson Roofs Inc
Revere PS	Paul Revere ES	Construction	New Construction	RF Walsh Collaborative Partners	Drumrey Rosane Anderson, Inc.		DBB - Contract Awarded	Delulis Brothers Construction Company
Rochester PS	Rochester Memorial ES	Construction	Addition/Renovation	PMA Consultants	Flansburgh Associates, Inc.	Horizon Engineering Associates, LLP	CMR - CM Selected	Gilbane Building Company
Rockland PS	John W Rogers MS	Design Development	Addition/Renovation	Daedalus Projects Inc	Dore & Whittier Architects, Inc.	Consulting Engineering Services, LLC	CMR - CM Selected	Agostini Construction Company, Inc.

# Master District Status List

Yellow = Wait List Project	
Grey = Complete	Red = Changes in last 60 days


District Name	School Name	Status	Preferred Schematic	OPM	Designer	Cx Authority	Procurement Status	CM/GC
Rockport PS	Rockport HS	Construction			Russo Barr Associates, Inc.		Undetermined	Feeley, McAnespie, Inc.
Salem PS	Collins MS	Local Clearance - Repair - 09						
Sandwich PS	Oak Ridge K-8	Local Clearance - Repair - 09						
Saugus PS	Belmonte Saugus MS	Local Clearance - 09/10						
Scituate PS	Wampatuck ES	OPM Selection						
Sharon PS	Sharon MS	Construction	Addition/Renovation	Daedalus Projects, Inc.	Kaestle Boos Associates, Inc.	Horizon Engineering Associates, LLP	CMR - CM Selected	Consigli Construction
Shawsheen Valley Voc PS	Shawsheen Valley Voc / Tech HS	Complete			Knight, Bagge & Anderson, Inc.		DBB - Contract Awarded	Gibson Roofs, Inc.
Shawsheen Valley Voc PS	Shawsheen Valley Voc / Tech HS	Approved Project Vote Pending			Knight, Bagge & Anderson, Inc.		Undetermined	Gibson Roofs Inc
Sherborn PS	Pine Hill ES	Complete					DBB - Contract Awarded	
Shrewsbury PS	Sherwood MS	Design Development	New Construction	PMA Consultants	Lamoureux Pagano & Associates, Inc.	RDK Engineering	CMR - CM Selected	Gilbane Building Company
Somerset PS	Somerset HS	Local Clearance - 09/10						
Somerville PS	E Somerville Community K-8	Preferred Schematic	Renovation	City of Somerville	Maguire Group Inc.			
South Hadley PS	Plains ES	Local Clearance - 09/10						
South Shore Reg Voc PS	South Shore Voc / Tech HS	Design Development		Lincoln Consultants	Gale Associates, Inc.			
Southbridge PS	Southbridge HS	Design Development	New Construction	Joslin, Lesser & Associates, Inc.	Tappe Associates, Inc.	Environmental Health and Engineering	CMR - CM Selected	Consigli Construction
Southeastern Reg Voc Tech PS	Southeastern Regional Voc / Tech HS	Feasibility Study		RF Walsh Collaborative Partners	Drumme Rosane Anderson, Inc.			
Southern Worcester Cty VT PS	Bay Path Regional Voc / Tech HS	Designer Selection		Heery International, Inc				
Southwick-Tolland	Woodland ES	Feasibility Study		Strategic Building Solutions, LLC	JCJ Architecture + Interiors, PC			
Spencer-E Brookfield PS	David Prouty HS	Local Clearance - Repair - 09						
Springfield PS	Putnam Voc / Tech HS	Construction	New Construction	ARCADIS	Drumme Rosane Anderson, Inc.	Strategic Building Solutions	CMR - CM Selected	Consigli Construction
Springfield PS	Forest Park Middle School	Preferred Schematic	Addition/Renovation	ARCADIS-U.S., Inc.				
Springfield PS	SCIPP	Construction	Repair					
Stoneham PS	Stoneham MS	OPM Selection						
Sturbridge PS	Burgess ES	Design Development	Addition/Renovation	Lamoureux Pagano & Associates, Inc.	Drumme Rosane Anderson, Inc.	Horizon Engineering Associates, LLP	DBB - In Design	
Sutton PS	Sutton MS	Design Development	Addition/Renovation	Strategic Building Solutions	Flansburgh Associates, Inc.			
Taunton PS	Taunton HS	Construction	Addition/Renovation	Gilbane	Design Partnership of Cambridge, Inc.		DBB - Contract Awarded	Bacon-Agostini Construction Joint Venture

# Master District Status List

Yellow = Wait List Project	
Grey = Complete	Red = Changes in last 60 days

District Name	School Name	Status	Preferred Schematic	OPM	Designer	Cx Authority	Procurement Status	CM/GC
Tewksbury PS	Tewksbury Memorial HS	Design Development	Model School	Heery International, Inc	Symmes Maini & McKee Associates	Sebesta Blomberg & Associates	DBB - In Design	
Tyngsborough PS	Tyngsborough ECC	Complete			LPBA Architects		DBB - Contract Awarded	Gibson Roofs Inc.
Uxbridge PS	Uxbridge HS	Project Scope & Budget	New Construction	Joslin, Lesser & Associates, Inc.	Raymond Design Associates, Inc.		Undetermined	
Wachusett PS	Mountview MS	Local Clearance - 09/10						
Wayland PS	Wayland HS	Design Development	New Construction	KV Associates	HMFH Architects, Inc.	WSP Flack + Kurtz	CMR - CM Selected	Shawmut Construction
Webster PS	Park Avenue ES	Local Clearance - 09/10						
Wellesley PS	Wellesley SHS	Construction	New Construction	Ryegate Inc	Symmes Maini & McKee Associates	RFS Engineering	CMR - CM Selected	Turner Construction
West Bridgewater PS	Rose L Macdonald ES	Complete			Russo Barr			Wayne Roofing Inc.
West Springfield PS	West Springfield HS	Local Clearance - 09/10	Model School					
Westborough PS	Sarah W Gibbons MS	Local Clearance - Repair - 09						
Westfield PS	Abner Gibbs ES	Local Clearance - 09/10						
Weston PS	Field ES School	OPM Selection						
Whitman-Hanson PS	Maquan ES	Local Clearance - 09/10						
Whittier Voc PS	Whittier Reg Voc HS	Construction		Heery International	Gale Associates, Inc.			
Williamsburg PS	Anne T Dunphy IS	OPM Selection						
Wilmington PS	Wilmington HS	OPM Selection						
Winchester PS	Vinson-Owen ES	Preferred Schematic		RF Walsh Collaborative Partners	Tappe Associates, Inc.		Undetermined	
Winchester PS	Winchester HS	Local Clearance - 09/10						
Winthrop PS	Winthrop Senior High	OPM Selection						
Woburn PS	Goodyear ES	Construction	New Construction	Municipal Building Consultants, Inc.	Tappe Associates, Inc.	Strategic Building Solutions	CMR - CM Selected	Gilbane Building Company
Worcester PS	North HS	Construction		Maguire Group Inc	City of Worcester		CMR - CM Selected	Gilbane Building Company

**No. of Projects: 174**

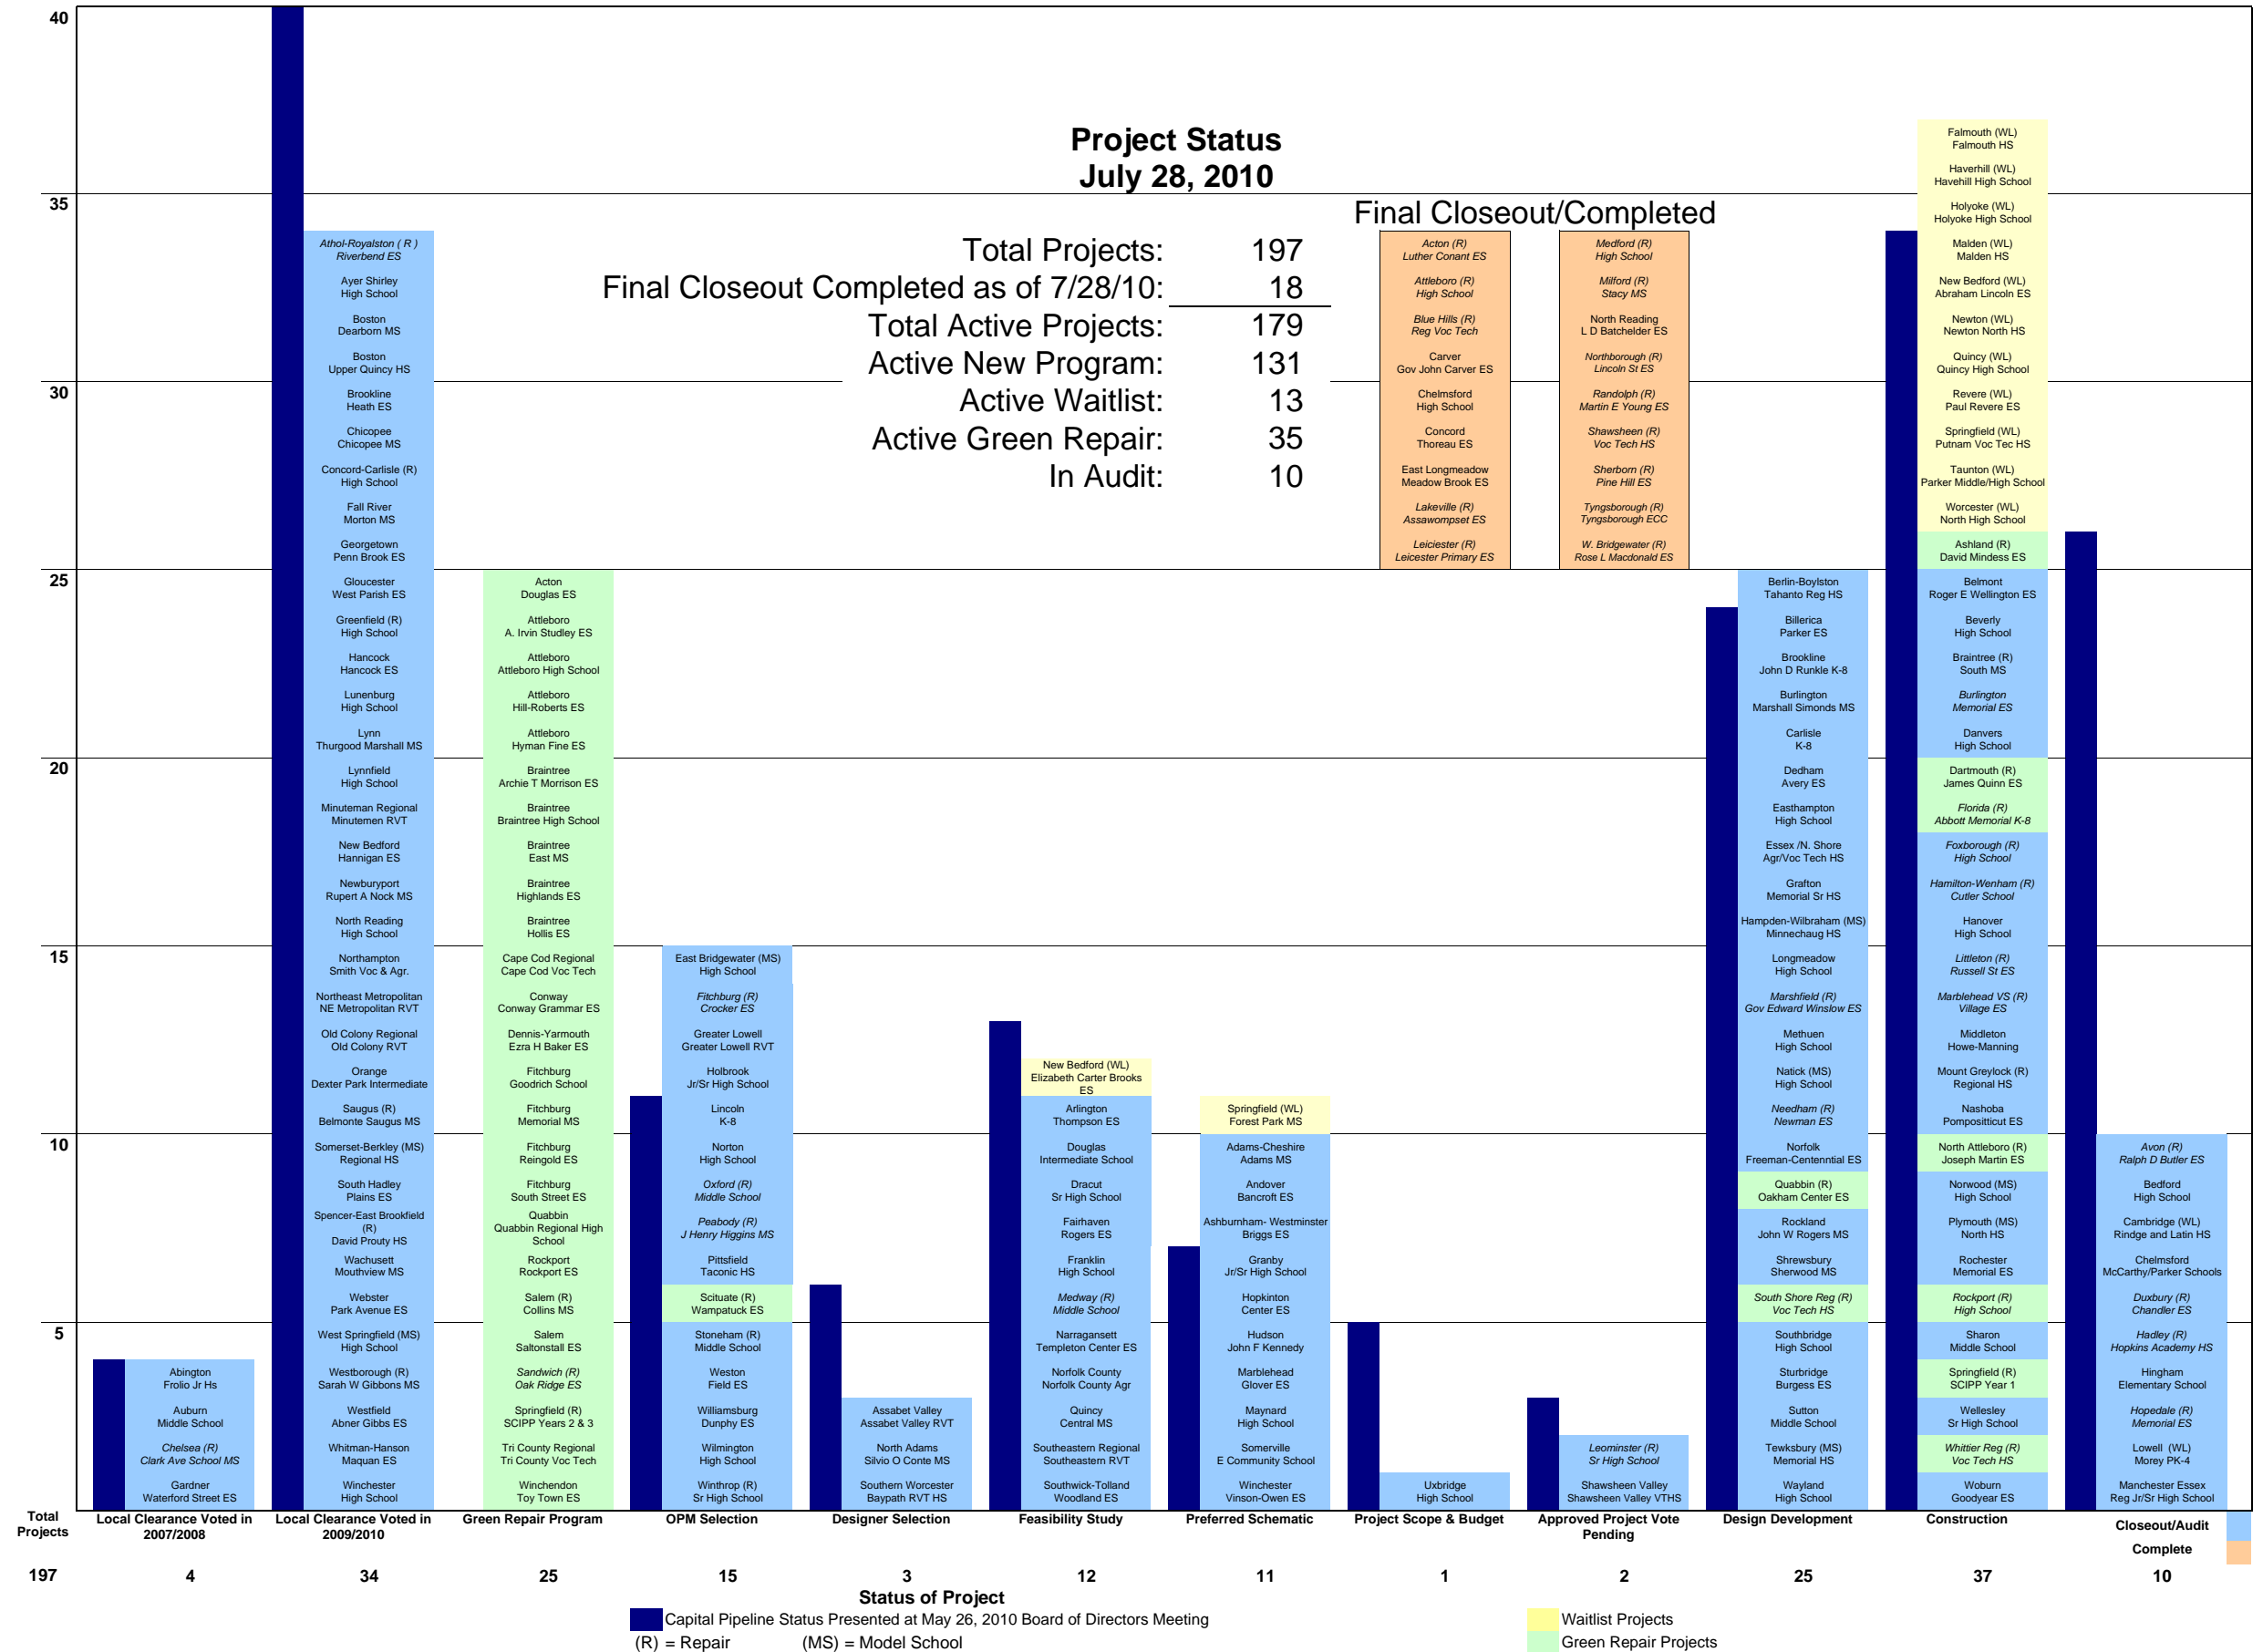

### 2010 Estimated Bid Dates

Note bid dates are **Estimates ONLY**. Please contact Districts for exact information.

Total Project Budget denotes total District costs and does not denote the basis of the MSBA Total Facilities Grant.

- Denotes bid phase in progress or complete
  - Denotes estimated bid dates

DISTRICT	DESIGN BASIS FOR ENROLLMENT	PROJECT BUDGET <small>Shown in Millions</small>	CONSTRUCTION BUDGET <small>Shown in Millions</small>	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC
<b>BURLINGTON</b>	500	\$27.1	\$22.2	Memorial ES New Construction: GC Bids rcv'd 1/28. NTP Issued 2/18.											
<b>*WELLESLEY</b>	1500	\$132.0	\$98.5	Senior HS New Construction: Filed-Sub Bids rcv'd 2/8, 2/9, 2/10. GMP Issued 3/25.											
<b>*WOBURN</b>	320	\$26.5	\$19.9	Goodyear ES New Construction: Filed-Sub Bids rcv'd 3/11. GMP Issued 3/24.											
<b>*SPRINGFIELD</b>	1440	\$125.0	\$101.5	Putnam Vo-Tech New Construction: Filed-Sub Bids rcv'd 3/11. GMP Issued 5/3.											
<b>MIDDLETON</b>	553	\$31.3	\$24.3	Howe-Manning ES New Construction: Filed-Sub Bids rcv'd 3/10. G.C. Bids rcv'd 3/26. NTP Issued 4/5.											
<b>PLYMOUTH</b>	1350	\$92.2	\$72.0	North HS New Construction: Filed Sub-Bids rcv'd 3/4. G.C. Bids rcv'd 3/30. NTP Issued 4/28.											
<b>*BELMONT</b>	575	\$40.0	\$28.7	Wellington ES New Construction: Filed Sub-Bids rcv'd 5/11. Non-Trade Bids rcv'd 5/20. GMP Targeted July.											
<b>*ROCHESTER</b>	635	\$26.5	\$20.5	Memorial ES Addition / Renovation: Filed Sub-Bids rcv'd 5/5. GMP Targeted July.											
<b>HAMPDEN-WILBRAHAM</b>	1225	\$78.9	\$66.4	Minnechaug HS New Construction: Filed-Sub Bids rcv'd 6/15. G.C. Bids rcv'd 7/20. NTP Targeted August.											
<b>HAMILTON-WENHAM</b>	300	\$1.5	\$1.2	Cutler ES Repair: Filed-Sub Bids rcv'd 3/30. G.C. Bids rcv'd 4/8. NTP Issued 4/16.											
<b>*SHARON</b>	845	\$49.5	\$34.7	Middle School Addition / Renovation: Early Release Bid Package rcv'd 5/17. Filed-Sub Bids rcv'd 5/18. GMP Targeted July.											
<b>ASHLAND</b>	596	\$3.1	\$2.6	David Mindess ES Repair: Filed-Sub Bids rcv'd 4/26. G.C. Bids rcv'd 5/3. NTP issued 6/17.											
<b>DARTMOUTH</b>	845	\$1.3	\$1.1	James Quinn ES Repair: G.C. Bids rcv'd 2/25. NTP Issued 3/31.											
<b>N. ATTLEBORO</b>	717	\$0.8	\$0.7	Joseph Martin ES Repair: Filed-Sub Bids rcv'd 4/23. NTP Issued 6/4.											
<b>ROCKPORT</b>	331	\$1.1	\$1.0	Rockport HS Repair: G.C. Bids rcv'd 2/26. NTP Issued 3/17.											
<b>MT GREYLOCK</b>	641	\$1.4	\$1.2	MT Greylock Regional H.S Repair: Filed-Sub Bids rcv'd 4/29. G.C. Bids rcv'd 5/6. NTP Issued 5/6.											
<b>WHITTIER REGIONAL</b>	1206	\$3.2	\$2.6	Regional VTHS Repair: Filed-Sub Bids rcv'd 3/31. G.C. Bids rcv'd 4/7. NTP Issued 5/19.											
<b>Subtotal</b>	<b>13,579</b>	<b>\$641.4</b>	<b>\$499.1</b>												

## 2010 Estimated Bid Dates

Note bid dates are **Estimates ONLY**. Please contact Districts for exact information.

Total Project Budget denotes total District costs and does not denote the basis of the MSBA Total Facilities Grant.

- Denotes bid phase in progress or complete
  - Denotes estimated bid dates

DISTRICT	DESIGN BASIS FOR ENROLLMENT	PROJECT BUDGET <small>Shown in Millions</small>	CONSTRUCTION BUDGET <small>Shown in Millions</small>	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC	
<small>*Projects Considering the CM @ Risk Method</small>																
<b>*WAYLAND</b>	900	\$70.8	\$56.2													Wayland HS New Construction: Early Bid Packages rcv'd 6/30, Add'l Packages Due August. Filed-Sub Bids Targeted September. GMP Targeted October.
<b>NATICK</b>	1300	\$89.0	\$70.8													Natick HS New Construction: Filed-Sub Bids Due 8/18. G.C. Bids Due 9/1. NTP Targeted September.
<b>NASHOBA</b>	600	\$37.8	\$28.8													Pompositticut ES Addition / Renovation: Filed-Sub Bids rcv'd 5/24. G.C. Bids rcv'd 6/7. NTP Issued 6/15.
<b>STURBRIDGE</b>	860	\$46.9	\$36.4													Burgess ES Addition/Renovation: Filed-Sub Bids rcv'd 7/14. G.C. Bids Due 7/27. NTP Targeted August.
<b>NORFOLK</b>	585	\$37.5	\$28.9													Freeman-Centennial ES New Construction: Filed-Sub Bids Due 10/1. G.C. Bids Due 10/14. NTP Targeted October.
<b>TEWKSBURY</b>	1100	\$84.2	\$65.9													Memorial HS (MS) New Construction: Filed-Sub Bids Due 8/25. G.C. Bids Due 9/8. NTP Targeted September.
<b>BILLERICA</b>	500	\$34	\$27.1													Parker ES New Construction: Filed-Sub Bids Due 8/19. G.C. Bids Due 9/2. NTP Targeted September
<b>*SOUTHBRIDGE</b>	1050	\$76.5	\$60.1													Southbridge: CM@R Completed. Southbridge HS New Construction: Early Site Package Bids Due 9/10. Filed-Sub Bids Due 1/21/11. GMP Targeted February 2011.
<b>*DEDHAM</b>	310	\$23.4	\$19.9													Dedham CM@R Completed. Avery ES New Construction: Filed-Sub Bids Due 8/1. GMP Targeted September.
<b>DANVERS</b>	1000	\$79	\$62.7													Danvers High School Addition / Renovation: Early Bid Packages For Demo & Abatement Bids rcv'd 5/6. Swing Space Bids rcv'd 5/26. Filed-Sub Bids Due 9/28. G.C. Bids Due 10/6. NTP Targeted October.
<b>BROOKLINE</b>	560	\$29.8	\$22.5													Runkle ES Addition / Renovation: Filed-Sub Bids Due 9/2. G.C. Bids Due 10/6. NTP Targeted October.
<b>*GRAFTON</b>	900	\$72.4	\$57.4													Grafton CM@R Completed. Memorial HS New Construction: Early Site Packages Due 8/13. Filed-Sub Bids Due 12/17. GMP Targeted December.
<b>*ROCKLAND</b>	1525	\$86.2	\$66.5													Rockland CM@R Completed. Rogers MS New Construction / HS Renovation: Filed-Sub Bids Due 12/1. GMP Targeted December.
<b>*UXBRIDGE</b>	600	\$43	\$34.4													Uxbridge HS New Construction: Filed-Sub Bids Targeted December to January 2011. GMP Targeted February.
<b>MARSHFIELD</b>	485	\$2.4	\$2.0													Marshfield Edward Winslow ES Repair: Filed-Sub Bids Targeted September. G.C. Targeted October. NTP Targeted November.
<b>SO. SHORE RVT</b>	595	\$3.2	\$2.6													Regional VTHS Repair: Filed-Sub & G.C. Bids Targeted October. NTP Targeted November.
<b>ESSEX-NS</b>	1440	\$125	\$96.5													Essex North Shore HS New Construction.
<b>*NEEDHAM</b>	759	\$27.4	\$21.9													Newman ES Repair: Early Modular Foundation Work Bids rcv'd 5/7. Early Elec Duct Bank & Waterline Extension Work. Filed-Sub Bids rcv'd 6/15. Filed-Sub Bids Due 12/31. GMP Targeted January 2011.
<b>Subtotal</b>	<b>15,069</b>	<b>\$968.5</b>	<b>\$760.6</b>													
<b>GRAND TOTAL</b>	<b>28,648</b>	<b>\$1.61 B</b>	<b>\$1.26B</b>													
<b>Number of Construction-related Employment Opportunities Created</b>			<b>6,299</b>													

### 2011 Estimated Bid Dates

Note bid dates are **Estimates ONLY**. Please contact Districts for exact information.

Total Project Budget denotes total District costs and does not denote the basis of the MSBA Total Facilities Grant.

- Denotes bid phase in progress or complete
  - Denotes estimated bid dates

DISTRICT <small>*Projects Considering the CM @ Risk Method</small>	DESIGN BASIS FOR ENROLLMENT	PROJECT BUDGET <small>Shown in Millions</small>	CONSTRUCTION BUDGET <small>Shown in Millions</small>	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC
<b>*SHREWSBURY</b>	900	\$47.3	\$37.0	Sherwood MS New Construction: Filed-Sub Bids Targeted January to February. GMP Targeted March.											
<b>CARLISLE</b>	700	\$20.0	\$15.6	Carlisle ES Addition/Renovation: Filed-Sub and G.C. Bids Targeted January to February. NTP Targeted March.											
<b>BERLIN / BOYLSTON</b>	560	\$44.0	\$34.2	Tahanto MS/HS New Construction: Filed-Sub and G.C. Bids Targeted February to April. NTP Targeted May.											
<b>EASTHAMPTON</b>	510	\$43.7	\$33.5	Easthampton HS New Construction: Filed-Sub and G.C. Bids Targeted March to May. NTP Targeted June.											
<b>*LONGMEADOW</b>	1000	\$78.5	\$63.8	Longmeadow HS New Construction: Filed-Sub Bids Targeted March to May. GMP Targeted June.											
<b>SUTTON</b>	840	\$59.9	\$46.4	Sutton MS New Construction: Filed-Sub and G.C. Bids Targeted March to April. NTP Targeted June.											
<b>Subtotal</b>	<b>4,510</b>	<b>\$293.4</b>	<b>\$230.5</b>												
<b>GRAND TOTAL</b>	<b>4,510</b>	<b>\$293.4 M</b>	<b>\$230.5 M</b>												
<b>Number of Construction-related Employment Opportunities Created</b>			<b>1,153</b>												



**Projects in Construction  
MSBA Grant Basis and Maximum Grant Amount**

New Program and Wait List Program Totals		34,556	6,277,165	1,857,530,168	1,460,757,307		\$1,024,428,936						
District	School	Grade	Projected Enroll	Proposed Square Footage	District Total Project Budget	MSBA Total Facility Grant Basis	Reimbursement Rate	Approximate Maximum Grant Amount	Project Type	CM-R/GC	Construction Start	Estimated Substantial Completion Date	Construction Status
<b>Capital Pipeline Projects in Construction</b>													
<b>New Program Totals</b>			<b>17,993</b>	<b>3,572,008</b>	<b>845,271,086</b>	<b>\$769,225,995</b>		<b>\$395,012,809</b>					
Ashland	David Mindess ES	3-5	628	96,000	\$2,384,021	\$2,173,515	48.68%	\$1,058,067	Design/Bid/Build	Greenwood Industries	22-Jun-10	23-Aug-10	Roof replacement began in June.
Belmont	Roger E Wellington ES	K-5	575	88,203	\$40,664,431	\$31,000,050	40.00%	\$12,400,020	CM-R	Skanska	1-Mar-10	Jul-11	Concrete footings and walls are nearly complete. Steel erection is in progress.
Beverly	Beverly HS	9-12	1,200	368,300	\$81,500,000	\$80,155,000	58.42%	\$46,826,551	Design/Bid/Build	CTA	6-Jan-09	16-Dec-11	Substantial Completion Dates: Phase 1A: New Academic Tower - Nov 18, 2010. Phase 1A: Auditorium/Music Rooms/Renovation Areas - Nov 18, 2010. Phase 1B: Locker Room/Upper Gym/Renovation Areas - substantially complete. Contractor working punch list. Phase 1C Existing Kitchen/Cafeteria/Renovation Areas: April, 2011. Phase 1D Field House/Renovated Areas: November 19, 2010. Phase 2 Existing Building Demolition/Site Work: December 16, 2011.
Braintree	South MS	6-8	523	72,041	\$3,052,702	\$2,687,302	48.47%	\$1,302,535	Design/Bid/Build	Construction Dynamics	1-Apr-10	1-Sep-10	Construction continues with the removal of the boiler and its components. A new exterior transformer pad and underground electrical conduit have been installed.
Burlington	Memorial ES	K-5	500	79,500	\$27,923,244	\$26,963,244	52.11%	\$14,050,546	Design/Bid/Build	CTA	8-Mar-10	11-Aug-11	Construction is approximately 17% complete to date.
Danvers	Danvers HS	9-12	1,000	249,792	\$79,843,732	\$74,694,239	56.11%	\$41,910,938	Design/Bid/Build	Selection ongoing	Oct-10	3-Aug-13	Construction bids to be awarded in September.
Dartmouth	James Quinn ES	PK-5	925	122,000	\$1,358,304	\$1,358,304	47.64%	\$647,096	Design/Bid/Build	Advantage Glass, Inc.	6-Jun-10	27-Aug-10	Removal and replacement of windows began in June.
Foxborough	Foxborough HS	9-12	885	218,500	\$19,993,200	\$19,037,185	49.31%	\$9,387,236	Design/Bid/Build	CTA	30-Mar-10	30-Dec-12	Per the OPM report, the project is slightly ahead of schedule and approximately 18% complete.
Hamilton-Wenham	Cutler ES	K-5	298	45,000	\$1,429,720	\$1,429,720	42.58%	\$608,775	Design/Bid/Build	Thomas E. Snowden Inc.	6-Jun-10	12-Oct-10	HVAC replacement began in May and is on schedule.
Hanover	Hanover HS	9-12	800	156,000	\$59,953,688	\$59,484,384	47.21%	\$28,082,578	Design/Bid/Build	Callahan	1-Nov-09	29-Nov-11	Building slab on grade is 50% complete. Second floor framing is complete and third floor is 50% complete. Exterior sheathing is 80% complete. Site work, drainage & utility installation is 90% complete. The project is approximately 45% complete. On July 9th the SJC ruled in favor of Hanover to proceed into contract with Callahan, Inc.
Hingham	Hingham ES	PK-5	630	92,291	\$26,360,290	\$23,989,292	40.00%	\$10,370,000	Design/Bid/Build	CTA	8-May-08	8-Aug-09	Substantially complete and occupied. Punch list being completed.
Littleton	Russell Street ES	3-5	N/A	N/A	\$15,131,820	\$14,754,732	47.84%	\$7,058,664	Design/Bid/Build	Colantonio	25-Jun-09	30-Aug-10	OPM states project is 2 months ahead of schedule. Window subcontractor is having difficulty staffing the project and may delay schedule. Window work is on the critical path. The completion date for window installation is July 30th. The elevator pit slab is formed and reinforced. 7/19/10 update the second floor has been shored up and the opening cut. The masonry is well under way and will be completed by weeks end. Completion of elevator is on the critical path to meet substantial completion date.
Marblehead	Village ES	4-6	N/A	123,000	\$15,749,456	\$14,509,468	40.00%	\$5,803,787	Design/Bid/Build	Groom Construction	22-Dec-08	4-Aug-10	Phase 1 is 99% complete. Punch list items to be completed end of July. Phase 2 is 95% complete. Punch list will begin 7/23/10. Punch list to be complete end of August. Ready for school opening in September.
Middleton	Howe-Manning ES	4 - 6	553	83,500	\$31,392,734	\$30,114,849	51.47%	\$15,500,113	CM-R	CTA	22-Apr-10	13-Jan-12	Site and foundation work continues to date. Structural steel erection to begin in July.
Mount Greylock	Mount Greylock Reg HS	7-12	651	N/A	\$1,049,986	\$1,042,186	54.16%	\$564,448	Design/Bid/Build	Adams Plumbing & Heating	14-Jun-10	Sep-10	Heating system replacement continues to date.
					\$1,369,906	\$1,358,646	54.16%	\$735,843	Design/Bid/Build	Salco Construction	May-10	Sep-10	Locker Room repair continues to date.
Nashoba	Pompositicut ES	K-2	600	98,030	\$37,829,870	\$35,640,351	50.85%	\$18,123,118	Design/Bid/Build	Stella P.J. Construction Corp.	16-Jun-10	12-Jun-12	NTP issued 6/15/10. Initial site mobilization, including construction trailers, establishment of survey controls, baseline layout, hay bale locations and project limits. Scheduled work to be performed July - August 2010. Phase 1A consists of site clearing, grubbing, preliminary site access from Hartly Road, complete with associated project infrastructure. Also included in this phase is asbestos abatement and selective demo of existing structure to be removed.
North Attleboro	Joseph Martin ES	K-5	699	79,886	\$625,750	\$625,750	52.06%	\$325,765	Design/Bid/Build	Eagle Rivet Roof Services	14-Jun-10	27-Aug-10	Roof replacement began in June.
Norwood	Norwood HS	9-12	1,100	227,374	\$68,655,476	\$64,364,981	59.21%	\$38,110,505	Design/Bid/Build	Agostini	19-May-09	13-Jun-11	Per OPM report, the project is approximately 4-6 weeks ahead of schedule and approximately 56% complete. Sections A-B: Roof, exterior walls and windows are complete, interior wallboard and plaster work continues. Ceiling grid and painting have begun. Sections C-D: MEP and fire-suppression rough-in work continues.
Plymouth	Plymouth HS	9-12	1,350	267,357	\$92,249,040	\$79,420,894	58.24%	\$46,254,729	Design/Bid/Build	J&J Contractors	3-May-10	11-May-12	Contractor has mobilized and secured the site. Building permit received. Site clearing has begun. The contractor has begun excavation for the interior spread and exterior wall footings followed by the placement of formwork, reinforcing steel and concrete.
Rochester	Memorial ES	K-6	635	105,023	\$26,500,000	\$25,268,708	57.94%	\$14,640,689	CM-R	Gilbane	19-Apr-10	1-Dec-10	Precast foundations complete, precast panels have arrived and erection has begun. Existing building seismic modifications are underway. Asbestos abatement in the existing building has begun. Project is approximately 14% complete.
Rockport	Rockport MS/HS	6-12	598	117,184	\$1,006,384	\$1,006,384	41.10%	\$413,624	Design/Bid/Build	Feeley, McAnespie, Inc.	21-Jun-10	27-Aug-10	Roof replacement began in June.
Sharon	Sharon MS	6-8	845	170,750	\$49,540,287	\$43,950,340	52.68%	\$23,153,039	CM-R	Consigli	1-Jun-10	22-Aug-11	The bid for sewer line and site work was awarded May 17, 2010 and work started on June 15, 2010. Building renovation work began when school let out on June 18, 2010.
Wellesley	Wellesley HS	9-12	1,500	280,000	\$131,054,929	\$107,751,342	40.00%	\$43,100,537	CM-R	Turner	24-Aug-09	5-Mar-12	Steel erection, concrete decking, exterior wall metal framing, ductwork and roofing continues.
Whittier Reg	Whittier Reg Voc Tech HS	9-12	1,178	365,000	\$2,147,762	\$2,069,360	66.18%	\$1,369,502	Design/Bid/Build	Greenwood Industries	28-Jun-10	27-Aug-10	Roof replacement began in June.
Woburn	Goodyear ES	K-5	320	67,277	\$26,504,354	\$24,375,769	54.21%	\$13,214,104	CM-R	Gilbane	24-Mar-10	15-Jul-11	Both site work and foundation have begun.
<b>Wait List Projects in Construction</b>													
<b>Wait List Program Totals</b>			<b>16,563</b>	<b>2,705,157</b>	<b>1,012,259,082</b>	<b>\$691,531,312</b>		<b>\$629,416,127</b>					
Cambridge	Rindge & Latin HS	9-12	1,529	82,938	\$112,116,300	\$33,620,000	69.47%	<b>\$33,973,519</b>	Design/Bid/Build	W.T. Rich, Inc.	May-07	Jul-11	HVAC and other upgrades currently ongoing.
Falmouth	Falmouth HS	9-12	1,003	266,654	\$86,325,000	\$56,263,993	59.70%	\$33,589,604	Design/Bid/Build	TLT Construction	Jun-05	Nov-10	Project is approximately 90% complete at this time with Phase 2 completion scheduled for Fall 2010.
Haverhill	Haverhill HS	9-12	1,864	N/A	\$33,739,532	\$33,739,532	68.48%	\$23,104,832	Design/Bid/Build	CTA	Apr-04	Aug-11	Site and perimeter work is ongoing with locker replacement and painting scheduled for Summer 2011.
Holyoke	Holyoke HS	9-12	1,252	N/A	\$22,738,000	\$15,964,800	90.00%	\$14,368,320	Design/Bid/Build	WJ Mountford	Mar-10	Aug-10	HVAC, windows and ADA upgrades are ongoing with an approximate completion date of August 2010.
Malden	Malden HS	9-12	1,720	365,271	\$77,033,447	\$77,072,181	90.00%	\$69,364,963	CM-R	Gilbane	8-Aug-10	Jun-12	This is a complete renovation of the existing high school and the work has been divided into nine (9) phases. The project is approximately 40 - 45 percent complete.
New Bedford	Abraham Lincoln ES	K-5	450	96,000	\$28,072,000	\$17,952,000	90.00%	<b>\$23,494,800</b>	Design/Bid/Build	CTA	1-Jun-09	15-Dec-10	The substantial completion date for Phase I, the new facility, is August 16, 2010 and Phase II, existing building demolition, is December 15, 2010. Furniture deliveries are scheduled for the end of July.
Newton	Newton North HS	9-12	1,795	375,000	\$197,499,511	\$77,628,610	60.00%	<b>\$61,577,166</b>	CM-R	Dimeo Construction	Feb-08	Aug-10	Phase I is 97% complete. The building has been inspected by Newton Fire Department and Inspectional Services Department and a temporary certificate of occupancy has been issued for the building. The permanent certificate of occupancy is expected to be received at the end of August once all punch list items have been completed and the school has been fitted-out with furniture. Phase II demo and abatement of the existing building has begun.
Quincy	Quincy HS	9-12	1,650	368,000	\$126,766,465	\$80,228,599	90.00%	<b>\$87,205,739</b>	CM-R	Gilbane	Jun-10	Dec-10	Construction is progressing. The total project budget shows the project at approximately 90% complete.
Revere	Paul Revere ES	K-5	350	57,500	\$17,409,000	\$10,752,500	90.00%	<b>\$16,152,185</b>	Design/Bid/Build	Delulis Brothers	Nov-10	Jun-10	The building has been completed. Furnishings, fixtures and equipment are being moved into the building. Only minor site work and punch list work is remaining.
Springfield	Putnam Voc Tech HS	9-12	1,400	315,000	\$125,000,000	\$125,000,000	90.00%	\$112,500,000	CM-R	Consigli	18-May-10	Jul-12	Underslab utilities and foundations are ongoing.
Taunton	Parker MS	5-8	2,350	539,224	\$112,759,827	\$112,759,827	83.00%	\$93,590,656	Design/Bid/Build	Bacon-Agostini	Jul-10	Jan-12	The new Middle School portion of the job is complete. Renovation of the existing High School continues and now stands at approximately 75% complete.
Worcester	North HS	9-12	1,200	239,570	\$72,800,000	\$50,549,270	90.00%	<b>\$60,494,343</b>	CM-R	Gilbane	24-Sep-08	May-11	The project schedule reflected a 12 month delay in the completion of construction plans and specs. Metal stud framing is 75% complete. Drywall installation is 50% complete. MEP rough-ins and fire suppression systems are ongoing. Interior masonry walls are 90% complete and exterior masonry is underway at the south and north elevations. The overall project is approximately 40% complete.

*Bold and italicized totals include an additional grant/loan amount to the Reimbursement Rate.*
