

Project Overview Report September 29, 2010

A total of 186 projects are currently in the MSBA's grant program. The following summary table provides the category (e.g., New Program, etc.) and the number of projects in each phase (e.g., Local Clearance, etc.):

	Total	Local Clearance	Feasibility Study/ Schematic Design	Design Development	Construction
New Program	123	35	45	21	24
Waitlist	13		2		11
Green Repair	39	12	17	1	7
Closeout/Audit Complete	11				
Total	186	47	64	22	42

The MSBA utilizes the Capital Pipeline Status chart to account for the ongoing status of all Districts in the pipeline. Activity for some of the key milestone activities are summarized in the table below with the numbers reported indicative of the category requirements. (For instance, enrollment certifications are not required for all projects, e.g., repairs, and Owner's Project Managers are not required for construction projects under \$1.5 million unless required by the MSBA.)

Critical Prerequisites:

An agreed upon enrollment is a key prerequisite for the MSBA to commence a Feasibility Study with a District. In order to begin the enrollment projection process, a District must file enrollment information utilizing the MSBA's online enrollment projection.

After the MSBA and the District have agreed upon an enrollment to be used as the design basis and executed a Feasibility Study Agreement, the District procures consultants, starting with Owner's Project Manager. Currently, there are 47 Districts in the Capital Pipeline who still need to procure an Owner's Project Manager.

After a District has selected an Owner's Project Manager and executed a contract with that Owner's Project Manager, it is ready for the selection of a Designer utilizing either a local designer selection process for projects under \$5 million or the MSBA's Designer Selection Panel for those projects over \$5 million. Currently, there are 61 Districts in the Capital Pipeline who still need to procure a Designer.

	District Action to complete	MSBA/ District Collaboration	Completed Activity this Period	Total Completed to Date*	Total
Enrollment	20	32 (9 certs. pending)	2	85	66,607 students
Owner's Project Manager	47	14	8	99	Over \$57 million in OPM fees
Designer	61	10	2	113	Over \$143 million in Designer Fees

Owner’s Project Managers

Since the July Board of Directors Meeting, the following Districts have completed the OPM selection process:

- Boston (Upper Quincy)
- Brookline (Heath)
- East Bridgewater (High School)
- Lincoln (K-8)
- Scituate (Wampatuck)
- Springfield (SCIPP)
- Tri County Regional (Voc Tech High School)
- Weston (Field Elementary School)

The schedule for the next OPM Review Panel meeting is shown below with the potential of 4 Districts submitting for review and approval.

Panel Date	District/School	Project Description Status	Estimated Project Cost
10/4/10	Norton/ HS	Feasibility Study	\$15-\$20 mil
10/4/10	Williamsburg/Helen E. James	Feasibility Study	\$6-\$10 mil
10/4/10	Winthrop/ Winthrop SR HS	Repair	\$10-\$45 mil
10/4/10	Saugus / Belmonte MS	Repair	\$8-\$10 mil

Designers

Since the July Board of Directors meeting, the DSP has met once resulting in 2 additional Districts completing the Designer selection process.

Panel Date	District/School	Status	Estimated Project Cost	# of Proposals Received	Top 3-Ranked Firms	Interviews Requested	First-Ranked Selection
9/7/2010	North Adams PS – Silvio O. Conte MS	Designer Selection	\$20m - \$28m	6	- Fletcher Thompson - JCJ Architecture - Margo Jones Arch.	No	Margo Jones Architects
9/21/2010	S. Worcester Cnty Reg. Voc. PS – Bay Path RVTHS	Designer Selection	\$10m - \$40m	7	- Fletcher Thompson - HMFH Architects - Kaestle Boos	Yes	TBD

The following Districts are tentatively scheduled for upcoming DSP meetings:

- Brookline (Heath)
- Essex North Shore Regional Voc Tech High School
- Springfield (Forest Park Middle School)
- Weston (Fields Elementary School)

Commissioning

Since the July Board of Directors meeting, the MSBA has assigned Commissioning Consultants to an additional 2 projects as presented in the table below. The MSBA has executed 39 Commissioning Consultant contracts to date, totaling \$5.2 Million.

District	School	Estimated Const. Cost (millions)	Commissioning Consultant	Contract Amount
Methuen PS	Methuen HS	\$74.70	Environmental Health & Engineering	\$299,400
Leominster PS	Leominster SHS	\$32.80	Horizon Engineering Associates	\$109,400
Total	2	\$107.5	Total	\$408,800

Projects for which we are currently seeking proposals and/or negotiating Work Orders include:

District	School	Responses Due
Ashland PS	David Mindess IS	8/23/2010
Dartmouth PS	James M. Quinn ES	8/23/2010
Rockport PS	Rockport HS	8/23/2010
Whittier Voc PS	Whittier Reg Voc HS	8/23/2010
Quabbin PS	Oakham Center ES	8/23/2010
North Attleborough PS	Joseph W Martin Jr ES	8/24/2010
Uxbridge PS	Uxbridge HS	9/17/10

Projects that are currently in the queue for assignment of a Commissioning Consultant and for which contract documents are being drafted include:

District	School
Burlington PS	Marshall Simonds MS
Marshfield PS	Gov Edward Winslow ES
South Shore Reg Voc PS	South Shore Voc / Tech HS

Attached to the Project Status report are the following:

- Master District Status List
- SOI Status - Capital Pipeline: As indicated in the attached chart, Districts continue to make progress with their projects. The narrow solid bar indicates the number of Districts in each category as reported at the July Board meeting.
- Estimated Bid Schedule.
- Construction Status Report



Massachusetts School Building Authority

No. of Projects: 186

Master District Status List

Yellow = Wait List Project

Green = Green Repair

Red = Changes in last 60 days

District Name	School Name	Status	Preferred Schematic	OPM	Designer	Cx Authority	Procurement Status	CM/GC
Abington PS	Frolio JHS	Local Clearance - 07/08						
Acton PS	Douglas ES	Project Scope & Budget	Repair	N/A	CBI Consulting, Inc.			
Adams-Cheshire PS	Adams MS	Project Scope & Budget	Addition/Renovation	URS Corporation	Tessier Associates		Undetermined	
Andover PS	Bancroft ES	Preferred Schematic	New Construction	Town of Andover	Symmes Maini & McKee Associates			
Arlington PS	Thompson ES	Feasibility Study		PMA Consultants	HMFH Architects, Inc.			
Ashburnham-West PS	Briggs ES	Preferred Schematic	New Construction	STV, Inc.	Lamoureux Pagano & Associates, Inc.			
Ashland PS	David Mindess IS	Building Completion 2010	Repair	Heery International, Inc	Gale Associates, Inc.		DBB - Contract Awarded	Greenwood Industries
Assabet Valley PS	Assabet Valley Voc HS	Feasibility Study		Strategic Building Solutions, LLC	Design Partnership of Cambridge, Inc.			
Athol-Royalston PS	Riverbend ES	Local Clearance - Repair - 09						
Attleboro PS	Hyman Fine ES	Project Scope & Budget	Repair	Skanska USA Building, Inc.	Russo Barr Associates			
Attleboro PS	Attleboro HS	Project Scope & Budget	Repair	Skanska USA Building, Inc.	Russo Barr Associates			
Attleboro PS	Hill-Roberts ES	Project Scope & Budget	Repair	Skanska USA Building, Inc.	Russo Barr Associates			
Attleboro PS	A. Irvin Studley ES	Project Scope & Budget	Repair	Skanska USA Building, Inc.	Russo Barr Associates			
Auburn PS	Auburn MS	Local Clearance - 07/08						
Avon PS	Ralph D Butler ES	Closeout/Audit	Repair		Richard D. Kimball Company, Inc.		DBB - Contract Awarded	Automatic Temperature Controls Inc.
Ayer PS	Ayer HS	Local Clearance - 09/10						
Bedford PS	Bedford HS	Closeout/Audit		Peter Cox	Symmes Maini & McKee Associates		DBB - Contract Awarded	Brait Builders Construction
Belmont PS	Roger E Wellington ES	Construction	New Construction	PMA Consultants	Jonathan Levi Architects LLC	Strategic Building Solutions	CMR - CM Selected	Skanska USA Building, Inc.
Berlin-Boylston PS	Tahanto Reg HS	Design Development	New Construction	PMA Consultants	HMFH Architects, Inc.	Strategic Building Solutions		
Beverly PS	Beverly HS	Construction		Heery International	Mount Vernon Group Architects, Inc.		DBB - Contract Awarded	CTA Construction Co.
Billerica PS	Parker ES	Construction	New Construction	Joslin, Lesser & Associates, Inc.	Symmes Maini & McKee Associates	Sebesta Blomberg & Associates	Undetermined	
Boston PS	Dearborn MS	Local Clearance - 09/10						
Boston PS	Quincy Upper School	Designer Selection		City of Boston				

Master District Status List

Yellow = Wait List Project	
Green = Green Repair	Red = Changes in last 60 days

District Name	School Name	Status	Preferred Schematic	OPM	Designer	Cx Authority	Procurement Status	CM/GC
Braintree PS	Archie T Morrison ES	Local Clearance	Repair					
Braintree PS	Highlands	Local Clearance	Repair					
Braintree PS	South MS	Construction	Repair	Town Employee	Habeeb & Associates Architects, Inc.		DBB - Contract Awarded	Construction Dynamics
Braintree PS	Hollis ES	Local Clearance	Repair					
Braintree PS	Braintree HS	Local Clearance	Repair					
Braintree PS	East MS	Local Clearance	Repair					
Brookline PS	John D Runkle K-8	Design Development	Addition/Renovation	Town of Brookline Building Department	Design Partnership of Cambridge, Inc.	Consulting Engineering Services, LLC	DBB - In Design	
Brookline PS	Heath K-8	Designer Selection		Town of Brookline Building Department				
Burlington PS	Marshall Simonds MS	Design Development	Addition/Renovation		Knight, Bagge & Anderson, Inc.			
Burlington PS	Memorial ES	Construction	New Construction	Construction Monitoring Services, Inc.	Knight, Bagge & Anderson, Inc.	Consulting Engineering Services, LLC	DBB - Contract Awarded	CTA Construction Co. Inc.
Cape Cod Region Voc Tech PS	Cape Cod Regional Voc / Tech HS	Local Clearance	Repair					
Carlisle PS	Carlisle K-8	Design Development	Addition/Renovation	Daedalus Projects, Inc.	HMFH Architects, Inc.	Horizon Engineering Associates, LLP	DBB - In Design	
Chelmsford PS	McCarthy MS	Closeout/Audit					DBB - Contract Awarded	Multiple
Chelsea PS	Clark Avenue MS	Local Clearance - 07/08			Jacobs			
Chicopee PS	Chicopee Academy	Local Clearance - 09/10						
Concord-Carlisle PS	Concord Carlisle HS	Local Clearance - Repair - 09						
Conway PS	Conway Grammar ES	Project Scope & Budget	Repair		Richardson Gorman Architects			
Danvers PS	Danvers HS	Construction	Addition/Renovation	Construction Monitoring Services, Inc.	DiNisco Design Partnership, Limited	Turner Facilities Management Solutions	DBB - In Design	
Dartmouth PS	James M. Quinn ES	Building Completion 2010	Repair		Russo Barr Associates, Inc.			
Dedham PS	Avery ES	Design Development	New Construction	Construction Monitoring Services, Inc.	Dore & Whittier Architects, Inc.	WSP Flack + Kurtz	CMR - CM Selected	Consigli Construction Co
Dennis-Yarmouth PS	Ezra H Baker ES	Local Clearance	Repair					
Douglas PS	Douglas IS	Feasibility Study		Heery International, Inc	DiNisco Design Partnership, Limited			
Dracut PS	Dracut SHS	Preferred Schematic	Addition/Renovation	RF Walsh Collaborative Partners	Mount Vernon Group Architects, Inc.		Undetermined	
Duxbury PS	Chandler ES	Closeout/Audit	Repair	N/A	Gale Associates, Inc.		DBB - Contract Awarded	Built-up Roofing Systems LLC
Duxbury PS	Duxbury HS	Local Clearance - 09/10						
East Bridgewater PS	East Bridgewater HS	Preferred Schematic	Model School	RF Walsh Collaborative Partners - pending	Ai3			

Master District Status List

Yellow = Wait List Project	
Green = Green Repair	Red = Changes in last 60 days

District Name	School Name	Status	Preferred Schematic	OPM	Designer	Cx Authority	Procurement Status	CM/GC
Easthampton PS	Easthampton HS	Design Development	New Construction	Strategic Building Solutions, LLC	Caolo & Bieniek Associates, Inc.	Consulting Engineering Services, LLC	Undetermined	
Essex North Shore Agr and Tech PS	Essex North Shore Agr and Tech School	Design Development	New Construction	PMA Consultants				
Fairhaven PS	Rogers ES	Feasibility Study		Daedalus Projects Inc	HMFH Architects, Inc.			
Fall River PS	Morton MS	OPM Selection						
Falmouth PS	Falmouth High School	Construction	Addition/Renovation	Gilbane Building Company	DiNisco Design Partnership, Limited		DBB - Contract Awarded	TLT Construction
Fitchburg PS	South Street ES	Project Scope & Budget	Repair	Compass Project Management, Inc.	BLW			
Fitchburg PS	Reingold ES	Project Scope & Budget	Repair	Compass Project Management, Inc.	BLW			
Fitchburg PS	Memorial IS	Project Scope & Budget	Repair	Compass Project Management, Inc.	BLW			
Fitchburg PS	Goodrich K Center	Project Scope & Budget	Repair	Compass Project Management, Inc.	BLW			
Fitchburg PS	Crocker ES	OPM Selection						
Florida PS	Abbott Memorial K-8	Construction	Repair		Dietz and Company		DBB - Contract Awarded	Waterman Excavating, Inc
Foxborough PS	Foxborough HS	Construction	Repair	Construction Monitoring Services, Inc.	Kaestle Boos Associates, Inc.	Consulting Engineering Services, LLC	DBB - Contract Awarded	CTA Construction Co.
Franklin PS	Franklin HS	Feasibility Study		Daedalus Projects Inc.	CGKV Architects, Inc.			
Gardner PS	Waterford Street Primary	Local Clearance - 07/08						
Georgetown PS	Penn Brook IS	Local Clearance - 09/10						
Gloucester PS	West Parish ES	Local Clearance - 09/10						
Grafton PS	Grafton Memorial SHS	Design Development	New Construction	Joslin, Lesser & Associates, Inc.	Symmes Maini & McKee Associates	Horizon Engineering Associates, LLP	CMR - CM Selected	Dimeo Construction
Granby PS	Granby JHS / SHS	Project Scope & Budget	New Construction	Skanska USA Building Inc.	Dore & Whittier Architects, Inc.			
Greater Lowell Voc Tec PS	Gr Lowell Regional Voc / Tech HS	OPM Selection						
Greenfield PS	Greenfield HS	Local Clearance - Repair - 09						
Hadley PS	Hopkins Academy	Closeout/Audit			Kaestle Boos Associates, Inc.			
Hamilton-Wenham PS	Cutler ES	Building Completion 2010	Repair	Municipal Building Consultants, Inc.	Richard D. Kimball Company, Inc.	Sebesta Blomberg & Associates	DBB - Contract Awarded	Thomas E. Snowden Inc.
Hampden-Wilbraham PS	Minnechaug Reg HS	Construction	Model School	ARCADIS U.S., Inc.	Mount Vernon Group Architects, Inc.	Horizon Engineering Associates, LLP	DBB - Contract Awarded	Fontaine Bros.
Hancock PS	Hancock ES	Project Scope & Budget		N/A	Westall Architects			
Hanover PS	Hanover HS	Construction	New Construction	PMA Consultants	HMFH Architects, Inc.	Horizon Engineering Associates, LLP	DBB - Contract Awarded	Callahan, Inc
Haverhill PS	Haverhill HS	Construction						

Master District Status List

Yellow = Wait List Project

Green = Green Repair

Red = Changes in last 60 days

District Name	School Name	Status	Preferred Schematic	OPM	Designer	Cx Authority	Procurement Status	CM/GC
Hingham PS	New Elementary School	Closeout/Audit	New Construction	Knight, Bagge & Anderson, Inc.	Ai3 Architects LLC		DBB - Contract Awarded	CTA Construction Co.
Holbrook PS	Holbrook JHS / SHS	OPM Selection						
Holyoke PS	Holyoke HS	Construction			Design Partnership of Cambridge, Inc.			
Hopedale PS	Memorial ES	Closeout/Audit	Repair		Gale Associates, Inc.		DBB - Contract Awarded	Greenwood Industries Inc.
Hopkinton PS	Center ES	Preferred Schematic	New Construction	Town of Hopkinton	Design Partnership of Cambridge, Inc.		Undetermined	
Hudson PS	John F Kennedy MS	Preferred Schematic	New Construction	PMA Consultants	The Office of Michael Rosenfeld, Inc.			
Leominster PS	Leominster SHS	Design Development	Addition/Renovation	Daedalus Projects, Inc.	Lamoureux Pagano & Associates, Inc.	Horizon Engineering Associates, LLP		
Lincoln PS	Lincoln K-8	Designer Selection		Skanska USA Building, Inc.				
Littleton PS	Russell St ES	Building Completion 2010	Repair	Daedalus Projects, Inc.	Drumrey Rosane Anderson, Inc.	WSP Flack + Kurtz	DBB - Contract Awarded	Colantonio, Inc.
Longmeadow PS	Longmeadow HS	Design Development	New Construction	Joslin, Lesser & Associates, Inc.	The Office of Michael Rosenfeld, Inc.	Foreman Building Commissioning, LP	CMR - CM Selected	Gilbane Building Company
Lowell PS	Charles W Morey ES	Closeout/Audit		Watermark			DBB - Contract Awarded	CTA Construction Co.
Lunenburg PS	Lunenburg HS	Local Clearance - 09/10						
Lynn PS	Thurgood Marshall MS	Local Clearance - 09/10						
Lynnfield PS	Lynnfield HS	Local Clearance - 09/10						
Malden PS	Malden HS	Construction	Renovation	URS Corporation	Flansburgh Associates, Inc.		CMR - CM Selected	Gilbane Building Company
Manchester Essex Regional PS	Manchester JHS / SHS	Closeout/Audit		Design Technique	Mount Vernon Group Architects, Inc.		DBB - Contract Awarded	TLT Construction
Marblehead PS	Glover Primary	Preferred Schematic	New Construction	Municipal Building Consultants, Inc.	JCJ Architecture + Interiors, PC		Undetermined	
Marblehead PS	Village IS	Building Completion 2010	Repair	Municipal Building Consultants, Inc.	Symmes Maini & McKee Associates	RDK Engineering	DBB - Contract Awarded	Groom Construction
Marshfield PS	Gov Edward Winslow ES	Design Development	Repair	Vertex Construction Services	Knight, Bagge & Anderson, Inc.			
Maynard PS	Maynard HS	Project Scope & Budget	New Construction	Municipal Building Consultants, Inc.	Tappe Associates, Inc.		Undetermined	
Medway PS	Medway MS	Project Scope & Budget		Compass Project Management, Inc.	Knight, Bagge & Anderson, Inc.			
Methuen PS	Methuen HS	Design Development	Addition/Renovation	KBA/Trident	Finegold Alexander and Associates, Inc.	Environmental Health and Engineering	Undetermined	
Middleton PS	Howe-Manning IS	Construction	New Construction	RF Walsh Collaborative Partners	DiNisco Design Partnership, Limited	Foreman Building Commissioning, LP	DBB - Contract Awarded	CTA Construction Co.
Minuteman Voc Tech PS	Minuteman Reg HS	Local Clearance - 09/10						
Mount Greylock PS	Mt Greylock Reg HS	Construction	Repair	N/A	Hesnor Engineering & Barry Architects	Horizon Engineering Associates, LLP	DBB - Contract Awarded	Adams Plumbing & Heating
Narragansett PS	Templeton Center	Feasibility Study		Strategic Building Solutions, LLC	Symmes Maini & McKee Associates		Undetermined	

Master District Status List

Yellow = Wait List Project

Green = Green Repair

Red = Changes in last 60 days

District Name	School Name	Status	Preferred Schematic	OPM	Designer	Cx Authority	Procurement Status	CM/GC
Nashoba PS	Pompositticut Primary	Construction	Addition/Renovation	Construction Monitoring Services, Inc.	Symmes Maini & McKee Associates	Strategic Building Solutions	DBB - Contract Awarded	Stella P.J. Construction Corp.
Nashoba Valley Tech PS	Nashoba Valley Tech HS	Approved Project Vote Pending	Repair					
Natick PS	Natick HS	Construction	Model School	RF Walsh Collaborative Partners	Ai3 Architects LLC	RFS Engineering	DBB - Contract Awarded	Brait Builders Corporation
Needham PS	Newman ES	Design Development	Repair	Town of Needham	Drumrey Rosane Anderson, Inc.	RFS Engineering	CMR - CM Selected	Consigli Construction Co.
New Bedford PS	Abraham Lincoln	Building Completion 2010	New Construction	Daedalus Projects Inc	Mount Vernon Group Architects, Inc.	Sebesta Blomberg & Associates	DBB - Contract Awarded	CTA Construction Co.
New Bedford PS	Elizabeth Carter Brooks ES	Feasibility Study						
New Bedford PS	John Hannigan ES	Local Clearance - 09/10						
Newburyport PS	Rupert A Nock MS	Local Clearance - 09/10						
Newton PS	Newton North HS	Building Completion 2010	New Construction	Turner Construction Company	Dore & Whittier Architects, Inc.		CMR - CM Selected	Dimeo Construction
Norfolk County Agr PS	Norfolk County Agr HS	Project Scope & Budget		Compass Project Management, Inc	Turowski2 Architecture, Inc.			
Norfolk PS	Freeman-Centennial IS	Design Development	New Construction	Joslin, Lesser & Associates, Inc.	Flansburgh Associates, Inc.	WSP Flack + Kurtz	DBB - In Design	
North Adams PS	Silvio O Conte MS	Feasibility Study		Strategic Building Solutions, LLC	Margo Jones Architects, Inc.			
North Attleborough PS	Joseph W Martin Jr ES	Building Completion 2010	Repair		CBI Consultants, Inc.		DBB - Contract Awarded	Eagle Rivet Roof Services Corporation
North Reading PS	North Reading HS	Local Clearance - 09/10						
Northampton-Smith PS	Smith Vocational and Agricultural HS	Local Clearance - 09/10						
Northeast Metro Voc PS	Northeast Metro Reg Voc HS	Local Clearance - 09/10						
Norton PS	Norton HS	OPM Selection						
Norwood PS	Norwood HS	Construction	Model School	Compass Project Management, Inc.	Ai3 Architects LLC		DBB - Contract Awarded	Agostini Construction Company, Inc.
Old Colony Reg Voc Tech PS	Old Colony Regional Voc / Tech HS	Local Clearance - 09/10						
Orange PS	Dexter Park IS	Local Clearance - 09/10						
Oxford PS	Oxford MS	OPM Selection						
Peabody PS	J Henry Higgins MS	OPM Selection						
Pittsfield PS	Taconic HS	OPM Selection						
Plymouth PS	Plymouth North HS	Construction	Model School	Ted Gentry Associates	Ai3 Architects LLC	Sebesta Blomberg & Associates	DBB - Contract Awarded	J&J Contractors Inc.
Quabbin PS	Oakham Center ES	Building Completion 2010	Repair		Russo Barr Associates, Inc.		DBB - Contract Awarded	Cape Way Roofing
Quabbin PS	Quabbin Reg HS	OPM Selection			LPBA Architects			

Master District Status List

Yellow = Wait List Project

Green = Green Repair

Red = Changes in last 60 days

District Name	School Name	Status	Preferred Schematic	OPM	Designer	Cx Authority	Procurement Status	CM/GC
Quincy PS	Central MS	Feasibility Study	New Construction	Tishman Construction Corporation of MA	Ai3 Architects LLC			
Quincy PS	Quincy High School	Building Completion 2010	New Construction	Tishman Construction Corporation of MA	Symmes Maini & McKee Associates		CMR - CM Selected	Gilbane Building Company
Revere PS	Paul Revere ES	Building Completion 2010	New Construction	RF Walsh Collaborative Partners	Drumme Rosane Anderson, Inc.		DBB - Contract Awarded	Delulis Brothers Construction Company
Rochester PS	Rochester Memorial ES	Construction	Addition/Renovation	PMA Consultants	Flansburgh Associates, Inc.	Horizon Engineering Associates, LLP	CMR - CM Selected	Gilbane Building Company
Rockland PS	John W Rogers MS	Design Development	Addition/Renovation	Daedalus Projects Inc	Dore & Whittier Architects, Inc.	Consulting Engineering Services, LLC	CMR - CM Selected	Agostini Construction Company, Inc.
Rockport PS	Rockport ES	Project Scope & Budget	Repair	N/A	Russo Barr Associates			
Rockport PS	Rockport HS	Building Completion 2010	Repair		Russo Barr Associates, Inc.		DBB - Contract Awarded	Feeley, McAnespie, Inc.
Salem PS	Collins MS	Local Clearance	Repair					
Salem PS	Saltonstall ES	Local Clearance	Repair					
Sandwich PS	Oak Ridge K-8	Local Clearance	Repair					
Saugus PS	Belmonte Saugus MS	OPM Selection						
Scituate PS	Wampatuck ES	Designer Selection	Repair	Bargmann Hendrie + Archetype				
Sharon PS	Sharon MS	Construction	Addition/Renovation	Daedalus Projects, Inc.	Kaestle Boos Associates, Inc.	Horizon Engineering Associates, LLP	CMR - CM Selected	Consigli Construction Co.
Shawsheen Valley Voc PS	Shawsheen Valley Voc / Tech HS	Design Development	Repair		Knight, Bagge & Anderson, Inc.		DBB - Contract Awarded	Gibson Roofs, Inc.
Shawsheen Valley Voc PS	Shawsheen Valley Voc / Tech HS	Approved Project Vote Pending			Knight, Bagge & Anderson, Inc.			
Shrewsbury PS	Sherwood MS	Design Development	New Construction	PMA Consultants	Lamoureux Pagano & Associates, Inc.	RDK Engineering	CMR - CM Selected	Gilbane Building Company
Somerset PS	Somerset HS	Local Clearance - 09/10						
Somerville PS	E Somerville Community K-8	Project Scope & Budget	Renovation	City of Somerville	Maguire Group Inc.			
South Hadley PS	Plains ES	Local Clearance - 09/10						
South Shore Reg Voc PS	South Shore Voc / Tech HS	Design Development	Repair	Lincoln Consultants	Gale Associates, Inc.			
Southbridge PS	Southbridge HS	Design Development	New Construction	Joslin, Lesser & Associates, Inc.	Tappe Associates, Inc.	Environmental Health and Engineering	CMR - CM Selected	Consigli Construction Co.
Southeastern Reg Voc Tech PS	Southeastern Regional Voc / Tech HS	Feasibility Study		RF Walsh Collaborative Partners	Drumme Rosane Anderson, Inc.			
Southern Worcester Cty VT PS	Bay Path Regional Voc / Tech HS	Designer Selection		Heery International, Inc				
Southwick-Tolland	Woodland ES	Feasibility Study		Strategic Building Solutions, LLC	JCJ Architecture + Interiors, PC			
Spencer-E Brookfield PS	David Prouty HS	Local Clearance - Repair - 09						
Springfield PS	SCIPP Year 1	Closeout/Audit	Repair					

Master District Status List

Yellow = Wait List Project

Green = Green Repair

Red = Changes in last 60 days

District Name	School Name	Status	Preferred Schematic	OPM	Designer	Cx Authority	Procurement Status	CM/GC
Springfield PS	SCIPP Years 2 & 3	Designer Selection						
Springfield PS	Putnam Voc / Tech HS	Construction	New Construction	ARCADIS	Drumme Rosane Anderson, Inc.	Strategic Building Solutions	CMR - CM Selected	Consigli Construction Co.
Springfield PS	Forest Park Middle School	Preferred Schematic	Addition/Renovation	ARCADIS-U.S., Inc.				
Stoneham PS	Stoneham MS	OPM Selection						
Sturbridge PS	Burgess ES	Construction	Addition/Renovation	Lamoureux Pagano & Associates, Inc.	Drumme Rosane Anderson, Inc.	Horizon Engineering Associates, LLP	DBB - Contract Awarded	Fontaine Bros.
Sutton PS	Sutton MS	Design Development	Addition/Renovation	Strategic Building Solutions	Flansburgh Associates, Inc.	RDK Engineering		
Taunton PS	Taunton HS	Construction	Addition/Renovation	Gilbane	Design Partnership of Cambridge, Inc.		DBB - Contract Awarded	Bacon-Agostini Construction Joint Venture
Tewksbury PS	Tewksbury Memorial HS	Design Development	Model School	Heery International, Inc	Symmes Maini & McKee Associates	Sebesta Blomberg & Associates	DBB - Out to Bid	
Tri County PS	Tri County Regional Voc / Tech HS	Local Clearance	Repair					
Uxbridge PS	Uxbridge HS	Design Development	New Construction	Joslin, Lesser & Associates, Inc.	Raymond Design Associates, Inc.		CMR - IG Application Pending	
Wachusett PS	Mountview MS	Local Clearance - 09/10						
Wakefield PS	Wakefield Memorial HS	PFA pending	Addition/Renovation					
Wakefield PS	Galvin MS	Local Clearance - 09/10						
Wayland PS	Wayland HS	Construction	New Construction	KV Associates	HMFH Architects, Inc.	WSP Flack + Kurtz	CMR - CM Selected	Shawmut Construction
Webster PS	Park Avenue ES	Local Clearance - 09/10						
Wellesley PS	Wellesley SHS	Construction	New Construction	Ryegate Inc	Symmes Maini & McKee Associates	RFS Engineering	CMR - CM Selected	Turner Construction
West Bridgewater PS	West Bridgewater JHS / SHS	Local Clearance - 09/10						
West Springfield PS	West Springfield HS	Local Clearance - 09/10	Model School					
Westborough PS	Sarah W Gibbons MS	Local Clearance - Repair - 09						
Westfield PS	Abner Gibbs ES	Local Clearance - 09/10						
Westfield PS	Southampton Road ES	Local Clearance	Repair					
Westfield PS	Highland School	Local Clearance	Repair					
Weston PS	Field ES School	Designer Selection		Compass Project Management, Inc				
Whitman-Hanson PS	Maquan ES	Local Clearance - 09/10						
Whittier Voc PS	Whittier Reg Voc HS	Construction	Repair	Heery International	Gale Associates, Inc.		DBB - Contract Awarded	Greenwood Industries
Williamsburg PS	Anne T Dunphy IS	OPM Selection						

Master District Status List

Yellow = Wait List Project

Green = Green Repair

Red = Changes in last 60 days


District Name	School Name	Status	Preferred Schematic	OPM	Designer	Cx Authority	Procurement Status	CM/GC
Wilmington PS	Wilmington HS	OPM Selection						
Winchendon PS	Toy Town ES	Project Scope & Budget	Repair					
Winchester PS	Vinson-Owen ES	Preferred Schematic	New Construction	RF Walsh Collaborative Partners	Tappe Associates, Inc.		Undetermined	
Winchester PS	Winchester HS	Local Clearance - 09/10						
Winthrop PS	Winthrop Senior High	OPM Selection						
Woburn PS	Goodyear ES	Construction	New Construction	Municipal Building Consultants, Inc.	Tappe Associates, Inc.	Strategic Building Solutions	CMR - CM Selected	Gilbane Building Company
Worcester PS	North HS	Construction		Maguire Group Inc	City of Worcester		CMR - CM Selected	Gilbane Building Company

No. of Projects: 186

Project Status September 29, 2010

New Program: 123
 Waitlist: 13
 Green Repair: 39
 Closeout/Audit Complete: 11

 Total Projects: 186

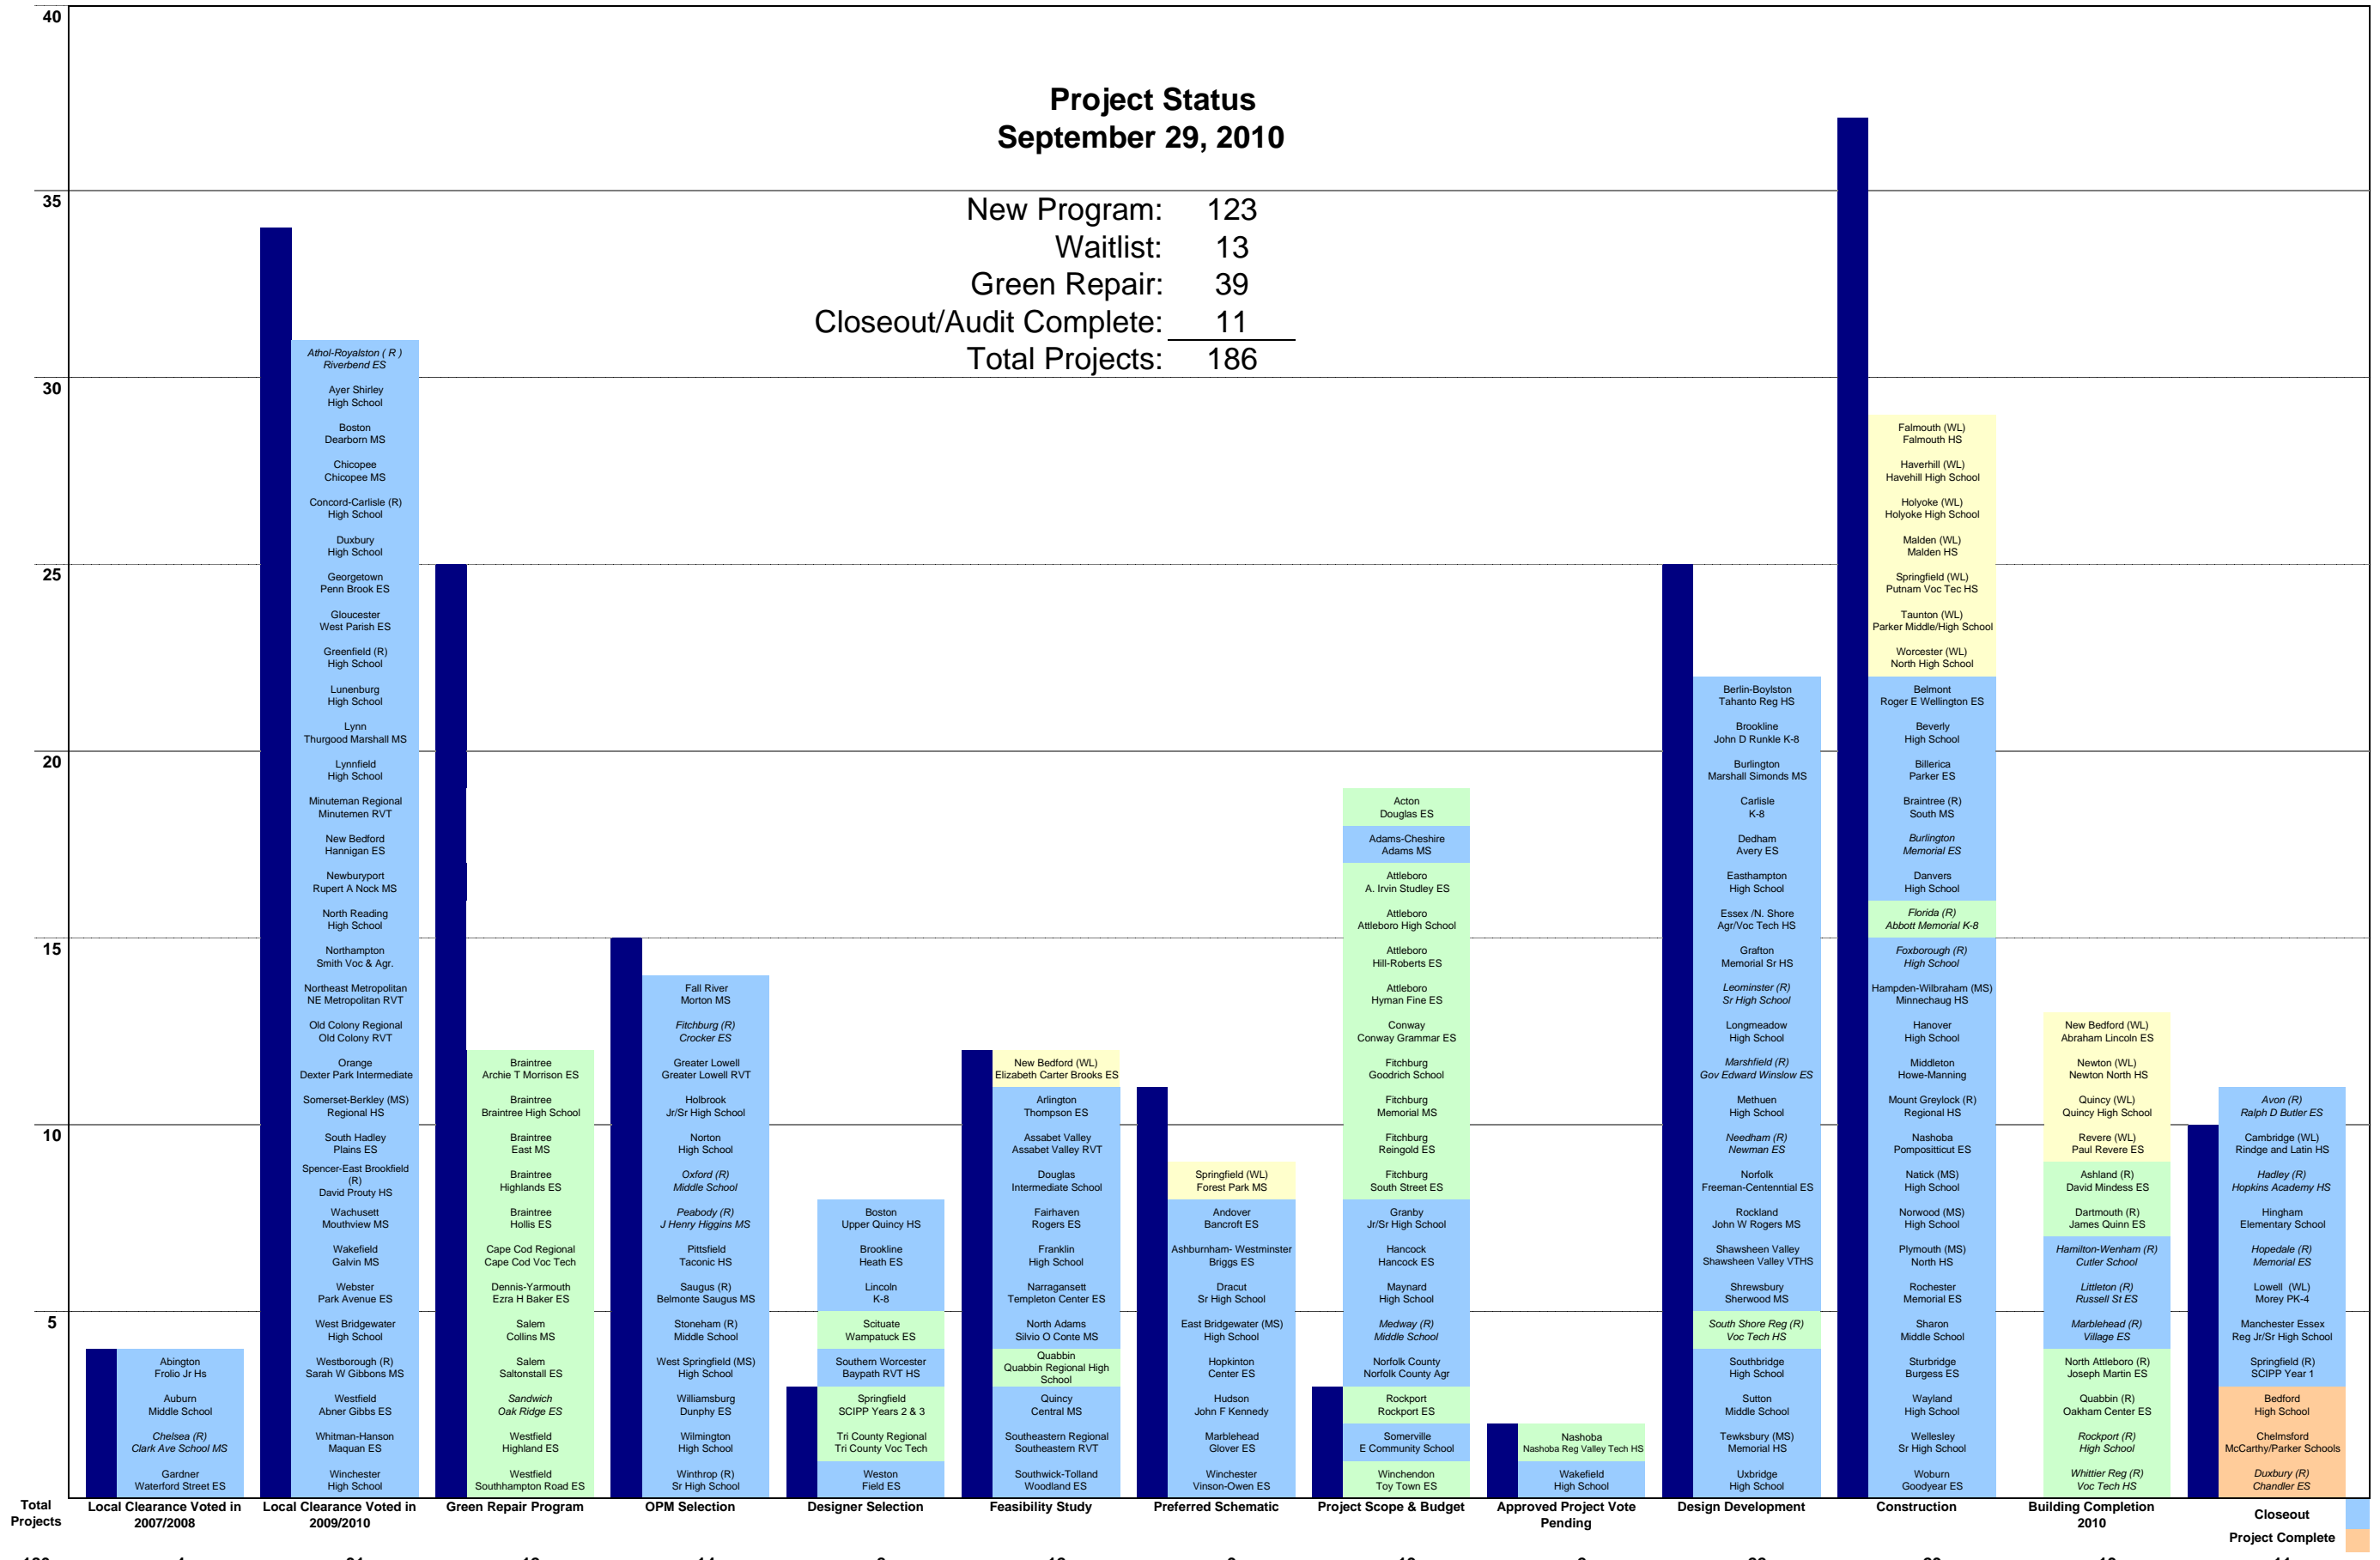

■ Capital Pipeline Status Presented at July 28, 2010 Board of Directors Meeting
(R) = Repair (MS) = Model School

■ Waitlist Projects
■ Green Repair Projects

2010 Estimated Bid Dates

Note bid dates are **Estimates ONLY**. Please contact Districts for exact information.

Total Project Budget denotes total District costs and does not denote the basis of the MSBA Total Facilities Grant.

- Denotes bid phase in progress or complete
 - Denotes estimated bid dates

DISTRICT	DESIGN BASIS FOR ENROLLMENT	PROJECT BUDGET <small>Shown in Millions</small>	CONSTRUCTION BUDGET <small>Shown in Millions</small>	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC
BURLINGTON	500	\$27.1	\$22.2	Memorial ES New Construction: GC Bids rcv'd 1/28. NTP Issued 2/18.											
*WELLESLEY	1500	\$132.0	\$98.5	Senior HS New Construction: Filed-Sub Bids rcv'd 2/8, 2/9, 2/10. GMP Issued 3/25.											
*WOBURN	320	\$26.5	\$19.9	Goodyear ES New Construction: Filed-Sub Bids rcv'd 3/11. GMP Issued 3/24.											
*SPRINGFIELD	1440	\$125.0	\$101.5	Putnam Vo-Tech New Construction: Filed-Sub Bids rcv'd 3/11. GMP Issued 5/3.											
MIDDLETON	553	\$31.3	\$24.3	Howe-Manning ES New Construction: Filed-Sub Bids rcv'd 3/10. G.C. Bids rcv'd 3/26. NTP Issued 4/5.											
PLYMOUTH	1350	\$92.2	\$72.0	North HS New Construction: Filed-Sub-Bids rcv'd 3/4. G.C. Bids rcv'd 3/30. NTP Issued 4/28.											
*BELMONT	575	\$40.0	\$28.7	Wellington ES New Construction: Filed-Sub-Bids rcv'd 5/11. Non-Trade Bids rcv'd 5/20. GMP Issued 7/20.											
QUABBIN	291	\$0.8	\$0.7	OakHam Center ES: Filed-Sub Bids rcv'd 4/30/10. NTP Issued 5/11.											
*ROCHESTER	635	\$26.5	\$20.5	Memorial ES Addition / Renovation: Filed-Sub-Bids rcv'd 5/5. GMP Issued 6/22.											
FLORIDA	115	\$0.5	\$0.4	Addot Memorial: Filed-Sub-Bids rcv'd 5/11. NTP Issued 5/17											
HAMPDEN-WILBRAHAM	1225	\$78.9	\$66.4	Minnechaug HS New Construction: Filed-Sub Bids rcv'd 6/15. G.C. Bids rcv'd 7/20. NTP Issued 7/27.											
HAMILTON-WENHAM	300	\$1.5	\$1.2	Cutler ES Repair: Filed-Sub Bids rcv'd 3/30. G.C. Bids rcv'd 4/8. NTP Issued 4/16.											
*SHARON	845	\$49.5	\$34.7	Middle School Addition / Renovation: Early Release Bid Package rcv'd 5/17. Filed-Sub Bids rcv'd 5/18. GMP Targeted September.											
ASHLAND	596	\$3.1	\$2.6	David Mindess ES Repair: Filed-Sub Bids rcv'd 4/26. G.C. Bids rcv'd 5/3. NTP issued 6/17.											
DARTMOUTH	845	\$1.3	\$1.1	James Quinn ES Repair: G.C. Bids rcv'd 2/25. NTP Issued 3/31.											
N. ATTLEBORO	717	\$0.8	\$0.7	Joseph Martin ES Repair: Filed-Sub Bids rcv'd 4/23. NTP Issued 6/4.											
ROCKPORT	331	\$1.1	\$1.0	Rockport HS Repair: G.C. Bids rcv'd 2/26. NTP Issued 3/17.											
MT GREYLOCK	641	\$1.4	\$1.2	MT Greylock Regional H.S Repair: Filed-Sub Bids rcv'd 4/29. G.C. Bids rcv'd 5/6. NTP Issued 5/6.											
WHITTIER REGIONAL	1206	\$3.2	\$2.6	Regional VTHS Repair: Filed-Sub Bids rcv'd 3/31. G.C. Bids rcv'd 4/7. NTP Issued 5/19.											
Subtotal	13,985	\$642.7	\$500.2												

2010 Estimated Bid Dates

Note bid dates are **Estimates ONLY**. Please contact Districts for exact information.

Total Project Budget denotes total District costs and does not denote the basis of the MSBA Total Facilities Grant.

- Denotes bid phase in progress or complete
 - Denotes estimated bid dates

DISTRICT	DESIGN BASIS FOR ENROLLMENT	PROJECT BUDGET	CONSTRUCTION BUDGET	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC	
*Projects Considering the CM @ Risk Method																
		Shown in Millions	Shown in Millions													
*WAYLAND	900	\$70.8	\$56.2					Wayland HS New Construction: Early Bid Packages rcv'd 6/30.						Filed-sub bid due 9/29 and 9/30. GMP Targeted for 10/15.		
NATICK	1300	\$89.0	\$70.8										Natick HS New Construction: Filed-Sub Bids rcv'd 9/1. NTP Targeted September.			
NASHOBA	600	\$37.8	\$28.8						Pompositticut ES Addition / Renovation: Filed-Sub Bids rcv'd 5/24. G.C. Bids rcv'd 6/7. NTP Issued 6/15.							
STURBRIDGE	860	\$46.9	\$36.4							Burgess ES Addition/Renovation: Filed-Sub Bids rcv'd 7/14. G.C. Bids rcv'd 7/27. NTP Issued 8/5.						
NORFOLK	585	\$37.5	\$28.9							Freeman-Centennial ES New Construction: Filed-Sub Bids Due 10/13. G.C. Bids Due 10/27. NTP Targeted November.						
TEWKSBURY	1100	\$84.2	\$65.9										Memorial HS (MS) New Construction: Filed-Sub Bids Due 9/15. G.C. Bids Due 9/29. NTP Targeted October.			
BILLERICA	500	\$34	\$27.1										Parker ES New Construction: Filed-Sub Bids rcv'd 8/19. G.C. Bids rcv'd 9/2. NTP Targeted September.			
*SOUTHBRIDGE	1050	\$76.5	\$60.1	Southbridge: CM@R Completed.					Southbridge HS New Construction: Early Site Package Bids rcv'd 8/19.				Filed-Sub Bids Due 12/23/10. GMP Targeted January 2011.			
*DEDHAM	310	\$23.4	\$19.9				Dedham CM@R Completed.			Avery ES New Construction: Filed-Sub Bids Due 10/29. GMP Targeted November.						
DANVERS	1000	\$79	\$62.7	Danvers High School Addition / Renovation: Early Bid Packages For Demo & Abatement Bids rcv'd 5/6. Swing Space Bids rcv'd 5/26.							Filed-Sub Bids Due 9/30.			G.C. Bids Due 10/20. NTP Targeted November.		
BROOKLINE	560	\$29.8	\$22.5						Runkle ES Addition / Renovation: Filed-Sub Bids Due 9/23. G.C. Bids Due 10/7. NTP Targeted November.							
*GRAFTON	900	\$72.4	\$57.4	Grafton CM@R Completed.					Memorial HS New Construction: Early Site/Foundation Package Due 9/24. Early Steel Packages Due 10/4.				Filed-Sub Bids Due 12/17. GMP Targeted December.			
*ROCKLAND	1525	\$86.2	\$66.5			Rockland CM@R Completed.			Rogers MS New Construction / HS Renovation: Early Site / Foundation Packages Due 9/28.				Filed-Sub Bids Due 12/1. GMP Targeted December.			
*UXBRIDGE	600	\$43.0	\$34.4					Uxbridge HS New Construction: CM RFQ Response rcv'd 9/8. RFP Due 10/1					Filed-Sub Bids Targeted December to January 2011. GMP Targeted February.			
MARSHFIELD	485	\$2.4	\$2.0											Marshfield Edward Winslow ES Repair: Filed-Sub Bids Targeted December.		
SO. SHORE RVT	595	\$3.2	\$2.6											Regional VTHS Repair: Filed-Sub & G.C. Bids Targeted December. NTP Targeted January 2011.		
ESSEX-NS	1440	\$125	\$96.5											Essex North Shore HS New Construction.		
SHAWSHEEN	1300	\$4.7	\$3.8											Shawsheen Voc Tech Repair: Filed Sub Due 11/3. G.C. Bids Due 11/10. NTP Targeted November.		
*NEEDHAM	759	\$27.4	\$21.9				Newman ES Repair: Early Modular Foundation Work Bids rcv'd 5/7.				Early Elec Duct Bank & Waterline Extension Work. Bids rcv'd 6/15.			Filed-Sub Bids Due 12/7. GMP Targeted December.		
Subtotal	16,369	\$973.2	\$764.4													
GRAND TOTAL	30,354	\$1.62 B	\$1.26B													
Number of Construction-related Employment			6,323													

2011 Estimated Bid Dates

Note bid dates are **Estimates ONLY**. Please contact Districts for exact information.

Total Project Budget denotes total District costs and does not denote the basis of the MSBA Total Facilities Grant.

- Denotes bid phase in progress or complete
 - Denotes estimated bid dates

DISTRICT <small>*Projects Considering the CM @ Risk Method</small>	DESIGN BASIS FOR ENROLLMENT	PROJECT BUDGET <small>Shown in Millions</small>	CONSTRUCTION BUDGET <small>Shown in Millions</small>	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC
*SHREWSBURY	900	\$47.3	\$37.0	Sherwood MS New Construction: Filed-Sub Bids Targeted December to January. GMP Targeted February.											
CARLISLE	700	\$20.0	\$15.6	Carlisle ES Addition/Renovation: Filed-Sub Bids Due 1/14. G.C. Bids due 1/28. NTP Targeted February.											
BURLINGTON	880	\$32.9	\$24.7	Marshall Simonds MS Addition/Renovation: Filed Sub and G.C Bids Targeted February to March. NTP Targeted April.											
BERLIN / BOYLSTON	560	\$44.0	\$34.2	Tahanto MS/HS New Construction: Filed-Sub and G.C. Bids Targeted February to April. NTP Targeted May.											
EASTHAMPTON	510	\$43.7	\$33.5	Easthampton HS New Construction: Filed-Sub and G.C. Bids Targeted March to May. NTP Targeted June.											
*LONGMEADOW	1000	\$78.5	\$63.8	Longmeadow HS New Construction: Filed-Sub Bids Targeted March to May. GMP Targeted June.											
LEOMINSTER	1805	\$45.9	\$32.7	Leominster HS Addition/Renovation: Filed-Sub and G.C. Bids Targeted March to May. NTP Targeted June.											
SUTTON	840	\$59.9	\$46.4	Sutton MS New Construction: Filed-Sub and G.C. Bids Targeted March to April. NTP Targeted June.											
METHUEN	2075	\$99.1	\$74.9	Methuen HS Addition/Renovation: Filed-Sub and G.C. Bids Targeted November to December. NTP Targeted January 2012.											
Subtotal	9,270	\$471.3	\$362.8												
GRAND TOTAL	9,270	\$471.3 M	\$362.8 M												
Number of Construction-related Employment				1,814											

**Projects in Construction
MSBA Grant Basis and Maximum Grant Amount**

New Program and Wait List Program Totals			39,013	7,112,241	2,152,133,542	\$1,732,743,782		\$1,157,183,941					
District	School	Grade	Projected Enroll	Proposed Square Footage	District Total Project Budget	MSBA Total Facility Grant Basis	Reimbursement Rate	Approximate Maximum Grant Amount	Project Type	CM-R/GC	Construction Start	Estimated Substantial Completion Date	Construction Status
Capital Pipeline Projects in Construction													
New Program Totals			22,450	4,407,084	1,139,874,460	\$1,041,212,470		\$542,767,814					
Ashland	David Mindess ES	3-5	628	96,000	\$2,384,021	\$2,173,515	48.68%	\$1,058,067	Design/Bid/Build	Greenwood Industries	22-Jun-10	27-Aug-10	New roof, skylight and ceiling tile replacement work is now complete. Punch list items remain and should be completed by the end of September.
Belmont	Roger E Wellington ES	K-5	575	88,203	\$40,664,431	\$31,000,050	40.00%	\$12,400,020	CM-R	Skanska	1-Mar-10	1-Jul-11	Concrete footings and walls are complete. Steel erection complete. Underslab utilities are being installed. Second floor slabs are being poured.
Beverly	Beverly HS	9-12	1,200	368,300	\$81,500,000	\$80,155,000	58.42%	\$46,826,551	Design/Bid/Build	CTA	6-Jan-09	16-Dec-11	Substantial Completion Dates: Phase 1A: New Academic Tower - Nov 18, 2010. Phase 1A: Auditorium/Music Rooms/Renovation Areas - Nov 18, 2010. Phase 1B: Locker Room/Upper Gym/Renovation Areas - substantially complete. Contractor working punch list. Phase 1C Existing Kitchen/Cafeteria/Renovation Areas: April, 2011. Phase 1D Field House/Renovated Areas: November 19, 2010. Phase 2 Existing Building Demolition/Site Work: December 16, 2011.
Billerica	Parker MS	K-5	500	89,093	\$34,007,436	\$31,565,064	55.69%	\$17,578,584	Design/Bid/Build	CTA	16-Sep-10	6-Sep-12	Pre-Phase 1 enabling work substantially complete. Notice to proceed issued to General contractor on 9/16/10.
Braintree	South MS	6-8	523	72,041	\$3,052,702	\$2,687,302	48.47%	\$1,302,535	Design/Bid/Build	Construction Dynamics	1-Apr-10	1-Oct-10	All construction has been completed with the exception of starting up the new boilers. This is scheduled to be accomplished prior to the need for heat in late October or early November 2010.
Burlington	Memorial ES	K-5	500	79,500	\$27,923,244	\$26,963,244	52.11%	\$14,050,546	Design/Bid/Build	CTA	8-Mar-10	11-Aug-11	The erection of structural steel is complete. The closing in of the exterior is on-going as is the installation of mechanical, plumbing and electrical work. Installation of metal stud walls and dry wall has begun.
Danvers	Danvers HS	9-12	1,000	249,792	\$79,843,732	\$74,694,239	56.11%	\$41,910,938	Design/Bid/Build	Bid ongoing	Oct-10	20-Aug-13	Abatement/Demo of links is now complete and graded. Infill of exterior walls from demo is on going and rerouting of electrical and tel/data is now complete.
Dartmouth	James Quinn ES	PK-5	925	122,000	\$1,358,304	\$1,358,304	47.64%	\$647,096	Design/Bid/Build	Advantage Glass, Inc.	6-Jun-10	30-Sep-10	Window replacement is over 95% complete. All academic areas are complete and remaining areas(Admin & Gym) will be complete by October 2010
Florida	Abbott Memorial K-8	K-8	115	23,241	\$490,347	\$487,829	60.76%	\$296,405	Design/Bid/Build	Waterman Excavating, Inc.	14-Jun-10	31-Aug-10	Waterproofing of foundation, installation of perimeter drain to mitigate water infiltration is complete. Punch list items that remain will be complete by 10/1/10.
Foxborough	Foxborough HS	9-12	885	218,500	\$19,993,200	\$19,037,185	49.31%	\$9,387,236	Design/Bid/Build	CTA	30-Mar-10	30-Dec-12	The building department toured the school on August 25th and signed off for the schools use. Boiler work continues and nearing completion for Oct 1st start-up. Roofing is 80% complete and will continue second shift and on Saturday to complete the metal edge trim on the completed areas. All site work curb cuts, handicap ramp and sidewalks are completed with only punch list work remaining.
Hamilton-Wenham	Cutler ES	K-5	298	45,000	\$1,429,720	\$1,429,720	42.58%	\$608,775	Design/Bid/Build	Thomas E. Snowden Inc.	6-Jun-10	31-Aug-10	HVAC replacement began in May and is 99% complete. Only Commissioning remains.
Hampden-Wilbraham	Minnechaug HS	9-12	1,225	231,467	\$78,986,658	\$76,796,379	61.73%	\$47,406,405	Design/Bid/Build	Fontaine Brothers	1-Aug-10	28-Jun-12	Site Contractor began clearing and grading the site. The General Contractor has secured the site.
Hanover	Hanover HS	9-12	800	156,000	\$59,953,688	\$59,484,384	47.21%	\$28,082,578	Design/Bid/Build	Callahan	1-Nov-09	1-May-12	Building slab on grade is complete. First floor framing underway. Exterior sheathing is 95% complete. Site work, drainage & utility installation is 95% complete. Brick facade installation underway. The project is approximately 55% complete.
Littleton	Russell Street ES	3-5	N/A	N/A	\$15,131,820	\$14,754,732	47.84%	\$7,058,664	Design/Bid/Build	Colantonio	25-Jun-09	30-Aug-10	The elevator is complete and elevator inspection is scheduled for the week of September 13th. All windows are installed. The project is substantially complete and 2 months ahead of schedule. Punch list remains and anticipated to be completed the second week of October.
Marblehead	Village ES	4-6	N/A	123,000	\$15,749,456	\$14,509,468	40.00%	\$5,803,787	Design/Bid/Build	Groom Construction	22-Dec-08	13-Aug-10	Construction on the project is now complete. Students and staff are using the building. Only minor punch list type work remains.
Middleton	Howe-Manning ES	4 - 6	553	83,500	\$31,392,734	\$30,114,849	51.47%	\$15,500,113	CM-R	CTA	22-Apr-10	13-Jan-12	Structural steel work has been completed. Mechanical, plumbing and electrical rough-in has begun.
Mount Greylock	Mount Greylock Reg HS	7-12	651	N/A	\$1,049,986	\$1,042,186	54.16%	\$564,448	Design/Bid/Build	Adams Plumbing & Heating	14-Jun-10	30-Sep-10	The heating system is approximately 80 % complete and will be completed prior to the need for heat.
					\$1,369,906	\$1,358,646	54.16%	\$735,843	Design/Bid/Build	Salco Construction	May-10	30-Sep-10	The renovations to the locker room areas are approximately 95% complete.
Nashoba	Pompositticut ES	K-2	600	98,030	\$37,829,870	\$35,640,351	50.85%	\$18,123,118	Design/Bid/Build	Stella P.J. Construction Corp.	16-Jun-10	12-Jun-12	Perimeter fencing, project layout, asbestos abatement and building demo completed during Phase 1A. Excavating for footings and concrete placement is underway.
Natick	Natick HS	9-12	1,300	254,095	\$88,987,414	\$82,016,562	52.63%	\$43,165,316	Design/Bid/Build	Brait Builders Corp.	15-Sep-10	15-Jun-13	Notice to proceed was issued to the General Contractor on 9/14/10. Mobilization and securing the site is complete.
North Attleboro	Joseph Martin ES	K-5	699	79,886	\$625,750	\$625,750	52.06%	\$325,765	Design/Bid/Build	Eagle Rivet Roof Services	14-Jun-10	1-Sep-10	Roof replacement is complete.
Norwood	Norwood HS	9-12	1,100	227,374	\$68,655,476	\$64,364,981	59.21%	\$38,110,505	Design/Bid/Build	Agostini	19-May-09	1-Jun-11	The project is approximately 67% complete. Sections C&D MEP rough-in continues. Interior wallboard and plaster is substantially complete. Ceiling grid and painting have begun. Tile flooring has begun in all toilet rooms. Sections A&B electrical finishes have begun. Site crews began construction of the east parking lot
Plymouth	Plymouth HS	9-12	1,350	267,357	\$92,249,040	\$79,420,894	58.24%	\$46,254,729	Design/Bid/Build	J&J Contractors	3-May-10	11-May-12	Contractor has mobilized and secured the site. Site work continues. Structural steel erection has begun
Quabbin	Oakham Center ES	PK-6	187	46,000	\$765,179	\$765,179	57.74%	\$441,814	Design/Bid/Build	Capeway Roofing	11-May-10	27-Aug-10	Roof and ceiling tile replacement projects are complete.
Rochester	Memorial ES	K-6	635	105,023	\$26,500,000	\$25,268,708	57.94%	\$14,640,689	CM-R	Gilbane	19-Apr-10	1-Sep-11	Phase 2 completed August 27- existing building turned back over to the town. Boiler room slab poured. Precast Bldg roof installation 50% complete. Interior framing 20% complete and MEP 35% complete. Site utilities 85% complete. Project is approximately 27% complete.
Rockport	Rockport MS/HS	6-12	598	117,184	\$1,006,384	\$1,006,384	41.10%	\$413,624	Design/Bid/Build	Feeley, McAnespie, Inc.	21-Jun-10	31-Aug-10	Roof replacement is on schedule and was completed Aug. 31st.
Sharon	Sharon MS	6-8	845	170,750	\$49,540,287	\$43,950,340	52.68%	\$23,153,039	CM-R	Consigli	1-Jun-10	22-Aug-11	All renovation work that could be accomplished to the existing school during the summer months has been accomplished. Students and staff are back in the existing building for this school year. Foundation work continues in front of the existing school building as does site work. Temporary driveways for dropping off and picking up students have been installed. Protective walkways separate the students from work area. All utilities such as telephone, electrical, gas and sewer have been connected.
Sturbridge	Burgess ES	K-6	860	129,300	\$46,926,630	\$41,844,754	57.92%	\$24,236,481	Design/Bid/Build	Fontaine Brothers	26-Aug-10	16-Oct-12	General Contractor mobilized, site secured.
Wayland	Wayland HS	9-12	900	154,171	\$70,800,000	\$62,500,000	40.00%	\$25,000,000	CM-R	Shawmut Design	28-Jun-10	1-Dec-11	Underground utilities are ongoing. Concrete footings and wall foundations are ongoing. Steel scheduled to arrive on October 7, 2010.
Wellesley	Wellesley HS	9-12	1,500	280,000	\$131,054,929	\$107,751,342	40.00%	\$43,100,537	CM-R	Turner	24-Aug-09	5-Mar-12	Concrete decking, exterior wall metal framing and sheathing continues. Brickwork ongoing at Bldg C. Mock-up window due w/e September 13, 2010. Balance of windows units due November, 2010.
Whittier Reg	Whittier Reg Voc Tech HS	9-12	1,178	365,000	\$2,147,762	\$2,069,360	66.18%	\$1,369,502	Design/Bid/Build	Greenwood Industries	28-Jun-10	15-Sep-10	Roof replacement was completed on September 15, 2010.

**Projects in Construction
MSBA Grant Basis and Maximum Grant Amount**

District	School	Grade	Projected Enroll	Proposed Square Footage	District Total Project Budget	MSBA Total Facility Grant Basis	Reimbursement Rate	Approximate Maximum Grant Amount	Project Type	CM-R/GC	Construction Start	Estimated Substantial Completion Date	Construction Status
Woburn	Goodyear ES	K-5	320	67,277	\$26,504,354	\$24,375,769	54.21%	\$13,214,104	CM-R	Gilbane	24-Mar-10	15-Jul-11	Structural steel has been erected. Concrete slab and concrete floor decks have been poured. Mechanical, electrical, plumbing and fire protection trades work on-going.
Wait List Projects in Construction													
Wait List Program Totals			16,563	2,705,157	1,012,259,082	\$691,531,312		\$614,416,127					
Cambridge	Rindge & Latin HS	9-12	1,529	82,938	\$112,116,300	\$33,620,000	69.47%	\$33,973,519	Design/Bid/Build	W.T. Rich, Inc.	May-07	Jul-11	Phase 1A is complete with ongoing work in phase 1B as well as phase 2 which began in July 2010.
Falmouth	Falmouth HS	9-12	1,003	266,654	\$86,325,000	\$56,263,993	59.70%	\$33,589,604	Design/Bid/Build	TLT Construction	Jun-05	Nov-10	Project is approximately 95% complete at this time with Phase 2 completion scheduled for Fall 2010.
Haverhill	Haverhill HS	9-12	1,864	N/A	\$33,739,532	\$33,739,532	68.48%	\$23,104,832	Design/Bid/Build	CTA	Apr-04	Aug-11	Major work on building is complete. Remaining work consists of site and perimeter work which is ongoing. The locker replacement and painting is scheduled for Summer 2011.
Holyoke	Holyoke HS	9-12	1,252	N/A	\$22,738,000	\$15,964,800	90.00%	\$14,368,320	Design/Bid/Build	WJ Mountford	Mar-10	Sep-10	HVAC, windows and ADA upgrades are ongoing with an approximate completion date of September 2010.
Malden	Malden HS	9-12	1,720	365,271	\$77,033,447	\$77,072,181	90.00%	\$69,364,963	CM-R	Gilbane	8-Aug-10	Jun-12	This is a complete renovation of the existing high school. Work has been divided into nine (9) phases. The project is approximately 50 percent complete.
New Bedford	Abraham Lincoln ES	K-5	450	96,000	\$28,072,000	\$17,952,000	90.00%	\$23,494,800	Design/Bid/Build	CTA	1-Jun-09	Dec-10	Substantial completion date for Phase I, the new facility, achieved on schedule, August 16, 2010. Minor punchlist work remaining. FF&E installation complete. Substantial completion for Phase II, existing building demolition, is December 15, 2010. Abatement is complete. Demo of existing building began September 14, 2010.
Newton	Newton North HS	9-12	1,795	375,000	\$197,499,511	\$77,628,610	60.00%	\$46,577,166	CM-R	Dimeo Construction	Feb-08	Aug-10	The permanent certificate of occupancy was received in August. Phase II, demo and abatement of the existing building, has begun.
Quincy	Quincy HS	9-12	1,650	368,000	\$126,766,465	\$80,228,599	90.00%	\$87,205,739	CM-R	Gilbane	Jun-10	Oct-10	Construction has been completed. The school staff began moving into the building in August of this year. Only punch list work needs to be completed.
Revere	Paul Revere ES	K-5	350	57,500	\$17,409,000	\$10,752,500	90.00%	\$16,152,185	Design/Bid/Build	Delulis Brothers	Nov-10	Aug-10	The building has been completed. Furnishings, fixtures and equipment along with students and staff are in the building.
Springfield	Putnam Voc Tech HS	9-12	1,400	315,000	\$125,000,000	\$125,000,000	90.00%	\$112,500,000	CM-R	Consigli	18-May-10	Jul-12	Underslab utilities, footings and foundations are ongoing. Steel erection for Bldg A is scheduled to start on September 27, 2010.
Taunton	Parker MS	5-8	2,350	539,224	\$112,759,827	\$112,759,827	83.00%	\$93,590,656	Design/Bid/Build	Bacon-Agostini	Jul-10	Jan-12	Renovation of the existing High School continues and now stands at approximately 80% complete.
Worcester	North HS	9-12	1,200	239,570	\$72,800,000	\$50,549,270	90.00%	\$60,494,343	CM-R	Gilbane	24-Sep-08	Jul-11	Metal stud framing is 85% complete. Drywall installation is 60% complete. MEP rough-ins and fire suppression systems are ongoing. Interior masonry walls are 90% complete and exterior masonry is underway at the south and north elevations. The overall project is approximately 45% complete.

Bold and italicized totals include an additional grant/loan amount to the Reimbursement Rate.
