

# Project Overview Report

## March 7, 2012

A total of 307 projects are currently in the MSBA's Capital Pipeline. The following summary table provides the category (e.g., New Program, Green Repair) and the number of projects in each phase (e.g., Local Clearance, Construction):

	Total	Local Clearance	Consultant Selection	Feasibility Study/Schematic Design	Design Development	Construction	Project Completion	Closeout	Audit
New Program	125	2	12	30	23	35	13	6	4
Waitlist	14	0	0	0	2	1	3	7	1
Green Repair	168	0	0	1	25	60	10	68	4
<b>Total</b>	<b>307</b>	<b>2</b>	<b>12</b>	<b>31</b>	<b>50</b>	<b>96</b>	<b>26</b>	<b>81</b>	<b>9</b>

The MSBA utilizes the Project Status chart (see attached) to account for the ongoing status of all District Statements of Interest (SOIs) in the Capital Pipeline. Activity for some of the key milestones is summarized in the table on page 2, with the numbers reported indicative of the category requirements. For instance, enrollment certifications are not required for all projects (e.g., repairs) and Owner's Project Managers (OPMs) are not mandatory for construction projects estimated to cost less than \$1.5 million unless required by the MSBA.

### Eligibility Period

There are 15 Districts in the Eligibility Period. Eleven of those Districts are seeking local funding and authorization within the next 60 days, and two of the 15 Districts have secured funding. The remaining two Districts have yet to confirm their dates for action.

An agreed-upon enrollment is a key prerequisite for the MSBA to commence a Feasibility Study with a District. To begin the enrollment projection process, a District must file enrollment information utilizing the MSBA's online enrollment projection tool.

### Capital Pipeline **Consultant Selection**

After the MSBA and the District have completed all Eligibility Period requirements, the District procures an Owner's Project Manager and then a Designer. There are seven Districts in the Capital Pipeline who still need to procure an OPM.

After a District has selected an OPM and executed a contract with that OPM, it selects a Designer utilizing either a local designer selection process for projects under \$5 million or the MSBA's Designer Selection Panel (DSP) for projects over \$5 million. There are 12 Districts in the Capital Pipeline who still need to procure a Designer.

	<b>District Action to Complete</b>	<b>MSBA/ District Collaboration</b>	<b>Completed Activity this Period</b>	<b>Total Completed to Date</b>	<b>Total</b>
Owner's Project Manager	0	7	3	117	Over \$84 million in OPM fees*
Designer	7	5	5	145	Over \$207.6 million in Designer Fees*

\*Does not include OPM and Designer Fees associated with repair projects

### Owner's Project Managers

Since the last report, the following three Districts have completed the OPM selection process:

- Andover – Bancroft Elementary School
- Somerville – East Community School
- Winchester – Winchester High School

The following Districts are tentatively scheduled for the upcoming OPM Review Panel meetings:

<b>Panel Date</b>	<b>District/School</b>	<b>Project Description Status</b>	<b>Estimated Project Cost</b>
4/2/2012	Lynn – Thurgood Marshall Middle School	Feasibility Study	\$50-\$65 million
5/7/2012	Old Colony RSD – Old Colony RVTHS	Repair	\$2-\$2.5 million

### Designers

Since the last Project Overview Report, the DSP has met four times, resulting in five additional Districts completing the designer selection process.

<b>Panel Date</b>	<b>District/School</b>	<b>Status</b>	<b>Estimated Project Cost</b>	<b># of Proposals Received</b>	<b>Top 3 Ranked Firms</b>	<b>Interviews Requested</b>	<b>First-Ranked Selection</b>
1/10/12	Newburyport – Nock/ Molin Middle School	Designer Selection	\$9.6 - \$14.4 million	7	- Miller Dyer Spears - SMMA - Flansburgh	Interviews held	Miller Dyer Spears
1/10/12	Whitman-Hanson RSD - Maquan Elementary School	Designer Selection	\$20 - \$30 million	5	- Fletcher Thompson - Raymond Design - Turowski2	Yes	TBD
1/10/12	Winchester – Winchester High School	Designer Selection	\$60 - \$90 million	14	- SMMA - Tappe - Flansburgh	Yes	TBD
1/24/12	Auburn – Auburn Middle School	Designer Selection	\$20 - \$40 million	12	- ARC - Lamoureux Pagano - OMR	Interviews held	Lamoureux Pagano

Panel Date	District/School	Status	Estimated Project Cost	# of Proposals Received	Top 3 Ranked Firms	Interviews Requested	First-Ranked Selection
1/24/12	Chicopee – Chicopee Academy	Designer Selection	\$15 - \$20 million	8	- Caolo & Bieniek - DRA - Lamoureux Pagano	Yes	TBD
2/7/12	Whitman-Hanson RSD - Maquan Elementary School	Designer Selection	\$20 - \$30 million	5	- Fletcher Thompson - Raymond Design - Turowski2	Interviews held	Turowski2
2/7/12	Winchester – Winchester High School	Designer Selection	\$60 - \$90 million	14	- SMMA - Tappe - Flansburgh	Interviews held	SMMA
2/28/12	Chicopee – Chicopee Academy	Designer Selection	\$15 - \$20 million	8	- Caolo & Bieniek - DRA - Lamoureux Pagano	Interviews held	Caolo & Bieniek
2/28/12	Berkshire Hills RSD – Monument Mountain RHS	Designer Selection	\$25 - \$30 million	11	- Flansburgh - SMMA - Tetra Tech	Yes	TBD
2/28/12	Spencer-East Brookfield RSD – David Prouty High School	Designer Selection	\$30 - \$40 million	7	- Arch. Res. Cambr. - Des. Part. of Cambr. - Lamoureux Pagano	Yes	TBD

The following Districts are tentatively scheduled for upcoming DSP meetings:

- Berkshire Hills RSD – Monument Mountain Regional High School – interviews on March 13, 2012
- Spencer-East Brookfield RSD – David Prouty High School – interviews on March 13, 2012
- Wachusett RSD – Mountainview Middle School – selection on March 27, 2012
- Revere – McKinley Elementary School – selection on April 24, 2012 (tentative)
- Winthrop – Winthrop High School – TBD

### Commissioning

Since the last Project Overview Report, the MSBA has assigned Commissioning Consultants to an additional eight projects as presented in the table below. The MSBA has executed 167 Commissioning Consultant contracts to date, totaling \$13.6 million.

District	School	Estimated Const. Cost (million)	Commissioning Consultant	Contract Amount
Wilmington	Wilmington High School	\$64.94	Symmes, Maini & McKee	\$144,333
Springfield	Green Repair - Multiple Schools	\$8.62	Building Enclosure Associates	\$165,000
Mendon-Upton RSD	Miscoe Hill Intermediate School	\$3.38	Sebesta Blomberg & Associates	\$46,700
Lowell	Green Repair - Multiple Schools	\$5.60	Building Enclosure Associates	\$88,000
Lexington	Joseph Estabrook Elementary School	\$31.10	BVH Integrated Services, Inc.	\$88,166
Springfield	Dryden Memorial Elementary School	\$10.50	BVH Integrated Services, Inc.	\$51,126
Lynnfield	Lynnfield High School	\$3.17	Fitzemeyer & Tocci Associates	\$13,687
Hadley	Hopkins Academy	\$0.52	Russo Barr Associates, Inc.	\$28,100

District	School	Estimated Const. Cost (million)	Commissioning Consultant	Contract Amount
<b>Total</b>		<b>\$127.82 million</b>	<b>Total</b>	
			<b>\$625,112</b>	

There are currently no projects for which we are seeking proposals or negotiating Work Orders.

Projects that are in the queue for assignment of a Commissioning Consultant and for which contract documents are being drafted include:

District	School
Assabet Valley RSD	Assabet Valley Vocational High School
Franklin	Franklin High School
Southern Worcester County Voc/Tech RSD	Bay Path Regional Voc/Tech High School
Stoneham	Stoneham Middle School
Williamsburg	Anne T. Dunphy Intermediate School
Haverhill	Green Repair - Multiple Schools
Southwick-Tolland RSD	Woodland Elementary School

**Status of Green Repair Program**


169 projects participating in the Green Repair Program have received authorization to enter into a PFA, totaling \$366,647,226 in Total Project Costs and \$222,885,258 in MSBA Total Facilities Grant funding.

**Green Repair Project Phase**

99% - 169 projects authorized for PFA

Total Project Budgets \$366,647,226

Total Maximum Facilities Grants \$222,885,258

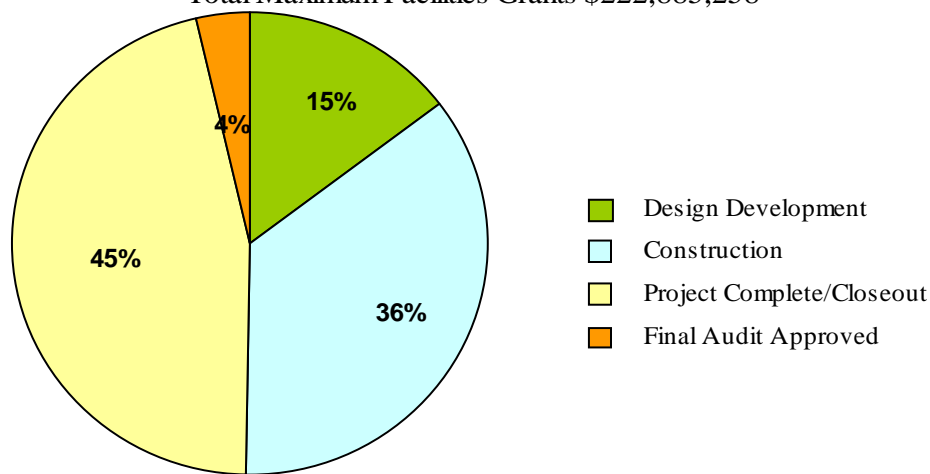

## Construction Bids – Green Repair

The following displays the total anticipated number of projects going out to bid between March 1, 2012 – April 30, 2012:

	<b>Roofs</b>	<b>Windows</b>	<b>Boilers</b>
March	11	11	7
April	7	2	1
<b>Total Remaining Bids</b>	<b>18</b>	<b>13</b>	<b>8</b>

Of the bids reviewed:

- 78% of roof projects have come in under budget
- 71% of window projects have come in under budget
- 47% of boiler projects have come in under budget

### Districts withdrawing from the Green Repair Program:

The following project is withdrawing from the Green Repair Program:

<b>District</b>	<b>School</b>	<b>Scope</b>	<b>Invite Date</b>
Westport	Westport Middle School	Windows	November 17, 2010

# Massachusetts School Building Authority

No. of Projects: 322

## Master District Status List

Yellow = Wait List Project
Green = Green Repair
Red = Changes in last 60 days

District Name	School Name	Status	Preferred Schematic	OPM	Designer	Cx Authority	Procurement Status	CM/GC
Abington PS	Woodsdale IS	Building Completion 2012	Repair	RF Walsh Collaborative Partners	Gale Associates, Inc.	Russo Barr Associates, Inc.		
Abington PS	Frolio JHS	Eligibility Period					Undetermined	
Acton PS	Douglas ES	Closeout/Audit	Repair	N/A	CBI Consulting Inc.		Undetermined	Gibson Roofs
Adams-Cheshire PS	Adams MS	Building Completion 2013	Addition/Renovation	URS Corporation	Tessier Associates, Inc.	Strategic Building Solutions, LLC	CMR - CM Selected	Gilbane Building Company
Agawam PS	Agawam Junior HS	Design Development	Repair	Municipal Building Consultants, Inc.	CSS Architects Incorporated	Building Enclosure Associates		
Amherst-Pelham PS	Amherst Reg MS	Building Completion 2012	Repair	Strategic Building Solutions, LLC	Bradley Architects, Inc.	Russo Barr Associates, Inc.		
Andover PS	Bancroft ES	Design Development	New Construction	Town of Andover	Symmes Maini & McKee Associates, Inc.	Sebesta Blomberg & Associates, Inc.	CMR - CM Selected	Skanska USA Building, Inc.
Andover PS	Andover West MS	Closeout/Audit	Repair	Skanska USA Building Inc.	Russo Barr Associates, Inc.	Simpson Gumpertz & Heger Inc.		
Arlington PS	Thompson ES	Design Development		PMA Consultants	HMFH Architects, Inc.	Consulting Engineering Services, LLC	DBB - In Design	
Arlington PS	M Norcross Stratton ES	Closeout/Audit	Repair	PMA Consultants	Turowski2 Architecture, Inc.		Undetermined	Unicon, Inc. and Federal Construction Corp.
Ashburnham-West PS	Briggs ES	Design Development	New Construction	STV, Inc.	Lamoureux Pagano & Associates, Inc.	Foreman Building Commissioning, LP	CMR - CM Selected	Consigli Construction Co.
Assabet Valley PS	Assabet Valley Voc HS	Design Development	Repair	Strategic Building Solutions, LLC	Design Partnership of Cambridge, Inc.			
Athol-Royalston PS	Riverbend ES	OPM Selection						
Attleboro PS	Hyman Fine ES	Closeout/Audit	Repair	Skanska USA Building, Inc.	Russo Barr Associates, Inc.	Gale Associates, Inc.		
Attleboro PS	A. Irvin Studley ES	Closeout/Audit	Repair	Skanska USA Building, Inc.	Russo Barr Associates, Inc.	Gale Associates, Inc.		
Attleboro PS	Hill-Roberts ES	Closeout/Audit	Repair	Skanska USA Building, Inc.	Russo Barr Associates, Inc.	Gale Associates, Inc.		
Attleboro PS	Attleboro HS	Closeout/Audit	Repair	Skanska USA Building, Inc.	Russo Barr Associates, Inc.	Gale Associates, Inc.		
Auburn PS	Auburn MS	Feasibility Study		Skanska USA Building, Inc.	Lamoureux Pagano & Associates, Inc.			
Avon PS	Ralph D Butler ES	Closeout/Audit	Repair	Skanska USA Building Inc.	Knight, Bagge & Anderson, Inc.	Cannon Design		
Ayer PS	Ayer HS	Feasibility Study		Dore and Whittier Management Partners	Symmes Maini & McKee Associates, Inc.			
Barnstable PS	West Barnstable ES	Building Completion 2012	Repair	PMA Construction Services	Gale Associates, Inc.	CBI Consulting Inc.		
Bellingham PS	Clara Macy ES	Eligibility Period						
Bellingham PS	Bellingham Memorial MS	Closeout/Audit	Repair	Daedalus Projects Inc	Richard D. Kimball Company, Inc.	WSP Flack + Kurtz	Undetermined	General Air Conditioning & Heating, Inc.

# Master District Status List

Yellow = Wait List Project

Green = Green Repair

Red = Changes in last 60 days

District Name	School Name	Status	Preferred Schematic	OPM	Designer	Cx Authority	Procurement Status	CM/GC
Belmont PS	Roger E Wellington ES	Substantial Completion	New Construction	PMA Consultants	Jonathan Levi Architects LLC	Strategic Building Solutions, LLC	CMR - CM Selected	Skanska USA Building, Inc.
Berkshire Hills PS	Monument Mt Reg HS	Designer Selection		Strategic Building Solutions, LLC				
Berlin-Boylston PS	Tahanto Reg HS	Building Completion 2013	New Construction	PMA Consultants	HMFH Architects, Inc.	Strategic Building Solutions, LLC	DBB - Contract Awarded	CTA Construction
Beverly PS	Beverly HS	Substantial Completion	Addition/Renovation	Heery International	Mount Vernon Group Architects, Inc.		DBB - Contract Awarded	CTA Construction Co.
Billerica PS	Billerica Memorial HS	Building Completion 2012	Repair	Municipal Building Consultants, Inc.	Knight, Bagge & Anderson, Inc.	Building Enclosure Associates		
Billerica PS	Parker ES	Building Completion 2012	New Construction	Joslin, Lesser & Associates, Inc.	Symmes Maini & McKee Associates, Inc.	Sebesta Blomberg & Associates, Inc.	DBB - Contract Awarded	CTA Construction Co
Blackstone Valley Reg PS	Blackstone Valley HS	Substantial Completion	Repair	Strategic Building Solutions, LLC	Reinhardt Associates, Inc.	Cannon Design		
Boston PS	Clarence R Edwards MS	Closeout/Audit	Repair	Daedalus Projects Inc	BLW Engineers, Inc.	Rist-Frost-Shumway Engineering, P.C.		
Boston PS	Washington Irving MS	Closeout/Audit	Repair	Daedalus Projects Inc	Gale Associates, Inc.	Simpson Gumpertz & Heger Inc.		
Boston PS	Thomas A Edison JHS	Closeout/Audit	Repair	Daedalus Projects Inc	BLW Engineers, Inc.	Simpson Gumpertz & Heger Inc.		
Boston PS	Joseph Lee ES*	Closeout/Audit	Repair	Daedalus Projects Inc	BLW Engineers, Inc./Gale Associates, Inc.	Simpson Gumpertz & Heger Inc.		
Boston PS	Excel HS	Building Completion 2012	Repair	Daedalus Projects Inc	Gale Associates, Inc.	Simpson Gumpertz & Heger Inc.		
Boston PS	Quincy Upper School	Feasibility Study		City of Boston	HMFH Architects, Inc.			
Boston PS	Dearborn MS	OPM Selection						
Boxford PS	Harry Lee Cole Primary	Closeout/Audit	Repair		Russo Barr Associates, Inc.		Undetermined	MDM Engineering, Inc
Braintree PS	South MS	Closeout/Audit	Repair	Town Employee	Habeeb & Associates Architects, Inc.		DBB - Contract Awarded	Construction Dynamics
Braintree PS	East MS	Closeout/Audit	Repair	RF Walsh Collaborative Partners	Habeeb & Associates Architects, Inc.	Cannon Design		
Braintree PS	Braintree HS	Closeout/Audit	Repair	RF Walsh Collaborative Partners	Habeeb & Associates Architects, Inc.	Cannon Design		
Braintree PS	Archie T Morrison ES	Closeout/Audit	Repair	RF Walsh Collaborative Partners	Habeeb & Associates Architects, Inc.	Cannon Design		
Braintree PS	Highlands	Closeout/Audit	Repair	RF Walsh Collaborative Partners	Habeeb & Associates Architects, Inc.	Cannon Design		
Braintree PS	Hollis ES	Closeout/Audit	Repair	RF Walsh Collaborative Partners	Habeeb & Associates Architects, Inc.	Cannon Design		
Brockton PS	West Junior HS	Building Completion 2012	Repair	Skanska USA Building Inc.	CSS Architects Incorporated	Simpson Gumpertz & Heger Inc.		
Brockton PS	Brockton HS	Building Completion 2012	Repair	Skanska USA Building Inc.	CSS Architects Incorporated	Simpson Gumpertz & Heger Inc.		
Brockton PS	Hancock ES	Closeout/Audit	Repair	Skanska USA Building Inc.	CSS Architects Incorporated	Simpson Gumpertz & Heger Inc.		
Brockton PS	Downey ES	Building Completion 2012	Repair	Skanska USA Building Inc.	CSS Architects Incorporated	Simpson Gumpertz & Heger Inc.		
Brockton PS	Oscar F Raymond ES	Building Completion 2012	Repair	Skanska USA Building Inc.	CSS Architects Incorporated	Simpson Gumpertz & Heger Inc.		

# Master District Status List

Yellow = Wait List Project

Green = Green Repair

Red = Changes in last 60 days

District Name	School Name	Status	Preferred Schematic	OPM	Designer	Cx Authority	Procurement Status	CM/GC
Brockton PS	East Junior HS	Building Completion 2012	Repair	Skanska USA Building Inc.	CSS Architects Incorporated	Rist-Frost-Shumway Engineering, P.C.		
Brockton PS	North Junior HS	Building Completion 2012	Repair	Skanska USA Building Inc.	CSS Architects Incorporated	Rist-Frost-Shumway Engineering, P.C.		
Brockton PS	Edgar B Davis ES	Building Completion 2012	Repair	Skanska USA Building Inc.	CSS Architects Incorporated	Simpson Gumpertz & Heger Inc.		
Brookfield PS	Brookfield ES	Building Completion 2012	Repair	Diversified Project Management	Habeeb & Associates Architects, Inc.	Cannon Design		
Brookline PS	Heath K-8	Building Completion 2012	Addition/Renovation	Town of Brookline Building Department	Miller Dyer Spears Inc.	Consulting Engineering Services, LLC		
Brookline PS	John D Runkle K-8	Building Completion 2012	Addition/Renovation	Town of Brookline Building Department	Design Partnership of Cambridge, Inc.	Consulting Engineering Services, LLC	DBB - Contract Awarded	G&R construction Inc.
Burlington PS	Marshall Simonds MS	Building Completion 2013	Addition/Renovation	Construction Monitoring Services, Inc.	Knight, Bagge & Anderson, Inc.	RDK Engineers	DBB - Contract Awarded	CTA Construction Co.
Burlington PS	Memorial ES	Substantial Completion	New Construction	Construction Monitoring Services, Inc.	Knight, Bagge & Anderson, Inc.	Consulting Engineering Services, LLC	DBB - Contract Awarded	CTA Construction Co.
Cambridge PS	Cambridge Rindge and Latin HS	Closeout/Audit			HMFH Architects, Inc.		DBB - Contract Awarded	W.T. Rich, Inc.
Canton PS	Rodman Pre-K Center	Closeout/Audit	Repair	Maguire Group	Russo Barr Associates, Inc.	Cannon Design		
Canton PS	Canton HS	Closeout/Audit	Repair	Maguire Group	Russo Barr Associates, Inc.	Cannon Design		
Cape Cod Region Voc Tech PS	Cape Cod Regional Voc / Tech HS	Building Completion 2012	Repair	URS Corporation	Garcia Galuska DeSousa	N/A		
Carlisle PS	Carlisle K-8	Building Completion 2012	Addition/Renovation	Daedalus Projects, Inc.	HMFH Architects, Inc.	Horizon Engineering Associates, LLP	DBB - Contract Awarded	H.V. Collins Company
Central Berkshire PS	Craneville ES	Building Completion 2012	Repair	Daedalus Projects Inc	Bradley Architects, Inc.	Strategic Building Solutions, LLC		
Central Berkshire PS	Kittredge ES	Building Completion 2012	Repair	Daedalus Projects Inc	Bradley Architects, Inc.	Strategic Building Solutions, LLC		
Chatham PS	Chatham HS	Designer Selection		Skanska USA Building, Inc.				
Chelmsford PS	Byam ES	Closeout/Audit	Repair	Vertex Construction Services, Inc.	Russo Barr Associates, Inc.	Simpson Gumpertz & Heger Inc.		
Chelmsford PS	Chelmsford HS	Substantial Completion	Repair	Vertex Construction Services, Inc.	Russo Barr Associates, Inc.	Simpson Gumpertz & Heger Inc.		
Chelsea PS	Clark Avenue MS	Eligibility Period			Jacobs			
Chicopee PS	Chicopee Academy	Designer Selection		ARCADIS U.S., Inc.	Caolo & Bieniek Associates, Inc.			
Concord-Carlisle PS	Concord Carlisle HS	Design Development		KV Associates, Inc.	OMR Architects, Inc.	Strategic Building Solutions, LLC	CMR - Procurement Pending	
Conway PS	Conway Grammar ES	Closeout/Audit	Repair		Richardson Gorman Architects		Undetermined	RAC Builders, Inc.
Danvers PS	Danvers HS	Building Completion 2013	Addition/Renovation	Construction Monitoring Services, Inc.	DiNisco Design Partnership, Limited	Turner Facilities Management Solutions	DBB - Contract Awarded	Bacon Construction Co., Inc.
Dartmouth PS	James M. Quinn ES	Closeout/Audit	Repair	Vertex Construction Services, Inc.	Russo Barr Associates, Inc.	Gale Associates, Inc.		
Dartmouth PS	James M. Quinn ES	Closeout/Audit	Repair					
Dedham PS	Avery ES	Substantial Completion	New Construction	Construction Monitoring Services, Inc.	Dore & Whittier Architects, Inc.	WSP Flack + Kurtz	CMR - CM Selected	Consigli Construction Co



# Master District Status List

Yellow = Wait List Project

Green = Green Repair

Red = Changes in last 60 days

District Name	School Name	Status	Preferred Schematic	OPM	Designer	Cx Authority	Procurement Status	CM/GC
Dennis-Yarmouth PS	Ezra H Baker ES	Building Completion 2012	Repair	STV Construction, Inc.	Knight, Bagge & Anderson, Inc.	CBI Consulting Inc.		
Douglas PS	Douglas IS	Design Development		Heery International, Inc	DiNisco Design Partnership, Limited	Consulting Engineering Services, LLC	DBB - In Design	
Dracut PS	Dracut SHS	Design Development	Addition/Renovation	RF Walsh Collaborative Partners	Mount Vernon Group Architects, Inc.	RDK Engineers	DBB - In Design	
Dudley-Charlton Reg PS	Shepherd Hill Reg HS	Closeout/Audit	Repair	Pinck & Co., Inc.	ICON architecture, inc.	Cannon Design		
Duxbury PS	Duxbury HS	Design Development		KV Associates, Inc.	Mount Vernon Group Architects, Inc.	WSP Flack + Kurtz	CMR - Procurement Pending	
East Bridgewater PS	East Bridgewater HS	Building Completion 2013	Model School	RF Walsh Collaborative Partners	Ai3 Architects LLC	Foreman Building Commissioning, LP	DBB - Contract Awarded	Fontaine Bros., Inc.
Easthampton PS	Easthampton HS	Building Completion 2013	New Construction	Strategic Building Solutions, LLC	Caolo & Bieniek Associates, Inc.	Consulting Engineering Services, LLC	DBB - Contract Awarded	Fontaine Bros., Inc
Essex North Shore Agr and Tech PS	Essex North Shore Agr and Tech School	Design Development	New Construction	PMA Consultants	Design Partnership of Cambridge, Inc.	Turner Facilities Management Solutions	CMR - CM Selected	Gilbane Building Company
Fairhaven PS	Rogers ES	Design Development		Daedalus Projects Inc	HMFH Architects, Inc.	Consulting Engineering Services, LLC	DBB - In Design	
Fairhaven PS	Hastings MS	Closeout/Audit	Repair	Daedalus Projects Inc	Durland Van Voorhis Architects, Inc.	Gale Associates, Inc.		
Fall River PS	Morton MS	Building Completion 2013		Maguire Group Inc.	Mount Vernon Group Architects, Inc.	Sebesta Blomberg & Associates, Inc.	DBB - Contract Awarded	J&J Contractors Inc.
Falmouth PS	Falmouth High School	Closeout/Audit	Addition/Renovation	Gilbane Building Company	DiNisco Design Partnership, Limited		DBB - Contract Awarded	TLT Construction
Falmouth PS	East Falmouth ES	Closeout/Audit	Repair		Keenan + Kenny Architects, LTD	Gale Associates, Inc.		
Falmouth PS	North Falmouth ES	Closeout/Audit	Repair		Keenan + Kenny Architects, LTD	Gale Associates, Inc.		
Fitchburg PS	Fitchburg HS	Closeout/Audit	Repair	Compass Project Management, Inc.	BLW Engineers, Inc.	RDK Engineers		
Fitchburg PS	Goodrich K Center	Closeout/Audit	Repair	Compass Project Management, Inc.	BLW Engineers, Inc.	RDK Engineers		
Fitchburg PS	Reingold ES	Closeout/Audit	Repair	Compass Project Management, Inc.	Knight, Bagge & Anderson, Inc.	RDK Engineers		
Fitchburg PS	South Street ES	Building Completion 2012		Compass Project Management, Inc.	Knight, Bagge & Anderson, Inc.	Simpson Gumpertz & Heger Inc.		
Fitchburg PS	South Street ES	Closeout/Audit	Repair	Compass Project Management, Inc.	BLW Engineers, Inc.	RDK Engineers		
Fitchburg PS	Reingold ES	Building Completion 2012	Repair	Compass Project Management, Inc.	BLW Engineers, Inc.	Simpson Gumpertz & Heger Inc.		
Fitchburg PS	Memorial IS	Building Completion 2012	Repair	Compass Project Management, Inc.	Knight, Bagge & Anderson, Inc.	Simpson Gumpertz & Heger Inc.		
Fitchburg PS	Memorial IS	Closeout/Audit	Repair	Compass Project Management, Inc.	BLW Engineers, Inc.	RDK Engineers		
Florida PS	Abbott Memorial K-8	Closeout/Audit	Repair		Dietz and Company		DBB - Contract Awarded	Waterman Excavating, Inc
Florida PS	Abbott Memorial K-8	Closeout/Audit	Repair					
Foxborough PS	Foxborough HS	Substantial Completion	Repair	Construction Monitoring Services, Inc.	Kaestle Boos Associates, Inc.	Consulting Engineering Services, LLC	DBB - Contract Awarded	CTA Construction Co.
Framingham PS	Mary E Stapleton ES	Building Completion 2012	Repair	Bargmann, Hendrie + Archetype, Inc.	Russo Barr Associates, Inc.	CBI Consulting Inc.		

# Master District Status List

Yellow = Wait List Project

Green = Green Repair

Red = Changes in last 60 days

District Name	School Name	Status	Preferred Schematic	OPM	Designer	Cx Authority	Procurement Status	CM/GC
Franklin PS	Franklin HS	Project Scope & Budget	Model School	Daedalus Projects Inc.	Ai3 Architects LLC			
Gardner PS	Waterford Street Primary	Closeout/Audit	Repair	P3 Project Planning Professionals	Knight, Bagge & Anderson, Inc.	Building Enclosure Associates		
Gardner PS	Gardner HS	Closeout/Audit	Repair	P3 Project Planning Professionals	Knight, Bagge & Anderson, Inc.	Building Enclosure Associates		
Gardner PS	Elm Street IS	Closeout/Audit	Repair	P3 Project Planning Professionals	Knight, Bagge & Anderson, Inc.	Building Enclosure Associates		
Georgetown PS	Penn Brook IS	Preferred Schematic		Municipal Building Consultants, Inc.	Drummey Rosane Anderson, Inc.			
Gloucester PS	Plum Cove School	Closeout/Audit	Repair	Knight, Bagge, & Anderson, Inc.	CGKV Architects, Inc.	Russo Barr Associates, Inc.		
Gloucester PS	Ralph B O'Maley MS	Closeout/Audit	Repair	Knight, Bagge, & Anderson, Inc.	CGKV Architects, Inc.	Russo Barr Associates, Inc.		
Gloucester PS	East Gloucester ES	Closeout/Audit	Repair	Knight, Bagge, & Anderson, Inc.	CGKV Architects, Inc.	Russo Barr Associates, Inc.		
Gloucester PS	Beeman Memorial IS	Closeout/Audit	Repair	Knight, Bagge, & Anderson, Inc.	CGKV Architects, Inc.	Russo Barr Associates, Inc.		
Gloucester PS	Veterans Memorial ES	Closeout/Audit	Repair	Knight, Bagge, & Anderson, Inc.	CGKV Architects, Inc.	Russo Barr Associates, Inc.		
Gloucester PS	West Parish ES	Eligibility Period						
Grafton PS	Grafton Memorial SHS	Building Completion 2012	Repair	URS Corporation	CGKV Architects, Inc.			
Grafton PS	Grafton Memorial SHS	Building Completion 2012	New Construction	Joslin, Lesser & Associates, Inc.	Symmes Maini & McKee Associates, Inc.	Horizon Engineering Associates, LLP	CMR - CM Selected	Dimeo Construction
Grafton PS	South Grafton ES	Building Completion 2012	Repair	URS Corporation	CGKV Architects, Inc.	Horizon Engineering Associates, LLP		
Greater Lawrence RVT PS	Gr Lawrence Regional Voc / Tech HS	OPM Selection						
Greater Lowell Voc Tec PS	Gr Lowell Regional Voc / Tech HS	Feasibility Study	Repair	Heery International, Inc	Knight, Bagge & Anderson, Inc.			
Greater New Bedford PS	Gr New Bedford Voc / Tech HS	Feasibility Study		Construction Monitoring Services, Inc.	Drummey Rosane Anderson, Inc.			
Greenfield PS	Four Corners ES	Design Development	Repair	P3 Project Planning Professionals	Tighe & Bond, Inc.	Strategic Building Solutions, LLC		
Greenfield PS	Greenfield HS	Preferred Schematic		Construction Monitoring Services, Inc.	Dore & Whittier Architects, Inc.			
Hadley PS	Hopkins Academy	Design Development	Repair	Strategic Building Solutions, LLC	CSS Architects Incorporated	Russo Barr Associates, Inc.		
Hamilton-Wenham PS	Cutler ES	Closeout/Audit	Repair	Municipal Building Consultants, Inc.	Richard D. Kimball Company, Inc.	Sebesta Blomberg & Associates, Inc.	DBB - Contract Awarded	Thomas E. Snowden Inc.
Hampden-Wilbraham PS	Minnechaug Reg HS	Building Completion 2012	Model School	ARCADIS U.S., Inc.	Mount Vernon Group Architects, Inc.	Horizon Engineering Associates, LLP	DBB - Contract Awarded	Fontaine Bros.
Hancock PS	Hancock ES	Building Completion 2012	Repair	N/A	Westall Architects			
Hanover PS	Hanover HS	Substantial Completion	New Construction	PMA Consultants	HMFH Architects, Inc.	Horizon Engineering Associates, LLP	DBB - Contract Awarded	Callahan, Inc
Haverhill PS	Walnut Square Primary	Design Development	Repair	Vertex Construction Services, Inc.	CSS Architects Incorporated			
Haverhill PS	Consentino MS	Design Development	Repair	Vertex Construction Services, Inc.	CSS Architects Incorporated			

# Master District Status List

Yellow = Wait List Project

Green = Green Repair

Red = Changes in last 60 days

District Name	School Name	Status	Preferred Schematic	OPM	Designer	Cx Authority	Procurement Status	CM/GC
Haverhill PS	John G Whittier MS	Approved Project Vote Pending	Repair	Vertex Construction Services, Inc.	CSS Architects Incorporated			
Haverhill PS	Haverhill HS	Construction		Vertex Construction Services, Inc.			DBB - Contract Awarded	
Haverhill PS	Caleb Dustin Hunking MS	Eligibility Period						
Haverhill PS	Tilton Primary	Design Development	Repair	Vertex Construction Services, Inc.	CSS Architects Incorporated			
Hingham PS	Hingham MS	Design Development	Model School	Knight, Bagge & Anderson, Inc.	Ai3 Architects LLC	Foreman Building Commissioning, LP	DBB - In Design	
Holbrook PS	Holbrook JHS / SHS	Eligibility Period						
Holyoke PS	Holyoke HS	Closeout/Audit			Design Partnership of Cambridge, Inc.		DBB - Contract Awarded	
Hudson PS	John F Kennedy MS	Building Completion 2013	New Construction	PMA Consultants	OMR Architects, Inc.	WSP Flack + Kurtz	DBB - Contract Awarded	Bacon/ Agostini Construction
Leicester PS	Leicester Memorial ES	Closeout/Audit	Repair	Maguire Group	Bradley Architects, Inc.	N/A		
Leicester PS	Leicester MS	Closeout/Audit	Repair	Maguire Group	Bradley Architects, Inc.	Cannon Design		
Leominster PS	Leominster SHS	Building Completion 2013	Addition/Renovation	Daedalus Projects, Inc.	Lamoureux Pagano & Associates, Inc.	Horizon Engineering Associates, LLP	CMR - CM Selected	WT Rich
Leverett PS	Leverett ES	Building Completion 2012	Repair	Potomac Capital Advisors	DiMarinisi & Wolfe Architects Urban	Russo Barr Associates, Inc.		
Lexington PS	Lexington HS	Closeout/Audit	Repair	Skanska USA Building Inc.	Russo Barr Associates, Inc.	Simpson Gumpertz & Heger Inc.		
Lexington PS	Joseph Estabrook ES	Preferred Schematic	New Construction	RF Walsh Collaborative Partners	DiNisco Design Partnership, Limited	BVH Integrated Services, Inc.		
Lincoln PS	Lincoln K-8	Preferred Schematic	Addition/Renovation	Skanska USA Building, Inc.	OMR Architects, Inc.			
Littleton PS	Russell St ES	Closeout/Audit	Repair	Daedalus Projects, Inc.	Drumrey Rosane Anderson, Inc.	WSP Flack + Kurtz	DBB - Contract Awarded	Colantonio, Inc.
Longmeadow PS	Longmeadow HS	Building Completion 2013	New Construction	Joslin, Lesser & Associates, Inc.	OMR Architects, Inc.	Foreman Building Commissioning, LP	CMR - CM Selected	Gilbane Building Company
Lowell PS	Peter W Reilly ES	Design Development	Repair	NETCO Construction Project Managers, Inc.	ICON architecture, inc.			
Lowell PS	Washington ES	Design Development	Repair	NETCO Construction Project Managers, Inc.	ICON architecture, inc.	RDK Engineers		
Lowell PS	Moody ES	Design Development	Repair	NETCO Construction Project Managers, Inc.	ICON architecture, inc.	Building Enclosure Associates		
Lowell PS	Lowell HS	Design Development	Repair	NETCO Construction Project Managers, Inc.	ICON architecture, inc.			
Lowell PS	Charles W Morey ES	Closeout/Audit		Watermark			DBB - Contract Awarded	CTA Construction Co.
Lunenburg PS	Lunenburg HS	Eligibility Period						
Lynn PS	Thurgood Marshall MS	OPM Selection						
Lynnfield PS	Lynnfield HS	Project Scope & Budget		Heery International, Inc	Edward Rowse Architects, Inc.	Fitzmeyer & Tocci Associates, Inc.		
Malden PS	Malden HS	Substantial Completion	Renovation	URS Corporation	Flansburgh Associates, Inc.		CMR - CM Selected	Gilbane Building Company

# Master District Status List

Yellow = Wait List Project

Green = Green Repair

Red = Changes in last 60 days

District Name	School Name	Status	Preferred Schematic	OPM	Designer	Cx Authority	Procurement Status	CM/GC
Manchester Essex Regional PS	Manchester JHS / SHS	Closeout/Audit		Design Technique	Mount Vernon Group Architects, Inc.		DBB - Contract Awarded	TLT Construction
Marblehead PS	Glover Primary	Design Development	New Construction	Municipal Building Consultants, Inc.	JCJ Architecture, PC	RDK Engineers	DBB - In Design	
Marblehead PS	Village IS	Closeout/Audit	Repair	Municipal Building Consultants, Inc.	Symmes Maini & McKee Associates, Inc.	RDK Engineers	DBB - Contract Awarded	Groom Construction
Marlborough PS	Francis J Kane Primary	Building Completion 2012	Repair	RF Walsh Collaborative Partners	Baker/Wohl Architects, Inc.	Building Enclosure Associates		
Marlborough PS	Marlborough HS	Building Completion 2012	Repair	RF Walsh Collaborative Partners	Baker/Wohl Architects, Inc.	RDK Engineers		
Marshfield PS	Marshfield HS	Design Development	Model School		Ai3 Architects LLC	Sebesta Blomberg & Associates, Inc.		
Marshfield PS	Gov Edward Winslow ES	Substantial Completion	Repair	Vertex Construction Services, Inc.	Knight, Bagge & Anderson, Inc.	RDK Engineers	DBB - Contract Awarded	Enterprise Equipment Co., Inc.
Maynard PS	Maynard HS	Building Completion 2013	New Construction	Municipal Building Consultants, Inc.	Tappe Associates, Inc.	WSP Flack + Kurtz	DBB - Contract Awarded	CTA Construction
Medway PS	Medway MS	Building Completion 2013		Compass Project Management, Inc.	Knight, Bagge & Anderson, Inc.	Sebesta Blomberg & Associates, Inc.	CMR - CM Selected	Consigli Construction Co.
Melrose PS	Melrose HS	Closeout/Audit	Repair	Municipal Building Consultants, Inc.	Gale Associates, Inc.	Russo Barr Associates, Inc.		
Mendon-Upton PS	Miscoe Hill IS	Design Development	Repair	Maguire Group	Habeeb & Associates Architects, Inc.	Sebesta Blomberg & Associates, Inc.		
Methuen PS	Methuen HS	Building Completion 2013	Addition/Renovation	KBA/Trident	Finegold Alexander and Associates Inc.	Environmental Health and Engineering	CMR - CM Selected	Dimeo Construction
Middleborough PS	Mary K. Goode ES	Construction	Repair	Maguire Group	Habeeb & Associates Architects, Inc.	Russo Barr Associates, Inc.		
Middleton PS	Howe-Manning IS	Substantial Completion	New Construction	RF Walsh Collaborative Partners	DiNisco Design Partnership, Limited	Foreman Building Commissioning, LP	DBB - Contract Awarded	CTA Construction Co.
Milford PS	Woodland ES	Eligibility Period						
Minuteman Voc Tech PS	Minuteman Reg HS	Eligibility Period						
Mohawk Trail PS	Mohawk Trail Reg HS	Design Development	Repair	Potomac Capital Advisors	Bradley Architects, Inc.	Strategic Building Solutions, LLC		
Mohawk Trail PS	Colrain Central ES	Design Development	Repair	Potomac Capital Advisors	Bradley Architects, Inc.	Strategic Building Solutions, LLC		
Mohawk Trail PS	Buckland-Shelburne Reg ES	Building Completion 2012	Repair	Potomac Capital Advisors	Bradley Architects, Inc.	Strategic Building Solutions, LLC		
Mount Greylock PS	Mt Greylock Reg HS	Closeout/Audit	Repair	N/A	Hesnor Engineering & Barry Architects	Horizon Engineering Associates, LLP	DBB - Contract Awarded	Adams Plumbing & Heating
Narragansett PS	Templeton Center	Feasibility Study (on hold)		Strategic Building Solutions, LLC	Symmes Maini & McKee Associates, Inc.		Undetermined	
Narragansett PS	Narragansett MS	Building Completion 2012	Repair	Potomac Capital Advisors	DiMarinisi & Wolfe Architects Urban	Rist-Frost-Shumway Engineering, P.C.		
Narragansett PS	Phillipston Memorial ES	Building Completion 2012	Repair	Potomac Capital Advisors	DiMarinisi & Wolfe Architects Urban	Rist-Frost-Shumway Engineering, P.C.		
Nashoba PS	Pompositicut Primary	Building Completion 2012	Addition/Renovation	Construction Monitoring Services, Inc.	Symmes Maini & McKee Associates, Inc.	Strategic Building Solutions, LLC	DBB - Contract Awarded	Stella P.J. Construction Corp.
Nashoba Valley Tech PS	Nashoba Valley Tech HS	Design Development	Repair					
Natick PS	Natick HS	Building Completion 2013	Model School	RF Walsh Collaborative Partners	Ai3 Architects LLC	Rist-Frost-Shumway Engineering, P.C.	DBB - Contract Awarded	Brait Builders Corporation

# Master District Status List

Yellow = Wait List Project

Green = Green Repair

Red = Changes in last 60 days

District Name	School Name	Status	Preferred Schematic	OPM	Designer	Cx Authority	Procurement Status	CM/GC
Nauset PS	Nauset Reg HS	Design Development	Repair	NETCO Construction Project Managers, Inc.	Habeeb & Associates Architects, Inc.	CBI Consulting Inc.		
Needham PS	Newman ES	Building Completion 2012	Repair	Town of Needham	Drummeay Rosane Anderson, Inc.	Rist-Frost-Shumway Engineering, P.C.	CMR - CM Selected	Consigli Construction Co.
Needham PS	Pollard MS	Substantial Completion	Repair	STV Construction, Inc.	Gale Associates, Inc. Gale Associates, Inc.	CBI Consulting Inc.		
New Bedford PS	New Bedford HS	OPM Selection						
New Bedford PS	Abraham Lincoln	Closeout/Audit	New Construction	Daedalus Projects Inc	Mount Vernon Group Architects, Inc.	Sebesta Blomberg & Associates, Inc.	DBB - Contract Awarded	CTA Construction Co.
New Bedford PS	John Hannigan ES	OPM Selection						
New Salem-Wendell PS	Swift River ES	Substantial Completion	Repair	Maguire Group	Bradley Architects, Inc.	Strategic Building Solutions, LLC		
Newburyport PS	Rupert A Nock MS	Feasibility Study			Miller Dyer Spears Inc.			
Newburyport PS	Francis T Bresnahan ES	Preferred Schematic			HMFH Architects, Inc.			
Newton PS	A E Angier ES	Eligibility Period						
Newton PS	Bowen ES	Building Completion 2012	Repair	STV Construction, Inc.	Habeeb & Associates Architects, Inc.			
Newton PS	Williams ES	Substantial Completion	Repair	STV Construction, Inc.	Habeeb & Associates Architects, Inc.			
Newton PS	Newton North HS	Closeout/Audit	New Construction	Turner Construction Company	Dore & Whittier Architects, Inc.		CMR - CM Selected	Dimeo Construction
Norfolk County Agr PS	Norfolk County Agr HS	Design Development	Addition/Renovation	Compass Project Management, Inc	Turowski2 Architecture, Inc.	Rist-Frost-Shumway Engineering, P.C.	DBB - In Design	
Norfolk PS	Freeman-Centennial IS	Building Completion 2012	New Construction	Joslin, Lesser & Associates, Inc.	Flansburgh Associates, Inc.	WSP Flack + Kurtz	DBB - In Design	Fontaine Bros., Inc.
North Adams PS	Silvio O Conte MS	Preferred Schematic			Strategic Building Solutions, LLC	Margo Jones Architects, Inc.		
North Andover PS	North Andover MS	Building Completion 2012	Repair	Municipal Building Consultants, Inc.	ICON architecture, inc.	Cannon Design		
North Andover PS	Atkinson ES	Building Completion 2012	Repair	Municipal Building Consultants, Inc.	ICON architecture, inc.	Cannon Design		
North Andover PS	Annie L Sargent ES	Building Completion 2012	Repair	Municipal Building Consultants, Inc.	ICON architecture, inc.	Cannon Design		
North Attleborough PS	Falls ES	Building Completion 2012	Repair	Atlantic Construction & Management, Inc.	CSS Architects Incorporated	Gale Associates, Inc.		
North Brookfield PS	North Brookfield ES	Substantial Completion	Repair	Vertex Construction Services, Inc.	LPBA/ Architects, Inc.	Simpson Gumpertz & Heger Inc.		
North Middlesex PS	Ashby ES	Building Completion 2012	Repair	Compass Project Management, Inc.	Russo Barr Associates, Inc.	Building Enclosure Associates		
North Middlesex PS	North Middlesex Reg HS	Eligibility Period						
North Middlesex PS	Spaulding Memorial Primary	Building Completion 2012	Repair	Compass Project Management	Russo Barr Associates, Inc.	Building Enclosure Associates		
North Reading PS	North Reading HS	Preferred Schematic	Addition/Renovation	PMA Consultants	Dore & Whittier Architects, Inc.			
Northampton-Smith PS	Smith Vocational and Agricultural HS	Eligibility Period						

# Master District Status List

Yellow = Wait List Project

Green = Green Repair

Red = Changes in last 60 days

District Name	School Name	Status	Preferred Schematic	OPM	Designer	Cx Authority	Procurement Status	CM/GC
Northborough PS	Lincoln Street ES	Eligibility Period						
Northborough PS	Robert E. Melican MS	Substantial Completion	Repair	Pinck & Co., Inc.	ICON architecture, inc.	Strategic Building Solutions, LLC		
Norton PS	Norton HS	Design Development		Pinck & Co., Inc.	JCJ Architecture, PC	Rist-Frost-Shumway Engineering, P.C.	CMR - CM Selected	W. T. Rich Company, Inc.
Norwood PS	Norwood HS	Substantial Completion	Model School	Compass Project Management, Inc.	Ai3 Architects LLC		DBB - Contract Awarded	Agostini Construction Company, Inc.
Old Colony Reg Voc Tech PS	Old Colony Regional Voc / Tech HS	OPM Selection						
Orange PS	Butterfield MS	Substantial Completion	Repair		Tighe & Bond, Inc.		Undetermined	SOM Construction, Inc.
Orange PS	Dexter Park IS	Eligibility Period						
Oxford PS	Oxford MS	OPM Selection	Repair					
Palmer PS	Converse MS	Building Completion 2012	Repair	Diversified Project Management	Tighe & Bond, Inc.	Strategic Building Solutions, LLC		
Palmer PS	Old Mill Pond ES	Building Completion 2012	Repair	Diversified Project Management	Tighe & Bond, Inc.	Strategic Building Solutions, LLC		
Palmer PS	Palmer HS	Building Completion 2012	Repair	Diversified Project Management	Tighe & Bond, Inc.	Strategic Building Solutions, LLC		
Peabody PS	John E Burke ES	Building Completion 2012	Repair	Daedalus Projects Inc	LPBA/ Architects, Inc.	Sebesta Blomberg & Associates, Inc.		
Peabody PS	William A Welch Sr ES	Design Development	Repair	Daedalus Projects Inc	LPBA/ Architects, Inc.	Sebesta Blomberg & Associates, Inc.		
Peabody PS	J Henry Higgins MS	Feasibility Study	Repair	Daedalus Projects Inc	DiNisco Design Partnership, Limited			
Pentucket PS	Dr John C Page ES	Building Completion 2012	Repair	PMA Consultants	Knight, Bagge & Anderson, Inc.	RDK Engineers		
Pentucket PS	Elmer S Bagnall ES	Building Completion 2012	Repair	PMA Consultants	Knight, Bagge & Anderson, Inc.	CBI Consulting Inc.		
Pentucket PS	Helen R Donaghue IS	Substantial Completion	Repair	PMA Consultants	Knight, Bagge & Anderson, Inc.	CBI Consulting Inc.		
Pentucket PS	Dr Frederick N Sweetsir Primary	Building Completion 2012	Repair	PMA Consultants	Knight, Bagge & Anderson, Inc.	CBI Consulting Inc.		
Pioneer Valley PS	Northfield ES	Building Completion 2012	Repair	Diversified Project Management	CGKV Architects, Inc.	Strategic Building Solutions, LLC		
Pioneer Valley PS	Pioneer Valley Reg MS / HS	Building Completion 2012	Repair	Diversified Project Management	CGKV Architects, Inc.	Strategic Building Solutions, LLC		
Pittsfield PS	Taconic HS	Feasibility Study		Skanska USA Building, Inc.				
Plymouth PS	West ES	Closeout/Audit	Repair					
Plymouth PS	Plymouth Community IS	Closeout/Audit	Repair		Knight, Bagge & Anderson, Inc.	Building Enclosure Associates		
Plymouth PS	Plymouth North HS	Building Completion 2012	Model School	Ted Gentry Associates	Ai3 Architects LLC	Sebesta Blomberg & Associates, Inc.	DBB - Contract Awarded	J&J Contractors Inc.
Quabbin PS	Oakham Center ES	Closeout/Audit	Repair		Russo Barr Associates, Inc.	Building Enclosure Associates	DBB - Contract Awarded	Cape Way Roofing
Quabbin PS	Quabbin Reg HS	Closeout/Audit	Repair	Vertex Construction Services, Inc.	LPBA/ Architects, Inc.	Building Enclosure Associates		

# Master District Status List

Yellow = Wait List Project

Green = Green Repair

Red = Changes in last 60 days

District Name	School Name	Status	Preferred Schematic	OPM	Designer	Cx Authority	Procurement Status	CM/GC
Quincy PS	Central MS	Design Development	New Construction	Tishman Construction Corporation of MA	Ai3 Architects LLC	Sebesta Blomberg & Associates, Inc.	DBB - In Design	
Reading PS	J Warren Killam ES	Closeout/Audit	Repair	Knight, Bagge, & Anderson, Inc.	LPBA/ Architects, Inc.	Russo Barr Associates, Inc.		
Reading PS	Birch Meadow ES	Closeout/Audit	Repair	Knight, Bagge, & Anderson, Inc.	LPBA/ Architects, Inc.	Russo Barr Associates, Inc.		
Revere PS	Paul Revere ES	Closeout/Audit	New Construction	RF Walsh Collaborative Partners	Drummey Rosane Anderson, Inc.		DBB - Contract Awarded	Delulis Brothers Construction Company
Revere PS	William McKinley ES	OPM Selection		RF Walsh Collaborative Partners				
Rochester PS	Rochester Memorial ES	Closeout/Audit	Addition/Renovation	PMA Consultants	Flansburgh Associates, Inc.	Horizon Engineering Associates, LLP	CMR - CM Selected	Gilbane Building Company
Rockland PS	John W Rogers MS	Building Completion 2012	Addition/Renovation	Daedalus Projects Inc	Dore & Whittier Architects, Inc.	Consulting Engineering Services, LLC	CMR - CM Selected	Agostini Construction Company, Inc.
Rockland PS	R Stewart Esten ES	Construction	Repair	Daedalus Projects Inc	Habeeb & Associates Architects, Inc.	Russo Barr Associates, Inc.		
Rockport PS	Rockport ES	Closeout/Audit	Repair	N/A	Russo Barr Associates, Inc.			
Rockport PS	Rockport HS	Closeout/Audit	Repair		Russo Barr Associates, Inc.	Building Enclosure Associates	DBB - Contract Awarded	Feeley, McAnespie, Inc.
Salem PS	Saltonstall ES	Design Development	Repair	KV Associates, Inc.	Reinhardt Associates, Inc.	Rist-Frost-Shumway Engineering, P.C.		
Salem PS	Collins MS	Design Development	Repair	KV Associates, Inc.	Reinhardt Associates, Inc.	Rist-Frost-Shumway Engineering, P.C.		
Sandwich PS	Forestdale K-8	Design Development	Repair	NETCO Construction Project Managers, Inc.	Habeeb & Associates Architects, Inc.	Gale Associates, Inc.		
Sandwich PS	Oak Ridge K-8	Design Development	Repair	NETCO Construction Project Managers, Inc.	Habeeb & Associates Architects, Inc.	Gale Associates, Inc.		
Saugus PS	Belmonte Saugus MS	Design Development	Repair	Skanska USA Building, Inc.	Fletcher Thompson Architecture Engineering,	Consulting Engineering Services, LLC	CMR - Procurement Pending	
Scituate PS	Wampatuck ES	Closeout/Audit	Repair	Bargmann, Hendrie + Archetype, Inc.	Knight, Bagge & Anderson, Inc.	Rist-Frost-Shumway Engineering, P.C.		
Scituate PS	Gates IS	Closeout/Audit	Repair					
Sharon PS	Sharon HS	Closeout/Audit	Repair	Daedalus Projects Inc	Baker/Wohl Architects, Inc.	Cannon Design	Undetermined	Titan Roofing, Inc.
Sharon PS	Sharon MS	Substantial Completion	Addition/Renovation	Daedalus Projects, Inc.	Kaestle Boos Associates, Inc.	Horizon Engineering Associates, LLP	CMR - CM Selected	Consigli Construction Co.
Shawsheen Valley Voc PS	Shawsheen Valley Voc / Tech HS	Closeout/Audit		Construction Monitoring Services Inc.	Knight, Bagge & Anderson, Inc.		DBB - Contract Awarded	Colantino Inc.
Shrewsbury PS	Sherwood MS	Building Completion 2013	New Construction	PMA Consultants	Lamoureux Pagano & Associates, Inc.	RDK Engineers	CMR - CM Selected	Gilbane Building Company
Shrewsbury PS	Spring Street ES	Building Completion 2012	Repair	PMA Consultants	Habeeb & Associates Architects, Inc.	Cannon Design		
Somerset PS	Somerset HS	Design Development		Skanska USA Building, Inc.	Ai3 Architects LLC	Horizon Engineering Associates, LLP		
Somerville PS	E Somerville Community K-8	Design Development	Renovation	City of Somerville	Maguire Group Inc.	Foreman Building Commissioning, LP	CMR - CM Selected	Gilbane Building Company
South Hadley PS	Plains ES	Feasibility Study		Arcadis	Margo Jones Architects, Inc.			
South Shore Reg Voc PS	South Shore Voc / Tech HS	Closeout/Audit	Repair	Vertex Construction Services, Inc.	Gale Associates, Inc.	Building Enclosure Associates		

# Master District Status List

Yellow = Wait List Project

Green = Green Repair

Red = Changes in last 60 days

District Name	School Name	Status	Preferred Schematic	OPM	Designer	Cx Authority	Procurement Status	CM/GC
Southbridge PS	Southbridge HS	Building Completion 2012	New Construction	Joslin, Lesser & Associates, Inc.	Tappe Associates, Inc.	Environmental Health and Engineering	CMR - CM Selected	Consigli Construction Co.
Southeastern Reg Voc Tech PS	Southeastern Regional Voc / Tech HS	Design Development	Addition/Renovation	RF Walsh Collaborative Partners	Drumme Rosane Anderson, Inc.	RDK Engineers	CMR - CM Selected	WT Rich Company Inc.
Southern Worcester Cty VT PS	Bay Path Regional Voc / Tech HS	Design Development		Heery International, Inc	Kaestle Boos Associates, Inc.			
Southwick-Tolland	Woodland ES	Approved Project Vote Pending		Strategic Building Solutions, LLC	JCJ Architecture, PC			
Spencer-E Brookfield PS	David Prouty HS	Designer Selection		Dore and Whittier Management Partners				
Springfield PS	Forest Park Middle School	Design Development	Addition/Renovation	ARCADIS-U.S., Inc.	Perkins Eastman	Foreman Building Commissioning, LP		
Springfield PS	SCIPP Year 2	Building Completion 2012	Repair		CGKV Architects, Inc./Gale Associates, Inc.	Building Enclosure Associates		
Springfield PS	SCIPP Year 3	Building Completion 2012	Repair		Gale Associates, Inc.	Building Enclosure Associates		
Springfield PS	Elias Brookings K-8	Preferred Schematic	Renovation					
Springfield PS	Dryden Memorial ES	Preferred Schematic	Addition/Renovation	ARCADIS U.S., Inc.	Drumme Rosane Anderson, Inc.	BVH Integrated Services, Inc.		
Springfield PS	Putnam Voc / Tech HS	Building Completion 2012	New Construction	ARCADIS	Drumme Rosane Anderson, Inc.	Strategic Building Solutions, LLC	CMR - CM Selected	Consigli Construction Co.
Stoneham PS	Stoneham MS	Project Scope & Budget		Joslin, Lesser & Associates	Tappe Associates, Inc.			
Sturbridge PS	Burgess ES	Building Completion 2012	Addition/Renovation	Lamoureux Pagano & Associates, Inc.	Drumme Rosane Anderson, Inc.	Horizon Engineering Associates, LLP	DBB - Contract Awarded	Fontaine Bros.
Sudbury PS	Peter Noyes ES	Closeout/Audit	Repair	Compass Project Management, Inc.	Russo Barr Associates, Inc./BLW Engineers, Inc.	RDK Engineers		
Sutton PS	Sutton MS	Building Completion 2013	Addition/Renovation	Strategic Building Solutions	Flansburgh Associates, Inc.	RDK Engineers	DBB - Contract Awarded	TLT Construction Corp.
Swampscott PS	Hadley ES	Eligibility Period						
Tantasqua PS	Tantasqua Reg JHS	Closeout/Audit	Repair	Diversified Project Management	Habeeb & Associates Architects, Inc.	Cannon Design		
Taunton PS	Taunton HS	Substantial Completion	Addition/Renovation	Gilbane	Design Partnership of Cambridge, Inc.		DBB - Contract Awarded	Bacon-Agostini Construction Joint Venture
Tewksbury PS	Tewksbury Memorial HS	Building Completion 2012	Model School	Heery International, Inc	Symmes Maini & McKee Associates, Inc.	Sebesta Blomberg & Associates, Inc.	DBB - Contract Awarded	CTA Ventures/ Methuen
Tri County PS	Tri County Regional Voc / Tech HS	Closeout/Audit	Repair	Knight, Bagge, & Anderson, Inc.	Richard D. Kimball Company, Inc.	WSP Flack + Kurtz		
Upper Cape Cod Voc Tech PS	Upper Cape Cod Voc / Tech HS	Building Completion 2012	Repair	NETCO Construction Project Managers, Inc.	Knight, Bagge & Anderson, Inc.	Gale Associates, Inc.		
Uxbridge PS	Uxbridge HS	Building Completion 2012	New Construction	Joslin, Lesser & Associates, Inc.	Raymond Design Associates, Inc.	Turner Facilities Management Solutions	CMR - CM Selected	Shawmut Design and Construction
Wachusett PS	Mountview MS	Designer Selection		Municipal Employee				
Wachusett PS	Naquag ES	Building Completion 2012	Repair	Strategic Building Solutions, LLC	LPBA/ Architects, Inc.	Rist-Frost-Shumway Engineering, P.C.		
Wachusett PS	Paxton K-8 Center	Building Completion 2012	Repair	Strategic Building Solutions, LLC	LPBA/ Architects, Inc.	Rist-Frost-Shumway Engineering, P.C.		
Wachusett PS	Thomas Prince K-8	Building Completion 2012	Repair	Strategic Building Solutions, LLC	LPBA/ Architects, Inc.	Rist-Frost-Shumway Engineering, P.C.		



# Master District Status List

Yellow = Wait List Project

Green = Green Repair

Red = Changes in last 60 days

District Name	School Name	Status	Preferred Schematic	OPM	Designer	Cx Authority	Procurement Status	CM/GC
Wakefield PS	Galvin MS	Preferred Schematic			Tappe Associates, Inc.			
Wakefield PS	Wakefield Memorial HS	Closeout/Audit	Addition/Renovation					
Wareham PS	Minot Forest IS	Eligibility Period						
Wayland PS	Wayland HS	Substantial Completion	New Construction	KV Associates	HMFH Architects, Inc.	WSP Flack + Kurtz	CMR - CM Selected	Shawmut Construction
Webster PS	Park Avenue ES	Preferred Schematic		RF Walsh Collaborative Partners	Dore & Whittier Architects, Inc.			
Wellesley PS	Wellesley SHS	Substantial Completion	New Construction	Ryegate Inc	Symmes Maini & McKee Associates, Inc.	Rist-Frost-Shumway Engineering, P.C.	CMR - CM Selected	Turner Construction
West Boylston PS	Major Edwards ES	Design Development	Repair	URS Corporation	Reinhardt Associates, Inc.	Cannon Design		
West Bridgewater PS	West Bridgewater JHS / SHS	Feasibility Study		Strategic Building Solutions, LLC	Flansburgh Associates, Inc.			
West Springfield PS	West Springfield HS	Building Completion 2014	Model School	Strategic Building Solutions, LLC	Symmes Maini & McKee Associates, Inc.	Turner Facilities Management Solutions	DBB - Contract Awarded	Fontaine Bros., Inc
Westborough PS	Sarah W Gibbons MS	Eligibility Period						
Westfield PS	Southampton Road ES	Closeout/Audit	Repair	P3 Project Planning Professionals	Tighe & Bond, Inc.	Strategic Building Solutions, LLC		
Westfield PS	Highland School	Design Development	Repair	P3 Project Planning Professionals	Tighe & Bond, Inc.	Strategic Building Solutions, LLC	Undetermined	Allied Restoration
Westfield PS	Southampton Road ES	Design Development	Repair	P3 Project Planning Professionals	Tighe & Bond, Inc.	Strategic Building Solutions, LLC	Undetermined	R&H Roofing
Westfield PS	Westfield HS	Design Development	Repair	P3 Project Planning Professionals	Tighe & Bond, Inc.	Strategic Building Solutions, LLC		
Westfield PS	Paper Mill ES	Design Development	Repair	P3 Project Planning Professionals	Tighe & Bond, Inc.	Strategic Building Solutions, LLC		
Westfield PS	Highland School	Closeout/Audit	Repair	P3 Project Planning Professionals	Tighe & Bond, Inc.	Strategic Building Solutions, LLC		
Westfield PS	Abner Gibbs ES	Design Development	Model School	Skanska USA Building Inc.	Margo Jones Architects, Inc.	Horizon Engineering Associates, LLP	DBB - In Design	
Westfield PS	Westfield Voc / Tech HS	Design Development	Repair	P3 Project Planning Professionals	Tighe & Bond, Inc.	Strategic Building Solutions, LLC		
Weston PS	Weston MS	Substantial Completion	Repair	Compass Project Management, Inc.	Russo Barr Associates, Inc.	RDK Engineers		
Weston PS	Field ES School	Design Development		Compass Project Management, Inc	Jonathan Levi Architects LLC	Foreman Building Commissioning, LP		
Weston PS	Weston HS	Building Completion 2012	Repair	Compass Project Management, Inc.	Garcia Galuska DeSousa	RDK Engineers		
Westport PS	Westport MS	Feasibility Study	Repair	Pinck & Co., Inc.	CGKV Architects, Inc.			
Westport PS	Alice A Macomber ECC	Building Completion 2012	Repair	Pinck & Co., Inc.	CGKV Architects, Inc.	CBI Consulting Inc.		
Westport PS	Westport HS	Building Completion 2012	Repair	Pinck & Co., Inc.	CGKV Architects, Inc.	CBI Consulting Inc.		
Weymouth PS	Abigail Adams MS	Closeout/Audit	Repair	Knight, Bagge, & Anderson, Inc.	Gale Associates, Inc.	Cannon Design		
Whitman-Hanson PS	John H Duval ES	Closeout/Audit	Repair		BETA Group, Inc.		Undetermined	S.I. Services, Inc.

# Master District Status List

Yellow = Wait List Project

Green = Green Repair

Red = Changes in last 60 days

District Name	School Name	Status	Preferred Schematic	OPM	Designer	Cx Authority	Procurement Status	CM/GC
Whitman-Hanson PS	Maquan ES	Feasibility Study		Knight, Bagge & Anderson, Inc.	Turowski2 Architecture, Inc.			
Williamsburg PS	Anne T Dunphy IS	Project Scope & Budget	New Construction	Arcadis	Drumme Rosane Anderson, Inc.			
Wilmington PS	Shawsheen ES	Closeout/Audit	Repair	P3 Project Planning Professionals	Russo Barr Associates, Inc.	CBI Consulting Inc.		
Wilmington PS	Wilmington HS	Design Development		Joslin, Lesser & Associates	Dore & Whittier Architects, Inc.	Symmes, Maini & McKee Associates	CMR - CM Selected	Gilbane Building Company
Winchendon PS	Toy Town ES	Closeout/Audit	Repair	NETCO Construction Project Managers, Inc.	Hesnor Engineering Company	Rist-Frost-Shumway Engineering, P.C.		
Winchester PS	Lynch ES	Closeout/Audit	Repair	Knight, Bagge, & Anderson, Inc.	Gale Associates, Inc.	Simpson Gumpertz & Heger Inc.		
Winchester PS	Vinson-Owen ES	Design Development	New Construction	Town of Winchester	Tappe Associates, Inc.	Turner Facilities Management Solutions	DBB - In Design	
Winchester PS	Winchester HS	Feasibility Study			Symmes Maini & McKee Associates, Inc.			
Winthrop PS	Winthrop Senior High	Designer Selection		Skanska USA Building, Inc.				
Woburn PS	John F Kennedy MS	Closeout/Audit	Repair	Municipal Building Consultants, Inc.	Gale Associates, Inc.	Simpson Gumpertz & Heger Inc.		
Woburn PS	Goodyear ES	Substantial Completion	New Construction	Municipal Building Consultants, Inc.	Tappe Associates, Inc.	Strategic Building Solutions, LLC	CMR - CM Selected	Gilbane Building Company
Woburn PS	Daniel L Joyce MS	Closeout/Audit	Repair	Municipal Building Consultants, Inc.	Gale Associates, Inc.	Simpson Gumpertz & Heger Inc.		
Worcester PS	North HS	Substantial Completion		Maguire Group Inc	City of Worcester		CMR - CM Selected	Gilbane Building Company

**No. of Projects: 322**

# 2012 Eligibility Period Status

March 7, 2012



District	2012												2013
	Jan	Feb	Mar	April	May	June	July	Aug	Sep	Oct	Nov	Dec	Jan
<b>Abington Frolio Jr HS</b>	Board Meeting 1 / 25	ICC (30 days) 2 / 8	SBC (60 days) 3 / 9	4 / 8				Maint Docs / Enroll Certification (180 days) 8 / 6				Local Authorization / FSA (270 days) 11 / 4	
<b>Bellingham Macy ES</b>		ICC (30 days)	SBC (60 days)					Maint Docs / Enroll Certification (180 days)				Local Authorization / FSA (270 days)	
<b>Chelsea (R) Clark Avenue MS</b>		ICC (30 days)	SBC (60 days)					Maint Docs / Enroll Certification (180 days)				Local Authorization / FSA (270 days)	
<b>Gloucester West Parish ES</b>		ICC (30 days)	SBC (60 days)					Maint Docs / Enroll Certification (180 days)				Local Authorization / FSA (270 days)	
<b>Haverhill Hunking MS</b>		ICC (30 days)	SBC (60 days)					Maint Docs / Enroll Certification (180 days)				Local Authorization / FSA (270 days)	
<b>Holbrook Holbrook Jr/Sr HS</b>		ICC (30 days)	SBC (60 days)					Maint Docs / Enroll Certification (180 days)		Local Authorization		FSA (270 days)	
<b>Lunenburg Lunenburg High School</b>		ICC (30 days)	SBC (60 days)					Maint Docs / Enroll Certification (180 days)				Local Authorization / FSA (270 days)	
<b>Milford Woodland ES</b>		ICC (30 days)	SBC (60 days)					Maint Docs / Enroll Certification (180 days)				Local Authorization / FSA (270 days)	
<b>Minuteman Regional Minutemen RVT</b>		ICC (30 days)	SBC (60 days)	Enroll Certification				Maint Docs (180 days)		Local Authorization		FSA (270 days)	
<b>Newton Angier ES</b>		All Preliminary Requirements Complete											
<b>Northborough Lincoln ES</b>		ICC (30 days)	SBC (60 days)					Maint Docs / Enroll Certification (180 days)				Local Authorization / FSA (270 days)	
<b>North Middlesex North Middlesex Regional HS</b>		ICC (30 days)	SBC (60 days)					Maint Docs / Enroll Certification (180 days)				Local Authorization / FSA (270 days)	
<b>Swampscott Hadley ES</b>		ICC (30 days)	SBC (60 days)					Maint Docs / Enroll Certification (180 days)				Local Authorization / FSA (270 days)	
<b>Wareham Minot Forest ES</b>		ICC (30 days)	SBC (60 days)					Maint Docs / Enroll Certification (180 days)				Local Authorization / FSA (270 days)	
<b>Westborough (R) Sarah W Gibbons MS</b>		ICC (30 days)	SBC (60 days)					Maint Docs / Enroll Certification (180 days)				Local Authorization / FSA (270 days)	

45

40

35

30

25

20


15

10

5

### Project Status | March 7, 2012

New Program:	100
Waitlist:	3
Green Repair:	85
Project Complete:	26
Closeout:	81
Projects to be removed from Pipeline:	3
Final Audit Approved:	9
<b>Total Projects:</b>	<b>307</b>

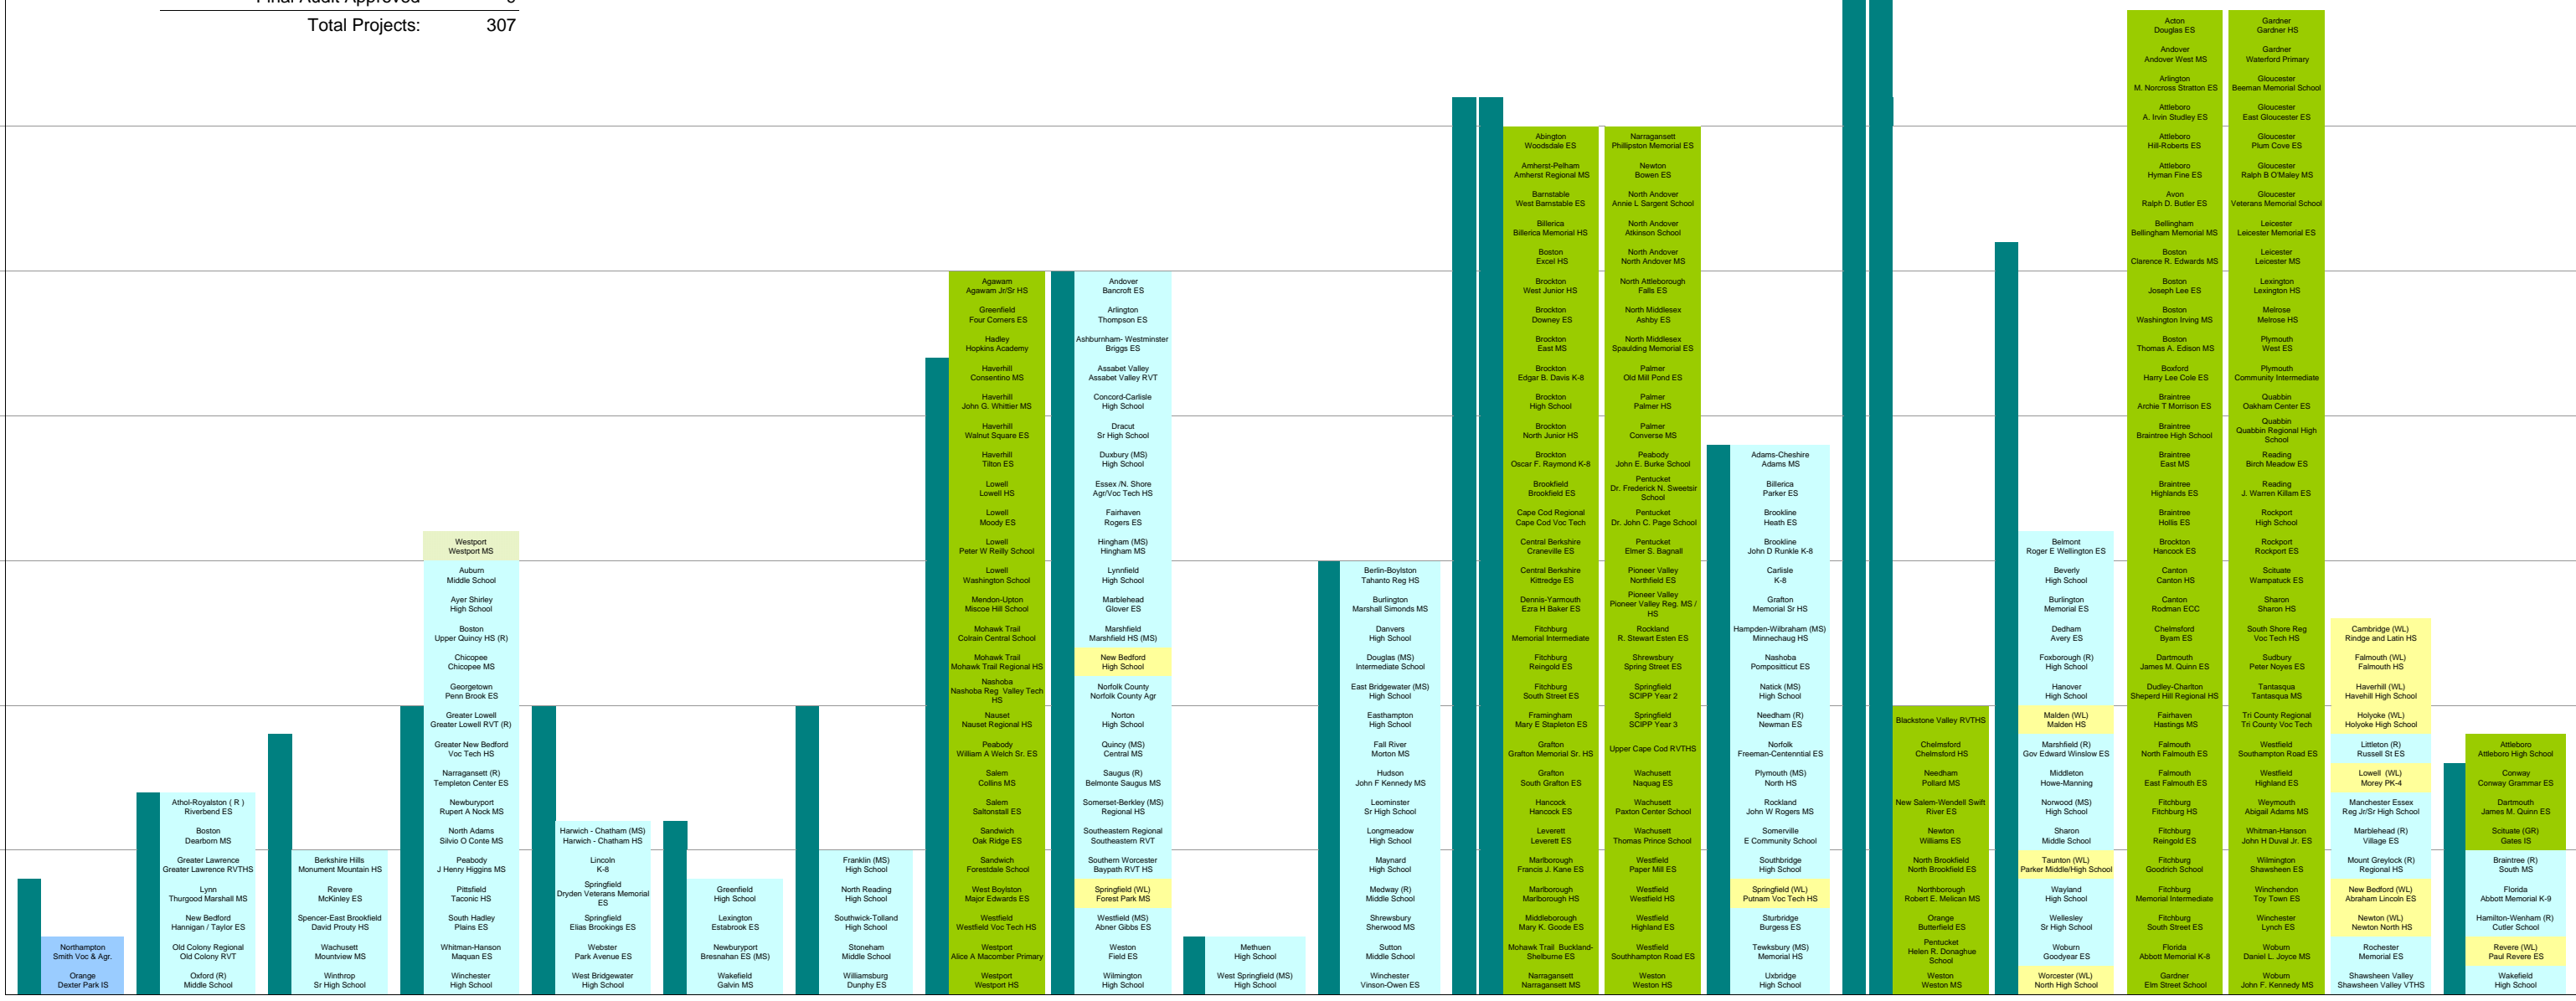

Local Clearance	OPM Selection	Designer Selection	Feasibility Study	Preferred Schematic	Project Scope & Budget	Approved Project Vote Pending	Design Development	Building Completion 2014	Building Completion 2013	Building Completion 2012	Project Complete	Closeout	Final Audit Approved
2	7	5	16	6	4	5	50	2	15	79	26	81	9

# PROJECT STATUS

307  
Total Projects

Green Repair Project - Removal from Pipeline  
Green Repair Project

New Program Project - Removal from Pipeline  
New Program Project

Waitlist Projects  
Capital Pipeline Status Presented at January 25, 2012 Board of Directors Meeting

**Projects in Construction  
MSBA Grant Basis and Maximum Grant Amount**

New Program and Wait List Program Totals			\$1,869,684,025	41,832		8,109,366											*Includes Alternates	\$1,333,175,069
Project	Grade	Contractor	Total Construction Cost*	Projected Enroll	PFA or Bid Data	Proposed Square Footage	Construction Cost per Square Foot	Building Cost	Building Cost per Square Foot	Project Type	Construction Start	Estimated Substantial Completion Date	Reporting Variance from Schedule	Physical Progress (%)	Change Orders (%)	Construction Status	Approximate Maximum Grant Amount *	
<b>CAPITAL PIPELINE PROJECTS IN CONSTRUCTION</b>																		
<b>New Program Totals</b>			<b>\$1,766,661,321</b>	<b>39,232</b>		<b>7,554,796</b>	<b>\$229</b>		<b>\$173</b>							<b>\$1,164,541,050</b>		
Berlin-Boylston Tahanto Reg MS/HS	6-12	CTA	\$32,162,000	560	Bid	126,100	\$255	26,629,999	\$211	Design/Bid/Build	10-May-11	1-Nov-12		55%	0.46%	The Building is enclosed and weather tight. Concrete stadium seating in Auditorium is complete. Ongoing work includes masonry in Gym, water piping/rough electrical/drywall in D Wing, and painting on the first & second floors of A wing. Installation of windows & curtain wall in A /D wing, rough plumbing in locker rooms, and rough electrical and HVAC in Gym/Cafeteria/Kitchen have started.	\$19,849,301	
Beverly Beverly HS	9-12	CTA	\$67,563,917	1,200	Bid	247,275	\$273	\$51,251,689	\$207	Design/Bid/Build	6-Jan-09	18-Nov-10		99%	1.47%	The main building was completed in November 2010. Phase 2, Existing Building Demolition, is now complete. Portions of the baseball field and irrigation system need to be completed in the Spring of 2012.	\$46,826,551	
Billerica Parker ES	K-5	CTA	\$22,842,500	500	Bid	89,093	\$256	\$17,913,441	\$201	Design/Bid/Build	15-Sep-10	10-May-12		71%	0.00%	Phase I, installation of interior finishes and casework, is underway, Phase II, demolition, is scheduled to be completed on November 26, 2012.	\$15,851,020	
Brookline Heath ES	K-8	Nauset	\$6,159,185	560	Bid	80,952	\$76	\$4,807,436	\$59	Design/Bid/Build	29-Sep-11	15-Aug-12	0-30 Days	22%	0.02%	Concrete slabs complete on new addition. Roof installation has begun. Renovation of existing building to commence April 2, 2012.	\$3,173,407	
Brookline Runkle ES	PK-8	G&R Construction	\$20,715,300	560	Bid	104,400	\$198	\$17,668,440	\$169	Design/Bid/Build	10-Nov-10	15-Aug-12	4-14 Days	46%	4.48%	Addition- Structural steel detailing continues as well as exterior masonry, interior metal studs, drywall and MEP rough-ins. All windows are installed. Existing building- MEP rough-ins, metal stud and drywall installations continue.	\$11,135,430	
Carlisle Carlisle K-8	K-8	H.V. Collins Co. Inc	\$15,277,344	700	Bid	140,312	\$109	\$11,342,751	\$81	Design/Bid/Build	9-Feb-11	20-Apr-12		61%	1.82%	Interior finishes are underway in the new addition working towards an April 2012 completion. Phase II, renovation, to be complete by the end of August 2012.	\$6,988,636	
Danvers Danvers HS	9-12	Bacon Construction	\$53,834,164	1,000	Bid	246,251	\$219	\$43,391,172	\$176	Design/Bid/Build	Oct-10	1-Jul-13		53%	89.00%	The Field House, locker rooms and fitness area were turned over and occupied in January 2012. Ongoing work in Phase I areas include the installation of mechanical, electrical and architectural finishes. Installation of windows, curtainwalls, and exterior metal panels are ongoing throughout the building.	\$37,324,055	
Douglas Douglas IS	6-8	CTA	\$14,180,050	448	PFA	83,277	\$170	\$10,604,454	\$127	Design/Bid/Build	Mar-12	6-Jun-13		0%	0.00%	The contractor's Notice to Proceed was issued on March 2, 2012.	\$9,319,892	
Douglas Douglas ES	2-5	CTA	\$24,832,888	552	PFA	83,100	\$299	\$16,740,347	\$201	Design/Bid/Build	Mar-12	6-Jun-13		0%	0.00%	The contractor's Notice to Proceed was issued on March 2, 2012.	\$17,611,449	
Easthampton Easthampton HS	9-12	Fontaine Brothers	\$30,904,000	510	Bid	110,400	\$280	\$26,642,589	\$241	Design/Bid/Build	16-May-11	25-Oct-13		26%	0.76%	Continuing slab on grade installation in Center and West Wings, steel erection in Center Wing, and steel decking in East and Center Wings. Roof installation has begun.	\$24,104,384	
East Bridgewater E. Bridgewater Jr/Sr HS	7-12	Fontaine Brothers	\$65,409,000	950	Bid	213,544	\$306	\$48,829,117	\$229	Design/Bid/Build	10-Aug-11	24-Jun-13	7 Days	5%	0.00%	Site work is underway. Steel is erected in Zones D&C. Remaining foundation work continues.	\$43,317,092	
Fall River Morton MS	6-8	J&J Contractors	\$37,654,000	625	Bid	130,576	\$288	\$29,921,971	\$229	Design/Bid/Build	4-Nov-11	30-May-13		3%	0.00%	GC contract was executed January 6, 2012. Footings are 50% complete with steel scheduled to arrive in April 2012.	\$38,251,808	
Foxborough Foxborough HS	9-12	CTA	\$11,628,733	885	Bid	218,500	\$53	\$9,274,400	\$42	Design/Bid/Build	25-Jan-10	31-Oct-11		100%	7.47%	Remaining punchlist work being completed on 2nd shift. Overall project completion was scheduled for February 29, 2012. The District is considering additional work that would extend the completion date.	\$7,226,509	
Hampden-Wilbraham Minnechaug HS	9-12	Fontaine Brothers	\$48,597,500	1,225	Bid	231,467	\$210	\$37,499,962	\$162	Design/Bid/Build	22-Jul-10	28-Jun-12		78%	1.55%	Casework installation underway as well as ceilings and above ceiling work. Painting continues. MEP installations continue in gym, cafeteria and auditorium.	\$34,863,838	
Hanover Hanover HS	9-12	Callahan	\$38,652,255	800	Bid	157,000	\$246	\$28,060,313	\$179	Design/Bid/Build	28-Sep-09	1-Jun-11		98%	4.30%	Working on punchlist of the new building. Minor sitework to be completed in the Spring of 2012.	\$22,263,877	
Hudson John F Kennedy MS	5-7	Agostini/Bacon	\$35,102,573	715	Bid	119,685	\$293	\$28,373,294	\$237	Design/Bid/Build	28-Sep-11	29-Nov-13		7%	0.12%	Steel erection began in late January and is on schedule. Site utility work and underground MEP utility work is proceeding on schedule.	\$24,005,749	
Maynard Maynard HS	8-12	CTA	\$36,650,000	410	Bid	121,544	\$302	\$30,630,013	\$252	Design/Bid/Build	18-Aug-11	6-Dec-13		11%	0.00%	Concrete foundation work is completed in all areas. Temporary construction power has been installed. Underslab work and steel erection has commenced.	\$23,483,860	
Marshfield Governor Winslow ES	K-5	Enterprise Equipment Co.	\$1,606,479	494	Bid	65,790	\$24	\$1,408,279	\$21	Design/Bid/Build	Apr-11	29-Feb-12		97%	1.70%	Construction on both the windows and HVAC is complete. The work to repair the windows that failed the commissioning test has been completed. Commissioning on HVAC is complete and training on system is ongoing.	\$991,294	
Middleton Howe-Manning ES	4-6	CTA	\$18,351,184	553	Bid	83,934	\$219	\$14,670,854	\$175	Design/Bid/Build	06-Apr-10	30-Jul-11		100%	6.03%	New building occupied September 7, 2011. Completing punchlist work and technology installation.	\$12,311,976	
Nashoba Pompositticut ES	K-5	P.J. Stella Construction	\$23,640,900	600	Bid	98,030	\$241	\$18,906,998	\$193	Design/Bid/Build	15-Jun-10	12-Jun-12	30 Days	78%	2.00%	Except for remaining punch list work, D-wing (classroom areas) and C-Wing (Administration, Library and Gymnasium / Cafeteria) have been completed. Students and staff moved into the new addition Phase I area on February 27 & 28, 2012 versus the planned date of January 17, 2012. Commissioning and functional testing work is ongoing on all mechanical and electrical equipment. Miscellaneous fence and security measures have been set up around the site in preparation for Phase II construction. Phase II abatement is underway.	\$15,239,622	
Natick Natick HS	9-12	Brait Builders Corp.	\$62,141,700	1,300	Bid	254,225	\$244	\$53,213,182	\$209	Design/Bid/Build	13-Sep-10	15-Jun-12		67%	2.70%	Finishes are underway in several areas. Casework, doors and hardware installed on the 2nd/3rd floors. Site work is suspended for the winter.	\$38,209,033	
Norfolk Freeman-Centennial ES	3-6	Fontaine Brothers	\$25,354,966	610	Bid	96,410	\$263	\$20,023,001	\$208	Design/Bid/Build	9-Nov-10	18-Jun-12		60%	1.26%	Commissioning ongoing for waterproofing, air barrier, windows, and MEP's. Exterior masonry complete. Sectors 1, 2, and 3 roofs are complete. Sectors 4 and 5 roofs are ongoing. Interior drywall installation is ongoing. Interior painting has commenced. Door frames are installed. HVAC is mostly complete. Electrical and plumbing rough-ins are complete and finishes are underway.	\$15,861,760	
Norwood Norwood HS	9-12	Agostini	\$54,377,098	1,100	Bid	227,374	\$239	\$42,573,646	\$187	Design/Bid/Build	19-May-09	13-May-11		99%	1.20%	Minor sitework remaining to be completed in the Spring of 2012.	\$38,154,487	
Plymouth Plymouth HS	9-12	J&J Contractors	\$64,887,000	1,350	Bid	267,497	\$243	\$48,779,703	\$182	Design/Bid/Build	3-May-10	15-May-12	7 Days	76%	4.75%	Finishes are underway on all floors. Site work was suspended until Spring of 2012. MEP contractors are installing finishes throughout the classroom wings. The kitchen, auditorium and gym are progressing.	\$41,810,972	
Sturbridge Burgess ES	K-6	Fontaine Brothers	\$22,946,000	860	Bid	131,630	\$174	\$17,591,000	\$134	Design/Bid/Build	10-Aug-10	1-Oct-12		89%	4.08%	New addition is complete and in service. Renovation of the attached existing building is progressing and is scheduled to be complete by the end of March 2012. Final demolition work and ball fields will then be constructed during summer months. Early completion is scheduled for November 2012.	\$16,616,077	
Sutton MS/HS	6-12	TLT Construction Corp.	\$41,230,800	840	Bid	171,401	\$241	\$32,998,403	\$193	Design/Bid/Build	1-Jul-11	1-Jul-14	42-56 Days	20%	0.00%	Footings and foundations for the new Middle School continue. Steel erection for the new Middle School is ongoing. Underground and overhead utilities at the south end of the site are nearing completion.	\$26,976,617	
Tewksbury Tewksbury HS	9-12	CTA/Methuen Construction Co.	\$51,600,000	1,100	Bid	218,781	\$236	\$40,159,651	\$184	Design/Bid/Build	15-Oct-10	3-Aug-12	28 Days	78%	2.54%	The installation of exterior curtain wall frames and glazing continue. Drywall and ceilings are well underway. Finishes have begun on some floors.	\$36,622,570	
West Springfield West Springfield HS	9-12	Fontaine Brothers	\$83,961,000	1,270	Bid	257,525	\$326	\$55,482,581	\$215	Design/Bid/Build	14-Dec-11	20-Jun-13		0%	0.00%	GC has mobilized and has started securing the site. Clearing and grading are underway.	\$68,808,290	
Winchester Vinson-Owen ES	K-5	CTA	\$21,731,066	420	PFA	74,774	\$291	\$15,558,357	\$208	Design/Bid/Build	13-Feb-12	1-May-13		<1%	0.00%	GC has not mobilized.	\$10,399,463	
Adams-Cheshire Hoosac Valley MSHS	6-12	Gilbane	\$32,439,293	805	Bid	173,999	\$186	24,009,952	\$138	CM-R	17-May-11	31-Jul-12		65%	<0.01%	Nearly all windows are installed. New skylight is complete. Permanent power and boilers are installed. Finish mechanicals and flooring are ongoing. HS gym is 65% complete. MS gym is 35% complete.	\$28,243,131	
Burlington Marshall Simonds MS	6-8	CTA	\$24,612,440	880	Bid	151,000	\$163	\$18,988,987	\$126	CM-R	15-Apr-11	17-May-13		32%	1.40%	Drywall finishes, tile and ceiling grid installations are ongoing in the new addition. Renovations are ongoing on the occupied building on the third of six phases to be completed this year.	\$16,933,103	
Dedham Avery ES	K-5	Consigli	\$18,174,209	310	Bid	62,723	\$290	\$13,528,098	\$216	CM-R	15-Oct-10	5-Mar-12		93%	5.24%	Substantial completion to be granted on March 5, 2012. Punchlist items are in process. Exterior work remaining includes completion of playgrounds and minor weather dependent work on roadway and walkway surfaces.	\$10,778,452	
Grafton Memorial Sr HS	9-12	Dimeo	\$54,030,917	900	Bid	186,351	\$290	\$42,033,245	\$226	CM-R	18-Aug-10	17-Jul-12		67%	0.90%	Exterior masonry complete. Window installation is near complete. Interior finishes ongoing include painting, furnishings, lighting, and wall tile. Lockers have been delivered and installation is ongoing. Floor tile installed in various sections. Roofing is ongoing and nearly complete at all locations. RTU's are mounted and installed. MEP rough-ins are complete and finishes are underway. Exterior metal panel installation and site work including finished sidewalks, paving, and curbing are ongoing.	\$36,108,679	
Leominster Leominster SHS	9-12	S.O.M.	\$33,186,700	1,825	Bid	295,859	\$112	\$25,087,969	\$85	CM-R	1-Jul-11	30-Aug-13		28%	0.19%	The fire separation wall, exterior wall sheathing, roofing, and interior partitions have been completed for the new science addition. Installation of ductwork and waste piping are underway. MEP trades continue rough-in work in the B/D wings.	\$30,693,543	
Longmeadow Longmeadow HS	9-12	Gilbane	\$63,685,998	1,000	Bid	184,365	\$345	\$38,733,395	\$210	CM-R	Nov-10	23-Feb-13		30%	0.63%	Steel erection and decking in area B are complete. The work installing the truss and the light monitors around the truss at the gym continue. Installation of heating piping on level one of Area C continues.	\$33,067,140	
Medway MS	5-8	Consigli	\$17,876,231	800	Bid	223,780	\$80	\$13,162,034	\$59	CM-R	Oct-11	30-Apr-13		12%	0.00%	Front entry work has progressed. Structural steel for the new entrance started on January 31, 2012.	\$10,051,609	
Methuen Methuen HS	9-12	Terminated Dimeo 12/31/2011	\$74,917,204	2,075	PFA	368,017	\$204	\$63,689,716	\$173	CM-R	21-Jul-11	Aug-14		5%	0.00%	Completed enabling package including abatement/demolition of the existing theater area, temporary plumbing, fire protection, HVAC and electrical work along with temporary steel support work required to maintain utility services. District terminated the CM-R contract effective December 31, 2011. The District's project team is currently negotiating a new CM-R contract.	\$64,734,701	

**Projects in Construction  
MSBA Grant Basis and Maximum Grant Amount**

Project	Grade	Contractor	Total Construction Cost*	Projected Enroll	PFA or Bid Data	Proposed Square Footage	Construction Cost per Square Foot	Building Cost	Building Cost per Square Foot	Project Type	Construction Start	Estimated Substantial Completion Date	Reporting Variance from Schedule	Physical Progress (%)	Change Orders (%)	Construction Status	Approximate Maximum Grant Amount *
Needham Newman ES	K-5	Consigli	\$19,064,745	680	Bid	119,264	\$160	\$13,367,855	\$112	CM-R	16-Jun-10	27-Aug-12		71%	3.70%	Punchlist items are underway in the core areas. Work in the classrooms and admin areas continue.	\$8,598,929
Rockland John Rogers MS/ HS	5-12	Agostini	\$66,362,037	1,525	Bid	268,106	\$248	\$47,721,785	\$178	CM-R	15-Jan-10	1-Aug-12		59%	0.00%	Phase 2 areas in the high school have been turned over, and phase 3 area work is underway. Classrooms in areas D & G and auditorium are in the finish phase including painting, wood doors, hardware installation, acoustical ceiling tile installation, casework and millwork installation. Floors have been prepped for sheet vinyl installation. The restrooms in area D have been tiled and plumbing fixtures installed. HVAC, plumbing, fire protection and electrical finishes in areas D & G are 75% complete. The auditorium is painted. Wood clouds and cat walk installation is 75% complete. Middle School: exterior brick veneer work is complete; window and curtain wall installation is 75% complete; metal panel installation is ongoing; MEP rough-in, drywall installation, painting and tiling is ongoing. Eagle Elevator Co has begun the elevator installation.	\$52,837,940
Sharon Sharon MS	6-8	Consigli	\$34,987,118	845	Bid	171,806	\$204	\$24,732,123	\$144	CM-R	1-Apr-10	23-Jan-12		92%	2.17%	The building was occupied after the February school break. Punch list work is being completed.	\$22,670,388
Shrewsbury Sherwood MS	5-6	Gilbane	\$33,986,286	900	Bid	129,939	\$262	\$22,823,030	\$176	CM-R	7-Mar-11	1-Sep-13		39%	0.23%	Building is enclosed. MEP rough-in work is progressing on schedule. Installation of drywall in classrooms is progressing.	\$23,912,246
Somerville E. Somerville Community School	K-8	Gilbane	\$27,570,102	500	PFA	121,100	\$228	\$21,575,058	\$178	CM-R	7-Nov-11	6-Mar-13		13%		CMU block walls continue in A&B Building. Underground plumbing and demolition of the exterior of C&D Building are underway.	
Southbridge Southbridge MS/HS	6-12	Consigli	\$59,307,632	1,050	Bid	199,740	\$297	\$41,487,200	\$208	CM-R	30-Nov-10	1-Jun-12		60%	0.22%	Interior CMU and glazed block have been completed. Exterior brick veneer and precast have been completed. Roof work is 98% complete. Drywall installation, taping, sanding and painting continues throughout the building.	\$52,019,398
Uxbridge High School	9-12	Shawmut Design	\$35,293,766	600	Bid	123,000	\$287	\$27,929,534	\$227	CM-R	28-Feb-11	20-Jun-12		56%	0.75%	Finishes are being installed throughout the building. MEP contractors are well underway.	\$21,973,620
Wayland Wayland HS	9-12	Shawmut Design	\$54,230,819	900	Bid	171,000	\$317	\$37,343,299	\$218	CM-R	28-Jun-10	1-Dec-11		90%	1.60%	New buildings occupied January 3, 2012. Demolition of existing buildings continue.	\$24,051,231
Wellesley Wellesley HS	9-12	Turner	\$82,942,222	1,500	Bid	280,000	\$296	\$55,814,300	\$199	CM-R	24-Aug-09	5-Feb-12		87%	1.83%	The new building was occupied after the February school break. Punch list work is nearing completion. Demolition and abatement of the old high school is underway.	\$40,117,222
<b>WAIT LIST PROJECTS IN CONSTRUCTION</b>																	
<b>Wait List Program Totals</b>			<b>\$135,184,704</b>	<b>2,600</b>		<b>554,570</b>											<b>\$148,784,718</b>
Springfield Putnam Voc Tech HS	9-12	Consigli	\$86,039,066	1,400	Bid	315,000	\$273	\$62,949,742	\$200	CM-R	18-May-10	20-Jul-12	30 Days Ahead	80%	0%	Exterior- Small amount of work remaining on main entrance and exterior doors. Interior- Finishes are ongoing throughout. Terrazo floor installation continues. Gym is complete except bleachers and scoreboard. FF&E scheduled to be delivered starting March 5, 2012. Permanent Certificate of Occupancy scheduled for June 1, 2012.	\$102,872,837
Worcester North HS	9-12	Gilbane	\$49,145,638	1,200	Bid	239,570	\$205	\$40,860,983	\$171	CM-R	24-Sep-08	Jun-11		90%	3%	Phase 3 of the project which includes abatement & demo of the existing school is underway and the remainder of the sitework to start in the Spring of 2012.	\$45,911,881

### 2012 Estimated Bid Dates

Note bid dates are **Estimates ONLY**. Please contact Districts for exact information.

Total Project Budget denotes total District costs and does not denote the basis of the MSBA Total Facilities Grant.

■ - Denotes bid phase in progress or complete    
 ■ - Denotes estimated bid dates    
 ■ - Denotes estimated GMP dates

DISTRICT	DESIGN BASIS FOR ENROLLMENT	PROJECT BUDGET <small>Shown in Millions</small>	CONSTRUCTION BUDGET <small>Shown in Millions</small>	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC
<small>*Projects Considering the CM @ Risk Method</small>															
<b>*ASHBURNHAM-WESTMINSTER</b>	520	\$30.0	\$24.8												
				JR Briggs ES New Construction: Filed-Sub Bids rcv'd 1/12. GMP issued 3/8.											
<b>NORFOLK COUNTY AGRICULTURAL</b>	550	\$28.6	\$22.3												
				Norfolk County Aggi Renovation: Filed-Sub Bids rcv'd 1/18. G.C. Bids due 2/1 NTP Targeted March.											
<b>*SRINGFIELD -FOREST PARK</b>	660	\$43.4	\$34.0												
				Springfield Forest Park MS: Filed-Sub Bids rcv'd 3/2. GMP Targeted March.											
<b>*SOMERVILLE</b>	500	\$33.2	\$15.2												
				East Somerville Community School Addition/Renovation: Filed-Sub Bids rcv'd 6/14 GMP Targeted March.											
<b>DOUGLAS</b>	552	\$50.7	\$38.9												
				Douglas IS New Construction: Filed-Sub Bids rcv'd 1/12. G.C. Bids rcv'd 1/20. NTP issued 3/2.											
<b>WINCHESTER</b>	420	\$28.7	21.7												
				Vinson-Owen ES New Construction: Filed-Sub Bids rcv'd 1/5. G.C. Bids Due 2/2. NTP issued 2/13.											
<b>DRACUT</b>	1160	\$60.4	\$47.30												
				Dracut Senior HS Addition/Renovation: Filed-Sub Bids Due 3/28. G.C. Bids Due 4/11. NTP Targeted May.											
<b>*SOUTHEASTERN REGIONAL RVT</b>	1370	\$34.2	\$26.5												
				SRVT Add/Reno: Filed-Sub Bids Due 2/29. GMP Targeted March.											
<b>*NORTON</b>	700	\$34.6	\$27.0												
				Norton HS Addition/Renovation: Filed-Sub Bids Due 3/15. GMP Targeted March.											
<b>QUINCY</b>	620	\$50.0	\$32.6												
				Central MS New Construction: Filed-Sub Bids Due 3/8. G.C. Bids Due 3/22. NTP Targeted March.											
<b>ARLINGTON</b>	380	\$20.7	\$15.7												
				Arlington Thompson ES New Construction: Filed-Sub Bids rcv'd 3/6. G.C. Bids Due 3/27. NTP Targeted April.											
<b>LYNNFIELD</b>	740	\$4.5	\$3.2												
				Lynnfield HS Addition: Filed-Sub Bids Due 4/19. G.C. Bids Due 4/27. NTP Targeted April.											
<b>MARBLEHEAD</b>	425	\$25.9	\$20.2												
				Marblehead Glover ES New Construction: Filed-Sub Bids Due 5/9. G.C. Bids Due 5/23. NTP Targeted June.											
<b>HINGHAM</b>	1020	\$60.9	\$50.4												
				Hingham MS New Construction: Filed-Sub Bids Due 5/4. G.C. Bids Due 5/14. NTP Targeted June.											
<b>WESTFIELD</b>	600	\$35.9	\$25.2												
				Abner Gibbs ES New Construction: Filed-Sub Bids Due 4/25. G.C. Bids Due 5/9. NTP Targeted May.											
<b>*ESSEX-NS</b>	1440	\$125.0	\$96.50												
				Essex Northshore HS New Construction: Early Site Packages Due 3/30. Filed-Sub Bids Due 5/30. GMP Targeted July.											
<b>*ANDOVER</b>	680	\$44.7	\$34.5												
				Andover Bancroft ES New Construction: Early Site, Steel, Foundations Packages due 5/4. Filed-Sub Bids due 6/1. GMP Targeted August.											
<b>*METHUEN</b>	2075	\$99.1	\$74.9												
				Methuen HS Addition/Renovation: GMP Targeted April.											
<b>SOMERSET BERKLEY</b>	1000	\$82.8	\$66.8												
				Somerset Berkley RHS New Construction: Filed-Sub Bids Due 5/23. G.C. Bids Due 6/6. NTP Targeted June.											
<b>*SAUGUS</b>	725	\$20.3	\$15.7												
				Saugus Belmonte MS Repair: Filed-Sub Bids Due 5/17. GMP Targeted June.											
<b>*DUXBURY</b>	1735	\$128.4	\$99.2												
				Duxbury HS/MS New Construction: Filed-Sub Bids Due 8/17. GMP Targeted September.											
<b>MARSHFIELD</b>	1310	\$103.9	\$80.8												
				Marshfield HS New Construction: Filed-Sub Bids Due 7/23. G.C. Bids Due 8/6. NTP Targeted August.											
<b>WESTON</b>	355	\$31.5	\$21.5												
				Field ES New Construction: Filed-Sub Bids Due 9/10. G.C. Bids Due 9/17. NTP Targeted October.											
<b>*WILMINGTON</b>	960	\$82.7	\$64.4												
				Wilmington HS New Construction: Early Sitework, Foundation, & Steel bid packages. Filed-Sub Bids Due 11/17. GMP Targeted November.											
<b>Subtotal</b>	<b>20,497</b>	<b>\$1,260</b>	<b>\$959.3</b>												
<b>GRAND TOTAL</b>	<b>20,497</b>	<b>\$1,260</b>	<b>\$959.3</b>												
<b>Number of Construction-Related Employment Opportunities Created</b>				<b>4,797</b>											
