

Project Overview Report September 14, 2011

A total of 317 projects are currently in the MSBA's Capital Pipeline. The following summary table provides the category (e.g., New Program, Green Repair) and the number of projects in each phase (e.g., Local Clearance, Construction):

	Total	Local Clearance	Consultant Selection	Feasibility Study/ Schematic Design	Design Development	Construction
Closeout/Audit Complete	39					
New Program	123	17	18	29	18	41
Waitlist	9	0	2	0	1	6
Green Repair	146	0	0	38	62	46
Total	317	17	20	67	81	93

The MSBA utilizes the Project Status chart (see attached) to account for the ongoing status of all District SOIs in the Capital Pipeline. Activity for some of the key milestones is summarized in the table below with the numbers reported indicative of the category requirements. For instance, enrollment certifications are not required for all projects (e.g., repairs) and Owner's Project Managers ("OPMs") are not mandatory for construction projects under \$1.5 million unless required by the MSBA.

Critical Prerequisites:

An agreed-upon enrollment is a key prerequisite for the MSBA to commence a Feasibility Study with a District. To begin the enrollment projection process, a District must file enrollment information utilizing the MSBA's online enrollment projection tool.

After the MSBA and the District have agreed upon an enrollment on which to base the design and executed a Feasibility Study Agreement, the District procures an Owner's Project Manager and then a Designer. There are 17 Districts in the Capital Pipeline who still need to procure an OPM.

After a District has selected an OPM and executed a contract with that OPM, it selects a Designer utilizing either a local designer selection process for projects under \$5 million or the MSBA's Designer Selection Panel for projects over \$5 million. There are 27 Districts in the Capital Pipeline who still need to procure a Designer.

	District Action to Complete	MSBA/ District Collaboration	Completed Activity this Period	Total Completed to Date	Total
Enrollment	9	16	5	113	101,345
Owner's Project Manager	17	11	4	108	Over \$84 million in OPM fees*
Designer	27	8	3	135	Over \$207.6 million in Designer Fees*

* Does not include OPM and Designer Fees associated with repair projects.

Owner’s Project Managers

Since the last report, the following four Districts have completed the OPM selection process:

- Lexington – Estabrook Elementary School
- Auburn – Auburn Middle School
- Newburyport – R.A. Nock Middle School
- Newburyport – F.T. Bresnahan Elementary School (Model School)

Andover - Bancroft Elementary School - The Town has completed the OPM selection process and presented at the September 12, 2011 OPM Review Panel. The Town has requested that MSBA delay the approval of the OPM selection until after it has a better understanding of the DEP appeals and any other legal action.

The following Districts are tentatively scheduled for the upcoming OPM Review Panel meetings:

Panel Date	District/School	Project Description Status	Estimated Project Cost
10/3/11	Greater Lowell / Greater Lowell RVT	Feasibility Study	\$30-\$40 million
10/3/11	Whitman-Hanson / Maquan ES	Feasibility Study	\$20-\$30 million
10/3/11	Ayer-Shirley / High School	Feasibility Study	\$30-\$40 million
11/7/11	Andover / Bancroft ES	Design Development	\$45 million

Designers

Since the last report, the DSP has met three times resulting in three additional Districts completing the Designer selection process.

Panel Date	District/School	Status	Estimated Project Cost	# of Proposals Received	Top 3 Ranked Firms	Interviews Requested	First-Ranked Selection
8/2/11	West Bridgewater – Middle-Senior HS	Designer Selection	\$35 - \$45 million	12	- Flansburgh - Design Partnership of Cambridge - Finegold Alexander	Yes	TBD
8/23/11	West Bridgewater – Middle-Senior HS	Feasibility Study	\$35 - \$45 million	12	- Flansburgh - Design Partnership of Cambridge - Finegold Alexander	Interviews Held	Flansburgh
8/23/11	Lexington – Joseph Estabrook ES	Designer Selection	\$20 - \$30 million	9	- DiNisco - SMMA - Mount Vernon	Yes	TBD
8/23/11	Webster – Park Avenue ES	Feasibility Study	\$10 - \$25 million	11	- Dore & Whittier - Taylor & Burns - Kaestle Boos	No	Dore & Whittier
8/23/11	Lexington – Joseph Estabrook ES	Feasibility Study	\$20 - \$30 million	9	- DiNisco - SMMA - Mount Vernon	Interviews Held	DiNisco

The following Districts are tentatively scheduled for upcoming DSP meetings:

Greater New Bedford Regional Technical High School – September 20, 2011
 Boston – Quincy Upper School – October 4, 2011
 Chicopee – Chicopee MS – TBD
 Lynnfield – Lynnfield HS – TBD
 Winthrop – Winthrop Sr. High School (Repair) – TBD
 South Hadley – Plains ES – TBD

Commissioning

Since the last report, the MSBA has assigned Commissioning Consultants to an additional four projects as presented in the table below. The MSBA has executed 132 Commissioning Consultant contracts to date, totaling \$10.9 million.

District	School	Estimated Const. Cost	Commissioning Consultant	Contract Amount
Norton	Norton High School	\$27 million	RFS Engineering	\$121,501
Fall River	Morton Middle School	\$42.5 million	Sebesta Blomberg & Associates	\$97,952
Arlington	Thompson Elementary School	\$15.8 million	Consulting Engineering Services,	\$69,517
Shrewsbury	Spring Street Elementary School	\$930,000	Cannon Design	\$28,600
	Total	\$86.23 million	Total	\$317,570

Projects for which we are currently seeking proposals and/or negotiating Work Orders include:

District	School	Responses Due
Marblehead	Glover Primary School	9/9/2011
Brookfield	Brookfield Elementary School	9/9/2011
Middleborough	Mary K. Goode Elementary School	9/9/2011
Mohawk Trail	Green Repair - Multiple Schools	9/9/2011
Nauset	Nauset Regional High School	9/9/2011
Peabody	Green Repair - Multiple Schools	9/9/2011
West Boylston	Major Edwards Elementary School	9/9/2011
Westport	Green Repair - Multiple Schools	9/9/2011
North Middlesex	Green Repair - Multiple Schools	9/9/2011
Salem	Saltonstall Elementary School	9/13/2011
Salem	Collins Middle School	9/13/2011

Projects that are currently in the queue for assignment of a Commissioning Consultant and for which contract documents are being drafted include:


District	School
Mendon-Upton	Miscoe Hill Intermediate School
Fairhaven	Rogers Elementary School
Narragansett	Templeton Center School
Somerset Berkley	Somerset Berkley High School
Cape Cod Regional Vocational Technical	Cape Cod Regional Vocational and Technical High School
Haverhill	Green Repair - Multiple Schools
Lowell	Green Repair - Multiple Schools
Northborough	Robert E. Melican Middle School
Duxbury PS	Duxbury Middle/High School
Pioneer Valley	Green Repair - Multiple Schools
Agawam	Agawam Middle School
Hadley	Hopkins Academy
Marlborough	Green Repair - Multiple Schools
North Andover	Green Repair - Multiple Schools

Status of Green Repair Program

At the September 28, 2011 meeting of the Board of Directors, MSBA staff will be recommending Project Funding Agreements (“PFA”) for five districts, representing 11 projects totaling \$9,340,034 in MSBA Total Facilities Grants. With the Board’s approval, 169 projects will have received authorization to enter into a PFA, totaling \$360,429,537 in Total Project Costs and \$219,855,600 in MSBA Total Facilities Grants.

Green Repair Project Phase

98% - 169 projects authorized for PFA
 Total Project Budgets \$360,429,537
 Total Maximum Facilities Grants \$219,855,600

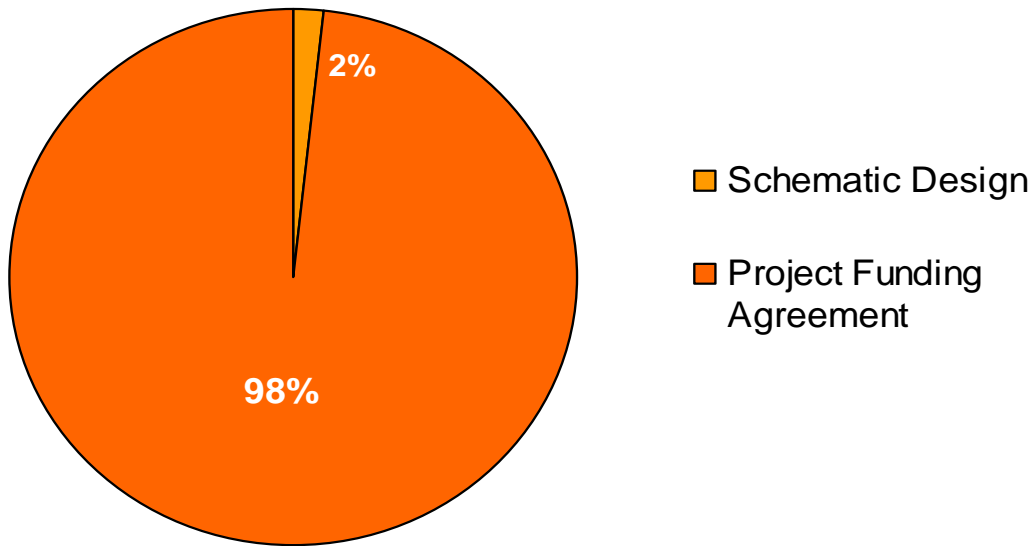

Construction Bids

The following displays the total anticipated number of projects going out to bid between October 1, 2011 – December 31, 2011, and those remaining for 2012:

	Roofs	Windows	Boilers
October	2	0	3
November	6	6	6
December	2	1	1
Total	10	7	10
Remaining 2012 Bids	19	25	10
Total Remaining Bids	29	32	20

Of the bids reviewed:

- 79% of roof projects have come in under budget
- 63% of window projects have come in under budget
- 35% of boiler projects have come in under budget

Remedies sought by Districts for those over budget include:

- Requesting schedule extensions to re-bid at a later date
- Appropriating additional funds to cover the costs of the contract
- Re-bidding immediately with revised bid documents

Districts remaining in Schematic Design:

The following two districts, representing three projects, are currently in the schematic design phase and soon will be submitting the conclusion of their studies:

District	School	Scope	Invite Date
Marlborough	Francis J. Kane Elementary School	Windows	November 17, 2010
Marlborough	Marlborough High School	Roof, Windows, Boiler	November 17, 2010
Westport	Westport Middle School	Windows	November 17, 2010

The following 2 projects will be removed from the Green Repair Program:

District	School	Scope	Invite Date
Natick	Johnson Elementary School	Windows, Boiler	February 9, 2011
West Boylston	Major Edwards Elementary School	Windows	November 17, 2010

Attached to the Project Overview Report are the following:

- Master District Status List
- Project Status Chart: As indicated in the attached chart, Districts continue to make progress with their projects. The narrow solid bar indicates the number of Districts in each category as reported at the June Board meeting.
- 2011 Estimated Bid Dates Schedule:
 - New Program
 - Green Repair Program
- Projects in Construction Report

Massachusetts School Building Authority

No. of Projects: 317

Master District Status List

Yellow = Wait List Project
Green = Green Repair
Red = Changes in last 60 days

District Name	School Name	Status	Preferred Schematic	OPM	Designer	Cx Authority	Procurement Status	CM/GC
Abington PS	Frolio JHS	Local Clearance - 07/08					Undetermined	
Abington PS	Woodsdale IS	Design Development	Repair	RF Walsh Collaborative Partners	Gale Associates, Inc.	Russo Barr Associates, Inc.		
Acton PS	Douglas ES	Closeout/Audit	Repair	N/A	CBI Consulting Inc.		Undetermined	Gibson Roofs
Adams-Cheshire PS	Adams MS	Design Development	Addition/Renovation	URS Corporation	Tessier Associates	Strategic Building Solutions	CMR - CM Selected	Gilbane Building Company
Agawam PS	Agawam Junior HS	Project Scope & Budget	Repair	Municipal Building Consultants, Inc.	CSS Architects Incorporated			
Amherst-Pelham PS	Amherst Reg MS	Design Development	Repair	Strategic Building Solutions, LLC	Bradley Architects, Inc.	Russo Barr Associates, Inc.		
Andover PS	Bancroft ES	Construction	New Construction	Town of Andover	Symmes Maini & McKee Associates, Inc.	Sebesta Blomberg & Associates	CMR - CM Selected	Skanska USA Building, Inc.
Andover PS	Andover West MS	Design Development	Repair	Skanska USA Building Inc.	Russo Barr Associates, Inc.	Simpson Gumpertz & Heger		
Arlington PS	Thompson ES	Design Development		PMA Consultants	HMFH Architects, Inc.	Consulting Engineering Services, LLC	DBB - In Design	
Arlington PS	M Norcross Stratton ES	Construction	Repair	PMA Consultants	Turowski2 Architecture, Inc.		Undetermined	Unicon, Inc. and Federal Construction Corp.
Ashburnham-West PS	Briggs ES	Design Development	New Construction	STV, Inc.	Lamoureux Pagano & Associates, Inc.	Foreman Building Commissioning, LP	CMR - CM Selected	Consigli Construction Co.
Assabet Valley PS	Assabet Valley Voc HS	Preferred Schematic	Repair	Strategic Building Solutions, LLC	Design Partnership of Cambridge, Inc.			
Athol-Royalston PS	Riverbend ES	Local Clearance - 09/10						
Attleboro PS	Hyman Fine ES	Construction	Repair	Skanska USA Building, Inc.	Russo Barr Associates, Inc.	Gale Associates, Inc.		
Attleboro PS	Hill-Roberts ES	Construction	Repair	Skanska USA Building, Inc.	Russo Barr Associates, Inc.	Gale Associates, Inc.		
Attleboro PS	Attleboro HS	Construction	Repair	Skanska USA Building, Inc.	Russo Barr Associates, Inc.	Gale Associates, Inc.		
Attleboro PS	A. Irvin Studley ES	Construction	Repair	Skanska USA Building, Inc.	Russo Barr Associates, Inc.	Gale Associates, Inc.		
Auburn PS	Auburn MS	Designer Selection						
Avon PS	Ralph D Butler ES	Construction	Repair	Skanska USA Building Inc.	Knight, Bagge & Anderson, Inc.	Cannon Design		
Ayer PS	Ayer HS	OPM Selection						
Barnstable PS	West Barnstable ES	Construction	Repair	PMA Construction Services	Gale Associates, Inc.	CBI Consulting Inc.		
Bellingham PS	Bellingham Memorial MS	Construction	Repair	Daedalus Projects Inc	Richard D. Kimball Company, Inc.	WSP Flack + Kurtz	Undetermined	General Air Conditioning & Heating, Inc.
Belmont PS	Roger E Wellington ES	Construction	New Construction	PMA Consultants	Jonathan Levi Architects LLC	Strategic Building Solutions	CMR - CM Selected	Skanska USA Building, Inc.

Master District Status List

Yellow = Wait List Project

Green = Green Repair

Red = Changes in last 60 days

District Name	School Name	Status	Preferred Schematic	OPM	Designer	Cx Authority	Procurement Status	CM/GC
Berkshire Hills PS	Monument Mt Reg HS	OPM Selection						
Berlin-Boylston PS	Tahanto Reg HS	Construction	New Construction	PMA Consultants	HMFH Architects, Inc.	Strategic Building Solutions	DBB - Contract Awarded	CTA Construction
Beverly PS	Beverly HS	Construction	Addition/Renovation	Heery International	Mount Vernon Group Architects, Inc.		DBB - Contract Awarded	CTA Construction Co.
Billerica PS	Parker ES	Construction	New Construction	Joslin, Lesser & Associates, Inc.	Symmes Maini & McKee Associates, Inc.	Sebesta Blomberg & Associates	DBB - Contract Awarded	CTA Construction Co
Billerica PS	Billerica Memorial HS	Construction	Repair	Municipal Building Consultants, Inc.	Knight, Bagge & Anderson, Inc.	VP Consultants, LLC		
Blackstone Valley Reg PS	Blackstone Valley HS	Construction	Repair	Strategic Building Solutions, LLC	Reinhardt Associates, Inc.	Cannon Design		
Boston PS	Excel HS	Approved Project Vote Pending	Repair	Daedalus Projects Inc	Gale Associates, Inc.	Simpson Gumpertz & Heger		
Boston PS	Joseph Lee ES*	Approved Project Vote Pending	Repair	Daedalus Projects Inc	BLW Engineers, Inc./Gale Associates, Inc.	Simpson Gumpertz & Heger		
Boston PS	Thomas A Edison JHS	Approved Project Vote Pending	Repair	Daedalus Projects Inc	BLW Engineers, Inc.	Simpson Gumpertz & Heger		
Boston PS	Washington Irving MS	Approved Project Vote Pending	Repair	Daedalus Projects Inc	Gale Associates, Inc.	Simpson Gumpertz & Heger		
Boston PS	Clarence R Edwards MS	Approved Project Vote Pending	Repair	Daedalus Projects Inc	BLW Engineers, Inc.	RFS Engineering		
Boston PS	Quincy Upper School	Designer Selection		City of Boston				
Boston PS	Dearborn MS	Local Clearance - 09/10						
Boxford PS	Harry Lee Cole Primary	Closeout/Audit	Repair		Russo Barr Associates, Inc.		Undetermined	MDM Engineering, Inc
Braintree PS	South MS	Closeout/Audit	Repair	Town Employee	Habeeb & Associates Architects, Inc.		DBB - Contract Awarded	Construction Dynamics
Braintree PS	Hollis ES	Construction	Repair	RF Walsh Collaborative Partners	Habeeb & Associates Architects, Inc.	Cannon Design		
Braintree PS	Highlands	Construction	Repair	RF Walsh Collaborative Partners	Habeeb & Associates Architects, Inc.	Cannon Design		
Braintree PS	East MS	Construction	Repair	RF Walsh Collaborative Partners	Habeeb & Associates Architects, Inc.	Cannon Design		
Braintree PS	Archie T Morrison ES	Construction	Repair	RF Walsh Collaborative Partners	Habeeb & Associates Architects, Inc.	Cannon Design		
Braintree PS	Braintree HS	Construction	Repair	RF Walsh Collaborative Partners	Habeeb & Associates Architects, Inc.	Cannon Design		
Brockton PS	North Junior HS	Building Completion 2011	Repair	Skanska USA Building Inc.	CSS Architects Incorporated	RFS Engineering		
Brockton PS	Brockton HS	Building Completion 2012	Repair	Skanska USA Building Inc.	CSS Architects Incorporated	Simpson Gumpertz & Heger		
Brockton PS	Downey ES	Building Completion 2012	Repair	Skanska USA Building Inc.	CSS Architects Incorporated	Simpson Gumpertz & Heger		
Brockton PS	East Junior HS	Building Completion 2012	Repair	Skanska USA Building Inc.	CSS Architects Incorporated	RFS Engineering		
Brockton PS	Edgar B Davis ES	Building Completion 2012	Repair	Skanska USA Building Inc.	CSS Architects Incorporated	Simpson Gumpertz & Heger		
Brockton PS	Hancock ES	Building Completion 2011	Repair	Skanska USA Building Inc.	CSS Architects Incorporated	Simpson Gumpertz & Heger		

Master District Status List

Yellow = Wait List Project

Green = Green Repair

Red = Changes in last 60 days

District Name	School Name	Status	Preferred Schematic	OPM	Designer	Cx Authority	Procurement Status	CM/GC
Brockton PS	Oscar F Raymond ES	Building Completion 2012	Repair	Skanska USA Building Inc.	CSS Architects Incorporated	Simpson Gumpertz & Heger		
Brockton PS	West Junior HS	Building Completion 2011	Repair	Skanska USA Building Inc.	CSS Architects Incorporated	Simpson Gumpertz & Heger		
Brookfield PS	Brookfield ES	Design Development	Repair	Diversified Project Management	Habeeb & Associates Architects, Inc.			
Brookline PS	Heath K-8	Design Development	Addition/Renovation	Town of Brookline Building Department	Miller Dyer Spears Inc.	Consulting Engineering Services, LLC		
Brookline PS	John D Runkle K-8	Construction	Addition/Renovation	Town of Brookline Building Department	Design Partnership of Cambridge, Inc.	Consulting Engineering Services, LLC	DBB - Contract Awarded	G&R construction Inc.
Burlington PS	Memorial ES	Construction	New Construction	Construction Monitoring Services, Inc.	Knight, Bagge & Anderson, Inc.	Consulting Engineering Services, LLC	DBB - Contract Awarded	CTA Construction Co.
Burlington PS	Marshall Simonds MS	Construction	Addition/Renovation	Construction Monitoring Services, Inc.	Knight, Bagge & Anderson, Inc.	RDK Engineering	CMR - CM Selected	CTA Construction Co.
Cambridge PS	Cambridge Rindge and Latin HS	Closeout/Audit			HMFH Architects, Inc.		DBB - Contract Awarded	W.T. Rich, Inc.
Canton PS	Rodman Pre-K Center	Construction	Repair	Maguire Group	Russo Barr Associates, Inc.	Cannon Design		
Canton PS	Canton HS	Construction	Repair	Maguire Group	Russo Barr Associates, Inc.	Cannon Design		
Cape Cod Region Voc Tech PS	Cape Cod Regional Voc / Tech HS	Approved Project Vote Pending	Repair	URS Corporation	Garcia Galuska DeSousa			
Carlisle PS	Carlisle K-8	Construction	Addition/Renovation	Daedalus Projects, Inc.	HMFH Architects, Inc.	Horizon Engineering Associates, LLP	DBB - Contract Awarded	H.V. Collins Company
Central Berkshire PS	Craneville ES	Design Development	Repair	Daedalus Projects Inc	Bradley Architects, Inc.	Strategic Building Solutions		
Central Berkshire PS	Kittredge ES	Design Development	Repair	Daedalus Projects Inc	Bradley Architects, Inc.	Strategic Building Solutions		
Chatham PS	Chatham HS	Local Clearance - 09/10						
Chelmsford PS	Chelmsford HS	Design Development	Repair	Vertex Construction Services, Inc.	Russo Barr Associates, Inc.	Simpson Gumpertz & Heger		
Chelmsford PS	Byam ES	Design Development	Repair	Vertex Construction Services, Inc.	Russo Barr Associates, Inc.	Simpson Gumpertz & Heger		
Chelsea PS	Clark Avenue MS	Local Clearance - 07/08			Jacobs			
Chicopee PS	Chicopee Academy	Designer Selection		Arcadis				
Concord-Carlisle PS	Concord Carlisle HS	Project Scope & Budget		KV Associates, Inc.	OMR Architects, Inc.			
Conway PS	Conway Grammar ES	Closeout/Audit	Repair		Richardson Gorman Architects		Undetermined	RAC Builders, Inc.
Danvers PS	Danvers HS	Construction	Addition/Renovation	Construction Monitoring Services, Inc.	DiNisco Design Partnership, Limited	Turner Facilities Management Solutions	DBB - In Design	Bacon Construction Co., Inc.
Dartmouth PS	James M. Quinn ES	Construction	Repair	Vertex Construction Services, Inc.	Russo Barr Associates, Inc.	Gale Associates, Inc.		
Dartmouth PS	James M. Quinn ES	Closeout/Audit	Repair					
Dedham PS	Avery ES	Construction	New Construction	Construction Monitoring Services, Inc.	Dore & Whittier Architects, Inc.	WSP Flack + Kurtz	CMR - CM Selected	Consigli Construction Co
Dennis-Yarmouth PS	Ezra H Baker ES	Construction	Repair	STV Construction, Inc.	Knight, Bagge & Anderson, Inc.	CBI Consulting Inc.		

Master District Status List

Yellow = Wait List Project

Green = Green Repair

Red = Changes in last 60 days

District Name	School Name	Status	Preferred Schematic	OPM	Designer	Cx Authority	Procurement Status	CM/GC
Douglas PS	Douglas IS	Design Development		Heery International, Inc	DiNisco Design Partnership, Limited	Consulting Engineering Services, LLC	DBB - In Design	
Dracut PS	Dracut SHS	Design Development	Addition/Renovation	RF Walsh Collaborative Partners	Mount Vernon Group Architects, Inc.	RDK Engineering	DBB - In Design	
Dudley-Charlton Reg PS	Shepherd Hill Reg HS	Construction	Repair	Pinck & Co., Inc.	ICON architecture, inc.	Cannon Design		
Duxbury PS	Duxbury HS	Project Scope & Budget		KV Associates, Inc.	Mount Vernon Group Architects, Inc.			
East Bridgewater PS	East Bridgewater HS	Design Development	Model School	RF Walsh Collaborative Partners	Ai3 Architects LLC	Foreman Building Commissioning, LP	DBB - Contract Awarded	Fontaine Bros., Inc.
Easthampton PS	Easthampton HS	Construction	New Construction	Strategic Building Solutions, LLC	Caolo & Bieniek Associates, Inc.	Consulting Engineering Services, LLC	DBB - Contract Awarded	Fontaine Bros., Inc
Essex North Shore Agr and Tech PS	Essex North Shore Agr and Tech School	Design Development	New Construction	PMA Consultants	Design Partnership of Cambridge, Inc.	Turner Facilities Management Solutions	CMR - CM Selected	Gilbane Building Company
Fairhaven PS	Rogers ES	Project Scope & Budget		Daedalus Projects Inc	HMFH Architects, Inc.			
Fairhaven PS	Hastings MS	Closeout/Audit	Repair	Daedalus Projects Inc	Durland Van Voorhis Architects, Inc.	Gale Associates, Inc.		
Fall River PS	Morton MS	Design Development		Maguire Group Inc.	Mount Vernon Group Architects, Inc.	Sebesta Blomberg & Associates	DBB - Out to Bid	
Falmouth PS	Falmouth High School	Building Completion 2011	Addition/Renovation	Gilbane Building Company	DiNisco Design Partnership, Limited		DBB - Contract Awarded	TLT Construction
Falmouth PS	East Falmouth ES	Closeout/Audit	Repair		Keenan + Kenny Architects, LTD	Gale Associates, Inc.		
Falmouth PS	North Falmouth ES	Closeout/Audit	Repair		Keenan + Kenny Architects, LTD	Gale Associates, Inc.		
Fitchburg PS	Reingold ES	Construction	Repair	Compass Project Management, Inc.	Knight, Bagge & Anderson, Inc.	RDK Engineering		
Fitchburg PS	Crocker ES	Local Clearance - 07/08						
Fitchburg PS	Fitchburg HS	Construction	Repair	Compass Project Management, Inc.	BLW Engineers, Inc.	RDK Engineering		
Fitchburg PS	Memorial IS	Construction	Repair	Compass Project Management, Inc.	BLW Engineers, Inc.	RDK Engineering		
Fitchburg PS	South Street ES	Construction	Repair	Compass Project Management, Inc.	BLW Engineers, Inc.	RDK Engineering		
Fitchburg PS	Memorial IS	Construction	Repair	Compass Project Management, Inc.	Knight, Bagge & Anderson, Inc.	Simpson Gumpertz & Heger		
Fitchburg PS	South Street ES	Closeout/Audit		Compass Project Management, Inc.	Knight, Bagge & Anderson, Inc.	Simpson Gumpertz & Heger		
Fitchburg PS	Reingold ES	Construction	Repair	Compass Project Management, Inc.	BLW Engineers, Inc.	Simpson Gumpertz & Heger		
Fitchburg PS	Goodrich K Center	Construction	Repair	Compass Project Management, Inc.	BLW Engineers, Inc.	RDK Engineering		
Florida PS	Abbott Memorial K-8	Building Completion 2011	Repair		Dietz and Company		DBB - Contract Awarded	Waterman Excavating, Inc
Foxborough PS	Foxborough HS	Building Completion 2011	Repair	Construction Monitoring Services, Inc.	Kaestle Boos Associates, Inc.	Consulting Engineering Services, LLC	DBB - Contract Awarded	CTA Construction Co.
Framingham PS	Mary E Stapleton ES	Construction	Repair	Bargmann, Hendrie + Archetype, Inc.	Russo Barr Associates, Inc.	CBI Consulting Inc.		
Franklin PS	Franklin HS	Preferred Schematic	Model School	Daedalus Projects Inc.				

Master District Status List

Yellow = Wait List Project

Green = Green Repair

Red = Changes in last 60 days

District Name	School Name	Status	Preferred Schematic	OPM	Designer	Cx Authority	Procurement Status	CM/GC
Gardner PS	Waterford Street Primary	Closeout/Audit	Repair	P3 Project Planning Professionals	Knight, Bagge & Anderson, Inc.	VP Consultants, LLC		
Gardner PS	Gardner HS	Closeout/Audit	Repair	P3 Project Planning Professionals	Knight, Bagge & Anderson, Inc.	VP Consultants, LLC		
Gardner PS	Elm Street IS	Closeout/Audit	Repair	P3 Project Planning Professionals	Knight, Bagge & Anderson, Inc.	VP Consultants, LLC		
Georgetown PS	Penn Brook IS	Feasibility Study		Municipal Building Consultants, Inc.	Drummey Rosane Anderson, Inc.			
Gloucester PS	Plum Cove School	Design Development	Repair	Knight, Bagge, & Anderson, Inc.	CGKV Architects, Inc.	Russo Barr Associates, Inc.		
Gloucester PS	Beeman Memorial IS	Design Development	Repair	Knight, Bagge, & Anderson, Inc.	CGKV Architects, Inc.	Russo Barr Associates, Inc.		
Gloucester PS	West Parish ES	Local Clearance - 09/10						
Gloucester PS	Veterans Memorial ES	Design Development	Repair	Knight, Bagge, & Anderson, Inc.	CGKV Architects, Inc.	Russo Barr Associates, Inc.		
Gloucester PS	Ralph B O'Maley MS	Design Development	Repair	Knight, Bagge, & Anderson, Inc.	CGKV Architects, Inc.	Russo Barr Associates, Inc.		
Gloucester PS	East Gloucester ES	Design Development	Repair	Knight, Bagge, & Anderson, Inc.	CGKV Architects, Inc.	Russo Barr Associates, Inc.		
Grafton PS	Grafton Memorial SHS	Design Development	Repair	URS Corporation	CGKV Architects, Inc.			
Grafton PS	Grafton Memorial SHS	Construction	New Construction	Joslin, Lesser & Associates, Inc.	Symmes Maini & McKee Associates, Inc.	Horizon Engineering Associates, LLP	CMR - CM Selected	Dimeo Construction
Grafton PS	South Grafton ES	Design Development	Repair	URS Corporation	CGKV Architects, Inc.	Horizon Engineering Associates, LLP		
Greater Lawrence RVT PS	Gr Lawrence Regional Voc / Tech HS	Local Clearance						
Greater Lowell Voc Tec PS	Gr Lowell Regional Voc / Tech HS	OPM Selection	Repair					
Greater New Bedford PS	Gr New Bedford Voc / Tech HS	Designer Selection		Construction Monitoring Services, Inc.				
Greenfield PS	Four Corners ES	Design Development	Repair	P3 Project Planning Professionals	Tighe & Bond, Inc.	Strategic Building Solutions		
Greenfield PS	Greenfield HS	Feasibility Study		Construction Monitoring Services, Inc.	Dore & Whittier Architects, Inc.			
Hadley PS	Hopkins Academy	Project Scope & Budget	Repair	Strategic Building Solutions, LLC	CSS Architects Incorporated			
Hamilton-Wenham PS	Cutler ES	Closeout/Audit	Repair	Municipal Building Consultants, Inc.	Richard D. Kimball Company, Inc.	Sebesta Blomberg & Associates	DBB - Contract Awarded	Thomas E. Snowden Inc.
Hampden-Wilbraham PS	Minnechaug Reg HS	Construction	Model School	ARCADIS U.S., Inc.	Mount Vernon Group Architects, Inc.	Horizon Engineering Associates, LLP	DBB - Contract Awarded	Fontaine Bros.
Hancock PS	Hancock ES	Construction	Repair	N/A	Westall Architects			
Hanover PS	Hanover HS	Construction	New Construction	PMA Consultants	HMFH Architects, Inc.	Horizon Engineering Associates, LLP	DBB - Contract Awarded	Callahan, Inc
Haverhill PS	Consentino MS	Approved Project Vote Pending	Repair	Vertex Construction Services, Inc.	CSS Architects Incorporated			
Haverhill PS	Greenleaf Primary	Approved Project Vote Pending	Repair	Vertex Construction Services, Inc.	CSS Architects Incorporated			
Haverhill PS	Haverhill HS	Construction		Vertex Construction Services, Inc.			DBB - Contract Awarded	

Master District Status List

Yellow = Wait List Project

Green = Green Repair

Red = Changes in last 60 days

District Name	School Name	Status	Preferred Schematic	OPM	Designer	Cx Authority	Procurement Status	CM/GC
Haverhill PS	John G Whittier MS	Approved Project Vote Pending	Repair	Vertex Construction Services, Inc.	CSS Architects Incorporated			
Haverhill PS	Tilton Primary	Approved Project Vote Pending	Repair	Vertex Construction Services, Inc.	CSS Architects Incorporated			
Haverhill PS	Walnut Square Primary	Approved Project Vote Pending	Repair	Vertex Construction Services, Inc.	CSS Architects Incorporated			
Haverhill PS	Caleb Dustin Hunking MS	Approved Project Vote Pending	Repair	Vertex Construction Services, Inc.	CSS Architects Incorporated			
Hingham PS	Hingham MS	Project Scope & Budget	Model School	Knight, Bagge & Anderson, Inc.	AI3 Architects LLC			
Holbrook PS	Holbrook JHS / SHS	OPM Selection						
Holyoke PS	Holyoke HS	Construction			Design Partnership of Cambridge, Inc.		DBB - Contract Awarded	
Hopkinton PS	Center ES	Approved Project Vote Pending	New Construction	Town of Hopkinton	Design Partnership of Cambridge, Inc.		Undetermined	
Hudson PS	John F Kennedy MS	Design Development	New Construction	PMA Consultants	OMR Architects, Inc.	WSP Flack + Kurtz	DBB - Contract Awarded	Bacon/ Agostini Construction
Leicester PS	Leicester Memorial ES	Design Development	Repair	Maguire Group	Bradley Architects, Inc.			
Leicester PS	Leicester MS	Design Development	Repair	Maguire Group	Bradley Architects, Inc.	Cannon Design		
Leominster PS	Leominster SHS	Design Development	Addition/Renovation	Daedalus Projects, Inc.	Lamoureux Pagano & Associates, Inc.	Horizon Engineering Associates, LLP	DBB - Contract Awarded	WT Rich
Leverett PS	Leverett ES	Design Development	Repair	Potomac Capital Advisors	DiMarinisi & Wolfe Architects Urban	Russo Barr Associates, Inc.		
Lexington PS	Lexington HS	Closeout/Audit	Repair	Skanska USA Building Inc.	Russo Barr Associates, Inc.	Simpson Gumpertz & Heger		
Lexington PS	Joseph Estabrook ES	Feasibility Study		RF Walsh Collaborative Partners	DiNisco Design Partnership, Limited			
Lincoln PS	Lincoln K-8	Feasibility Study		Skanska USA Building, Inc.	OMR Architects, Inc.			
Littleton PS	Russell St ES	Closeout/Audit	Repair	Daedalus Projects, Inc.	Drumme Rosane Anderson, Inc.	WSP Flack + Kurtz	DBB - Contract Awarded	Colantonio, Inc.
Longmeadow PS	Longmeadow HS	Construction	New Construction	Joslin, Lesser & Associates, Inc.	OMR Architects, Inc.	Foreman Building Commissioning, LP	CMR - CM Selected	Gilbane Building Company
Lowell PS	Charles W Morey ES	Closeout/Audit		Watermark			DBB - Contract Awarded	CTA Construction Co.
Lowell PS	Lowell HS	Project Scope & Budget	Repair	Knight, Bagge, & Anderson, Inc.	ICON architecture, inc.			
Lowell PS	Moody ES	Project Scope & Budget	Repair	Knight, Bagge, & Anderson, Inc.	ICON architecture, inc.			
Lowell PS	Peter W Reilly ES	Project Scope & Budget	Repair	Knight, Bagge, & Anderson, Inc.	ICON architecture, inc.			
Lowell PS	Washington ES	Project Scope & Budget	Repair	Knight, Bagge, & Anderson, Inc.	ICON architecture, inc.			
Lunenburg PS	Lunenburg HS	Local Clearance - 09/10						
Lynn PS	Thurgood Marshall MS	Local Clearance - 09/10						
Lynnfield PS	Lynnfield HS	Designer Selection						

Master District Status List

Yellow = Wait List Project

Green = Green Repair

Red = Changes in last 60 days

District Name	School Name	Status	Preferred Schematic	OPM	Designer	Cx Authority	Procurement Status	CM/GC
Malden PS	Malden HS	Construction	Renovation	URS Corporation	Flansburgh Associates, Inc.		CMR - CM Selected	Gilbane Building Company
Manchester Essex Regional PSM	Manchester JHS / SHS	Closeout/Audit		Design Technique	Mount Vernon Group Architects, Inc.		DBB - Contract Awarded	TLT Construction
Marblehead PS	Village IS	Building Completion 2011	Repair	Municipal Building Consultants, Inc.	Symmes Maini & McKee Associates, Inc.	RDK Engineering	DBB - Contract Awarded	Groom Construction
Marblehead PS	Glover Primary	Design Development	New Construction	Municipal Building Consultants, Inc.	JCJ Architecture, PC		DBB - In Design	
Marlborough PS	Marlborough HS	Project Scope & Budget	Repair	RF Walsh Collaborative Partners	Baker/Wohl Architects, Inc.			
Marlborough PS	Francis J Kane Primary	Project Scope & Budget	Repair	RF Walsh Collaborative Partners	Baker/Wohl Architects, Inc.			
Marshfield PS	Marshfield HS	Preferred Schematic			Ai3 Architects LLC			
Marshfield PS	Gov Edward Winslow ES	Construction	Repair	Vertex Construction Services, Inc.	Knight, Bagge & Anderson, Inc.	RDK Engineering	DBB - Contract Awarded	Enterprise Equipment Co., Inc.
Maynard PS	Maynard HS	Construction	New Construction	Municipal Building Consultants, Inc.	Tappe Associates, Inc.	WSP Flack + Kurtz	DBB - Contract Awarded	CTA Construction
Medway PS	Medway MS	Design Development		Compass Project Management, Inc.	Knight, Bagge & Anderson, Inc.	Sebesta Blomberg & Associates	CMR - CM Selected	Consigli Construction Co.
Melrose PS	Melrose HS	Design Development	Repair	Municipal Building Consultants, Inc.	Gale Associates, Inc.	Russo Barr Associates, Inc.		
Mendon-Upton PS	Miscoe Hill IS	Design Development	Repair	Maguire Group	Habeeb & Associates Architects, Inc.			
Methuen PS	Methuen HS	Construction	Addition/Renovation	KBA/Trident	Finegold Alexander and Associates Inc.	Environmental Health and Engineering	CMR - CM Selected	Dimeo Construction
Middleborough PS	Mary K. Goode ES	Design Development	Repair	Maguire Group	Habeeb & Associates Architects, Inc.	Russo Barr Associates, Inc.		
Middleton PS	Howe-Manning IS	Construction	New Construction	RF Walsh Collaborative Partners	DiNisco Design Partnership, Limited	Foreman Building Commissioning, LP	DBB - Contract Awarded	CTA Construction Co.
Minuteman Voc Tech PS	Minuteman Reg HS	Local Clearance - 09/10						
Mohawk Trail PS	Mohawk Trail Reg HS	Approved Project Vote Pending	Repair	Potomac Capital Advisors	Bradley Architects, Inc.	Strategic Building Solutions		
Mohawk Trail PS	Colrain Central ES	Approved Project Vote Pending	Repair	Potomac Capital Advisors	Bradley Architects, Inc.	Strategic Building Solutions		
Mohawk Trail PS	Buckland-Shelburne Reg ES	Approved Project Vote Pending	Repair	Potomac Capital Advisors	Bradley Architects, Inc.	Strategic Building Solutions		
Mount Greylock PS	Mt Greylock Reg HS	Closeout/Audit	Repair	N/A	Hesnor Engineering & Barry Architects	Horizon Engineering Associates, LLP	DBB - Contract Awarded	Adams Plumbing & Heating
Narragansett PS	Narragansett MS	Design Development	Repair	Potomac Capital Advisors	DiMarinisi & Wolfe Architects Urban	RFS Engineering		
Narragansett PS	Phillipston Memorial ES	Design Development	Repair	Potomac Capital Advisors	DiMarinisi & Wolfe Architects Urban	RFS Engineering		
Narragansett PS	Templeton Center	Feasibility Study (on hold)		Strategic Building Solutions, LLC	Symmes Maini & McKee Associates, Inc.		Undetermined	
Nashoba PS	Pompositicut Primary	Construction	Addition/Renovation	Construction Monitoring Services, Inc.	Symmes Maini & McKee Associates, Inc.	Strategic Building Solutions	DBB - Contract Awarded	Stella P.J. Construction Corp.
Nashoba Valley Tech PS	Nashoba Valley Tech HS	Design Development	Repair					
Natick PS	Johnson ES	Feasibility Study	Repair	Municipal Building Consultants, Inc.	Knight, Bagge & Anderson, Inc.			

Master District Status List

Yellow = Wait List Project

Green = Green Repair

Red = Changes in last 60 days

District Name	School Name	Status	Preferred Schematic	OPM	Designer	Cx Authority	Procurement Status	CM/GC
Natick PS	Natick HS	Construction	Model School	RF Walsh Collaborative Partners	Ai3 Architects LLC	RFS Engineering	DBB - Contract Awarded	Brait Builders Corporation
Nauset PS	Nauset Reg HS	Approved Project Vote Pending	Repair	NETCO Construction Project Managers, Inc.	Habeeb & Associates Architects, Inc.	CBI Consulting Inc.		
Needham PS	Newman ES	Construction	Repair	Town of Needham	Drumme Rosane Anderson, Inc.	RFS Engineering	CMR - CM Selected	Consigli Construction Co.
Needham PS	Pollard MS	Construction	Repair	STV Construction, Inc.	Gale Associates, Inc. Gale Associates, Inc.	CBI Consulting Inc.		
New Bedford PS	New Bedford HS	OPM Selection						
New Bedford PS	Abraham Lincoln	Building Completion 2011	New Construction	Daedalus Projects Inc	Mount Vernon Group Architects, Inc.	Sebesta Blomberg & Associates	DBB - Contract Awarded	CTA Construction Co.
New Bedford PS	John Hannigan ES	OPM Selection						
New Salem-Wendell PS	Swift River ES	Design Development	Repair	Maguire Group	Bradley Architects, Inc.			
Newburyport PS	Francis T Bresnahan ES	Designer Selection						
Newburyport PS	Rupert A Nock MS	Designer Selection						
Newton PS	Bowen ES	Design Development	Repair	STV Construction, Inc.	Habeeb & Associates Architects, Inc.			
Newton PS	Williams ES	Design Development	Repair	STV Construction, Inc.	Habeeb & Associates Architects, Inc.			
Newton PS	Newton North HS	Closeout/Audit	New Construction	Turner Construction Company	Dore & Whittier Architects, Inc.		CMR - CM Selected	Dimeo Construction
Norfolk County Agr PS	Norfolk County Agr HS	Design Development	Addition/Renovation	Compass Project Management, Inc	Turowski2 Architecture, Inc.	RFS Engineering	DBB - In Design	
Norfolk PS	Freeman-Centennial IS	Construction	New Construction	Joslin, Lesser & Associates, Inc.	Flansburgh Associates, Inc.	WSP Flack + Kurtz	DBB - In Design	Fontaine Bros., Inc.
North Adams PS	Silvio O Conte MS	Feasibility Study		Strategic Building Solutions, LLC	Margo Jones Architects, Inc.			
North Andover PS	Atkinson ES	Project Scope & Budget	Repair	Municipal Building Consultants, Inc.	ICON architecture, inc.			
North Andover PS	North Andover MS	Project Scope & Budget	Repair	Municipal Building Consultants, Inc.	ICON architecture, inc.			
North Andover PS	Annie L Sargent ES	Project Scope & Budget	Repair	Municipal Building Consultants, Inc.	ICON architecture, inc.			
North Attleborough PS	Falls ES	Construction	Repair	Atlantic Construction & Management, Inc.	CSS Architects Incorporated	Gale Associates, Inc.		
North Brookfield PS	North Brookfield ES	Design Development	Repair	Vertex Construction Services, Inc.	LPBA/ Architects, Inc.	Simpson Gumpertz & Heger		
North Middlesex PS	Ashby ES	Construction	Repair	Compass Project Management, Inc.	Russo Barr Associates, Inc.	VP Consultants, LLC		
North Middlesex PS	Spaulding Memorial Primary	Construction	Repair	Compass Project Management	Russo Barr Associates, Inc.	VP Consultants, LLC		
North Reading PS	North Reading HS	Feasibility Study		PMA Consultants	Dore & Whittier Architects, Inc.			
Northampton-Smith PS	Smith Vocational and Agricultural HS	Local Clearance - 09/10						
Northborough PS	Robert E. Melican MS	Design Development	Repair	Pinck & Co., Inc.	ICON architecture, inc.	Strategic Building Solutions		

Master District Status List

Yellow = Wait List Project

Green = Green Repair

Red = Changes in last 60 days

District Name	School Name	Status	Preferred Schematic	OPM	Designer	Cx Authority	Procurement Status	CM/GC
Northeast Metro Voc PS	Northeast Metro Reg Voc HS	Local Clearance - 09/10						
Norton PS	Norton HS	Design Development		Pinck & Co., Inc.	JCJ Architecture, PC	RFS Engineering	CMR - IG Application Pending	
Norwood PS	Norwood HS	Construction	Model School	Compass Project Management, Inc.	Ai3 Architects LLC		DBB - Contract Awarded	Agostini Construction Company, Inc.
Old Colony Reg Voc Tech PS	Old Colony Regional Voc / Tech HS	OPM Selection						
Orange PS	Butterfield MS	Closeout/Audit	Repair		Tighe & Bond, Inc.		Undetermined	SOM Construction, Inc.
Orange PS	Dexter Park IS	Local Clearance - 09/10						
Oxford PS	Oxford MS	Local Clearance - 09/10	Repair					
Palmer PS	Converse MS	Construction	Repair	Diversified Project Management	Tighe & Bond, Inc.	Strategic Building Solutions		
Palmer PS	Old Mill Pond ES	Construction	Repair	Diversified Project Management	Tighe & Bond, Inc.	Strategic Building Solutions		
Palmer PS	Palmer HS	Construction	Repair	Diversified Project Management	Tighe & Bond, Inc.	Strategic Building Solutions		
Peabody PS	J Henry Higgins MS	Feasibility Study	Repair	Daedalus Projects Inc	DiNisco Design Partnership, Limited			
Peabody PS	John E Burke ES	Approved Project Vote Pending	Repair	Daedalus Projects Inc	LPBA/ Architects, Inc.			
Peabody PS	William A Welch Sr ES	Approved Project Vote Pending	Repair	Daedalus Projects Inc	LPBA/ Architects, Inc.			
Pentucket PS	Dr Frederick N Sweetsir Primary	Building Completion 2012	Repair	PMA Consultants	Knight, Bagge & Anderson, Inc.	CBI Consulting Inc.		
Pentucket PS	Dr John C Page ES	Building Completion 2012	Repair	PMA Consultants	Knight, Bagge & Anderson, Inc.	RDK Engineering		
Pentucket PS	Elmer S Bagnall ES	Building Completion 2012	Repair	PMA Consultants	Knight, Bagge & Anderson, Inc.	CBI Consulting Inc.		
Pentucket PS	Helen R Donaghue IS	Building Completion 2012	Repair	PMA Consultants	Knight, Bagge & Anderson, Inc.	CBI Consulting Inc.		
Pioneer Valley PS	Pioneer Valley Reg MS / HS	Project Scope & Budget	Repair	Diversified Project Management	CGKV Architects, Inc.			
Pioneer Valley PS	Bernardston ES	Feasibility Study	Repair	Diversified Project Management	CGKV Architects, Inc.			
Pioneer Valley PS	Northfield ES	Project Scope & Budget	Repair	Diversified Project Management	CGKV Architects, Inc.			
Pittsfield PS	Taconic HS	Feasibility Study		Skanska USA Building, Inc.				
Plymouth PS	Plymouth Community IS	Construction	Repair		Knight, Bagge & Anderson, Inc.	VP Consultants, LLC		
Plymouth PS	Plymouth North HS	Construction	Model School	Ted Gentry Associates	Ai3 Architects LLC	Sebesta Blomberg & Associates	DBB - Contract Awarded	J&J Contractors Inc.
Plymouth PS	West ES	Closeout/Audit	Repair					
Quabbin PS	Oakham Center ES	Closeout/Audit	Repair		Russo Barr Associates, Inc.	VP Consultants, LLC	DBB - Contract Awarded	Cape Way Roofing
Quabbin PS	Quabbin Reg HS	Construction	Repair	Vertex Construction Services, Inc.	LPBA/ Architects, Inc.	VP Consultants, LLC		

Master District Status List

Yellow = Wait List Project

Green = Green Repair

Red = Changes in last 60 days

District Name	School Name	Status	Preferred Schematic	OPM	Designer	Cx Authority	Procurement Status	CM/GC
Quincy PS	Central MS	Design Development	New Construction	Tishman Construction Corporation of MA	Ai3 Architects LLC	Sebesta Blomberg & Associates	DBB - In Design	
Reading PS	Birch Meadow ES	Construction	Repair	Knight, Bagge, & Anderson, Inc.	LPBA/ Architects, Inc.	Russo Barr Associates, Inc.		
Reading PS	J Warren Killam ES	Closeout/Audit	Repair	Knight, Bagge, & Anderson, Inc.	LPBA/ Architects, Inc.	Russo Barr Associates, Inc.		
Revere PS	William McKinley ES	Local Clearance - 09/10						
Revere PS	Paul Revere ES	Building Completion 2011	New Construction	RF Walsh Collaborative Partners	Drumme Rosane Anderson, Inc.		DBB - Contract Awarded	Delulis Brothers Construction Company
Rochester PS	Rochester Memorial ES	Construction	Addition/Renovation	PMA Consultants	Flansburgh Associates, Inc.	Horizon Engineering Associates, LLP	CMR - CM Selected	Gilbane Building Company
Rockland PS	John W Rogers MS	Construction	Addition/Renovation	Daedalus Projects Inc	Dore & Whittier Architects, Inc.	Consulting Engineering Services, LLC	CMR - CM Selected	Agostini Construction Company, Inc.
Rockland PS	R Stewart Esten ES	Design Development	Repair	Daedalus Projects Inc	Habeeb & Associates Architects, Inc.	Russo Barr Associates, Inc.		
Rockport PS	Rockport ES	Closeout/Audit	Repair	N/A	Russo Barr Associates, Inc.			
Rockport PS	Rockport HS	Closeout/Audit	Repair		Russo Barr Associates, Inc.	VP Consultants, LLC	DBB - Contract Awarded	Feeley, McAnespie, Inc.
Salem PS	Saltonstall ES	Design Development	Repair	KV Associates, Inc.	Reinhardt Associates, Inc.	RFS Engineering		
Salem PS	Collins MS	Design Development	Repair	KV Associates, Inc.	Reinhardt Associates, Inc.	RFS Engineering		
Sandwich PS	Oak Ridge K-8	Design Development	Repair	NETCO Construction Project Managers, Inc.	Habeeb & Associates Architects, Inc.	Gale Associates, Inc.		
Sandwich PS	Forestdale K-8	Design Development	Repair	NETCO Construction Project Managers, Inc.	Habeeb & Associates Architects, Inc.	Gale Associates, Inc.		
Saugus PS	Belmonte Saugus MS	Project Scope & Budget	Repair	Skanska USA Building, Inc.	Fletcher Thompson Architecture Engineering,			
Scituate PS	Wampanoag ES	Closeout/Audit	Repair	Bargmann, Hendrie + Archetype, Inc.	Knight, Bagge & Anderson, Inc.	RFS Engineering		
Sharon PS	Sharon HS	Building Completion 2011	Repair	Daedalus Projects Inc	Baker/Wohl Architects, Inc.	Cannon Design	Undetermined	Titan Roofing, Inc.
Sharon PS	Sharon MS	Construction	Addition/Renovation	Daedalus Projects, Inc.	Kaestle Boos Associates, Inc.	Horizon Engineering Associates, LLP	CMR - CM Selected	Consigli Construction Co.
Shawsheen Valley Voc PS	Shawsheen Valley Voc / Tech HS	Construction		Construction Monitoring Services Inc.	Knight, Bagge & Anderson, Inc.		DBB - Contract Awarded	Colantino Inc.
Shrewsbury PS	Sherwood MS	Construction	New Construction	PMA Consultants	Lamoureux Pagano & Associates, Inc.	RDK Engineering	CMR - CM Selected	Gilbane Building Company
Shrewsbury PS	Spring Street ES	Construction	Repair	PMA Consultants	Habeeb & Associates Architects, Inc.	Cannon Design		
Somerset PS	Somerset HS	Preferred Schematic			Skanska USA Building, Inc.			
Somerville PS	E Somerville Community K-8	Design Development	Renovation	City of Somerville	Maguire Group Inc.	Foreman Building Commissioning, LP	CMR - CM Selected	Gilbane Building Company
South Hadley PS	Plains ES	Designer Selection			Arcadis			
South Shore Reg Voc PS	South Shore Voc / Tech HS	Construction	Repair	Vertex Construction Services, Inc.	Gale Associates, Inc.	VP Consultants, LLC		
Southbridge PS	Southbridge HS	Construction	New Construction	Joslin, Lesser & Associates, Inc.	Tappe Associates, Inc.	Environmental Health and Engineering	CMR - CM Selected	Consigli Construction Co.

Master District Status List

Yellow = Wait List Project

Green = Green Repair

Red = Changes in last 60 days

District Name	School Name	Status	Preferred Schematic	OPM	Designer	Cx Authority	Procurement Status	CM/GC
Southeastern Reg Voc Tech PS	Southeastern Regional Voc / Tech HS	Design Development	Addition/Renovation	RF Walsh Collaborative Partners	Drumme Rosane Anderson, Inc.	RDK Engineering	CMR - CM Selected	WT Rich Company Inc.
Southern Worcester Cty VT PS	Bay Path Regional Voc / Tech HS	Preferred Schematic		Heery International, Inc	Kaestle Boos Associates, Inc.			
Southwick-Tolland	Woodland ES	Feasibility Study		Strategic Building Solutions, LLC	JCJ Architecture, PC			
Spencer-E Brookfield PS	David Prouty HS	OPM Selection						
Springfield PS	Forest Park Middle School	Design Development	Addition/Renovation	ARCADIS-U.S., Inc.	Perkins Eastman	Foreman Building Commissioning, LP		
Springfield PS	Putnam Voc / Tech HS	Construction	New Construction	ARCADIS	Drumme Rosane Anderson, Inc.	Strategic Building Solutions	CMR - CM Selected	Consigli Construction Co.
Springfield PS	SCI PP Years 2 & 3	Construction	Repair		CGKV Architects, Inc./Gale Associates, Inc.	VP Consultants, LLC		
Stoneham PS	Stoneham MS	Preferred Schematic		Joslin, Lesser & Associates	Tappe Associates, Inc.			
Sturbridge PS	Burgess ES	Construction	Addition/Renovation	Lamoureux Pagano & Associates, Inc.	Drumme Rosane Anderson, Inc.	Horizon Engineering Associates, LLP	DBB - Contract Awarded	Fontaine Bros.
Sudbury PS	Peter Noyes ES	Construction	Repair	Compass Project Management, Inc.	Russo Barr Associates, Inc./BLW Engineers, Inc.	RDK Engineering		
Sutton PS	Sutton MS	Construction	Addition/Renovation	Strategic Building Solutions	Flansburgh Associates, Inc.	RDK Engineering	DBB - Contract Awarded	TLT Construction Corp.
Tantasqua PS	Tantasqua Reg JHS	Design Development	Repair	Diversified Project Management	Habeeb & Associates Architects, Inc.	Cannon Design		
Taunton PS	Taunton HS	Construction	Addition/Renovation	Gilbane	Design Partnership of Cambridge, Inc.		DBB - Contract Awarded	Bacon-Agostini Construction Joint Venture
Tewksbury PS	Tewksbury Memorial HS	Construction	Model School	Heery International, Inc	Symmes Maini & McKee Associates, Inc.	Sebesta Blomberg & Associates	DBB - Contract Awarded	CTA Ventures/ Methuen
Tri County PS	Tri County Regional Voc / Tech HS	Construction	Repair	Knight, Bagge, & Anderson, Inc.	Richard D. Kimball Company, Inc.	WSP Flack + Kurtz		
Upper Cape Cod Voc Tech PS	Upper Cape Cod Voc / Tech HS	Construction	Repair	NETCO Construction Project Managers, Inc.	Knight, Bagge & Anderson, Inc.	Gale Associates, Inc.		
Uxbridge PS	Uxbridge HS	Construction	New Construction	Joslin, Lesser & Associates, Inc.	Raymond Design Associates, Inc.	Turner Facilities Management Solutions	CMR - CM Selected	Shawmut Design and Construction
Wachusett PS	Mountview MS	OPM Selection		Town Employee				
Wachusett PS	Naquag ES	Design Development	Repair	Strategic Building Solutions, LLC	LPBA/ Architects, Inc.	RFS Engineering		
Wachusett PS	Paxton K-8 Center	Design Development	Repair	Strategic Building Solutions, LLC	LPBA/ Architects, Inc.	RFS Engineering		
Wachusett PS	Thomas Prince K-8	Design Development	Repair	Strategic Building Solutions, LLC	LPBA/ Architects, Inc.	RFS Engineering		
Wakefield PS	Wakefield Memorial HS	Closeout/Audit	Addition/Renovation					
Wakefield PS	Galvin MS	Feasibility Study			Tappe Associates, Inc.			
Wayland PS	Wayland HS	Construction	New Construction	KV Associates	HMFH Architects, Inc.	WSP Flack + Kurtz	CMR - CM Selected	Shawmut Construction
Webster PS	Park Avenue ES	Feasibility Study		RF Walsh Collaborative Partners	Dore & Whittier Architects, Inc.			
Wellesley PS	Wellesley SHS	Construction	New Construction	Ryegate Inc	Symmes Maini & McKee Associates, Inc.	RFS Engineering	CMR - CM Selected	Turner Construction

Master District Status List

Yellow = Wait List Project

Green = Green Repair

Red = Changes in last 60 days

District Name	School Name	Status	Preferred Schematic	OPM	Designer	Cx Authority	Procurement Status	CM/GC
West Boylston PS	Major Edwards ES	Approved Project Vote Pending	Repair	URS Corporation	Reinhardt Associates, Inc.	Cannon Design		
West Boylston PS	West Boylston JHS / SHS	Feasibility Study	Repair	URS Corporation	Reinhardt Associates, Inc.			
West Bridgewater PS	West Bridgewater JHS / SHS	Feasibility Study		Strategic Building Solutions, LLC	Flansburgh Associates, Inc.			
West Springfield PS	West Springfield HS	Design Development	Model School	Strategic Building Solutions, LLC	Symmes Maini & McKee Associates, Inc.	Turner Facilities Management Solutions	DBB - Out to Bid	
Westborough PS	Sarah W Gibbons MS	Local Clearance - 09/10						
Westfield PS	Highland School	Building Completion 2011	Repair	P3 Project Planning Professionals	Tighe & Bond, Inc.	Strategic Building Solutions		
Westfield PS	Southampton Road ES	Design Development	Repair	P3 Project Planning Professionals	Tighe & Bond, Inc.	Strategic Building Solutions	Undetermined	R&H Roofing
Westfield PS	Westfield Voc / Tech HS	Design Development	Repair	P3 Project Planning Professionals	Tighe & Bond, Inc.	Strategic Building Solutions		
Westfield PS	Westfield HS	Design Development	Repair	P3 Project Planning Professionals	Tighe & Bond, Inc.	Strategic Building Solutions		
Westfield PS	Paper Mill ES	Design Development	Repair	P3 Project Planning Professionals	Tighe & Bond, Inc.	Strategic Building Solutions		
Westfield PS	Abner Gibbs ES	Project Scope & Budget	Model School	Skanska USA Building Inc.	Margo Jones Architects, Inc.			
Westfield PS	Highland School	Design Development	Repair	P3 Project Planning Professionals	Tighe & Bond, Inc.	Strategic Building Solutions	Undetermined	Allied Restoration
Westfield PS	Southampton Road ES	Building Completion 2011	Repair	P3 Project Planning Professionals	Tighe & Bond, Inc.	Strategic Building Solutions		
Weston PS	Field ES School	Project Scope & Budget		Compass Project Management, Inc.	Jonathan Levi Architects LLC			
Weston PS	Weston HS	Design Development	Repair	Compass Project Management, Inc.	Garcia Galuska DeSousa	RDK Engineering		
Weston PS	Weston MS	Construction	Repair	Compass Project Management, Inc.	Russo Barr Associates, Inc.	RDK Engineering		
Westport PS	Alice A Macomber ECC	Design Development	Repair	Pinck & Co., Inc.	CGKV Architects, Inc.	CBI Consulting Inc.		
Westport PS	Westport HS	Design Development	Repair	Pinck & Co., Inc.	CGKV Architects, Inc.	CBI Consulting Inc.		
Westport PS	Westport MS	Feasibility Study	Repair	Pinck & Co., Inc.	CGKV Architects, Inc.			
Weymouth PS	Abigail Adams MS	Construction	Repair	Knight, Bagge, & Anderson, Inc.	Gale Associates, Inc.	Cannon Design		
Whitman-Hanson PS	John H Duval ES	Closeout/Audit	Repair		BETA Group, Inc.		Undetermined	S.I. Services, Inc.
Whitman-Hanson PS	Maquan ES	OPM Selection						
Williamsburg PS	Anne T Dunphy IS	Preferred Schematic		Arcadis	Drumme Rosane Anderson, Inc.			
Wilmington PS	Wilmington HS	Preferred Schematic		Joslin, Lesser & Associates	Dore & Whittier Architects, Inc.			
Wilmington PS	Shawsheen ES	Design Development	Repair	P3 Project Planning Professionals	Russo Barr Associates, Inc.	CBI Consulting Inc.		
Winchendon PS	Toy Town ES	Closeout/Audit	Repair	NETCO Construction Project Managers, Inc.	Hesnor Engineering Company	RFS Engineering		

Master District Status List

Yellow = Wait List Project

Green = Green Repair

Red = Changes in last 60 days

District Name	School Name	Status	Preferred Schematic	OPM	Designer	Cx Authority	Procurement Status	CM/GC
Winchester PS	Winchester HS	OPM Selection						
Winchester PS	Vinson-Owen ES	Design Development	New Construction	Town of Winchester	Tappe Associates, Inc.	Turner Facilities Management Solutions	DBB - In Design	
Winchester PS	Lynch ES	Closeout/Audit	Repair	Knight, Bagge, & Anderson, Inc.	Gale Associates, Inc.	Simpson Gumpertz & Heger		
Winthrop PS	Winthrop Senior High	Designer Selection		Skanska USA Building, Inc.				
Woburn PS	John F Kennedy MS	Construction	Repair	Municipal Building Consultants, Inc.	Gale Associates, Inc.	Simpson Gumpertz & Heger		
Woburn PS	Goodyear ES	Construction	New Construction	Municipal Building Consultants, Inc.	Tappe Associates, Inc.	Strategic Building Solutions	CMR - CM Selected	Gilbane Building Company
Woburn PS	Daniel L Joyce MS	Closeout/Audit	Repair	Municipal Building Consultants, Inc.	Gale Associates, Inc.	Simpson Gumpertz & Heger		
Worcester PS	North HS	Construction		Maguire Group Inc	City of Worcester		CMR - CM Selected	Gilbane Building Company

No. of Projects: 317

Project Status | September 14, 2011


New Program: 123

Waitlist: 9

Green Repair: 146

Closeout / Audit Complete: 39

Total Projects: 317

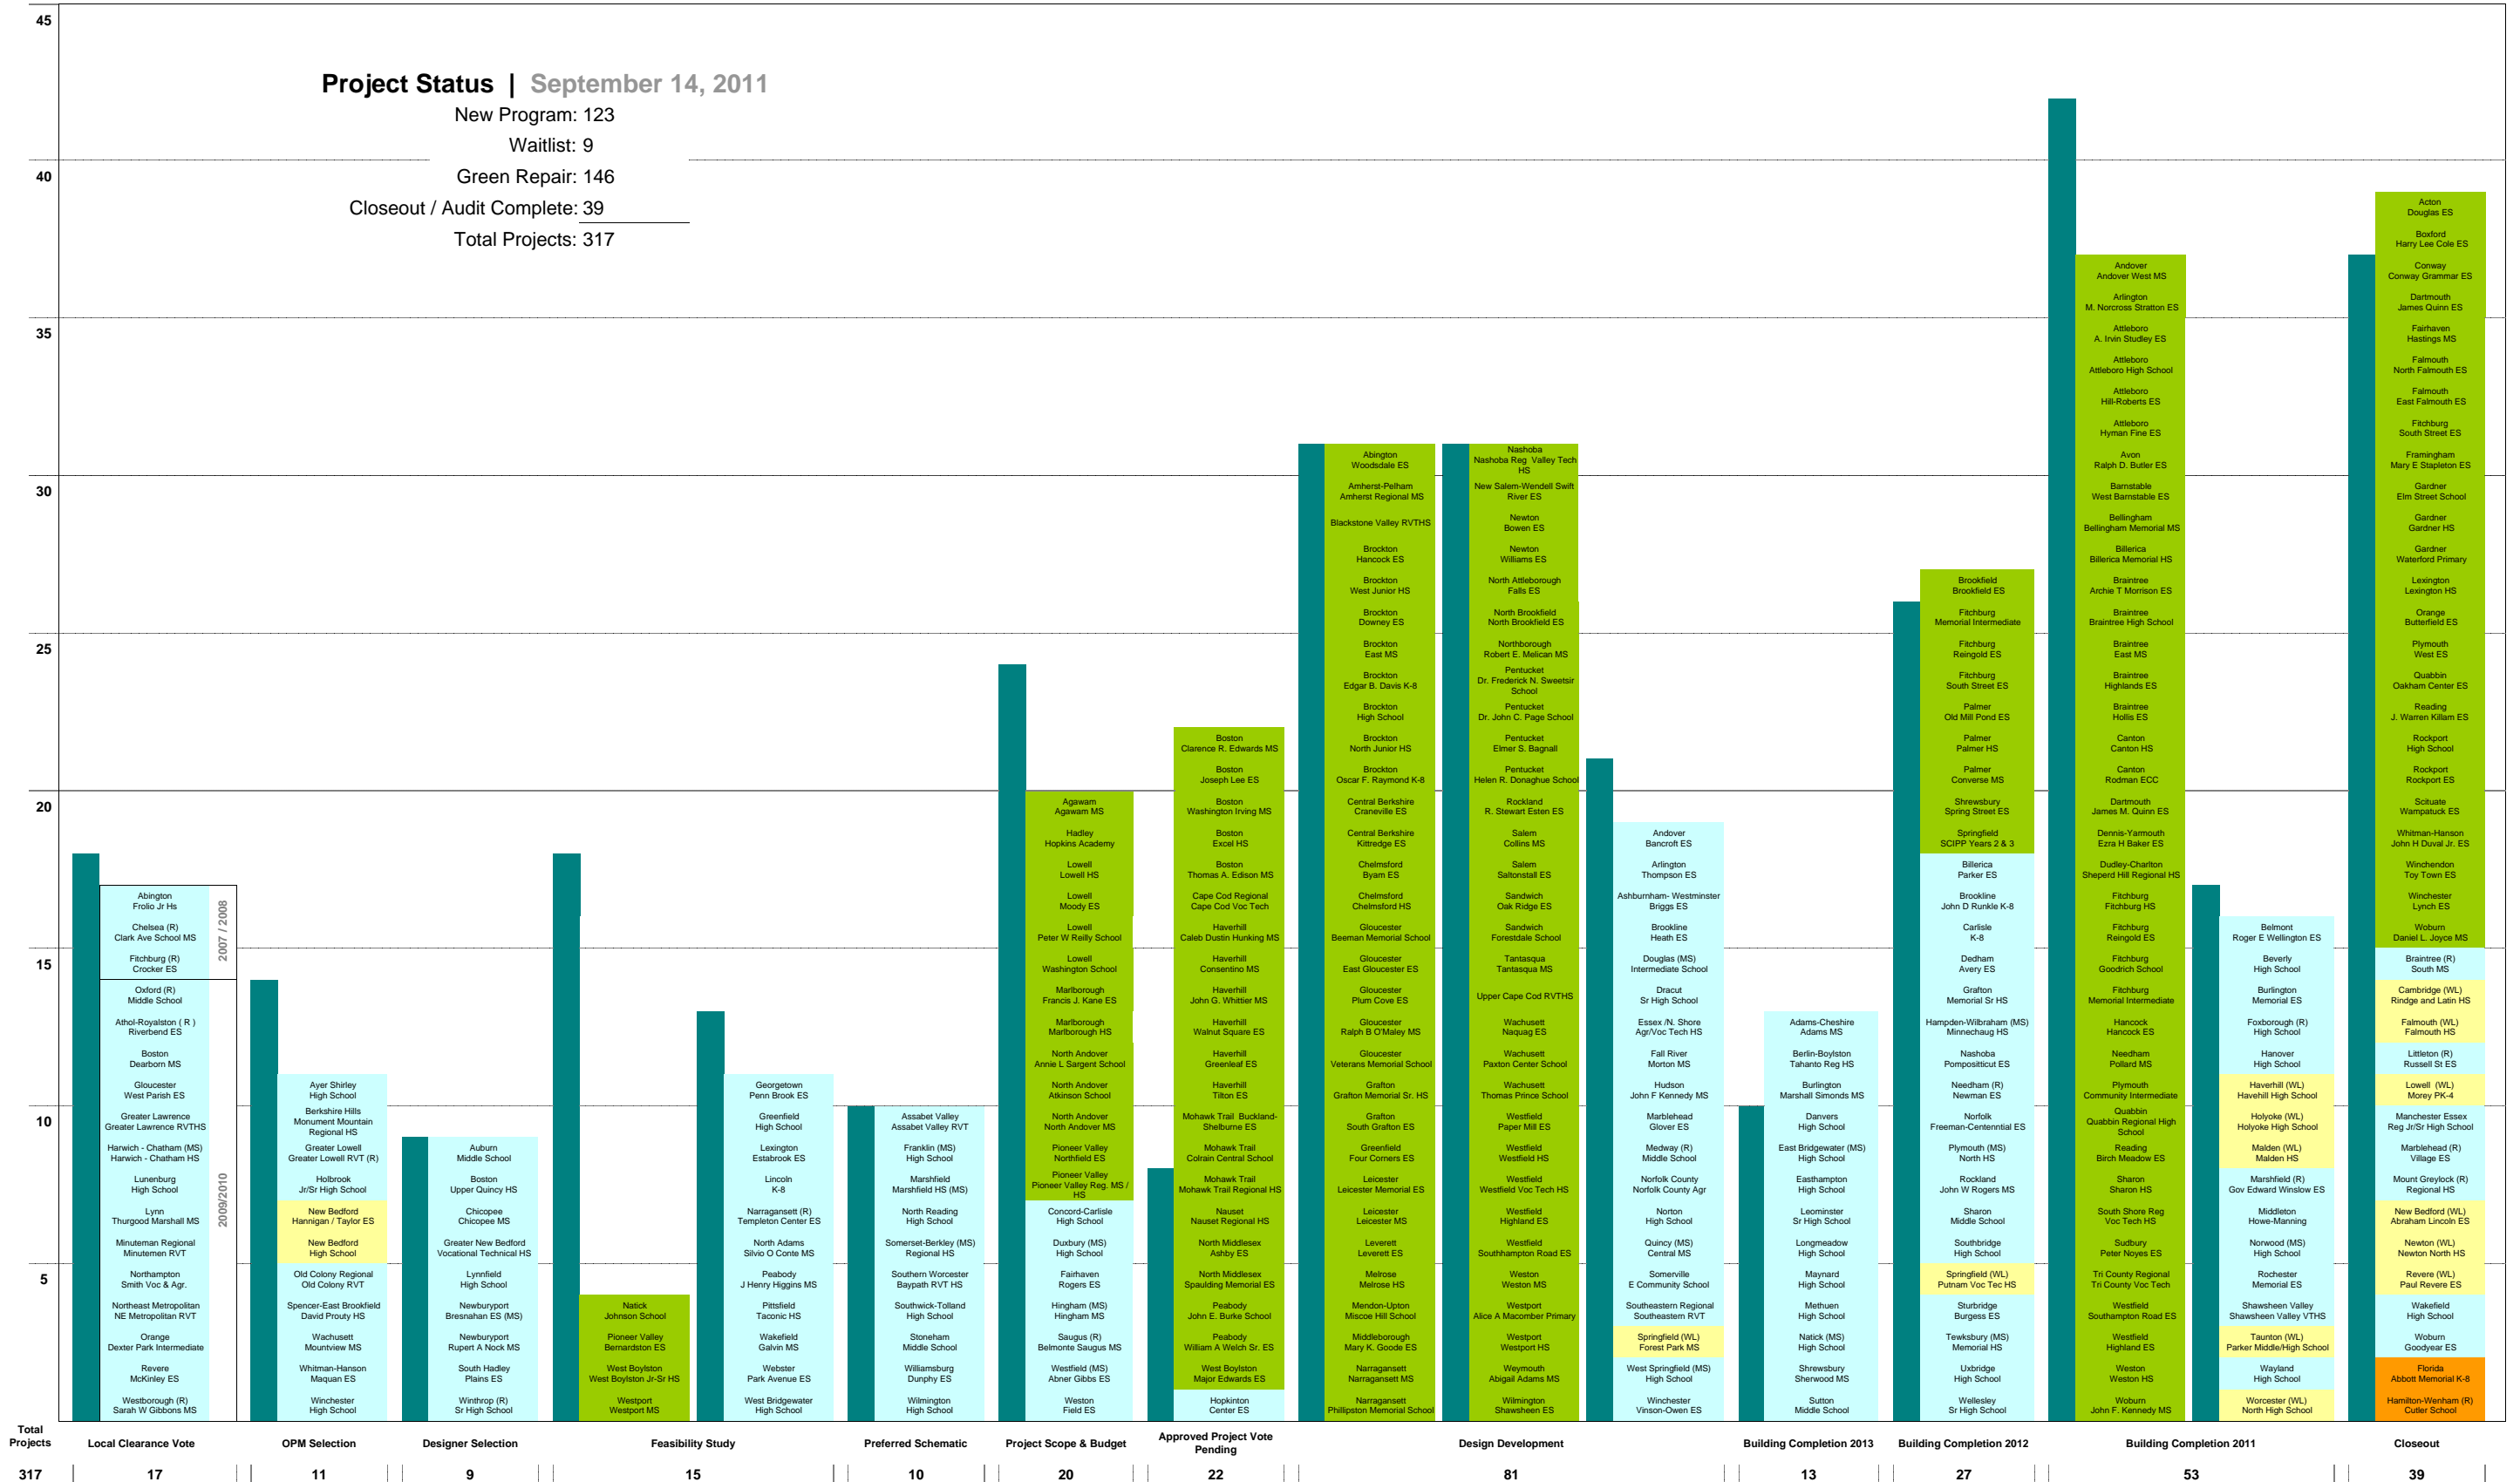

PROJECT STATUS

- Waitlist Projects
- Green Repair Projects
- Project Complete
- New Program Projects
- Capital Pipeline Status Presented at July 27, 2011 Board of Directors Meeting

2011 Estimated Bid Dates

Note bid dates are **Estimates ONLY**. Please contact Districts for exact information.

Total Project Budget denotes total District costs and does not denote the basis of the MSBA Total Facilities Grant.

- Denotes bid phase in progress or complete

- Denotes estimated bid dates

DISTRICT <small>*Projects Considering the CM @ Risk Method</small>	DESIGN BASIS FOR ENROLLMENT	PROJECT BUDGET <small>Shown in Millions</small>	CONSTRUCTION BUDGET <small>Shown in Millions</small>	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC
*SOUTHBRIDGE	1050	\$76.5	60.1	Southbridge HS New Construction: Filed-Sub Bids rcv'd 1/7. GMP Issued 2/7.											
*SHREWSBURY	900	\$47.3	\$37.0	Sherwood MS New Construction: Filed-Sub Bids rcv'd 2/7. GMP Issued 5/10.											
SO. SHORE RVT	595	\$3.2	\$2.6	Regional VTHS Repair: Filed-Sub Bids rcv'd 1/7. G.C. Bids rcv'd 1/18. NTP issued 5/9.											
CARLISLE	700	\$20.0	\$15.6	Carlisle ES Addition/Renovation: Filed-Sub Bids rcv'd 1/26. G.C. Bids rcv'd 2/4. NTP Issued 2/9.											
MARSHFIELD	485	\$2.4	\$2.0	Marshfield Edward Winslow ES Repair: Filed-Sub Bids rcv'd 1/14. G.C. Bids rcv'd 1/21. NTP Issued 2/12.											
*UXBRIDGE	600	\$43.0	\$34.4	Uxbridge HS New Construction: Early Site & Steel Package rcv'd 1/13. Filed-Sub Bids rcv'd 3/17. GMP Issued 3/31.											
*BURLINGTON	880	\$32.9	\$24.7	Marshall Simonds MS Addition/Renovation: Filed-Sub Bids rcv'd 3/22. GMP Issued 4/12.											
BERLIN / BOYLSTON	560	\$44.0	\$34.2	Tahanto MS/HS New Construction: Filed-Sub Bids rcv'd 4/7. G.C. Bids rcv'd 4/20. NTP issued 5/10.											
EASTHAMPTON	510	\$43.7	\$33.5	Easthampton HS New Construction: Filed-Sub Bids rcv'd 4/20. G.C. Bids rcv'd 5/6. NTP issued 5/16.											
*LONGMEADOW	1000	\$78.5	\$63.8	Longmeadow HS New Construction: Filed-Sub Bids rcv'd 4/28. GMP issued 5/12.											
SUTTON	840	\$59.9	\$46.4	Sutton MS New Construction: Filed-Sub Bids rcv'd 5/4. G.C. Bids rcv'd 5/18. NTP issued 5/26.											
*LEOMINSTER	1805	\$45.9	\$32.7	Leominster HS Addition/Renovation: Filed-Sub Bids rcv'd 6/2. GMP issued 6/23.											
*SOMERVILLE	500	\$33.2	\$15.2	East Somerville Community School Addition/Renovation: Filed-Sub Bids rcv'd 6/14. GMP Targeted July.											
*ADAMS/CHESHIRE	805	\$40.6	\$30.0	Hoosac Valley MHS Addition/Renovation: Filed-Sub Bids Due 9/26. GMP Targeted October.											
MAYNARD	410	\$45.8	\$35.6	Maynard HS New Construction: Filed-Sub Bids rcv'd 7/13. G.C. Bids rcv'd 7/27. NTP issued 8/18.											
HUDSON	715	\$44.1	\$34.8	JFK MS New Construction: Filed-Sub Bids rcv'd 8/29. G.C. Bids rcv'd 9/14. NTP Targeted September.											
*METHUEN	2075	\$99.1	\$74.9	Methuen HS Addition/Renovation: Filed-Sub Bids Due 9/26. GMP Targeted Oct.											
Subtotal	14,430	\$760.1	\$577.5												

2012 Estimated Bid Dates

Note bid dates are **Estimates ONLY**. Please contact Districts for exact information.

Total Project Budget denotes total District costs and does not denote the basis of the MSBA Total Facilities Grant.

- Denotes bid phase in progress or complete
 - Denotes estimated bid dates

DISTRICT <small>*Projects Considering the CM @ Risk Method</small>	DESIGN BASIS FOR ENROLLMENT	PROJECT BUDGET <small>Shown in Millions</small>	CONSTRUCTION BUDGET <small>Shown in Millions</small>	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC
*ESSEX-NS	1440	\$125.0	\$96.50	Essex Northshore HS New Construction: Early Site Packages Due 2/29. Filed-Sub Bids Due 4/13/12. GMP Targeted June.											
WINCHESTER	420	\$28.7	21.7	Vinson-Owen ES New Construction: Filed-Sub Bids Due 1/5. G.C. Bids Due 1/26. NTP Targeted February.											
DRACUT	1160	\$60.4	\$47.30	Dracut Senior HS Addition/Renovation: Filed-Sub Bids Due 2/1. G.C. Bids Due 2/15. NTP Targeted March											
*NORTON	700	\$34.6	\$27.0	Norton HS Addition/Renovation Filed-Sub Bids Due 2/9. GMP Targeted March.											
MARBLEHEAD	425	\$25.9	\$20.2	Marblehead Glover ES New Construction: Filed-Sub Bids Due 2/29. GMP Targeted March.											
ARLINGTON	380	\$20.7	\$15.7	Arlington Thompson ES New Construction: Filed-Sub Bids Due 3/21. G.C. Bids Due 4/2. NTP Targeted April.											
Subtotal	4,525	\$295.3	\$228.4												
GRAND TOTAL	4,525	\$295	\$228												
Number of Construction-Related Employment				1,142											

District-MSBA	Project Name	Due Date	2011											2012					
			F	M	A	M	J	Jul	A	S	Oct	N	D	J	F	M	A	M	J
Window Projects																			
Wilmington	Shawsheen Elementary School	1/21/11 A	1/21/11	A															
Attleboro	Attleboro High School	2/23/11 A	◆	2/23/11	A														
Arlington	Arlington Norcross Stratton	3/1/11 A	◆	3/1/11	A														
Braintree	Archie T Morrison Elementary	3/10/11 A	◆	3/10/11	A														
Braintree	East Middle School	3/10/11 A	◆	3/10/11	A														
Braintree	Highlands Elementary School	3/10/11 A	◆	3/10/11	A														
Braintree	Hollis Elementary School	3/10/11 A	◆	3/10/11	A														
Springfield PS	Frank H Freedman ES	4/13/11 A		◆	4/13/11	A													
Springfield PS	Warner ES	4/13/11 A		◆	4/13/11	A													
Springfield PS	Washington ES	4/13/11 A		◆	4/13/11	A													
Springfield PS	White Street ES	4/13/11 A		◆	4/13/11	A													
Sudbury	Peter Noyes	4/14/11 A		◆	4/14/11	A													
Fairhaven	Hastings Middle	4/21/11 A		◆	4/21/11	A													
Dudley Charlton Reg	Shepherd Hill Reg High	4/28/11 A		◆	4/28/11	A													
Chelmsford	Chelmsford High	4/29/11 A		◆	4/29/11	A													
Framingham	Mary E Stapleton Elem	5/4/11 A		◆	5/4/11	A													
Tantasqua	Brookfield Elementary	5/18/11 A		◆	5/18/11	A													
Barnstable	West Barnstable Elem	5/20/11 A		◆	5/20/11	A													
Fitchburg	Reingold Elementary (Phase 2)	5/28/11 A		◆	5/28/11	A													
Fitchburg	South Street Elementary (Phase 2)	5/28/11 A		◆	5/28/11	A													
Fitchburg	Memorial Intermediate (Phase 2)	5/28/11 A		◆	5/28/11	A													
Reading	Birch Meadow	6/1/11 A		◆	6/1/11	A													
Dennis Yarmouth	Ezra H Baker Elementary School	6/3/11 A		◆	6/3/11	A													
Leverett	Leverett Elementary	6/7/11 A		◆	6/7/11	A													
Abington	Woodsdale Elementary School	6/8/11 A		◆	6/8/11	A													
Pentucket	Dr Frederick Sweetsir	6/13/11 A		◆	6/13/11	A													
Pentucket	Dr John C Page School	6/13/11 A		◆	6/13/11	A													
Pentucket	Elmer S Bagnall	6/13/11 A		◆	6/13/11	A													
Billerica	Billerica Memorial High School	6/14/11 A		◆	6/14/11	A													
Rockland	R Stewart Esten ES	6/20/11 A		◆	6/20/11	A													
Amherst-Pelham	Amherst Regional MS	7/14/11 A		◆	7/14/11	A													
North Attleboro	Falls	7/27/11 A		◆	7/27/11	A													
Brockton	Brockton High	7/29/11 A		◆	7/29/11	A													
Brockton	Downey	7/29/11 A		◆	7/29/11	A													
North Brookfield	North Brookfield Elem	8/1/11 A		◆	8/1/11	A													
Upper Capecod VT	Upper Cape Cod Voc Tech	8/5/11 A		◆	8/5/11	A													
North Middlesex	Ashby Elementary	8/25/11 A		◆	8/25/11	A													
Sandwich	Forestdale	9/15/11		◆	9/15/11														
Sandwich	Oak Ridge K-8	9/15/11		◆	9/15/11														
Wachusett	Naquag Elementary	9/29/11		◆	9/29/11														
Wachusett	Paxton Center	9/29/11		◆	9/29/11														
Pioneer Valley	Northfield ES	11/1/11		◆	11/1/11														
West Boylston	Major Edwards ES	11/2/11		◆	11/2/11														
West Boylston	West Boylston Jr-Sr HS	11/2/11		◆	11/2/11														
Marlborough	Francis J Kane	11/14/11		◆	11/14/11														
Marlborough	Marlborough High	11/14/11		◆	11/14/11														
Westfield	Westfield Voc Tech HS	11/15/11		◆	11/15/11														
Middleborough	Mary K Goode ES	12/8/11		◆	12/8/11														
Springfield PS	John J Duggan MS	12/10/11		◆	12/10/11														
Mohawk Trail	Colrain Central	1/2/12		◆	1/2/12														
Mohawk Trail	Mohawk Trail Reg High	1/2/12		◆	1/2/12														
North Andover	Atkinson School	1/15/12		◆	1/15/12														

District-MSBA	Project Name	Due Date	2011												2012						
			F	M	A	M	J	Jul	A	S	Oct	N	D	J	F	M	A	M	J		
	Brookfield	Brookfield Elementary	1/30/12														◆	1/30/12			
	Central Berkshire	Kittredge	1/30/12														◆	1/30/12			
	Greenfield	Four Corners	1/30/12														◆	1/30/12			
	Haverhill	Caleb Dustin Hunking	1/30/12														◆	1/30/12			
	Haverhill	Consentino	1/30/12														◆	1/30/12			
	Haverhill	John G Whittier	1/30/12														◆	1/30/12			
	Mendon Upton	Miscoe Hill School	1/30/12														◆	1/30/12			
	Nauset	Nauset Regional High	1/30/12														◆	1/30/12			
	Peabody	John E Burke School	1/30/12														◆	1/30/12			
	Shrewsbury	Spring Street School	1/30/12														◆	1/30/12			
	Wachusett	Thomas Prince	1/30/12														◆	1/30/12			
	Westport	Westport Middle	1/30/12														◆	1/30/12			
	Lowell	Moody ES	1/30/12														◆	1/30/12			
	Lowell	Peter W Reilly School	1/30/12														◆	1/30/12			
	Lowell	Washington School	1/30/12														◆	1/30/12			
	Agawam	Agawam Junior High	2/1/12														◆	2/1/12			
	Salem	Collins MS	2/29/12														◆	2/29/12			
	Salem	Saltonstall Elementary School	2/29/12														◆	2/29/12			

District-MSBA	Project Name	Due Date	2011											2012					
			F	M	A	M	J	Jul	A	S	Oct	N	D	J	F	M	A	M	J
Boiler Projects																			
Fitchburg	Reingold Elementary School (Pha...	1/26/11 A																	
Fitchburg	Memorial Middle School (Phase 1)	1/26/11 A																	
Tri County Regional	Tri County Regional Voc Tech	2/24/11 A																	
Arlington	Arlington Norcross Stratton	3/1/11 A																	
Scituate PS	Wampatuck ES	3/3/11 A																	
Sudbury	Peter Noyes	4/14/11 A																	
Fitchburg	Fitchburg High (Phase 2)	5/17/11 A																	
Leicester	Leicester Memorial Elem	5/18/11 A																	
Newton	Williams	5/20/11 A																	
Bellingham	Bellingham Memorial Middle	6/3/11 A																	
Boston	Clarence R Edwards Middle	6/11/11 A																	
Pentucket	Dr Frederick Sweetsir	6/13/11 A																	
Pentucket	Dr John C Page School	6/13/11 A																	
Pentucket	Elmer S Bagnall	6/13/11 A																	
Weston	Weston High	6/17/11 A																	
Boston	Thomas A Edison Jr High	6/24/11 A																	
New Salem Wendell	Swift River	7/7/11 A																	
Narrangsett	Phillipston Memorial	7/13/11 A																	
Northborough	Robert E. Melican Middle School	7/25/11 A																	
Greenfield	Four Corners	7/27/11 A																	
Brockton	East Junior High	7/29/11 A																	
Brockton	North Junior High	7/29/11 A																	
Peabody	John E Burke School	8/2/11 A																	
Pioneer Valley	Bernardston ES	9/8/11																	
Lowell	Moody ES	9/14/11																	
Haverhill	Consentino	9/17/11																	
Wachusett	Naquag Elementary	9/29/11																	
Lowell	Washington School	10/1/11																	
Cape Cod Regional	Cape Cod Regional Voc Tech	10/15/11																	
Pioneer Valley	Pioneer Valley Regional School	10/25/11																	
Marlborough	Marlborough High	11/6/11																	
Westfield	Highland Elementary School	11/15/11																	
Westfield	Paper Mill ES	11/15/11																	
Westfield	Westfield HS	11/15/11																	
Westfield	Westfield Voc Tech HS	11/15/11																	
Westfield	Southampton Road ES	11/15/11																	
Middleborough	Mary K Goode ES	12/8/11																	
Grafton	South Grafton Elementary	1/30/12																	
Hancock.	Hancock Elementary	1/30/12																	
Mendon Upton	Miscoe Hill School	1/30/12																	
Palmer	Palmer High	1/30/12																	
Palmer	Old Mill Pond	1/30/12																	
Palmer	Converse Middle	1/30/12																	
Wachusett	Thomas Prince	1/30/12																	
Salem	Collins MS	2/29/12																	
Salem	Saltonstall Elementary School	2/29/12																	

District-MSBA	Project Name	Due Date	2011												2012				
			F	M	A	M	J	Jul	A	S	Oct	N	D	J	F	M	A	M	J
Roof Projects																			
Hancock.	Hancock Elementary	2/15/11 A	◆																
Attleboro	A Irvin Studley Elementary School	2/23/11 A	◆																
Attleboro	Hill Roberts Elementary School	2/23/11 A	◆																
Attleboro	Hyman Fine Elementary School	2/23/11 A	◆																
Falmouth	East Falmouth Elem	2/24/11 A	◆																
Falmouth	North Falmouth Elem	2/24/11 A	◆																
Braintree	Braintree High School	3/10/11 A	◆																
Quabbin	Quabbin Regional High School	3/22/11 A	◆																
Andover	Andover West Middle	3/28/11 A	◆																
Sharon	Sharon High School	4/11/11 A	◆																
Sudbury	Peter Noyes	4/14/11 A	◆																
Melrose	Melrose High	4/20/11 A	◆																
Chelmsford	Byam School	4/28/11 A	◆																
Needham	Pollard Middle	5/3/11 A	◆																
Winchester	Lynch Elementary	5/3/11 A	◆																
Lexington	Lexington High	5/4/11 A	◆																
Springfield PS	John F Kennedy MS	5/4/11 A	◆																
Springfield PS	Gerena ES	5/5/11 A	◆																
Canton	Canton High	5/6/11 A	◆																
Canton	Rodman Early Childhood Center	5/6/11 A	◆																
Palmer	Palmer High	5/13/11 A	◆																
Tantasqua	Tantasqua Reg Jr High	5/17/11 A	◆																
Palmer	Old Mill Pond	5/25/11 A	◆																
Westfield	Southampton Road ES	5/26/11 A	◆																
Westfield	Highland ES	5/26/11 A	◆																
Fitchburg	Reingold Elementary (Phase 2)	5/28/11 A	◆																
Fitchburg	Memorial Intermediate (Phase 2)	5/28/11 A	◆																
Orange.	Butterfield	5/31/11 A	◆																
Reading	J Warren Killam	6/1/11 A	◆																
Gardner	Elm Street School	6/2/11 A	◆																
Gardner	Gardner High	6/2/11 A	◆																
Gardner	Waterford Primary School	6/2/11 A	◆																
Dennis Yarmouth	Ezra H Baker Elementary School	6/3/11 A	◆																
Weston	Weston Middle	6/4/11 A	◆																
Leverett	Leverett Elementary	6/7/11 A	◆																
Narrangsett	Narragansett Middle	6/8/11 A	◆																
Springfield PS	Warner ES	6/9/11 A	◆																
Pentucket	Dr John C Page School	6/13/11 A	◆																
Pentucket	Elmer S Bagnall	6/13/11 A	◆																
Pentucket	Helen R Donaghue School	6/13/11 A	◆																
Boston	Washington Irving Middle	6/14/11 A	◆																
Leicester	Leicester Middle	6/15/11 A	◆																
Woburn	John F Kennedy Middle School	6/15/11 A	◆																
Plymouth	Plymouth Commun Intermed	6/16/11 A	◆																
Avon	Ralph D Butler	6/22/11 A	◆																
Woburn	Daniel L Joyce Middle School	6/22/11 A	◆																
Boston	Joseph Lee	6/24/11 A	◆																
Boston	Thomas A Edison Jr High	6/24/11 A	◆																
Weymouth	Abigali Adams Middle School	6/30/11 A	◆																
Shrewsbury	Spring Street School	7/1/11 A	◆																
Gloucester	Beeman Memorial School	7/6/11 A	◆																
Gloucester	East Gloucester Elementary School	7/6/11 A	◆																

**Projects in Construction
MSBA Grant Basis and Maximum Grant Amount**

New Program and Wait List Program Totals			\$1,981,786,871	47,987		9,760,878	*Italicized amounts are estimates. Amounts based on bid results have yet to be determined.										\$1,423,073,806			
District & School	Grade	Contractor	Total Construction Cost	Projected Enroll	PFA or Bid Data	Proposed Square Footage	Construction Cost per Square Foot	Building Cost	Building Cost per Square Foot	Project Type	Construction Start	Estimated Substantial Completion Date	Physical Progress (%)	Change Orders (%)	Construction Status	Approximate Maximum Grant Amount *				
New Program Totals			\$1,577,353,165	36,672		6,911,042	\$229		\$170	Capital Pipeline Projects in Construction										\$1,045,501,577
Berlin-Boylston Tahanto Reg MS/HS	6-12	CTA	\$31,287,000	560	Bid	126,100	\$248	24,629,999	\$195	Design/Bid/Build	10-May-11	31-Dec-12	14%	0.00%	Structural steel activities are in process. Underground MEP within the building footprint has been completed. Concrete slabs were poured in the gym and cafeteria area. Site drainage work is progressing.	\$20,792,722				
Beverly Beverly HS	9-12	CTA	\$67,563,917	1,200	PFA	247,275	\$273	\$51,251,689	\$207	Design/Bid/Build	6-Jan-09	18-Nov-10	97%	1.20%	The main building was completed November 2010. Phase 2, Existing Building Demolition is now completed. Site Work to be completed by December 2011.	\$46,826,551				
Billerica Parker ES	K-5	CTA	\$22,842,500	500	Bid	89,093	\$256	\$17,913,441	\$201	Design/Bid/Build	15-Sep-10	10-May-12	34%	0.00%	Construction of building envelope has commenced. Substantial Date shown is for Phase I building construction. Phase I scheduled completion scheduled May 10, 2012. Phase II is scheduled to be complete on November 26, 2012.	\$15,851,020				
Brookline Runkle ES	PK-8	G&R Construction	\$20,715,300	560	Bid	104,400	\$198	\$17,668,440	\$169	Design/Bid/Build	10-Nov-10	10-Jul-12	20%	1.80%	Addition- Steel nearly complete. Slab placement is ongoing. Existing building- MEP rough-ins continue. Metal stud installation is ongoing. Drywall installation started. Excavation and pipe installation is ongoing for water retention system.	\$11,135,430				
Burlington Memorial ES	K-5	CTA	\$16,389,000	500	Bid	79,185	\$207	\$13,092,323	\$165	Design/Bid/Build	4-Mar-10	15-Jul-11	92%	2.50%	CTA Construction has obtained Substantial Completion for the Project Milestone associated with the completion of the new Memorial School. Final Occupancy Permit signatures have been obtained. Demolition of the old Memorial School is underway.	\$11,019,590				
Carlisle Carlisle K-8	K-8	H.V. Collins Co. Inc	\$15,277,344	700	Bid	140,312	\$109	\$11,342,751	\$81	Design/Bid/Build	9-Feb-11	20-Apr-12	20%	0.15%	Steel is completed. Roofing is underway. Site utilities 65% complete. Light gauge metal framing underway.	\$6,620,942				
Danvers Danvers HS	9-12	Bacon Construction	\$51,098,700	1,000	Bid	246,251	\$208	\$42,760,342	\$174	Design/Bid/Build	Oct-10	1-Jul-13	25%	0.00%	Construction operations include ongoing light gauge metal framing, MEP/FP rough-ins, concrete flatwork, masonry installations and extensive site work. Exterior envelope construction includes precast panel delivery and installation, as well as roofing removal and replacement.	\$37,218,572				
Easthampton Easthampton HS	9-12	Fontaine Brothers	\$30,451,000	510	Bid	110,400	\$276	\$26,159,589	\$237	Design/Bid/Build	16-May-11	25-Oct-13	2%	0.50%	Completing installation of the planned soil consolidation system (Rammed Aggregate Piers) and grouted Uplift columns. Continuing placement of preload settlement fill and monitoring of settlement. Delivery, setup and utility connections of field office trailers complete.	\$23,787,780				
East Bridgewater E. Bridgewater Jr/Sr HS	7-12	Fontaine Brothers	\$61,054,000	950	Bid	213,544	\$286	\$45,219,394	\$212	Design/Bid/Build	10-Aug-11	24-Jun-13	0%	0.00%	Site prep and mobilization is underway.	\$43,317,092				
Foxborough Foxborough HS	9-12	CTA	\$11,469,333	885	Bid	218,500	\$52	\$8,845,000	\$40	Design/Bid/Build	25-Jan-10	30-Sep-11	83%	5.92%	Interior work including painting, door replacement, bathroom renovations as well as re-roofing are finished. Ductwork and piping to be rerouted through auditorium after demo of main lobby revealed inadequate wall and ceiling space.	\$7,226,509				
Hampden-Wilbraham Minnechaug HS	9-12	Fontaine Brothers	\$48,597,500	1,225	Bid	231,467	\$210	\$37,499,962	\$162	Design/Bid/Build	22-Jul-10	28-Jun-12	54%	0.97%	Light gauge metal framing completed in classroom wing. MEP rough-ins well underway. Asphalt binder course has been placed.	\$34,863,838				
Hanover Hanover HS	9-12	Callahan	\$37,306,499	800	Bid	157,000	\$238	\$28,060,313	\$179	Design/Bid/Build	28-Sep-09	1-Jun-11	95%	3.80%	Abatement of the existing HS. Punchlist of the new building.	\$22,263,877				
Maynard Maynard HS	8-12	CTA	\$36,650,000	410	Bid	121,000	\$303	TBD	TBD	Design/Bid/Build	18-Aug-11	6-Dec-13	1%	0.00%	Fencing has been installed. Temporary parking is in place. Site clearing is underway for the preparation of foundation work.	\$28,854,703				
Marshfield Governor Winslow ES	K-5	Enterprise Equipment Co.	\$1,606,479	494	Bid	65,790	\$24	\$1,408,279	\$21	Design/Bid/Build	Apr-11	15-Oct-11	85%	0.10%	Window installation is complete & HAVC work is ongoing as well as commissioning.	\$1,112,880				
Middleton Howe-Manning ES	4-6	CTA	\$18,210,000	553	Bid	83,934	\$217	\$14,529,671	\$173	Design/Bid/Build	06-Apr-10	30-Jul-11	100%	3.10%	Completed new structure at punchlist stage. FF&E and Technology equipment in final installation. Abatement and demolition at old structure complete.	\$12,311,976				
Nashoba Pompositticut ES	K-2	P.J. Stella Construction	\$23,640,900	600	Bid	98,030	\$241	\$18,431,325	\$188	Design/Bid/Build	15-Jun-10	12-Apr-12	47%	1.00%	Commencement of gypsum drywall. On-going MEP/FP rough in, light gauge metal framing, and stair installation. Installation of exterior metal windows, air vapor barrier, brick veneer and the last of the roof construction. Commenced wastewater system component installation as well as wastewater disposal fields.	\$15,042,648				
Natick Natick HS	9-12	Brait Builders Corp.	\$60,270,000	1,300	Bid	254,225	\$237	\$53,213,182	\$209	Design/Bid/Build	13-Sep-10	15-Jun-13	47%	2.20%	Exterior CMU is 85% complete. Windows installation underway. Rough plumbing and electrical are underway. Drywall has begun. Site work continues. Manpower is over 180 everyday.	\$38,209,033				
Norfolk Freeman-Centennial ES	3-6	Fontaine Brothers	\$25,354,966	610	Bid	96,410	\$263	\$20,023,001	\$208	Design/Bid/Build	9-Nov-10	15-Jun-12	21%	0.00%	Steel erection is complete. Exterior masonry wall complete. Concrete slabs for sector 1-3 are complete.	\$15,861,760				
Norwood Norwood HS	9-12	Agostini	\$52,627,980	1,100	Bid	227,374	\$231	\$42,573,646	\$187	Design/Bid/Build	19-May-09	13-May-11	96%	1.10%	New school is occupied and open. Existing HS demolished and in the process of being removed.	\$38,154,487				
Plymouth Plymouth HS	9-12	J&J Contractors	\$64,407,000	1,350	Bid	267,357	\$241	\$51,579,703	\$193	Design/Bid/Build	3-May-10	15-May-12	53%	1.00%	Exterior brick veneer continues around the perimeter of the bldg. Window installation underway. MEP rough throughout bldg. Site work continues to get asphalt binder completed in the fall.	\$41,810,972				
Shawsheen Shawsheen Voc Tech HS	9-12	Colantonio	\$3,329,510	1,300	Bid	15,115	\$220	\$2,670,380	\$177	Design/Bid/Build	3-Jan-11	15-Aug-11	92%	0.80%	Addition and renovation work completed. Minor punch list work is underway.	\$2,497,790				
Sturbridge Burgess ES	K-6	Fontaine Brothers	\$22,931,000	860	Bid	131,630	\$174	\$17,591,000	\$134	Design/Bid/Build	10-Aug-10	1-Oct-12	78%	1.00%	The new addition to the school is complete with the exception of some minor punchlist work. An occupancy permit was granted and school commenced with use of the new building on 9-6-11. Renovations to other parts of the school not in use are in process.	\$16,808,626				
Sutton Sutton MS/HS	6-12	TLT Construction Corp.	\$42,123,807	840	Bid	171,401	\$246	\$32,998,403	\$193	Design/Bid/Build	1-Jul-11	1-Jul-14	3%	0.00%	Modular classroom work is being completed. Plumbing, electrical, and fire alarm internal connections and ceiling work completed. Fire road and sidewalk grading initiated. Transformer arrived to site and permanent power was established.	\$29,843,511				
Tewksbury Tewksbury HS	9-12	CTA/Methuen Construction Co.	\$50,800,000	1,100	Bid	218,781	\$232	\$40,159,651	\$184	Design/Bid/Build	15-Oct-10	3-Aug-12	41%	1.70%	Exterior framing, sheathing and AVB are underway. MEP's rough-ins are well underway. Site utilities are continuing.	\$36,622,570				
Adams-Cheshire Hoosac Valley MSHS	6-12	Gilbane	\$30,075,221	805	PFA	173,999	\$173	15,483,125	\$89	CM-R	17-May-11	31-Jul-12	5%	0.00%	Addition- Footings installed. Existing building- Commenced saw-cutting of slabs for footings and piping installation. Demo and abatement continues.	\$28,243,131				
Belmont Roger E Wellington ES	K-5	Skanska	\$27,912,000	575	Bid	88,203	\$316	\$19,931,588	\$226	CM-R	1-Mar-10	24-Aug-11	90%	3.70%	A Temporary Occupancy permit was issued. The Contractor and OPM are coordinating to complete remaining work and punch list items. CTA Construction has commenced steel erection. Foundation construction at the Kitchen and Music Room additions has been completed. The modular (swing space) classrooms have been delivered and installations are underway.	\$12,245,940				
Burlington Marshall Simonds MS	6-8	CTA	\$24,683,286	880	Bid	151,000	\$163	\$18,923,176	\$125	CM-R	15-Apr-11	17-May-13	11%	0.00%	Exterior masonry continues and is 60% complete. Roof is weather tight with some metal roof work remaining. MEP rough-in continues all three floors. Sheetrock is complete on the 3rd floor and has started on the 2nd floor. Site work includes curbing installation on Recreation Road entrance with grading completed at west parking area and west play area.	\$17,143,488				
Dedham Avery ES	K-5	Consigli	\$18,174,209	310	Bid	62,887	\$289	\$13,524,768	\$215	CM-R	15-Oct-10	1-Jan-12	45%	2.20%	Slabs on grade complete. Continue brick/granite masonry work. Applied fire proofing complete. MEP/FP work on going. Exterior stud framing near completion. Interior stud framing on going.	\$11,086,460				
Grafton Memorial Sr HS	9-12	Dimeo	\$54,059,520	900	Bid	186,351	\$290	\$41,783,110	\$224	CM-R	18-Aug-10	17-Jul-12	36%	0.00%	Modular classroom work is being completed. Contractor has poured the footings and walls for the Science wing foundation. The demolition of the ceilings and floor tiles in the hallways has begun. Ceiling demolition and abatement in areas A, C, E, and F have been completed.	\$36,163,052				
Leominster Leominster SHS	9-12	S.O.M.	\$32,709,051	1,825	Bid	295,859	\$111	\$22,855,000	\$77	CM-R	1-Jul-11	30-Aug-13	10%	0.00%	The Installation of footings and foundation walls continue. The damp proofing of foundation walls is ongoing. Electrical conduits installed and are ready for encasement. Site work is ongoing.	\$34,004,658				
Longmeadow Longmeadow HS	9-12	Gilbane	\$63,773,971	1,000	PFA	184,365	\$346	\$38,354,307	\$208	CM-R	Nov-10	23-Feb-13	10%	0.00%	Commenced enabling package consisting of abatement of contaminated materials and building demolition of the existing theatre area. Also includes temporary plumbing, fire protection, HVAC, electrical work along with temporary steel supports.	\$64,734,701				
Methuen Methuen HS	9-12	Dimeo	\$74,917,204	2,075	PFA	368,017	\$204	\$63,689,716	\$173	CM-R	21-Jul-11	Feb-14	0%	0.00%	Phase 3 of the demolition is underway. Students are in the modular classrooms.	\$8,598,929				
Needham Newman ES	K-5	Consigli	\$18,451,284	680	Bid	119,264	\$155	\$12,806,351	\$107	CM-R	16-Jun-10	27-Aug-12	10%	0.70%	Project has full Occupancy Certificate Sept. 6, 2011. Punchlist items will be completed by the end of October.	\$14,438,137				
Rochester Memorial ES	K-6	Gilbane	\$20,568,696	635	PFA	107,183	\$192	\$14,165,117	\$132	CM-R	19-Apr-10	1-Sep-11	98%	3.27%						

**Projects in Construction
MSBA Grant Basis and Maximum Grant Amount**

District & School	Grade	Contractor	Total Construction Cost	Projected Enroll	PFA or Bid Data	Proposed Square Footage	Construction Cost per Square Foot	Building Cost	Building Cost per Square Foot	Project Type	Construction Start	Estimated Substantial Completion Date	Physical Progress (%)	Change Orders (%)	Construction Status	Approximate Maximum Grant Amount *
Rockland John Rogers MS/ HS	5-12	Agostini	\$64,461,963	1,525	Bid	268,106	\$240	\$45,821,680	\$171	CM-R	15-Jan-10	3-Aug-12	20%	0.00%	Phase 1 construction of CMU block walls complete. Commenced re-pointing of existing brick. Primary and secondary electrical duct banks complete and emergency generator is in place. Commenced phase 2 demo. Underground sanitary, storm, and drainage complete for phase 1. Steel erection is 95% complete, and MEP/FP is on going.	\$53,356,682
Sharon Sharon MS	6-8	Consigli	\$34,676,018	845	Bid	171,806	\$202	\$24,732,123	\$144	CM-R	1-Apr-10	23-Jan-12	70%	0.51%	Contractor continues final finishes in the new addition, Café, and Kitchen. Final cleaning, punch lists and FF&E are being finalized. Renovation work is ongoing in existing classrooms.	\$22,670,388
Shrewsbury Sherwood MS	5-6	Gilbane	\$33,986,285	900	Bid	129,378	\$263	\$22,823,030	\$176	CM-R	7-Mar-11	1-Sep-13	23%	0.14%	Foundations and structural steel framing is complete. Placement of concrete slabs is 65% complete. Roofing and light gauge metal framing for building envelope is commencing.	\$23,912,246
Southbridge Southbridge MS/HS	6-12	Consigli	\$57,397,363	1,050	Bid	199,740	\$287	\$41,487,200	\$208	CM-R	30-Nov-10	1-Jun-12	26%	0.00%	Slab-on-grade completed for sections C, D and the stage (B). Metal roof and floor decking are 100% complete. Underground waste, vent, and acid waste piping completed in B. In slab conduit completed in the C and B wing. Site drainage utilities are in progress and approximately 80% complete.	\$52,019,398
Uxbridge High School	9-12	Shawmut Design	\$35,265,819	600	Bid	123,000	\$287	\$25,169,257	\$205	CM-R	28-Feb-11	20-Jun-12	25%	0.00%	Structural steel is complete. Slab on deck 75% complete. Slab on grade complete. CMU is ongoing in the interior of the building. Site utility installation and rough grading is nearly complete.	\$21,973,620
Wayland Wayland HS	9-12	Shawmut Design	\$54,230,819	900	Bid	171,000	\$317	\$37,343,299	\$218	CM-R	28-Jun-10	1-Dec-11	70%	0.71%	Bldg A- MEP work and drywall installation is nearly complete. Drywall taping and painting are ongoing. Bldg B- Drywall taping and painting are nearly complete. Acoustical ceiling grid installations are complete. Ceramic tile and acoustical ceiling tile installations are ongoing. The Field House was completed on August 24, 2011 and turned over to the District.	\$24,051,231
Wellesley Wellesley HS	9-12	Turner	\$82,942,222	1,500	Bid	280,000	\$296	\$55,814,300	\$199	CM-R	24-Aug-09	5-Feb-12	67%	1.00%	Finishes are advancing throughout the building. Interior tile installation to corridors and bathrooms are in progress. Installation of interior metal stairs, interior painting and suspended ceiling layout is ongoing. Installation of interior casework is underway.	\$40,117,222
Woburn Goodyear ES	K-5	Gilbane	\$17,994,825	320	Bid	67,278	\$267	\$13,989,980	\$208	CM-R	9-Mar-10	19-Aug-11	99%	1.10%	Construction activities have been completed with the exception of some minor punchlist items. An occupancy permit was granted and school commenced on September 6, 2011. CM Contract closeout activities are in process.	\$12,441,343
Wait List Projects in Construction																
Wait List Program Totals			\$404,433,706	11,315		2,849,836										\$377,572,229
Cambridge Rindge & Latin HS	9-12	W.T. Rich, Inc.	\$89,957,728	1,529	PFA	470,700	\$191	TBD	TBD	Design/Bid/Build	May-07	Sep-11	96%	8%	Exterior renovation complete. Completion of punchlist is on-going.	\$28,026,977
Haverhill Haverhill HS	9-12	CTA	\$21,878,214	1,864	PFA	677,333	\$32	TBD	TBD	Design/Bid/Build	Apr-04	Sep-11	97%	7%	Finishes package being installed. Project completion expected in September of 2011.	\$23,436,595
Holyoke Holyoke HS	9-12	WJ Mountford	\$16,943,500	1,252	PFA	242,738	\$71	TBD	TBD	Design/Bid/Build	Mar-10	Sep-11	99%	20%	Contractor and District finishing punchlist items. Delays were encountered due to late material delivery.	\$14,368,320
Taunton Parker MS	5-8	Bacon-Agostini	\$88,467,267	2,350	PFA	539,224	\$164	TBD	TBD	Design/Bid/Build	01-Jul-08	29-Aug-11	99%	5%	Substantially Complete August 30, 2011	\$93,590,656
Malden Malden HS	9-12	Gilbane	\$50,002,293	1,720	PFA	365,271	\$137	TBD	TBD	CM-R	20-Apr-09	06-Jan-12	88%	10%	Substantial Completion is scheduled for October 27, 2011.	\$69,364,963
Springfield Putnam Voc Tech HS	9-12	Consigli	\$86,039,066	1,400	Bid	315,000	\$273	\$62,949,742	\$200	CM-R	18-May-10	20-Jul-12	60%	0%	Curtain wall and interior masonry wall installations continue. Window, MEP, drywall, taping and painting are ongoing.	\$102,872,837
Worcester North HS	9-12	Gilbane	\$51,145,638	1,200	PFA	239,570	\$213	\$40,860,983	\$171	CM-R	24-Sep-08	Jun-11	90%	4%	Design for Phase 3&4 of the project which include abatement & demo of the existing school, construction of athletic fields and parking lots are underway.	\$45,911,881
