


Project Overview Report

September 12, 2012

A total of 332 projects that have received invitations from the Board of Directors to collaborate with the MSBA are currently in the MSBA's Eligibility Period and Capital Pipeline. The following summary chart provides the number of projects in the Eligibility Period and each phase of the Capital Pipeline:

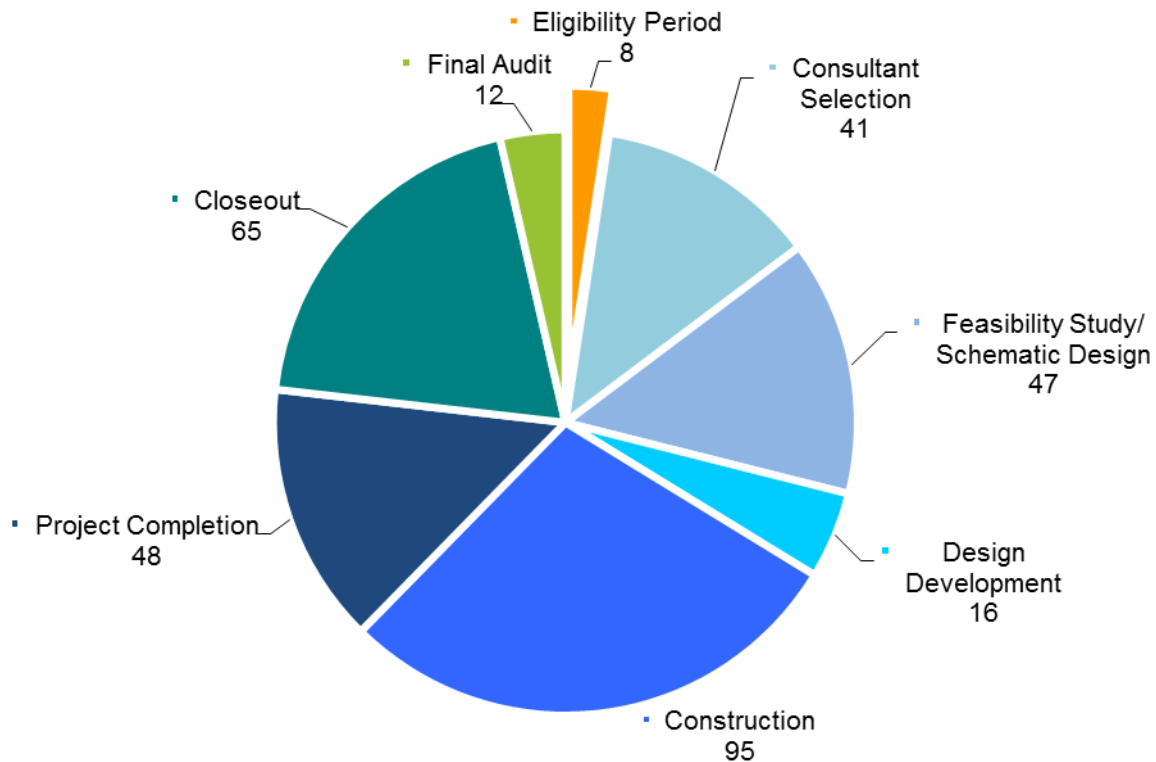

Statement of Interest ("SOI") Review Status

- 280 SOIs submitted:
 - 13 SOIs were filed for the Science Lab Initiative
 - 11 SOIs have been invited into the Eligibility Period
 - 38 SOIs have been invited into the Accelerated Repair Program
 - 218 SOIs are being reviewed for the Core Program

11 of the 13 SOIs filed for the Science Lab Initiative have been invited into the Program. Swansea has requested removal of its SOI for further consideration due to funding concerns.

2 of the 38 facilities invited into the Accelerated Repair Program, Rowe Elementary School and the John A. Parker Elementary School in New Bedford have requested removal of their SOIs for further consideration due to funding concerns.

Eligibility Period

There are eight districts in the Eligibility Period. Four districts are seeking local funding and authorization within the next 60 days, and three of the eight districts have secured funding. The remaining District, Bellingham, held a vote to appropriate Feasibility Study funds on May 24th which failed. The MSBA is awaiting the District's written request to confirm removal from the Eligibility Period.

An agreed-upon enrollment is a key pre-requisite for the MSBA to commence a Feasibility Study with a district. To begin the enrollment projection process, a district must file enrollment information utilizing the MSBA's online enrollment projection tool. Since the last report, four districts have completed the enrollment process.

Based upon the district's anticipated schedules for completion of the Eligibility Period requirements, staff expect that the remaining districts in Eligibility Period may be brought to the Board for Invitation to Feasibility Study at the November and January Board meetings.

Capital Pipeline

Consultant Selection

After the district has completed all Eligibility Period requirements and received a Board Invitation to Feasibility Study, the district procures an Owner's Project Manager ("OPM"). There are 11 districts in the Capital Pipeline who need to procure an OPM.

After a district has selected and executed a contract with an OPM, it selects a Designer utilizing either a local designer selection process for projects under \$5 million or the MSBA's Designer Selection Panel ("DSP") for projects over \$5 million. There are three districts in the Capital Pipeline who are in the process of procuring a Designer.

Feasibility Study

Once a district has procured an OPM and Designer and a Feasibility Study Agreement has been established, the district and its consultants must complete two Feasibility Study submittals, the Preliminary Design Program and the Preferred Schematic Report, prior to Board consideration to proceed into Schematic Design. Based on the most recent data and schedules provided to the MSBA by districts, the MSBA anticipates that eight districts will present their preferred schematic designs to the Board at the upcoming November and January Board meetings.

Prior to consideration by the Board for Project Scope and Budget authorization, a district must submit a schematic design to the MSBA for review. Based on the most recent data and schedules provided to the MSBA by districts, the MSBA anticipates that five districts will appear before the Board for Project Scope and Budget Agreement authorization at the upcoming November and January Board meetings.

Commissioning

Since the last report, the MSBA has assigned Commissioning Consultants to an additional seven projects as presented in the table below. The MSBA has executed 184 Commissioning Consultant contracts to date, totaling \$15.5 million. To date, 25 contracts have been completed.

District	School	Estimated Const. Cost (million)	Commissioning Consultant	Contract Amount
Monomoy Regional	Monomoy Regional High School	\$52.90	Sebesta Blomberg & Associates, Inc.	\$126,000
Southwick-Tolland-Granville Regional	Powder Mill School	\$14.70	BVH Integrated Services, Inc.	\$89,071
Southwick-Tolland-Granville Regional	Southwick Tolland Granville Regional Middle/High School	\$31.40	BVH Integrated Services, Inc.	\$124,495
Southwick-Tolland-Granville Regional	Woodland Elementary	\$7.30	BVH Integrated Services, Inc.	\$77,292
Oxford	Oxford Middle School	\$5.10	Cannon Design	\$69,700
Webster	Park Avenue Elementary	\$35.80	Cannon Design	\$93,798
Wakefield	Galvin Middle School	\$59.80	B2Q Associates, Inc.	\$140,828
Total		\$207.00 million	Total \$721,184	

Design Development

Once a district has secured local funding and has entered into a Project Funding Agreement with the MSBA, it enters the Design Development phase. Currently there are 16 Core Program Projects in Design Development with a total estimated construction cost of \$859.1 million:

Elementary School Districts

Lexington
Newburyport
Webster
Weston
Williamsburg

Middle School Districts

Stoneham
Wakefield

High School Districts

Assabet Valley Regional Technical
Concord-Carlisle Regional
Duxbury
Franklin
Greenfield
Monomoy Regional
North Reading
Southwick-Tolland-Granville Regional
Wilmington

Construction

When a district issues a Notice to Proceed, the project is advanced to the Construction Phase. Currently, there are 95 Projects in the Construction phase with a total estimated construction cost of \$2.6 billion: 53 Green Repair Projects, 40 Core Program Projects, and two Waitlist Projects. The 40 Core Program Projects have a total estimated construction cost of \$2.5 billion and are listed below.

Elementary School Districts	Middle and Middle/High School Districts	High School Districts
Andover Arlington Ashburnham-Westminster Regional Brookline (Runkle) Douglas Fairhaven Marblehead Somerville Springfield (Dryden) Westfield Winchester	Burlington Douglas Fall River Hingham Hudson Medway Oxford Quincy Rockland Saugus Shrewsbury Sutton	<u>Addition/Renovation</u> Danvers Dracut Leominster Lynnfield Methuen Norfolk County Agricultural Norton Southeastern Regional Voc/Tech <u>New</u> Berlin-Boylston Regional Easthampton Longmeadow Essex/North Shore Regional Voc/Tech Maynard <u>Model</u> East Bridgewater Marshfield Somerset-Berkley Regional West Springfield

Project Update

Green Repair Project Update: Lowell


As a result to severe delays in window delivery time for the Moody and Washington Elementary schools, the City of Lowell has requested an extension to the Project Funding Agreement until Friday, August 30, 2013.

The MSBA reviewed the City's request and will grant a conditional extension pending the City's compliance with the following stipulations:

- Per the letter from the MSBA to the City dated August 24, 2012, the City must submit detailed, revised construction timelines showing how the work will be completed at each school by August 30, 2013.
- The MSBA and the City of Lowell will need to execute a second Amendment to the Project Funding Agreement including these updated project schedules.
- Any costs that may result from the City's requested extension of the construction schedules at the Moody and Washington Elementary Schools will be the sole responsibility of the City and are categorically ineligible for reimbursement by the MSBA.


Status of Green Repair Program

169 projects participating in the Green Repair Program have received authorization to enter into a PFA, totaling \$366,647,226 in Total Project Costs and \$222,885,258 in MSBA grants.

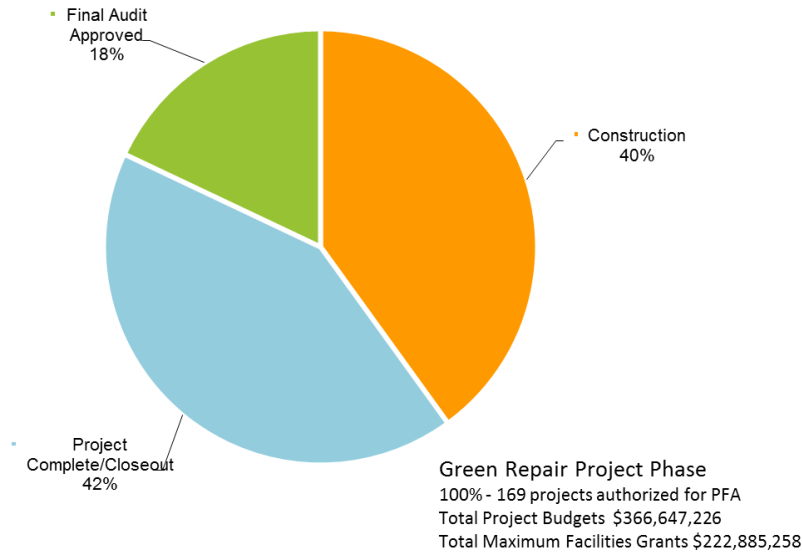

Status of Accelerated Repair Program


Currently there are a total of 24 districts, representing 36 projects, in the Accelerated Repair Program. Upon its request, one of the 24 districts is currently preparing a written request to remove its Statement of Interest from the program. Meanwhile, two districts previously invited into the Program will be removed by a Board Vote at the October 3rd Board of Directors Meeting. All remaining participants successfully completed the required MSBA pre-requisite documents and received consultant assignments. Districts in the Accelerated Repair Program were assigned pre-selected OPMs and Designers procured by the MSBA through a Request for Services issued in April. Eleven projects are under contract with consultants and have advanced into the preferred schematic phase. One Accelerated Repair project will be eligible to execute a Project Funding Agreement pending a Board Vote at the October 3rd Board of Directors Meeting.

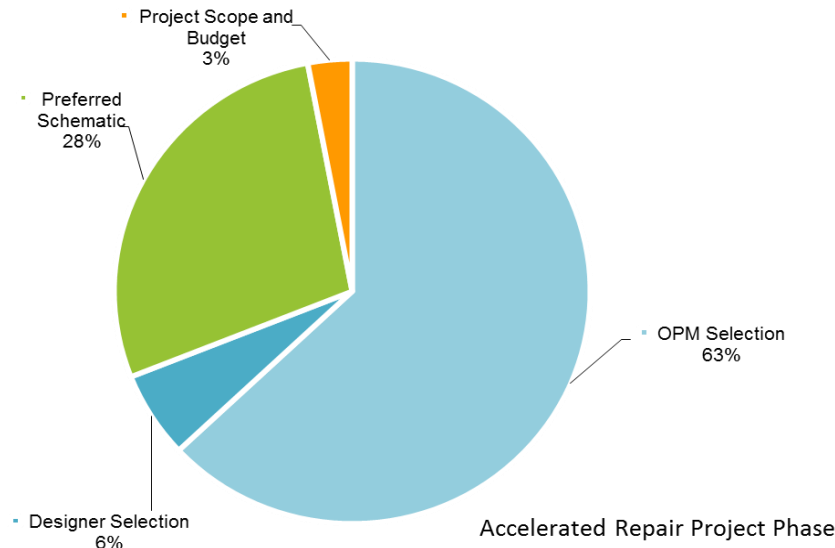

2012 Eligibility Period Status

September 12, 2012


8 Projects in Eligibility Period



District	2012												2013				
	Jan	Feb	Mar	April	May	June	July	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	April	May
Bellingham Macy ES	Board Meeting 1/25/12	ICC (30 days) 2/8/12	SBC (60 days) 3/9/12	Maint Docs 4/8/12		Enroll Certification (180 days) 8/6/12						Local Authorization / FSA (270 days) 11/4/12					
Haverhill Hunking MS		ICC (30 days)	SBC (60 days)	Maint Docs		Enroll Certification (180 days)						Local Authorization / FSA (270 days)					
Holbrook Holbrook Jr/Sr HS		ICC (30 days)	SBC (60 days)	Maint Docs		Enroll Certification (180 days)			Local Authorization			FSA (270 days)					
Swampscott Hadley ES		ICC (30 days)	SBC (60 days)	Maint Docs		Enroll Certification (180 days)						Local Authorization / FSA (270 days)					
Westborough (R) Sarah W Gibbons MS		ICC (30 days)	SBC (60 days)	Maint Docs		Enroll Certification (180 days)			Local Authorization			FSA (270 days)					
Brookline Edward Devotion School				3/28/12	4/11/12	5/11/12	6/11/12				10/8/12		1/7/13				
Worcester Nelson Place ES							6/6/12	7/9/12	8/8/12	9/7/12			1/5/13	Local Authorization		FSA (270 days)	4/5/13
Plymouth South HS								7/25/12	8/8/12	9/7/12	10/8/12				2/4/13		5/6/13
District	Jan	Feb	Mar	April	May	June	July	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	April	May

Project Status | September 12, 2012

Core Program:	63
Waitlist:	2
Green Repair:	85
Accelerated Repair:	36
Science Lab Initiative:	10
Project Complete:	48
Closeout:	65
Final Audit Approved:	12
Projects to be Removed:	3
Total Projects:	324

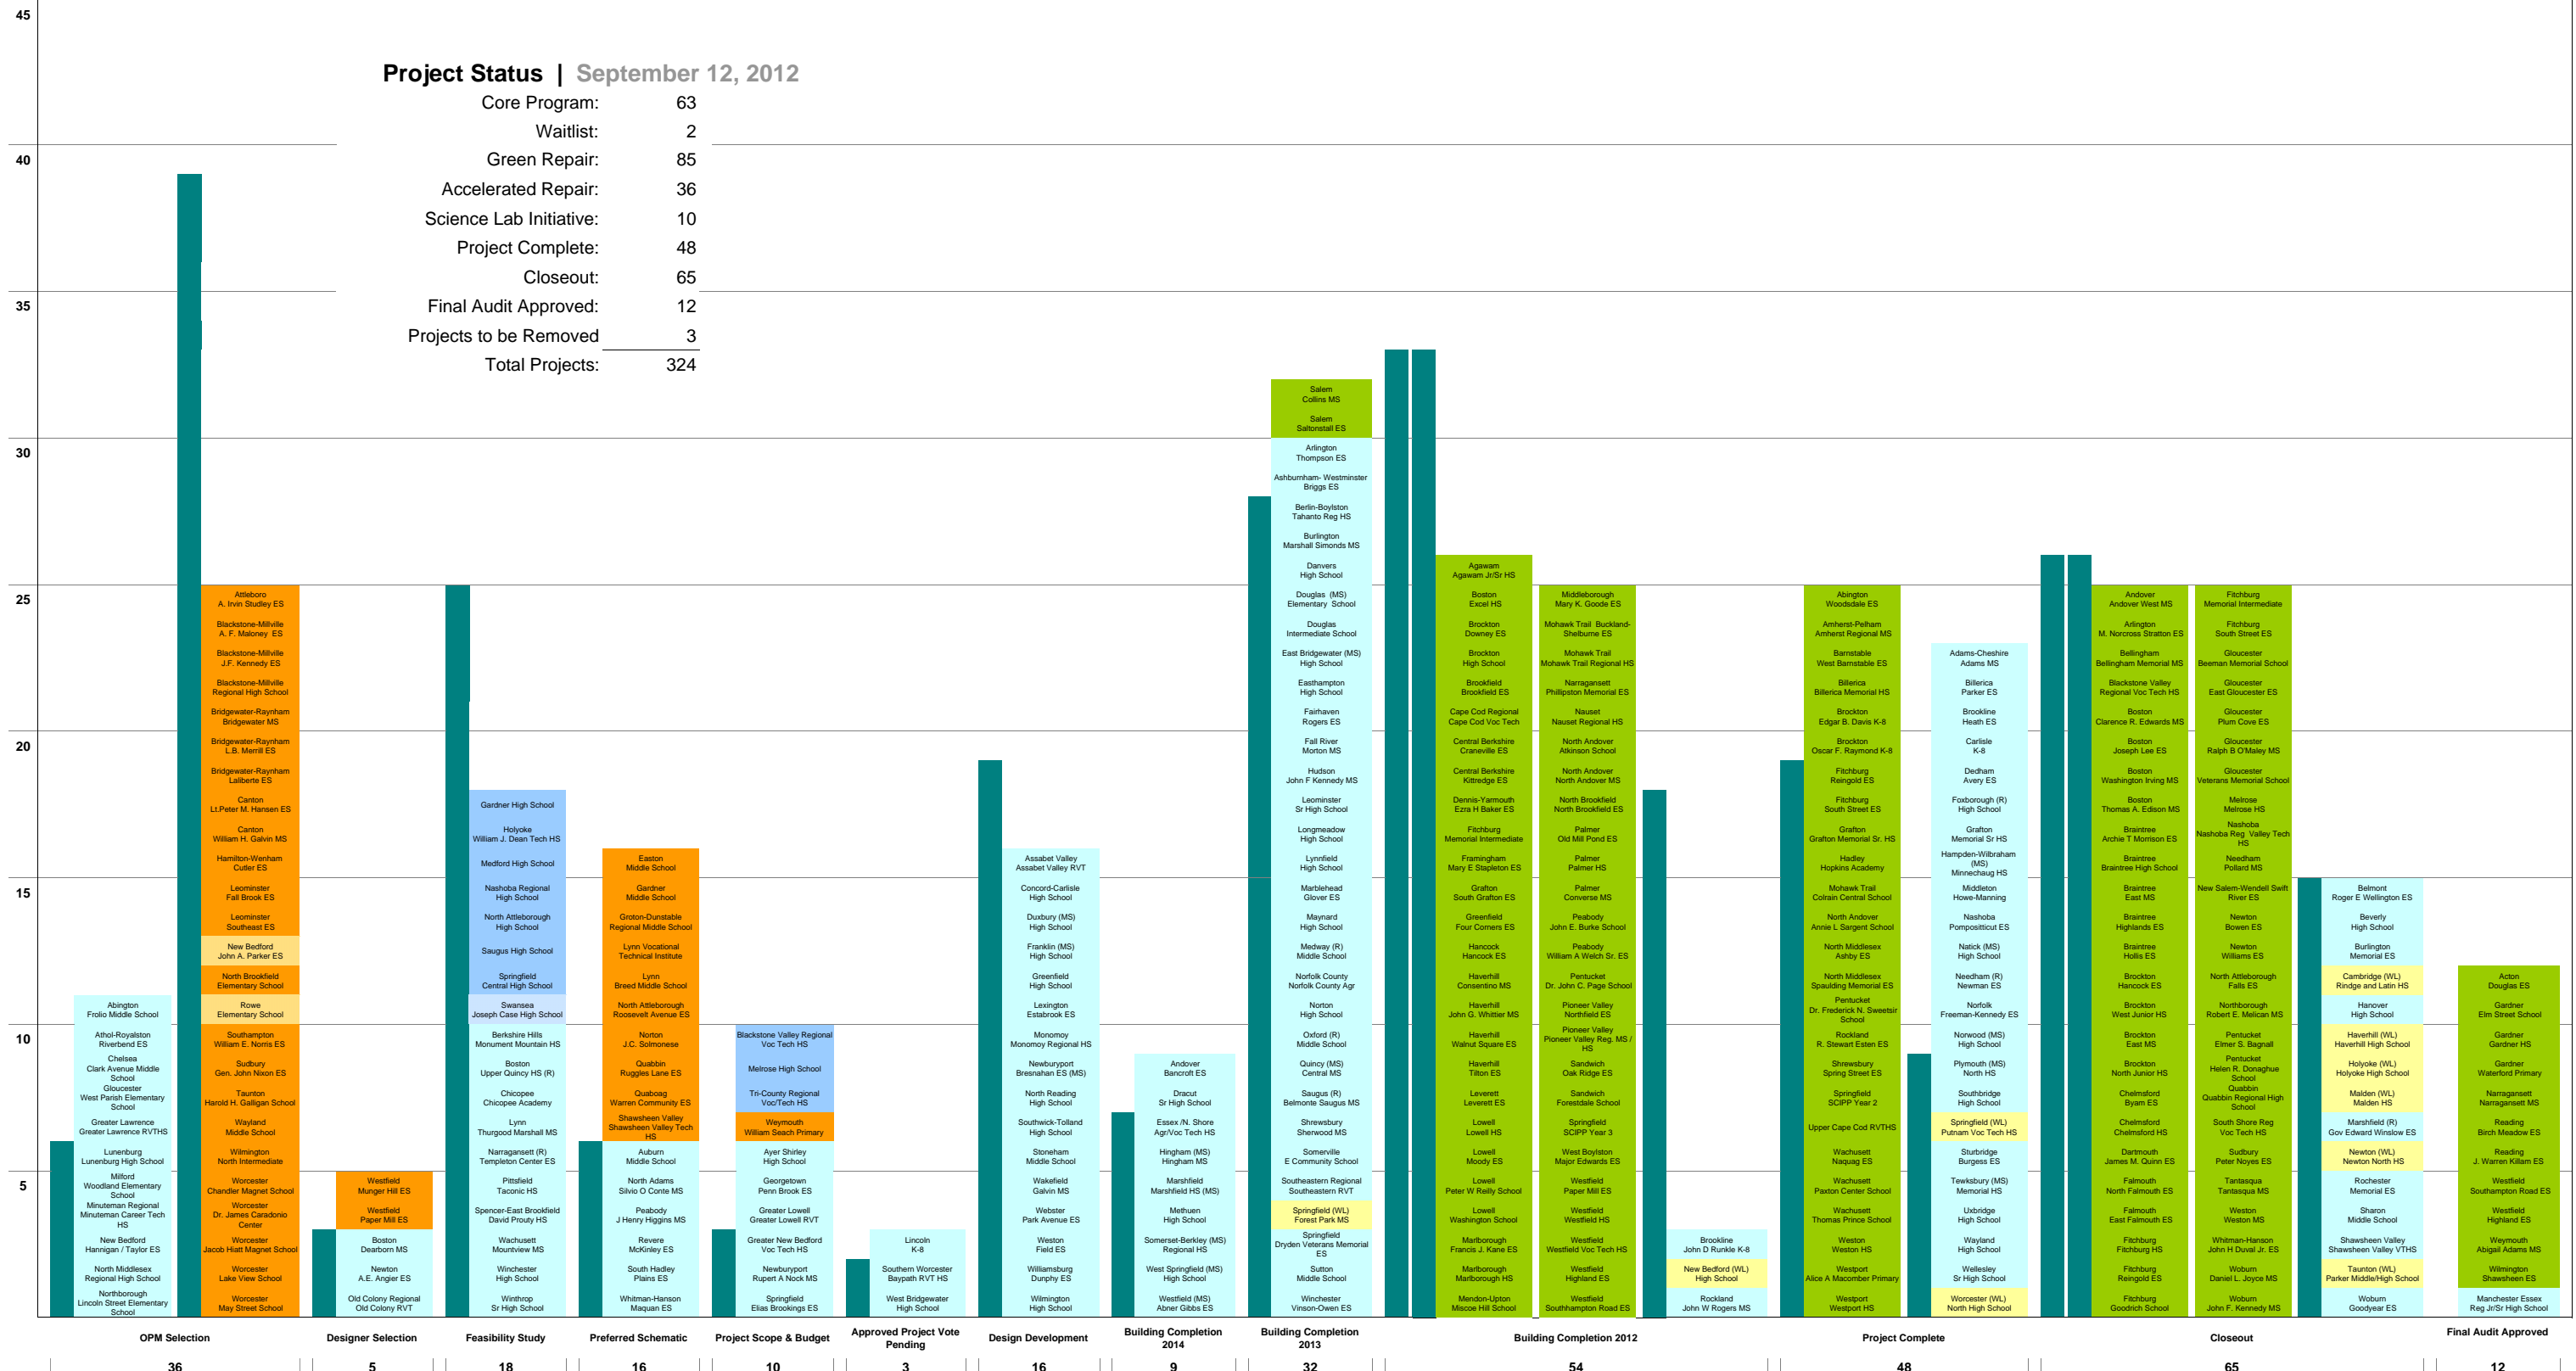

PROJECT STATUS

324
Total Active
Projects

- Green Repair Program
- Accelerated Repair Program
- Science Lab Initiative Project
- Science Lab Initiative Project - To Be Removed
- Waitlist Projects
- Capital Pipeline Status Presented at July 25, 2012 Board of Directors Meeting

2012 Estimated Bid Dates

Note bid dates are **Estimates ONLY**. Please contact Districts for exact information.

Total Project Budget denotes total District costs and does not denote the basis of the MSBA Total Facilities Grant.

■ - Denotes bid phase in progress or complete
 ■ - Denotes estimated bid dates
 ■ - Denotes estimated GMP dates

DISTRICT	DESIGN BASIS FOR ENROLLMENT	PROJECT BUDGET <small>Shown in Millions</small>	CONSTRUCTION BUDGET <small>Shown in Millions</small>	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC
<small>*Projects Considering the CM @ Risk Method</small>															
*ASHBURNHAM-WESTMINSTER	520	\$30.0	\$24.8	JR Briggs ES New Construction: Filed-Sub Bids rcv'd 1/12. GMP issued 3/8.											
NORFOLK COUNTY AGRICULTURAL	550	\$28.6	\$22.3	Norfolk County Aggi Renovation: Filed-Sub Bids rcv'd 1/18. G.C. Bids due 2/1 NTP issued 3/21.											
*SPRINGFIELD -FOREST PARK	660	\$43.4	\$34.0	Springfield Forest Park MS: Filed-Sub Bids rcv'd 3/2. GMP issued 3/26.											
*SOMERVILLE	500	\$33.2	\$15.2	East Somerville Community School Addition/Renovation: Filed-Sub Bids rcv'd 6/14. GMP Targeted September.											
DOUGLAS	552	\$50.7	\$38.9	Douglas IS New Construction: Filed-Sub Bids rcv'd 1/12. G.C. Bids rcv'd 1/20. NTP issued 3/2.											
WINCHESTER	420	\$28.7	21.7	Vinson-Owen ES New Construction: Filed-Sub Bids rcv'd 1/5. G.C. Bids Due 2/2. NTP issued 2/13.											
DRACUT	1160	\$60.4	\$47.30	Dracut Senior HS Addition/Renovation: Filed-Sub Bids rcv'd 7/17. G.C. Bids rcv'd 7/24. NTP issued 8/27.											
*SOUTHEASTERN REGIONAL RVT	1370	\$34.2	\$26.5	SRVT Add/Reno: Filed-Sub Bids rcv'd 2/29. GMP issued 4/2.											
*NORTON	700	\$34.6	\$27.0	Norton HS Addition/Renovation: Filed-Sub Bids rcv'd 3/15. GMP issued 3/27.											
QUINCY	620	\$50.0	\$32.6	Central MS New Construction: Filed-Sub Bids rcv'd 5/8. G.C. Bids rcv'd 5/22. NTP issued 5/24.											
ARLINGTON	380	\$20.7	\$15.7	Arlington Thompson ES New Construction: Filed-Sub Bids rcv'd 3/6. G.C. Bids rcv'd 3/27. NTP issued 4/2.											
LYNNFIELD	740	\$4.5	\$3.2	Lynnfield HS Addition: Filed-Sub Bids rcv'd 4/26. G.C. Bids rcv'd 5/10. NTP issued 6/25.											
MARBLEHEAD	425	\$25.9	\$20.2	Marblehead Glover ES New Construction: Filed-Sub Bids rcv'd 5/9. G.C. Bids rcv'd 5/23. NTP issued 7/16.											
HINGHAM	1020	\$60.9	\$50.4	Hingham MS New Construction: Filed-Sub Bids rcv'd 4/25. G.C. Bids rcv'd 5/10. NTP issued 6/7.											
WESTFIELD	600	\$35.9	\$25.2	Abner Gibbs ES New Construction: Filed-Sub Bids rcv'd 7/19. G.C. Bids rcv'd 8/7. NTP issued 8/24.											
*ESSEX-NS	1440	\$125.0	\$96.50	Essex Northshore HS New Construction: Early Site Packages rcv'd 3/30. Filed-Sub rcv'd 8/29. GMP Targeted Septembert.											
*ANDOVER	680	\$44.7	\$34.5	Andover Bancroft ES New Construction: Early Site, Steel, Foundations Packages. Andover Bancroft ES New Construction: Filed-Sub Bids due 9/22. GMP Targeted November.											
*METHUEN	2075	\$99.1	\$74.9	Methuen HS Addition/Renovation: GMP Issued 5/21.											
FAIRHAVEN	370	\$24.7	\$20.2	Fairhaven Rogers ES _New Construction: Filed-sub rcv'd 5/31. G.C. Bids rcv'd 6/14. NTP issued 6/29.											
SOMERSET BERKLEY	1000	\$82.8	\$66.8	Somerset-Berkley RHS New Construction: Filed-Sub Bids rcv'd 5/30. G.C. Bids rcv'd 6/13. NTP issued 6/28.											
*SAUGUS	725	\$20.3	\$15.7	Saugus Belmonte MS Repair: Filed-Sub Bids rcv'd 6/21. GMP issued 8/15.											
*DUXBURY	1735	\$128.4	\$99.2	Duxbury HS/MS New Construction: Filed-Sub Bids Due 9/20. GMP Targeted September.											
MARSHFIELD	1310	\$103.9	\$80.8	Marshfield HS New Construction: Filed-Sub Bids Due 7/23. G.C. Bids Due 8/6. NTP issued 8/31.											

2012 Estimated Bid Dates

Note bid dates are **Estimates ONLY**. Please contact Districts for exact information.

Total Project Budget denotes total District costs and does not denote the basis of the MSBA Total Facilities Grant.

■ - Denotes bid phase in progress or complete
 ■ - Denotes estimated bid dates
 ■ - Denotes estimated GMP dates

DISTRICT	DESIGN BASIS FOR ENROLLMENT	PROJECT BUDGET <small>Shown in Millions</small>	CONSTRUCTION BUDGET <small>Shown in Millions</small>	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC
<small>*Projects Considering the CM @ Risk Method</small>															
WESTON	355	\$31.5	\$21.5										■		
*SPRINGFIELD-DRYDEN	280	\$13.1	\$10.7									■	■	■	
FRANKLIN	1650	\$104.6	\$87.9									■	■		
*WILMINGTON	960	\$82.7	\$64.4				■	■	■				■	■	
*LEXINGTON	540	\$40.8	31.1					■	■			■	■	■	■
NEWBURYPORT	660	\$37.3	\$31.1												■
MONOMOY REGIONAL SCHOOL	700	\$64.7	52.9											■	■
Subtotal	24,697	\$1,545	\$1,193.2												
GRAND TOTAL	24,697	\$1,545	\$1,193.2												
Number of Construction-Related Employment Opportunities Created			5,966												

2013 Estimated Bid Dates

Note bid dates are **Estimates ONLY**. Please contact Districts for exact information.

Total Project Budget denotes total District costs and does not denote the basis of the MSBA Total Facilities Grant.

■ - Denotes bid phase in progress or complete
 ■ - Denotes estimated bid dates
 ■ - Denotes estimated GMP dates

DISTRICT <small>*Projects Considering the CM @ Risk Method</small>	DESIGN BASIS FOR ENROLLMENT	PROJECT BUDGET <small>Shown in Millions</small>	CONSTRUCTION BUDGET <small>Shown in Millions</small>	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC
STONEHAM	775	\$38.6	\$32.0	Stoneham MS New Construction: Filed-Sub Bids Due 1/11. GMP Targeted February.											
*NORTH READING	1370	\$103.4	86.3	N.Reading HS New Construction: Filed-Sub Bids Due 2/8. GMP Targeted February.											
ASSABET VALLEY	1000	\$62.4	\$50.8	Assabet Valley Regional HS Repair: Filed-sub Bids Due 2/13. G.C. due 2/20. NTP Targeted March.											
WILLIAMSBURG	170	\$12.0	\$9.6	Williamsburg Anne T. Dunphy IS Addition/Renovation: Filed-Sub Bids Due 2/12. G.C. Due 2/26. NTP Targeted March.											
*CONCORD/CARLISLE	1225	\$92.6	\$71.4	Concord/Carlisle HS New Construction: Filed-Sub Bids Due 2/4. GMP Targeted March.											
*GREENFIELD	585	\$63.4	\$52.9	Greenfield HS New Construction: Filed-Sub Bids Due 4/12. GMP Targeted April.											
*WAKEFIELD	1070	\$70.1	\$59.7	Wakefield Galvin MS New Construction: Filed-Sub Bids Due 5/7. GMP Targeted May.											
WEBSTER	720	\$44.9	\$35.8	Webster Park Ave ES New Construction: Filed-Sub Bids Due 5/21. G.C. Bids Due 6/6. NTP Targeted June.											
SOUTHWICK-TOLLAND-GRANVILLE	790	\$71.8	\$55.0	Southwick-Tolland-Granville Addition/Renovation: Filed-Sub Bids Due 7/10. G.C. Due 7/31. NTP Targeted September.											
Subtotal	7,705	\$559	\$453.5												
GRAND TOTAL	7,705	\$559	\$453.5												
Number of Construction-Related Employment Opportunities Created				2,268											

**Projects in Construction
MSBA Grant Basis and Maximum Grant Amount**

New Program and Wait List Program Totals			\$2,279,903,166	50,755		9,855,417											*Includes Alternates	\$1,643,032,774
Project	Grade	Contractor	Total Construction Cost*	Projected Enroll	PFA or Bid Data	Proposed Square Footage	Construction Cost per Square Foot	Building Cost	Building Cost per Square Foot	Project Type	Construction Start	Estimated Substantial Completion Date	Reporting Variance from Schedule	Physical Progress (%)	Change Orders (%)	Construction Status	Approximate Maximum Grant Amount *	
CAPITAL PIPELINE PROJECTS IN CONSTRUCTION																		
New Program Totals			\$2,191,280,202	48,695		9,391,727	\$230		\$174							\$1,481,970,139		
Arlington	K-5	G&R Construction	\$15,340,026	380	Bid	57,614	\$266	\$12,403,811	\$215	Design/Bid/Build	7-Apr-12	28-Jun-13		10%	0.72%	Abatement and demolition of the old Thompson school has been completed under a separate early site contract. A contract was awarded and Notice to Proceed issued on April 20, 2012. Foundations and footings have been installed and steel erection for Sections A & B of the building is progressing.	\$9,441,396	
Berlin-Boylston Tahanto Reg MS/HS	6-12	CTA	\$32,162,000	560	Bid	126,100	\$255	24,629,999	\$195	Design/Bid/Build	10-May-11	1-Jul-13		81%	0.73%	The building is enclosed and weather tight. Ongoing work includes boiler installation, grinding and polishing floors, installation of ceramic tile in the kitchen, and plumbing and light fixtures throughout the building. Auditorium concrete upper risers are out of tolerance and are being re-worked.	\$19,849,301	
Billerica Parker ES	K-5	CTA	\$22,842,500	500	Bid	89,093	\$256	\$17,913,441	\$201	Design/Bid/Build	15-Sep-10	29-Aug-12	90 days	92%	0.00%	New school is substantially complete. Phase II, demolition, is scheduled to be complete by November 26, 2012.	\$15,851,020	
Brookline Heath ES	K-8	Nauset	\$6,284,185	560	Bid	80,952	\$78	\$4,807,436	\$59	Design/Bid/Build	29-Sep-11	15-Aug-12		96%	1.13%	The existing building and the new addition were ready for the start of the new school year. Finish work remains in the cafeteria, auditorium and library.	\$3,173,407	
Brookline Runkle ES	PK-8	G&R Construction	\$20,715,300	560	Bid	104,000	\$199	\$17,668,440	\$170	Design/Bid/Build	10-Nov-10	10-Sep-12	18 days	95%	7.82%	Classrooms and hallways nearly complete. Finish work remains in gym, Media Room, Auditorium and Main Lobby. Furniture is being installed. Site work is ongoing. Playground equipment installation is nearly complete.	\$11,135,430	
Carlisle Carlisle K-8	K-8	H.V. Collins Co. Inc	\$15,277,344	700	Bid	140,312	\$109	\$11,342,751	\$81	Design/Bid/Build	9-Feb-11	31-Aug-12		90%	3.20%	Remaining work of Phase II is scheduled to be complete by the mid to end of September 2012.	\$6,988,636	
Danvers Danvers HS	9-12	Bacon Construction	\$53,834,164	1,000	Bid	246,251	\$219	\$43,710,809	\$178	Design/Bid/Build	14-Nov-10	1-Jul-13		82%	1.56%	Work in the Phase 1 area has been completed. Punch work in the Phase I area is underway. Millwork installation is progressing in the Auditorium and Auditorium Lobby. Abatement and demolition is ongoing in the Dunn Building. Phase II construction of foundations and under slab work has commenced.	\$37,324,055	
Douglas Douglas ES	2-5	CTA	\$23,857,111	552	Bid	83,100	\$287	\$15,737,891	\$189	Design/Bid/Build	Mar-12	23-Jun-13		20%	0.00%	Sitework continues. Steel placement complete. Topping-off ceremony held on September 7, 2012. Roughing mech systems ongoing. Metal stud framing starting interior and exterior.	\$17,611,449	
Douglas Douglas IS	6-8	CTA	\$11,953,015	448	Bid	83,277	\$144	\$9,357,212	\$112	Design/Bid/Build	Mar-12	31-Jan-14		20%	0.00%	Sitework continues. Summer work in the Middle School is complete in the Auditorium and Gym areas.	\$9,319,892	
Dracut Dracut HS	9-12	CTA	\$47,290,611	1,160	PFA	174,671	\$271	\$29,420,210	\$168	Design/Bid/Build	27-Aug-12	17-Dec-14		1%	0.00%	The installation of office trailers and temporary fencing is underway. Installation of erosion control and tree cutting has commenced.	\$36,499,334	
East Bridgewater E. Bridgewater Jr/Sr HS	7-12	Fontaine Brothers	\$65,409,000	950	Bid	213,544	\$306	\$47,684,117	\$223	Design/Bid/Build	10-Aug-11	24-Jun-13		47%	0.10%	Sitework is progressing to complete paving by the end of the year. Underground duct back underway awaiting National Grid. Exterior light gauge framing, spray fireproofing, interior CMU and MEP rough-ins continue.	\$43,317,092	
Easthampton Easthampton HS	9-12	Fontaine Brothers	\$30,934,000	510	Bid	110,400	\$280	\$24,511,000	\$222	Design/Bid/Build	16-May-11	25-Oct-13	28 days	61%	1.04%	Exterior CRM framing complete. Interior CRM framing 90% complete. Installation of roof-top HVAC units complete. Installation of new gas service and relocation of existing service completed. Installation of new water service completed.	\$24,104,384	
Fairhaven Rogers ES	K-5	CTA	\$20,177,237	370	PFA	77,871	\$259	\$14,406,187	\$185	Design/Bid/Build	21-May-12	4-Jul-13		3%	0.00%	Asbestos removal in the existing building has commenced in preparation for the upcoming demolition. Site preparation is complete in the footprint of the new classroom wing. Water and sewer lines have been installed. Concrete footing and wall construction has been initiated.	\$14,992,503	
Fall River Morton MS	6-8	J&J Contractors	\$37,654,000	625	Bid	130,576	\$288	\$29,921,971	\$229	Design/Bid/Build	4-Nov-11	15-Jun-13		39%	8.50%	Site work continues. Scheduled to place asphalt by the end of the year. MEP rough-ins are underway. Windows are scheduled to be installed in November.	\$38,251,808	
Foxborough Foxborough HS	9-12	CTA	\$11,469,333	885	Bid	218,500	\$52	\$8,845,000	\$40	Design/Bid/Build	25-Jan-10	31-Oct-11		100%	9.16%	Final punch list and change order work is being completed. The District has implemented additional scope that has extended the final completion date.	\$7,226,509	
Hampden-Wilbraham Minnechaug HS	9-12	Fontaine Brothers	\$48,597,500	1,225	Bid	231,467	\$210	\$37,499,962	\$162	Design/Bid/Build	22-Jul-10	28-Jun-12		93%	1.90%	Abatement and demolition have begun.	\$34,863,838	
Hingham Hingham MS	6-8	Brait Builders Corp.	\$50,432,439	1,020	PFA	176,385	\$286	\$38,006,989	\$215	Design/Bid/Build	7-Jun-12	30-Dec-14		9%	0.00%	Aggregate piles are complete. Footings and foundations are underway. Site work is ongoing. Steel scheduled to arrive in November.	\$25,909,580	
Hudson John F Kennedy MS	5-7	Agostini/Bacon	\$35,102,573	715	Bid	118,850	\$295	\$28,373,294	\$239	Design/Bid/Build	28-Sep-11	22-Nov-13		45%	1.00%	Ongoing work includes MEP rough installation, exterior waterproofing and masonry, interior framing and door frame installation. Site utility work continues. Interior abatement of existing school was complete prior to the start of classes.	\$24,005,749	
Lynnfield Lynnfield HS	9-12	E.A. Colangeli	\$3,165,166	740	Bid	10,950	\$289	\$2,940,991	\$269	Design/Bid/Build	25-Jun-12	25-Jan-13		22%	0.00%	Contractor completed the substructure concrete work and is in the process of installing the below slab piping. Elevated levels of metals have been discovered in the east parking lot.	\$1,948,020	
Marblehead Glover ES	K-3	G&R Construction	\$20,868,000	425	Bid	79,108	\$264	\$16,977,513	\$215	Design/Bid/Build	25-Jun-12	9-Dec-13		1%	0.00%	Installation of temporary fencing, erosion control measures, loam stripping, tree removal and site clearing has been completed. Abatement and demolition of the existing elementary school is nearly complete. Pre-blast surveys are progressing and meetings with abutters have been conducted to inform them of upcoming blast activities.	\$9,688,418	
Marshfield Governor Winslow ES		Enterprise Equipment Co.	\$1,606,479	494	Bid	65,790	\$24	\$1,408,279	\$21	Design/Bid/Build	Apr-11	26-Aug-11		100%	1.45%	Project is complete and in closeout stage.	\$991,294	
Marshfield High School		Brait Brothers	\$87,308,752	1,310	PFA	267,469	\$326	\$57,027,596	\$213	Design/Bid/Build	Aug-12	7-Jul-14		1%	0.00%	Notice To Proceed issued August 16, 2012. Contractor mobilized and began installation of erosion controls and performed preliminary site work.	\$49,225,401	
Maynard Maynard HS	8-12	CTA	\$36,650,000	410	Bid	121,520	\$302	\$30,630,013	\$252	Design/Bid/Build	18-Aug-11	6-Dec-13		39%	0.79%	Masonry CMU work is ongoing throughout the building. Installation of air vapor barrier in Areas D & C have begun. Fireproofing is complete in all areas. Under slab electrical and plumbing has been completed in all areas.	\$23,483,860	
Middleton Howe-Manning ES	4-6	CTA	\$18,210,000	553	Bid	83,934	\$217	\$14,529,671	\$173	Design/Bid/Build	06-Apr-10	30-Jul-11		100%	6.75%	New building occupied September 7, 2011. Completing change order work. Scheduled to be complete by end of October.	\$12,311,976	
Nashoba Pompositicut ES	K-5	P.J. Stella Construction/Brait Builders	\$23,640,900	600	Bid	98,030	\$241	\$18,427,425	\$188	Design/Bid/Build	15-Jun-10	31-Aug-12		98%	3.32%	Occupancy permit received for the entire project in late August, 2012. Work was completed for the start of the new school year in early September. Corrective work on the rear fields has commenced (tiling and regrading). Remaining minor work items, punch list work, and remaining corrective work are expected to continue through the month of September.	\$15,239,622	
Natick Natick HS	9-12	Brait Builders Corp.	\$63,303,452	1,300	Bid	254,225	\$249	\$53,213,182	\$209	Design/Bid/Build	13-Sep-10	15-Jun-12		90%	3.00%	Abatement and demolition have begun on the existing building. Site work continues and is scheduled to be completed by the end of the year.	\$38,209,033	
Norfolk County Agricultural HS	9-12	TLT Construction Corp.	\$22,256,709	550	PFA	114,816	\$194	\$18,826,079	\$164	Design/Bid/Build	27-Mar-12	23-Aug-13		17%	0.21%	Installation of site utilities for the Animal Science (AS) Building and Agricultural-Mechanical (AG) Building underway. Slab-on-grade at AG complete. Masonry work at first floor of AS nearly complete. Structural steel and MEP work at AS building underway. Cut-over transition to new campus MDF room complete.	\$15,369,712	
Norfolk Freeman-Kennedy ES	3-6	Fontaine Brothers	\$25,354,966	585	Bid	96,410	\$263	\$20,023,001	\$208	Design/Bid/Build	9-Nov-10	10-Jun-12		88%	2.25%	Classes started in the new school in September. Phase II demolition of the existing school was completed and the bus loop and student drop-off was installed with a binder course of pavement. The top coat will be finished in October. Phase III demolition of the remainder of the existing school is underway.	\$15,861,760	
Norwood Norwood HS	9-12	Agostini	\$54,400,480	1,100	Bid	227,374	\$239	\$42,573,646	\$187	Design/Bid/Build	19-May-09	13-May-11		99%	2.40%	Landscaping issues to be resolved this Fall.	\$38,154,487	
Plymouth Plymouth HS	9-12	J&J Contractors	\$67,687,000	1,350	Bid	267,497	\$253	\$51,579,703	\$193	Design/Bid/Build	3-May-10	22-Jun-12	30 days	92%	4.70%	Abatement and demo of the existing building is underway. Punch list work continues.	\$41,810,972	
Quincy Central MS	6-8	H.V. Collins Co. Inc	\$32,607,101	620	PFA	114,975	\$284	\$24,440,102	\$213	Design/Bid/Build	24-May-12	22-Aug-13		7%	0.00%	Footings, foundations and structural steel are underway. Site utilities have begun.	\$32,996,822	
Somerset Berkely Somerset Berkley RHS	9-12	Agostini	\$66,840,822	1,000	PFA	222,826	\$300	\$49,956,137	\$224	Design/Bid/Build	3-Jul-12	1-Jul-14		1%	0.00%	Clearing and site work have begun.	\$50,068,817	
Sturbridge Burgess ES	K-6	Fontaine Brothers	\$22,946,000	860	Bid	131,630	\$174	\$17,591,000	\$134	Design/Bid/Build	10-Aug-10	1-Oct-12		99%	6.71%	Both the new addition and the adjacent building renovations are complete. The final phase of the project consisting of the demolition of the existing school, construction of ball fields, and final landscaping began after school ended in June 2012 and will be complete in November 2012.	\$16,616,077	
Sutton MS/HS	6-12	TLT Construction Corp.	\$41,230,800	840	Bid	179,040	\$230	\$32,998,403	\$184	Design/Bid/Build	1-Jul-11	31-Dec-14	120 days	41%	0.26%	Exterior brick work is underway. Exterior window and MEP installations are in progress.	\$27,837,016	

**Projects in Construction
MSBA Grant Basis and Maximum Grant Amount**

Project	Grade	Contractor	Total Construction Cost*	Projected Enroll	PFA or Bid Data	Proposed Square Footage	Construction Cost per Square Foot	Building Cost	Building Cost per Square Foot	Project Type	Construction Start	Estimated Substantial Completion Date	Reporting Variance from Schedule	Physical Progress (%)	Change Orders (%)	Construction Status	Approximate Maximum Grant Amount *
Tewksbury Tewksbury HS	9-12	CTA/Methuen Construction Co.	\$51,600,000	1,100	Bid	218,781	\$236	\$40,159,651	\$184	Design/Bid/Build	15-Oct-10	3-Aug-12		88%	3.90%	Abatement and demolition of the existing school is underway. Punch list work continues.	\$36,622,570
West Springfield West Springfield HS	9-12	Fontaine Brothers	\$85,006,020	1,270	Bid	257,525	\$330	\$56,875,181	\$221	Design/Bid/Build	14-Dec-11	31-Dec-13		35%	0.00%	Structural steel placement and roofing continue. Light gauge metal framing and MEP rough-ins have begun. Site work is ongoing.	\$68,808,290
Winchester Vinson-Owen ES	K-5	CTA	\$21,290,000	420	PFA	74,774	\$285	17,586,599	\$235	Design/Bid/Build	17-Feb-12	13-May-13		38%	1.70%	Early demo package is complete. Footings and foundations for new building complete. Structural steel erection has started. Site utilities continue. Slabs-on-deck placed.	\$10,292,465
Adams-Cheshire Hoosac Valley MSHS	6-12	Gilbane	\$33,474,193	805	Bid	174,758	\$192	24,009,952	\$137	CM-R	17-May-11	31-Jul-12		97%	0.05%	Certificate of Occupancy was obtained and the renovated building opened for the new school year. Deferred pavement work is complete. PV installation is scheduled to be complete in mid-November.	\$28,243,131
Burlington Marshall Simonds MS	6-8	CTA	\$24,612,440	880	Bid	151,000	\$163	\$18,988,987	\$126	CM-R	15-Apr-11	17-May-13	150 days ahead	80%	2.33%	Renovation of all first floor classrooms has been completed. The last phase of classroom renovations has commenced at the second floor. Renovations of the locker rooms and gymnasium are ongoing.	\$16,933,103
Dedham Avery ES	K-5	Consigli	\$18,174,209	310	Bid	62,723	\$290	\$13,528,098	\$216	CM-R	15-Oct-10	8-Mar-12		99%	6.41%	Completion of final punch list work is ongoing.	\$10,778,452
Essex North Shore Agricultural & Technical School	9-12	Gilbane	\$99,484,995	1,440	PFA	337,000	\$295	\$68,270,270	\$203	CM-R	7-May-12	30-Jun-14		7%	0.00%	Underground utility installations as well as footing and foundation installations continue. Farmstead demolition is complete. Site drainage structures and retaining wall construction are ongoing.	\$77,500,000
Grafton Memorial Sr HS	9-12	Dimeo	\$54,881,977	900	Bid	186,000	\$295	\$41,783,110	\$225	CM-R	18-Aug-10	10-Jul-12		91%	6.00%	New building is complete and punch list work continue. Installation of the second turf field along with the baseball field are ongoing.	\$36,108,679
Leominster Leominster SHS	9-12	S.O.M.	\$33,794,797	1,825	Bid	295,859	\$114	\$25,382,707	\$86	CM-R	1-Jul-11	30-Aug-13		53%	4.99%	Punch list work is progressing in the A/C wings. Renovation of the CTE wing is complete. New windows have been installed. Roof top units have been installed with power and control work underway.	\$30,693,543
Longmeadow Longmeadow HS	9-12	Gilbane	\$63,685,998	1,000	Bid	236,985	\$269	\$46,573,364	\$197	CM-R	Nov-10	1-Nov-13		52%	0.82%	Exterior masonry work has been completed with interior masonry work ongoing. Installation of the metal roofing on the area C monitors was completed. Drywall work and finishes are underway.	\$33,067,140
Medway MS	5-8	Consigli	\$18,211,824	800	Bid	223,780	\$81	\$12,885,464	\$58	CM-R	Oct-11	28-Feb-13		75%	1.10%	This is a 4-phase project. Phase 1 and 2 were completed as scheduled and the Phase 1 area was turned over on April 18, 2012. Currently working on Phase 1 and 2 punch lists. Phase 3, which was the "summer slammer" to get the school ready for the students return, was completed on August 15, 2012. Work has also started on Phase 4.	\$10,352,981
Methuen Methuen HS	9-12	Terminated Dimeo 12/31/2011. Consigli as of 5/21/2012	\$74,917,204	2,075	PFA	368,017	\$204	\$63,689,716	\$173	CM-R	21-Jul-11	Jun-14		10%	0.00%	Site crews are excavating at the back of the building to prepare for the new fire access road. Installation of hydrants and water line on the fire access road is complete. Location for wet lab/temporary trailers has been cleared. Crews are excavating to sub-grade to prepare for foundation and footing installation. Crews have begun to demolish corridors. Abatement crews are removing VCT and mastic at select locations. Electrical crews are installing lights and power supply for temporary classroom spaces. Temporary fire alarm system has been installed.	\$64,734,701
Needham Newman ES	K-5	Consigli	\$19,064,745	754	Bid	119,264	\$160	\$13,367,855	\$112	CM-R	16-Jun-10	27-Aug-12		96%	8.40%	School is open and punch list work continues. Minor site work remains to be completed.	\$8,598,929
Norton Norton HS	9-12	WT Rich	\$27,023,541	700	Bid	130,755	\$207	\$20,590,559	\$157	CMR	12-Mar-12	27-Dec-13		15%	1.18%	Asbestos remediation in all corridors has been completed. Steel framing for the addition is complete. New electrical service and the relocation of existing electrical lines have been completed.	\$21,484,408
Rockland John Rogers MS/ HS	5-12	Agostini	\$66,362,037	1,525	Bid	275,700	\$241	\$47,724,091	\$173	CM-R	15-Jan-10	8/31/12 for MS 12/31/12 for HS		88%	2.00%	The Middle School is complete and minor punch list items continue. The High School has completed Phase 3 and 45% complete in Phase 4 work. Selective demolition for Phase 4 work is ongoing. Area E & F classrooms, cafeteria, kitchen, boy's locker room and gymnasium were turned over for occupancy for the start of the 2012 school year. The High School roof is ongoing. Band Room and loading dock steel erection are complete. Site work continued during August including the setting of curbing and placing of sidewalks. Demolition of the existing school is ongoing.	\$52,837,940
Saugus Belmonte Middle School	6-8	Consigli	\$15,712,630	709	PFA	160,000	\$98	\$11,141,407	\$70	CM-R	23-May-12	23-Aug-13		9%	0.32%	Mobilization is complete. All Phase 1 abatement and demo is complete. New Fire Alarm and Fire Protection systems throughout the entire building are complete, inspected and active. MEP Trades for Phase 1 are underway. Shop drawings are underway and lead times are on schedule for Phase 1.	\$10,097,544
Sharon Sharon MS	6-8	Consigli	\$34,987,118	845	Bid	171,495	\$204	\$24,732,123	\$144	CM-R	1-Apr-10	23-Jan-12		99%	1.89%	Remaining punch list items are being completed. Project closeout is in progress.	\$22,670,388
Shrewsbury Sherwood MS	5-6	Gilbane	\$33,986,286	900	Bid	129,378	\$263	\$22,823,030	\$176	CM-R	7-Mar-11	31-Oct-13		84%	1.60%	Construction of the building has progressed to the point that the third floor and one half of the second floor is being punch listed while the finishes are being completed in the remainder of the new school building. Start-up of roof top units, boilers, air handlers and pumps is ongoing. Window testing has been successfully completed and a scan of the roof is scheduled to be performed in October 2012. Improvements to the parking lot between the existing school and new school were recently completed. FF&E procurement is in process. Fit out of the space is expected to be completed by the end of 2012.	\$22,369,828
Somerville E. Somerville Community School	K-8	Gilbane	\$32,590,244	500	Bid	121,100	\$269	\$24,613,842	\$203	CM-R	7-Nov-11	6-Mar-13		40%	0.30%	Exterior windows and finishes continue. Interior MEP rough-ins are ongoing.	\$15,237,996
Southbridge Southbridge MS/HS	6-12	Consigli	\$59,307,632	1,050	Bid	199,740	\$297	\$41,487,200	\$208	CM-R	30-Nov-10	18-Jun-12	77 days	98%	0.56%	Certificate of substantial completion was issued July 30th. Final completion reached August 7 th . The new building was occupied in September. Punch list work is ongoing.	\$52,019,398
Southeastern Regional Voc Tech High School	9-12	WT Rich	\$26,576,567	1,370	PFA	308,250	\$86	\$17,611,703	\$57	CM-R	27-Jun-11	20-Jan-14		10%	0.20%	Extensive progress has been made on the new gym addition with the completion of new slabs, rough plumbing, interior & exterior masonry walls, rough wiring and installation of a new roofing membrane. Bio Retention Basin No. 4, a new water line for the fire suppression system, and a grease trap and lift station for the cafeteria waste line were completed. The school renovation activities included completion of demolition, saw cutting of slabs for new underground utilities, MEP roughs and wall closures. Finish work is progressing.	\$25,988,607
Uxbridge High School	9-12	Shawmut Design	\$37,293,765	600	Bid	123,000	\$303	\$27,562,625	\$224	CM-R	28-Feb-11	20-Jun-12		93%	1.59%	School is open and construction of the all-purpose fields continue.	\$21,973,620
Wayland ** Wayland HS	9-12	Shawmut Design	\$54,230,819	900	Bid	171,000	\$317	\$37,343,299	\$218	CM-R	28-Jun-10	1-Dec-11		99%	2.59%	Minor punch list items remaining.	\$24,051,231
Wellesley Wellesley HS	9-12	Turner	\$82,942,222	1,500	Bid	280,000	\$296	\$55,814,300	\$199	CM-R	24-Aug-09	1-May-13		97%	4.29%	Demolition of the old High School is complete. Water and drainage utility work are underway.	\$40,117,222
** Excludes Field House																	
Wait List Program Totals			\$120,784,964	2,060		463,690											\$141,213,334
Springfield Forest Park MS	6-8	Consigli	\$34,745,898	660	Bid	148,800	\$234	\$26,209,932	\$176	CM-R	26-Mar-12	26-Jul-13		16%	0.00%	Site work for the additional Gym building is ongoing. Underground plumbing, storm sewer work are in progress. Rough carpentry work is ongoing including LVL installations and window blocking installations. Mechanical coordination with the MEP subcontractors is in progress. Electrical rough is underway. Masonry work at the existing building exterior has started. Concrete work for the Gym footings and foundation walls continues.	\$38,340,497
Springfield Putnam Voc Tech HS	9-12	Consigli	\$86,039,066	1,400	Bid	314,890	\$273	\$62,949,742	\$200	CM-R	18-May-10	20-Jul-12		90%	0.66%	The new building opened on August 27, 2012 for the new school year. Demolition of the existing building continues.	\$102,872,837
Worcester North HS	9-12	Gilbane	\$49,145,638	1,200	Bid	239,570	\$205	\$40,860,983	\$171	CM-R	24-Sep-08	Jun-11		90%	3.20%	The phase 4 contractor mobilized to complete site drainage and infrastructure associated with the parking lots and reconstruction of the ball fields. The existing HS has been demolished	\$45,911,881

You are Currently Viewing Active Projects.

Date of Report: 9/12/12

Active Projects: 332

MSBA ID	District	School	Phase	Project Scope	Procurement Type	OPM	Designer	Cx_ Com	CM/GC
200800010405	Abington	Frolio Middle School	OPM Selection						
201100010015G	Abington	Woodsdale	Project Complete	Repair - Accelerated	DBB	RF Walsh Collaborative Partners	Gale Associates, Inc.	Rus so	Lockheed Window Corporations
201000020020G	Acton	C. T. Douglas Elementary School	Final Audit Approved	Repair - Accelerated	DBB	-	CBI Consulting, Inc.		Gibson Roofs, Inc.
200806030305	Adams-Cheshire	Adams Memorial Middle School	Project Complete	Addition / Renovation	CM@R	URS Corporation	Tessier Associates, Inc.	Strat egic	Gilbane Building Company
201100050405G	Agawam	Agawam Junior High	Construction	Repair - Accelerated	DBB	Municipal Building Consultants, Inc.	CSS Architects Incorporated	Build ing	-
201106050405G	Amherst-Pelham	Amherst Regional MS	Project Complete	Repair - Accelerated	DBB	Strategic Building Solutions, LLC	Bradley Architects, Inc.	Rus so	R&R Window Contractors, Inc.
201100090310G	Andover	Andover West Middle	Closeout	Repair - Accelerated	DBB	Skanska USA Building, Inc	Russo Barr Associates, Inc.	Sim pson	Eagle Rivet Roof Services Corporation
200800090003	Andover	Bancroft Elementary School	Construction	New Construction	CM@R	Dore & Whittier Management Partners, Inc.	Symmes Maini & McKee Associates, Inc.	Seb esta	Skanska USA Building, Inc. Federal Construction Corp. Unicon Inc.
201100100055G	Arlington	M Norcross Stratton Thompson Elementary School	Closeout	Repair - Accelerated	DBB	PMA Construction Services	Turowski2 Architecture, Inc.	Con sulti	G & R Construction, Inc.
200900100050	Arlington	John R. Briggs Elementary School	Construction	New Construction	DBB	PMA Construction Services	HMFH Architects, Inc.	Fore man	Consigli Construction Company, Inc.
200806100025	Ashburnham-Westminster	Assabet Valley Regional Technical High School	Construction	New Construction	CM@R	STV Incorporated	Lamoureux Pagano & Associates, Inc.	Sym mes,	-
200908010605	Assabet Valley	Assabet Valley Regional Technical High School	Design Development		DBB	Strategic Building Solutions, LLC	Design Partnership of Cambridge, Inc.		
200906150020	Athol-Royalston	Riverbend School	OPM Selection	Repair- Accelerated		Symmes Maini & McKee Associates, Inc.			
201200160001	Attleboro	A. Irvin Studley Elementary School	OPM Selection	Repair - Accelerated					
200800170305	Auburn	Auburn Middle School	Preferred Schematic			Skanska USA Building, Inc	Lamoureux Pagano & Associates, Inc.		
9999	Ayer-Shirley	Ayer-Shirley Regional Middle/High School	Project Scope & Budget	Addition / Renovation		Dore and Whittier Architects, Inc.	Symmes Maini & McKee Associates, Inc.		
201100200005G	Barnstable	West Barnstable Elementary School	Project Complete	Repair - Accelerated	DBB	PMA Construction Services	Gale Associates, Inc.	CBI Con	Paul J. Rogan Co., Inc.
201100250315G	Bellingham	Bellingham Memorial Middle School	Closeout	Repair - Accelerated	DBB	Daedalus Projects Inc	Richard D. Kimball Company, Inc.	WS P	General Air Conditioning & Heating, Inc.
201200250009	Bellingham	Clara Macy Elementary	Eligibility Period						
200800260035	Belmont	Roger Wellington Elementary School	Closeout	New Construction	CM@R	PMA Construction Services	Jonathan Levi Architects LLC	Strat egic	Skanska USA Building, Inc.
201006180505	Berkshire Hills	Monument Mountain Regional High School	Feasibility Study			Strategic Building Solutions, LLC	Symmes Maini & McKee Associates, Inc.		
200806200505	Berlin-Boylston	Tahanto Regional High School	Construction	New Construction	DBB	PMA Construction Services	HMFH Architects, Inc.	Strat egic	CTA Construction Co., Inc.
200800300505	Beverly	Beverly HS	Closeout	Addition / Renovation		HEERY	Mount Vernon Group Architects, Inc.		CTA Construction Co., Inc.
200800310015	Billerica	Parker Elementary School	Project Complete	New Construction	DBB	Joslin, Lesser + Associates Inc.	Symmes Maini & McKee Associates, Inc.	Seb esta	CTA Construction Co., Inc. RS Hurford
201100310505G	Billerica	Memorial High School	Project Complete	Repair		Municipal Building Consultants, Inc.	Knight, Bagge & Anderson, Inc.	Buil ding	
201108050605G	Blackstone Valley Reg	Blackstone Valley	Closeout	Repair - Accelerated	DBB	Strategic Building Solutions, LLC	Reinhardt Associates, Inc.	Can non	Greenwood Industries, Inc.
201208050605	Blackstone Valley Reg	Blackstone Valley	Feasibility Study	Science Lab		Compass Project Management, Inc.	Flansburgh Associates, Inc.		

You are Currently Viewing Active Projects.
 Date of Report: 9/12/12
 Active Projects: 332

MSBA ID	District	School	Phase	Project Scope	Procurement Type	OPM	Designer	Cx Com CM/GC
201206220015	Blackstone Valley - Millville	A.F. Maloney Elementary School	OPM Selection	Repair- Accelerated				
201206220008	Blackstone Valley - Millville	J.F. Kennedy Elementary School	OPM Selection	Repair- Accelerated				
201206220505	Blackstone Valley - Millville	Regional High School	OPM Selection	Repair - Accelerated				Can non
201100350430G	Boston	Clarence R Edwards Middle School	Closeout	Repair - Accelerated	DBB	Daedalus Projects Inc	BLW Engineers, Inc.	Rist-Fros - Sim
201100350522G	Boston	Excel High School	Construction	Repair - Accelerated	DBB	Daedalus Projects Inc	BLW Engineers, Inc.	pson -
201000350074	Boston	Henry Dearborn Middle School	Designer Selection			Daedalus Projects Inc	-	-
201100350183G	Boston	Joseph Lee Elementary School	Closeout	Repair - Accelerated	DBB	Daedalus Projects Inc	BLW Engineers, Inc.	Sim pson Gale Associates, Inc.
201000350565	Boston	Quincy Upper School	Feasibility Study			Maureen Anderson - City Employee	HMFH Architects, Inc.	-
201100350425G	Boston	Thomas A Edison Jr High School	Closeout	Repair - Accelerated	DBB	Daedalus Projects Inc	BLW Engineers, Inc.	Sim pson -
201100350445G	Boston	Washington Irving Middle School	Closeout	Repair - Accelerated	DBB	Daedalus Projects Inc	Gale Associates, Inc.	Sim pson -
201000400033G	Braintree	Archie T Morrison Elementary School	Closeout	Repair - Accelerated	DBB	RF Walsh Collaborative Partners	Habeeb & Associates Architects, Inc.	Can non Modern Glass & Aluminum, Inc.
201000400505G	Braintree	Braintree High School	Closeout	Repair - Accelerated	DBB	RF Walsh Collaborative Partners	Habeeb & Associates Architects, Inc.	Can non Gibson Roofs, Inc.
201000400305G	Braintree	East Middle School	Closeout	Repair - Accelerated	DBB	RF Walsh Collaborative Partners	Habeeb & Associates Architects, Inc.	Can non Modern Glass & Aluminum, Inc.
201000400015G	Braintree	Highlands Elementary School	Closeout	Repair - Accelerated	DBB	RF Walsh Collaborative Partners	Habeeb & Associates Architects, Inc.	Can non Modern Glass & Aluminum, Inc.
201000400005G	Braintree	Hollis Elementary School	Closeout	Repair - Accelerated	DBB	RF Walsh Collaborative Partners	Habeeb & Associates Architects, Inc.	Can non Modern Glass & Aluminum, Inc.
201206250320	Bridgewater-Raynham	Bridgewater Middle School	OPM Selection	Repair - Accelerated				
201206250020	Bridgewater-Raynham	L.B. Merrill Elementary School	OPM Selection	Repair - Accelerated				
201206250050	Bridgewater-Raynham	Laliberte Elementary School	OPM Selection	Repair - Accelerated				
201100440505G	Brockton	Brockton High School	Construction	Repair - Accelerated	DBB	Skanska USA Building, Inc	CSS Architects Incorporated	Sim pson Gibson Roofs, Inc.
201100440110G	Brockton	Downey Elementary School	Construction	Repair - Accelerated	DBB	Skanska USA Building, Inc	CSS Architects Incorporated	Sim pson Built-up Roofing Systems LLC
201100440405G	Brockton	East Junior High School	Closeout	Repair - Accelerated	DBB	Skanska USA Building, Inc	CSS Architects Incorporated	Rist-Fros Reliable Roofing and Sheet Metal, LLC
201100440023G	Brockton	Edgar B Davis	Project Complete	Repair - Accelerated	DBB	Skanska USA Building, Inc	CSS Architects Incorporated	Sim pson Reliable Roofing and Sheet Metal, LLC
201100440045G	Brockton	Hancock Elementary School	Closeout	Repair - Accelerated	DBB	Skanska USA Building, Inc	CSS Architects Incorporated	Sim pson Reliable Roofing and Sheet Metal, LLC
201100440410G	Brockton	North Junior High School	Closeout	Repair - Accelerated	DBB	Skanska USA Building, Inc	CSS Architects Incorporated	Rist-Fros Arden Engineering Constructors, LLC Built-up
201100440078G	Brockton	Oscar F Raymond K-8	Project Complete	Repair - Accelerated	DBB	Skanska USA Building, Inc	CSS Architects Incorporated	Sim pson Reliable Roofing and Sheet Metal, LLC
201100440420G	Brockton	West Junior High School	Closeout	Repair - Accelerated	DBB	Skanska USA Building, Inc	CSS Architects Incorporated	Sim pson Reliable Roofing and Sheet Metal, LLC
201100450005G	Brookfield	Brookfield Elementary School	Construction	Repair - Accelerated	DBB	Diversified Project Management	Habeeb & Associates Architects, Inc.	Can non Northeast Energy Control Systems

You are Currently Viewing Active Projects.
 Date of Report: 9/12/12
 Active Projects: 332

MSBA ID	District	School	Phase	Project Scope	Procurement Type	OPM	Designer	Cx Com	CM/GC
201100460015	Brookline	Edward Devotion	Eligibility Period						
201000460025	Brookline	Heath Elementary School	Project Complete	Addition / Renovation	DBB	Town of Brookline Building Department	Miller Dyer Spears Inc.	Con sulti	Nauset Construction Corporation
200800460045	Brookline	John D. Runkle School	Construction	Addition / Renovation	DBB	Town of Brookline Building Department	Design Partnership of Cambridge, Inc.	Con sulti	G & R Construction, Inc.
201000480303	Burlington	Marshall Simonds Middle School	Construction	Addition / Renovation	DBB	Construction Monitoring Services, Inc.	Knight, Bagge & Anderson, Inc.	Engi	CTA Construction Co., Inc.
200800480015	Burlington	Memorial Elementary School	Closeout	New Construction	DBB	Construction Monitoring Services, Inc.	Knight, Bagge & Anderson, Inc.	Con sulti	CTA Construction Co., Inc.
W20024323	Cambridge	Cambridge Rindge and Latin High School	Closeout	Addition / Renovation	DBB	-	HMFH Architects, Inc.		W. T. Rich Company Inc.
201200500012	Canton	Lt. Peter M. Hansen	OPM Selection	Repair - Accelerated					
201200500305	Canton	William H. Galvin Middle School	OPM Selection	Repair - Accelerated					
201008150605G	Cape Cod Region Voc Tech	Cape Cod Region Voc Tech	Construction	Repair - Accelerated	DBB	URS Corporation	Garcia Galuska DeSousa Consulting Engineers Inc.	Fitze mey -	
200800510025	Carlisle	Carlisle School	Project Complete	Addition / Renovation	DBB	Daedalus Projects Inc	HMFH Architects, Inc.	Horizon	H.V. Collins Co., Inc.
201106350025G	Central Berkshire	Craneville Elementary School	Construction	Repair - Accelerated	DBB	Daedalus Projects Inc	Bradley Architects, Inc.	Strategic	Titan Roofing, Inc.
201106350035G	Central Berkshire	Kittredge Elementary School	Construction	Repair - Accelerated	DBB	Daedalus Projects Inc	Bradley Architects, Inc.	Strategic	A.J. Schnopp Jr., Construction, Inc. Alpha
201100560030G	Chelmsford	Byam Elementary School	Closeout	Repair - Accelerated	DBB	Vertex Construction Services	Russo Barr Associates, Inc.	Sim pson	S.O.M. Construction Ent., Inc.
201100560505G	Chelmsford	Chelmsford High School	Closeout	Repair - Accelerated	DBB	Vertex Construction Services	Russo Barr Associates, Inc.	Sim pson	Lockheed Window Corporations
200800570050	Chelsea	Clark Avenue School	OPM Selection			-	-	-	-
200900610021	Chicopee	Chicopee Academy	Feasibility Study			Arcadis	Caolo & Bieniek Associates, Inc.	-	-
200906400505	Concord-Carlisle	Concord-Carlisle Regional High School	Design Development	New Construction	CM@R	KV Associates, Inc.	OMR Architects, Inc.	Strategic	Turner Construction Company
200800710505	Danvers	Danvers High School	Construction	Addition / Renovation	DBB	Construction Monitoring Services, Inc.	DiNisco Design Partnership, Limited	Turner	Bacon Construction Co, Inc.
201100720040G	Dartmouth	James M. Quinn Elementary School	Closeout	Repair - Accelerated	DBB	Vertex Construction Services	Russo Barr Associates, Inc.	Gale Asso	Capeway Roofing Systems, Inc.
200800730010	Dedham	Avery Elementary School	Project Complete	New Construction	CM@R	Construction Monitoring Services, Inc.	Dore & Whittier Architects, Inc.	WS P	Consigli Construction Company, Inc.
201006450005G	Dennis-Yarmouth	Ezra Baker Elementary School	Construction	Repair - Accelerated	DBB	STV Incorporated	Knight, Bagge & Anderson, Inc.	CBI Con	Antonelli Construction Co., Inc.
200800770010	Douglas	Douglas Elementary School	Construction	New Construction		HEERY	DiNisco Design Partnership, Limited	Con sulti	CTA Construction Co., Inc.
200800770100G	Douglas	Douglas Intermediate Elementary School	Construction	Repair - Accelerated	DBB	HEERY	DiNisco Design Partnership, Limited	Con sulti	CTA Construction Co., Inc.
200800790505	Dracut	Dracut Senior High School	Construction	Addition / Renovation	DBB	RF Walsh Collaborative Partners	Mount Vernon Group Architects, Inc.	Engi	-
201000820505	Duxbury	Duxbury High School	Design Development	New Construction	CM@R	KV Associates, Inc.	Mount Vernon Group Architects, Inc.	WS P	Dimeo Construction Company
200900830505	East Bridgewater	East Bridgewater High School	Construction	New Construction	DBB	RF Walsh Collaborative Partners	Ai3 Architects LLC	Foreman	Fontaine Brothers, Inc.
200800860505	Easthampton	Easthampton High School	Construction	New Construction	DBB	Strategic Building Solutions, LLC	Caolo & Bieniek Associates, Inc.	Con sulti	Fontaine Brothers, Inc.

You are Currently Viewing Active Projects.
 Date of Report: 9/12/12
 Active Projects: 332

MSBA ID	District	School	Phase	Project Scope	Procurement Type	OPM	Designer	Cx_ Com CM/IGC
201200880405	Easton	Easton Junior High School	Preferred Schematic	Repair - Accelerated		PMA Construction Services	Russo Barr Associates, Inc.	-
200809130705	Essex Agr Tech	Essex Agricultural and Technical High School	Construction	New Construction	CM@R	PMA Construction Services	Design Partnership of Cambridge, Inc.	Turner Gilbane Building Company
200800940020	Fairhaven	Rogers Elementary School	Construction	New Construction	DBB	Daedalus Projects Inc	HMFH Architects, Inc.	Con sulti -
200900950315	Fall River	James Madison Morton Middle School	Construction	New Construction	DBB	Maguire Group Inc.	Mount Vernon Group Architects, Inc.	Seb esta J & J Contractors, Inc.
201100960005G	Falmouth	East Falmouth Elementary School	Closeout	Repair - Accelerated	DBB	No OPM	Keenan and Kenny Architects, Ltd.	Gale Meadows Construction Asso Company LLC
201100960030G	Falmouth	North Falmouth Elementary School	Closeout	Repair - Accelerated	DBB	No OPM	Keenan and Kenny Architects, Ltd.	Gale Meadows Construction Asso Company LLC
201100970505G	Fitchburg	Fitchburg High School	Closeout	Repair - Accelerated	DBB	Compass Project Management, Inc.	BLW Engineers, Inc.	RDK Engi -
201000970025G	Fitchburg	Goodrich Kindergarten	Closeout	Repair - Accelerated	DBB	Compass Project Management, Inc.	BLW Engineers, Inc.	RDK CAM HVAC & Construction, Inc.
200900970048G	Fitchburg	Memorial Intermediate	Closeout	Repair - Accelerated	DBB	Compass Project Management, Inc.	BLW Engineers, Inc.	Engi E. Amanti & Sons, Inc.
201100970048G	Fitchburg	Memorial Intermediate	Construction	Repair - Accelerated	DBB	Compass Project Management, Inc.	Knight, Bagge & Anderson, Inc.	Sim Lockhead Window Corporations
201100970043G	Fitchburg	Reingold Elementary School	Project Complete	Repair - Accelerated	DBB	Compass Project Management, Inc.	Knight, Bagge & Anderson, Inc.	RDK Lockhead Window Corporations
200900970043G	Fitchburg	Reingold Elementary School	Closeout	Repair - Accelerated	DBB	Compass Project Management, Inc.	BLW Engineers, Inc.	Sim pson E. Amanti & Sons, Inc.
200900970060G	Fitchburg	South Street Elementary	Closeout	Repair - Accelerated	DBB	Compass Project Management, Inc.	BLW Engineers, Inc.	RDK CAM HVAC & Construction, Inc.
201100970060G	Fitchburg	South Street Elementary	Project Complete	Repair - Accelerated	DBB	Compass Project Management, Inc.	Knight, Bagge & Anderson, Inc.	Sim Lockhead Window Corporations
200800990505	Foxborough	Foxborough High School	Project Complete	Repair - Major	DBB	Construction Monitoring Services, Inc.	Kaestle Boos Associates, Inc.	Con sulti CTA Construction Co., Inc.
201101000045G	Framingham	Mary E Stapleton Elementary School	Construction	Repair - Accelerated	DBB	Bargmann, Flendrie & Archetype, Inc.	Russo Barr Associates, Inc.	CBI Con -
200901010505	Franklin	Franklin High School	Design Development	New Construction	DBB	Daedalus Projects Inc	Ai3 Architects LLC	Con sulti -
201101030001G	Gardner	Elm Street School	Final Audit Approved	Repair - Accelerated	DBB	P3 Inc.	Knight, Bagge & Anderson, Inc.	Build ing Reliable Roofing and Sheet Metal, LLC
201101030505G	Gardner	Gardner High School	Final Audit Approved	Repair - Accelerated	DBB	P3 Inc.	Knight, Bagge & Anderson, Inc.	Reliable Roofing and Sheet Metal, LLC
201201030505	Gardner	Gardner High School	Feasibility Study	Science Lab		Pinck & Co., Inc.	Lamoureux Pagano & Associates, Inc.	Build ing -
201201030405	Gardner	Gardner Middle School	Preferred Schematic	Repair - Accelerated		Leftfield, LLC	Richard D. Kimball Company, Inc.	
200801030020G	Gardner	Waterford Street Primary Penn Brook Elementary School	Final Audit Approved	Repair - Accelerated	DBB	P3 Inc.	Knight, Bagge & Anderson, Inc.	Reliable Roofing and Sheet Metal, LLC
200901050010	Georgetown	School	Project Scope & Budget	New Construction		Municipal Building Consultants, Inc.	Drummey Rosane Anderson, Inc.	-
201101070010G	Gloucester	Beeman Memorial School	Closeout	Repair - Accelerated	DBB	Knight, Bagge & Anderson Inc.	CGKV Architects, Inc.	Rus so Built-up Roofing Systems LLC
201101070020G	Gloucester	East Gloucester Elementary School	Closeout	Repair - Accelerated	DBB	Knight, Bagge & Anderson Inc.	CGKV Architects, Inc.	Rus so Stanley Roofing Company, Inc.
201101070042G	Gloucester	Plum Cove Elementary School	Closeout	Repair - Accelerated	DBB	Knight, Bagge & Anderson Inc.	CGKV Architects, Inc.	Rus so Built-up Roofing Systems LLC
201101070305G	Gloucester	Ralph B O'Maley Middle	Closeout	Repair - Accelerated	DBB	Knight, Bagge & Anderson Inc.	CGKV Architects, Inc.	Rus so Titan Roofing, Inc.

You are Currently Viewing Active Projects.
 Date of Report: 9/12/12
 Active Projects: 332

MSBA ID	District	School	Phase	Project Scope	Procurement Type	OPM	Designer	Cx_ Com	CM/IGC
201101070045G	Gloucester	Veterans Memorial West Parish Elementary School	Closeout	Repair - Accelerated	DBB	Knight, Bagge & Anderson Inc.	CGKV Architects, Inc.	Rus so	Stanley Roofing Company, Inc.
200901070050	Gloucester	West Parish Elementary School	OPM Selection			-	-	-	
200801100505	Grafton	Grafton Memorial Senior	Project Complete	New Construction	CM@R	Joslin, Lesser + Associates Inc.	Symmes Maini & McKee Associates, Inc.		Dimeo Construction Company
201101100505G	Grafton	Grafton Memorial Senior	Project Complete	Repair - Accelerated	DBB	URS Corporation	CGKV Architects, Inc.	Hori zon	S.O.M. Construction Ent., Inc.
201101100005G	Grafton	South Grafton Elementary	Construction	Repair - Accelerated	DBB	URS Corporation	CGKV Architects, Inc.	Hori zon	AAlanco Service Corporation
201108230605	Greater Lawrence RVT	Gr Lawrence Reg Voc Tech	OPM Selection			-	-	-	
200908280605	Greater Lowell Voc Tec	Greater Lowell Regional Technical High School	Project Scope & Budget	Repair		HEERY	Knight, Bagge & Anderson, Inc.		
201008250605	Greater New Bedford	Greater New Bedford Vocational Technical High	Project Scope & Budget	Addition / Renovation		Construction Monitoring Services, Inc.	Drumme Rosane Anderson, Inc.		
201101140025G	Greenfield	Four Corners	Construction	Repair - Accelerated	DBB	P3 Project Planning Construction Monitoring Services, Inc.	Tighe & Bond, Inc.	Strat egic	Five Star Building Corp.
200901140505	Greenfield	Greenfield High School	Design Development	New Construction	DBB	Construction Monitoring Services, Inc.	Dore & Whittier Architects, Inc.	BVH Integ	
201206730305	Groton-Dunstable	Groton Dunstable Regional Middle School	Preferred Schematic	Repair - Accelerated		Collaborative Partners Strategic Building Solutions, LLC	ICON architecture, inc.		
201101170505G	Hadley	Hopkins Academy	Project Complete	Repair - Accelerated	DBB		CCS Presentation Systems	Rus so	
201206750010	Hamilton-Wenham	Cutler School	OPM Selection	Repair - Accelerated					
200806800505	Hampden-Wilbraham	Minnechaug Regional High School	Project Complete	New Construction	DBB	Pinnacle One, Inc.	Mount Vernon Group Architects, Inc.	Hori zon	Fontaine Brothers, Inc.
201001210005G	Hancock	Hancock Elementary School	Construction	Repair - Accelerated	DBB	-	Westall Architects		Salco Construction Company, Inc.
200801220505	Hanover	Hanover High School	Closeout	New Construction	DBB	PMA Construction Services	HMFH Architects, Inc.	Hori zon	Callahan, Inc.
201201280035	Haverhill	Caleb Dustin Hunking	Eligibility Period			-	-	-	
201101280100G	Haverhill	Consentino Middle School	Construction	Repair - Accelerated	DBB	Vertex Construction Services	CSS Architects Incorporated	RDK Engi	
	Haverhill	High School	Closeout						
201101280085G	Haverhill	John G Whittier Middle School	Construction	Repair - Accelerated	DBB	Vertex Construction Services	CSS Architects Incorporated	Rus so	
201101280075G	Haverhill	Tilton Elementary School	Construction	Repair - Accelerated	DBB	Vertex Construction Services	CSS Architects Incorporated	Rus so	
201101280080G	Haverhill	Walnut Square Elementary School	Construction	Repair - Accelerated	DBB	Vertex Construction Services	CSS Architects Incorporated	RDK Engi	
201001310410	Hingham	Hingham Middle School	Construction	New Construction	DBB	Knight, Bagge & Anderson Inc.	Ai3 Architects LLC	Fore man	Brait Builders Corp.
200801330505	Holbrook	Holbrook Junior-Senior High School	Eligibility Period			-	-	-	
W20034396	Holyoke	Holyoke High School	Closeout	Repair - Major	DBB	-	Design Partnership of Cambridge, Inc.		
201201370605	Holyoke	Wm J Dean Voc Tech High	Feasibility Study	Science Lab		Skanska USA Building, Inc	Kaestle Boos Associates, Inc.		
200801410410	Hudson	John F. Kennedy Middle School	Construction	New Construction	DBB	PMA Construction Services	OMR Architects, Inc.	WS P	Bacon-Agostini Construction Joint Venture

You are Currently Viewing Active Projects.

Date of Report: 9/12/12

Active Projects: 332

MSBA ID	District	School	Phase	Project Scope	Procurement Type	OPM	Designer	Cx_ Com CM/GC
200801530505	Leominster	Leominster High School	Construction	Addition / Renovation	CM@R	Daedalus Projects Inc	Lamoureux Pagano & Associates, Inc.	Hori zon S.O.M. Construction Ent., Inc.
201201530007	Leominster	Fall Brook	OPM Selection	Repair - Accelerated				
201201530010	Leominster	Southeast School	OPM Selection	Repair - Accelerated				
201101540005G	Leverett	Leverett Elementary School	Construction	Repair - Accelerated	DBB	Potomac Capital Advisors	DiMarinisi & Wolfe Architects Urban Designers	Rus so -
201101550010E	Lexington	Joseph Estabrook Elementary School	Design Development	New Construction		RF Walsh Collaborative Partners	DiNisco Design Partnership, Limited	BVH Integ -
200901570025	Lincoln	Lincoln School	Approved Project Vote Pending	Addition / Renovation		Skanska USA Building, Inc	OMR Architects, Inc.	-
200801590505	Longmeadow	Longmeadow High School	Construction	New Construction	CM@R	Joslin, Lesser + Associates Inc.	OMR Architects, Inc.	Fore man Gilbane Building Company
201101600505G	Lowell	Lowell High School	Construction	Repair - Accelerated	DBB	NETCO Construction Project Managers, Inc.	ICON architecture, inc.	Buil ding -
201101600027G	Lowell	Moody Elementary School	Construction	Repair - Accelerated	DBB	NETCO Construction Project Managers, Inc.	ICON architecture, inc.	Build ing -
201101600040G	Lowell	Peter W Reilly School	Construction	Repair - Accelerated	DBB	NETCO Construction Project Managers, Inc.	ICON architecture, inc.	Buil ding -
201101600055G	Lowell	Washington School	Construction	Repair - Accelerated	DBB	NETCO Construction Project Managers, Inc.	ICON architecture, inc.	Buil ding -
200801620505	Lunenburg	Lunenburg High School	OPM Selection					-
201201630405	Lynn	Breed Middle School	Preferred Schematic	Repair - Accelerated		Diversified Project Management	Kaestle Boos Associates, Inc.	
200901630305	Lynn	Thurgood Marshall Middle School	Feasibility Study			Joslin, Lesser + Associates Inc.	Raymond Design Associates, Inc.	-
201201630605	Lynn	Lynn Vocational Tech Institute	Preferred Schematic	Repair - Accelerated		Diversified Project Management	Kaestle Boos Associates, Inc.	
200901640505	Lynnfield	Lynnfield High School	Construction	Addition / Renovation	DBB	HEERY	Edward Rowse Architects, Inc.	Fitze mey -
W20024319	Malden	Malden High School	Closeout	Addition / Renovation	CM@R	URS Corporation	Flansburgh Associates, Inc.	Gilbane Building Company
200806980610	Manchester Essex Regional	Manchester Essex Regional High School	Final Audit Approved	New Construction	DBB	Design Technique Inc.	Mount Vernon Group Architects, Inc.	TLT Construction Corporation
200801680020	Marblehead	Glover Elementary School	Construction	New Construction	DBB	Municipal Building Consultants, Inc.	JCJ Architecture, PC	RDK Engi -
201101700008G	Marlborough	Francis J Kane Elementary School	Construction	Repair - Accelerated	DBB	RF Walsh Collaborative Partners	Baker/Wohl Architects, Inc.	Build ing A&A Window Products, Inc.
201101700505G	Marlborough	Marlborough High School	Construction	Repair - Accelerated	DBB	RF Walsh Collaborative Partners	Baker/Wohl Architects, Inc.	RDK A&A Window Products, Inc. Engi Feeley, McAnespie, Inc.]
200801710020	Marshfield	Governor Edward Winslow Elementary School	Closeout	Repair - Major	DBB	Vertex Construction Services	Knight, Bagge & Anderson, Inc.	RDK Enterprise Equipment Co., Engi Inc.
201101710505	Marshfield	Marshfield High School	Construction	New Construction	DBB	Compass Project Management, Inc.	Ai3 Architects LLC	Seb esta -
200801740505	Maynard	Maynard High School	Construction	New Construction	DBB	Municipal Building Consultants, Inc.	Tappe Associates, Inc.	WS P CTA Construction Co., Inc.
201201760505	Medford	Medford High School	Feasibility Study	Science Lab		Leftfield, LLC	DiNisco Design Partnership, Limited	-
200801770305	Medway	Medway Middle School	Construction	Repair - Major	CM@R	Compass Project Management, Inc.	Knight, Bagge & Anderson, Inc.	Seb Consigni Construction Company, Inc.
201201780505	Melrose	Melrose High School	Feasibility Study	Science Lab		CPI/Collaborative Partners	Ai3 Architects LLC	-

You are Currently Viewing Active Projects.
 Date of Report: 9/12/12
 Active Projects: 332

MSBA ID	District	School	Phase	Project Scope	Procurement Type	OPM	Designer	Cx_ Com	CM/GC
201101780505G	Melrose	Melrose High School	Closeout	Repair - Accelerated	DBB	Municipal Building Consultants, Inc.	Gale Associates, Inc.	Rus so	Commercial Roofing and Contracting, Inc.
201107100015G	Mendon-Upton	Miscoe Hill School	Construction	Repair - Accelerated	DBB	Maguire Group Inc.	Habeeb & Associates Architects, Inc.	Seb esta	-
200801810505	Methuen	Methuen High School	Construction	Addition / Renovation	CM@R	KBA/Trident	Finegold Alexander and Associates Inc.	Envi ron	Dimeo Construction Company
201101820025G	Middleborough	Mary K. Goode Elementary School	Construction	Repair - Accelerated	DBB	Maguire Group Inc.	Habeeb & Associates Architects, Inc.	Rus so	J.J. Cardosi, Inc.
200801840005	Middleton	Howe-Manning School	Project Complete	New Construction	DBB	RF Walsh Collaborative Partners	DiNisco Design Partnership, Limited	Fore man	CTA Construction Co., Inc.
201101850090	Milford	Woodland	OPM Selection			-	-	-	-
200908300605	Minuteman Voc Tech	Minuteman Regional High School (Career Tech)	OPM Selection			-	-	-	-
201107170005G	Mohawk Trail	Buckland-Shelburne Reg	Construction	Repair - Accelerated	DBB	Potomac Capital Advisors	Bradley Architects, Inc.	Strat egic	-
201107170010G	Mohawk Trail	Colrain Central School	Project Complete	Repair - Accelerated	DBB	Potomac Capital Advisors	Bradley Architects, Inc.	Strat egic	-
201107170505G	Mohawk Trail	Mohawk Trail Reg High School	Construction	Repair - Accelerated	DBB	Potomac Capital Advisors	Bradley Architects, Inc.	Strat egic	-
201122229999	Monomoy	Monomoy Regional High School	Design Development	New Construction		Skanska USA Building, Inc	Mount Vernon Group Architects, Inc.	Seb esta	-
201107200305G	Narragansett	Narragansett Middle School	Final Audit Approved	Repair - Accelerated	DBB	Potomac Capital Advisors	DiMarinisi & Wolfe Architects Urban Designers	Rist-Fros	-
201107200003G	Narragansett	Phillipston Memorial	Construction	Repair - Accelerated	DBB	Potomac Capital Advisors	DiMarinisi & Wolfe Architects Urban Designers	Rist-Fros	-
200807200020	Narragansett	Templeton Center School	Feasibility Study	Repair - Major		Strategic Building Solutions, LLC	Symmes Maini & McKee Associates, Inc.	-	-
201207250505	Nashoba	Nashoba Regional High School	Feasibility Study	Science Lab		Strategic Building Solutions, LLC	Symmes Maini & McKee Associates, Inc.	-	-
200807250015	Nashoba	Pompositticut Elementary School	Project Complete	Addition / Renovation	DBB	Construction Monitoring Services, Inc.	Symmes Maini & McKee Associates, Inc.	Strat egic	P.J. Stella Construction Corp.
200908520605G	Nashoba Valley Tech	Nashoba Valley Technical High School	Closeout	Repair - Accelerated	DBB	-	-	-	-
200801980505	Natick	Natick High School	Project Complete	New Construction	DBB	RF Walsh Collaborative Partners	Ai3 Architects LLC	Rist-Fros	-
201106600505G	Nauset	Nauset Regional High School	Construction	Repair - Accelerated	DBB	NETCO Construction Project Managers, Inc.	Habeeb & Associates Architects, Inc.	CBI Con	Capeway Roofing Systems, Inc. Modern Glass & Consigli Construction
200901990050	Needham	Newman Elementary School	Project Complete	Repair - Major	CM@R	Steven H. Popper - Town Employee	Drumrey Rosane Anderson, Inc.	Rist-Fros	Company, Inc. Triumph Wayne Roofing Systems, LLC
201101990405G	Needham	Pollard Middle	Closeout	Repair - Accelerated	DBB	STV Incorporated	Gale Associates, Inc.	CBI Con	LLC
200902010070	New Bedford	John Hannigan	OPM Selection			-	-	-	-
201202010115	New Bedford	John A. Parker Elementary School	OPM Selection	Repair - Accelerated					
201002010505	New Bedford	New Bedford High School	Construction		DBB	-	-	-	-
201107280015G	New Salem-Wendell	Swift River Elementary School	Closeout	Repair - Accelerated	DBB	Maguire Group Inc.	Bradley Architects, Inc.	Strat egic	RAC Builders, Inc.
201102040005	Newburyport	Francis T Bresnahan Elementary School	Design Development	New Construction		HEERY	HMFH Architects, Inc.	Fitze mey	-
201002040305	Newburyport	Rupert A. Nock Middle School	Project Scope & Budget	Renovation		HEERY	Miller Dyer Spears Inc.	-	-

You are Currently Viewing Active Projects.
 Date of Report: 9/12/12
 Active Projects: 332

MSBA ID	District	School	Phase	Project Scope	Procurement Type	OPM	Designer	Cx_ Com CM GC
201102070005	Newton	A E Angier Elementary School	Designer Selection			Joslin, Lesser + Associates Inc.		-
201102070015G	Newton	Bowen	Closeout	Repair - Accelerated	DBB	STV Incorporated	Habeeb & Associates Architects, Inc.	-
W20014216	Newton	Newton North High School	Closeout	New Construction	CM@R	Turner Construction Co.	Dore & Whittier Architects, Inc.	Dim eo -
201102070125G	Newton	Williams Elementary School	Closeout	Repair - Accelerated	DBB	STV Incorporated	Habeeb & Associates Architects, Inc.	-
200802080005	Norfolk	Freeman-Kennedy Elementary School	Project Complete	New Construction	DBB	Joslin, Lesser + Associates Inc.	Flansburgh Associates, Inc.	WS P Fontaine Brothers, Inc.
200909150705	Norfolk County Agriculture	Norfolk County Agricultural High School	Construction	Addition / Renovation	DBB	Compass Project Management, Inc.	Turowski2 Architecture, Inc.	Rist- TLT Construction Corporation
200802090305	North Adams	Silvio O Conte Middle School	Preferred Schematic	Addition / Renovation		Strategic Building Solutions, LLC	Margo Jones Architects, Inc.	-
201102110018G	North Andover	Annie L Sargent School	Project Complete	Repair - Accelerated	DBB	Municipal Building Consultants, Inc.	ICON architecture, inc.	Can non Varieka Construction, Inc.
201102110001G	North Andover	Atkinson School	Construction	Repair - Accelerated	DBB	Municipal Building Consultants, Inc.	ICON architecture, inc.	Can non Paul J. Rogan Co., Inc.
201102110305G	North Andover	North Andover Middle School	Construction	Repair - Accelerated	DBB	Municipal Building Consultants, Inc.	ICON architecture, inc.	Can non Stanley Roofing Company, Inc.
201102120010G	North Attleborough	Falls Elementary School	Closeout	Repair - Accelerated	DBB	Atlantic Construction and Management, Inc.	CSS Architects Incorporated	Gale Northeast Energy Control Asso Systems
201202120505	North Attleborough	North Attleboro High	Feasibility Study	Science Lab		Skanska USA Building, Inc	Kaestle Boos Associates, Inc.	-
201202120015	North Attleborough	Rossevelt Avenue Elementary School	Preferred Schematic	Repair- Accelerated				
201202150015	North Brookfield	North Brookfield Elementary School	OPM Selection	Repair- Accelerated				
201102150015G	North Brookfield	North Brookfield Elementary School	Construction	Repair - Accelerated	DBB	Vertex Construction Services	LPBA/ Architects, Inc.	Sim Lockhead Window Corporation
201107350010G	North Middlesex	Ashby Elementary	Project Complete	Repair - Accelerated	DBB	Compass Project Management, Inc.	Russo Barr Associates, Inc.	Build Greenwood Industries, Inc. ing GVW, Inc.
201107350505	North Middlesex	North Middlesex Regional High School	OPM Selection			-	-	-
201107350005G	North Middlesex	Spaulding Memorial	Project Complete	Repair - Accelerated	DBB	Compass Project Management, Inc.	Russo Barr Associates, Inc.	Build ing MDM Engineering
201002170505	North Reading	North Reading High School	Design Development	Addition / Renovation	DBB	PMA Construction Services	Dore & Whittier Architects, Inc.	Can non -
201102130003	Northborough	Lincoln Street	OPM Selection			-	-	-
201102130305G	Northborough	Robert E. Melican Middle School	Closeout	Repair - Accelerated	DBB	Pinck & Co., Inc.	ICON architecture, inc.	Strat AAlanco Service egic Corporation
201202180015	Norton	J C Solmonese	Preferred Schematic	Repair - Accelerated		Joslin, Lesser + Associates Inc.	Habeeb & Associates Architects, Inc.	
200902180505	Norton	Norton High School	Construction	Addition / Renovation	CM@R	Pinck & Co., Inc.	JCJ Architecture, PC	Rist- W. T. Rich Company Inc.
200802200505	Norwood	Norwood High School	Project Complete	New Construction	DBB	Compass Project Management, Inc.	Ai3 Architects LLC	Agostini Construction Co., Inc.
200908550605	Old Colony Reg Voc Tech	Old Colony Regional Vocational Technical High	Designer Selection			Vertex Construction Services	-	-
200802260405	Oxford	Oxford Middle School	Construction	Repair - Major		Diversified Project Management	CGKV Architects, Inc.	-
201102270305G	Palmer	Converse Middle School	Construction	Repair - Accelerated	DBB	Diversified Project Management	Tighe & Bond, Inc.	Strat Royal Steam Heater Co. egic Titan Roofing, Inc.

You are Currently Viewing Active Projects.

Date of Report: 9/12/12

Active Projects: 332

MSBA ID	District	School	Phase	Project Scope	Procurement Type	OPM	Designer	Cx_ Com CM/GC
201102270008G	Palmer	Old Mill Pond Elementary School	Construction	Repair - Accelerated	DBB	Diversified Project Management	Tighe & Bond, Inc.	Strategic Royal Steam Heater Co.
201102270505G	Palmer	Palmer High School	Construction	Repair - Accelerated	DBB	Diversified Project Management	Tighe & Bond, Inc.	Strategic Royal Steam Heater Co.] Titan Roofing, Inc.
200802290305	Peabody	J Henry Higgins Middle School	Preferred Schematic	New Construction		Daedalus Projects Inc	DiNisco Design Partnership, Limited	-
201102290007G	Peabody	John E Burke School	Construction	Repair - Accelerated	DBB	Daedalus Projects Inc	LPBA/ Architects, Inc.	Sebesta -
201102290027G	Peabody	William A Welch Sr	Construction	Repair - Accelerated	DBB	Daedalus Projects Inc	LPBA/ Architects, Inc.	Sebesta -
201107450020G	Pentucket	Dr Frederick N Sweetsir	Project Complete	Repair - Accelerated	DBB	PMA Construction Services	Knight, Bagge & Anderson, Inc.	CBI Con E. Amanti & Sons, Inc.
201107450015G	Pentucket	Dr John C Page School	Construction	Repair - Accelerated	DBB	PMA Construction Services	Knight, Bagge & Anderson, Inc.	RDK Capeway Roofing Systems, Engi Inc.
201107450005G	Pentucket	Elmer S Bagnall	Closeout	Repair - Accelerated	DBB	PMA Construction Services	Knight, Bagge & Anderson, Inc.	CBI Con Gibson Roofs, Inc.
201107450010G	Pentucket	Helen R Donaghue School	Closeout	Repair - Accelerated	DBB	PMA Construction Services	Knight, Bagge & Anderson, Inc.	CBI Con Gibson Roofs, Inc.
201107500008G	Pioneer Valley	Northfield Elementary School	Construction	Repair - Accelerated	DBB	Diversified Project Management	CGKV Architects, Inc.	Strategic -
201107500505G	Pioneer Valley	Pioneer Valley Reg	Construction	Repair - Accelerated	DBB	Diversified Project Management	CGKV Architects, Inc.	Strategic -
201002360510	Pittsfield	Taconic High School	Feasibility Study			Skanska USA Building, Inc	-	-
201202390515	Plymouth	Plymouth South High School	Eligibility Period					
200802390505	Plymouth	Plymouth North High School	Project Complete	New Construction	DBB	Ted Gentry Associates, Inc	Ai3 Architects LLC	Sebesta J & J Contractors, Inc.
201007530505G	Quabbin	Quabbin Regional High School	Closeout	Repair - Accelerated	DBB	Vertex Construction Services	LPBA/ Architects, Inc.	Build Kronenberger & Sons ing Restoration, INC.
201207530030	Quabbin	Ruggles Lane Elementary School	Preferred Schematic	Repair - Accelerated				
201207780005	Quaboag	Warren Community Elementary School	Preferred Schematic	Repair - Accelerated				
200802430315	Quincy	Central Middle School	Construction	New Construction	DBB	Tishman Construction Corporation of MA	Ai3 Architects LLC	Sebesta -
201102460005G	Reading	Birch Meadow Elementary School	Final Audit Approved	Repair - Accelerated	DBB	KBA Architects	LPBA/ Architects, Inc.	Russo Paul J. Rogan Co., Inc.
201102460017G	Reading	J Warren Killam Elementary School	Final Audit Approved	Repair - Accelerated	DBB	KBA Architects	LPBA/ Architects, Inc.	Russo Capeway Roofing Systems, Inc.
201002480035	Revere	William McKinley Elementary School	Preferred Schematic			RF Walsh Collaborative Partners	Drumme Rosane Anderson, Inc.	-
200802500005	Rochester	Rochester Memorial School	Closeout	Addition / Renovation	CM@R	PMA Construction Services	Flansburgh Associates, Inc.	Horizon Gilbane Building Company
200802510305	Rockland	John W. Rogers Middle School	Construction	Addition / Renovation	CM@R	Daedalus Projects Inc	Dore & Whittier Architects, Inc.	Con Agostini Construction Co., sulti Inc.
201102510025G	Rockland	R Stewart Esten	Project Complete	Repair - Accelerated	DBB	Daedalus Projects Inc	Habeeb & Associates Architects, Inc.	Russo Northeast Energy Control so Systems
201202530005	Rowe	Rowe Elementary School	OPM Selection	Repair - Accelerated				
200902580305G	Salem	Collins Middle School	Construction	Repair - Accelerated	CM@R	KV Associates, Inc.	Reinhardt Associates, Inc.	Rist-Fros -
201002580050G	Salem	Saltonstall School	Construction	Repair - Accelerated	CM@R	KV Associates, Inc.	Reinhardt Associates, Inc.	Rist-Fros -

You are Currently Viewing Active Projects.

Date of Report: 9/12/12

Active Projects: 332

MSBA ID	District	School	Phase	Project Scope	Procurement Type	OPM	Designer	Cx_ Com CM/GC
201102610010G	Sandwich	Forestdale School	Construction	Repair - Accelerated	DBB	NETCO Construction Project Managers, Inc.	Habeeb & Associates Architects, Inc.	Gale Asso Varieka Construction, Inc.
200902610025G	Sandwich	Oak Ridge School	Construction	Repair - Accelerated	DBB	NETCO Construction Project Managers, Inc.	Habeeb & Associates Architects, Inc.	Gale Asso J.J. Cardosi, Inc.
201002620305	Saugus	Belmonte Middle School	Construction	Repair - Major	DBB	Skanska USA Building, Inc	Fletcher Thompson Architecture Engineering, LLC	Con sulti -
201202620505	Saugus	Saugus High School	Feasibility Study	Science Lab		Strategic Building Solutions, LLC	Symmes Maini & McKee Associates, Inc.	-
200802660305	Sharon	Sharon Middle School	Closeout	Addition / Renovation	CM@R	Daedalus Projects Inc	Kaestle Boos Associates, Inc.	Hori Consigli Construction zon Company, Inc.
201008710605	Shawsheen Valley Voc Tech	Shawsheen Valley Voc Tech High School	Closeout	Addition / Renovation	DBB	Construction Monitoring Services, Inc.	Knight, Bagge & Anderson, Inc.	Colantonio, Inc.
201208710605	Shawsheen Valley Voc Tech	Shawsheen Valley Voc Tech High School	Preferred Schematic	Repair- Accelerated				
200802710305	Shrewsbury	Sherwood Middle School	Construction	New Construction	CM@R	PMA Construction Services	Lamoureux Pagano & Associates, Inc.	RDK Engi Gilbane Building Company
201102710035G	Shrewsbury	Spring Street Elementary School	Project Complete	Repair - Accelerated	DBB	PMA Construction Services	Habeeb & Associates Architects, Inc.	Can non Corp.
200811119999	Somerset-Berkley	Somerset-Berkley High School	Construction	New Construction		Skanska USA Building, Inc	Ai3 Architects LLC	Hori zon -
200902740111E	Somerville	East Somerville Community School at Cummings	Construction	Addition / Renovation	DBB	PMA Construction Services	Maguire Group, Inc.	Fore man Gilbane Building Company
200902780015	South Hadley	Plains School	Preferred Schematic	New Construction		Arcadis	Margo Jones Architects, Inc.	-
200808730605G	South Shore Reg Voc Tech	South Shore Vocational Technical High School	Closeout	Repair - Accelerated	DBB	Vertex Construction Services	Gale Associates, Inc.	Build ing -
200802770505	Southbridge	Southbridge High School	Project Complete	New Construction	CM@R	Joslin, Lesser + Associates Inc.	Tappe Associates, Inc.	Envi Consigli Construction ron Company, Inc.
201202750005	Southampton	William E. Norris Elementary School	OPM Selection	Repair - Accelerated				
200908720605	Southeastern Reg Voc Tech	Southeastern Regional Vocational Technical School	Construction	Addition / Renovation	CM@R	RF Walsh Collaborative Partners	Drumme Rosane Anderson, Inc.	RDK Engi W. T. Rich Company Inc.
200908760605	Southern Worcester Cty VT	Bay Path Regional Vocational Technical High School	Approved Project Vote Pending	Addition / Renovation	DBB	HEERY	Kaestle Boos Associates, Inc.	-
201107660505	Southwick-Tolland	Regional High School	Design Development	Addition / Renovation				BVH Integrated Services, Inc.
200807670505	Spencer-E Brookfield	David Prouty High School	Feasibility Study			Dore and Whittier Architects, Inc.	Design Partnership of Cambridge, Inc.	-
	Springfield	SCIPP Year 2	Project Complete					
	Springfield	SCIPP Year 3	Construction					
201102810125E	Springfield	Dryden Veterans Memorial Elementary School	Construction	Addition / Renovation		Arcadis	Drumme Rosane Anderson, Inc.	BVH Integ -
201102810030E	Springfield	Elias Brookings Elementary School	Project Scope & Budget	New Construction		Arcadis	Drumme Rosane Anderson, Inc.	-
W20014137	Springfield	Forest Park Middle School	Construction	Addition / Renovation	DBB	Arcadis	Perkins Eastman	Fore man -
W20054428	Springfield	Roger L. Putnam Vocational Technical High School	Project Complete	New Construction	CM@R	Pinnacle One, Inc.	Drumme Rosane Anderson Inc.	Strat egic Consigli/Morganti
201202810500	Springfield	Central High School	Feasibility Study	Science Lab		Leftfield, LLC	DiNisco Design Partnership, Limited	
200902840405	Stoneham	Stoneham Middle School	Design Development	Addition / Renovation	CM@R	Joslin, Lesser + Associates Inc.	Tappe Associates, Inc.	RDK Shawmut Design and Engi Construction

You are Currently Viewing Active Projects.
 Date of Report: 9/12/12
 Active Projects: 332

MSBA ID	District	School	Phase	Project Scope	Procurement Type	OPM	Designer	Cx_ Com CM/GC
200802870005	Sturbridge	Burgess Elementary School	Project Complete	Addition / Renovation	DBB	Lamoureux Pagano & Associates, Inc.	Drumme Rosane Anderson, Inc.	Hori zon Fontaine Brothers, Inc.
201102880030G	Sudbury	Peter Noyes Elementary School	Closeout	Repair - Accelerated	DBB	Compass Project Management, Inc.	Russo Barr Associates, Inc.	RDK Engi Gibson Roofs, Inc.
201202880025	Sudbury	General John Nixon Elementary School	OPM Selection	Repair - Accelerated				
200802900305	Sutton	Sutton Middle School	Construction	Addition / Renovation	DBB	Strategic Building Solutions, LLC	Flansburgh Associates, Inc.	RDK TLT Construction Engi Corporation
201102910010	Swampscott	Hadley	Eligibility Period					
201202920305	Swansea	Joseph Case Jr High	Feasibility Study	Repair - Accelerated				
201107700405G	Tantasqua	Tantasqua Regional Jr High School	Closeout	Repair- Accelerated	DBB	Diversified Project Management	Habeeb & Associates Architects, Inc.	Greenwood Industries, Inc.
201202930057	Taunton	Harold H Galligan School	OPM Selection	Repair - Accelerated				
W20014194	Taunton	Parker Middle/Taunton High School	Closeout	Addition / Renovation	CM@R	Gilbane Building Company	Design Partnership of Cambridge, Inc.	Bacon-Agostini Construction Joint Venture
200802950505	Tewksbury	Tewksbury Memorial High School	Project Complete	New Construction	DBB	HEERY	Symmes Maini & McKee Associates, Inc.	Seb esta CTA Ventures
201208780605	Tri County	Tri County Reg Voc Tech	Feasibility Study	Science Lab		Collaborative Partners	Ai3 Architects LLC	-
201108790605G	Upper Cape Cod Voc Tech	Upper Cape Cod Voc Tech	Project Complete	Repair - Accelerated	DBB	NETCO Construction Project Managers, Inc.	Knight, Bagge & Anderson, Inc.	Gale Modern Glass & Aluminum, Asso Inc.
200803040505	Uxbridge	Uxbridge High School	Project Complete	New Construction	CM@R	Joslin, Lesser + Associates Inc.	Raymond Design Associates, Inc.	Turn er Shawmut Design and Construction
200907750305	Wachusett	Mountview Middle School	Feasibility Study			Gary Kaczmarek - Town Employee	Lamoureux Pagano & Associates, Inc.	-
201107750035G	Wachusett	Naquag Elementary School	Project Complete	Repair - Accelerated	DBB	Strategic Building Solutions, LLC	LPBA/ Architects, Inc.	Rist-Fros MDM Engineering
201107750040G	Wachusett	Paxton Center School	Project Complete	Repair - Accelerated	DBB	Strategic Building Solutions, LLC	LPBA/ Architects, Inc.	Rist-Fros MDM Engineering
201107750045G	Wachusett	Thomas Prince School	Project Complete	Repair - Accelerated	DBB	Strategic Building Solutions, LLC	LPBA/ Architects, Inc.	Rist-Fros MDM Engineering
201003050310	Wakefield	Galvin Middle School	Design Development	New Construction	DBB	Joslin, Lesser + Associates Inc.	Tappe Associates, Inc.	B2Q Asso -
201203150305	Wayland	Wayland Middle School	OPM Selection	Repair - Accelerated				
200803150505	Wayland	Wayland High School	Project Complete	New Construction	CM@R	KV Associates, Inc.	HMFH Architects, Inc.	WS Shawmut Design and P Construction
200903160015	Webster	Park Avenue Elementary School	Design Development	New Construction	DBB	RF Walsh Collaborative Partners	Dore & Whittier Architects, Inc.	-
200803170505	Wellesley	Wellesley Senior School	Project Complete	New Construction	CM@R	Ryegate, Inc.	Symmes Maini & McKee Associates, Inc.	Rist-Fros Turner Construction Company
201103220005G	West Boylston	Major Edwards Elementary	Construction	Repair - Accelerated	DBB	URS Corporation	Reinhardt Associates, Inc.	Can non -
201003230505	West Bridgewater	West Bridgewater Middle-Senior High School	Approved Project Vote Pending	New Construction		Strategic Building Solutions, LLC	Flansburgh Associates, Inc.	-
200903320505	West Springfield	West Springfield High School	Construction	New Construction	DBB	Strategic Building Solutions, LLC	Symmes Maini & McKee Associates, Inc.	Turn er Fontaine Brothers, Inc.
200903210305	Westborough	Gibbons Middle School	Eligibility Period					
200903250020	Westfield	Abner Gibbs Elementary School	Construction	New Construction	DBB	Skanska USA Building, Inc	Margo Jones Architects, Inc.	Hori zon -

You are Currently Viewing Active Projects.

Date of Report: 9/12/12

Active Projects: 332

MSBA ID	District	School	Phase	Project Scope	Procurement Type	OPM	Designer	Cx_ Com CM/GC
201103250025G	Westfield	Highland Elementary School	Construction	Repair - Accelerated	DBB	P3 Project Planning	Tighe & Bond, Inc.	
201003250025G	Westfield	Highland Elementary School	Final Audit Approved	Repair - Accelerated	DBB	P3 Project Planning	Tighe & Bond, Inc.	Strat egic -
201103250033E	Westfield	Munger Hill Elementary School	Designer Selection	Repair - Accelerated				
201103250036G	Westfield	Paper Mill Elementary School	Construction	Repair - Accelerated	DBB	P3 Project Planning	Tighe & Bond, Inc.	Strat egic -
201203250036	Westfield	Paper Mill Elementary School	Designer Selection	Repair - Accelerated				
201103250040G	Westfield	Southampton Road Elementary School	Final Audit Approved	Repair - Accelerated	DBB	P3 Inc.	Tighe & Bond, Inc.	
201003250040G	Westfield	Southampton Road Elementary School	Construction	Repair - Accelerated	DBB	P3 Project Planning	Tighe & Bond, Inc.	Strat egic R & H Roofing
201103250505G	Westfield	Westfield High School	Construction	Repair - Accelerated	DBB	P3 Project Planning	Tighe & Bond, Inc.	Strat egic -
201103250605G	Westfield	Westfield Voc Tech High School	Construction	Repair - Accelerated	DBB	P3 Project Planning	Tighe & Bond, Inc.	Strat egic -
200903300012	Weston	Field Elementary School	Design Development	New Construction	DBB	Compass Project Management, Inc.	Jonathan Levi Architects LLC	Fore man -
201103300505G	Weston	Weston High School	Project Complete	Repair - Accelerated	DBB	Compass Project Management, Inc.	Garcia Galuska DeSousa Consulting RDK Engineers Inc.	Engi -
201103300305G	Weston	Weston Middle School	Closeout	Repair - Accelerated	DBB	Compass Project Management, Inc.	Russo Barr Associates, Inc.	Engi Greenwood Industries, Inc.
201103310015G	Westport	Alice A Macomber Primary	Project Complete	Repair - Accelerated	DBB	Pinck & Co., Inc.	CGKV Architects, Inc.	CBI Con -
201103310505G	Westport	Westport High School	Project Complete	Repair - Accelerated	DBB	Pinck & Co., Inc.	CGKV Architects, Inc.	CBI Con -
201103360310G	Weymouth	Abigail Adams Middle School	Final Audit Approved	Repair - Accelerated	DBB	KBA Architects	Gale Associates, Inc.	Can non Greenwood Industries, Inc.
201203360080	Weymouth	William Seach Primary	Preferred Schematic	Repair - Accelerated				
201107800030G	Whitman-Hanson	John H Duval Jr Elementary School	Closeout	Repair - Accelerated	DBB	-	BETA Group, Inc.	S.I. Services, Inc.
200907800025	Whitman-Hanson	Maquan Elementary School	Preferred Schematic			Knight, Bagge & Anderson Inc.	Turowski2 Architecture, Inc.	-
200803400005	Williamsburg	Anne T. Dunphy School	Design Development	Addition / Renovation	DBB	Arcadis	Drumrey Rosane Anderson, Inc.	B2Q Asso -
201203420060	Wilmington	North Intermediate	OPM Selection	Repair - Accelerated				
201103420025G	Wilmington	Shawsheen Elementary School	Final Audit Approved	Repair - Accelerated	DBB	P3 Inc.	Russo Barr Associates, Inc.	CBI Lockheed Window Con Corporations
200903420505	Wilmington	Wilmington High School	Design Development	New Construction	CM@R	Joslin, Lesser + Associates Inc.	Dore & Whittier Architects, Inc.	Sym mes, Gilbane Building Company
200803440025	Winchester	Vinson-Owen Elementary School	Construction	New Construction	DBB	Neil Foley - Town Employee	Tappe Associates, Inc.	Turn er CTA Construction Co., Inc.
201003440505	Winchester	Winchester High School	Feasibility Study			Skanska USA Building, Inc	Symmes Maini & McKee Associates, Inc.	-
200803460505	Winthrop	Winthrop Sr High School	Feasibility Study			Skanska USA Building, Inc	HMFH Architects, Inc.	-
201103470410G	Woburn	Daniel L Joyce Middle School	Closeout	Repair - Accelerated	DBB	Municipal Building Consultants, Inc.	Gale Associates, Inc.	Sim Reliable Roofing and Sheet pson Metal, LLC
200803470015	Woburn	Goodyear School	Closeout	New Construction	CM@R	Municipal Building Consultants, Inc.	Tappe Associates, Inc.	Strat egic Gilbane Building Company

You are Currently Viewing Active Projects.

Date of Report: 9/12/12

Active Projects: 332

MSBA ID	District	School	Phase	Project Scope	Procurement Type	OPM	Designer	Cx_ Com CM/GC
201103470405G	Woburn	John F Kennedy Middle School	Closeout	Repair - Accelerated	DBB	Municipal Building Consultants, Inc.	Gale Associates, Inc.	Sim pson Greenwood Industries, Inc.
201203480052	Worcester	Chandler Magnet School	OPM Selection	Repair - Accelerated				
201203488099	Worcester	Dr. James Caradonio Center	OPM Selection	Repair - Accelerated				
201203480140	Worcester	Jacob Hiatt Magnet School	OPM Selection	Repair - Accelerated				
201203480145	Worcester	Lake View School	OPM Selection	Repair - Accelerated				
201203480175	Worcester	May Street School	OPM Selection	Repair - Accelerated				
201203480200	Worcester	Nelson Place	Eligibility Period			-	-	-
W20004048	Worcester	North High School	Project Complete	New Construction	CM@R	-	Maguire Group, Inc.	Arc hite Gilbane Building Company
