


Project Overview Report

October 24, 2012

A total of 330 projects that have received invitations from the Board of Directors (“Board”) to collaborate with the MSBA are currently in the MSBA’s Eligibility Period and Capital Pipeline. The following summary chart provides the number of projects in the Eligibility Period and each phase of the Capital Pipeline:

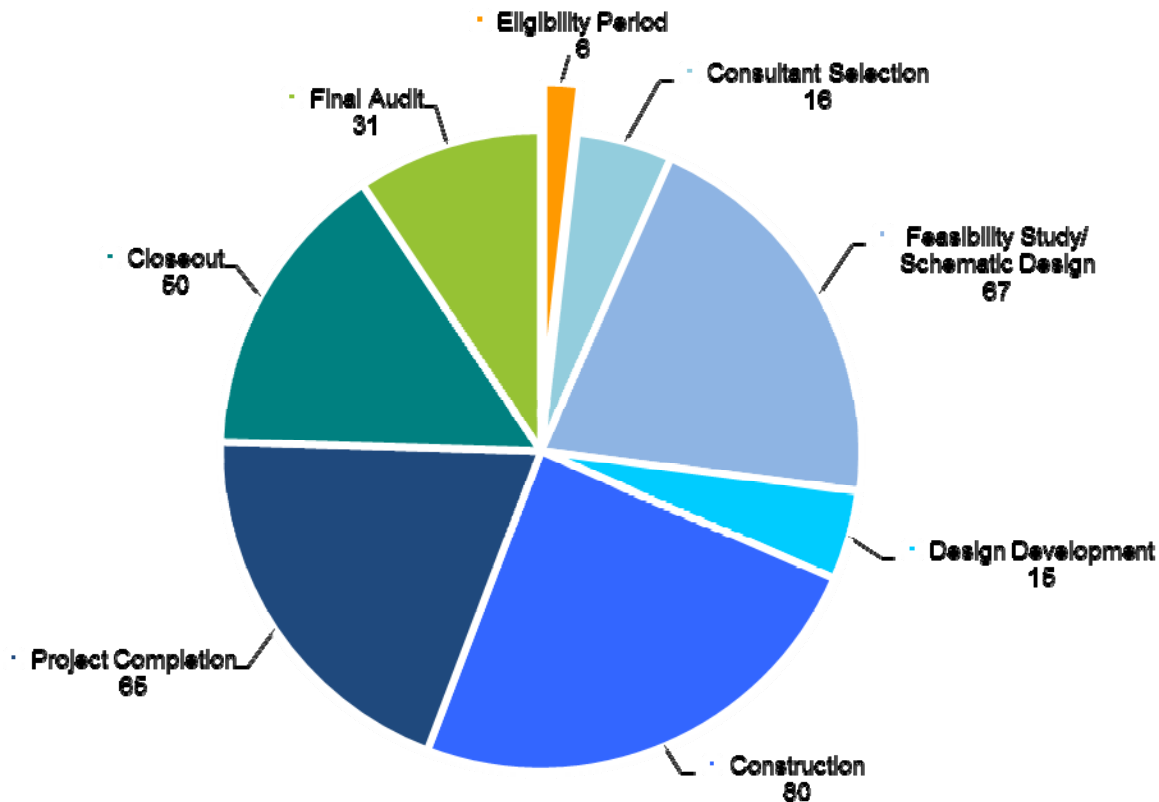

Statement of Interest (“SOP”) Review Status

- 280 SOIs submitted:
 - 13 SOIs were filed for the Science Lab Initiative
 - 11 SOIs have been invited into the Eligibility Period
 - 39 SOIs have been invited into the Accelerated Repair Program
 - 217 SOIs are being reviewed for the Core Program

Eleven of the 13 SOIs filed for the Science Lab Initiative have been invited into the Program. The Joseph Case High School in Swansea and Saugus High School have requested removal of further consideration due to funding concerns.

Three of the 39 facilities invited into the Accelerated Repair Program have requested removal of further consideration due to funding concerns: Rowe Elementary School in Rowe, the John A. Parker Elementary School in New Bedford, and the Joseph Case Junior High School in Swansea.

Eligibility Period

There are six districts in the Eligibility Period. Two districts are seeking local funding and authorization within the next 60 days, and three of the six districts have secured funding. The remaining District, Bellingham, held a vote to appropriate Feasibility Study funds on May 24th, which failed. The MSBA has received the District's written request to confirm removal from the Eligibility Period.

An agreed-upon enrollment is a key pre-requisite for the MSBA to commence a Feasibility Study with a district. To begin the enrollment projection process, a district must file enrollment information utilizing the MSBA's online enrollment projection tool. Since the last report, two districts have completed the enrollment process.

Based upon the district's anticipated schedules for completion of the Eligibility Period requirements, staff expect that the remaining districts in Eligibility Period may be brought to the Board for Invitation to Feasibility Study at the January and April Board meetings. Staff also anticipates that as many as five districts may be invited to collaborate with the MSBA in the Eligibility Period process at upcoming Board Meetings.

Capital Pipeline

Consultant Selection

After the district has completed all Eligibility Period requirements and received a Board Invitation to Feasibility Study, the district procures an Owner's Project Manager ("OPM"). There are 12 districts in the Capital Pipeline who need to procure an OPM.

After a district has selected and executed a contract with an OPM, it selects a Designer utilizing either a local designer selection process for projects under \$5 million or the MSBA's Designer Selection Panel ("DSP") for projects over \$5 million. There are two districts in the Capital Pipeline who are in the process of procuring a Designer.

Feasibility Study

Once a district has procured an OPM and Designer and a Feasibility Study Agreement has been established, the district and its consultants must complete two Feasibility Study submittals, the Preliminary Design Program and the Preferred Schematic Report, prior to Board consideration to proceed into Schematic Design. Based on the most recent data and schedules provided to the MSBA by districts, the MSBA anticipates that six districts will present their preferred schematic designs to the Board at the upcoming January and April Board meetings.

Prior to consideration by the Board for Project Scope and Budget authorization, a district must submit a schematic design to the MSBA for review. Based on the most recent data and schedules provided to the MSBA by districts, the MSBA anticipates that nine districts will appear before the Board for Project Scope and Budget Agreement authorization at the upcoming January and April Board meetings.

Commissioning

Since the last report, the MSBA has assigned Commissioning Consultants to an additional seven projects as presented in the table below. The MSBA has executed 191 Commissioning Consultant contracts to date, totaling \$15.9 million. To date, 34 contracts have been completed.

District	School	Estimated Const. Cost (million)	Commissioning Consultant	Contract Amount
Blackstone Valley Regional	Blackstone Valley Regional Voc Tech HS - Science Lab Initiative	\$0.87	Horizon Engineering Associates, LLP	\$12,400
Melrose	Melrose HS - Science Lab Initiative	\$4.94	WSP Flack + Kurtz, Inc.	\$20,500
Holyoke	Holyoke Dean Technical HS - Science Lab Initiative	\$5.35	BVH Integrated Services	\$22,183
Weymouth	Seach ES - Accelerated Repair, Boilers	\$0.43	B2Q Associates, Inc.	\$12,600
Newburyport	Rupert A. Nock MS/Molin Upper ES	\$21.80	Fitzmeyer & Tocci Associates, Inc.	\$121,126
Southern Worcester County Regional	Bay Path Regional Voc Tech HS	\$58.20	RDK Engineers	\$187,139
West Bridgewater	West Bridgewater Middle-Senior HS	\$49.70	Cannon Design	\$105,937
Total		\$141.29 million	Total	\$481,885

Design Development

Once a district has secured local funding and has entered into a Project Funding Agreement with the MSBA, it enters the Design Development phase. Currently there are 13 Core Program Projects in Design Development with a total estimated construction cost of \$593.6 million:

Elementary School Districts

Newburyport (Bresnahan)
Webster
Williamsburg

Middle School Districts

Stoneham
Wakefield
Newburyport (Nock)

High School Districts

Assabet Valley Regional Technical
Concord-Carlisle Regional
Greenfield
Monomoy Regional
Southern Worcester Regional Technical
Southwick-Tolland-Granville Regional
West Bridgewater

Construction

When a district issues a Notice to Proceed, the project is advanced to the Construction Phase. Currently, there are 80 Projects in the Construction phase with a total estimated construction cost of \$3.0 billion: 33 Green Repair Projects, 45 Core Program Projects, and two Waitlist Projects. The 45 Core Program Projects have a total estimated construction cost of \$2.82 billion and are listed below.

Elementary School Districts	Middle and Middle/High School Districts	High School Districts
Andover Arlington Ashburnham-Westminster Regional Douglas Fairhaven Lexington Marblehead Somerville Springfield (Dryden) Westfield Weston Winchester	Burlington Douglas Fall River Hingham Hudson Medway North Reading Oxford Quincy Rockland Saugus Shrewsbury Sutton	<u data-bbox="1175 506 1414 533">Addition/Renovation</u> Danvers Dracut Leominster Lynnfield Methuen Norfolk County Agricultural Norton Southeastern Regional Voc/Tech <u data-bbox="1268 810 1321 837">New</u> Berlin-Boylston Regional Easthampton Essex/North Shore Regional Voc/Tech Longmeadow Maynard Wilmington <u data-bbox="1256 1056 1333 1083">Model</u> Duxbury East Bridgewater Franklin Marshfield Somerset-Berkley Regional West Springfield

Project Update:

Green Repair – Schedule Extension Update

Six of the 169 Green Repair Projects will not meet their anticipated construction completion deadline in 2012. Schedule delays can be attributed to bid protests, lead time for windows, and construction delays on site.

The MSBA granted each district a conditional extension to its Project Funding Agreement pending compliance with the following stipulations:

- The district must submit a detailed, revised construction timeline showing how the work will be completed at each school by August 30, 2013 at the latest.
- An Amendment to the Project Funding Agreement between the MSBA and the district must be executed to include the updated project schedule.
- Any costs that may result from the district's requested extension of the construction schedule will be the sole responsibility of the district and are categorically ineligible for reimbursement by the MSBA.

Each of the projects below has a revised construction schedule and will be complete by the beginning of the 2013-2014 school year. In no event has the extended schedule resulted in an increase to the estimated maximum Total Facilities Grant as authorized by the Board.

District	School	Scope	Original Construction Completion Date	Updated Construction Completion Date	Reason for Schedule Extension
Brockton	Brockton High School	Windows and Roof	31-Dec-12	30-Aug-13	Construction fell behind schedule and the District did not want work being done in an occupied building. The roof work is complete.
Haverhill	Consentino Middle School	Windows and Boiler	31-Dec-12	31-May-13	Bid protests and lead times caused the window project to extend beyond the 2012 construction deadline. The boiler project is complete.
Haverhill	John G. Whittier Middle School	Windows	31-Dec-12	31-May-13	Bid protests and lead times caused the window project to extend beyond the 2012 construction deadline.
Lowell	Moody Elementary School	Windows	15-Aug-12	30-Aug-13	Construction fell behind schedule and the District did not want work being done in an occupied building.
Lowell	Washington Elementary School	Windows	15-Aug-12	30-Aug-13	Construction fell behind schedule and the District did not want work being done in an occupied building.
Wachusett Regional	Thomas Prince Elementary School	Windows and Boiler	23-Mar-12	30-Apr-13	The district issued a change order to replace an existing skylight and due to lead times the work cannot be done until Spring 2013. The window and boiler work is complete.


Green Repair - Total Project Budget Update

Upon receiving Project Scope and Budget Approval from the Board, the MSBA and participating districts enter into a Project Funding Agreement that establishes the Total Project Budget and the estimated maximum Total Facilities Grant for an approved project. Of the 169 grants authorized by the Board for the Green Repair Program, 11 projects have increased their Total Project Budgets due to acceptance of construction bids higher than the project estimates, or as a result of change orders issued on the project. In no event has the increase in budget resulted in an increase to the estimated maximum Total Facilities Grant as authorized by the Board. Please note that staff reported on the budget increases for six of the projects shaded and shown below at previous Board meetings (Brockton, Hancock ES and West Junior HS; Florida; Lexington; Narragansett; and Pentucket).

District	School Name	Scope	Project Funding Agreement		PFA Bid Amendment		Reason for Increase to Total Project Budget
			Total Project Budget	Total Maximum Facilities Grant	Total Project Budget	Total Maximum Facilities Grant	
Green Repair Program							
Arlington	M. Norcross Stratton Elementary School	Roof, Window, Boiler	\$2,445,395	\$739,336	\$2,445,395	\$739,336	Change Orders exhausted the construction contingency.
Brockton	Hancock Elementary School	Roof	\$2,292,164	\$1,814,937	\$2,422,742	\$1,814,937	District elected to accept the base bid that was higher than the approved budget. District appropriated additional funds to support overage.
Brockton	West Junior High School	Roof	\$2,742,386	\$2,171,001	\$3,069,905	\$2,171,001	District elected to accept the base bid that was higher than the approved budget. District appropriated additional funds to support overage.
Fitchburg	South Street Elementary School	Boiler	\$701,186	\$560,949	\$705,391	\$501,079	Change Orders exhausted the construction contingency.
Florida	Gabriel Abbott Memorial School	Roof	\$380,310	\$213,172	\$389,422	\$188,804	Project included \$80,153 in Change Orders that offset bid savings and exhausted the construction contingency.
Hancock	Hancock Elementary School	Roof/ HVAC	\$277,450	\$125,740	\$400,805	\$125,740	District elected to accept the base bids in Phases 2 and 3 that were higher than the approved budget. District needs to appropriate the overage.
Lexington	Lexington High School	Roof	\$1,122,890	\$381,221	\$1,197,444	\$381,221	District elected to accept base bid and alternates. District appropriated additional funds to support overage.
Narragansett Regional	Phillipston Memorial Elementary School	Boiler	\$143,225	\$85,712	\$161,232	\$83,275	District elected to accept the base bid that was higher than the approved budget. District appropriated additional funds to support overage.
Pentucket Regional	Dr. John C. Page Elementary School	Roof, Window, Boiler	\$3,148,424	\$1,618,920	\$3,272,630	\$1,618,920	District elected to accept the base bid that was higher than the approved budget. District appropriated additional funds to support overage.
Reading	Birch Meadow ES	Window	\$735,846	\$347,393	\$787,640	\$347,393	District elected to accept the base bid that was higher than the approved budget. Town Accountant certified that the FY2011 School Committee Operating Budget had an appropriation and encumbrance for the additional costs of the project.
Westfield	Westfield Vocational Technical High School	Roof, Window, Boiler	\$8,442,762	\$5,296,989	\$8,751,795	\$5,296,989	District elected to accept the base bid that was higher than the approved budget. District appropriated additional funds to support overage.


Status of Green Repair Program

169 projects participating in the Green Repair Program have received authorization to enter into a PFA, totaling \$366,647,226 in Total Project Costs and \$222,885,258 in MSBA grants.

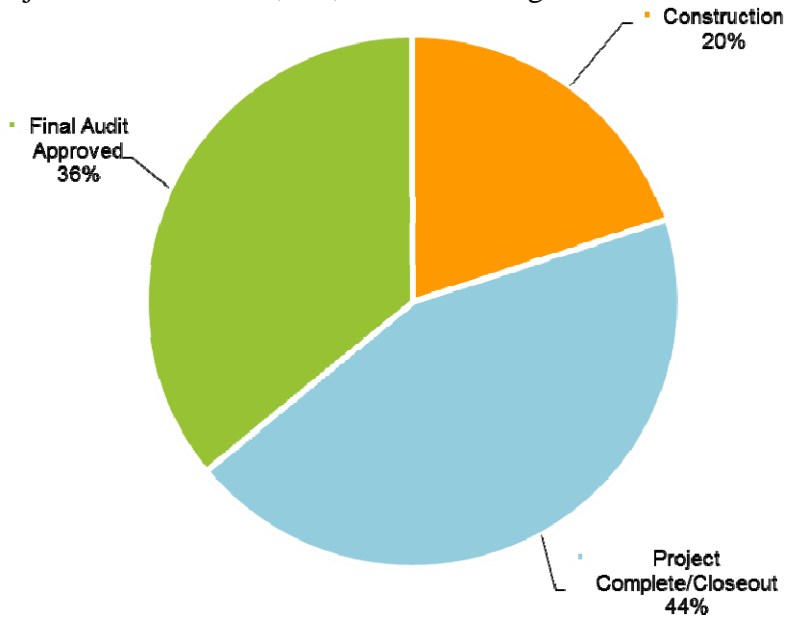

Status of Accelerated Repair Program

Currently there are a total of 24 districts, representing 36 projects, in the Accelerated Repair Program. Thirty-four projects are under contract with consultants and have advanced into the preferred schematic or project scope and budget phases. At the November 14th meeting of the Board of Directors, MSBA staff will be recommending a Project Funding Agreement (“PFA”) for 11 districts, representing 13 projects totaling \$21,115,474 in MSBA Total Project Costs. With the Board’s approval, 14 projects will be authorized to enter into a PFA, totaling \$21,665,270 in Total Project Costs and \$13,196,074 in MSBA Total Facilities Grant funding.

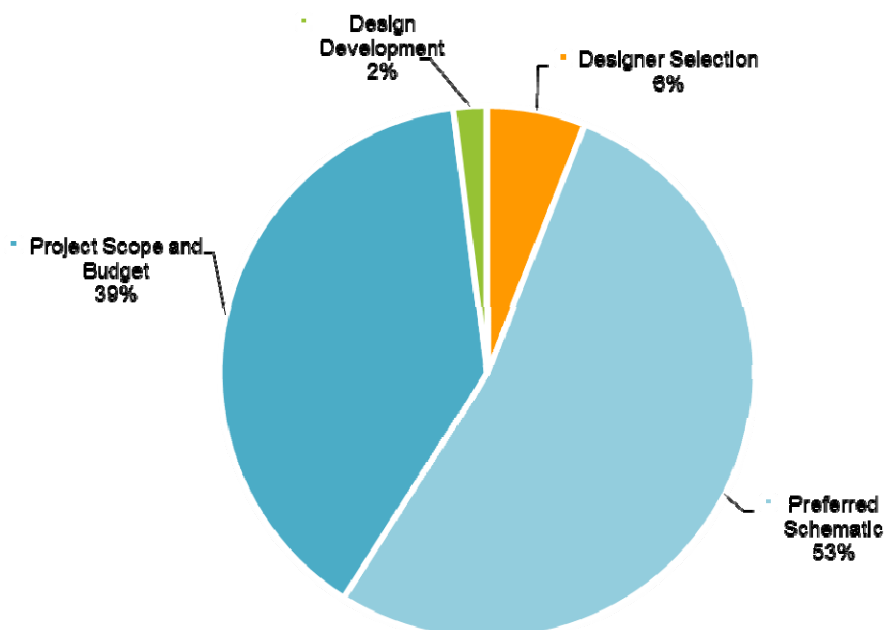

You are Currently Viewing Active Projects.

Date of Report: 10/24/12

Active Projects: 330

MSBA ID	District	School	Phase	Project Scope	Procurement Type	OPM	Designer	Cx_Company	CM/GC
200800010405	Abington	Frolio Middle School	OPM Selection			Knight, Bagge & Anderson Inc.	-		-
201100010015G	Abington	Woodsdale	Project Complete/Substantial Completion	Repair - Accelerated	DBB	RF Walsh Collaborative Partners	Gale Associates, Inc.	Russo Barr Associates, Inc.	Lockheed Window Corporations
201000020020G	Acton	C. T. Douglas Elementary School	Final Audit Approved Project	Repair - Accelerated	DBB	-	CBI Consulting, Inc.		Gibson Roofs, Inc.
200806030305	Adams-Cheshire	Adams Memorial Middle School	Project Complete/Substantial Completion	Addition / Renovation	CM@R	URS Corporation	Tessier Associates, Inc.	Strategic Building Solutions, LLC	Gilbane Building Company
201100050405G	Agawam	Agawam Junior/Senior High	Project Complete/Substantial Completion	Repair - Accelerated	DBB	Municipal Building Consultants, Inc.	CSS Architects Incorporated	Building Enclosure Associates	-
201106050405G	Amherst-Pelham	Amherst Regional Middle School	Project Complete/Substantial Completion	Repair - Accelerated	DBB	Strategic Building Solutions, LLC	Bradley Architects, Inc.	Russo Barr Associates, Inc.	R&R Window Contractors, Inc.
201100090310G	Andover	Andover West Middle	Closeout	Repair - Accelerated	DBB	Skanska USA Building, Inc	Russo Barr Associates, Inc.	Simpson Gumpertz & Heger Inc.	Eagle Rivet Roof Services Corporation
200800090003	Andover	Bancroft Elementary School	Construction	New Construction	CM@R	Dore & Whittier Management Partners, Inc.	Symmes Maini & McKee Associates, Inc.	Sebesta Blomberg & Associates, Inc.	Skanska USA Building, Inc.
201100100055G	Arlington	M Norcross Stratton	Closeout	Repair - Accelerated	DBB	PMA Construction Services	Turowski2 Architecture, Inc.		Federal Construction Corp. Unicon Inc.
200900100050	Arlington	Thompson Elementary School	Construction	New Construction	DBB	PMA Construction Services	HMFH Architects, Inc.	Consulting Engineering Services, LLC	G & R Construction, Inc.
200806100025	Ashburnham-Westminster	John R. Briggs Elementary School	Construction	New Construction	CM@R	STV Incorporated	Lamoureux Pagano & Associates, Inc.	Foreman Building Commissioning, LP	Consigli Construction Company, Inc.
200908010605	Assabet Valley	Assabet Valley Regional Technical High School	Design Development		DBB	Strategic Building Solutions, LLC	Design Partnership of Cambridge, Inc.	Symmes, Maini & McKee Associates	-
200906150020	Athol-Royalston	Riverbend School	Feasibility Study	Repair- Accelerated		Symmes Maini & McKee Associates, Inc.	Mount Vernon Group Architects, Inc.		-
201200160001	Attleboro	A. Irvin Studley Elementary School	Schematic Design	Repair - Accelerated					
200800170305	Auburn	Auburn Middle School	Schematic Design	New Construction		Skanska USA Building, Inc	Lamoureux Pagano & Associates, Inc.		-
9999	Ayer-Shirley	Ayer-Shirley Regional Middle/High School	Project Vote Pending	Addition / Renovation		Dore and Whittier Architects, Inc.	Symmes Maini & McKee Associates, Inc.		-
201100200005G	Barnstable	West Barnstable Elementary School	Project Complete/Substantial Completion	Repair - Accelerated	DBB	PMA Construction Services	Gale Associates, Inc.	CBI Consulting Inc.	Paul J. Rogan Co., Inc.
201100250315G	Bellingham	Bellingham Memorial Middle School	Final Audit Approved	Repair - Accelerated	DBB	Daedalus Projects Inc	Richard D. Kimball Company, Inc.	WSP Flack + Kurtz	General Air Conditioning & Heating, Inc.
201200250009	Bellingham	Clara Macy Elementary	Eligibility Period			-	-		-
200800260035	Belmont	Roger Wellington Elementary School	Closeout	New Construction	CM@R	PMA Construction Services	Jonathan Levi Architects LLC	Strategic Building Solutions, LLC	Skanska USA Building, Inc.
201006180505	Berkshire Hills	Monument Mountain Regional High School	Feasibility Study			Strategic Building Solutions, LLC	Symmes Maini & McKee Associates, Inc.		-
200806200505	Berlin-Boylston	Tahanto Regional High School	Construction	New Construction	DBB	PMA Construction Services	HMFH Architects, Inc.	Strategic Building Solutions, LLC	CTA Construction Co., Inc.
200800300505	Beverly	Beverly HS	Closeout Project	Addition / Renovation		HEERY	Mount Vernon Group Architects, Inc.		CTA Construction Co., Inc.
200800310015	Billerica	Parker Elementary School	Project Complete/Substantial Completion	New Construction	DBB	Joslin, Lesser + Associates Inc.	Symmes Maini & McKee Associates, Inc.	Sebesta Blomberg & Associates, Inc.	CTA Construction Co., Inc. RS Hurford

You are Currently Viewing Active Projects.

Date of Report: 10/24/12

Active Projects: 330

MSBA ID	District	School	Phase	Project Scope	Procurement Type	OPM	Designer	Cx_Company	CM/GC
201100310505G	Billerica	Memorial High School	Project Complete/Substantial Completion	Repair		Municipal Building Consultants, Inc.	Knight, Bagge & Anderson, Inc.	Building Enclosure Associates	
201108050605G	Blackstone Valley Reg	Blackstone Valley	Final Audit Approved	Repair - Accelerated	DBB	Strategic Building Solutions, LLC	Reinhardt Associates, Inc.	Cannon Design	Greenwood Industries, Inc.
201208050605	Blackstone Valley Reg	Blackstone Valley	Design Development	Science Lab		Compass Project Management, Inc.	Flansburgh Associates, Inc.		-
201206220015	Blackstone Valley - Millville	A.F. Maloney Elementary School	Schematic Design	Repair- Accelerated					
201206220008	Blackstone Valley - Millville	J.F. Kennedy Elementary School	Schematic Design	Repair- Accelerated					
201206220505	Blackstone Valley - Millville	Regional High School	Schematic Design	Repair - Accelerated				Cannon Design	
201100350430G	Boston	Clarence R Edwards Middle School	Closeout	Repair - Accelerated	DBB	Daedalus Projects Inc	BLW Engineers, Inc.	Rist-Frost-Shumway Engineering, P.C.	-
201100350522G	Boston	Excel High School	Construction	Repair - Accelerated	DBB	Daedalus Projects Inc	BLW Engineers, Inc.	Simpson Gumpertz & Heger Inc.	-
201000350074	Boston	Henry Dearborn Middle School	Designer Selection			Compass Project Management, Inc.	-		-
201100350183G	Boston	Joseph Lee Elementary School	Closeout	Repair - Accelerated	DBB	Daedalus Projects Inc	BLW Engineers, Inc.	Simpson Gumpertz & Heger Inc.	Gale Associates, Inc.
201000350565	Boston	Quincy Upper School	Feasibility Study			Maureen Anderson - City Employee	HMFH Architects, Inc.		-
201100350425G	Boston	Thomas A Edison Jr High School	Closeout	Repair - Accelerated	DBB	Daedalus Projects Inc	BLW Engineers, Inc.	Simpson Gumpertz & Heger Inc.	-
201100350445G	Boston	Washington Irving Middle School	Closeout	Repair - Accelerated	DBB	Daedalus Projects Inc	Gale Associates, Inc.	Simpson Gumpertz & Heger Inc.	-
201000400033G	Braintree	Archie T Morrison Elementary School	Final Audit Approved	Repair - Accelerated	DBB	RF Walsh Collaborative Partners	Habeeb & Associates Architects, Inc.	Cannon Design	Modern Glass & Aluminum, Inc.
201000400505G	Braintree	Braintree High School	Final Audit Approved	Repair - Accelerated	DBB	RF Walsh Collaborative Partners	Habeeb & Associates Architects, Inc.	Cannon Design	Gibson Roofs, Inc.
201000400305G	Braintree	East Middle School	Final Audit Approved	Repair - Accelerated	DBB	RF Walsh Collaborative Partners	Habeeb & Associates Architects, Inc.	Cannon Design	Modern Glass & Aluminum, Inc.
201000400015G	Braintree	Highlands Elementary School	Final Audit Approved	Repair - Accelerated	DBB	RF Walsh Collaborative Partners	Habeeb & Associates Architects, Inc.	Cannon Design	Modern Glass & Aluminum, Inc.
201000400005G	Braintree	Hollis Elementary School	Final Audit Approved	Repair - Accelerated	DBB	RF Walsh Collaborative Partners	Habeeb & Associates Architects, Inc.	Cannon Design	Modern Glass & Aluminum, Inc.
201206250320	Bridgewater-Raynham	Bridgewater Middle School	Schematic Design	Repair - Accelerated					
201206250020	Bridgewater-Raynham	L.B. Merrill Elementary School	Schematic Design	Repair - Accelerated					
201206250050	Bridgewater-Raynham	Laliberte Elementary School	Schematic Design	Repair - Accelerated					
201100440505G	Brockton	Brockton High School	Construction	Repair - Accelerated	DBB	Skanska USA Building, Inc	CSS Architects Incorporated	Simpson Gumpertz & Heger Inc.	Gibson Roofs, Inc.
201100440110G	Brockton	Downey Elementary School	Project Complete/Substantial Completion	Repair - Accelerated	DBB	Skanska USA Building, Inc	CSS Architects Incorporated	Simpson Gumpertz & Heger Inc.	Built-up Roofing Systems LLC
201100440405G	Brockton	East Junior High School	Closeout	Repair - Accelerated	DBB	Skanska USA Building, Inc	CSS Architects Incorporated	Rist-Frost-Shumway Engineering, P.C.	Reliable Roofing and Sheet Metal, LLC
201100440023G	Brockton	Edgar B Davis	Project Complete/Substantial Completion	Repair - Accelerated	DBB	Skanska USA Building, Inc	CSS Architects Incorporated	Simpson Gumpertz & Heger Inc.	Reliable Roofing and Sheet Metal, LLC
201100440045G	Brockton	Hancock Elementary School	Closeout	Repair - Accelerated	DBB	Skanska USA Building, Inc	CSS Architects Incorporated	Simpson Gumpertz & Heger Inc.	Reliable Roofing and Sheet Metal, LLC

You are Currently Viewing Active Projects.

Date of Report: 10/24/12

Active Projects: 330

MSBA ID	District	School	Phase	Project Scope	Procurement Type	OPM	Designer	Cx Company	CM/GC
201100440410G	Brockton	North Junior High School	Closeout	Repair - Accelerated	DBB	Skanska USA Building, Inc	CSS Architects Incorporated	Rist-Frost-Shumway Engineering, P.C.	Constructors, LLC Built-up Roofing Systems LLC
201100440078G	Brockton	Oscar F Raymond K-8	Project Complete/Substantial Completion	Repair - Accelerated	DBB	Skanska USA Building, Inc	CSS Architects Incorporated	Simpson Gumpertz & Heger Inc.	Reliable Roofing and Sheet Metal, LLC
201100440420G	Brockton	West Junior High School	Closeout	Repair - Accelerated	DBB	Skanska USA Building, Inc	CSS Architects Incorporated	Simpson Gumpertz & Heger Inc.	Reliable Roofing and Sheet Metal, LLC
201100450005G	Brookfield	Brookfield Elementary School	Construction	Repair - Accelerated	DBB	Diversified Project Management	Habeeb & Associates Architects, Inc.	Cannon Design	Northeast Energy Control Systems
201100460015	Brookline	Edward Devotion	Eligibility Period						
201000460025	Brookline	Heath Elementary School	Project Complete/Substantial Completion	Addition / Renovation	DBB	Town of Brookline Building Department	Miller Dyer Spears Inc.	Consulting Engineering Services, LLC	Nauset Construction Corporation
200800460045	Brookline	John D. Runkle School	Project Complete/Substantial Completion	Addition / Renovation	DBB	Town of Brookline Building Department	Design Partnership of Cambridge, Inc.	Consulting Engineering Services, LLC	G & R Construction, Inc.
201000480303	Burlington	Marshall Simonds Middle School	Construction	Addition / Renovation	DBB	Construction Monitoring Services, Inc.	Knight, Bagge & Anderson, Inc.	RDK Engineers	CTA Construction Co., Inc.
200800480015	Burlington	Memorial Elementary School	Closeout	New Construction	DBB	Construction Monitoring Services, Inc.	Knight, Bagge & Anderson, Inc.	Consulting Engineering Services, LLC	CTA Construction Co., Inc.
W20024323	Cambridge	Cambridge Rindge and Latin High School	Closeout	Addition / Renovation	DBB	-	HMFH Architects, Inc.		W. T. Rich Company Inc.
201200500012	Canton	Lt. Peter M. Hansen	Schematic Design	Repair - Accelerated					
201200500305	Canton	William H. Galvin Middle School	Schematic Design	Repair - Accelerated					
201008150605G	Cape Cod Region Voc Tech	Cape Cod Region Voc Tech	Project Complete/Substantial Completion	Repair - Accelerated	DBB	URS Corporation	Garcia Galuska DeSousa Consulting Engineers Inc.	Fitzmeyer & Tocci Associates, Inc.	-
200800510025	Carlisle	Carlisle School	Project Complete/Substantial Completion	Addition / Renovation	DBB	Daedalus Projects Inc	HMFH Architects, Inc.	Horizon Engineering Associates, LLP	H.V. Collins Co., Inc.
201106350025G	Central Berkshire	Craneville Elementary School	Project Complete/Substantial Completion	Repair - Accelerated	DBB	Daedalus Projects Inc	Bradley Architects, Inc.	Strategic Building Solutions, LLC	Titan Roofing, Inc.
201106350035G	Central Berkshire	Kittredge Elementary School	Project Complete/Substantial Completion	Repair - Accelerated	DBB	Daedalus Projects Inc	Bradley Architects, Inc.	Strategic Building Solutions, LLC	A.J. Schnopp Jr., Construction, Inc. Alpha Contracting Associates, Inc.
201100560030G	Chelmsford	Byam Elementary School	Closeout	Repair - Accelerated	DBB	Vertex Construction Services	Russo Barr Associates, Inc.	Simpson Gumpertz & Heger Inc.	S.O.M. Construction Ent., Inc.
201100560505G	Chelmsford	Chelmsford High School	Closeout	Repair - Accelerated	DBB	Vertex Construction Services	Russo Barr Associates, Inc.	Simpson Gumpertz & Heger Inc.	Lockheed Window Corporations
200800570050	Chelsea	Clark Avenue School	OPM Selection			-	-		-
200900610021	Chicopee	Chicopee Academy	Feasibility Study			Arcadis	Caolo & Bieniek Associates, Inc.		-
200906400505	Concord-Carlisle	Concord-Carlisle Regional High School	Design Development	New Construction	CM@R	KV Associates, Inc.	OMR Architects, Inc.	Strategic Building Solutions, LLC	Turner Construction Company
200800710505	Danvers	Danvers High School	Construction	Addition / Renovation	DBB	Construction Monitoring Services, Inc.	DiNisco Design Partnership, Limited	Turner Facilities Management Solutions	Bacon Construction Co, Inc.
201100720040G	Dartmouth	James M. Quinn Elementary School	Closeout	Repair - Accelerated	DBB	Vertex Construction Services	Russo Barr Associates, Inc.	Gale Associates, Inc.	Capeway Roofing Systems, Inc.

You are Currently Viewing Active Projects.

Date of Report: 10/24/12

Active Projects: 330

MSBA ID	District	School	Phase	Project Scope	Procurement Type	OPM	Designer	Cx Company	CM/GC
200800730010	Dedham	Avery Elementary School	Project Complete/Substantial Completion	New Construction	CM@R	Construction Monitoring Services, Inc.	Dore & Whittier Architects, Inc.	WSP Flack + Kurtz	Consigli Construction Company, Inc.
201006450005G	Dennis-Yarmouth	Ezra Baker Elementary School	Construction	Repair - Accelerated	DBB	STV Incorporated	Knight, Bagge & Anderson, Inc.	CBI Consulting Inc.	Antonelli Construction Co., Inc.
200800770010	Douglas	Douglas Elementary School	Construction	New Construction		HEERY	DiNisco Design Partnership, Limited	Consulting Engineering Services, LLC	CTA Construction Co., Inc.
200800770100G	Douglas	Douglas Intermediate Elementary School	Construction	Repair - Accelerated	DBB	HEERY	DiNisco Design Partnership, Limited	Consulting Engineering Services, LLC	CTA Construction Co., Inc.
200800790505	Dracut	Dracut Senior High School	Construction	Addition / Renovation	DBB	RF Walsh Collaborative Partners	Mount Vernon Group Architects, Inc.	RDK Engineers	-
201000820505	Duxbury	Duxbury High School	Construction	New Construction	CM@R	KV Associates, Inc.	Mount Vernon Group Architects, Inc.	WSP Flack + Kurtz	Dimeo Construction Company
200900830505	East Bridgewater	East Bridgewater High School	Construction	New Construction	DBB	RF Walsh Collaborative Partners	Ai3 Architects LLC	Foreman Building Commissioning, LP	Fontaine Brothers, Inc.
200800860505	Easthampton	Easthampton High School	Construction	New Construction	DBB	Strategic Building Solutions, LLC	Caolo & Bieniek Associates, Inc.	Consulting Engineering Services, LLC	Fontaine Brothers, Inc.
201200880405	Easton	Easton Junior High School	Project Scope & Budget	Repair - Accelerated		PMA Construction Services	Russo Barr Associates, Inc.		-
200809130705	Essex Agr Tech	Essex Agricultural and Technical High School	Construction	New Construction	CM@R	PMA Construction Services	Design Partnership of Cambridge, Inc.	Turner Facilities Management Solutions	Gilbane Building Company
200800940020	Fairhaven	Rogers Elementary School	Construction	New Construction	DBB	Daedalus Projects Inc	HMFH Architects, Inc.	Consulting Engineering Services, LLC	-
200900950315	Fall River	James Madison Morton Middle School	Construction	New Construction	DBB	Maguire Group Inc.	Mount Vernon Group Architects, Inc.	Sebesta Blomberg & Associates, Inc.	J & J Contractors, Inc.
201100960005G	Falmouth	East Falmouth Elementary School	Final Audit Approved	Repair - Accelerated	DBB	No OPM	Keenan and Kenny Architects, Ltd.	Gale Associates, Inc.	Meadows Construction Company LLC
201100960030G	Falmouth	North Falmouth Elementary School	Final Audit Approved	Repair - Accelerated	DBB	No OPM	Keenan and Kenny Architects, Ltd.	Gale Associates, Inc.	Meadows Construction Company LLC
201100970505G	Fitchburg	Fitchburg High School	Closeout	Repair - Accelerated	DBB	Compass Project Management, Inc.	BLW Engineers, Inc.	RDK Engineers	-
201000970025G	Fitchburg	Goodrich Kindergarten	Closeout	Repair - Accelerated	DBB	Compass Project Management, Inc.	BLW Engineers, Inc.	RDK Engineers	CAM HVAC & Construction, Inc.
200900970048G	Fitchburg	Memorial Intermediate	Closeout	Repair - Accelerated	DBB	Compass Project Management, Inc.	BLW Engineers, Inc.	RDK Engineers	E. Amanti & Sons, Inc.
201100970048G	Fitchburg	Memorial Intermediate	Construction	Repair - Accelerated	DBB	Compass Project Management, Inc.	Knight, Bagge & Anderson, Inc.	Simpson Gumpertz & Heger Inc.	Lockheed Window Corporations
201100970043G	Fitchburg	Reingold Elementary School	Closeout	Repair - Accelerated	DBB	Compass Project Management, Inc.	Knight, Bagge & Anderson, Inc.	RDK Engineers	Lockheed Window Corporations
200900970043G	Fitchburg	Reingold Elementary School	Closeout	Repair - Accelerated	DBB	Compass Project Management, Inc.	BLW Engineers, Inc.	Simpson Gumpertz & Heger Inc.	E. Amanti & Sons, Inc.
200900970060G	Fitchburg	South Street Elementary	Closeout	Repair - Accelerated	DBB	Compass Project Management, Inc.	BLW Engineers, Inc.	RDK Engineers	CAM HVAC & Construction, Inc.
201100970060G	Fitchburg	South Street Elementary	Construction	Repair - Accelerated	DBB	Compass Project Management, Inc.	Knight, Bagge & Anderson, Inc.	Simpson Gumpertz & Heger Inc.	Lockheed Window Corporations
200800990505	Foxborough	Foxborough High School	Project Complete/Substantial Completion	Repair - Major	DBB	Construction Monitoring Services, Inc.	Kaestle Boos Associates, Inc.	Consulting Engineering Services, LLC	CTA Construction Co., Inc.
201101000045G	Framingham	Mary E Stapleton Elementary School	Project Complete/Substantial Completion	Repair - Accelerated	DBB	Bargmann, Flendrie & Archetype, Inc.	Russo Barr Associates, Inc.	CBI Consulting Inc.	-
200901010505	Franklin	Franklin High School	Construction	New Construction	DBB	Daedalus Projects Inc	Ai3 Architects LLC	Consulting Engineering Services, LLC	-
201101030001G	Gardner	Elm Street School	Final Audit Approved	Repair - Accelerated	DBB	P3 Inc.	Knight, Bagge & Anderson, Inc.	Building Enclosure Associates	Reliable Roofing and Sheet Metal, LLC

You are Currently Viewing Active Projects.

Date of Report: 10/24/12

Active Projects: 330

MSBA ID	District	School	Phase	Project Scope	Procurement Type	OPM	Designer	Cx Company	CMGC
201101030505G	Gardner	Gardner High School	Final Audit Approved	Repair - Accelerated	DBB	P3 Inc.	Knight, Bagge & Anderson, Inc.		Reliable Roofing and Sheet Metal, LLC
201201030505	Gardner	Gardner High School	Project Scope & Budget	Science Lab		Pinck & Co., Inc.	Lamoureux Pagano & Associates, Inc.	Building Enclosure Associates	-
201201030405	Gardner	Gardner Middle School	Project Scope & Budget	Repair - Accelerated		Leftfield, LLC	Richard D. Kimball Company, Inc.		
200801030020G	Gardner	Waterford Street Primary	Final Audit Approved	Repair - Accelerated	DBB	P3 Inc.	Knight, Bagge & Anderson, Inc.		Reliable Roofing and Sheet Metal, LLC
200901050010	Georgetown	Penn Brook Elementary School	Approved Project Vote Pending	New Construction		Municipal Building Consultants, Inc.	Drummey Rosane Anderson, Inc.		-
200801050505	Georgetown	Georgetown Middle/High School	Eligibility Period						
201101070010G	Gloucester	Beeman Memorial School	Final Audit Approved	Repair - Accelerated	DBB	Knight, Bagge & Anderson Inc.	CGKV Architects, Inc.	Russo Barr Associates, Inc.	Built-up Roofing Systems LLC
201101070020G	Gloucester	East Gloucester Elementary School	Final Audit Approved	Repair - Accelerated	DBB	Knight, Bagge & Anderson Inc.	CGKV Architects, Inc.	Russo Barr Associates, Inc.	Stanley Roofing Company, Inc.
201101070042G	Gloucester	Plum Cove Elementary School	Final Audit Approved	Repair - Accelerated	DBB	Knight, Bagge & Anderson Inc.	CGKV Architects, Inc.	Russo Barr Associates, Inc.	Built-up Roofing Systems LLC
201101070305G	Gloucester	Ralph B O'Maley Middle	Final Audit Approved	Repair - Accelerated	DBB	Knight, Bagge & Anderson Inc.	CGKV Architects, Inc.	Russo Barr Associates, Inc.	Titan Roofing, Inc.
201101070045G	Gloucester	Veterans Memorial	Final Audit Approved	Repair - Accelerated	DBB	Knight, Bagge & Anderson Inc.	CGKV Architects, Inc.	Russo Barr Associates, Inc.	Stanley Roofing Company, Inc.
200901070050	Gloucester	West Parish Elementary School	OPM Selection			Knight, Bagge & Anderson Inc.	-		-
200801100505	Grafton	Grafton Memorial Senior	Project Complete/Substantial Completion	New Construction	CM@R	Joslin, Lesser + Associates Inc.	Symmes Maini & McKee Associates, Inc.		Dimeo Construction Company
201101100505G	Grafton	Grafton Memorial Senior	Project Complete/Substantial Completion	Repair - Accelerated	DBB	URS Corporation	CGKV Architects, Inc.	Horizon Engineering Associates, LLP	S.O.M. Construction Ent., Inc.
201101100005G	Grafton	South Grafton Elementary	Project Complete/Substantial Completion	Repair - Accelerated	DBB	URS Corporation	CGKV Architects, Inc.	Horizon Engineering Associates, LLP	AAlanco Service Corporation
201108230605	Greater Lawrence RVT	Greater Lawrence Reg Voc Tech	Designer Selection	Repair - Major		Vertex Construction Services	-		-
200908280605	Greater Lowell Voc Tec	Greater Lowell Regional Technical High School	Approved Project Vote Pending	Repair - Major		HEERY	Knight, Bagge & Anderson, Inc.		-
201008250605	Greater New Bedford	Vocational Technical High School	Approved Project Vote Pending	Addition / Renovation		Construction Monitoring Services, Inc.	Drummey Rosane Anderson, Inc.		-
201101140025G	Greenfield	Four Corners	Construction	Repair - Accelerated	DBB	P3 Project Planning	Tighe & Bond, Inc.	Strategic Building Solutions, LLC	Five Star Building Corp.
200901140505	Greenfield	Greenfield High School	Design Development	New Construction	DBB	Construction Monitoring Services, Inc.	Dore & Whittier Architects, Inc.	BVH Integrated Services, Inc.	-
201206730305	Groton-Dunstable	Groton Dunstable Regional Middle School	Project Scope & Budget	Repair - Accelerated		Collaborative Partners	ICON architecture, inc.		-
201101170505G	Hadley	Hopkins Academy	Closeout	Repair - Accelerated	DBB	Strategic Building Solutions, LLC	CCS Presentation Systems	Russo Barr Associates, Inc.	-
201206750010	Hamilton-Wenham	Cutler School	Project Scope & Budget	Repair - Accelerated					
200806800505	Hampden-Wilbraham	Minnechaug Regional High School	Project Complete/Substantial Completion	New Construction	DBB	Pinnacle One, Inc.	Mount Vernon Group Architects, Inc.	Horizon Engineering Associates, LLP	Fontaine Brothers, Inc.
201001210005G	Hancock	Hancock Elementary School	Construction	Repair - Accelerated	DBB	-	Westall Architects		Salco Construction Company, Inc.
200801220505	Hanover	Hanover High School	Closeout	New Construction	DBB	PMA Construction Services	HMFH Architects, Inc.	Horizon Engineering Associates, LLP	Callahan, Inc.

You are Currently Viewing Active Projects.

Date of Report: 10/24/12

Active Projects: 330

MSBA ID	District	School	Phase	Project Scope	Procurement Type	OPM	Designer	Cx_Company	CM/GC
201201280035	Haverhill	Caleb Dustin Hunking	OPM Selection			-	-		-
201101280100G	Haverhill	Consentino Middle School	Construction	Repair - Accelerated	DBB	Vertex Construction Services	CSS Architects Incorporated	RDK Engineers Russo Barr Associates, Inc.	
	Haverhill	High School	Closeout						
201101280085G	Haverhill	John G Whittier Middle School	Construction	Repair - Accelerated	DBB	Vertex Construction Services	CSS Architects Incorporated	Russo Barr Associates, Inc.	-
201101280075G	Haverhill	Tilton Elementary School	Construction	Repair - Accelerated	DBB	Vertex Construction Services	CSS Architects Incorporated	Russo Barr Associates, Inc.	-
201101280080G	Haverhill	Walnut Square Elementary School	Construction	Repair - Accelerated	DBB	Vertex Construction Services	CSS Architects Incorporated	RDK Engineers Russo Barr Associates, Inc.	-
201001310410	Hingham	Hingham Middle School	Construction	New Construction	DBB	Knight, Bagge & Anderson Inc.	Ai3 Architects LLC	Foreman Building Commissioning, LP	Brait Builders Corp.
200801330505	Holbrook	Holbrook Junior-Senior High School	OPM Selection			-	-		-
W20034396	Holyoke	Holyoke High School	Closeout	Repair - Major	DBB	-	Design Partnership of Cambridge, Inc.		-
201201370605	Holyoke	Wm J Dean Voc Tech High	Project Scope & Budget	Science Lab		Skanska USA Building, Inc	Kaestle Boos Associates, Inc.		-
200801410410	Hudson	John F. Kennedy Middle School	Construction	New Construction	DBB	PMA Construction Services	OMR Architects, Inc.	WSP Flack + Kurtz	Bacon-Agostini Construction Joint Venture
200801530505	Leominster	Leominster High School	Construction	Addition / Renovation	CM@R	Daedalus Projects Inc	Lamoureux Pagano & Associates, Inc.	Horizon Engineering Associates, LLP	S.O.M. Construction Ent., Inc.
201201530007	Leominster	Fall Brook	Schematic Design	Repair - Accelerated					
201201530010	Leominster	Southeast School	Schematic Design	Repair - Accelerated					
201101540005G	Leverett	Leverett Elementary School	Construction	Repair - Accelerated	DBB	Potomac Capital Advisors	DiMarinisi & Wolfe Architects Urban Designers	Russo Barr Associates, Inc.	-
201101550010E	Lexington	Joseph Estabrook Elementary School	Construction	New Construction		RF Walsh Collaborative Partners	DiNisco Design Partnership, Limited	BVH Integrated Services, Inc.	-
200901570025	Lincoln	Lincoln School	Approved Project Vote Pending	Addition / Renovation		Skanska USA Building, Inc	OMR Architects, Inc.		-
200801590505	Longmeadow	Longmeadow High School	Construction	New Construction	CM@R	Joslin, Lesser + Associates Inc.	OMR Architects, Inc.	Foreman Building Commissioning, LP	Gilbane Building Company
201101600505G	Lowell	Lowell High School	Construction	Repair - Accelerated	DBB	NETCO Construction Project Managers, Inc.	ICON architecture, inc.	Building Enclosure Associates	-
201101600027G	Lowell	Moody Elementary School	Construction	Repair - Accelerated	DBB	NETCO Construction Project Managers, Inc.	ICON architecture, inc.	Building Enclosure Associates	-
201101600040G	Lowell	Peter W Reilly School	Construction	Repair - Accelerated	DBB	NETCO Construction Project Managers, Inc.	ICON architecture, inc.	Building Enclosure Associates	-
201101600055G	Lowell	Washington School	Construction	Repair - Accelerated	DBB	NETCO Construction Project Managers, Inc.	ICON architecture, inc.	Building Enclosure Associates RDK Engineers	-
200801620505	Lunenburg	Lunenburg High School	OPM Selection			Joslin, Lesser + Associates Inc.	-		-
201201630405	Lynn	Breed Middle School	Project Scope & Budget	Repair - Accelerated		Diversified Project Management	Kaestle Boos Associates, Inc.		
200901630305	Lynn	Thurgood Marshall Middle School	Feasibility Study			Joslin, Lesser + Associates Inc.	Raymond Design Associates, Inc.		-
201201630605	Lynn	Lynn Vocational Tech Institute	Project Scope & Budget	Repair- Accelerated		Diversified Project Management	Kaestle Boos Associates, Inc.		
200901640505	Lynnfield	Lynnfield High School	Construction	Addition / Renovation	DBB	HEERY	Edward Rowse Architects, Inc.	Fitzmeyer & Tocci Associates, Inc.	-
W20024319	Malden	Malden High School	Closeout	Addition / Renovation	CM@R	URS Corporation	Flansburgh Associates, Inc.		Gilbane Building Company

You are Currently Viewing Active Projects.

Date of Report: 10/24/12

Active Projects: 330

MSBA ID	District	School	Phase	Project Scope	Procurement Type	OPM	Designer	Cx Company	CMGC
200806980610	Manchester Essex Regional	Manchester Essex Regional High School	Final Audit Approved	New Construction	DBB	Design Technique Inc.	Mount Vernon Group Architects, Inc.		TLT Construction Corporation
200801680020	Marblehead	Glover Elementary School	Construction Project	New Construction	DBB	Municipal Building Consultants, Inc.	JCJ Architecture, PC	RDK Engineers	-
201101700008G	Marlborough	Francis J Kane Elementary School	Complete/Substantial Completion	Repair - Accelerated	DBB	RF Walsh Collaborative Partners	Baker/Wohl Architects, Inc.	Building Enclosure Associates	A&A Window Products, Inc.
201101700505G	Marlborough	Marlborough High School	Construction	Repair - Accelerated	DBB	RF Walsh Collaborative Partners	Baker/Wohl Architects, Inc.	RDK Engineers	A&A Window Products, Inc. Feeley, McAnespie, Inc. Veterans Development Corporation, Inc.
200801710020	Marshfield	Governor Edward Winslow Elementary School	Closeout	Repair - Major	DBB	Vertex Construction Services	Knight, Bagge & Anderson, Inc.	RDK Engineers	Enterprise Equipment Co., Inc.
201101710505	Marshfield	Marshfield High School	Construction	New Construction	DBB	Compass Project Management, Inc.	Ai3 Architects LLC	Sebesta Blomberg & Associates, Inc.	-
200801740505	Maynard	Maynard High School	Construction	New Construction	DBB	Municipal Building Consultants, Inc.	Tappe Associates, Inc.	WSP Flack + Kurtz	CTA Construction Co., Inc.
201201760505	Medford	Medford High School	Feasibility Study	Science Lab		Leftfield, LLC	DiNisco Design Partnership, Limited		-
200801770305	Medway	Medway Middle School	Construction	Repair - Major	CM@R	Compass Project Management, Inc.	Knight, Bagge & Anderson, Inc.	Sebesta Blomberg & Associates, Inc.	Consigli Construction Company, Inc.
201201780505	Melrose	Melrose High School	Approved Project Vote Pending	Science Lab		CPI/Collaborative Partners	Ai3 Architects LLC		-
201101780505G	Melrose	Melrose High School	Final Audit Approved	Repair - Accelerated	DBB	Municipal Building Consultants, Inc.	Gale Associates, Inc.	Russo Barr Associates, Inc.	Commercial Roofing and Contracting, Inc.
201107100015G	Mendon-Upton	Miscoe Hill School	Construction	Repair - Accelerated	DBB	Maguire Group Inc.	Habeeb & Associates Architects, Inc.	Sebesta Blomberg & Associates, Inc.	-
200801810505	Methuen	Methuen High School	Construction	Addition / Renovation	CM@R	KBA/Trident	Finegold Alexander and Associates Inc.	Environmental Health and Engineering	Dimeo Construction Company
201101820025G	Middleborough	Mary K. Goode Elementary School	Project Complete/Substantial Completion	Repair - Accelerated	DBB	Maguire Group Inc.	Habeeb & Associates Architects, Inc.	Russo Barr Associates, Inc.	J.J. Cardosi, Inc.
200801840005	Middleton	Howe-Manning School	Project Complete/Substantial Completion	New Construction	DBB	RF Walsh Collaborative Partners	DiNisco Design Partnership, Limited	Foreman Building Commissioning, LP	CTA Construction Co., Inc.
201101850090	Milford	Woodland Elementary School	OPM Selection			-	-		-
200908300605	Minuteman Voc Tech	Minuteman Regional High School (Career Tech)	OPM Selection			-	-		-
201107170005G	Mohawk Trail	Buckland-Shelburne Reg	Project Complete/Substantial Completion	Repair - Accelerated	DBB	Potomac Capital Advisors	Bradley Architects, Inc.	Strategic Building Solutions, LLC	-
201107170010G	Mohawk Trail	Colrain Central School	Project Complete/Substantial Completion	Repair - Accelerated	DBB	Potomac Capital Advisors	Bradley Architects, Inc.	Strategic Building Solutions, LLC	-
201107170505G	Mohawk Trail	Mohawk Trail Reg High School	Construction	Repair - Accelerated	DBB	Potomac Capital Advisors	Bradley Architects, Inc.	Strategic Building Solutions, LLC	-
201122229999	Monomoy	Monomoy Regional High School	Design Development	New Construction		Skanska USA Building, Inc	Mount Vernon Group Architects, Inc.	Sebesta Blomberg & Associates, Inc.	-
201107200305G	Narragansett	Narragansett Middle School	Final Audit Approved	Repair - Accelerated	DBB	Potomac Capital Advisors	DiMarinisi & Wolfe Architects Urban Designers	Rist-Frost-Shumway Engineering, P.C.	-
201107200003G	Narragansett	Phillipston Memorial Elementary School	Construction	Repair - Accelerated	DBB	Potomac Capital Advisors	DiMarinisi & Wolfe Architects Urban Designers	Rist-Frost-Shumway Engineering, P.C.	-
200807200020	Narragansett	Templeton Center School	Feasibility Study	Repair - Major		Strategic Building Solutions, LLC	Symmes Maini & McKee Associates, Inc.		-

You are Currently Viewing Active Projects.

Date of Report: 10/24/12

Active Projects: 330

MSBA ID	District	School	Phase	Project Scope	Procurement Type	OPM	Designer	Cx Company	CM/GC
201207250505	Nashoba	Nashoba Regional High School	Feasibility Study	Science Lab		Strategic Building Solutions, LLC	Symmes Maini & McKee Associates, Inc.		-
200807250015	Nashoba	Pompositticut Elementary School	Project Complete/Substantial Completion	Addition / Renovation	DBB	Construction Monitoring Services, Inc.	Symmes Maini & McKee Associates, Inc.	Strategic Building Solutions, LLC	P.J. Stella Construction Corp.
200908520605G	Nashoba Valley Tech	Nashoba Valley Technical High School	Closeout	Repair - Accelerated	DBB	-	-		-
200801980505	Natick	Natick High School	Project Complete/Substantial Completion	New Construction	DBB	RF Walsh Collaborative Partners	Ai3 Architects LLC	Rist-Frost-Shumway Engineering, P.C.	-
201106600505G	Nauset	Nauset Regional High School	Construction	Repair - Accelerated	DBB	NETCO Construction Project Managers, Inc.	Habeeb & Associates Architects, Inc.	CBI Consulting Inc.	Capeway Roofing Systems, Inc. Modern Glass & Aluminum, Inc.
200901990050	Needham	Newman Elementary School	Project Complete/Substantial Completion	Repair - Major	CM@R	Steven H. Popper - Town Employee	Drumme Rosane Anderson, Inc.	Rist-Frost-Shumway Engineering, P.C.	Consigli Construction Company, Inc. Triumph Leasing Corporation
201101990405G	Needham	Pollard Middle	Closeout	Repair - Accelerated	DBB	STV Incorporated	Gale Associates, Inc.	CBI Consulting Inc.	Wayne Roofing Systems, LLC
200902010070	New Bedford	John Hannigan	OPM Selection			-	-		-
201002010505	New Bedford	New Bedford High School	Construction		DBB	-	-		-
201107280015G	New Salem-Wendell	Swift River Elementary School	Closeout	Repair - Accelerated	DBB	Maguire Group Inc.	Bradley Architects, Inc.	Strategic Building Solutions, LLC	RAC Builders, Inc.
201102040005	Newburyport	Francis T Bresnahan Elementary School	Design Development	New Construction		HEERY	HMFH Architects, Inc.	Fitzmeyer & Tocci Associates, Inc.	-
201002040305	Newburyport	Rupert A. Nock Middle School	Design Development	Addition / Renovation		HEERY	Miller Dyer Spears Inc.		-
201102070005	Newton	A E Angier Elementary School	Feasibility Study			Joslin, Lesser + Associates Inc.			-
201102070015G	Newton	Bowen	Closeout	Repair - Accelerated	DBB	STV Incorporated	Habeeb & Associates Architects, Inc.		-
W20014216	Newton	Newton North High School	Closeout	New Construction	CM@R	Turner Construction Co.	Dore & Whittier Architects, Inc.	Dimeo Construction Company	-
201102070125G	Newton	Williams Elementary School	Closeout	Repair - Accelerated	DBB	STV Incorporated	Habeeb & Associates Architects, Inc.		-
200802080005	Norfolk	Freeman-Kennedy Elementary School	Project Complete/Substantial Completion	New Construction	DBB	Joslin, Lesser + Associates Inc.	Flansburgh Associates, Inc.	WSP Flack + Kurtz	Fontaine Brothers, Inc.
200909150705	Norfolk County Agriculture	Norfolk County Agricultural High School	Construction	Addition / Renovation	DBB	Compass Project Management, Inc.	Turowski2 Architecture, Inc.	Rist-Frost-Shumway Engineering, P.C.	TLT Construction Corporation
200802090305	North Adams	Silvio O Conte Middle School	Project Scope & Budget	Addition / Renovation		Strategic Building Solutions, LLC	Margo Jones Architects, Inc.		-
201102110018G	North Andover	Annie L Sargent School	Project Complete/Substantial Completion	Repair - Accelerated	DBB	Municipal Building Consultants, Inc.	ICON architecture, inc.	Cannon Design	Varioka Construction, Inc.
201102110001G	North Andover	Atkinson School	Project Complete/Substantial Completion	Repair - Accelerated	DBB	Municipal Building Consultants, Inc.	ICON architecture, inc.	Cannon Design	Paul J. Rogan Co., Inc.
201102110305G	North Andover	North Andover Middle School	Project Complete/Substantial Completion	Repair - Accelerated	DBB	Municipal Building Consultants, Inc.	ICON architecture, inc.	Cannon Design	Stanley Roofing Company, Inc.
201102120010G	North Attleborough	Falls Elementary School	Closeout	Repair - Accelerated	DBB	Atlantic Construction and Management, Inc.	CSS Architects Incorporated	Gale Associates, Inc.	Northeast Energy Control Systems
201202120505	North Attleborough	North Attleboro High	Project Scope & Budget	Science Lab		Skanska USA Building, Inc	Kaestle Boos Associates, Inc.		-

You are Currently Viewing Active Projects.

Date of Report: 10/24/12

Active Projects: 330

MSBA ID	District	School	Phase	Project Scope	Procurement Type	OPM	Designer	Cx_Company	CM/GC
201202120015	North Attleborough	Roosevelt Avenue Elementary School	Project Scope & Budget	Repair- Accelerated		Skanska USA Building, Inc	Russo Barr Associates, Inc.		
201202150015	North Brookfield	North Brookfield Elementary School	Project Scope & Budget	Repair- Accelerated		Strategic Building Solutions, LLC	CBI Consulting, Inc.		
201102150015G	North Brookfield	North Brookfield Elementary School	Project Complete/Substantial Completion	Repair - Accelerated	DBB	Vertex Construction Services	LPBA/ Architects, Inc.	Simpson Gumpertz & Heger Inc.	Lockheed Window Corporations
201107350010G	North Middlesex	Ashby Elementary	Project Complete/Substantial Completion	Repair - Accelerated	DBB	Compass Project Management, Inc.	Russo Barr Associates, Inc.	Building Enclosure Associates	Greenwood Industries, Inc. GVW, Inc.
201107350505	North Middlesex	North Middlesex Regional High School	OPM Selection			HEERY	-		-
201107350005G	North Middlesex	Spaulding Memorial	Project Complete/substantial Completion	Repair - Accelerated	DBB	Compass Project Management, Inc.	Russo Barr Associates, Inc.	Building Enclosure Associates	MDM Engineering
201002170505	North Reading	North Reading High School	Construction	Addition / Renovation	DBB	PMA Construction Services	Dore & Whittier Architects, Inc.	Cannon Design	-
201102130003	Northborough	Lincoln Street	OPM Selection			-	-		-
201102130305G	Northborough	Robert E. Melican Middle School	Final Audit Approved	Repair - Accelerated	DBB	Pinck & Co., Inc.	ICON architecture, inc.	Strategic Building Solutions, LLC	AAlanco Service Corporation
201202180015	Norton	J C Solmonese	Schematic Design	Repair - Accelerated		Joslin, Lesser + Associates Inc.	Habeeb & Associates Architects, Inc.		
200902180505	Norton	Norton High School	Construction	Addition / Renovation	CM@R	Pinck & Co., Inc.	JCJ Architecture, PC	Rist-Frost-Shumway Engineering, P.C.	W. T. Rich Company Inc.
200802200505	Norwood	Norwood High School	Project Complete/Substantial Completion	New Construction	DBB	Compass Project Management, Inc.	Ai3 Architects LLC		Agostini Construction Co., Inc.
200908550605	Old Colony Reg Voc Tech	Vocational Technical High School	Feasibility Study			Vertex Construction Services -			-
200802260405	Oxford	Oxford Middle School	Construction	Repair - Major		Diversified Project Management	CGKV Architects, Inc.		-
201102270305G	Palmer	Converse Middle School	Construction	Repair - Accelerated	DBB	Diversified Project Management	Tighe & Bond, Inc.	Strategic Building Solutions, LLC	Royal Steam Heater Co. Titan Roofing, Inc.
201102270008G	Palmer	Old Mill Pond Elementary School	Construction	Repair - Accelerated	DBB	Diversified Project Management	Tighe & Bond, Inc.	Strategic Building Solutions, LLC	Royal Steam Heater Co.
201102270505G	Palmer	Palmer High School	Construction	Repair - Accelerated	DBB	Diversified Project Management	Tighe & Bond, Inc.	Strategic Building Solutions, LLC	Royal Steam Heater Co. Titan Roofing, Inc.
200802290305	Peabody	J Henry Higgins Middle School	Schematic Design	New Construction		Daedalus Projects Inc	DiNisco Design Partnership, Limited		-
201102290007G	Peabody	John E Burke School	Construction	Repair - Accelerated	DBB	Daedalus Projects Inc	LPBA/ Architects, Inc.	Sebesta Blomberg & Associates, Inc.	-
201102290027G	Peabody	William A Welch Sr	Project Complete/Substantial Completion	Repair - Accelerated	DBB	Daedalus Projects Inc	LPBA/ Architects, Inc.	Sebesta Blomberg & Associates, Inc.	-
201107450020G	Pentucket	Dr Frederick N Sweetsir	Closeout	Repair - Accelerated	DBB	PMA Construction Services	Knight, Bagge & Anderson, Inc.	CBI Consulting Inc.	E. Amanti & Sons, Inc.
201107450015G	Pentucket	Dr John C Page School	Closeout	Repair - Accelerated	DBB	PMA Construction Services	Knight, Bagge & Anderson, Inc.	RDK Engineers	Capeway Roofing Systems, Inc.
201107450005G	Pentucket	Elmer S Bagnall	Closeout	Repair - Accelerated	DBB	PMA Construction Services	Knight, Bagge & Anderson, Inc.	CBI Consulting Inc.	Gibson Roofs, Inc.
201107450010G	Pentucket	Helen R Donaghue School	Closeout	Repair - Accelerated	DBB	PMA Construction Services	Knight, Bagge & Anderson, Inc.	CBI Consulting Inc.	Gibson Roofs, Inc.
201107500008G	Pioneer Valley	Northfield Elementary School	Project Complete/Substantial Completion	Repair - Accelerated	DBB	Diversified Project Management	CGKV Architects, Inc.	Strategic Building Solutions, LLC	-

You are Currently Viewing Active Projects.

Date of Report: 10/24/12

Active Projects: 330

MSBA ID	District	School	Phase	Project Scope	Procurement Type	OPM	Designer	Cx Company	CM/GC
201107500505G	Pioneer Valley	Pioneer Valley Reg Middle School/High School	Construction	Repair - Accelerated	DBB	Diversified Project Management	CGKV Architects, Inc.	Strategic Building Solutions, LLC	-
201002360510	Pittsfield	Taconic High School	Feasibility Study			Skanska USA Building, Inc	-		-
201202390515	Plymouth	Plymouth South High School	Eligibility Period						
200802390505	Plymouth	Plymouth North High School	Project Complete/Substantial Completion	New Construction	DBB	Ted Gentry Associates, Inc	Ai3 Architects LLC	Sebesta Blomberg & Associates, Inc.	J & J Contractors, Inc.
201007530505G	Quabbin	Quabbin Regional High School	Closeout	Repair - Accelerated	DBB	Vertex Construction Services	LPBA/ Architects, Inc.	Building Enclosure Associates	Kronenberger & Sons Restoration, INC.
201207530030	Quabbin	Ruggles Lane Elementary School	Project Scope & Budget	Repair - Accelerated		Vertex Construction Services	Turowski2 Architecture, Inc.		
201207780005	Quaboag	Warren Community Elementary School	Schematic Design	Repair - Accelerated		Coast & Harbor Associates, Inc.	Lindgren & Sharples, Inc.		
200802430315	Quincy	Central Middle School	Construction	New Construction	DBB	Tishman Construction Corporation of MA	Ai3 Architects LLC	Sebesta Blomberg & Associates, Inc.	-
201102460005G	Reading	Birch Meadow Elementary School	Final Audit Approved	Repair - Accelerated	DBB	KBA Architects	LPBA/ Architects, Inc.	Russo Barr Associates, Inc.	Paul J. Rogan Co., Inc.
201102460017G	Reading	J Warren Killam Elementary School	Final Audit Approved	Repair - Accelerated	DBB	KBA Architects	LPBA/ Architects, Inc.	Russo Barr Associates, Inc.	Capeway Roofing Systems, Inc.
201002480035	Revere	William McKinley Elementary School	Schematic Design			RF Walsh Collaborative Partners	Drumme Rosane Anderson, Inc.		-
200802500005	Rochester	Rochester Memorial School	Closeout	Addition / Renovation	CM@R	PMA Construction Services	Flansburgh Associates, Inc.	Horizon Engineering Associates, LLP	Gilbane Building Company
200802510305	Rockland	John W. Rogers Middle School	Construction	Addition / Renovation	CM@R	Daedalus Projects Inc	Dore & Whittier Architects, Inc.	Consulting Engineering Services, LLC	Agostini Construction Co., Inc.
201102510025G	Rockland	R Stewart Esten	Project Complete/Substantial Completion	Repair - Accelerated	DBB	Daedalus Projects Inc	Habeeb & Associates Architects, Inc.	Russo Barr Associates, Inc.	Northeast Energy Control Systems
200902580305G	Salem	Collins Middle School	Construction	Repair - Accelerated	CM@R	KV Associates, Inc.	Reinhardt Associates, Inc.	Rist-Frost-Shumway Engineering, P.C.	-
201002580050G	Salem	Saltonstall School	Construction	Repair - Accelerated	CM@R	KV Associates, Inc.	Reinhardt Associates, Inc.	Rist-Frost-Shumway Engineering, P.C.	-
201102610010G	Sandwich	Forestdale School	Project Complete/Substantial Completion	Repair - Accelerated	DBB	NETCO Construction Project Managers, Inc.	Habeeb & Associates Architects, Inc.	Gale Associates, Inc.	Varioka Construction, Inc.
200902610025G	Sandwich	Oak Ridge School	Project Complete/Substantial Completion	Repair - Accelerated	DBB	NETCO Construction Project Managers, Inc.	Habeeb & Associates Architects, Inc.	Gale Associates, Inc.	J.J. Cardosi, Inc.
201002620305	Saugus	Belmonte Middle School	Construction	Repair - Major	CM@R	Skanska USA Building, Inc	Fletcher Thompson Architecture Engineering, LLC	Consulting Engineering Services, LLC	-
201202620505	Saugus	Saugus High School	Feasibility Study	Science Lab		Strategic Building Solutions, LLC	Symmes Maini & McKee Associates, Inc.		-
200802660305	Sharon	Sharon Middle School	Closeout	Addition / Renovation	CM@R	Daedalus Projects Inc	Kaestle Boos Associates, Inc.	Horizon Engineering Associates, LLP	Consigli Construction Company, Inc.
201008710605	Shawsheen Valley Voc Tech	Shawsheen Valley Voc Tech High School	Closeout	Addition / Renovation	DBB	Construction Monitoring Services, Inc.	Knight, Bagge & Anderson, Inc.		Colantonio, Inc.
201208710605	Shawsheen Valley Voc Tech	Shawsheen Valley Voc Tech High School	Project Scope & Budget	Repair - Accelerated		Diversified Project Management	Shekar & Associates, Inc.		
200802710305	Shrewsbury	Sherwood Middle School	Construction	New Construction	CM@R	PMA Construction Services	Lamoureux Pagano & Associates, Inc.	RDK Engineers	Gilbane Building Company
201102710035G	Shrewsbury	Spring Street Elementary School	Project Complete/Substantial Completion	Repair - Accelerated	DBB	PMA Construction Services	Habeeb & Associates Architects, Inc.	Cannon Design	Lambrian Construction Corp.

You are Currently Viewing Active Projects.

Date of Report: 10/24/12

Active Projects: 330

MSBA ID	District	School	Phase	Project Scope	Procurement Type	OPM	Designer	Cx Company	CMGC
200811119999	Somerset-Berkley	Somerset-Berkley High School	Construction	New Construction		Skanska USA Building, Inc	Ai3 Architects LLC	Horizon Engineering Associates, LLP	-
200902740111E	Somerville	East Somerville Community School at Cummings	Construction	Addition / Renovation	CM@R	PMA Construction Services	Maguire Group, Inc.	Foreman Building Commissioning, LP	Gilbane Building Company
200902780015	South Hadley	Plains School	Project Scope & Budget	New Construction		Arcadis	Margo Jones Architects, Inc.		-
200808730605G	South Shore Reg Voc Tech	South Shore Vocational Technical High School	Closeout	Repair - Accelerated	DBB	Vertex Construction Services	Gale Associates, Inc.	Building Enclosure Associates	-
200802770505	Southbridge	Southbridge High School	Project Complete/substantial Completion	New Construction	CM@R	Joslin, Lesser + Associates Inc.	Tappe Associates, Inc.	Environmental Health and Engineering	Consigli Construction Company, Inc.
201202750005	Southampton	William E. Norris Elementary School	Designer Selection	Repair - Accelerated					
200908720605	Southeastern Reg Voc Tech	Southeastern Regional Vocational Technical School	Construction	Addition / Renovation	CM@R	RF Walsh Collaborative Partners	Drumme Rosane Anderson, Inc.	RDK Engineers	W. T. Rich Company Inc.
200908760605	Southern Worcester Cty VT	Bay Path Regional Vocational Technical High School	Design Development	Addition / Renovation	DBB	HEERY	Kaestle Boos Associates, Inc.		-
201107660505	Southwick-Tolland	Regional High School	Design Development	Addition / Renovation		Strategic Building Solutions, LLC	JCJ Architecture, PC		BVH Integrated Services, Inc.
200807670505	Spencer-E Brookfield	David Prouty High School	Schematic Design	Addition / Renovation		Dore and Whittier Architects, Inc.	Design Partnership of Cambridge, Inc.		-
	Springfield	SCIPP Year 2	Project Complete/Substantial Completion						
	Springfield	SCIPP Year 3	Construction						
201102810125E	Springfield	Dryden Veterans Memorial Elementary School	Construction	Addition / Renovation		Arcadis	Drumme Rosane Anderson, Inc.	BVH Integrated Services, Inc.	-
201102810030E	Springfield	Elias Brookings Elementary School	Approved Project Vote Pending	New Construction		Arcadis	Drumme Rosane Anderson, Inc.		-
W20014137	Springfield	Forest Park Middle School	Construction	Addition / Renovation	DBB	Arcadis	Perkins Eastman	Foreman Building Commissioning, LP	-
W20054428	Springfield	Roger L. Putnam Vocational Technical High School	Project Complete/Substantial Completion	New Construction	CM@R	Pinnacle One, Inc.	Drumme Rosane Anderson Inc.	Strategic Building Solutions, LLC	Consigli/Morganti
201202810500	Springfield	Central High School	Feasibility Study	Science Lab		Leftfield, LLC	DiNisco Design Partnership, Limited		
200902840405	Stoneham	Stoneham Middle School	Design Development	Addition / Renovation	CM@R	Joslin, Lesser + Associates Inc.	Tappe Associates, Inc.	RDK Engineers	Shawmut Design and Construction
200802870005	Sturbridge	Burgess Elementary School	Project Complete/Substantial Completion	Addition / Renovation	DBB	Lamoureux Pagano & Associates, Inc.	Drumme Rosane Anderson, Inc.	Horizon Engineering Associates, LLP	Fontaine Brothers, Inc.
201102880030G	Sudbury	Peter Noyes Elementary School	Final Audit Approved	Repair - Accelerated	DBB	Compass Project Management, Inc.	Russo Barr Associates, Inc.	RDK Engineers	Gibson Roofs, Inc.
201202880025	Sudbury	General John Nixon Elementary School	Project Scope & Budget	Repair - Accelerated					
200802900305	Sutton	Sutton Middle School	Construction	Addition / Renovation	DBB	Strategic Building Solutions, LLC	Flansburgh Associates, Inc.	RDK Engineers	TLT Construction Corporation
201102910010	Swampscott	Hadley	Eligibility Period			-	-		-
201107700405G	Tantasqua	Tantasqua Regional Jr High School	Closeout	Repair- Accelerated	DBB	Diversified Project Management	Habeeb & Associates Architects, Inc.		Greenwood Industries, Inc.
201202930057	Taunton	Harold H Galligan School	Designer Selection	Repair - Accelerated					
W20014194	Taunton	Parker Middle/Taunton High School	Closeout	Addition / Renovation	CM@R	Gilbane Building Company	Design Partnership of Cambridge, Inc.		Bacon-Agostini Construction Joint Venture

You are Currently Viewing Active Projects.

Date of Report: 10/24/12

Active Projects: 330

MSBA ID	District	School	Phase	Project Scope	Procurement Type	OPM	Designer	Cx Company	CM/GC
200802950505	Tewksbury	Tewksbury Memorial High School	Project Complete/Substantial Completion	New Construction	DBB	HEERY	Symmes Maini & McKee Associates, Inc.	Sebesta Blomberg & Associates, Inc.	CTA Ventures
201208780605	Tri County	Tri County Reg Voc Tech	Approved Project Vote Pending	Science Lab		Collaborative Partners	Ai3 Architects LLC		-
201108790605G	Upper Cape Cod Voc Tech	Upper Cape Cod Voc Tech	Project Complete/Substantial Completion	Repair - Accelerated	DBB	NETCO Construction Project Managers, Inc.	Knight, Bagge & Anderson, Inc.	Gale Associates, Inc.	Modern Glass & Aluminum, Inc.
200803040505	Uxbridge	Uxbridge High School	Project Complete/Substantial Completion	New Construction	CM@R	Joslin, Lesser + Associates Inc.	Raymond Design Associates, Inc.	Turner Facilities Management Solutions	Shawmut Design and Construction
200907750305	Wachusett	Mountview Middle School	Schematic Design			Gary Kaczmarek - Town Employee	Lamoureux Pagano & Associates, Inc.		-
201107750035G	Wachusett	Naquag Elementary School	Project Complete/Substantial Completion	Repair - Accelerated	DBB	Strategic Building Solutions, LLC	LPBA/ Architects, Inc.	Rist-Frost-Shumway Engineering, P.C.	MDM Engineering
201107750040G	Wachusett	Paxton Center School	Project Complete/Substantial Completion	Repair - Accelerated	DBB	Strategic Building Solutions, LLC	LPBA/ Architects, Inc.	Rist-Frost-Shumway Engineering, P.C.	MDM Engineering
201107750045G	Wachusett	Thomas Prince School	Construction	Repair - Accelerated	DBB	Strategic Building Solutions, LLC	LPBA/ Architects, Inc.	Rist-Frost-Shumway Engineering, P.C.	MDM Engineering
201003050310	Wakefield	Galvin Middle School	Design Development	New Construction	DBB	Joslin, Lesser + Associates Inc.	Tappe Associates, Inc.	B2Q Associates, Inc.	-
201203150305	Wayland	Wayland Middle School	Schematic Design	Repair - Accelerated		Joslin, Lesser + Associates Inc.	DiMarinisi & Wolfe Architects Urban Designers		
200803150505	Wayland	Wayland High School	Project Complete/Substantial Completion	New Construction	CM@R	KV Associates, Inc.	HMFH Architects, Inc.	WSP Flack + Kurtz	Shawmut Design and Construction
200903160015	Webster	Park Avenue Elementary School	Design Development	New Construction	DBB	RF Walsh Collaborative Partners	Dore & Whittier Architects, Inc.		-
200803170505	Wellesley	Wellesley Senior School	Project Complete/Substantial Completion	New Construction	CM@R	Ryegate, Inc.	Symmes Maini & McKee Associates, Inc.	Rist-Frost-Shumway Engineering, P.C.	Turner Construction Company
201103220005G	West Boylston	Major Edwards Elementary	Construction	Repair - Accelerated	DBB	URS Corporation	Reinhardt Associates, Inc.	Cannon Design	-
201003230505	West Bridgewater	West Bridgewater Middle-Senior High School	Design Development	New Construction		Strategic Building Solutions, LLC	Flansburgh Associates, Inc.		-
200903320505	West Springfield	West Springfield High School	Construction	New Construction	DBB	Strategic Building Solutions, LLC	Symmes Maini & McKee Associates, Inc.	Turner Facilities Management Solutions	Fontaine Brothers, Inc.
200903210305	Westborough	Gibbons Middle School	OPM Selection			-	-		-
200903250020	Westfield	Abner Gibbs Elementary School	Construction	New Construction	DBB	Skanska USA Building, Inc	Margo Jones Architects, Inc.	Horizon Engineering Associates, LLP	-
201103250025G	Westfield	Highland Elementary School	Project Complete/Substantial Completion	Repair - Accelerated	DBB	P3 Project Planning	Tighe & Bond, Inc.		
201003250025G	Westfield	Highland Elementary School	Final Audit Approved	Repair - Accelerated	DBB	P3 Project Planning	Tighe & Bond, Inc.	Strategic Building Solutions, LLC	-
201103250033E	Westfield	Munger Hill Elementary School	Project Scope & Budget	Repair - Accelerated			Knight, Bagge & Anderson, Inc.		
201103250036G	Westfield	Paper Mill Elementary School	Project Complete/Substantial Completion	Repair - Accelerated	DBB	P3 Project Planning	Tighe & Bond, Inc.	Strategic Building Solutions, LLC	-
201203250036	Westfield	Paper Mill Elementary School	Project Scope & Budget	Repair - Accelerated			Lindgren & Sharples, Inc.		

You are Currently Viewing Active Projects.

Date of Report: 10/24/12

Active Projects: 330

MSBA ID	District	School	Phase	Project Scope	Procurement Type	OPM	Designer	Cx_Company	CM/GC
201103250040G	Westfield	Southampton Road Elementary School	Final Audit Approved	Repair - Accelerated	DBB	P3 Inc.	Tighe & Bond, Inc.		
201003250040G	Westfield	Southampton Road Elementary School	Project Complete/Substantial Completion	Repair - Accelerated	DBB	P3 Project Planning	Tighe & Bond, Inc.	Strategic Building Solutions, LLC	R & H Roofing
201103250505G	Westfield	Westfield High School	Project Complete/Substantial Completion	Repair - Accelerated	DBB	P3 Project Planning	Tighe & Bond, Inc.	Strategic Building Solutions, LLC	-
201103250605G	Westfield	Westfield Voc Tech High School	Construction	Repair - Accelerated	DBB	P3 Project Planning	Tighe & Bond, Inc.	Strategic Building Solutions, LLC	-
200903300012	Weston	Field Elementary School	Construction	New Construction	DBB	Compass Project Management, Inc.	Jonathan Levi Architects LLC	Foreman Building Commissioning, LP	-
201103300505G	Weston	Weston High School	Project Complete/Substantial Completion	Repair - Accelerated	DBB	Compass Project Management, Inc.	Garcia Galuska DeSousa Consulting Engineers Inc.	RDK Engineers	-
201103300305G	Weston	Weston Middle School	Final Audit Approved	Repair - Accelerated	DBB	Compass Project Management, Inc.	Russo Barr Associates, Inc.	RDK Engineers	Greenwood Industries, Inc.
201103310015G	Westport	Alice A Macomber Primary	Project Complete/Substantial Completion	Repair - Accelerated	DBB	Pinck & Co., Inc.	CGKV Architects, Inc.	CBI Consulting Inc.	-
201103310505G	Westport	Westport High School	Project Complete/Substantial Completion	Repair - Accelerated	DBB	Pinck & Co., Inc.	CGKV Architects, Inc.	CBI Consulting Inc.	-
201103360310G	Weymouth	Abigail Adams Middle School	Final Audit Approved	Repair - Accelerated	DBB	KBA Architects	Gale Associates, Inc.	Cannon Design	Greenwood Industries, Inc.
201203360080	Weymouth	William Seach Primary	Design Development	Repair - Accelerated					
201107800030G	Whitman-Hanson	John H Duval Jr Elementary School	Final Audit Approved	Repair - Accelerated	DBB	-	BETA Group, Inc.		S.I. Services, Inc.
200907800025	Whitman-Hanson	Maquan Elementary School	Schematic Design			Knight, Bagge & Anderson Inc.	Turowski2 Architecture, Inc.		-
200803400005	Williamsburg	Anne T. Dunphy School	Design Development	Addition / Renovation	DBB	Arcadis	Drumme Rosane Anderson, Inc.	B2Q Associates, Inc.	-
201203420060	Wilmington	North Intermediate	Project Scope & Budget	Repair - Accelerated					
201103420025G	Wilmington	Shawsheen Elementary School	Final Audit Approved	Repair - Accelerated	DBB	P3 Inc.	Russo Barr Associates, Inc.	CBI Consulting Inc.	Lockheed Window Corporations
200903420505	Wilmington	Wilmington High School	Construction	New Construction	CM@R	Joslin, Lesser + Associates Inc.	Dore & Whittier Architects, Inc.	Symmes, Maini & McKee Associates	Gilbane Building Company
200803440025	Winchester	Vinson-Owen Elementary School	Construction	New Construction	DBB	Neil Foley - Town Employee	Tappe Associates, Inc.	Turner Facilities Management Solutions	CTA Construction Co., Inc.
201003440505	Winchester	Winchester High School	Feasibility Study			Skanska USA Building, Inc	Symmes Maini & McKee Associates, Inc.		-
200803460505	Winthrop	Winthrop Sr High School	Feasibility Study			Skanska USA Building, Inc	HMFH Architects, Inc.		-
201103470410G	Woburn	Daniel L Joyce Middle School	Closeout	Repair - Accelerated	DBB	Municipal Building Consultants, Inc.	Gale Associates, Inc.	Simpson Gumpertz & Heger Inc.	Reliable Roofing and Sheet Metal, LLC
200803470015	Woburn	Goodyear School	Closeout	New Construction	CM@R	Municipal Building Consultants, Inc.	Tappe Associates, Inc.	Strategic Building Solutions, LLC	Gilbane Building Company
201103470405G	Woburn	John F Kennedy Middle School	Closeout	Repair - Accelerated	DBB	Municipal Building Consultants, Inc.	Gale Associates, Inc.	Simpson Gumpertz & Heger Inc.	Greenwood Industries, Inc.
201203480052	Worcester	Chandler Magnet School	Schematic Design	Repair - Accelerated					
201203488099	Worcester	Dr. James Caradonio Center	Schematic Design	Repair - Accelerated					

You are Currently Viewing Active Projects.

Date of Report: 10/24/12


Active Projects: 330

MSBA ID	District	School	Phase	Project Scope	Procurement Type	OPM	Designer	Cx_Company	CM/GC
201203480140	Worcester	Jacob Hiatt Magnet School	Schematic Design	Repair - Accelerated					
201203480145	Worcester	Lake View School	Schematic Design	Repair - Accelerated					
201203480175	Worcester	May Street School	Schematic Design	Repair - Accelerated					
201203480200	Worcester	Nelson Place	Eligibility Period			-	-		-
W20004048	Worcester	North High School	Project Complete/Substantial Completion	New Construction	CM@R	-	Maguire Group, Inc.	Architectural Services	Gilbane Building Company

2012 Eligibility Period Status

October 24, 2012


6 Projects in Eligibility Period

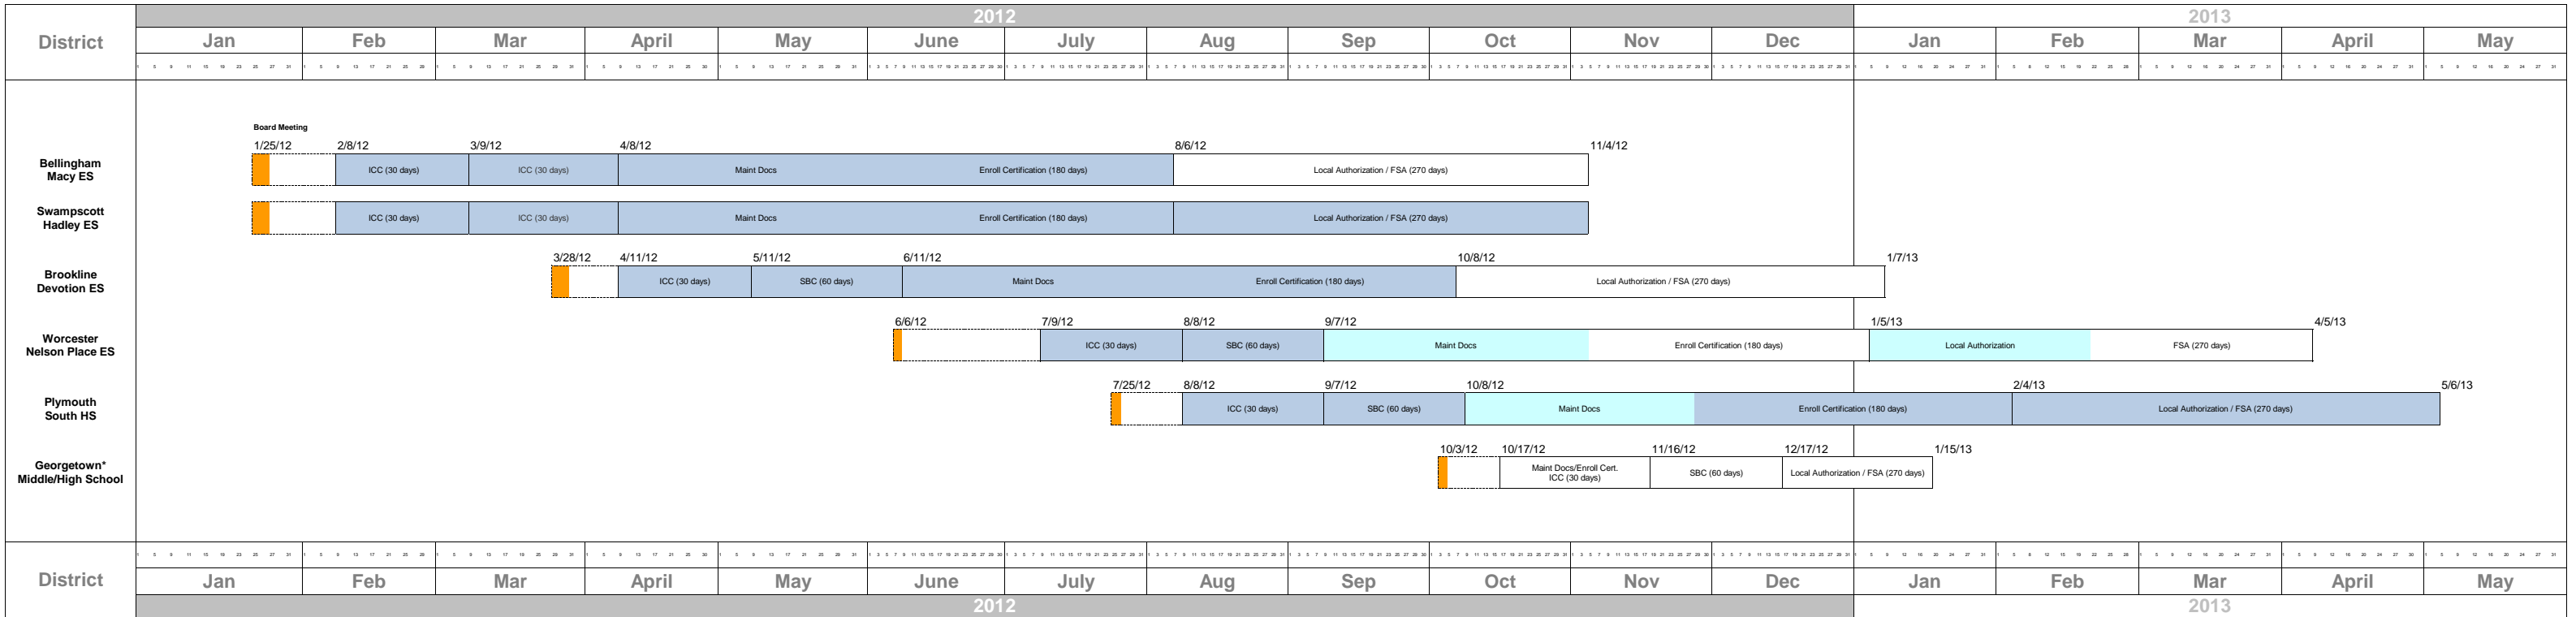

*This project is a requirement in the Project Scope and Budget Agreement for the Penn Brook Elementary School. Therefore, the District's Maintenance Documentation and Enrollment Certification were completed prior to invitation to the Eligibility Period.

Project Status | October 24, 2012

Core Program:	47
Waitlist:	2
Green Repair:	85
Accelerated Repair:	36
Science Lab Initiative:	8
Project Complete / Substantial Completion:	65
Closeout:	50
Final Audit Approved:	31
Projects to be Removed:	2
Total Projects:	324

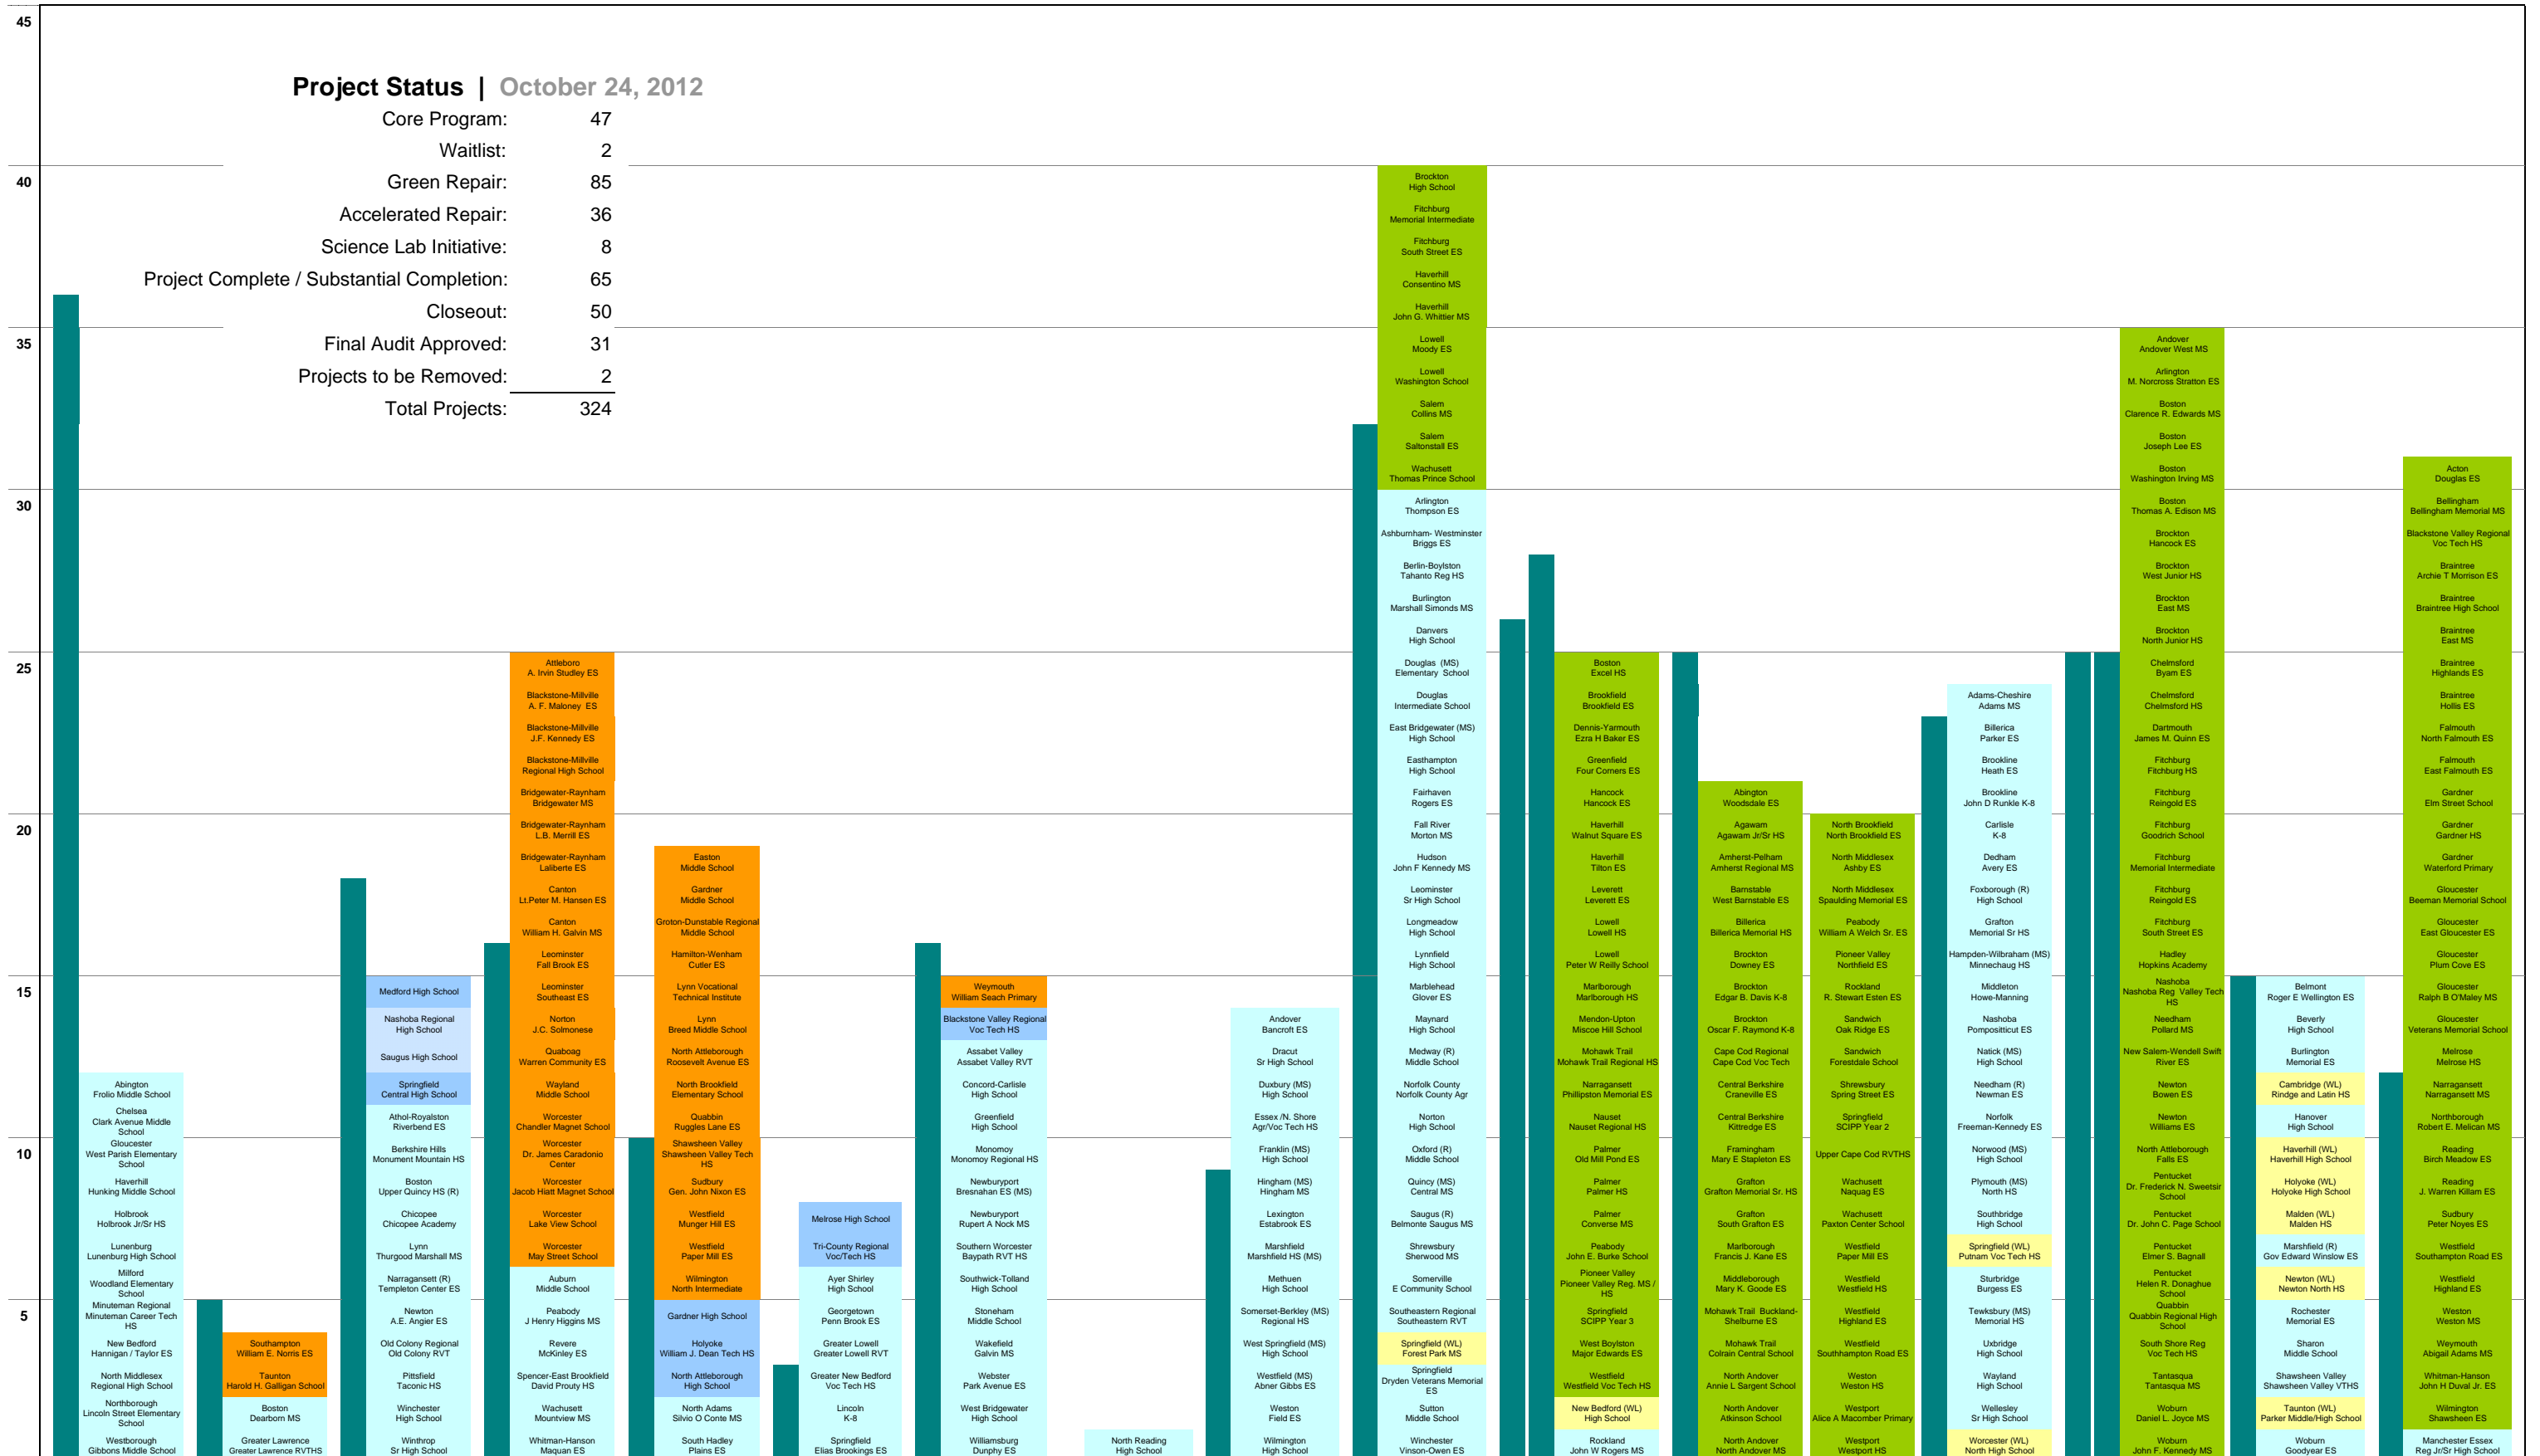

OPM Selection	Designer Selection	Feasibility Study	Schematic Design	Project Scope & Budget	Approved Project Vote Pending	Design Development	Building Completion 2015	Building Completion 2014	Building Completion 2013	Building Completion 2012	Project Complete / Substantial Completion	Closeout	Final Audit Approved
12	4	15	25	19	8	15	1	14	40	25	65	50	31

PROJECT STATUS

324
Total Active
Projects

■ Green Repair Program
■ Accelerated Repair Program

■ New Program Project
■ Science Lab Initiative Project
■ Science Lab Initiative Project - To Be Removed at November Board

■ Waitlist Projects
■ Capital Pipeline Status Presented at October 3, 2012 Board of Directors Meeting

2012 Estimated Bid Dates

Note bid dates are **Estimates ONLY**. Please contact Districts for exact information.

Total Project Budget denotes total District costs and does not denote the basis of the MSBA Total Facilities Grant.

■ - Denotes bid phase in progress or complete
 ■ - Denotes estimated bid dates
 ■ - Denotes estimated GMP dates

DISTRICT	DESIGN BASIS FOR ENROLLMENT	PROJECT BUDGET <small>Shown in Millions</small>	CONSTRUCTION BUDGET <small>Shown in Millions</small>	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC
<small>*Projects Considering the CM @ Risk Method</small>															
*ASHBURNHAM-WESTMINSTER	520	\$30.0	\$24.8	JR Briggs ES New Construction: Filed-Sub Bids rcv'd 1/12. GMP issued 3/8.											
NORFOLK COUNTY AGRICULTURAL	550	\$28.6	\$22.3	Norfolk County Aggi Renovation: Filed-Sub Bids rcv'd 1/18. G.C. Bids due 2/1 NTP issued 3/21.											
*SPRINGFIELD -FOREST PARK	660	\$43.4	\$34.0	Springfield Forest Park MS: Filed-Sub Bids rcv'd 3/2. GMP issued 3/26.											
*SOMERVILLE	500	\$33.2	\$15.2	East Somerville Community School Addition/Renovation: Filed-Sub Bids rcv'd 6/14. GMP issued 10/31.											
DOUGLAS	552	\$50.7	\$38.9	Douglas IS New Construction: Filed-Sub Bids rcv'd 1/12. G.C. Bids rcv'd 1/20. NTP issued 3/2.											
WINCHESTER	420	\$28.7	21.7	Vinson-Owen ES New Construction: Filed-Sub Bids rcv'd 1/5. G.C. Bids Due 2/2. NTP issued 2/13.											
DRACUT	1160	\$60.4	\$47.30	Dracut Senior HS Addition/Renovation: Filed-Sub Bids rcv'd 7/17. G.C. Bids rcv'd 7/24. NTP issued 8/27.											
*SOUTHEASTERN REGIONAL RVT	1370	\$34.2	\$26.5	SRVT Add/Reno: Filed-Sub Bids rcv'd 2/29. GMP issued 4/2.											
*NORTON	700	\$34.6	\$27.0	Norton HS Addition/Renovation: Filed-Sub Bids rcv'd 3/15. GMP issued 3/27.											
QUINCY	620	\$50.0	\$32.6	Central MS New Construction: Filed-Sub Bids rcv'd 5/8. G.C. Bids rcv'd 5/22. NTP issued 5/24.											
ARLINGTON	380	\$20.7	\$15.7	Arlington Thompson ES New Construction: Filed-Sub Bids rcv'd 3/6. G.C. Bids rcv'd 3/27. NTP issued 4/2.											
LYNNFIELD	740	\$4.5	\$3.2	Lynnfield HS Addition: Filed-Sub Bids rcv'd 4/26. G.C. Bids rcv'd 5/10. NTP issued 6/25.											
MARBLEHEAD	425	\$25.9	\$20.2	Marblehead Glover ES New Construction: Filed-Sub Bids rcv'd 5/9. G.C. Bids rcv'd 5/23. NTP issued 7/16.											
HINGHAM	1020	\$60.9	\$50.4	Hingham MS New Construction: Filed-Sub Bids rcv'd 4/25. G.C. Bids rcv'd 5/10. NTP issued 6/7.											
WESTFIELD	600	\$35.9	\$25.2	Abner Gibbs ES New Construction: Filed-Sub Bids rcv'd 7/19. G.C. Bids rcv'd 8/7. NTP issued 8/24.											
*ESSEX-NS	1440	\$125.0	\$96.50	Essex Northshore HS New Construction: Early Site Packages rcv'd 3/30. Filed-Sub rcv'd 8/29. GMP Targeted November.											
*ANDOVER	680	\$44.7	\$34.5	Andover Bancroft ES New Construction: Early Site, Steel, Foundations Packages. Filed-Sub Bids rcv'd 9/22. Non Filed-Sub Bids due 11/2. GMP Targeted December.											
*METHUEN	2075	\$99.1	\$74.9	Methuen HS Addition/Renovation: GMP Issued 5/21.											
FAIRHAVEN	370	\$24.7	\$20.2	Fairhaven Rogers ES _New Construction: Filed-sub rcv'd 5/31. G.C. Bids rcv'd 6/14. NTP issued 6/29.											
SOMERSET BERKLEY	1000	\$82.8	\$66.8	Somerset-Berkley RHS New Construction: Filed-Sub Bids rcv'd 5/30. G.C. Bids rcv'd 6/13. NTP issued 6/28.											
*SAUGUS	725	\$20.3	\$15.7	Saugus Belmonte MS Repair: Filed-Sub Bids rcv'd 6/21. GMP issued 8/15.											
*DUXBURY	1735	\$128.4	\$99.2	Duxbury HS/MS New Construction: Filed-Sub Bids rcv'd 9/20. GMP Issued 10/9.											

2012 Estimated Bid Dates

Note bid dates are **Estimates ONLY**. Please contact Districts for exact information.

Total Project Budget denotes total District costs and does not denote the basis of the MSBA Total Facilities Grant.

■ - Denotes bid phase in progress or complete
 ■ - Denotes estimated bid dates
 ■ - Denotes estimated GMP dates

DISTRICT	DESIGN BASIS FOR ENROLLMENT	PROJECT BUDGET <small>Shown in Millions</small>	CONSTRUCTION BUDGET <small>Shown in Millions</small>	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC
<small>*Projects Considering the CM @ Risk Method</small>															
MARSHFIELD	1310	\$103.9	\$80.8	Marshfield HS New Construction: Filed-Sub Bids Due 7/23. G.C Bids Due 8/6. NTP issued 8/31. ■											
WESTON	355	\$31.5	\$21.5	Field ES New Construction: Filed-Sub Bids rcv'd 10/31. G.C. Bids Due 11/14. NTP Targeted December. ■											
*SPRINGFIELD-DRYDEN	280	\$13.1	\$10.7	Dryden ES Addition/Renovation: Filed-Sub Bids rcv'd 10/4. GMP issued 10/19. ■											
FRANKLIN	1650	\$104.6	\$87.9	Franklin HS New Construction: Filed-Sub Bids rcv'd 9/7. G.C Bids rcv'd 9/25. NTP issued 10/9. ■											
*WILMINGTON	960	\$82.7	\$64.4	Wilmington HS New Construction: Early Sitework, Foundation, & Steel bid packages ■ Wilmington HS New Construction: Filed-Sub Bids Due 11/30. GMP Targeted January 2013. ■											
*LEXINGTON	540	\$40.8	31.1	Lexington Estabrook ES New Construction: Early Sitework bid packages. ■ Lexington Estabrook ES New Construction: Early Foundation bid packages ■ Lexington Estabrook ES New Construction: Filed-Sub Bids Due 12/4. GMP Targeted for January 2013. ■											
NEWBURYPORT	660	\$37.3	\$31.1	Newburyport Bresnhan ES New Construction: Filed-Sub Bids Due 12/26. G.C Bids Due 1/9/13. NTP Targeted January 2013. ■											
MONOMOY REGIONAL SCHOOL	700	\$64.7	52.9	Monomoy Regional HS New Construction: Filed-Sub Bids Due 12/26. G.C Bids Due 1/9/13. NTP Targeted January 2013. ■											
Subtotal				24,697	\$1,545	\$1,193.2									
GRAND TOTAL				24,697	\$1,545	\$1,193.2									
Number of Construction-Related Employment Opportunities Created			5,966												

2013 Estimated Bid Dates

Note bid dates are **Estimates ONLY**. Please contact Districts for exact information.

Total Project Budget denotes total District costs and does not denote the basis of the MSBA Total Facilities Grant.

■ - Denotes bid phase in progress or complete
 ■ - Denotes estimated bid dates
 ■ - Denotes estimated GMP dates

DISTRICT <small>*Projects Considering the CM @ Risk Method</small>	DESIGN BASIS FOR ENROLLMENT	PROJECT BUDGET <small>Shown in Millions</small>	CONSTRUCTION BUDGET <small>Shown in Millions</small>	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC
*STONEHAM	775	\$38.6	\$32.0	Stoneham MS New Construction: Filed-Sub Bids Due 1/11. GMP Targeted February.											
*NORTH READING	1370	\$103.4	86.3	N.Reading HS New Construction: Filed-Sub Bids Due 2/8. GMP Targeted February.											
ASSABET VALLEY	1000	\$62.4	\$50.8	Assabet Valley Regional HS Repair: Filed-sub Bids Due 2/11. G.C. due 2/20. NTP Targeted March.											
WILLIAMSBURG	170	\$12.0	\$9.6	Williamsburg Anne T. Dunphy IS Addition/Renovation: Filed-Sub Bids Due 2/12. G.C. Due 2/26. NTP Targeted March.											
*CONCORD/CARLISLE	1225	\$92.6	\$71.4	Concord/Carlisle HS New Construction: Filed-Sub Bids Due 2/4. GMP Targeted March.											
*NEWBURYPORT	845	\$26.9	\$21.8	Newburyport Nock ES Renovation: Filed-Sub Bids Due 2/18. GMP Targeted March.											
*GREENFIELD	585	\$63.4	\$52.9	Greenfield HS New Construction: Filed-Sub Bids Due 3/28. GMP Targeted April.											
*WAKEFIELD	1070	\$70.1	\$59.7	Wakefield Galvin MS New Construction: Filed-Sub Bids Due 5/7. GMP Targeted May.											
WEBSTER	720	\$44.9	\$35.8	Webster Park Ave ES New Construction: Filed-Sub Bids Due 5/21. G.C. Bids Due 6/6. NTP Targeted June.											
SOUTHWICK-TOLLAND-GRANVILLE PowderMill IS	545	\$18.5	\$14.8	PowderMill IS Repair: Filed-Sub Bids Due 4/10. G.C. Due 5/1. NTP Targeted May.											
SOUTHWICK-TOLLAND-GRANVILLE Woodland ES	400	\$9.7	\$7.3	Woodland ES Repair: Filed-Sub Bids Due 4/10. G.C. Due 5/1. NTP Targeted May.											
SOUTHWICK-TOLLAND-GRANVILLE STG Regional HS	790	\$40.7	\$31.4	STG MS/HS Addition/Renovation: Filed-Sub Bids Due 7/10. G.C. Due 7/31. NTP Targeted September.											
*SPRINGFIELD	320	\$27.9	22.7	Springfield Brookings ES New Construction: Filed-Sub Bids Due 8/28. GMP Targeted October.											
WEST BRIDGEWATER	625	\$63.7	49.7	West Bridgewater MS/HS New Construction: Filed-Sub Bids Due 8/28. G.C. Due 9/13. NTP Targeted September.											
Subtotal	10,440	\$675	\$546.2												
GRAND TOTAL	10,440	\$675	\$546.2												
Number of Construction-Related Employment Opportunities Created				2,731											

**Projects in Construction
MSBA Grant Basis and Maximum Grant Amount**

New Program and Wait List Program Totals			\$2,437,563,857	53,295		10,335,995											*Includes Alternates	\$1,727,814,160
Project	Grade	Contractor	Total Construction Cost*	Projected Enroll	PFA or Bid Data	Proposed Square Footage	Construction Cost per Square Foot	Building Cost	Building Cost per Square Foot	Project Type	Construction Start	Estimated Substantial Completion Date	Reporting Variance from Schedule	Physical Progress (%)	Change Orders (%)	Construction Status	Approximate Maximum Grant Amount *	
CAPITAL PIPELINE PROJECTS IN CONSTRUCTION																		
New Program Totals			\$2,348,940,893	51,235		9,872,305	\$233		\$176							\$1,566,751,525		
Arlington	K-5	G&R Construction	\$15,340,026	380	Bid	57,614	\$266	\$12,403,811	\$215	Design/Bid/Build	7-Apr-12	28-Jun-13		22%	0.72%	Foundations and footings have been installed and structural steel is substantially complete. Exterior wall work is progressing on the A & B sections of the building. Slab on deck placement is complete. Installation of underground utilities needed prior to slab on grade placement is ongoing.	\$9,441,396	
Berlin-Boylston Tahanto Reg MS/HS	6-12	CTA	\$32,162,000	560	Bid	126,100	\$255	24,629,999	\$195	Design/Bid/Build	10-May-11	1-Jul-13		87%	2.02%	Interior finishes are nearing completion. Completion of floors, wall panels, final electrical, and finish painting work is in process. Verizon work which is prerequisite to system tests, final inspections and permitting for the elevator, fire detection and other systems, is due to be completed by November 7, 2012. Substantial Completion for the building is planned for November 1, 2012. Completion of Punchlist work, FFE installation, and final permitting is needed to support occupancy in early January 2013.	\$19,849,301	
Billerica Parker ES	K-5	CTA	\$22,842,500	500	Bid	89,093	\$256	\$17,913,441	\$201	Design/Bid/Build	15-Sep-10	29-Aug-12	90 days	95%	0.00%	The new building is substantially complete. Phase II, demolition, is scheduled to be completed by November 26, 2012. \$382,161 of change orders, or 1.7% of construction cost, have been processed for approvals but have not been executed by the Contractor. Claims totaling \$1.9 M have been submitted by the Contractor and are pending resolution.	\$15,851,020	
Brookline Heath ES	K-8	Nauset	\$6,284,185	560	Bid	80,952	\$78	\$4,807,436	\$59	Design/Bid/Build	29-Sep-11	15-Aug-12		97%	1.33%	Punch list work remaining, in particular, the cafeteria, auditorium and library. Auditorium seating has been completed.	\$3,173,407	
Brookline Runkle ES	PK-8	G&R Construction	\$20,715,300	560	Bid	104,000	\$199	\$17,668,440	\$170	Design/Bid/Build	10-Nov-10	10-Sep-12		95%	7.86%	The new and renovated sections of the building opened on October 11, 2012. Punch list work is remaining.	\$11,135,430	
Carlisle Carlisle K-8	K-8	H.V. Collins Co. Inc	\$15,277,344	700	Bid	140,312	\$109	\$11,342,751	\$81	Design/Bid/Build	9-Feb-11	31-Aug-12		90%	3.20%	Punch list work continues.	\$6,988,636	
Danvers Danvers HS	9-12	Bacon Construction	\$53,834,164	1,000	Bid	246,251	\$219	\$43,710,809	\$178	Design/Bid/Build	14-Nov-10	2-Jul-13		86%	1.56%	Work continues on Phase I punch list. Phase II activities are ongoing with demolition and removal of the Dunn building. Steel erection, slabs on grade installations, roofing installations and rough-ins of mechanical and electrical systems are ongoing in the District offices.	\$37,324,055	
Douglas Douglas ES	2-5	CTA	\$23,857,111	552	Bid	83,100	\$287	\$19,026,763	\$229	Design/Bid/Build	Mar-12	9-Jun-13		26%	0.00%	Site work continues. ES steel placement complete. MEP roughins, metal stud framing, exterior sheathing and roofing are underway.	\$17,573,941	
Douglas Douglas HS	6-8	CTA	\$12,081,767	448	Bid	88,245	\$137	\$9,417,212	\$107	Design/Bid/Build	Mar-12	31-Jan-14		20%	0.00%	Site work continues. School is in session. Summer work is complete in the auditorium and gym areas.	\$8,203,129	
Dracut Dracut HS	9-12	CTA	\$47,290,611	1,160	PFA	174,671	\$271	\$29,420,210	\$168	Design/Bid/Build	27-Aug-12	17-Dec-14		2%	0.00%	Phase I construction has begun. Interior demolition and excavation for underground utilities are underway. Installation of foundations and footings are ongoing.	\$36,499,334	
East Bridgewater E. Bridgewater Jr/Sr HS	7-12	Fontaine Brothers	\$65,409,000	950	Bid	213,544	\$306	\$47,684,117	\$223	Design/Bid/Build	10-Aug-11	24-Jun-13		47%	0.07%	Site work is progressing to complete paving by the end of the year. Window installation has begun. MEP and sprinkler rough-ins have begun on the 3rd floor.	\$43,317,092	
Easthampton Easthampton HS	9-12	Fontaine Brothers	\$30,934,000	510	Bid	110,400	\$280	\$24,511,000	\$222	Design/Bid/Build	16-May-11	25-Oct-13	28 days	74%	1.27%	Continuing MEP rough-ins. Completing application of exterior wall foam insulation and metal paneling. Finishing interior cold rolled metal framing and starting drywall installation.	\$24,104,384	
Fairhaven Rogers ES	K-5	CTA	\$20,177,237	370	PFA	77,871	\$259	\$14,406,187	\$185	Design/Bid/Build	21-May-12	4-Jul-13		4%	0.00%	Excavation and compaction of footings and foundation wall in building A is nearing completion. Excavation and placement of underground utilities is ongoing. Slab on grade placement in B section was completed. Structural steel has been delivered and steel erection has started.	\$14,992,503	
Fall River Morton MS	6-8	J&J Contractors	\$37,654,000	625	Bid	130,576	\$288	\$29,921,971	\$229	Design/Bid/Build	4-Nov-11	15-Jun-13		45%	8.50%	Site work continues and paving is scheduled for the first week in November. MEP rough-ins are underway. Window installation will begin the end of October.	\$38,251,808	
Foxborough Foxborough HS	9-12	CTA	\$11,469,333	885	Bid	218,500	\$52	\$8,845,000	\$40	Design/Bid/Build	25-Jan-10	31-Oct-11		99%	10.28%	Final punch list and change order work is being completed. The District has implemented additional scope that has extended the final completion date. Work to be completed at or near end of October.	\$7,226,509	
Franklin Franklin HS	9 - 12	Agostini/Bacon	\$87,914,728	1,650	PFA	325,000	\$271	\$62,777,616	\$193.16	Design/Bid/Build	15-Oct-12	15-Oct-14		0%	0.00%	Notice To Proceed issued October 16, 2012. Contractor is mobilizing.	\$57,246,685	
Hampden-Wilbraham Minnechaug HS	9-12	Fontaine Brothers	\$48,597,500	1,225	Bid	231,467	\$210	\$37,499,962	\$162	Design/Bid/Build	22-Jul-10	28-Jun-12		94%	1.99%	Abatement and demolition of the existing High School have begun.	\$34,863,838	
Hingham Hingham MS	6-8	Brait Builders Corp.	\$50,432,439	1,020	PFA	176,385	\$286	\$38,006,989	\$215	Design/Bid/Build	7-Jun-12	30-Dec-14		17%	0.00%	Underground water and electrical service installations to the building continue and underground storm water infiltration system has been installed. Installation of under-slab plumbing and electrical systems have begun. Steel scheduled to arrive in November.	\$25,909,580	
Hudson John F Kennedy MS	5-7	Agostini/Bacon	\$35,102,573	715	Bid	118,850	\$295	\$28,373,294	\$239	Design/Bid/Build	28-Sep-11	22-Nov-13		57%	1.00%	Ongoing work includes MEP rough-ins, window installation, brick veneer work, interior drywall partitions, and the finishes on the mock up classroom. Building is expected to be weather tight by the end of October.	\$24,005,749	
Lynnfield Lynnfield HS	9-12	E.A. Colangeli	\$3,165,166	740	Bid	10,950	\$289	\$2,940,991	\$269	Design/Bid/Build	25-Jun-12	25-Jan-13		28%	0.00%	Contractor is progressing the first floor masonry and has installed piping, conduit, valves etc. to allow HVAC piping and electrical to be extended to the addition without interruption of service to the existing building. Work in the east parking lot is delayed due to unforeseen conditions.	\$1,948,020	
Marblehead Glover ES	K-3	G&R Construction	\$20,868,000	425	Bid	79,108	\$264	\$16,977,513	\$215	Design/Bid/Build	25-Jun-12	9-Dec-13		7%	0.00%	Abatement and demolition of the existing elementary school is complete. Pre-blast surveys were completed and blasting and excavation for foundations is in process.	\$9,688,418	
Marshfield Governor Winslow ES		Enterprise Equipment Co.	\$1,606,479	494	Bid	65,790	\$24	\$1,408,279	\$21	Design/Bid/Build	Apr-11	26-Aug-11		100%	1.45%	Project is complete and in closeout stage.	\$991,294	
Marshfield High School	9 - 12	Brait Brothers	\$87,308,752	1,310	PFA	267,469	\$326	\$57,027,596	\$213	Design/Bid/Build	Aug-12	7-Jul-14		1%	0.00%	Notice To Proceed issued August 16, 2012. Site work is underway.	\$49,225,401	
Maynard Maynard HS	8-12	CTA	\$36,650,000	410	Bid	121,520	\$302	\$30,630,013	\$252	Design/Bid/Build	18-Aug-11	6-Dec-13		47%	0.81%	Brick veneer work continues. Window and curtain wall installations have commenced. Final slabs have been poured and MEP rough-ins continue.	\$23,483,860	
Middleton Howe-Manning ES	4-6	CTA	\$18,210,000	553	Bid	83,934	\$217	\$14,529,671	\$173	Design/Bid/Build	06-Apr-10	30-Jul-11		99%	6.75%	New building occupied September 7, 2011. Completing change order work. Work scheduled to be complete by end of October.	\$12,311,976	
Nashoba Pompositicut ES	K-5	P.J. Stella Construction/Brait Builders	\$23,640,900	600	Bid	98,030	\$241	\$18,427,425	\$188	Design/Bid/Build	15-Jun-10	31-Aug-12		99%	3.78%	Contractor pursuing completion of remaining punchlist items as well as remaining site work including rear field resurfacing and sodding.	\$15,239,622	
Natick Natick HS	9-12	Brait Builders Corp.	\$63,303,452	1,300	Bid	254,225	\$249	\$53,213,182	\$209	Design/Bid/Build	13-Sep-10	15-Jun-12		92%	2.84%	Abatement and demolition of the existing building has been completed. Site work continues and is scheduled to be complete by the end of the year. Punch list items are still being addressed.	\$38,209,033	
Norfolk County Agricultural HS	9-12	TLT Construction Corp.	\$22,256,709	550	PFA	114,816	\$194	\$18,826,079	\$164	Design/Bid/Build	27-Mar-12	23-Aug-13		25%	0.21%	Installation of site utilities for the Animal Science (AS) Building and Agricultural-Mechanical (AG) Building underway. Slab-on-grade at AG is complete. Structural steel and MEP work at AG underway. Masonry work ongoing at AS. Foundation walls poured at Equine Center. Cut-over transition to new campus MDF room complete.	\$15,369,712	
Norfolk Freeman-Kennedy ES	3-6	Fontaine Brothers	\$25,354,966	585	Bid	96,410	\$263	\$20,023,001	\$208	Design/Bid/Build	9-Nov-10	10-Jun-12		92%	2.84%	Phase III demolition of existing building ongoing and expected to be done in December. Final paving and seeding may not be completed until the Spring.	\$15,861,760	
Norwood Norwood HS	9-12	Agostini	\$54,400,480	1,100	Bid	227,374	\$239	\$42,573,646	\$187	Design/Bid/Build	19-May-09	13-May-11		99%	2.40%	Landscaping issues to be completed by the end of October.	\$38,154,487	
Plymouth Plymouth HS	9-12	J&J Contractors	\$67,687,000	1,350	Bid	267,497	\$253	\$51,579,703	\$193	Design/Bid/Build	3-May-10	22-Jun-12	30 days	96%	4.75%	Abatement and demo of the existing building has been completed. Site work continues for the ball fields. Remaining paving scheduled for November.	\$41,810,972	
Quincy Central MS	6-8	H.V. Collins Co. Inc	\$32,699,769	620	PFA	114,975	\$284	\$27,182,118	\$236	Design/Bid/Build	24-May-12	5-Sep-13	14 days	18%	0.00%	Footings, foundations and structural steel are underway. Steel complete at bldg "A". Site utilities underway. Under-slab concrete placed at the gym.	\$32,949,685	
Somerset Berkely Somerset Berkley RHS	9-12	Agostini	\$66,840,822	1,000	PFA	222,826	\$300	\$49,956,137	\$224	Design/Bid/Build	3-Jul-12	15-Aug-14		1%	0.00%	Clearing and site work have begun.	\$50,068,817	
Sturbridge Burgess ES	K-6	Fontaine Brothers	\$22,946,000	860	Bid	131,630	\$174	\$17,591,000	\$134	Design/Bid/Build	10-Aug-10	1-Oct-12		97%	7.00%	Both the new addition and the adjacent building renovations are complete and in use. Abatement and demolition of the existing school have been completed. Construction of play area, ball fields and final landscaping are in process and are scheduled for completion in Spring 2013.	\$16,616,077	
Sutton MS/HS	6-12	TLT Construction Corp.	\$41,230,800	840	Bid	179,040	\$230	\$32,998,403	\$184	Design/Bid/Build	1-Jul-11	31-Dec-14	120 days	44%	0.26%	Ductwork installations continue in the Middle School and Media Center areas. Windows, roofing and exterior brick work are ongoing.	\$27,837,016	

**Projects in Construction
MSBA Grant Basis and Maximum Grant Amount**

Project	Grade	Contractor	Total Construction Cost*	Projected Enroll	PFA or Bid Data	Proposed Square Footage	Construction Cost per Square Foot	Building Cost	Building Cost per Square Foot	Project Type	Construction Start	Estimated Substantial Completion Date	Reporting Variance from Schedule	Physical Progress (%)	Change Orders (%)	Construction Status	Approximate Maximum Grant Amount *
Tewksbury Tewksbury HS	9-12	CTA/Methuen Construction Co.	\$51,600,000	1,100	Bid	218,781	\$236	\$40,159,651	\$184	Design/Bid/Build	15-Oct-10	3-Aug-12		88%	3.59%	Abatement and demolition of the existing school are underway. Punch list work continues.	\$36,622,570
West Springfield West Springfield HS	9-12	Fontaine Brothers	\$85,006,020	1,270	Bid	257,525	\$330	\$56,875,181	\$221	Design/Bid/Build	14-Dec-11	31-Dec-13		40%	0.00%	Curtain wall and window installation continues at Building A & B. Structural steel placement and roofing continue. Light gauge metal framing and MEP rough-ins have begun in Bldg A & B. Slabs on deck are being placed in Building C. Site work continues.	\$68,808,290
Winchester Vinson-Owen ES	K-5	CTA	\$21,290,000	420	PFA	74,774	\$285	17,586,599	\$235	Design/Bid/Build	17-Feb-12	13-May-13		39%	1.79%	Footings, foundations and structural steel are complete. Site utilities continue. Slabs-on-deck placed. Metal stud framing, sheathing and GWB underway.	\$10,292,465
Adams-Cheshire Hoosac Valley MSHS	6-12	Gilbane	\$33,474,193	805	Bid	174,758	\$192	24,009,952	\$137	CM-R	17-May-11	31-Jul-12		99%	0.06%	Commissioning is ongoing. PV installation scheduled to be completed by the end of November.	\$28,243,131
Burlington Marshall Simonds MS	6-8	CTA	\$24,612,440	880	Bid	151,000	\$163	\$18,988,987	\$126	CM-R	15-Apr-11	17-May-13	150 days ahead	84%	2.77%	Renovation of the eight remaining second floor classrooms in Areas 9 & 10 is ongoing with turnover scheduled for early November. Work is progressing in the auditorium, gymnasium, and locker rooms.	\$16,933,103
Dedham Avery ES	K-5	Consigli	\$18,174,209	310	Bid	62,723	\$290	\$13,528,098	\$216	CM-R	15-Oct-10	8-Mar-12		99%	6.50%	Completion of final punch list work (remedial loam and seeding) is ongoing.	\$10,778,452
Duxbury HS	6-12	Dimeo	\$104,511,661	1,735	PFA	322,105	\$324	\$66,940,020	\$208	CM-R	9-Jul-12	9-Jun-14		5%	0.00%	Site work and earthwork activities are underway. Building foundation work is underway with Area A foundations recently completed. Site utility work is advancing with the temporary relocation of the existing sewer line.	\$51,406,497
Essex North Shore Agricultural & Technical School	9-12	Gilbane	\$99,484,995	1,440	PFA	337,000	\$295	\$68,270,270	\$203	CM-R	7-May-12	30-Jun-14		8%	0.00%	Concrete placement continues for main building. Constructing access road behind building. Steel erection continues. Second crane on site and mobilized. Farmstead building site prep commenced. Site development of upper Middleton fields, including retaining walls, continues.	\$77,500,000
Grafton Memorial Sr HS	9-12	Dimeo	\$54,881,977	900	Bid	186,000	\$295	\$41,783,110	\$225	CM-R	18-Aug-10	12-Jul-12		93%	5.40%	New building is complete and minor punch list work continues. Installation of the second turf field along with the baseball field is near completion.	\$36,108,679
Leominster Leominster SHS	9-12	S.O.M.	\$33,794,797	1,825	Bid	295,859	\$114	\$25,382,707	\$86	CM-R	1-Jul-11	30-Aug-13		72%	4.99%	Work is progressing in the 2012 Fall- 2013 Winter phase. Underground plumbing and rough sprinkler, HVAC and electrical work are underway. Additional CMU and metal framing are ongoing. Structural steel for new roof has been installed.	\$30,693,543
Longmeadow Longmeadow HS	9-12	Gilbane	\$63,685,998	1,000	Bid	236,985	\$269	\$46,573,364	\$197	CM-R	Nov-10	1-Nov-13		58%	0.82%	Masonry work is nearing completion. Interior finishes are underway.	\$33,067,140
Medway MS	5-8	Consigli	\$18,211,824	800	Bid	223,780	\$81	\$12,885,464	\$58	CM-R	Oct-11	28-Feb-13	60 days ahead	83%	1.00%	This is a 4-phase project. Phase 1 and 2 were completed as scheduled and the Phase 1 area was turned over on April 18, 2012. Currently working on Phase 1 and 2 punch lists. Phase 3, which was the "summer slammer" to get the school ready for the students return, was completed on August 15, 2012. Phase 3 punch list work is ongoing and Phase 4 has begun.	\$10,352,981
Methuen Methuen HS	9-12	Terminated Dimeo 12/31/2011. Consigli as of 5/21/2012	\$74,917,204	2,075	PFA	368,017	\$204	\$63,689,716	\$173	CM-R	21-Jul-11	Jun-14		15%	0.00%	Foundation and site work for the new addition are ongoing. Phase I interior abatement is ongoing. MEP rough-ins have begun.	\$64,734,701
Needham Newman ES	K-5	Consigli	\$19,064,745	754	Bid	119,264	\$160	\$13,367,855	\$112	CM-R	16-Jun-10	27-Aug-12		99%	8.40%	School is open and punch list work continues. Minor site work remains to be completed in October for a Certificate of Occupancy.	\$8,598,929
Norton Norton HS	9-12	WT Rich	\$27,023,541	700	Bid	130,755	\$207	\$20,590,559	\$157	CMR	12-Mar-12	27-Dec-13		30%	2.49%	Exterior brick and block veneer flashing completed where the old building meets the new addition. MEP work is progressing in the addition and the new mechanical room.	\$21,484,408
Rockland John Rogers MS/ HS	5-12	Agostini	\$66,362,037	1,525	Bid	275,700	\$241	\$47,724,091	\$173	CM-R	15-Jan-10	8/31/12 for MS 12/31/12 for HS		90%	2.58%	Phase 4 High School work continues including Band Room, TV Studios, Admin offices, Art Classrooms, and SPED Classrooms. High School completion is expected in December 2012. Demolition of existing John Rogers MS is now complete. Site work continues around the campus as well as the west side parking lot. Middle School and High School Phase 2 and 3 punch list is ongoing.	\$52,837,940
Saugus Belmonte Middle School	6-8	Consigli	\$15,712,630	709	PFA	160,000	\$98	\$11,141,407	\$70	CM-R	23-May-12	23-Aug-13		22%	1.00%	Phase 1A is complete and Phase 1B has begun. Mechanical, electrical and plumbing rough-in are nearly complete. Elevator pit and foundation are complete and CMU shaft construction is underway. Delivery of windows, exterior metal panels and unit ventilators are critical path. They are scheduled for delivery in early November and are being monitored very closely by the Project Team.	\$10,097,544
Shrewsbury Sherwood MS	5-6	Gilbane	\$33,986,286	900	Bid	129,378	\$263	\$22,823,030	\$176	CM-R	7-Mar-11	31-Oct-13		87%	2.00%	Punchlist and commissioning activities are in process. Substantial completion for the building is planned for November. Exterior landscaping and paving work is in process. Abatement and demolition of the old school building is expected to begin in January 2013.	\$22,369,828
Somerville E. Somerville Community School	K-8	Gilbane	\$32,590,244	500	Bid	121,100	\$269	\$24,613,842	\$203	CM-R	7-Nov-11	6-Mar-13		66%	0.30%	Exterior windows and finishes continue. Interior MEP rough-ins are ongoing. Site is being prepped for paving in November.	\$15,237,996
Southbridge Southbridge MS/HS	6-12	Consigli	\$59,307,632	1,050	Bid	199,740	\$297	\$41,487,200	\$208	CM-R	30-Nov-10	18-Jun-12	77 days	99%	0.56%	Minor punchlist work remaining. Project closeout is in progress.	\$52,019,398
Southeastern Regional Voc Tech High School	9-12	WT Rich	\$26,576,567	1,370	PFA	308,250	\$86	\$17,611,703	\$57	CM-R	27-Jun-11	20-Jan-14		30%	0.20%	The Phase II (Interior Renovation) work was completed and a partial Certificate of Occupancy has been granted. Exterior brick veneer for the Phase 1 (New Gymnasium) work is nearly complete. All interior CMU wall partitions in the new gym addition and locker rooms are complete. The concrete slab ramp leading up to the addition access point has been placed. Completed site work includes bio retention basins 1 -4, early education playground & fencing, installation of new granite curbing and associated asphalt paving.	\$25,988,607
Uxbridge High School	9-12	Shawmut Design	\$37,293,765	600	Bid	123,000	\$303	\$27,562,625	\$224	CM-R	28-Feb-11	20-Jun-12		93%	2.50%	School is open and construction of the all-purpose fields continue.	\$21,973,620
Wayland ** Wayland HS	9-12	Shawmut Design	\$54,230,819	900	Bid	171,000	\$317	\$37,343,299	\$218	CM-R	28-Jun-10	1-Dec-11		99%	2.76%	Minor punch list items remaining.	\$24,051,231
Wellesley Wellesley HS	9-12	Turner	\$82,942,222	1,500	Bid	280,000	\$296	\$55,814,300	\$199	CM-R	24-Aug-09	1-May-13		98%	4.29%	Remaining site and utility work are underway. Binder course paving, curbing and sidewalk installations have commenced.	\$40,117,222
** Excludes Field House																	
Wait List Program Totals			\$120,784,964	2,060		463,690											\$141,213,334
Springfield Forest Park MS	6-8	Consigli	\$34,745,898	660	Bid	148,800	\$234	\$26,209,932	\$176	CM-R	26-Mar-12	26-Jul-13		20%	0.00%	Site work is ongoing. Third floor ductwork installation has begun. Concrete pour of the gym floor slab is complete. MEP rough work on all floors along with drywall framing are in progress. Roof work is ongoing.	\$38,340,497
Springfield Putnam Voc Tech HS	9-12	Consigli	\$86,039,066	1,400	Bid	314,890	\$273	\$62,949,742	\$200	CM-R	18-May-10	20-Jul-12		92%	0.66%	Demolition of existing building continues. Punch list work on new building is scheduled to be completed by the end of November.	\$102,872,837
Worcester North HS	9-12	Gilbane	\$49,145,638	1,200	Bid	239,570	\$205	\$40,860,983	\$171	CM-R	24-Sep-08	Jun-11		90%	3.20%	The phase 4 contractor mobilized to complete site drainage and infrastructure associated with the parking lots and reconstruction of the ball fields. The existing HS has been demolished	\$45,911,881
