

Project Overview Report

January 4, 2011

A total of 310 projects are currently in the MSBA's Capital Pipeline. The following summary table provides the category (e.g., New Program, Green Repair) and the number of projects in each phase (e.g., Local Clearance, Construction):

	Total	Local Clearance	Consultant Selection	Feasibility Study/ Schematic Design	Design Development	Construction
Closeout/Audit Complete	108					
New Program	106	5	15	28	23	35
Waitlist	4	0	1	0	2	1
Green Repair	92	0	0	8	22	62
Total	310	5	16	36	47	98

The MSBA utilizes the Project Status chart (see attached) to account for the ongoing status of all District Statements of Interest (SOIs) in the Capital Pipeline. Activity for some of the key milestones is summarized in the table below with the numbers reported indicative of the category requirements. For instance, enrollment certifications are not required for all projects (e.g., repairs) and Owner's Project Managers (OPMs) are not mandatory for construction projects under \$1.5 million unless required by the MSBA.

Critical Prerequisites

An agreed-upon enrollment is a key prerequisite for the MSBA to commence a Feasibility Study with a District. To begin the enrollment projection process, a District must file enrollment information utilizing the MSBA's online enrollment projection tool.

After the MSBA and the District have agreed upon an enrollment on which to base the design and executed a Feasibility Study Agreement, the District procures an Owner's Project Manager and then a Designer. There are 10 Districts in the Capital Pipeline who still need to procure an OPM.

After a District has selected an OPM and executed a contract with that OPM, it selects a Designer utilizing either a local designer selection process for projects under \$5 million or the MSBA's Designer Selection Panel (DSP) for projects over \$5 million. There are 19 Districts in the Capital Pipeline who still need to procure a Designer.

	District Action to Complete	MSBA/ District Collaboration	Completed Activity this Period	Total Completed to Date	Total
Enrollment	6	10	2	114	104,035
Owner's Project Manager	5	7	3	114	Over \$84 million in OPM fees*
Designer	12	9	3	140	Over \$207.6 million in Designer Fees*

* Does not include OPM and Designer Fees associated with repair projects.

Owner's Project Managers

Since the last report, the following three Districts have completed the OPM selection process:

- Revere – McKinley Elementary School
- Harwich-Chatham – Monomoy Regional High School
- Berkshire Hills Regional School District – Monument Mountain Regional High School

The following Districts are tentatively scheduled for the upcoming OPM Review Panel meetings:

Panel Date	District/School	Project Description Status	Estimated Project Cost
3/5/2012	Southwick-Tolland-Granville – Middle/High School, Woodland Elementary School, and Powder Mill Elementary School	Approved Project Vote Pending	\$71.8 million
3/5/2012	Winchester High School	Feasibility Study	\$60-\$90 million

Designers

Since the last report, the DSP has met four times, resulting in three additional Districts completing the designer selection process.

Panel Date	District/School	Status	Estimated Project Cost	# of Proposals Received	Top 3 Ranked Firms	Interviews Requested	First-Ranked Selection
11/8/11	South Hadley – Plains Elementary School	Feasibility Study	\$15 - \$20 million	14	- Margo Jones - Flansburgh - Design Partnership of Cambridge	Yes	TBD
11/22/11	South Hadley – Plains Elementary School	Feasibility Study	\$15 - \$20 million	14	- Margo Jones - Flansburgh - Design Partnership of Cambridge	Interviews Held	Margo Jones
12/6/11	Ayer-Shirley RSD – Ayer-Shirley Middle/High School	Feasibility Study	\$30 - \$40 million	11	- SMMA - Design Partnership of Cambridge - Flansburgh	Yes	TBD
12/6/11	Gr. Lowell VoTech – Gr. Lowell Reg. Tech. High School	Feasibility Study	\$24 - \$32 million	5	- Knight, Bagge & Anderson - Kaestle Boos - Lamoureux Pagano	No	Knight, Bagge & Anderson
12/20/11	Ayer-Shirley RSD – Ayer-Shirley Middle/High School	Feasibility Study	\$30 - \$40 million	11	- SMMA - Design Partnership of Cambridge - Flansburgh	Interviews Held	SMMA
12/20/11	Newburyport – Nock/Molin Middle School	Designer Selection	\$9.6 - \$14.4 million	7	- Miller Dyer Spears - SMMA - Flansburgh	Yes	TBD
12/20/11	Auburn – Auburn Middle School	Designer Selection	\$20 - \$40 million	12	- ARC - Lamoureux Pagano - OMR	Yes	TBD

The following Districts are tentatively scheduled for upcoming DSP meetings:

- Newburyport – Rupert A Nock Middle School – interviews on January 10, 2012
- Winchester High School (Repair) – selection on January 10, 2012
- Whitman-Hanson – Maquan Elementary School – selection on January 10, 2012
- Auburn – Auburn Middle School – interviews on January 24, 2012
- Chicopee – Chicopee High School Renovation – selection on January 24, 2012
- Spencer-East Brookfield – David Prouty High School – selection on February 28, 2012 (tentative)

Commissioning

Since the last report, the MSBA has assigned Commissioning Consultants to an additional eight projects as presented in the table below. The MSBA has executed 159 Commissioning Consultant contracts to date, totaling \$13.0 million.

District	School	Estimated Const. Cost (million)	Commissioning Consultant	Contract Amount
Weston	Field Elementary School	\$21.49	Foreman Building Commissioning	\$74,545
Saugus	Belmonte Middle School	\$15.73	Consulting Engineering Services	\$120,000
Marshfield	Marshfield High School	\$80.85	Sebesta Blomberg & Associates, Inc.	\$200,602
Somerset-Berkley	Somerset Berkley Reg. High School	\$66.84	Horizon Engineering Associates	\$167,119
New Salem-Wendell	Swift River Elementary School	\$0.92	Strategic Building Solutions	\$16,168
Marlborough	Marlborough High School	\$1.70	RDK Engineers	\$26,090
Marlborough	Green Repair - Multiple Schools	\$5.17	Building Enclosure Associates	\$48,000
Pioneer Valley	Green Repair - Multiple Schools	\$0.54	Strategic Building Solutions	\$21,360
Total		\$193.24 million	Total	\$673,884

There are currently no projects for which we are seeking proposals or negotiating Work Orders.

Projects that are in the queue for assignment of a Commissioning Consultant and for which contract documents are being drafted include:

District	School
Assabet Valley	Assabet Valley Voc High School
Franklin	Franklin High School
Southern Worcester County Voc/Tech	Bay Path Regional Voc/Tech High School
Stoneham	Stoneham Middle School
Williamsburg	Anne T Dunphy Intermediate School
Wilmington	Wilmington High School
Haverhill	Green Repair - Multiple Schools
Hadley	Hopkins Academy
Lowell	Green Repair - Multiple Schools
Southwick-Tolland	Woodland Elementary School

Status of Green Repair Program


171 projects have received authorization to enter into a Project Funding Agreement (PFA), totaling \$368,580,906 in Total Project Costs and \$224,252,881 in MSBA Total Facilities Grant funding.

Green Repair Project Phase

99% - 171 projects authorized for PFA

Total Project Budgets \$368,580,906

Total Maximum Facilities Grants \$224,252,881

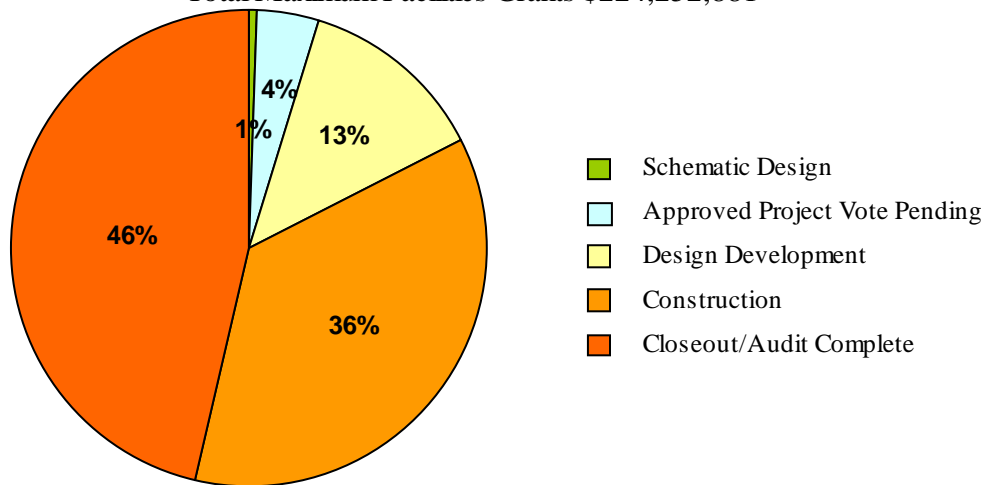

Construction Bids

The following displays the total anticipated number of projects going out to bid between January 1, 2012 – April 30, 2012:

	Roofs	Windows	Boilers
January	10	10	6
February	7	8	3
March	4	4	1
April	2	0	1
Total Remaining Bids	23	22	11

Of the bids reviewed:

- 77% of roof projects have come in under budget
- 70% of window projects have come in under budget
- 41% of boiler projects have come in under budget

Districts remaining in Schematic Design:

The following project is currently in the schematic design phase and is working with the MSBA to reach the conclusion of its study:

District	School	Scope	Invite Date
Westport	Westport Middle School	Windows	November 17, 2010

The following projects will be removed from the Green Repair Program:

District	School	Scope	Invite Date
Haverhill	Caleb Dustin Hunking Middle School	Windows	November 17, 2010
Haverhill	Greenleaf Elementary School	Roof	November 17, 2010

Green Repair Program Labor Data Update

The MSBA's 2010 Needs Survey found that the majority of the state's school facilities are generally in good condition, yet many of those facilities have specific building systems (roofs, windows, and boilers) in need of repair. Since its launch in March 2010, the Green Repair Program has provided over 90 districts with the opportunity to access MSBA funding in order to complete much needed repairs to roofs, windows, and boilers across multiple facilities.

The Associated General Contractors of America reported that Massachusetts saw a 2.8% increase in construction employment in 2011. The MSBA's Green Repair Program has contributed to the recent increase in construction employment, with approximately 130 roof, window, and boiler construction contracts bid in 2011 and 57 construction contracts scheduled to bid in 2012. These projects offered employment opportunities for owner's project managers, designers, and various construction trades including: carpenters, electricians, masons, plumbers, roofers, HVAC, and sheet metal workers.

Owner's project managers were asked to submit labor data for roof, window, and boiler projects completed in 2011. To date, MSBA staff has reviewed data on 56 construction contracts totaling approximately 22,927 days of work. This represents 43% of construction contracts bid in 2011. Not all construction jobs bid in 2011 are complete, and owner's project managers will continue to submit data as projects conclude throughout 2012.

In terms of estimated construction contract dollars, the projects reported represent \$61,665,820, or 35% of total construction dollars bid in 2011, and 22% of the total estimated construction costs associated with the Green Repair Program.

Scope	Number of Projects	Construction Budget	Square Footage	Days of Work*
Roof	34	\$44,715,472	1,919,727	15,439
Window	8	\$4,301,658	48,056	3,383
Boiler	12	\$8,247,138	1,344,271	2,670
Roof, Window, Boiler	2	\$4,401,552	96,505	1,435
Total	56	\$61,665,820	3,408,559	22,927

*One day of work equals eight hours

The following chart illustrates the number of 8-hour days of labor created per construction division as reported by owner's project managers for 56 completed projects:

Trade	Tradespeople	Laborer
Division 3 - Concrete	250	218
Division 4 - Masonry	704	244
Division 5 - Metals	17	32
Division 6 - Woods, Plastics and Composites	190	0
Division 7 - Thermal and Moisture Protection	13,652	505
Division 8 - Openings	2,840	615
Division 9 - Finishes	179	81
Division 22 - Plumbing	485	20
Division 23 - HVAC	1,232	405
Division 25 - Integrated Automation	198	74
Division 26 - Electrical	258	76
Other	317	335
Total	20,322	2,605

The Green Repair Team will continue to track labor data as more projects finish over the next year. Data is still being collected for approximately 20 construction contracts completed in 2011. After all 2011 data is compiled and reviewed, MSBA staff will use this information to determine the number of employment opportunities created in 2011 and generate a forecast for 2012 employment opportunities created by the Green Repair Program.

Massachusetts School Building Authority

No. of Projects: 317

Master District Status List

Yellow = Wait List Project
Green = Green Repair
Red = Changes in last 60 days

District Name	School Name	Status	Preferred Schematic	OPM	Designer	Cx Authority	Procurement Status	CM/GC
Abington PS	Woodsdale IS	Design Development	Repair	RF Walsh Collaborative Partners	Gale Associates, Inc.	Russo Barr Associates, Inc.		
Abington PS	Frolio JHS	Eligibility Period					Undetermined	
Acton PS	Douglas ES	Closeout/Audit	Repair	N/A	CBI Consulting Inc.		Undetermined	Gibson Roofs
Adams-Cheshire PS	Adams MS	Building Completion 2013	Addition/Renovation	URS Corporation	Tessier Associates, Inc.	Strategic Building Solutions, LLC	CMR - CM Selected	Gilbane Building Company
Agawam PS	Agawam Junior HS	Building Completion 2012	Repair	Municipal Building Consultants, Inc.	CSS Architects Incorporated	Building Enclosure Associates		
Amherst-Pelham PS	Amherst Reg MS	Design Development	Repair	Strategic Building Solutions, LLC	Bradley Architects, Inc.	Russo Barr Associates, Inc.		
Andover PS	Andover West MS	Closeout/Audit	Repair	Skanska USA Building Inc.	Russo Barr Associates, Inc.	Simpson Gumpertz & Heger Inc.		
Andover PS	Bancroft ES	Design Development	New Construction	Town of Andover	Symmes Maini & McKee Associates, Inc.	Sebesta Blomberg & Associates, Inc.	CMR - CM Selected	Skanska USA Building, Inc.
Arlington PS	M Norcross Stratton ES	Closeout/Audit	Repair	PMA Consultants	Turowski2 Architecture, Inc.		Undetermined	Unicon, Inc. and Federal Construction Corp.
Arlington PS	Thompson ES	Design Development		PMA Consultants	HMFH Architects, Inc.	Consulting Engineering Services, LLC	DBB - In Design	
Ashburnham-West PS	Briggs ES	Design Development	New Construction	STV, Inc.	Lamoureux Pagano & Associates, Inc.	Foreman Building Commissioning, LP	CMR - CM Selected	Consigli Construction Co.
Assabet Valley PS	Assabet Valley Voc HS	Approved Project Vote Pending	Repair	Strategic Building Solutions, LLC	Design Partnership of Cambridge, Inc.			
Athol-Royalston PS	Riverbend ES	OPM Selection						
Attleboro PS	Attleboro HS	Building Completion 2011	Repair	Skanska USA Building, Inc.	Russo Barr Associates, Inc.	Gale Associates, Inc.		
Attleboro PS	A. Irvin Studley ES	Building Completion 2011	Repair	Skanska USA Building, Inc.	Russo Barr Associates, Inc.	Gale Associates, Inc.		
Attleboro PS	Hill-Roberts ES	Building Completion 2011	Repair	Skanska USA Building, Inc.	Russo Barr Associates, Inc.	Gale Associates, Inc.		
Attleboro PS	Hyman Fine ES	Building Completion 2011	Repair	Skanska USA Building, Inc.	Russo Barr Associates, Inc.	Gale Associates, Inc.		
Auburn PS	Auburn MS	Designer Selection						
Avon PS	Ralph D Butler ES	Closeout/Audit	Repair	Skanska USA Building Inc.	Knight, Bagge & Anderson, Inc.	Cannon Design		
Ayer PS	Ayer HS	Feasibility Study		Dore and Whittier Architects, Inc.	Symmes Maini & McKee Associates, Inc.			
Barnstable PS	West Barnstable ES	Building Completion 2011	Repair	PMA Construction Services	Gale Associates, Inc.	CBI Consulting Inc.		
Bellingham PS	Bellingham Memorial MS	Closeout/Audit	Repair	Daedalus Projects Inc	Richard D. Kimball Company, Inc.	WSP Flack + Kurtz	Undetermined	General Air Conditioning & Heating, Inc.
Belmont PS	Roger E Wellington ES	Closeout/Audit	New Construction	PMA Consultants	Jonathan Levi Architects LLC	Strategic Building Solutions, LLC	CMR - CM Selected	Skanska USA Building, Inc.

Master District Status List

Yellow = Wait List Project

Green = Green Repair

Red = Changes in last 60 days

District Name	School Name	Status	Preferred Schematic	OPM	Designer	Cx Authority	Procurement Status	CM/GC
Berkshire Hills PS	Monument Mt Reg HS	OPM Selection						
Berlin-Boylston PS	Tahanto Reg HS	Building Completion 2013	New Construction	PMA Consultants	HMFH Architects, Inc.	Strategic Building Solutions, LLC	DBB - Contract Awarded	CTA Construction
Beverly PS	Beverly HS	Closeout/Audit	Addition/Renovation	Heery International	Mount Vernon Group Architects, Inc.		DBB - Contract Awarded	CTA Construction Co.
Billerica PS	Billerica Memorial HS	Building Completion 2011	Repair	Municipal Building Consultants, Inc.	Knight, Bagge & Anderson, Inc.	Building Enclosure Associates		
Billerica PS	Parker ES	Building Completion 2012	New Construction	Joslin, Lesser & Associates, Inc.	Symmes Maini & McKee Associates, Inc.	Sebesta Blomberg & Associates, Inc.	DBB - Contract Awarded	CTA Construction Co
Blackstone Valley Reg PS	Blackstone Valley HS	Building Completion 2011	Repair	Strategic Building Solutions, LLC	Reinhardt Associates, Inc.	Cannon Design		
Boston PS	Thomas A Edison JHS	Closeout/Audit	Repair	Daedalus Projects Inc	BLW Engineers, Inc.	Simpson Gumpertz & Heger Inc.		
Boston PS	Quincy Upper School	Feasibility Study		City of Boston	HMFH Architects, Inc.			
Boston PS	Clarence R Edwards MS	Closeout/Audit	Repair	Daedalus Projects Inc	BLW Engineers, Inc.	Rist-Frost-Shumway Engineering, P.C.		
Boston PS	Washington Irving MS	Closeout/Audit	Repair	Daedalus Projects Inc	Gale Associates, Inc.	Simpson Gumpertz & Heger Inc.		
Boston PS	Excel HS	Building Completion 2012	Repair	Daedalus Projects Inc	Gale Associates, Inc.	Simpson Gumpertz & Heger Inc.		
Boston PS	Dearborn MS	OPM Selection						
Boston PS	Joseph Lee ES*	Closeout/Audit	Repair	Daedalus Projects Inc	BLW Engineers, Inc./Gale Associates, Inc.	Simpson Gumpertz & Heger Inc.		
Boxford PS	Harry Lee Cole Primary	Closeout/Audit	Repair		Russo Barr Associates, Inc.		Undetermined	MDM Engineering, Inc
Braintree PS	South MS	Closeout/Audit	Repair	Town Employee	Habeeb & Associates Architects, Inc.		DBB - Contract Awarded	Construction Dynamics
Braintree PS	Hollis ES	Closeout/Audit	Repair	RF Walsh Collaborative Partners	Habeeb & Associates Architects, Inc.	Cannon Design		
Braintree PS	Highlands	Closeout/Audit	Repair	RF Walsh Collaborative Partners	Habeeb & Associates Architects, Inc.	Cannon Design		
Braintree PS	East MS	Closeout/Audit	Repair	RF Walsh Collaborative Partners	Habeeb & Associates Architects, Inc.	Cannon Design		
Braintree PS	Archie T Morrison ES	Closeout/Audit	Repair	RF Walsh Collaborative Partners	Habeeb & Associates Architects, Inc.	Cannon Design		
Braintree PS	Braintree HS	Closeout/Audit	Repair	RF Walsh Collaborative Partners	Habeeb & Associates Architects, Inc.	Cannon Design		
Brockton PS	Brockton HS	Building Completion 2012	Repair	Skanska USA Building Inc.	CSS Architects Incorporated	Simpson Gumpertz & Heger Inc.		
Brockton PS	Downey ES	Building Completion 2012	Repair	Skanska USA Building Inc.	CSS Architects Incorporated	Simpson Gumpertz & Heger Inc.		
Brockton PS	East Junior HS	Building Completion 2012	Repair	Skanska USA Building Inc.	CSS Architects Incorporated	Rist-Frost-Shumway Engineering, P.C.		
Brockton PS	Edgar B Davis ES	Building Completion 2012	Repair	Skanska USA Building Inc.	CSS Architects Incorporated	Simpson Gumpertz & Heger Inc.		
Brockton PS	North Junior HS	Building Completion 2011	Repair	Skanska USA Building Inc.	CSS Architects Incorporated	Rist-Frost-Shumway Engineering, P.C.		
Brockton PS	Oscar F Raymond ES	Building Completion 2012	Repair	Skanska USA Building Inc.	CSS Architects Incorporated	Simpson Gumpertz & Heger Inc.		

Master District Status List

Yellow = Wait List Project

Green = Green Repair

Red = Changes in last 60 days

District Name	School Name	Status	Preferred Schematic	OPM	Designer	Cx Authority	Procurement Status	CM/GC
Brockton PS	West Junior HS	Building Completion 2011	Repair	Skanska USA Building Inc.	CSS Architects Incorporated	Simpson Gumpertz & Heger Inc.		
Brockton PS	Hancock ES	Building Completion 2011	Repair	Skanska USA Building Inc.	CSS Architects Incorporated	Simpson Gumpertz & Heger Inc.		
Brookfield PS	Brookfield ES	Building Completion 2012	Repair	Diversified Project Management	Habeeb & Associates Architects, Inc.	Cannon Design		
Brookline PS	Heath K-8	Building Completion 2012	Addition/Renovation	Town of Brookline Building Department	Miller Dyer Spears Inc.	Consulting Engineering Services, LLC		
Brookline PS	John D Runkle K-8	Building Completion 2012	Addition/Renovation	Town of Brookline Building Department	Design Partnership of Cambridge, Inc.	Consulting Engineering Services, LLC	DBB - Contract Awarded	G&R construction Inc.
Burlington PS	Marshall Simonds MS	Building Completion 2013	Addition/Renovation	Construction Monitoring Services, Inc.	Knight, Bagge & Anderson, Inc.	RDK Engineers	CMR - CM Selected	CTA Construction Co.
Burlington PS	Memorial ES	Closeout/Audit	New Construction	Construction Monitoring Services, Inc.	Knight, Bagge & Anderson, Inc.	Consulting Engineering Services, LLC	DBB - Contract Awarded	CTA Construction Co.
Cambridge PS	Cambridge Rindge and Latin HS	Closeout/Audit			HMFH Architects, Inc.		DBB - Contract Awarded	W.T. Rich, Inc.
Canton PS	Rodman Pre-K Center	Building Completion 2011	Repair	Maguire Group	Russo Barr Associates, Inc.	Cannon Design		
Canton PS	Canton HS	Building Completion 2011	Repair	Maguire Group	Russo Barr Associates, Inc.	Cannon Design		
Cape Cod Region Voc Tech PS	Cape Cod Regional Voc / Tech HS	Approved Project Vote Pending	Repair	URS Corporation	Garcia Galuska DeSousa			
Carlisle PS	Carlisle K-8	Building Completion 2012	Addition/Renovation	Daedalus Projects, Inc.	HMFH Architects, Inc.	Horizon Engineering Associates, LLP	DBB - Contract Awarded	H.V. Collins Company
Central Berkshire PS	Kittredge ES	Design Development	Repair	Daedalus Projects Inc	Bradley Architects, Inc.	Strategic Building Solutions, LLC		
Central Berkshire PS	Craneville ES	Design Development	Repair	Daedalus Projects Inc	Bradley Architects, Inc.	Strategic Building Solutions, LLC		
Chatham PS	Chatham HS	OPM Selection						
Chelmsford PS	Chelmsford HS	Design Development	Repair	Vertex Construction Services, Inc.	Russo Barr Associates, Inc.	Simpson Gumpertz & Heger Inc.		
Chelmsford PS	Byam ES	Design Development	Repair	Vertex Construction Services, Inc.	Russo Barr Associates, Inc.	Simpson Gumpertz & Heger Inc.		
Chelsea PS	Clark Avenue MS	Eligibility Period			Jacobs			
Chicopee PS	Chicopee Academy	Designer Selection		Arcadis				
Concord-Carlisle PS	Concord Carlisle HS	Design Development		KV Associates, Inc.	OMR Architects, Inc.	Strategic Building Solutions, LLC	CMR - Procurement Pending	
Conway PS	Conway Grammar ES	Closeout/Audit	Repair		Richardson Gorman Architects		Undetermined	RAC Builders, Inc.
Danvers PS	Danvers HS	Building Completion 2013	Addition/Renovation	Construction Monitoring Services, Inc.	DiNisco Design Partnership, Limited	Turner Facilities Management Solutions	DBB - In Design	Bacon Construction Co., Inc.
Dartmouth PS	James M. Quinn ES	Closeout/Audit	Repair	Vertex Construction Services, Inc.	Russo Barr Associates, Inc.	Gale Associates, Inc.		
Dartmouth PS	James M. Quinn ES	Closeout/Audit	Repair					
Dedham PS	Avery ES	Building Completion 2012	New Construction	Construction Monitoring Services, Inc.	Dore & Whittier Architects, Inc.	WSP Flack + Kurtz	CMR - CM Selected	Consigli Construction Co
Dennis-Yarmouth PS	Ezra H Baker ES	Building Completion 2012	Repair	STV Construction, Inc.	Knight, Bagge & Anderson, Inc.	CBI Consulting Inc.		

Master District Status List

Yellow = Wait List Project	
Green = Green Repair	Red = Changes in last 60 days

District Name	School Name	Status	Preferred Schematic	OPM	Designer	Cx Authority	Procurement Status	CM/GC
Douglas PS	Douglas IS	Design Development		Heery International, Inc	DiNisco Design Partnership, Limited	Consulting Engineering Services, LLC	DBB - In Design	
Dracut PS	Dracut SHS	Design Development	Addition/Renovation	RF Walsh Collaborative Partners	Mount Vernon Group Architects, Inc.	RDK Engineers	DBB - In Design	
Dudley-Charlton Reg PS	Shepherd Hill Reg HS	Closeout/Audit	Repair	Pinck & Co., Inc.	ICON architecture, inc.	Cannon Design		
Duxbury PS	Duxbury HS	Design Development		KV Associates, Inc.	Mount Vernon Group Architects, Inc.	WSP Flack + Kurtz	CMR - IG Application Pending	
East Bridgewater PS	East Bridgewater HS	Building Completion 2013	Model School	RF Walsh Collaborative Partners	Ai3 Architects LLC	Foreman Building Commissioning, LP	DBB - Contract Awarded	Fontaine Bros., Inc.
Easthampton PS	Easthampton HS	Building Completion 2013	New Construction	Strategic Building Solutions, LLC	Caolo & Bieniek Associates, Inc.	Consulting Engineering Services, LLC	DBB - Contract Awarded	Fontaine Bros., Inc
Essex North Shore Agr and Tech PS	Essex North Shore Agr and Tech School	Design Development	New Construction	PMA Consultants	Design Partnership of Cambridge, Inc.	Turner Facilities Management Solutions	CMR - CM Selected	Gilbane Building Company
Fairhaven PS	Rogers ES	Design Development		Daedalus Projects Inc	HMFH Architects, Inc.	Consulting Engineering Services, LLC	DBB - In Design	
Fairhaven PS	Hastings MS	Closeout/Audit	Repair	Daedalus Projects Inc	Durland Van Voorhis Architects, Inc.	Gale Associates, Inc.		
Fall River PS	Morton MS	Building Completion 2013		Maguire Group Inc.	Mount Vernon Group Architects, Inc.	Sebesta Blomberg & Associates, Inc.	DBB - Out to Bid	
Falmouth PS	Falmouth High School	Building Completion 2011	Addition/Renovation	Gilbane Building Company	DiNisco Design Partnership, Limited		DBB - Contract Awarded	TLT Construction
Falmouth PS	North Falmouth ES	Closeout/Audit	Repair		Keenan + Kenny Architects, LTD	Gale Associates, Inc.		
Falmouth PS	East Falmouth ES	Closeout/Audit	Repair		Keenan + Kenny Architects, LTD	Gale Associates, Inc.		
Fitchburg PS	South Street ES	Building Completion 2012	Repair	Compass Project Management, Inc.	BLW Engineers, Inc.	RDK Engineers		
Fitchburg PS	Fitchburg HS	Closeout/Audit	Repair	Compass Project Management, Inc.	BLW Engineers, Inc.	RDK Engineers		
Fitchburg PS	Goodrich K Center	Closeout/Audit	Repair	Compass Project Management, Inc.	BLW Engineers, Inc.	RDK Engineers		
Fitchburg PS	Reingold ES	Closeout/Audit	Repair	Compass Project Management, Inc.	Knight, Bagge & Anderson, Inc.	RDK Engineers		
Fitchburg PS	Reingold ES	Building Completion 2012	Repair	Compass Project Management, Inc.	BLW Engineers, Inc.	Simpson Gumpertz & Heger Inc.		
Fitchburg PS	Memorial IS	Building Completion 2012	Repair	Compass Project Management, Inc.	Knight, Bagge & Anderson, Inc.	Simpson Gumpertz & Heger Inc.		
Fitchburg PS	South Street ES	Closeout/Audit		Compass Project Management, Inc.	Knight, Bagge & Anderson, Inc.	Simpson Gumpertz & Heger Inc.		
Fitchburg PS	Memorial IS	Closeout/Audit	Repair	Compass Project Management, Inc.	BLW Engineers, Inc.	RDK Engineers		
Florida PS	Abbott Memorial K-8	Closeout/Audit	Repair		Dietz and Company		DBB - Contract Awarded	Waterman Excavating, Inc
Florida PS	Abbott Memorial K-8	Closeout/Audit	Repair					
Foxborough PS	Foxborough HS	Closeout/Audit	Repair	Construction Monitoring Services, Inc.	Kaestle Boos Associates, Inc.	Consulting Engineering Services, LLC	DBB - Contract Awarded	CTA Construction Co.
Framingham PS	Mary E Stapleton ES	Building Completion 2012	Repair	Bargmann, Hendrie + Archetype, Inc.	Russo Barr Associates, Inc.	CBI Consulting Inc.		
Franklin PS	Franklin HS	Project Scope & Budget	Model School	Daedalus Projects Inc.	Ai3 Architects LLC			

Master District Status List

Yellow = Wait List Project

Green = Green Repair

Red = Changes in last 60 days

District Name	School Name	Status	Preferred Schematic	OPM	Designer	Cx Authority	Procurement Status	CM/GC
Gardner PS	Waterford Street Primary	Closeout/Audit	Repair	P3 Project Planning Professionals	Knight, Bagge & Anderson, Inc.	Building Enclosure Associates		
Gardner PS	Gardner HS	Closeout/Audit	Repair	P3 Project Planning Professionals	Knight, Bagge & Anderson, Inc.	Building Enclosure Associates		
Gardner PS	Elm Street IS	Closeout/Audit	Repair	P3 Project Planning Professionals	Knight, Bagge & Anderson, Inc.	Building Enclosure Associates		
Georgetown PS	Penn Brook IS	Preferred Schematic		Municipal Building Consultants, Inc.	Drumme Rosane Anderson, Inc.			
Gloucester PS	Plum Cove School	Closeout/Audit	Repair	Knight, Bagge, & Anderson, Inc.	CGKV Architects, Inc.	Russo Barr Associates, Inc.		
Gloucester PS	Beeman Memorial IS	Closeout/Audit	Repair	Knight, Bagge, & Anderson, Inc.	CGKV Architects, Inc.	Russo Barr Associates, Inc.		
Gloucester PS	West Parish ES	Eligibility Period						
Gloucester PS	Veterans Memorial ES	Closeout/Audit	Repair	Knight, Bagge, & Anderson, Inc.	CGKV Architects, Inc.	Russo Barr Associates, Inc.		
Gloucester PS	Ralph B O'Maley MS	Closeout/Audit	Repair	Knight, Bagge, & Anderson, Inc.	CGKV Architects, Inc.	Russo Barr Associates, Inc.		
Gloucester PS	East Gloucester ES	Closeout/Audit	Repair	Knight, Bagge, & Anderson, Inc.	CGKV Architects, Inc.	Russo Barr Associates, Inc.		
Grafton PS	Grafton Memorial SHS	Building Completion 2012	Repair	URS Corporation	CGKV Architects, Inc.			
Grafton PS	Grafton Memorial SHS	Building Completion 2012	New Construction	Joslin, Lesser & Associates, Inc.	Symmes Maini & McKee Associates, Inc.	Horizon Engineering Associates, LLP	CMR - CM Selected	Dimeo Construction
Grafton PS	South Grafton ES	Design Development	Repair	URS Corporation	CGKV Architects, Inc.	Horizon Engineering Associates, LLP		
Greater Lawrence RVT PS	Gr Lawrence Regional Voc / Tech HS	OPM Selection						
Greater Lowell Voc Tec PS	Gr Lowell Regional Voc / Tech HS	Feasibility Study	Repair	Heery International, Inc	Knight, Bagge & Anderson, Inc.			
Greater New Bedford PS	Gr New Bedford Voc / Tech HS	Feasibility Study		Construction Monitoring Services, Inc.	Drumme Rosane Anderson, Inc.			
Greenfield PS	Four Corners ES	Building Completion 2012	Repair	P3 Project Planning Professionals	Tighe & Bond, Inc.	Strategic Building Solutions, LLC		
Greenfield PS	Greenfield HS	Preferred Schematic		Construction Monitoring Services, Inc.	Dore & Whittier Architects, Inc.			
Hadley PS	Hopkins Academy	Design Development	Repair	Strategic Building Solutions, LLC	CSS Architects Incorporated			
Hamilton-Wenham PS	Cutler ES	Closeout/Audit	Repair	Municipal Building Consultants, Inc.	Richard D. Kimball Company, Inc.	Sebesta Blomberg & Associates, Inc.	DBB - Contract Awarded	Thomas E. Snowden Inc.
Hampden-Wilbraham PS	Minnechaug Reg HS	Building Completion 2012	Model School	ARCADIS U.S., Inc.	Mount Vernon Group Architects, Inc.	Horizon Engineering Associates, LLP	DBB - Contract Awarded	Fontaine Bros.
Hancock PS	Hancock ES	Building Completion 2011	Repair	N/A	Westall Architects			
Hanover PS	Hanover HS	Building Completion 2011	New Construction	PMA Consultants	HMFH Architects, Inc.	Horizon Engineering Associates, LLP	DBB - Contract Awarded	Callahan, Inc
Haverhill PS	Consentino MS	Approved Project Vote Pending	Repair	Vertex Construction Services, Inc.	CSS Architects Incorporated			
Haverhill PS	Greenleaf Primary	Approved Project Vote Pending	Repair	Vertex Construction Services, Inc.	CSS Architects Incorporated			
Haverhill PS	Haverhill HS	Construction		Vertex Construction Services, Inc.			DBB - Contract Awarded	

Master District Status List

Yellow = Wait List Project	
Green = Green Repair	Red = Changes in last 60 days

District Name	School Name	Status	Preferred Schematic	OPM	Designer	Cx Authority	Procurement Status	CM/GC
Haverhill PS	John G Whittier MS	Approved Project Vote Pending	Repair	Vertex Construction Services, Inc.	CSS Architects Incorporated			
Haverhill PS	Tilton Primary	Approved Project Vote Pending	Repair	Vertex Construction Services, Inc.	CSS Architects Incorporated			
Haverhill PS	Walnut Square Primary	Approved Project Vote Pending	Repair	Vertex Construction Services, Inc.	CSS Architects Incorporated			
Haverhill PS	Caleb Dustin Hunking MS	Approved Project Vote Pending	Repair	Vertex Construction Services, Inc.	CSS Architects Incorporated			
Hingham PS	Hingham MS	Design Development	Model School	Knight, Bagge & Anderson, Inc.	Ai3 Architects LLC	Foreman Building Commissioning, LP	DBB - In Design	
Holbrook PS	Holbrook JHS / SHS	Eligibility Period						
Holyoke PS	Holyoke HS	Closeout/Audit			Design Partnership of Cambridge, Inc.		DBB - Contract Awarded	
Hopkinton PS	Center ES	Approved Project Vote Pending	New Construction	Town of Hopkinton	Design Partnership of Cambridge, Inc.		Undetermined	
Hudson PS	John F Kennedy MS	Building Completion 2013	New Construction	PMA Consultants	OMR Architects, Inc.	WSP Flack + Kurtz	DBB - Contract Awarded	Bacon/ Agostini Construction
Leicester PS	Leicester Memorial ES	Closeout/Audit	Repair	Maguire Group	Bradley Architects, Inc.			
Leicester PS	Leicester MS	Closeout/Audit	Repair	Maguire Group	Bradley Architects, Inc.	Cannon Design		
Leominster PS	Leominster SHS	Building Completion 2013	Addition/Renovation	Daedalus Projects, Inc.	Lamoureux Pagano & Associates, Inc.	Horizon Engineering Associates, LLP	CMR - CM Selected	WT Rich
Leverett PS	Leverett ES	Building Completion 2012	Repair	Potomac Capital Advisors	DiMarinisi & Wolfe Architects Urban	Russo Barr Associates, Inc.		
Lexington PS	Lexington HS	Closeout/Audit	Repair	Skanska USA Building Inc.	Russo Barr Associates, Inc.	Simpson Gumpertz & Heger Inc.		
Lexington PS	Joseph Estabrook ES	Preferred Schematic	New Construction	RF Walsh Collaborative Partners	DiNisco Design Partnership, Limited			
Lincoln PS	Lincoln K-8	Preferred Schematic	Addition/Renovation	Skanska USA Building, Inc.	OMR Architects, Inc.			
Littleton PS	Russell St ES	Closeout/Audit	Repair	Daedalus Projects, Inc.	Drummeey Rosane Anderson, Inc.	WSP Flack + Kurtz	DBB - Contract Awarded	Colantonio, Inc.
Longmeadow PS	Longmeadow HS	Building Completion 2013	New Construction	Joslin, Lesser & Associates, Inc.	OMR Architects, Inc.	Foreman Building Commissioning, LP	CMR - CM Selected	Gilbane Building Company
Lowell PS	Charles W Morey ES	Closeout/Audit		Watermark			DBB - Contract Awarded	CTA Construction Co.
Lowell PS	Lowell HS	Approved Project Vote Pending	Repair	NETCO Construction Project Managers, Inc.	ICON architecture, inc.			
Lowell PS	Moody ES	Approved Project Vote Pending	Repair	NETCO Construction Project Managers, Inc.	ICON architecture, inc.			
Lowell PS	Peter W Reilly ES	Approved Project Vote Pending	Repair	NETCO Construction Project Managers, Inc.	ICON architecture, inc.			
Lowell PS	Washington ES	Design Development	Repair	NETCO Construction Project Managers, Inc.	ICON architecture, inc.	RDK Engineers		
Lunenburg PS	Lunenburg HS	Eligibility Period						
Lynn PS	Thurgood Marshall MS	OPM Selection						
Lynnfield PS	Lynnfield HS	Project Scope & Budget			Edward Rowse Architects, Inc.			

Master District Status List

Yellow = Wait List Project	
Green = Green Repair	Red = Changes in last 60 days

District Name	School Name	Status	Preferred Schematic	OPM	Designer	Cx Authority	Procurement Status	CM/GC
Malden PS	Malden HS	Building Completion 2011	Renovation	URS Corporation	Flansburgh Associates, Inc.		CMR - CM Selected	Gilbane Building Company
Manchester Essex Regional PS	Manchester JHS / SHS	Closeout/Audit		Design Technique	Mount Vernon Group Architects, Inc.		DBB - Contract Awarded	TLT Construction
Marblehead PS	Glover Primary	Design Development	New Construction	Municipal Building Consultants, Inc.	JCJ Architecture, PC	RDK Engineers	DBB - In Design	
Marblehead PS	Village IS	Closeout/Audit	Repair	Municipal Building Consultants, Inc.	Symmes Maini & McKee Associates, Inc.	RDK Engineers	DBB - Contract Awarded	Groom Construction
Marlborough PS	Francis J Kane Primary	Project Scope & Budget	Repair	RF Walsh Collaborative Partners	Baker/Wohl Architects, Inc.	Building Enclosure Associates		
Marlborough PS	Marlborough HS	Project Scope & Budget	Repair	RF Walsh Collaborative Partners	Baker/Wohl Architects, Inc.	RDK Engineers		
Marshfield PS	Gov Edward Winslow ES	Closeout/Audit	Repair	Vertex Construction Services, Inc.	Knight, Bagge & Anderson, Inc.	RDK Engineers	DBB - Contract Awarded	Enterprise Equipment Co., Inc.
Marshfield PS	Marshfield HS	Design Development	Model School		Ai3 Architects LLC	Sebesta Blomberg & Associates, Inc.		
Maynard PS	Maynard HS	Building Completion 2013	New Construction	Municipal Building Consultants, Inc.	Tappe Associates, Inc.	WSP Flack + Kurtz	DBB - Contract Awarded	CTA Construction
Medway PS	Medway MS	Building Completion 2013		Compass Project Management, Inc.	Knight, Bagge & Anderson, Inc.	Sebesta Blomberg & Associates, Inc.	CMR - CM Selected	Consigli Construction Co.
Melrose PS	Melrose HS	Closeout/Audit	Repair	Municipal Building Consultants, Inc.	Gale Associates, Inc.	Russo Barr Associates, Inc.		
Mendon-Upton PS	Miscoe Hill IS	Building Completion 2012	Repair	Maguire Group	Habeeb & Associates Architects, Inc.			
Methuen PS	Methuen HS	Building Completion 2013	Addition/Renovation	KBA/Trident	Finegold Alexander and Associates Inc.	Environmental Health and Engineering	CMR - CM Selected	Dimeo Construction
Middleborough PS	Mary K. Goode ES	Construction	Repair	Maguire Group	Habeeb & Associates Architects, Inc.	Russo Barr Associates, Inc.		
Middleton PS	Howe-Manning IS	Closeout/Audit	New Construction	RF Walsh Collaborative Partners	DiNisco Design Partnership, Limited	Foreman Building Commissioning, LP	DBB - Contract Awarded	CTA Construction Co.
Minuteman Voc Tech PS	Minuteman Reg HS	Eligibility Period						
Mohawk Trail PS	Mohawk Trail Reg HS	Design Development	Repair	Potomac Capital Advisors	Bradley Architects, Inc.	Strategic Building Solutions, LLC		
Mohawk Trail PS	Colrain Central ES	Design Development	Repair	Potomac Capital Advisors	Bradley Architects, Inc.	Strategic Building Solutions, LLC		
Mohawk Trail PS	Buckland-Shelburne Reg ES	Design Development	Repair	Potomac Capital Advisors	Bradley Architects, Inc.	Strategic Building Solutions, LLC		
Mount Greylock PS	Mt Greylock Reg HS	Closeout/Audit	Repair	N/A	Hesnor Engineering & Barry Architects	Horizon Engineering Associates, LLP	DBB - Contract Awarded	Adams Plumbing & Heating
Narragansett PS	Phillipston Memorial ES	Building Completion 2012	Repair	Potomac Capital Advisors	DiMarinisi & Wolfe Architects Urban	Rist-Frost-Shumway Engineering, P.C.		
Narragansett PS	Templeton Center	Feasibility Study (on hold)		Strategic Building Solutions, LLC	Symmes Maini & McKee Associates, Inc.		Undetermined	
Narragansett PS	Narragansett MS	Building Completion 2011	Repair	Potomac Capital Advisors	DiMarinisi & Wolfe Architects Urban	Rist-Frost-Shumway Engineering, P.C.		
Nashoba PS	Pompositicut Primary	Building Completion 2012	Addition/Renovation	Construction Monitoring Services, Inc.	Symmes Maini & McKee Associates, Inc.	Strategic Building Solutions, LLC	DBB - Contract Awarded	Stella P.J. Construction Corp.
Nashoba Valley Tech PS	Nashoba Valley Tech HS	Design Development	Repair					
Natick PS	Natick HS	Building Completion 2013	Model School	RF Walsh Collaborative Partners	Ai3 Architects LLC	Rist-Frost-Shumway Engineering, P.C.	DBB - Contract Awarded	Brait Builders Corporation

Master District Status List

Yellow = Wait List Project

Green = Green Repair

Red = Changes in last 60 days

District Name	School Name	Status	Preferred Schematic	OPM	Designer	Cx Authority	Procurement Status	CM/GC
Nauset PS	Nauset Reg HS	Approved Project Vote Pending	Repair	NETCO Construction Project Managers, Inc.	Habeeb & Associates Architects, Inc.	CBI Consulting Inc.		
Needham PS	Newman ES	Building Completion 2011	Repair	Town of Needham	Drummeay Rosane Anderson, Inc.	Rist-Frost-Shumway Engineering, P.C.	CMR - CM Selected	Consigli Construction Co.
Needham PS	Pollard MS	Closeout/Audit	Repair	STV Construction, Inc.	Gale Associates, Inc. Gale Associates, Inc.	CBI Consulting Inc.		
New Bedford PS	John Hannigan ES	OPM Selection						
New Bedford PS	Abraham Lincoln	Closeout/Audit	New Construction	Daedalus Projects Inc	Mount Vernon Group Architects, Inc.	Sebesta Blomberg & Associates, Inc.	DBB - Contract Awarded	CTA Construction Co.
New Bedford PS	New Bedford HS	OPM Selection						
New Salem-Wendell PS	Swift River ES	Building Completion 2011	Repair	Maguire Group	Bradley Architects, Inc.	Strategic Building Solutions, LLC		
Newburyport PS	Francis T Bresnahan ES	Project Scope & Budget			HMFH Architects, Inc.			
Newburyport PS	Rupert A Nock MS	Designer Selection						
Newton PS	Bowen ES	Building Completion 2011	Repair	STV Construction, Inc.	Habeeb & Associates Architects, Inc.			
Newton PS	Williams ES	Building Completion 2011	Repair	STV Construction, Inc.	Habeeb & Associates Architects, Inc.			
Newton PS	Newton North HS	Closeout/Audit	New Construction	Turner Construction Company	Dore & Whittier Architects, Inc.		CMR - CM Selected	Dimeo Construction
Norfolk County Agr PS	Norfolk County Agr HS	Design Development	Addition/Renovation	Compass Project Management, Inc	Turowski2 Architecture, Inc.	Rist-Frost-Shumway Engineering, P.C.	DBB - In Design	
Norfolk PS	Freeman-Centennial IS	Building Completion 2012	New Construction	Joslin, Lesser & Associates, Inc.	Flansburgh Associates, Inc.	WSP Flack + Kurtz	DBB - In Design	Fontaine Bros., Inc.
North Adams PS	Silvio O Conte MS	Preferred Schematic			Strategic Building Solutions, LLC	Margo Jones Architects, Inc.		
North Andover PS	North Andover MS	Approved Project Vote Pending	Repair	Municipal Building Consultants, Inc.	ICON architecture, inc.	Cannon Design		
North Andover PS	Atkinson ES	Approved Project Vote Pending	Repair	Municipal Building Consultants, Inc.	ICON architecture, inc.	Cannon Design		
North Andover PS	Annie L Sargent ES	Approved Project Vote Pending	Repair	Municipal Building Consultants, Inc.	ICON architecture, inc.	Cannon Design		
North Attleborough PS	Falls ES	Building Completion 2011	Repair	Atlantic Construction & Management, Inc.	CSS Architects Incorporated	Gale Associates, Inc.		
North Brookfield PS	North Brookfield ES	Design Development	Repair	Vertex Construction Services, Inc.	LPBA/ Architects, Inc.	Simpson Gumpertz & Heger Inc.		
North Middlesex PS	Ashby ES	Building Completion 2011	Repair	Compass Project Management, Inc.	Russo Barr Associates, Inc.	Building Enclosure Associates		
North Middlesex PS	Spaulding Memorial Primary	Building Completion 2011	Repair	Compass Project Management	Russo Barr Associates, Inc.	Building Enclosure Associates		
North Reading PS	North Reading HS	Preferred Schematic		PMA Consultants	Dore & Whittier Architects, Inc.			
Northampton-Smith PS	Smith Vocational and Agricultural HS	Eligibility Period						
Northborough PS	Robert E. Melican MS	Design Development	Repair	Pinck & Co., Inc.	ICON architecture, inc.	Strategic Building Solutions, LLC		
Northeast Metro Voc PS	Northeast Metro Reg Voc HS	Eligibility Period						

Master District Status List

Yellow = Wait List Project	
Green = Green Repair	Red = Changes in last 60 days

District Name	School Name	Status	Preferred Schematic	OPM	Designer	Cx Authority	Procurement Status	CM/GC
Norton PS	Norton HS	Design Development		Pinck & Co., Inc.	JCJ Architecture, PC	Rist-Frost-Shumway Engineering, P.C.	CMR - CM Selected	Consigli Construction Co
Norwood PS	Norwood HS	Building Completion 2011	Model School	Compass Project Management, Inc.	Ai3 Architects LLC		DBB - Contract Awarded	Agostini Construction Company, Inc.
Old Colony Reg Voc Tech PS	Old Colony Regional Voc / Tech HS	OPM Selection						
Orange PS	Dexter Park IS	Eligibility Period						
Orange PS	Butterfield MS	Closeout/Audit	Repair		Tighe & Bond, Inc.		Undetermined	SOM Construction, Inc.
Oxford PS	Oxford MS	OPM Selection	Repair					
Palmer PS	Palmer HS	Building Completion 2012	Repair	Diversified Project Management	Tighe & Bond, Inc.	Strategic Building Solutions, LLC		
Palmer PS	Converse MS	Building Completion 2012	Repair	Diversified Project Management	Tighe & Bond, Inc.	Strategic Building Solutions, LLC		
Palmer PS	Old Mill Pond ES	Building Completion 2012	Repair	Diversified Project Management	Tighe & Bond, Inc.	Strategic Building Solutions, LLC		
Peabody PS	William A Welch Sr ES	Building Completion 2012	Repair	Daedalus Projects Inc	LPBA/ Architects, Inc.	Sebesta Blomberg & Associates, Inc.		
Peabody PS	J Henry Higgins MS	Feasibility Study	Repair	Daedalus Projects Inc	DiNisco Design Partnership, Limited			
Peabody PS	John E Burke ES	Building Completion 2012	Repair	Daedalus Projects Inc	LPBA/ Architects, Inc.	Sebesta Blomberg & Associates, Inc.		
Pentucket PS	Dr Frederick N Sweetsir Primary	Building Completion 2012	Repair	PMA Consultants	Knight, Bagge & Anderson, Inc.	CBI Consulting Inc.		
Pentucket PS	Dr John C Page ES	Building Completion 2011	Repair	PMA Consultants	Knight, Bagge & Anderson, Inc.	RDK Engineers		
Pentucket PS	Elmer S Bagnall ES	Building Completion 2011	Repair	PMA Consultants	Knight, Bagge & Anderson, Inc.	CBI Consulting Inc.		
Pentucket PS	Helen R Donaghue IS	Building Completion 2011	Repair	PMA Consultants	Knight, Bagge & Anderson, Inc.	CBI Consulting Inc.		
Pioneer Valley PS	Pioneer Valley Reg MS / HS	Approved Project Vote Pending	Repair	Diversified Project Management	CGKV Architects, Inc.	Strategic Building Solutions, LLC		
Pioneer Valley PS	Northfield ES	Approved Project Vote Pending	Repair	Diversified Project Management	CGKV Architects, Inc.	Strategic Building Solutions, LLC		
Pittsfield PS	Taconic HS	Feasibility Study		Skanska USA Building, Inc.				
Plymouth PS	Plymouth Community IS	Closeout/Audit	Repair		Knight, Bagge & Anderson, Inc.	Building Enclosure Associates		
Plymouth PS	Plymouth North HS	Building Completion 2012	Model School	Ted Gentry Associates	Ai3 Architects LLC	Sebesta Blomberg & Associates, Inc.	DBB - Contract Awarded	J&J Contractors Inc.
Plymouth PS	West ES	Closeout/Audit	Repair					
Quabbin PS	Oakham Center ES	Closeout/Audit	Repair		Russo Barr Associates, Inc.	Building Enclosure Associates	DBB - Contract Awarded	Cape Way Roofing
Quabbin PS	Quabbin Reg HS	Closeout/Audit	Repair	Vertex Construction Services, Inc.	LPBA/ Architects, Inc.	Building Enclosure Associates		
Quincy PS	Central MS	Design Development	New Construction	Tishman Construction Corporation of MA	Ai3 Architects LLC	Sebesta Blomberg & Associates, Inc.	DBB - In Design	
Reading PS	Birch Meadow ES	Building Completion 2011	Repair	Knight, Bagge, & Anderson, Inc.	LPBA/ Architects, Inc.	Russo Barr Associates, Inc.		

Master District Status List

Yellow = Wait List Project

Green = Green Repair

Red = Changes in last 60 days

District Name	School Name	Status	Preferred Schematic	OPM	Designer	Cx Authority	Procurement Status	CM/GC
Reading PS	J Warren Killam ES	Closeout/Audit	Repair	Knight, Bagge, & Anderson, Inc.	LPBA/ Architects, Inc.	Russo Barr Associates, Inc.		
Revere PS	William McKinley ES	Designer Selection						
Revere PS	Paul Revere ES	Building Completion 2011	New Construction	RF Walsh Collaborative Partners	Drummey Rosane Anderson, Inc.		DBB - Contract Awarded	Delulis Brothers Construction Company
Rochester PS	Rochester Memorial ES	Closeout/Audit	Addition/Renovation	PMA Consultants	Flansburgh Associates, Inc.	Horizon Engineering Associates, LLP	CMR - CM Selected	Gilbane Building Company
Rockland PS	John W Rogers MS	Building Completion 2012	Addition/Renovation	Daedalus Projects Inc	Dore & Whittier Architects, Inc.	Consulting Engineering Services, LLC	CMR - CM Selected	Agostini Construction Company, Inc.
Rockland PS	R Stewart Esten ES	Construction	Repair	Daedalus Projects Inc	Habeeb & Associates Architects, Inc.	Russo Barr Associates, Inc.		
Rockport PS	Rockport ES	Closeout/Audit	Repair	N/A	Russo Barr Associates, Inc.			
Rockport PS	Rockport HS	Closeout/Audit	Repair		Russo Barr Associates, Inc.	Building Enclosure Associates	DBB - Contract Awarded	Feeley, McAnespie, Inc.
Salem PS	Saltonstall ES	Design Development	Repair	KV Associates, Inc.	Reinhardt Associates, Inc.	Rist-Frost-Shumway Engineering, P.C.		
Salem PS	Collins MS	Design Development	Repair	KV Associates, Inc.	Reinhardt Associates, Inc.	Rist-Frost-Shumway Engineering, P.C.		
Sandwich PS	Forestdale K-8	Design Development	Repair	NETCO Construction Project Managers, Inc.	Habeeb & Associates Architects, Inc.	Gale Associates, Inc.		
Sandwich PS	Oak Ridge K-8	Design Development	Repair	NETCO Construction Project Managers, Inc.	Habeeb & Associates Architects, Inc.	Gale Associates, Inc.		
Saugus PS	Belmonte Saugus MS	Design Development	Repair	Skanska USA Building, Inc.	Fletcher Thompson Architecture Engineering,	Consulting Engineering Services, LLC		
Scituate PS	Wampatuck ES	Closeout/Audit	Repair	Bargmann, Hendrie + Archetype, Inc.	Knight, Bagge & Anderson, Inc.	Rist-Frost-Shumway Engineering, P.C.		
Scituate PS	Gates IS	Closeout/Audit	Repair					
Sharon PS	Sharon HS	Closeout/Audit	Repair	Daedalus Projects Inc	Baker/Wohl Architects, Inc.	Cannon Design	Undetermined	Titan Roofing, Inc.
Sharon PS	Sharon MS	Building Completion 2012	Addition/Renovation	Daedalus Projects, Inc.	Kaestle Boos Associates, Inc.	Horizon Engineering Associates, LLP	CMR - CM Selected	Consigli Construction Co.
Shawsheen Valley Voc PS	Shawsheen Valley Voc / Tech HS	Closeout/Audit		Construction Monitoring Services Inc.	Knight, Bagge & Anderson, Inc.		DBB - Contract Awarded	Colantino Inc.
Shrewsbury PS	Spring Street ES	Building Completion 2012	Repair	PMA Consultants	Habeeb & Associates Architects, Inc.	Cannon Design		
Shrewsbury PS	Sherwood MS	Building Completion 2013	New Construction	PMA Consultants	Lamoureux Pagano & Associates, Inc.	RDK Engineers	CMR - CM Selected	Gilbane Building Company
Somerset PS	Somerset HS	Design Development		Skanska USA Building, Inc.	Ai3 Architects LLC	Horizon Engineering Associates, LLP		
Somerville PS	E Somerville Community K-8	Design Development	Renovation	City of Somerville	Maguire Group Inc.	Foreman Building Commissioning, LP	CMR - CM Selected	Gilbane Building Company
South Hadley PS	Plains ES	Feasibility Study		Arcadis	Margo Jones Architects, Inc.			
South Shore Reg Voc PS	South Shore Voc / Tech HS	Closeout/Audit	Repair	Vertex Construction Services, Inc.	Gale Associates, Inc.	Building Enclosure Associates		
Southbridge PS	Southbridge HS	Building Completion 2012	New Construction	Joslin, Lesser & Associates, Inc.	Tappe Associates, Inc.	Environmental Health and Engineering	CMR - CM Selected	Consigli Construction Co.
Southeastern Reg Voc Tech PS	Southeastern Regional Voc / Tech HS	Design Development	Addition/Renovation	RF Walsh Collaborative Partners	Drummey Rosane Anderson, Inc.	RDK Engineers	CMR - CM Selected	WT Rich Company Inc.

Master District Status List

Yellow = Wait List Project	
Green = Green Repair	Red = Changes in last 60 days

District Name	School Name	Status	Preferred Schematic	OPM	Designer	Cx Authority	Procurement Status	CM/GC
Southern Worcester Cty VT PS	Bay Path Regional Voc / Tech HS	Preferred Schematic		Heery International, Inc	Kaestle Boos Associates, Inc.			
Southwick-Tolland	Woodland ES	Approved Project Vote Pending		Strategic Building Solutions, LLC	JCJ Architecture, PC			
Spencer-E Brookfield PS	David Prouty HS	Designer Selection						
Springfield PS	Putnam Voc / Tech HS	Building Completion 2012	New Construction	ARCADIS	Drumme Rosane Anderson, Inc.	Strategic Building Solutions, LLC	CMR - CM Selected	Consigli Construction Co.
Springfield PS	Forest Park Middle School	Design Development	Addition/Renovation	ARCADIS-U.S., Inc.	Perkins Eastman	Foreman Building Commissioning, LP		
Springfield PS	Elias Brookings K-8	Preferred Schematic	Renovation					
Springfield PS	SCIPP Years 2 & 3	Building Completion 2012	Repair		CGKV Architects, Inc./Gale Associates, Inc.	Building Enclosure Associates		
Springfield PS	Dryden Memorial ES	Preferred Schematic	Addition/Renovation					
Stoneham PS	Stoneham MS	Project Scope & Budget		Joslin, Lesser & Associates	Tappe Associates, Inc.			
Sturbridge PS	Burgess ES	Building Completion 2012	Addition/Renovation	Lamoureux Pagano & Associates, Inc.	Drumme Rosane Anderson, Inc.	Horizon Engineering Associates, LLP	DBB - Contract Awarded	Fontaine Bros.
Sudbury PS	Peter Noyes ES	Closeout/Audit	Repair	Compass Project Management, Inc.	Russo Barr Associates, Inc./BLW Engineers, Inc.	RDK Engineers		
Sutton PS	Sutton MS	Building Completion 2013	Addition/Renovation	Strategic Building Solutions	Flansburgh Associates, Inc.	RDK Engineers	DBB - Contract Awarded	TLT Construction Corp.
Tantasqua PS	Tantasqua Reg JHS	Closeout/Audit	Repair	Diversified Project Management	Habeeb & Associates Architects, Inc.	Cannon Design		
Taunton PS	Taunton HS	Closeout/Audit	Addition/Renovation	Gilbane	Design Partnership of Cambridge, Inc.		DBB - Contract Awarded	Bacon-Agostini Construction Joint Venture
Tewksbury PS	Tewksbury Memorial HS	Building Completion 2012	Model School	Heery International, Inc	Symmes Maini & McKee Associates, Inc.	Sebesta Blomberg & Associates, Inc.	DBB - Contract Awarded	CTA Ventures/ Methuen
Tri County PS	Tri County Regional Voc / Tech HS	Building Completion 2011	Repair	Knight, Bagge, & Anderson, Inc.	Richard D. Kimball Company, Inc.	WSP Flack + Kurtz		
Upper Cape Cod Voc Tech PS	Upper Cape Cod Voc / Tech HS	Building Completion 2011	Repair	NETCO Construction Project Managers, Inc.	Knight, Bagge & Anderson, Inc.	Gale Associates, Inc.		
Uxbridge PS	Uxbridge HS	Building Completion 2012	New Construction	Joslin, Lesser & Associates, Inc.	Raymond Design Associates, Inc.	Turner Facilities Management Solutions	CMR - CM Selected	Shawmut Design and Construction
Wachusett PS	Mountview MS	Designer Selection		Town Employee				
Wachusett PS	Naquag ES	Building Completion 2012	Repair	Strategic Building Solutions, LLC	LPBA/ Architects, Inc.	Rist-Frost-Shumway Engineering, P.C.		
Wachusett PS	Paxton K-8 Center	Building Completion 2012	Repair	Strategic Building Solutions, LLC	LPBA/ Architects, Inc.	Rist-Frost-Shumway Engineering, P.C.		
Wachusett PS	Thomas Prince K-8	Building Completion 2012	Repair	Strategic Building Solutions, LLC	LPBA/ Architects, Inc.	Rist-Frost-Shumway Engineering, P.C.		
Wakefield PS	Galvin MS	Project Scope & Budget			Tappe Associates, Inc.			
Wakefield PS	Wakefield Memorial HS	Closeout/Audit	Addition/Renovation					
Wayland PS	Wayland HS	Building Completion 2011	New Construction	KV Associates	HMFH Architects, Inc.	WSP Flack + Kurtz	CMR - CM Selected	Shawmut Construction
Webster PS	Park Avenue ES	Preferred Schematic		RF Walsh Collaborative Partners	Dore & Whittier Architects, Inc.			

Master District Status List

Yellow = Wait List Project

Green = Green Repair

Red = Changes in last 60 days

District Name	School Name	Status	Preferred Schematic	OPM	Designer	Cx Authority	Procurement Status	CM/GC
Wellesley PS	Wellesley SHS	Building Completion 2012	New Construction	Ryegate Inc	Symmes Maini & McKee Associates, Inc.	Rist-Frost-Shumway Engineering, P.C.	CMR - CM Selected	Turner Construction
West Boylston PS	Major Edwards ES	Design Development	Repair	URS Corporation	Reinhardt Associates, Inc.	Cannon Design		
West Bridgewater PS	West Bridgewater JHS / SHS	Feasibility Study		Strategic Building Solutions, LLC	Flansburgh Associates, Inc.			
West Springfield PS	West Springfield HS	Building Completion 2014	Model School	Strategic Building Solutions, LLC	Symmes Maini & McKee Associates, Inc.	Turner Facilities Management Solutions	DBB - Out to Bid	
Westborough PS	Sarah W Gibbons MS	Eligibility Period						
Westfield PS	Highland School	Closeout/Audit	Repair	P3 Project Planning Professionals	Tighe & Bond, Inc.	Strategic Building Solutions, LLC		
Westfield PS	Southampton Road ES	Design Development	Repair	P3 Project Planning Professionals	Tighe & Bond, Inc.	Strategic Building Solutions, LLC	Undetermined	R&H Roofing
Westfield PS	Westfield Voc / Tech HS	Design Development	Repair	P3 Project Planning Professionals	Tighe & Bond, Inc.	Strategic Building Solutions, LLC		
Westfield PS	Westfield HS	Design Development	Repair	P3 Project Planning Professionals	Tighe & Bond, Inc.	Strategic Building Solutions, LLC		
Westfield PS	Paper Mill ES	Design Development	Repair	P3 Project Planning Professionals	Tighe & Bond, Inc.	Strategic Building Solutions, LLC		
Westfield PS	Abner Gibbs ES	Design Development	Model School	Skanska USA Building Inc.	Margo Jones Architects, Inc.	Horizon Engineering Associates, LLP	DBB - In Design	
Westfield PS	Highland School	Design Development	Repair	P3 Project Planning Professionals	Tighe & Bond, Inc.	Strategic Building Solutions, LLC	Undetermined	Allied Restoration
Westfield PS	Southampton Road ES	Closeout/Audit	Repair	P3 Project Planning Professionals	Tighe & Bond, Inc.	Strategic Building Solutions, LLC		
Weston PS	Field ES School	Design Development		Compass Project Management, Inc	Jonathan Levi Architects LLC	Foreman Building Commissioning, LP		
Weston PS	Weston HS	Closeout/Audit	Repair	Compass Project Management, Inc.	Garcia Galuska DeSousa	RDK Engineers		
Weston PS	Weston MS	Design Development	Repair	Compass Project Management, Inc.	Russo Barr Associates, Inc.	RDK Engineers		
Westport PS	Alice A Macomber ECC	Design Development	Repair	Pinck & Co., Inc.	CGKV Architects, Inc.	CBI Consulting Inc.		
Westport PS	Westport HS	Design Development	Repair	Pinck & Co., Inc.	CGKV Architects, Inc.	CBI Consulting Inc.		
Westport PS	Westport MS	Feasibility Study	Repair	Pinck & Co., Inc.	CGKV Architects, Inc.			
Weymouth PS	Abigail Adams MS	Closeout/Audit	Repair	Knight, Bagge, & Anderson, Inc.	Gale Associates, Inc.	Cannon Design		
Whitman-Hanson PS	John H Duval ES	Closeout/Audit	Repair		BETA Group, Inc.		Undetermined	S.I. Services, Inc.
Whitman-Hanson PS	Maquan ES	Designer Selection						
Williamsburg PS	Anne T Dunphy IS	Project Scope & Budget		Arcadis	Drumme Rosane Anderson, Inc.			
Wilmington PS	Wilmington HS	Design Development		Joslin, Lesser & Associates	Dore & Whittier Architects, Inc.		CMR - CM Selected	Gilbane Building Company
Wilmington PS	Shawsheen ES	Closeout/Audit	Repair	P3 Project Planning Professionals	Russo Barr Associates, Inc.	CBI Consulting Inc.		
Winchendon PS	Toy Town ES	Closeout/Audit	Repair	NETCO Construction Project Managers, Inc.	Hesnor Engineering Company	Rist-Frost-Shumway Engineering, P.C.		

Master District Status List


Yellow = Wait List Project	
Green = Green Repair	Red = Changes in last 60 days

District Name	School Name	Status	Preferred Schematic	OPM	Designer	Cx Authority	Procurement Status	CM/GC
Winchester PS	Winchester HS	OPM Selection						
Winchester PS	Vinson-Owen ES	Design Development	New Construction	Town of Winchester	Tappe Associates, Inc.	Turner Facilities Management Solutions	DBB - In Design	
Winchester PS	Lynch ES	Closeout/Audit	Repair		Knight, Bagge, & Anderson, Inc.	Gale Associates, Inc.	Simpson Gumpertz & Heger Inc.	
Winthrop PS	Winthrop Senior High	Designer Selection						
Woburn PS	John F Kennedy MS	Closeout/Audit	Repair			Skanska USA Building, Inc.		
Woburn PS	John F Kennedy MS	Closeout/Audit	Repair			Municipal Building Consultants, Inc.	Gale Associates, Inc.	Simpson Gumpertz & Heger Inc.
Woburn PS	Goodyear ES	Closeout/Audit	New Construction			Municipal Building Consultants, Inc.	Tappe Associates, Inc.	Strategic Building Solutions, LLC
Woburn PS	Daniel L Joyce MS	Closeout/Audit	Repair			Municipal Building Consultants, Inc.	Gale Associates, Inc.	Simpson Gumpertz & Heger Inc.
Worcester PS	North HS	Building Completion 2011				Maguire Group Inc	City of Worcester	CMR - CM Selected
								Gilbane Building Company

No. of Projects: 317

Project Status | January 4, 2012

New Program:	104
Waitlist:	4
Green Repair:	90
Project Complete / Closeout	100
Projects to be removed from Pipeline	4
Final Audit Approved	8
Total Projects:	310

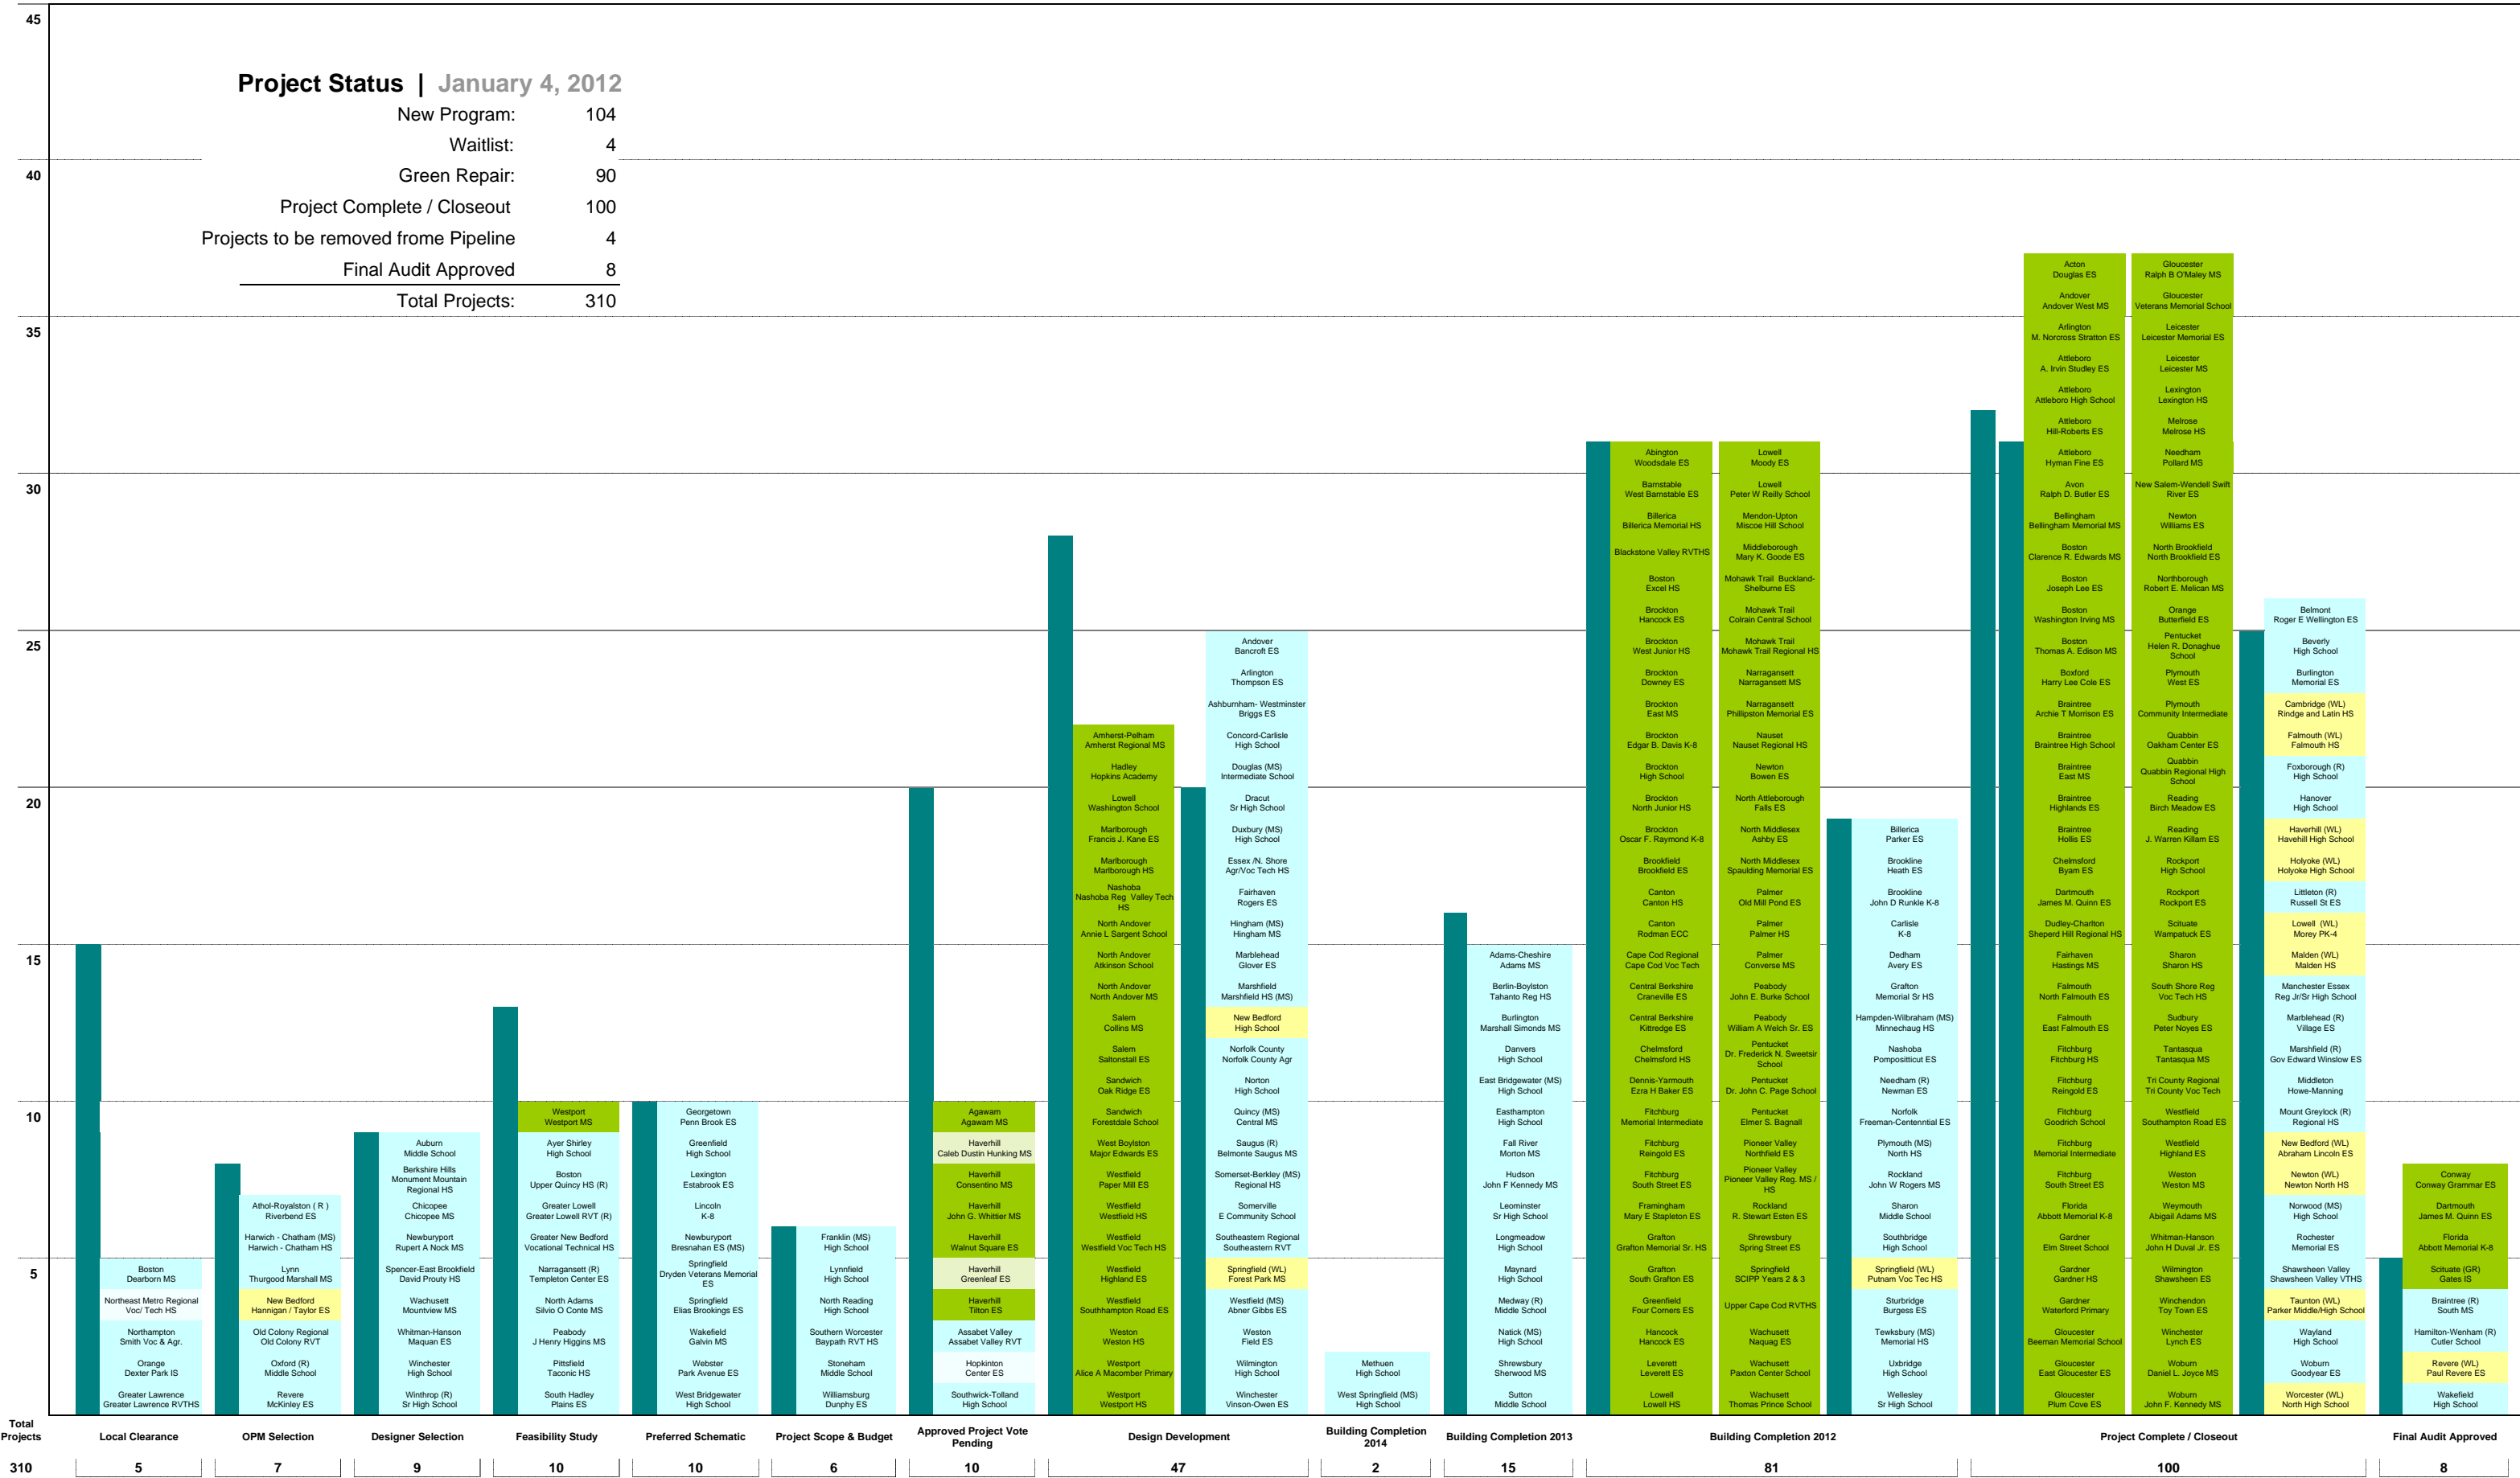

■ Green Repair Project - Removal from Pipeline
■ New Program Project - Removal from Pipeline
■ Waitlist Projects
■ Capital Pipeline Status Presented at November 16, 2011 Board of Directors Meeting

PROJECT STATUS

2012 Estimated Bid Dates

Note bid dates are **Estimates ONLY**. Please contact Districts for exact information.

Total Project Budget denotes total District costs and does not denote the basis of the MSBA Total Facilities Grant.

■ - Denotes bid phase in progress or complete
 ■ - Denotes estimated bid dates
 ■ - Denotes estimated GMP dates

DISTRICT	DESIGN BASIS FOR ENROLLMENT	PROJECT BUDGET <small>Shown in Millions</small>	CONSTRUCTION BUDGET <small>Shown in Millions</small>	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC			
*Projects Considering the CM @ Risk Method																		
*ASHBURNHAM-WESTMINSTER	520	\$30.0	\$24.8	■	■	JR Briggs ES New Construction: Filed-Sub Bids Due 1/12. GMP Targeted February.												
NORFOLK COUNTY AGRICULTURAL	550	\$28.6	\$22.3	■	■	Norfolk County Aggi Renovation: Filed-Sub Bids Due 1/18. G.C. Bids due 2/1 NTP Targeted February.												
*SRINGFIELD -FOREST PARK	660	\$43.4	\$34.0	■	■	Springfield Forest Park MS: Filed-Sub Bids Due 1/16. GMP Targeted February.												
*SOMERVILLE	500	\$33.2	\$15.2	■	■	East Somerville Community School Addition/Renovation: Filed-Sub Bids rcv/d6/14. GMP Targeted January.												
DOUGLAS	552	\$50.7	\$38.9	■	■	Douglas IS New Construction: Filed-Sub Bids Due 1/12. G.C. Bids Due 1/20. NTP Targeted February.												
WINCHESTER	420	\$28.7	21.7	■	■	Vinson-Owen ES New Construction: Filed-Sub Bids Due 1/5. G.C. Bids Due 1/26. NTP Targeted February.												
DRACUT	1160	\$60.4	\$47.30	■	■	Dracut Senior HS Addition/Renovation: Filed-Sub Bids Due 2/1. G.C. Bids Due 2/15. NTP Targeted March												
*SOUTHEASTERN REGIONAL RVT	1370	\$34.2	\$26.5	■	■	SRVT Add/Reno: Filed-Sub Bids Due 2/8. GMP Targeted February.												
*NORTON	700	\$34.6	\$27.0	■	■	Norton HS Addition/Renovation: Filed-Sub Bids Due 2/9. GMP Targeted March.												
QUINCY	620	\$50.0	\$32.6	■	■	Central MS New Construction: Filed-Sub Bids Due 2/16. G.C. Bids Due 3/9. NTP Targeted March.												
*ESSEX-NS	1440	\$125.0	\$96.50	■	■	Essex Northshore HS New Construction: Early Site Packages Due 3/29. Filed-Sub Bids Due 4/13/12. GMP Targeted June.												
MARBLEHEAD	425	\$25.9	\$20.2	■	■	Marblehead Glover ES New Construction: Filed-Sub Bids Due 2/29. GMP Targeted March.												
ARLINGTON	380	\$20.7	\$15.7	■	■	Arlington Thompson ES New Construction: Filed-Sub Bids Due 3/21. G.C. Bids Due 4/2. NTP Targeted April.												
*ANDOVER	680	\$44.7	\$34.5	Andover is on HOLD due to litigation arising out of Order of Conditions issued by local Conservation Commission .														
*METHUEN	2075	\$99.1	\$74.9	■	Methuen HS Addition/Renovation: GMP Targeted April													
HINGHAM	1020	\$60.9	\$50.4	■	Hingham MS New Construction: Filed-Sub Bids Due 5/7. G.C Bids Due 5/15. NTP Targeted June													
*DUXBURY	1735	\$128.4	\$99.2	■	Duxbury HS/MS New Construction: Filed-Sub Bids Due 5/18. G.C Bids Due 6/15. NTP Targeted June													
WESTFIELD	600	\$35.9	\$25.2	■	Abner Gibbs ES New Construction: Filed-Sub Bids Due 5/5. G.C Bids Due 6/5. NTP Targeted June													
SOMERSET BERKLEY	1000	\$82.8	\$66.8	■	Somerset-Berkley RHS New Construction: Filed-Sub Bids Due 5/23. G.C Bids Due 6/6. NTP Targeted June													
SAUGUS	725	\$20.3	\$15.7	■	■	Saugus Belmonte MS Repair: Filed-Sub Bids Due 5/23. GMP Targeted June.												
MARSHFIELD	1310	\$103.9	\$80.8	■	Marshfield HS New Construction: Filed-Sub Bids Due 7/23. G.C Bids Due 8/6. NTP Targeted August.													
WESTON	355	\$31.5	\$21.5	Field ES New Construction: Filed-Sub Bids Due 10/24. G.C. Bids Due 10/31. NTP Targeted November										■				
*WILMINGTON	960	\$82.7	\$64.4	Wilmington HS New Construction: Early Sitework, Foundation, & Steel bid packages			■	Wilmington HS New Construction: Filed-Sub Bids Due November. GMP Targeted November.										■
Subtotal	19,757	\$1,256	\$956.1															
GRAND TOTAL	19,757	\$1,256	\$956.1															
Number of Construction-Related Employment Opportunities Created				4,781														

2011 Estimated Bid Dates

Note bid dates are **Estimates ONLY**. Please contact Districts for exact information.

Total Project Budget denotes total District costs and does not denote the basis of the MSBA Total Facilities Grant.

■ - Denotes bid phase in progress or complete

■ - Denotes estimated bid dates

DISTRICT	DESIGN BASIS FOR ENROLLMENT	PROJECT BUDGET <small>Shown in Millions</small>	CONSTRUCTION BUDGET <small>Shown in Millions</small>	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC
*SOUTHBRIDGE	1050	\$76.5	\$60.1	■ Southbridge HS New Construction: Filed-Sub Bids rcv'd 1/7. GMP Issued 2/7.											
*SHREWSBURY	900	\$47.3	\$37.0	■ Sherwood MS New Construction: Filed-Sub Bids rcv'd 2/7. GMP Issued 5/10.											
SO. SHORE RVT	595	\$3.2	\$2.6	■ Regional VTHS Repair: Filed-Sub Bids rcv'd 1/7. G.C. Bids rcv'd 1/18. NTP issued 5/9.											
CARLISLE	700	\$20.0	\$15.6	■ Carlisle ES Addition/Renovation: Filed-Sub Bids rcv'd 1/26. G.C. Bids rcv'd 2/4. NTP Issued 2/9.											
MARSHFIELD	485	\$2.4	\$2.0	■ Marshfield Edward Winslow ES Repair: Filed-Sub Bids rcv'd 1/14. G.C. Bids rcv'd 1/21. NTP Issued 2/12.											
*UXBRIDGE	600	\$43.0	\$34.4	■ Uxbridge HS New Construction: Early Site & Steel Package rcv'd 1/13. Filed-Sub Bids rcv'd 3/17. GMP Issued 3/31.											
*BURLINGTON	880	\$32.9	\$24.7	■ Marshall Simonds MS Addition/Renovation: Filed-Sub Bids rcv'd 3/22. GMP Issued 4/12.											
BERLIN / BOYLSTON	560	\$44.0	\$34.2	■ Tahanto MS/HS New Construction: Filed-Sub Bids rcv'd 4/7. G.C. Bids rcv'd 4/20. NTP issued 5/10.											
EASTHAMPTON	510	\$43.7	\$33.5	■ Easthampton HS New Construction: Filed-Sub Bids rcv'd 4/20. G.C. Bids rcv'd 5/6. NTP issued 5/16.											
*LONGMEADOW	1000	\$78.5	\$63.8	■ Longmeadow HS New Construction: Filed-Sub Bids rcv'd 4/28. GMP issued 5/12.											
SUTTON	840	\$59.9	\$46.4	■ Sutton MS New Construction: Filed-Sub Bids rcv'd 5/4. G.C. Bids rcv'd 5/18. NTP issued 5/26.											
*LEOMINSTER	1805	\$45.9	\$32.7	■ Leominster HS Addition/Renovation: Filed-Sub Bids rcv'd 6/2. GMP issued 6/23.											
*ADAMS/CHESHIRE	805	\$40.6	\$30.0	■ Hposac Valley MHS Addition/Renovation: Filed-Sub Bids rcv'd 10/14. GMP issued 11/17.											
MAYNARD	410	\$45.8	\$35.6	■ Maynard HS New Construction: Filed-Sub Bids rcv'd 7/13. G.C. Bids rcv'd 7/27. NTP issued 8/18.											
HUDSON	715	\$44.1	\$34.8	■ JFK MS New Construction: Filed-Sub Bids rcv'd 8/29. G.C. Bids rcv'd 9/14. NTP issued 9/28.											
*MEDWAY	853	\$22.1	\$18.2	■ Medway MS Repair: Early Demo & Abatement, Steel & Concrete Packages rcv'd 9/13. Filed-Sub Bids rcv'd 9/29. GMP issued 12/15.											
EAST BRIDGEWATER	950	\$77.1	\$60.3	■ East Bridgewater Junior/Senior HS New Construction: Filed-Sub Bids rcv'd 7/19. G.C. Bids rcv'd 8/4. NTP issued 8/10.											
BROOKLINE	560	\$8.8	\$7.0	■ Brookline Heath ES Addition/Renovation: Filed-Sub Bids rcv'd 8/29. G.C. Bids rcv'd 9/13. NTP issued 9/29.											
WEST SPRINGFIELD	1270	\$107.6	\$73.3	■ West Springfield HS New Construction: Filed-Sub Bids rcv'd 10/27. G.C. Bids Due 11/10 NTP issued 11/22.											
FALL RIVER	625	\$53.2	\$42.4	■ Fall River Morton MS New Construction: Filed-Sub Bids rcv'd 10/6. G.C. Bids rcv'd 10/31. NTP issued 11/30.											
Subtotal	16,113	\$896.6	\$688.6												
GRAND TOTAL	16,113	\$896.6	\$688.6												
Number of Construction-Related Employment				3,443											

**Projects in Construction
MSBA Grant Basis and Maximum Grant Amount**

New Program and Wait List Program Totals			\$1,835,200,914	41,387		8,011,175	*Italicized amounts are estimates. Amounts based on bid results have yet to be determined.										\$1,263,506,542
Grade	Contractor	Total Construction Cost	Projected Enroll	PFA or Bid Data	Proposed Square Footage	Construction Cost per Square Foot	Building Cost	Building Cost per Square Foot	Project Type	Construction Start	Estimated Substantial Completion Date	Reporting Variance from Schedule	Physical Progress (%)	Change Orders (%)	Construction Status	Approximate Maximum Grant Amount *	
Capital Pipeline Projects in Construction																	
New Program Totals			\$1,700,016,210	38,787		7,456,605	\$226		\$168							\$1,114,721,824	
Berlin-Boylston Tahanto Reg MS/HS	6-12	CTA	\$32,162,000	560	Bid	126,100	\$255	25,381,909	\$201	Design/Bid/Build	10-May-11	1-Nov-12		42%	0.24%	Most of the building is enclosed and weather tight for inside winter work. Enclosing the balance of the building is in process. Primary electrical feeds to new school are complete and propane tanks have been installed. Installation of HVAC, water piping, and rough electrical installations in MS wing are in process. CMU masonry installation is proceeding in the MS wing, HS wing, and building parts A & D. Binder has been installed around the building perimeter.	\$20,792,722
Beverly Beverly HS	9-12	CTA	\$67,563,917	1,200	PFA	247,275	\$273	\$51,251,689	\$207	Design/Bid/Build	6-Jan-09	18-Nov-10		99%	1.20%	The main building was completed in November 2010. Phase 2, Existing Building Demolition, is now complete. Portions of the baseball field and irrigation system need to be completed in the Spring of 2012.	\$46,826,551
Billerica Parker ES	K-5	CTA	\$22,842,500	500	Bid	89,093	\$256	\$17,913,441	\$201	Design/Bid/Build	15-Sep-10	10-May-12		61%	0.00%	Phase I, building envelope is complete. Phase II, demolition, is scheduled to be complete on November 26, 2012.	\$15,851,020
Brookline Heath ES	K-8	Nauset	\$6,159,185	560	Bid	66,544	\$93	\$4,807,436	\$72	Design/Bid/Build	29-Sep-11	15-Aug-12		6%	0.00%	Work is progressing on the new addition. Foundations have been installed. Backfilling and compacting is ongoing.	\$3,173,407
Brookline Runkle ES	PK-8	G&R Construction	\$20,715,300	560	Bid	104,400	\$198	\$17,668,440	\$169	Design/Bid/Build	10-Nov-10	15-Aug-12	30-60 Days	45%	4.00%	Addition- Structural steel detailing continues as well as exterior masonry, interior metal studs, drywall and MEP rough-ins. Existing building- MEP rough-ins, metal stud and drywall installations continue.	\$11,135,430
Carlisle Carlisle K-8	K-8	H.V. Collins Co. Inc	\$15,277,344	700	Bid	140,312	\$109	\$11,342,751	\$81	Design/Bid/Build	9-Feb-11	20-Apr-12	14 Days	45%	1.50%	Building is tight for the winter months. Interior finishes are underway in the new addition working towards an April completion.	\$6,620,942
Danvers Danvers HS	9-12	Bacon Construction	\$53,514,527	1,000	Bid	246,251	\$217	\$42,760,342	\$174	Design/Bid/Build	Oct-10	1-Jul-13		48%	0.51%	Work is progressing through Phase I / IA areas with rough-in construction activity nearing completion in the academic wing and science wing. Finishes have commenced in the field house and locker room area.	\$41,910,938
Easthampton Easthampton HS	9-12	Fontaine Brothers	\$30,904,000	510	Bid	110,400	\$280	\$26,159,589	\$237	Design/Bid/Build	16-May-11	25-Oct-13		15%	0.76%	Foundation walls and interior foundation piers in the west wing of the building are complete. Installation of storm drainage, gas utility piping, and all underslab piping and raceways continue. Starting installation of structural steel and pouring of the east and center wing slabs.	\$24,104,384
East Bridgewater E. Bridgewater Jr/Sr HS	7-12	Fontaine Brothers	\$65,409,000	950	Bid	213,544	\$306	\$48,829,117	\$229	Design/Bid/Build	10-Aug-11	24-Jun-13	7 Days	4%	0.00%	Site work is underway. Preloading soil has begun. Project is about 1 week behind due to weather and ground water issues. Foundations have started and steel is scheduled to arrive in February.	\$43,317,092
Fall River Morton MS	6-8	TBD	\$42,458,029	625	PFA	130,600	\$325	\$28,366,149	\$217	Design/Bid/Build	4-Nov-11	30-May-13		3%	0.00%	GC has mobilized and has started securing the site. The demolition work was procured by the City and has been completed.	\$40,555,087
Foxborough Foxborough HS	9-12	CTA	\$11,632,000	885	Bid	218,500	\$53	\$9,274,000	\$42	Design/Bid/Build	25-Jan-10	31-Oct-11		98%	6.96%	Completion of punchlist items estimated for early January. Remaining work being completed on 2nd shift.	\$7,226,509
Hampden-Wilbraham Minnechaug HS	9-12	Fontaine Brothers	\$48,597,500	1,225	Bid	231,467	\$210	\$37,499,962	\$162	Design/Bid/Build	22-Jul-10	28-Jun-12		58%	1.40%	Walls are closed up in academic wings. Primer and paint is underway. Ceilings and above ceiling work also underway. Working on closing up the exterior walls in the gym. Portions of site work have been completed in preparation for the winter.	\$34,863,838
Hanover Hanover HS	9-12	Callahan	\$38,652,255	800	Bid	157,000	\$246	\$28,060,313	\$179	Design/Bid/Build	28-Sep-09	1-Jun-11		98%	4.30%	Working on punchlist of the new building. Minor sitework to be completed in the Spring of 2012.	\$22,263,877
Hudson John F Kennedy MS	5-7	Agostini/Bacon	\$35,102,573	715	PFA	119,685	\$293	\$28,373,294	\$237	DBB	28-Sep-11	11-Sep-11		5%	0.00%	GC has mobilized on site. Early site package has been completed.	\$24,067,405
Maynard Maynard HS	8-12	CTA	\$36,650,000	410	Bid	121,544	\$302	\$30,630,013	\$252	Design/Bid/Build	18-Aug-11	6-Dec-13		8%	0.00%	Rock crushing completed from the blasting activities. Foundation and footings of Area D were completed. Foundations and footings in Area C are underway. Footing preparation work has commenced in A and B sections. Site drainage work is underway.	\$23,854,703
Marshfield Governor Winslow ES	K-5	Enterprise Equipment Co.	\$1,606,479	494	Bid	65,790	\$24	\$1,408,279	\$21	Design/Bid/Build	Apr-11	31-Oct-11		95%	1.00%	Construction on both the windows and HVAC is complete. Windows failed Commissioning test (District, Designer, Cx Agent and OPM working on solution). MSBA is waiting for a plan of action from team. Commissioning on HVAC is complete and training on system is ongoing.	\$991,294
Middleton Howe-Manning ES	4-6	CTA	\$18,280,592	553	Bid	83,934	\$218	\$14,600,262	\$174	Design/Bid/Build	06-Apr-10	30-Jul-11		100%	4.59%	New building occupied September 7, 2011. Completing punchlist work and technology installation. Completing site work for playground.	\$12,311,976
Nashoba Pompositicut ES	K-5	P.J. Stella Construction	\$23,640,900	600	Bid	98,030	\$241	\$18,906,998	\$193	Design/Bid/Build	15-Jun-10	12-Jun-12	30 Days	70%	1.20%	Phase I work nearing completion. Students and staff are expected to move into the new Phase I addition on January 17, 2012 then the GC will commence work on the Phase II existing school.	\$15,239,622
Natick Natick HS	9-12	Brait Builders Corp.	\$62,141,700	1,300	Bid	254,225	\$244	\$53,213,182	\$209	Design/Bid/Build	13-Sep-10	15-Jun-13		53%	2.50%	Finishes are underway in several areas. Site work is suspending for the winter.	\$38,209,033
Norfolk Freeman-Centennial ES	3-6	Fontaine Brothers	\$25,354,966	610	Bid	96,410	\$263	\$20,023,001	\$208	Design/Bid/Build	9-Nov-10	18-Jun-12		50%	0.60%	Veneer cladding of exterior facade is complete. Roofing and flashing complete. All doors are installed. Sprinkler piping is on-going. Windows are starting to be delivered and installation has begun. First floor framing is complete. Second floor framing is on-going. RTU's are being set and MEP's are ongoing. Elevator equipment is installed.	\$15,861,760
Norwood Norwood HS	9-12	Agostini	\$54,377,098	1,100	Bid	227,374	\$239	\$42,573,646	\$187	Design/Bid/Build	19-May-09	13-May-11		99%	1.20%	Minor sitework to be completed in the Spring of 2012.	\$38,154,487
Plymouth Plymouth HS	9-12	J&J Contractors	\$64,887,000	1,350	Bid	267,357	\$243	\$51,579,703	\$193	Design/Bid/Build	3-May-10	15-May-12	14 Days	70%	4.70%	Finishes are underway on all floors. Site work has come to a stop until Spring. MEP's are installing finishes throughout the classroom wings. The kitchen, auditorium and gym are trailing behind.	\$41,810,972
Sturbridge Burgess ES	K-6	Fontaine Brothers	\$22,931,000	860	Bid	131,630	\$174	\$18,391	\$0	Design/Bid/Build	10-Aug-10	1-Oct-12		81%	1.65%	New addition is complete and in service. Renovation of the attached existing building is progressing and is scheduled to be complete in February 2012. Final demolition work and ball fields will then be constructed during summer months. Early completion is scheduled for November 2012.	\$16,808,626
Sutton MS/HS	6-12	TLT Construction Corp.	\$42,123,807	840	Bid	171,401	\$246	\$32,998,403	\$193	Design/Bid/Build	1-Jul-11	1-Jul-14	42 Days	16%	0.00%	Demolition of the old middle school has been completed. The installation of footings and foundation walls for the new building are underway. Construction of the new well house structure is ongoing. Site work and utility work are ongoing.	\$29,843,511
Tewksbury Tewksbury HS	9-12	CTA/Methuen Construction Co.	\$51,600,000	1,100	Bid	218,781	\$236	\$40,159,651	\$184	Design/Bid/Build	15-Oct-10	3-Aug-12	28 Days	46%	2.10%	Drywall and ceilings are well underway. Finishes have begun on some floors. Certain portions of site work have been completed in preparation for the winter.	\$36,622,570
West Springfield West Springfield HS	9-12	Fontaine Brothers	\$73,295,000	1,270	PFA	257,525	\$285	\$52,306,700	\$203	DBB	22-Nov-11	20-Jun-13		0%	0.00%	GC has mobilized and has started securing the site.	
Adams-Cheshire Hoosac Valley MSHS	6-12	Gilbane	\$32,439,293	805	PFA	173,999	\$186	24,009,952	\$138	CM-R	17-May-11	31-Jul-12		41%	0.00%	Additions- Steel detailing and spray insulation continues. Existing building- Below slab piping, seismic bracing and CMU installations continue as well as drywall installation and taping. Cafeteria windows have been replaced. RTU's are in place on roof but not connected. Reinforcing steel has commenced in pool area.	\$28,243,131
Burlington Marshall Simonds MS	6-8	CTA	\$24,612,440	880	Bid	151,000	\$163	\$18,988,987	\$126	CM-R	15-Apr-11	17-May-13		31%	0.22%	Ongoing construction of the addition includes extensive MEP rough-ins, exterior envelope construction (masonry veneer and windows), interior partition walls and soffit framing. Kitchen renovation work is ongoing. Renovations of the occupied school include completion of demolition and interior framing and drywall in the Phase 15 renovation area.	\$16,933,103
Dedham Avery ES	K-5	Consigli	\$18,174,209	310	Bid	62,723	\$290	\$13,528,098	\$216	CM-R	15-Oct-10	1-Jan-12		80%	4.16%	Interior finishes, exterior site work, roofing and MEP system installations continue. Commissioning and start up of mechanical systems, plumbing, and electrical systems has begun.	\$11,086,460
Grafton Memorial Sr HS	9-12	Dimeo	\$54,030,917	900	Bid	186,351	\$290	\$42,033,245	\$226	CM-R	18-Aug-10	17-Jul-12		41%	0.00%	Building veneer complete. Intumescent spray fireproofing complete. Windows are being delivered and installation is ongoing. Interior framing is complete throughout most of the building and drywall installation is going. MEP's are on-going and commissioning is set to begin.	\$36,108,679
Leominster Leominster SHS	9-12	S.O.M.	\$32,709,051	1,825	Bid	295,859	\$111	\$22,855,000	\$77	CM-R	1-Jul-11	30-Aug-13		20%	0.00%	The fire separation wall, exterior wall sheathing, roofing, and interior partitions have been completed at the new science addition. Installation of ductwork and waste piping is underway. MEP trades continue rough-in work in the B/D wings.	\$31,038,794
Longmeadow Longmeadow HS	9-12	Gilbane	\$62,898,149	1,000	Bid	184,365	\$341	\$38,733,395	\$210	CM-R	Nov-10	23-Feb-13		22%	0.63%	Steel erection and all detailing work have been completed. Installation of exterior wall framing and sheathing has been completed for Area C from L line to the west. The layout of interior partition walls continues on the first and second floors of Area C.	\$34,004,658
Medway MS	5-8	Consigli	\$17,876,231	800	Bid	223,780	\$80	\$13,162,034	\$59	CM-R	Oct-11	7-Mar-13		0%	0.00%	Construction began in November which included abatement, selective demo and misc. sitework.	\$10,582,018
Methuen Methuen HS	9-12	Dimeo	\$74,917,204	2,075	PFA	368,017	\$204	\$63,689,716	\$173	CM-R	21-Jul-11	Feb-14		5%	0.00%	Enabling package complete. The District has elected to terminate its contract with Dimeo on the basis of inability to negotiate a GMP. Dimeo has demobilized from the site. The District is currently in the process of procuring a contract with another CM-R.	\$64,734,701
Needham Newman ES	K-5	Consigli	\$19,064,745	680	Bid	119,264	\$160	\$12,806,351	\$107	CM-R	16-Jun-10	27-Aug-12		35%	2.30%	Phase 3, MEP rough-in's, is underway. Closing up walls and ceilings are projected for February 2012.	\$8,598,929
Rochester Memorial ES	K-6	Gilbane	\$20,564,981	635	PFA	107,183	\$192	\$14,165,117	\$132	CM-R	19-Apr-10	1-Sep-11		99%	4.56%	Project received full Occupancy Certificate on September 6, 2011.	\$14,438,137

**Projects in Construction
MSBA Grant Basis and Maximum Grant Amount**

	Grade	Contractor	Total Construction Cost	Projected Enroll	PFA or Bid Data	Proposed Square Footage	Construction Cost per Square Foot	Building Cost	Building Cost per Square Foot	Project Type	Construction Start	Estimated Substantial Completion Date	Reporting Variance from Schedule	Physical Progress (%)	Change Orders (%)	Construction Status	Approximate Maximum Grant Amount *
Rockland John Rogers MS/ HS	5-12	Agostini	\$66,362,037	1,525	Bid	268,106	\$248	\$47,721,785	\$178	CM-R	15-Jan-10	3-Aug-12		49%	0.00%	Continued masonry work in the auditorium. Framing in area D&G classrooms of the high school is ongoing. MEP in the HS is 50% complete. All RTU's have been placed on the HS roof. Binder has been placed around the south and west sides of the HS and granite curb has been set. MS roof is complete. All RTU's have been placed. Interior framing has begun in the MS. Interior CMU walls are complete. Rough MEP in areas A&B of the MS is 75% complete. Stair 1, metal stairway, has begun. Window installation on east elevation of MS is complete and has begun on the west elevation.	\$52,740,564
Sharon Sharon MS	6-8	Consigli	\$34,676,018	845	Bid	171,806	\$202	\$24,732,123	\$144	CM-R	1-Apr-10	23-Jan-12		88%	1.80%	Renovations continue in the final phase of interior work which is scheduled for turnover at the end of January 2012. The gym has been turned over for District use. Bleacher and equipment installations continue during off school hours.	\$22,670,388
Shrewsbury Sherwood MS	5-6	Gilbane	\$33,986,286	900	Bid	129,939	\$262	\$23,100,633	\$178	CM-R	7-Mar-11	1-Sep-13		39%	0.23%	Building is 65% enclosed and has temporary heat in place. Balance of enclosure is progressing. MEP rough-in work is progressing on schedule. Installation of drywall in classrooms has started.	\$23,912,246
Southbridge Southbridge MS/HS	6-12	Consigli	\$57,397,363	1,050	Bid	199,740	\$287	\$41,487,200	\$208	CM-R	30-Nov-10	1-Jun-12		46%	0.14%	Interior CMU and glazed block installations continue in the D wing. Exterior metal stud framing is complete. Classroom window installations are 95% complete. Interior rough-in water, waste & vent, and gas piping is ongoing throughout the building.	\$52,019,398
Uxbridge High School	9-12	Shawmut Design	\$35,293,766	600	Bid	123,000	\$287	\$27,145,604	\$221	CM-R	28-Feb-11	20-Jun-12		45%	0.10%	Certain portions of site work have been completed in preparation for the winter. MEP's well underway. CMU is ongoing in the interior of the building. Remaining windows to be installed in January 2012.	\$21,973,620
Wayland Wayland HS	9-12	Shawmut Design	\$54,230,819	900	Bid	171,000	\$317	\$37,343,299	\$218	CM-R	28-Jun-10	1-Dec-11		85%	1.47%	New buildings occupied January 3, 2012. Selective demolition of existing buildings is in process. Abatement to commence shortly.	\$24,051,231
Wellesley Wellesley HS	9-12	Turner	\$82,942,222	1,500	Bid	280,000	\$296	\$55,814,300	\$199	CM-R	24-Aug-09	5-Feb-12		81%	1.57%	Finishes are advancing throughout the building. Final trim and finish details are ongoing. MEP coordination and training is underway. The photovoltaic system installation is complete. The construction is on schedule to the revised project schedule for an early occupancy of the new building in February 2012. A temporary occupancy permit was issued in late December.	\$40,117,222
Wait List Projects in Construction																	
Wait List Program Totals			\$135,184,704	2,600		554,570											\$148,784,718
Springfield Putnam Voc Tech HS	9-12	Consigli	\$86,039,066	1,400	Bid	315,000	\$273	\$62,949,742	\$200	CM-R	18-May-10	01-Jun-12		75%	0%	Exterior- Small amount of work remaining on curtain walls and doors. All windows installed. Interior- Finishes are ongoing throughout. Terrazo flooring being installed in cafeteria and Putnam Hall. Gym is nearly complete except flooring and bleachers. FF&E scheduled to be delivered starting March 5, 2012. Permanent Certificate of Occupancy scheduled for June 1, 2012.	\$102,872,837
Worcester North HS	9-12	Gilbane	\$49,145,638	1,200	PFA	239,570	\$205	\$40,860,983	\$171	CM-R	24-Sep-08	Jun-11		90%	3%	Phase 3 of the project which includes abatement & demo of the existing school is underway.	\$45,911,881

District-MSBA	Project Name	Due Date	2011												2012				
			J	F	M	A	M	J	Jul	A	S	O	N	D	J	F	M	A	M
Window Projects																			
Wilmington	Shawsheen Elementary School	21-Jan-11 A	◆																
Attleboro	Attleboro High School	23-Feb-11 A		◆															
Arlington	Arlington Norcross Stratton	1-Mar-11 A		◆															
Braintree	Archie T Morrison Elementary	10-Mar-11 A		◆															
Braintree	East Middle School	10-Mar-11 A		◆															
Braintree	Highlands Elementary School	10-Mar-11 A		◆															
Braintree	Hollis Elementary School	10-Mar-11 A		◆															
Springfield PS	Frank H Freedman ES	13-Apr-11 A			◆														
Springfield PS	Warner ES	13-Apr-11 A			◆														
Springfield PS	Washington ES	13-Apr-11 A			◆														
Springfield PS	White Street ES	13-Apr-11 A			◆														
Sudbury	Peter Noyes	14-Apr-11 A			◆														
Fairhaven	Hastings Middle	21-Apr-11 A			◆														
Dudley Charlton Reg	Shepherd Hill Reg High	28-Apr-11 A			◆														
Chelmsford	Chelmsford High	29-Apr-11 A			◆														
Framingham	Mary E Stapleton Elem	4-May-11 A			◆														
Tantasqua	Brookfield Elementary	18-May-11 A			◆														
Barnstable	West Barnstable Elem	20-May-11 A			◆														
Fitchburg	Reingold Elementary (Phase 2)	28-May-11 A			◆														
Fitchburg	South Street Elementary (Phase 2)	28-May-11 A			◆														
Fitchburg	Memorial Intermediate (Phase 2)	28-May-11 A			◆														
Reading	Birch Meadow	1-Jun-11 A			◆														
Dennis Yarmouth	Ezra H Baker Elementary School	3-Jun-11 A			◆														
Leverett	Leverett Elementary	7-Jun-11 A			◆														
Abington	Woodsdale Elementary School	8-Jun-11 A			◆														
Pentucket	Dr Frederick Sweetsir	13-Jun-11 A			◆														
Pentucket	Dr John C Page School	13-Jun-11 A			◆														
Pentucket	Elmer S Bagnall	13-Jun-11 A			◆														
BillERICA	BillERICA Memorial High School	14-Jun-11 A			◆														
Rockland	R Stewart Esten ES	20-Jun-11 A			◆														
Amherst-Pelham	Amherst Regional MS	14-Jul-11 A			◆														
North Attleboro	Falls	27-Jul-11 A			◆														
Brockton	Brockton High	29-Jul-11 A			◆														
Brockton	Downey	29-Jul-11 A			◆														
North Brookfield	North Brookfield Elem	1-Aug-11 A			◆														
Upper Capecod VT	Upper Cape Cod Voc Tech	5-Aug-11 A			◆														
North Middlesex	Ashby Elementary	25-Aug-11 A			◆														
Wachusett	Naquag Elementary	6-Oct-11 A											◆						
Wachusett	Paxton Center	6-Oct-11 A											◆						
Wachusett	Thomas Prince	26-Oct-11 A											◆						
Pioneer Valley	Northfield ES	1-Nov-11 A											◆						
West Boylston	Major Edwards ES	2-Nov-11 A											◆						
West Boylston	West Boylston Jr-Sr HS	2-Nov-11 A											◆						
Marlborough	Francis J Kane	14-Nov-11 A											◆						
Marlborough	Marlborough High	14-Nov-11 A											◆						
Middleborough	Mary K Goode ES	8-Dec-11												◆					
Springfield PS	John J Duggan MS	10-Dec-11												◆					
Shrewsbury	Spring Street School	15-Dec-11												◆					
Mohawk Trail	Colrain Central	2-Jan-12													◆				
Mohawk Trail	Mohawk Trail Reg High	2-Jan-12													◆				
Sandwich	Forestdale	15-Jan-12													◆				
North Andover	Atkinson School	15-Jan-12													◆				

District-MSBA	Project Name	Due Date	2011												2012					
			J	F	M	A	M	J	Jul	A	S	O	N	D	J	F	M	A	M	
Sandwich	Oak Ridge K-8	15-Jan-12															◆	15-Jan-12		
Westfield	Westfield Voc Tech HS	20-Jan-12																◆	20-Jan-12	
Brookfield	Brookfield Elementary	30-Jan-12																◆	30-Jan-12	
Central Berkshire	Kittredge	30-Jan-12																◆	30-Jan-12	
Greenfield	Four Corners	30-Jan-12																◆	30-Jan-12	
Haverhill	Caleb Dustin Hunking	30-Jan-12																◆	30-Jan-12	
Haverhill	Consentino	30-Jan-12																◆	30-Jan-12	
Haverhill	John G Whittier	30-Jan-12																◆	30-Jan-12	
Mendon Upton	Miscoe Hill School	30-Jan-12																◆	30-Jan-12	
Nauset	Nauset Regional High	30-Jan-12																◆	30-Jan-12	
Peabody	John E Burke School	30-Jan-12																◆	30-Jan-12	
Westport	Westport Middle	30-Jan-12																◆	30-Jan-12	
Lowell	Moody ES	30-Jan-12																◆	30-Jan-12	
Lowell	Peter W Reilly School	30-Jan-12																◆	30-Jan-12	
Lowell	Washington School	30-Jan-12																◆	30-Jan-12	
Agawam	Agawam Junior High	1-Feb-12																◆	1-Feb-12	
Salem	Collins MS	15-Feb-12																◆	15-Feb-12	
Salem	Saltonstall Elementary School	15-Feb-12																◆	15-Feb-12	

District-MSBA	Project Name	Due Date	2011												2012				
			J	F	M	A	M	J	Jul	A	S	O	N	D	J	F	M	A	M
Boiler Projects																			
Fitchburg	Reingold Elementary School (Pha...	26-Jan-11 A	◆																
Fitchburg	Memorial Middle School (Phase 1)	26-Jan-11 A	◆																
Tri County Regional	Tri County Regional Voc Tech	24-Feb-11 A	◆																
Arlington	Arlington Norcross Stratton	1-Mar-11 A	◆																
Scituate PS	Wampatuck ES	3-Mar-11 A	◆																
Sudbury	Peter Noyes	14-Apr-11 A				◆													
Fitchburg	Fitchburg High (Phase 2)	17-May-11 A						◆											
Leicester	Leicester Memorial Elem	18-May-11 A						◆											
Newton	Williams	20-May-11 A						◆											
Bellingham	Bellingham Memorial Middle	3-Jun-11 A						◆											
Boston	Clarence R Edwards Middle	11-Jun-11 A						◆											
Pentucket	Dr Frederick Sweetsir	13-Jun-11 A						◆											
Pentucket	Dr John C Page School	13-Jun-11 A						◆											
Pentucket	Elmer S Bagnall	13-Jun-11 A						◆											
Weston	Weston High	17-Jun-11 A						◆											
Boston	Thomas A Edison Jr High	24-Jun-11 A						◆											
New Salem Wendell	Swift River	7-Jul-11 A						◆											
Narrangsett	Phillipston Memorial	13-Jul-11 A						◆											
Northborough	Robert E. Melican Middle School	25-Jul-11 A						◆											
Brockton	East Junior High	29-Jul-11 A						◆											
Brockton	North Junior High	29-Jul-11 A						◆											
Peabody	John E Burke School	2-Aug-11 A						◆											
Lowell	Washington School	1-Oct-11 A										◆							
Wachusett	Naquag Elementary	6-Oct-11 A										◆							
Wachusett	Thomas Prince	26-Oct-11 A										◆							
Marlborough	Marlborough High	6-Nov-11 A										◆							
Pioneer Valley	Pioneer Valley Regional School	22-Nov-11 A										◆							
Salem	Collins MS	15-Dec-11											◆						
Salem	Saltonstall Elementary School	15-Dec-11											◆						
Westfield	Highland Elementary School	20-Jan-12																◆	20-Jan-12
Westfield	Paper Mill ES	20-Jan-12																	◆
Westfield	Westfield HS	20-Jan-12																	◆
Westfield	Westfield Voc Tech HS	20-Jan-12																	◆
Westfield	Southampton Road ES	20-Jan-12																	◆
Grafton	South Grafton Elementary	30-Jan-12																	◆
Greenfield	Four Corners	30-Jan-12																	◆
Hancock.	Hancock Elementary	30-Jan-12																	◆
Haverhill	Consentino	30-Jan-12																	◆
Mendon Upton	Miscoe Hill School	30-Jan-12																	◆
Palmer	Palmer High	30-Jan-12																	◆
Palmer	Old Mill Pond	30-Jan-12																	◆
Palmer	Converse Middle	30-Jan-12																	◆

District-MSBA	Project Name	Due Date	2011												2012			
			J	F	M	A	M	J	Jul	A	S	O	N	D	J	F	M	A
Roof Projects																		
Hancock.	Hancock Elementary	15-Feb-11 A		◆														
Attleboro	A Irvin Studley Elementary School	23-Feb-11 A		◆														
Attleboro	Hill Roberts Elementary School	23-Feb-11 A		◆														
Attleboro	Hyman Fine Elementary School	23-Feb-11 A		◆														
Falmouth	East Falmouth Elem	24-Feb-11 A		◆														
Falmouth	North Falmouth Elem	24-Feb-11 A		◆														
Braintree	Braintree High School	10-Mar-11 A			◆													
Quabbin	Quabbin Regional High School	22-Mar-11 A			◆													
Andover	Andover West Middle	28-Mar-11 A			◆													
Sharon	Sharon High School	11-Apr-11 A			◆													
Sudbury	Peter Noyes	14-Apr-11 A			◆													
Melrose	Melrose High	20-Apr-11 A			◆													
Chelmsford	Byam School	28-Apr-11 A			◆													
Needham	Pollard Middle	3-May-11 A			◆													
Winchester	Lynch Elementary	3-May-11 A			◆													
Lexington	Lexington High	4-May-11 A			◆													
Springfield PS	John F Kennedy MS	4-May-11 A			◆													
Springfield PS	Gerena ES	5-May-11 A			◆													
Canton	Canton High	6-May-11 A			◆													
Canton	Rodman Early Childhood Center	6-May-11 A			◆													
Palmer	Palmer High	13-May-11 A			◆													
Tantasqua	Tantasqua Reg Jr High	17-May-11 A			◆													
Palmer	Old Mill Pond	25-May-11 A			◆													
Westfield	Southampton Road ES	26-May-11 A			◆													
Westfield	Highland ES	26-May-11 A			◆													
Fitchburg	Reingold Elementary (Phase 2)	28-May-11 A			◆													
Fitchburg	Memorial Intermediate (Phase 2)	28-May-11 A			◆													
Orange.	Butterfield	31-May-11 A			◆													
Reading	J Warren Killam	1-Jun-11 A			◆													
Gardner	Elm Street School	2-Jun-11 A			◆													
Gardner	Gardner High	2-Jun-11 A			◆													
Gardner	Waterford Primary School	2-Jun-11 A			◆													
Dennis Yarmouth	Ezra H Baker Elementary School	3-Jun-11 A			◆													
Weston	Weston Middle	4-Jun-11 A			◆													
Leverett	Leverett Elementary	7-Jun-11 A			◆													
Narrangsett	Narragansett Middle	8-Jun-11 A			◆													
Springfield PS	Warner ES	9-Jun-11 A			◆													
Pentucket	Dr John C Page School	13-Jun-11 A			◆													
Pentucket	Elmer S Bagnall	13-Jun-11 A			◆													
Pentucket	Helen R Donaghue School	13-Jun-11 A			◆													
Boston	Washington Irving Middle	14-Jun-11 A			◆													
Leicester	Leicester Middle	15-Jun-11 A			◆													
Woburn	John F Kennedy Middle School	15-Jun-11 A			◆													
Plymouth	Plymouth Commun Intermed	16-Jun-11 A			◆													
Avon	Ralph D Butler	22-Jun-11 A			◆													
Woburn	Daniel L Joyce Middle School	22-Jun-11 A			◆													
Boston	Joseph Lee	24-Jun-11 A			◆													
Boston	Thomas A Edison Jr High	24-Jun-11 A			◆													
Weymouth	Abigali Adams Middle School	30-Jun-11 A			◆													
Shrewsbury	Spring Street School	1-Jul-11 A			◆													
Gloucester	Beeman Memorial School	6-Jul-11 A			◆													
Gloucester	East Gloucester Elementary School	6-Jul-11 A			◆													

