


# Project Overview Report

## October 30, 2013

A total of 314 projects that have received invitations from the Board of Directors (“Board”) to collaborate with the MSBA are currently in the MSBA’s Eligibility Period and Capital Pipeline. The following summary chart provides the number of projects in the Eligibility Period and each phase of the Capital Pipeline:

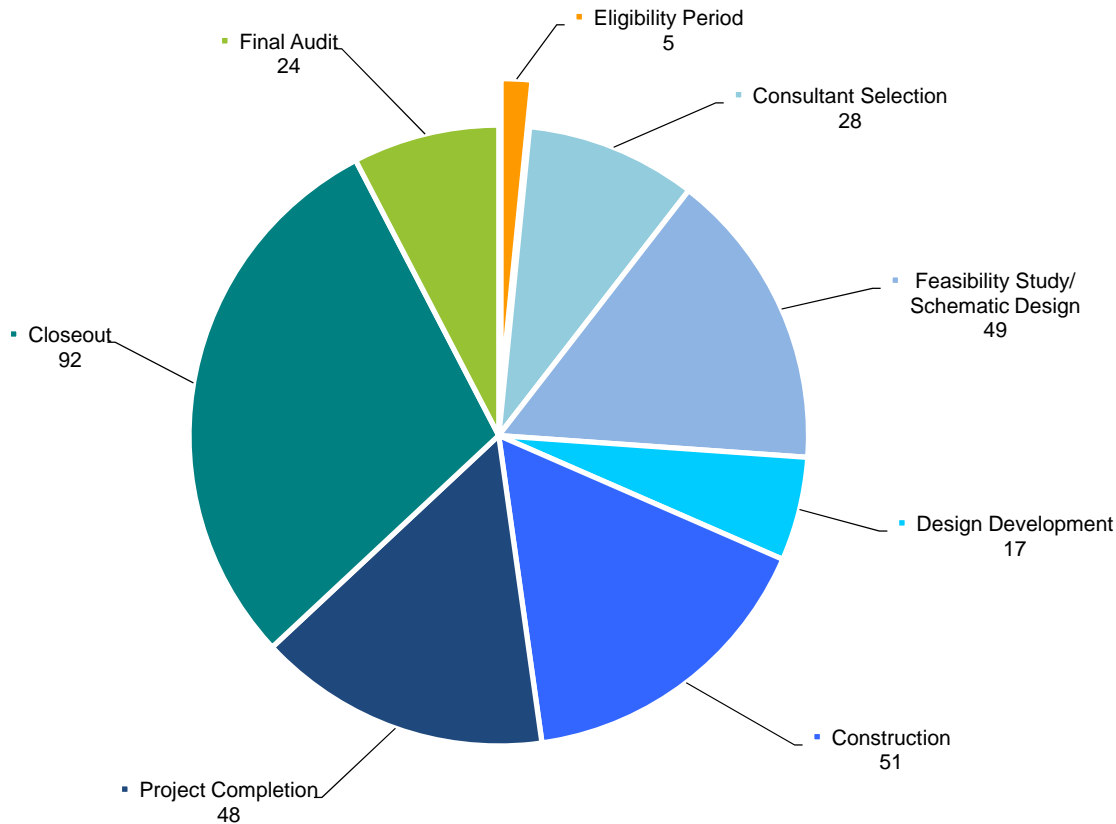

### Statement of Interest (“SOI”) Review Status

The Fiscal Year 2013 Statement of Interest Process opened on January 9, 2013 and closed on April 10, 2013, 117 Districts submitted 201 Statements of Interest.

The Districts have identified the potential scope of the 201 SOIs as follows:

- 37 – New Construction
- 66 – Addition/Renovation
- 98 – Repair

50 of the of the 201 SOIs have been invited into the Accelerated Repair Program at the June, July, and October Board meetings, closing invites into the Accelerated Repair Program for 2013. Core Program SOI review will continue through the fall, with Eligibility Period invites anticipated at the late fall/winter Board meetings.

### **Eligibility Period**

There are five districts in the Eligibility Period. One district is seeking local funding and authorization within the next 90 days, and two of the five districts have already secured funding. The remaining two districts have yet to confirm their date for action.

An agreed-upon enrollment is a key prerequisite for the MSBA to commence a Feasibility Study with a district. To begin the enrollment projection process, a district must file enrollment information utilizing the MSBA's online enrollment projection tool. Since the last report, one district has completed the enrollment process.

Based upon the schedules anticipated by the districts for completion of the Eligibility Period requirements, staff anticipates recommending the five districts in Eligibility Period for an Invitation to Feasibility Study at upcoming Board meetings.

### **Capital Pipeline**

#### **Consultant Selection**

After the district has completed all Eligibility Period requirements and has received a Board Invitation to Feasibility Study, the district procures an Owner's Project Manager ("OPM"). There are two districts in the Capital Pipeline that need to procure an OPM.

After a district has selected and executed a contract with an OPM, it selects a Designer utilizing either a local designer selection process for projects under \$5 million or the MSBA's Designer Selection Panel ("DSP") for projects over \$5 million. There are two districts in the Capital Pipeline that are in the process of procuring a Designer.

#### **Feasibility Study**

Once a district has procured an OPM and Designer and a Feasibility Study Agreement has been executed, the district and its consultants must complete two Feasibility Study submittals, the Preliminary Design Program and the Preferred Schematic Report, prior to Board consideration to proceed into Schematic Design. Based on the most recent data and schedules provided to the MSBA by districts, the MSBA anticipates that seven districts will present their preferred schematic designs to the Board at the upcoming January and March Board meetings.

Prior to consideration by the Board for Project Scope and Budget authorization, a district must submit a schematic design to the MSBA for review. Based on the most recent data and schedules provided to the MSBA by districts, the MSBA anticipates that nine districts will appear before the Board for Project Scope and Budget Agreement authorization at the upcoming January and March Board meetings.

## Commissioning

Since the last report, the MSBA has assigned Commissioning Consultants to an additional two projects presented in the table below. To date, the MSBA has executed 235 Commissioning Consultant contracts, totaling \$18.4 million; 84 contracts have been completed.

District	School	Estimated Const. Cost (million)	Commissioning Consultant	Contract Amount
Newton	A.E. Angier Elementary School	\$27.00	Fitzmeyer & Tocci	\$83,206
Lynn	Thurgood Marshall Middle School	\$65.00	RFS Engineering	\$136,385
<b>Total</b>		<b>\$92.00 million</b>	<b>Total</b>	<b>\$219,591</b>

The table below represents the status of commissioning assignments sorted by the fiscal year in which the commissioning work orders were issued.

Fiscal Year	No. Work Orders Issued	Value of Work Orders Issued	Total Invoiced	Percent Complete
FY10	31	\$4,231,376	\$4,060,239	96%
FY11	95	\$6,328,287	\$4,841,461	77%
FY12	52	\$4,459,061	\$2,237,891	50%
FY13	55	\$3,386,847	\$806,482	24%
FY14	2	\$219,591	\$0.00	0%

## Design Development

Once a district has secured local funding and has entered into a Project Funding Agreement with the MSBA, it enters the Design Development phase. Currently, there are 17 projects in the Design Development phase with a total estimated construction cost of \$420.16 million: seven Accelerated Repair projects and 10 Core Program projects. The 10 Core Program projects in Design Development have a total estimated construction cost of \$408.9 million:

### Elementary School Districts

Newton  
South Hadley  
Revere

### Middle School Districts

Auburn  
Chicopee  
Lynn  
North Adams  
Peabody  
Wachusett Regional

### High School Districts

Greater Lowell Regional Voc/Tech

## Construction

When a district issues a Notice to Proceed, the project is advanced to the Construction phase. Currently, there are 51 projects in the Construction phase with a total estimated construction cost of \$1.918 billion: one Green Repair project, eight Accelerated Repair projects, two Science Lab Initiative projects, and 40 Core Program projects. The 40 Core Program projects have a total estimated construction cost of \$1.851 billion and are listed below. This does not include the 48 projects that have reached substantial completion and are currently in the Project Completion phase.

### Elementary School Districts

Andover  
Georgetown  
Lexington  
Marblehead  
Newburyport (Bresnahan)  
Springfield (Brookings)  
Springfield (Dryden)  
Webster  
Westfield  
Weston  
Williamsburg

### Middle and Middle/High School Districts

Douglas  
Greenfield  
Hingham  
Newburyport (Nock)  
Oxford  
Stoneham  
Sutton  
Wakefield

### High School Districts

**Addition/Renovation**  
Assabet Valley Regional Technical  
Ayer Shirley Regional  
Danvers  
Dracut  
Greater New Bedford Voc/Tech  
Methuen  
Norfolk County Agricultural  
North Reading  
Norton  
Southern Worcester Regional Voc/Tech  
Southwick-Tolland-Granville Regional

**New**  
Concord-Carlisle Regional  
Essex/North Shore Regional Voc/Tech  
West Bridgewater  
Wilmington

**Model**  
Duxbury  
Franklin  
Marshfield  
Monomoy Regional  
Somerset-Berkley Regional  
West Springfield

## Summary of Bid Data

- These numbers are based on preliminary information received from the District and are subject to further review and calculation.
- The 2013 numbers include Core Program and Science Lab Initiative projects, not Accelerated Repair projects.
- Anticipated remaining bids in 2013 are Springfield (Brookings ES), Southern Worcester County Voc/Tech (Bay Path Regional), and Ayer Shirley Regional.

Year	Number of Projects	Design Basis for Enrollment	Project Budget	Construction Budget
2013	31	24,093	\$1.21 B	\$972.0 M
2014	8	6,810	\$397.0 M	\$315.1 M
<b>Grand Total</b>	39	30,903	\$1.607 B	\$1.29 B

## Core Program – Construction Estimate vs. 2013 Bid Amount

- 11 bids received and 9 GMPs executed in 2013.
- Of the 20 projects, 13 bids came in within the estimated budget.
- No new bids since the October Board Meeting.

District	School	Scope	Project Type	Bid Date	Construction Estimate **	Bid Amount **	Variance from Construction Estimate	Reimbursement Rate	Potential Grant Variance *
				Total	\$791,132,655	\$781,571,103	\$9,561,552	-	\$23,250,545
Lexington	Estabrook ES	New	CMR	Jan-13	\$31,145,045	\$32,792,348	-\$1,647,303	37.27%	\$0
Monomoy RSD	Monomoy Regional HS	New	DBB	Feb-13	\$52,962,105	\$47,490,700	\$5,471,405	51.53%	\$2,819,415
Newburyport	Bresnahan ES	New	DBB	Feb-13	\$31,117,441	\$27,405,000	\$3,712,441	52.78%	\$1,959,426
Williamsburg	Anne T. Dunphy IS	Add/Reno	DBB	Mar-13	\$9,553,527	\$8,990,457	\$563,070	61.86%	\$348,315
Assabet Valley RVTSD	Assabet Valley RVTHS	Repair/Reno	DBB	Mar-13	\$50,755,300	\$45,215,000	\$5,540,300	53.48%	\$2,962,952
Stoneham	Stoneham MS	Add/Reno	CMR	Mar-13	\$32,028,239	\$33,086,864	-\$1,058,625	57.50%	\$0
Old Colony RSD	Old Colony RVTHS	Roof/SLI	DBB	Apr-13	\$2,179,947	\$2,037,200	\$142,747	54.16%	\$77,312
Newburyport	Nock MS	Add/Reno	CMR	Apr-13	\$21,831,202	\$20,877,414	\$953,788	53.78%	\$512,947
***Southwick-Tolland-Granville RSD	Powder Mill ES / Woodland ES	Repair	DBB	May-13	\$22,075,590	\$20,297,491	\$1,778,099	55.63%	\$989,156
Wilmington	Wilmington HS	New	CMR	Jun-13	\$64,408,261	\$65,690,437	-\$1,282,176	55.19%	\$0
North Reading	North Reading HS	Add/Reno	CMR	Jun-13	\$86,315,287	\$101,328,353	-\$15,013,066	51.49%	\$0
Webster	Park Ave ES	New	DBB	Jun-13	\$35,840,565	\$31,650,000	\$4,190,565	76.86%	\$3,220,868
Wakefield	Galvin MS	New	CMR	Jun-13	\$59,756,583	\$59,756,583	\$0	54.67%	\$0
Andover	Bancroft ES	New	CMR	Jul-13	\$34,527,063	\$40,218,065	-\$5,691,002	44.00%	\$0
Southwick-Tolland-Granville RSD	MS/HS	Add/Reno	DBB	Jul-13	\$31,408,667	\$24,994,000	\$6,414,667	66.53%	\$4,267,678
Greenfield	Greenfield HS	New	CMR	Aug-13	\$52,936,594	\$53,507,787	-\$571,193	80.00%	\$0
Concord-Carlisle RSD	Concord Carlisle HS	New	CMR	Aug-13	\$71,904,161	\$76,143,704	-\$4,239,543	35.58%	\$0
Greater New Bedford RVT	Greater New Bedford RVTHS	Add/Reno	DBB	Sep-13	\$13,679,847	\$11,779,700	\$1,900,147	80.00%	\$1,520,118
Georgetown	Penn Brook ES	New	DBB	Sep-13	\$36,979,465	\$32,910,000	\$4,069,465	54.76%	\$2,228,439
West Bridgewater	MS/HS	New	DBB	Sep-13	\$49,727,766	\$45,400,000	\$4,327,766	54.16%	\$2,343,918

\*These numbers are based on preliminary information received from the district and are subject to further review and calculation.

\*\*The construction estimate and bid amount do not include pre-construction services and alternatives.

\*\*\*Southwick-Tolland-Granville Powder Mill ES & Woodland ES projects are two separate projects but were bid as one project. The data is combined until further information is available.

## Science Lab Initiative – Construction Estimate vs. 2013 Bid Amount

- Of the eight projects; eight bids have been received.
- All eight are within the district’s estimated budget.
- One new bid since the October Board Meeting.

District	School	Scope	Project Type	Bid Date	Construction Estimate **	Bid Amount **	Variance from Construction Estimate	Reimbursement Rate	Potential Grant Variance *
				Total	\$56,316,432	\$46,287,013	\$10,029,419	-	\$6,921,826
Melrose	Melrose HS	SLI	DBB	Feb-13	\$4,938,311	\$3,239,000	\$1,699,311	50.79%	\$863,080
Gardner	Gardner HS	SLI/Windows	DBB	Feb-13	\$2,934,333	\$2,745,319	\$189,014	78.95%	\$149,227
Blackstone Valley RSD	Blackstone Valley RHS	SLI	DBB	Feb-13	\$625,395	\$553,997	\$71,398	53.53%	\$38,219
Holyoke RSD	William Dean VTHS	SLI	DBB	Mar-13	\$5,352,000	\$4,022,000	\$1,330,000	80.00%	\$1,064,000
Tri-County RVSD	Tri-County RVTHS	SLI	DBB	Mar-13	\$1,241,940	\$908,000	\$333,940	50.79%	\$169,608
North Attleborough	North Attleborough HS	SLI	DBB	Apr-13	\$4,650,000	\$4,411,000	\$239,000	52.06%	\$124,423
Medford	Medford HS	SLI	DBB	Aug-13	\$10,866,010	\$8,850,000	\$2,016,010	59.16%	\$1,192,672
Springfield	Central HS	SLI/Add	CMR	Sep-13	\$25,708,443	\$21,557,697	\$4,150,746	80.00%	\$3,320,597

\*These numbers are based on preliminary information received from the district and are subject to further review and calculation.

\*\*The construction estimate and bid amount do not include pre-construction services and alternatives.

## Core Program – Total Project Budget Update


Upon receiving the Board’s approval of the Project Scope and Budget, the MSBA and participating districts enter into a Project Funding Agreement that establishes the Total Project Budget and the Estimated Maximum Total Facilities Grant for an approved project. Of the grants authorized by the Board, nine projects have increased their Total Project Budgets due to acceptance of construction bids higher than the project estimates, and one project has increased their Total Project Budget due to an increase in its site acquisition cost budget. In no event has the increase in budget resulted in an increase to the Estimated Maximum Total Facilities Grant as authorized by the Board. Please note that staff reported on the budget increases for the seven projects shaded below at previous Board meetings.

District	School Name	Scope	Project Funding Agreement		PFA Bid Amendment		Reason for Increase to Total Project Budget
			Total Project Budget	Total Maximum Facilities Grant	Total Project Budget	Total Maximum Facilities Grant	
<b>Core Program</b>							
Andover	Bancroft Elementary School	New	\$44,659,837	\$16,773,753	\$50,374,837	TBD*	The District has appropriated additional funds to cover the costs associated with increased construction costs and additional contingencies for litigation/settlement costs and other ineligible costs.
Essex North Shore Agricultural & Technical School	Essex North Shore Agricultural & Technical School District	New	\$125,000,000	\$77,500,000	\$133,770,000	\$77,500,000	The Board was informed at the March 30, 2011 meeting that the Total Project Budget had increased due to additional ineligible scope that would be funded by DCAM.
Essex North Shore Agricultural & Technical School	Essex North Shore Agricultural & Technical School	New	\$125,000,000	\$77,500,000	\$134,501,368	\$77,500,000	The District has appropriated additional funds to cover the costs associated with increased construction costs for horse tack barn renovations.
Lexington	Estabrook Elementary School	New	\$40,792,248	\$12,250,739	\$42,554,862	TBD*	The District has executed a GMP that exceeds the Construction Budget of the PFA. The District is currently reviewing its project budget to determine the use of the additional appropriation funds it appropriated in excess of the Total Project Budget.
North Reading	North Reading Middle /High School	Add/Reno	\$107,727,074	\$49,323,123	\$123,227,074	\$49,323,123	This is a CMR project. The estimated, reconciled construction costs tracked over budget at DD (\$9,746,655 over), 60% (\$4,655,965 over), and 90% (\$15,136,846 over). A Town override vote in March 2013 obtained an additional \$15,500,000 in local funding to proceed.
Revere	Staff Sergeant James J. Hill Elementary School (currently the McKinley ES)	New	\$45,402,396	\$29,551,048	TBD*	\$29,551,048	At Project Scope and Budget, the Total Project Budget was approved at \$44,382,396. The City of Revere has increased the land acquisition budget. Therefore, the projected total project budget at PFA has increased to \$45,402,396. Note that the MSBA grant has not changed since the Project Scope and Budget Agreement.
Somerville	East Somerville Community School	Add/Reno	\$33,185,258	\$15,237,996	\$38,006,621	\$15,237,996	At the March 28, 2012 Board Meeting, the Board approved an amendment to the PFA and a \$6.25M District loan.
Uxbridge	Uxbridge High School	New	\$43,000,000	\$22,362,328	\$44,986,479	\$22,362,328	The District has appropriated additional funds to cover the costs associated with the construction of athletic fields originally included in the PFA but which were not included in the bid as the District's construction contract would have exceeded the budget.

\*PFA Bid Amendment has not been developed to calculate a revised total facilities grant amount. The Total Maximum Facilities Grant will not exceed the Board authorized amount in the PFA but upon review may decrease.

## Status of Green Repair Program

169 projects participating in the Green Repair Program have received authorization to enter into a PFA, totaling \$366,647,226 in Total Project Costs and \$222,885,258 in MSBA grants.

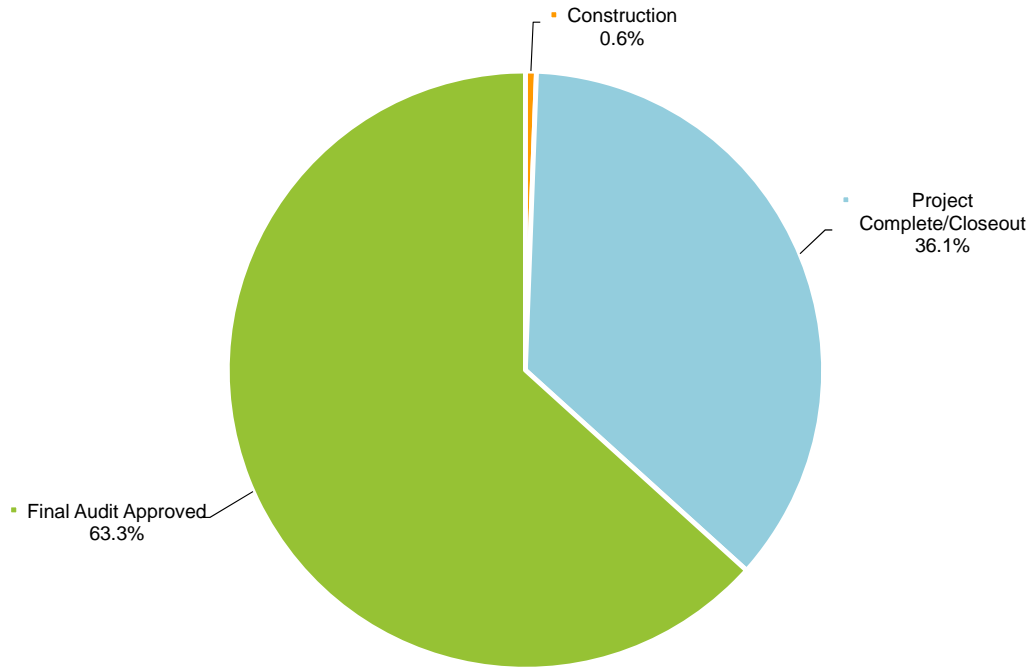

Since the October report, one project has completed construction leaving one project with an anticipated completion in December 2013. Since the October report, 11 additional projects have had a final audit approved.



## Green Repair – Schedule Extension Update

Eight of the 169 Green Repair Projects did not meet their anticipated construction completion deadline in 2012. Schedule delays can be attributed to bid protests, lead time for windows, and construction delays on site.

The MSBA granted each district a conditional extension to its Project Funding Agreement pending compliance with the following stipulations:

- The district needed to submit a detailed, revised construction timeline showing how the work will be completed at each school by August 30, 2013;
- An Amendment to the Project Funding Agreement between the MSBA and the district needed to be executed to include the updated project schedule; and
- Any costs that may result from the district’s requested extension of the construction schedule will be the sole responsibility of the district and are categorically ineligible for reimbursement by the MSBA.

Each of these projects has a revised construction schedule and will be complete by the beginning of the 2013-2014 school year. In no event has the extended schedule resulted in an increase to the Estimated Maximum Total Facilities Grant as authorized by the Board. Please note that staff reported on the schedule extensions for the eight projects shaded below at previous Board meetings: Since last report, the remaining projects have achieved substantial completion. ***No changes to this report.***

District	School	Scope	Original Construction Completion Date	Updated Construction Completion Date	Reason for Schedule Extension
Brockton	Brockton High School	Windows and Roof	31-Dec-12	Complete Dec - 2012	Construction fell behind schedule and the District did not want work being done in an occupied building. The roof work is complete.
Haverhill	Consentino Middle School	Windows and Boiler	31-Dec-12	Complete Aug - 2013	Bid protests and lead times caused the window project to extend beyond the 2012 construction deadline. The boiler project is complete.
Haverhill	John G. Whittier Middle School	Windows	31-Dec-12	Complete Aug - 2013	Bid protests and lead times caused the window project to extend beyond the 2012 construction deadline.
Lowell	Moody Elementary School	Windows	15-Aug-12	Complete Aug - 2013	Construction fell behind schedule and the District did not want work being done in an occupied building.
Lowell	Washington Elementary School	Windows	15-Aug-12	Complete Aug - 2013	Construction fell behind schedule and the District did not want work being done in an occupied building.
Shrewsbury	Spring Street Elementary School	Roof and Windows	24-Dec-12	Complete Feb - 2013	The district issued a Change Order to add shrouds over the window wall unit ventilators.
Wachusett Regional	Thomas Prince Elementary School	Roof	23-Mar-12	Complete April - 2013	The district issued a Change Order to replace an existing skylight and due to lead times the work cannot be done until the spring of 2013.
Westport	Westport High School	Roof	4-Sep-12	Complete April - 2013	The district issued a Change Order to add scuppers to the roof and the work will be completed in the spring of 2013.

## Green Repair - Total Project Budget Update

Upon receiving the Board's approval of the Project Scope and Budget, the MSBA and participating districts enter into a Project Funding Agreement that establishes the Total Project Budget and the Estimated Maximum Total Facilities Grant for an approved project. Of the 169 grants authorized by the Board for the Green Repair Program, 17 projects have increased their Total Project Budgets due to acceptance of construction bids higher than the project estimates, or as a result of change orders issued on the project. In no event has the increase in budget resulted in an increase to the Estimated Maximum Total Facilities Grant as authorized by the Board. Please also note that staff reported on the budget increases for all 17 of the projects shaded and shown below at previous Board meetings. *No changes to this report.*


District	School Name	Scope	Project Funding Agreement		PFA Bid Amendment		Reason for Increase to Total Project Budget
			Total Project Budget	Total Maximum Facilities Grant	Total Project Budget	Total Maximum Facilities Grant	
<b>Green Repair Program</b>							
Arlington	M. Norcross Stratton Elementary School	Roof, Window, Boiler	\$2,445,395	\$739,336	\$2,445,395	\$739,336	Change Orders exhausted the construction contingency.
Barnstable	West Barnstable Elementary School	Windows	\$1,173,175	\$437,829	\$1,239,205	\$437,829	Change Orders exhausted the construction contingency.
Boston	Excel High School	Roof	\$1,227,180	\$908,850	\$1,454,735	\$908,850	District elected to accept the base bid that was higher than the approved budget. District appropriated additional funds to support overage.
Boston	Excel High School	Roof	\$1,454,735	\$908,850	\$1,544,018	\$908,850	Change Orders exhausted the construction contingency.
Brockton	Hancock Elementary School	Roof	\$2,292,164	\$1,814,937	\$2,422,742	\$1,814,937	District elected to accept the base bid that was higher than the approved budget. District appropriated additional funds to support overage.
Brockton	West Junior High School	Roof	\$2,742,386	\$2,171,001	\$3,069,905	\$2,171,001	District elected to accept the base bid that was higher than the approved budget. District appropriated additional funds to support overage.
Fitchburg	South Street Elementary School	Boiler	\$701,186	\$560,949	\$705,391	\$501,079	Change Orders exhausted the construction contingency.
Florida	Gabriel Abbott Memorial School	Roof	\$380,310	\$213,172	\$389,422	\$188,804	Project included \$80,153 in Change Orders that offset bid savings and exhausted the construction contingency.
Hancock	Hancock Elementary School	Roof/HVAC	\$277,450	\$125,740	\$400,805	\$125,740	District elected to accept the base bids in Phases 2 and 3 that were higher than the approved budget. District needs to appropriate the overage.
Lexington	Lexington High School	Roof	\$1,122,890	\$381,221	\$1,197,444	\$381,221	District elected to accept base bid and alternates. District appropriated additional funds to support overage.
Narragansett Regional	Phillipston Memorial Elementary School	Boiler	\$143,225	\$85,712	\$161,232	\$83,275	District elected to accept the base bid that was higher than the approved budget. District appropriated additional funds to support overage.
North Attleborough	Falls Elementary School	Windows	\$701,263	\$361,433	\$710,000	\$348,948	District elected to accept the base bid that was higher than the approved budget. District's original appropriation was for \$710,000; therefore the overage was covered.
Peabody	John E. Burke Elementary School	Roof, Window, Boiler	\$2,909,873	\$1,452,745	\$3,473,534	\$1,431,417	District elected to accept the base bid that was higher than the approved budget. District appropriated additional funds to support overage.
Peabody	William A. Welch Elementary School	Roof	\$1,280,511	\$646,728	\$1,437,800	\$630,732	District elected to accept the base bid that was higher than the approved budget. District appropriated additional funds to support overage.
Pentucket Regional	Dr. John C. Page Elementary School	Roof, Window, Boiler	\$3,148,424	\$1,618,920	\$3,272,630	\$1,618,920	District elected to accept the base bid that was higher than the approved budget. District appropriated additional funds to support overage.
Reading	Birch Meadow Elementary School	Window	\$735,846	\$347,393	\$787,640	\$347,393	District elected to accept the base bid that was higher than the approved budget. Town Accountant certified that the FY2011 School Committee Operating Budget had an appropriation and encumbrance for the additional costs of the project.
Westfield	Westfield Vocational Technical High School	Roof, Window, Boiler	\$8,442,762	\$5,296,989	\$8,895,495	\$5,296,989	District elected to accept the base bid that was higher than the approved budget. District also approved an amendment to its Designer contract which increased the fee. District appropriated additional funds to support overage.

## **Status of Accelerated Repair Program**

Currently there are a total of 50 districts, representing 83 projects, in the Accelerated Repair Program.

### **2012 Accelerated Repair Program**

All 24 districts, representing 36 projects, approved in 2012 are under contract with consultants and have been authorized to enter into a PFA, totaling \$63,009,653 in Total Project Costs and a maximum of \$38,267,952 in MSBA Total Facilities Grant funding. Of the 36 projects, 28 are scheduled to complete construction in 2013, and eight are scheduled to complete construction in 2014. The chart below represents the progress of the 36 projects approved in 2012.

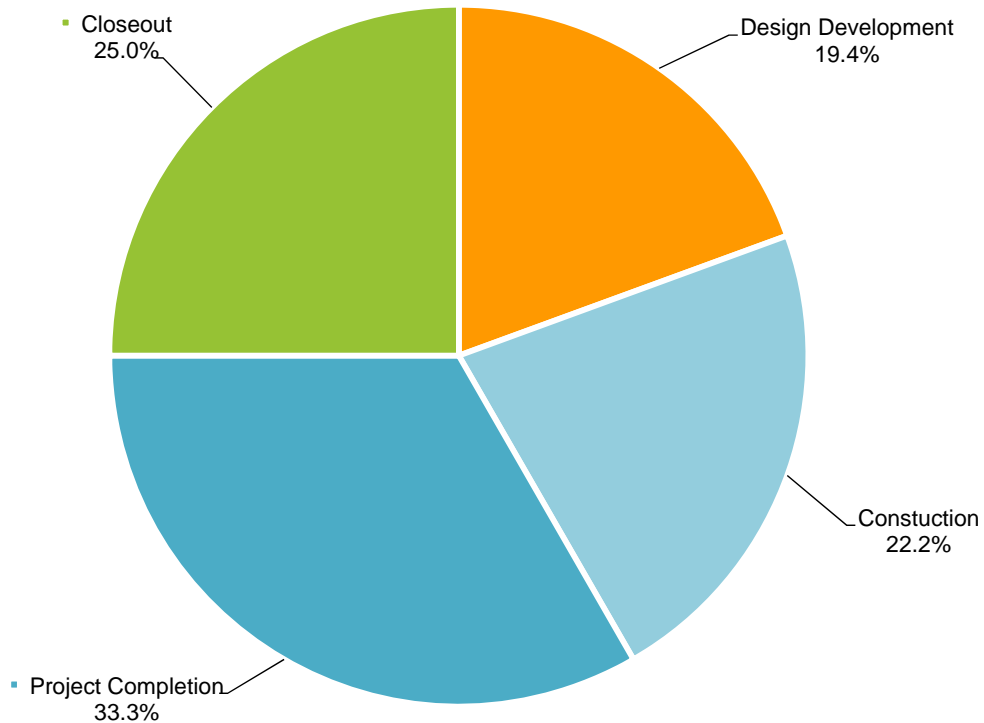

### **2013 Accelerated Repair Program**

Through the October Board meeting, 28 districts, representing 50 projects, were invited into the Accelerated Repair Program. At the October Board Meeting, one district, representing two projects, was removed from the Program. One district, representing one project, is scheduled for Program removal at the November Board Meeting. Following the Board's vote, the Accelerated Repair Program will have 26 districts, representing 47 projects. Of the 26 districts, two districts, representing seven projects, are seeking approval for Project Funding Agreements at the November Board Meeting.

## Accelerated Repair Projects – Construction Estimate vs. 2013 Bid Amount

- Out of 36 projects, 32 expected to bid in 2013.
- Of the 32, 29 bids have been received.
- Of the 29 projects, 25 bids came within the estimated budget.
- No new bids since the October Board Meeting.

District	School	Scope	Project Type	Bid Date	Construction Estimate **	Bid Amount **	Variance from Construction Estimate	Reimbursement Rate	Potential Grant Variance *
				Total	\$40,231,802	\$31,039,736	\$9,192,066	-	\$6,108,260
Weymouth	William Seach PS	Boiler	DBB	Dec-12	\$425,213	\$459,104	-\$33,891	54.16%	\$0
Groton-Dunstable RSD	Gronton-Dunstable MS	Roof	DBB	Feb-13	\$1,316,890	\$942,000	\$374,890	45.74%	\$171,475
Hamilton-Wenham	Cutler ES	Roof	DBB	Feb-13	\$547,326	\$444,150	\$103,176	43.42%	\$44,799
North Brookfield	North Brookfield ES	Windows	DBB	Feb-13	\$274,254	\$199,400	\$74,854	62.67%	\$46,911
Shawsheen Valley Voc/Tech.	Shawsheen Valley VTHS	Boiler	DBB	Mar-13	\$805,423	\$535,000	\$270,423	52.06%	\$140,782
Sudbury	Gen. John Nixon ES	Roof	DBB	Mar-13	\$621,554	\$542,775	\$78,779	36.89%	\$29,062
Easton	Easton Jr. HS	Roof	DBB	Mar-13	\$1,850,830	\$1,889,000	-\$38,170	50.16%	\$0
Norton	Solmonese ES	Roof	DBB	Mar-13	\$1,166,044	\$986,000	\$180,044	55.63%	\$100,158
Attleborough	Irvin Studley ES	Roof	DBB	Mar-13	\$773,363	\$489,000	\$284,363	57.74%	\$164,191
Lynn	Breed MS	Windows	DBB	Mar-13	\$1,796,674	\$2,167,300	-\$370,626	80.00%	\$0
Lynn	Lynn Voc. Tech	Roof	DBB	Mar-13	\$4,173,000	\$3,097,000	\$1,076,000	80.00%	\$860,800
Worcester	Chandler Magnet	Windows	DBB	Mar-13	\$3,723,463	\$3,142,320	\$581,143	80.00%	\$464,914
Worcester	Jacob Hiatt Magnet	Boiler	DBB	Mar-13	\$298,877	\$321,703	-\$22,826	80.00%	\$0
Worcester	James Caradonio Center	Windows & Boiler	DBB	Mar-13	\$1,021,820	\$1,007,132	\$14,688	80.00%	\$11,750
Worcester	Lake View	Windows	DBB	Mar-13	\$1,127,970	\$789,398	\$338,572	80.00%	\$270,858
Worcester	May Street	Windows	DBB	Mar-13	\$1,655,289	\$1,548,167	\$107,122	80.00%	\$85,698
Gardner	Gardner MS	Boiler	DBB	Apr-13	\$438,439	\$396,100	\$42,339	78.95%	\$33,427
North Attleborough	Roosevelt Ave. ES	Windows	DBB	Apr-13	\$768,000	\$656,483	\$111,517	52.06%	\$58,056
Quabaog RSD	Warren ES	Boiler	DBB	Apr-13	\$207,000	\$182,444	\$24,556	68.34%	\$16,782
Quabbin	Ruggles Lane ES	Roof & Windows	DBB	Apr-13	\$2,588,409	\$2,287,836	\$300,573	57.74%	\$173,551
Leominster	Fall Brook ES	Boiler	DBB	Apr-13	\$949,550	\$684,000	\$265,550	73.38%	\$194,861
Leominster	Southeast ES	Roof & Boiler	DBB	Apr-13	\$3,146,097	\$1,948,000	\$1,198,097	73.38%	\$879,164
Westfield	Munger Hill ES	Roof	DBB	Apr-13	\$1,170,735	\$593,499	\$577,236	59.84%	\$345,418
Westfield	Paper Mill ES	Roof	DBB	Apr-13	\$1,170,735	\$562,525	\$608,210	59.84%	\$363,953
Southampton	William Norris ES	Roof	DBB	May-13	\$1,504,147	\$922,000	\$582,147	55.00%	\$320,181
Taunton	Galligan School	Roof	DBB	May-13	\$543,570	\$486,600	\$56,970	73.95%	\$42,129
Wayland	Wayland MS	Roof	DBB	May-13	\$2,445,767	\$1,965,800	\$479,967	36.89%	\$177,060
Blackstone-Milville RSD	Maloney ES	Roof	DBB	Sep-13	\$1,405,656	\$702,000	\$703,656	57.74%	\$406,291
Blackstone-Milville RSD	J.F.Kennedy ES	Roof	DBB	Sep-13	\$2,315,707	\$1,093,000	\$1,222,707	57.74%	\$705,991


\*These numbers are based on preliminary information received from the district and are subject to further review and calculation.

\*\*The construction estimate and bid amount do not include pre-construction services and alternatives.

# 2012-2014 Eligibility Period Status

October 30, 2013  
5 Projects in Eligibility Period


Task Remaining    
  Partial Task Completed  
 Invite / Completion Date    
  Completed Task



District	2012		2013												2014						
	Nov	Dec	Jan	Feb	Mar	April	May	June	July	Aug	Sept	Oct	Nov	Dec	Jan	Feb	Mar	April	May	June	July
Holyoke Lt. McMahon ES	11/14/12	11/28/12	12/28/12	1/28/13	Maintenance Docs		Enrollment Certification		5/27/13	Local Authorization		FSA (270 days)									
Dedham Early Education Center			1/30/13	2/14/13	3/16/13	4/16/13	5/14/13		8/13/13		11/12/13										
Granby West Street School			1/30/13	2/14/13	3/16/13	4/16/13	5/14/13		8/13/13		11/12/13										
Beverly Briscoe Middle School									10/2/13	10/16/13	11/15/13	12/16/13	1/14/14				4/14/14		7/14/2014		
Mount Greylock RSD Mount Greylock RHS									10/2/13	10/16/13	11/15/13	12/16/13	1/14/14				4/14/14		7/14/2014		
District	Nov	Dec	Jan	Feb	Mar	April	May	June	July	Aug	Sept	Oct	Nov	Dec	Jan	Feb	Mar	April	May	June	July

## Project Status | October 30, 2013

Core Program:	79
Waitlist:	0
Green Repair:	1
Accelerated Repair:	63
Science Lab Initiative:	2
Project Complete / Substantial Completion:	48
Closeout:	92
Final Audit Approved:	24
<b>Total Projects:</b>	<b>309</b>

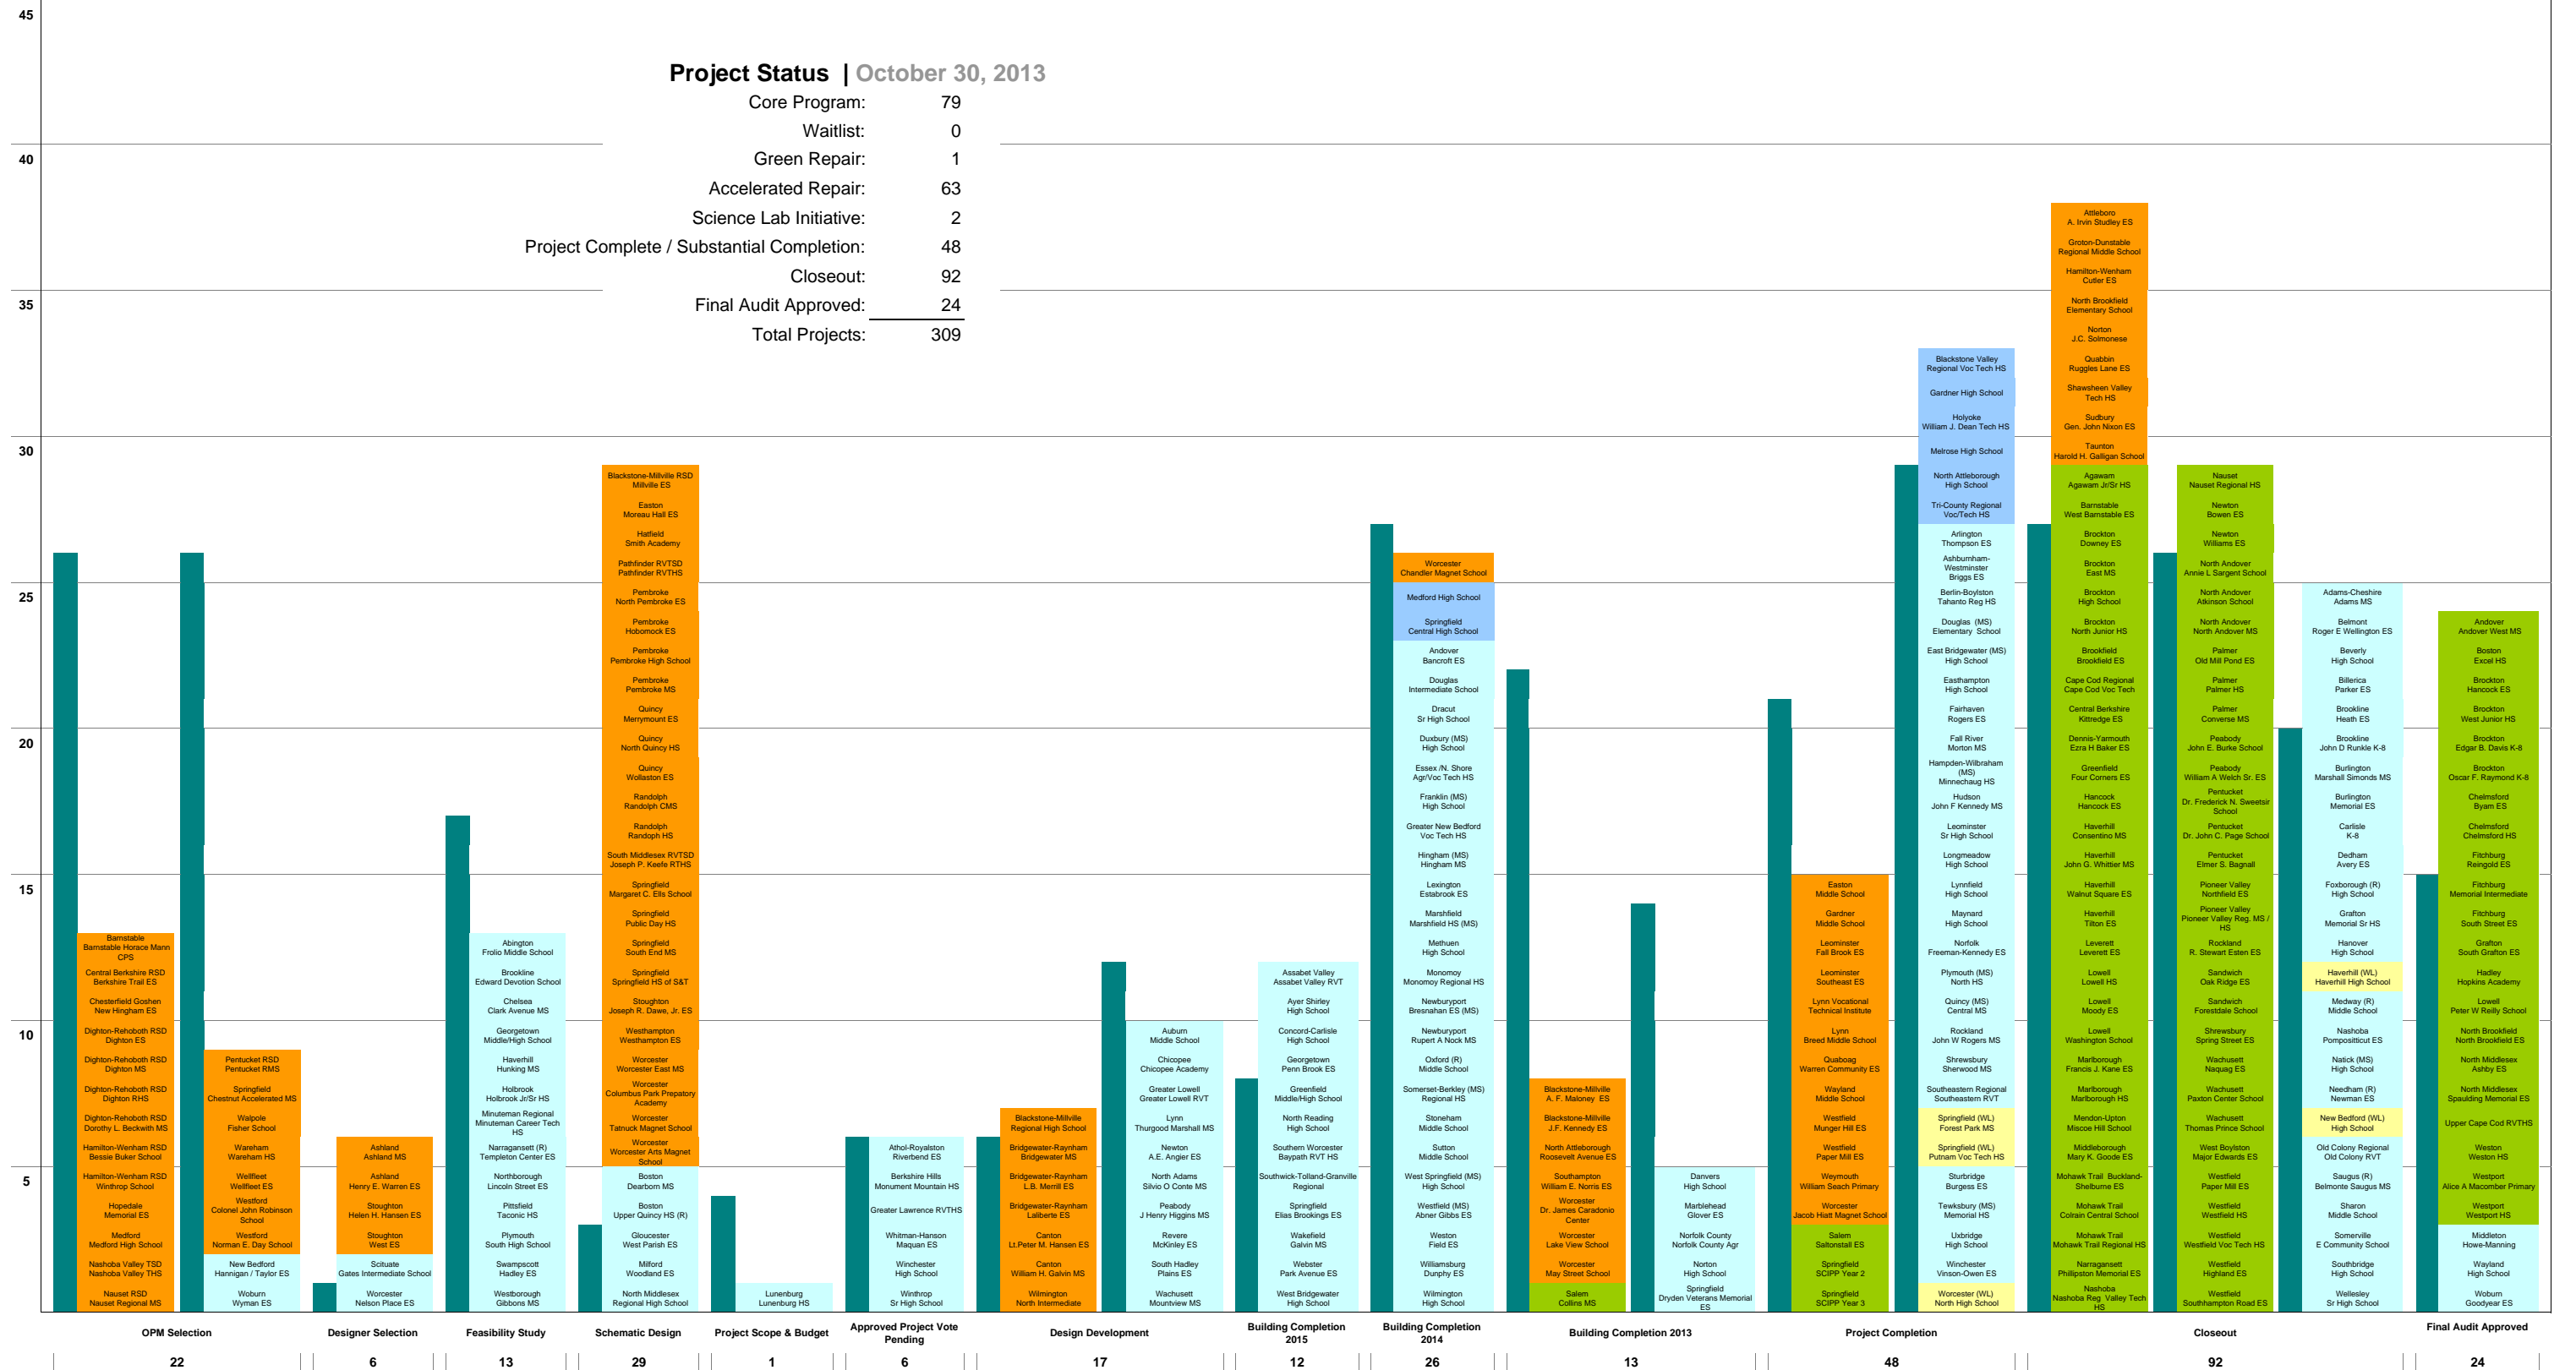

# PROJECT STATUS


309  
Total Active  
Projects

- Green Repair Program
- Accelerated Repair Program
- Science Lab Initiative Project
- Accelerated Repair Program - To Be Removed

- Waitlist Projects
- Capital Pipeline Status Presented at July 31, 2013 Board of Directors Meeting

## Project Status | October 30, 2013

Core Program:	79
Waitlist:	0
Green Repair:	1
Accelerated Repair:	63
Science Lab Initiative:	2
Project Complete / Substantial Completion:	48
Closeout:	92
Final Audit Approved:	24
<b>Total Projects:</b>	<b>309</b>

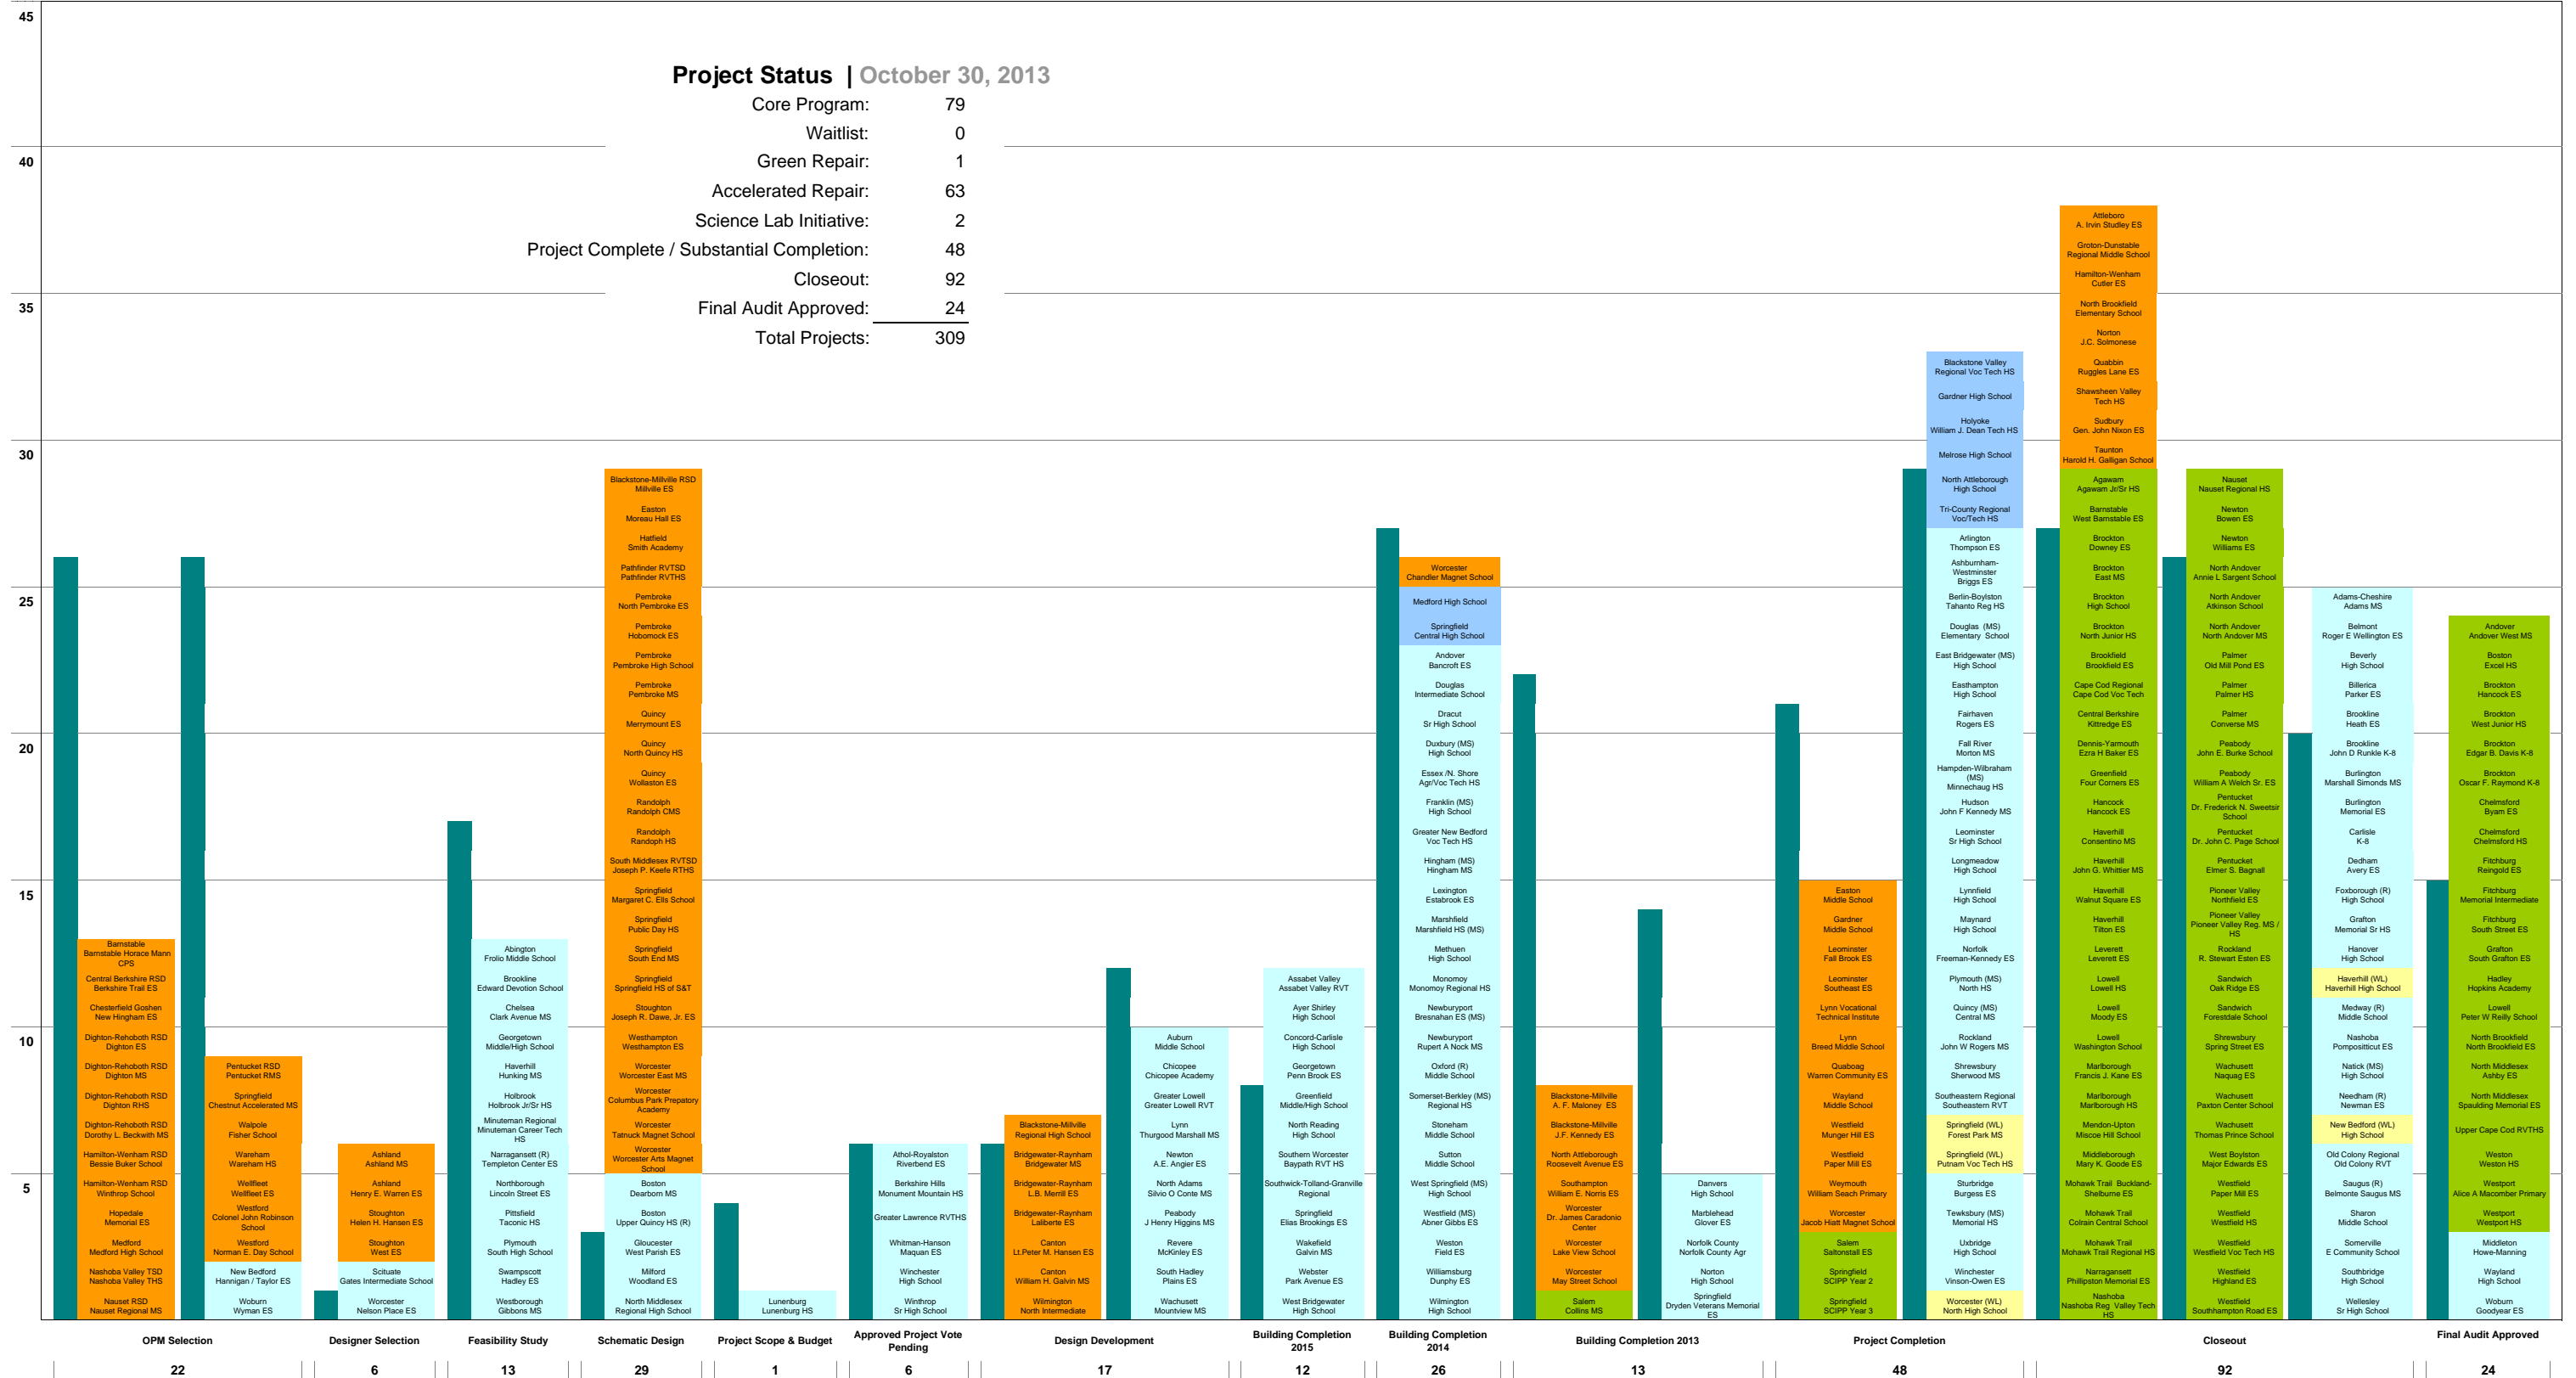

# PROJECT STATUS

309  
Total Active  
Projects

- Green Repair Program
- Accelerated Repair Program
- Science Lab Initiative Project
- Accelerated Repair Program - To Be Removed

- Waitlist Projects
- Capital Pipeline Status Presented at July 31, 2013 Board of Directors Meeting



MSBA ID	District	School	Phase	Project Scope	Procurement Type	OPM	Designer	Cx Company	CMGC
20080010405	Abington	Froio Middle School	Feasibility Study			Knight, Bagge & Anderson Inc.	Ai3 Architects LLC		-
200806030305	Adams-Cheshire	Adams Memorial Middle School	Closeout	Addition / Renovation	CM@R	URS Corporation	Tessier Associates, Inc.	Strategic Building Solutions, LLC	Gilbane Building Company
201100050405G	Agawam	Agawam Junior/Senior High School	Closeout	Repair - Accelerated	DBB	Municipal Building Consultants, Inc.	CSS Architects Incorporated	Building Enclosure Associates	Capeway Roofing Systems, Inc.] Chandler Architectural Products, Inc.
200800090003	Andover	Bancroft Elementary School	Construction	New Construction	CM@R	Dore & Whittier Management Partners, Inc.	Symmes Maini & McKee Associates, Inc.	Sebesta Blomberg & Associates, Inc.	Skanska USA Building, Inc.
201100090310G	Andover	Andover West Middle School	Final Audit Approved	Repair - Accelerated	DBB	Skanska USA Building, Inc	Russo Barr Associates, Inc.	Simpson Gumpertz & Heger Inc.	Eagle Rivet Roof Services Corporation
200900100050	Arlington	Thompson Elementary School	Project Completion	New Construction	DBB	PMA Construction Services	HMFH Architects, Inc.	Consulting Engineering Services, LLC	G & R Construction, Inc.
200806100025	Ashburnham-Westminster	John R. Briggs Elementary School	Project Completion	New Construction	CM@R	STV Incorporated	Lamoureux Pagano & Associates, Inc.	Foreman Building Commissioning, LP	Consigli Construction Company, Inc.
201300140405	Ashland	Ashland Middle School	Designer Selection	Repair - Accelerated					
201300140010	Ashland	Henry E Warren Elementary School	Designer Selection	Repair - Accelerated					
200908010605	Assabet Valley	Assabet Valley Regional Technical High School	Construction	Repair - Major	DBB	Strategic Building Solutions, LLC	Design Partnership of Cambridge, Inc.	Symmes, Maini & McKee Associates	-
200906150020	Athol-Royalston	Riverbend Elementary School	Approved Project Vote Pending	Repair- Accelerated		Symmes Maini & McKee Associates, Inc.	Mount Vernon Group Architects, Inc.		-
201200160001	Attleboro	A. Irvin Studley Elementary School	Closeout	Repair - Accelerated		Tishman Construction Corporation of MA	Gale Associates, Inc.	CBI Consulting Inc.	
200800170305	Auburn	Auburn Middle School	Design Development	New Construction		Skanska USA Building, Inc	Lamoureux Pagano & Associates, Inc.	WSP Flack + Kurtz	-
9999	Ayer-Shirley	Ayer-Shirley Regional Middle/High School	Construction	Addition / Renovation	CM@R	Dore and Whittier Architects, Inc.	Symmes Maini & McKee Associates, Inc.	WSP Flack + Kurtz	Consigli Construction Company, Inc.
201100200005G	Barnstable	West Barnstable Elementary School	Closeout	Repair - Accelerated	DBB	PMA Construction Services	Gale Associates, Inc.	CBI Consulting Inc.	Paul J. Rogan Co., Inc.
201300200010	Barnstable	Horace Mann Charter School	OPM Selection	Repair - Accelerated					
200800260035	Belmont	Roger Wellington Elementary School	Closeout	New Construction	CM@R	PMA Construction Services	Jonathan Levi Architects LLC	Strategic Building Solutions, LLC	Skanska USA Building, Inc.
201006180505	Berkshire Hills	Monument Mountain Regional High School	Approved Project Vote Pending			Strategic Building Solutions, LLC	Symmes Maini & McKee Associates, Inc.		-
200806200505	Berlin-Boylston	Tahanto Regional High School	Project Completion	New Construction	DBB	PMA Construction Services	HMFH Architects, Inc.	Strategic Building Solutions, LLC	CTA Construction Co., Inc.
200800300505	Beverly	Beverly High School	Closeout	Addition / Renovation		HEERY	Mount Vernon Group Architects, Inc.		
201300300305	Beverly	Briscoe Middle School	Eligibility Period						
200800310015	Billerica	Parker Elementary School	Closeout	New Construction	DBB	Joslin, Lesser + Associates Inc.	Symmes Maini & McKee Associates, Inc.	Sebesta Blomberg & Associates, Inc.	CTA Construction Co., Inc.   RS Hurford
201306220010	Blackstone - Millville	Millville Elementary School	Schematic Design	Repair - Accelerated					
201206220015	Blackstone Valley - Millville	A.F. Maloney Elementary School	Construction	Repair- Accelerated		Arcadis	DiMarinisi & Wolfe Architects Urban Designers	Gale Associates, Inc.	
201206220008	Blackstone Valley - Millville	J.F. Kennedy Elementary School	Construction	Repair- Accelerated		Arcadis	DiMarinisi & Wolfe Architects Urban Designers	Gale Associates, Inc.	
201206220505	Blackstone Valley - Millville	Regional High School	Design Development	Repair - Accelerated		Arcadis	DiMarinisi & Wolfe Architects Urban Designers	Gale Associates, Inc.	
201208050605	Blackstone Valley Reg	Blackstone Valley	Project Completion	Science Lab		Compass Project Management, Inc.	Flansburgh Associates, Inc.	Horizon Engineering Associates, LLP	Pergola Constrion Company, Inc.
201100350522G	Boston	Excel High School	Final Audit Approved	Repair - Accelerated	DBB	Daedalus Projects Inc	BLW Engineers, Inc.	Simpson Gumpertz & Heger Inc.	-
201000350074	Boston	Henry Dearborn Middle School	Schematic Design			Daedalus Projects Inc	Jonathan Levi Architects LLC		-
201000350565	Boston	Quincy Upper High School	Schematic Design			Maureen Anderson - City Employee	HMFH Architects, Inc.		-
201206250320	Bridgewater-Raynham	Bridgewater Middle School	Design Development	Repair - Accelerated		Pinck & Co., Inc.			
201206250020	Bridgewater-Raynham	L.B. Merrill Elementary School	Design Development	Repair - Accelerated		Pinck & Co., Inc.			
201206250050	Bridgewater-Raynham	Laliberte Elementary School	Design Development	Repair - Accelerated		Pinck & Co., Inc.			





MSBA ID	District	School	Phase	Project Scope	Procurement Type	OPM	Designer	Cx_Company	CMGC
201100440110G	Brockton	Downey Elementary School	Closeout	Repair - Accelerated	DBB	Skanska USA Building, Inc	CSS Architects Incorporated	Simpson Gumpertz & Heger Inc.	Built-up Roofing Systems LLC
201100440405G	Brockton	East Junior High School	Closeout	Repair - Accelerated	DBB	Skanska USA Building, Inc	CSS Architects Incorporated	Rist-Frost-Shumway Engineering, P.C.	Reliable Roofing and Sheet Metal, LLC
201100440410G	Brockton	North Junior High School	Closeout	Repair - Accelerated	DBB	Skanska USA Building, Inc	CSS Architects Incorporated	Rist-Frost-Shumway Engineering, P.C.	Arden Engineering Constructors, LLC Built-up Roofing Systems LLC
201100440505G	Brockton	Brockton High School	Closeout	Repair - Accelerated	DBB	Skanska USA Building, Inc	CSS Architects Incorporated	Simpson Gumpertz & Heger Inc.	Gibson Roofs, Inc.
201100440078G	Brockton	Oscar F Raymond K-8	Final Audit Approved	Repair - Accelerated	DBB	Skanska USA Building, Inc	CSS Architects Incorporated	Simpson Gumpertz & Heger Inc.	Reliable Roofing and Sheet Metal, LLC
201100440045G	Brockton	Hancock Elementary School	Final Audit Approved	Repair - Accelerated	DBB	Skanska USA Building, Inc	CSS Architects Incorporated	Simpson Gumpertz & Heger Inc.	Reliable Roofing and Sheet Metal, LLC
201100440420G	Brockton	West Junior High School	Final Audit Approved	Repair - Accelerated	DBB	Skanska USA Building, Inc	CSS Architects Incorporated	Simpson Gumpertz & Heger Inc.	Reliable Roofing and Sheet Metal, LLC
201100440023G	Brockton	Edgar B Davis School	Final Audit Approved	Repair - Accelerated	DBB	Skanska USA Building, Inc	CSS Architects Incorporated	Simpson Gumpertz & Heger Inc.	Reliable Roofing and Sheet Metal, LLC
201100450005G	Brookfield	Brookfield Elementary School	Closeout	Repair - Accelerated	DBB	Diversified Project Management	Habeeb & Associates Architects, Inc.	Cannon Design	Northeast Energy Control Systems
201000460025	Brookline	Heath Elementary School	Closeout	Addition / Renovation	DBB	Town of Brookline Building Department	Miller Dyer Spears Inc.	Consulting Engineering Services, LLC	Nauset Construction Corporation
200800460045	Brookline	John D. Runkle School	Closeout	Addition / Renovation	DBB	Town of Brookline Building Department	Design Partnership of Cambridge, Inc.	Consulting Engineering Services, LLC	G & R Construction, Inc.
201100460015	Brookline	Edward Devotion	Feasibility Study			Anthony Guigli - Town Employee	HMFH Architects, Inc.		
200800480015	Burlington	Memorial Elementary School	Closeout	New Construction	DBB	Construction Monitoring Services, Inc.	Knight, Bagge & Anderson, Inc.	Consulting Engineering Services, LLC	CTA Construction Co., Inc.
201000480303	Burlington	Marshall Simonds Middle School	Closeout	Addition / Renovation	DBB	Construction Monitoring Services, Inc.	Knight, Bagge & Anderson, Inc.	RDK Engineers	CTA Construction Co., Inc.
201200500012	Canton	Lt. Peter M. Hansen	Design Development	Repair - Accelerated		Vertex Construction Services	CSS Architects Incorporated		
201200500305	Canton	William H. Galvin Middle School	Design Development	Repair - Accelerated		Vertex Construction Services	CSS Architects Incorporated		
201008150605G	Cape Cod Region Voc Tech	Cape Cod Region Voc Tech High School	Closeout	Repair - Accelerated	DBB	URS Corporation	Garcia Galuska DeSousa Consulting Engineers Inc.	Fitzmeyer & Tocci Associates, Inc.	-
200800510025	Carlisle	Carlisle School	Closeout	Addition / Renovation	DBB	Daedalus Projects Inc	HMFH Architects, Inc.	Horizon Engineering Associates, LLP	H.V. Collins Co., Inc.
201106350035G	Central Berkshire	Kittredge Elementary School	Closeout	Repair - Accelerated	DBB	Daedalus Projects Inc	Bradley Architects, Inc.	Strategic Building Solutions, LLC	A.J. Schnopp Jr., Construction, Inc.   Alpha Contracting Associates, Inc.
201306350010	Central Berkshire	Berkshire Trail Elementary School	OPM Selection	Repair - Accelerated					
201100560505G	Chelmsford	Chelmsford High School	Final Audit Approved	Repair - Accelerated	DBB	Vertex Construction Services	Russo Barr Associates, Inc.	Simpson Gumpertz & Heger Inc.	Lockheed Window Corporations
201100560030G	Chelmsford	Byam Elementary School	Final Audit Approved	Repair - Accelerated	DBB	Vertex Construction Services	Russo Barr Associates, Inc.	Simpson Gumpertz & Heger Inc.	S.O.M. Construction Ent., Inc.
	Chelmsford - Goshen	New Hingham Elementary School	OPM Selection	Repair - Accelerated					
200800570050	Chelsea	Clark Avenue School	Feasibility Study			Pinck & Co., Inc.	HMFH Architects, Inc.		-
200900610021	Chicopee	Chicopee Academy	Design Development			Arcadis	Caolo & Bieniek Associates, Inc.	Symmes, Maini & McKee Associates	-
200906400505	Concord-Carlisle	Concord-Carlisle Regional High School	Construction	New Construction	CM@R	KV Associates, Inc.	OMR Architects, Inc.	Strategic Building Solutions, LLC	Turner Construction Company
200800710505	Danvers	Danvers High School	Construction	Addition / Renovation	DBB	Construction Monitoring Services, Inc.	DiNisco Design Partnership, Limited	Turner Facilities Management Solutions	Bacon Construction Co, Inc.
200800730010	Dedham	Avery Elementary School	Closeout	New Construction	CM@R	Construction Monitoring Services, Inc.	Dore & Whittier Architects, Inc.	WSP Flack + Kurtz	Consigli Construction Company, Inc.
201200730005	Dedham	Early Childhood Education Center	Eligibility Period						
201006450005G	Dennis-Yarmouth	Ezra Baker Elementary School	Closeout	Repair - Accelerated	DBB	STV Incorporated	Knight, Bagge & Anderson, Inc.	CBI Consulting Inc.	Antonelli Construction Co., Inc.
201306500005	Dighton-Rehoboth	Dighton Elementary School	OPM Selection						
201306500305	Dighton-Rehoboth	Dighton Middle School	OPM Selection						
201306500505	Dighton-Rehoboth	Dighton-Rehoboth Regional High School	OPM Selection						



MSBA ID	District	School	Phase	Project Scope	Procurement Type	OPM	Designer	Cx Company	CMGC
201306500310	Dighton-Rehoboth	Dorothy L. Beckwith Middle School	OPM Selection						
200800770100G	Douglas	Douglas Intermediate School	Construction	Repair - Accelerated	DBB	HEERY	DiNisco Design Partnership, Limited	Consulting Engineering Services, LLC	CTA Construction Co., Inc.
200800770010	Douglas	Douglas Elementary School	Project Completion	New Construction		HEERY	DiNisco Design Partnership, Limited	Consulting Engineering Services, LLC	CTA Construction Co., Inc.
200800790505	Dracut	Dracut Senior High School	Construction	Addition / Renovation	DBB	RF Walsh Collaborative Partners	Mount Vernon Group Architects, Inc.	RDK Engineers	CTA Construction Co., Inc.
201000820505	Duxbury	Duxbury High School	Construction	New Construction	CM@R	KV Associates, Inc.	Mount Vernon Group Architects, Inc.	WSP Flack + Kurtz	Dimeo Construction Company
200900830505	East Bridgewater	East Bridgewater High School	Project Completion	New Construction	DBB	RF Walsh Collaborative Partners	Ai3 Architects LLC	Foreman Building Commissioning, LP	Fontaine Brothers, Inc.
200800860505	Easthampton	Easthampton High School	Project Completion	New Construction	DBB	Strategic Building Solutions, LLC	Caolo & Bieniek Associates, Inc.	Consulting Engineering Services, LLC	Fontaine Brothers, Inc.
201200880405	Easton	Easton Junior High School	Project Completion	Repair - Accelerated		PMA Construction Services	Russo Barr Associates, Inc.	Gale Associates, Inc.	Gibson Roofs, Inc.
201300880020	Easton	Moreau Hall Elementary School	Schematic Design	Repair - Accelerated		Skanska USA Building, Inc	Baker/Wohl Architects, Inc.		
200809130705	Essex Agr Tech	Essex Agricultural and Technical High School	Construction	New Construction	CM@R	PMA Construction Services	Design Partnership of Cambridge, Inc.	Turner Facilities Management Solutions	Gilbane Building Company
200800940020	Fairhaven	Rogers Elementary School	Project Completion	New Construction	DBB	Daedalus Projects Inc	HMFH Architects, Inc.	Consulting Engineering Services, LLC	CTA Construction Co., Inc.
200900950315	Fall River	James Madison Morton Middle School	Project Completion	New Construction	DBB	Maguire Group Inc.	Mount Vernon Group Architects, Inc.	Sebesta Blomberg & Associates, Inc.	J & J Contractors, Inc.
201100970048G	Fitchburg	Memorial Intermediate	Final Audit Approved	Repair - Accelerated	DBB	Compass Project Management, Inc.	Knight, Bagge & Anderson, Inc.	Simpson Gumpertz & Heger Inc.	Lockheed Window Corporations
201100970043G	Fitchburg	Reingold Elementary School	Final Audit Approved	Repair - Accelerated	DBB	Compass Project Management, Inc.	Knight, Bagge & Anderson, Inc.	Simpson Gumpertz & Heger Inc.	Lockheed Window Corporations
201100970060G	Fitchburg	South Street Elementary	Final Audit Approved	Repair - Accelerated	DBB	Compass Project Management, Inc.	Knight, Bagge & Anderson, Inc.	Simpson Gumpertz & Heger Inc.	CAM HVAC & Construction, Inc.
200800990505	Foxborough	Foxborough High School	Closeout	Repair - Major	DBB	Construction Monitoring Services, Inc.	Kaestle Boos Associates, Inc.	Consulting Engineering Services, LLC	CTA Construction Co., Inc.
200901010505	Franklin	Franklin High School	Construction	New Construction	DBB	Daedalus Projects Inc	Ai3 Architects LLC	Consulting Engineering Services, LLC	Bacon-Agostini Construction Joint Venture
201201030405	Gardner	Gardner Middle School	Project Completion	Repair - Accelerated		Leftfield, LLC	Richard D. Kimball Company, Inc.	Fitzmeyer & Tocci Associates, Inc.	
201201030505	Gardner	Gardner High School	Project Completion	Science Lab		Pinck & Co., Inc.	Lamoureux Pagano & Associates, Inc.	Fitzmeyer & Tocci Associates, Inc.	-
200901050010	Georgetown	Penn Brook Elementary School	Construction	New Construction		Municipal Building Consultants, Inc.	Drumme Rosane Anderson, Inc.	Rist-Frost-Shumway Engineering, P.C.	-
200801050505	Georgetown	Georgetown Middle/High School	Feasibility Study			Municipal Building Consultants, Inc.	Drumme Rosane Anderson, Inc.		
200901070050	Gloucester	West Parish Elementary School	Schematic Design			Knight, Bagge & Anderson Inc.	Dore & Whittier Architects, Inc.		-
200801100505	Grafton	Grafton Memorial Senior	Closeout	New Construction	CM@R	Joslin, Lesser + Associates Inc.	Symmes Maini & McKee Associates, Inc.	Horizon Engineering Associates, LLP	Dimeo Construction Company
201101100005G	Grafton	South Grafton Elementary School	Final Audit Approved	Repair - Accelerated	DBB	URS Corporation	CGKV Architects, Inc.	Horizon Engineering Associates, LLP	AAIanco Service Corporation
201201110010	Granby	West Street School	Eligibility Period						
201108230605	Greater Lawrence RVT	Greater Lawrence Reg Voc Tech	Approved Project Vote Pending	Repair - Major		Vertex Construction Services	Richard D. Kimball Company, Inc.		-
200908280605	Greater Lowell Voc Tec	Greater Lowell Regional Technical High School	Design Development	Repair - Major		Joslin, Lesser + Associates Inc.	Knight, Bagge & Anderson, Inc.	Horizon Engineering Associates, LLP	Consigli Construction Company, Inc.
201008250605	Greater New Bedford	Vocational Technical High School	Construction	Addition / Renovation		Construction Monitoring Services, Inc.	Drumme Rosane Anderson, Inc.	Symmes, Maini & McKee Associates	-
201101140025G	Greenfield	Four Corners	Closeout	Repair - Accelerated	DBB	P3 Project Planning	Tighe & Bond, Inc.	Strategic Building Solutions, LLC	Five Star Building Corp.
200901140505	Greenfield	Greenfield Middle/High School	Construction	New Construction	DBB	Construction Monitoring Services, Inc.	Dore & Whittier Architects, Inc.	BVH Integrated Services, Inc.	Shawmut Design and Construction
201206730305	Groton-Dunstable	Groton Dunstable Regional Middle School	Closeout	Repair - Accelerated		Collaborative Partners	ICON architecture, inc.	Russo Barr Associates, Inc.	-
201101170505G	Hadley	Hopkins Academy	Final Audit Approved	Repair - Accelerated	DBB	Strategic Building Solutions, LLC	CCS Presentation Systems	Russo Barr Associates, Inc.	MDM Engineering
201206750010	Hamilton-Wenham	Cutler School	Closeout	Repair - Accelerated		Coast & Harbor Associates, Inc.	CBI Consulting, Inc.	Russo Barr Associates, Inc.	



MSBA ID	District	School	Phase	Project Scope	Procurement Type	OPM	Designer	Cx Company	CMGC
201306750007	Hamilton-Wenham	Bessie Buker Elementary School	OPM Selection	Repair - Accelerated					
201306750015	Hamilton-Wenham	Winthrop School	OPM Selection	Repair - Accelerated					
200806800505	Hampden-Wilbraham	Minnechaug Regional High School	Project Completion	New Construction	DBB	Pinnacle One, Inc.	Mount Vernon Group Architects, Inc.	Horizon Engineering Associates, LLP	Fontaine Brothers, Inc.
201001210005G	Hancock	Hancock Elementary School	Closeout	Repair - Accelerated	DBB	-	Westall Architects		Salco Construction Company, Inc.
200801220505	Hanover	Hanover High School	Closeout	New Construction	DBB	PMA Construction Services	HMF Architects, Inc.	Horizon Engineering Associates, LLP	Callahan, Inc.
201301270505	Hatfield	Smith Academy	Schematic Design	Repair - Accelerated			Collaborative Partners		
	Haverhill	High School	Closeout						
201101280100G	Haverhill	Consentino Middle School	Closeout	Repair - Accelerated	DBB	Vertex Construction Services	CSS Architects Incorporated	RDK Engineers  Russo Barr Associates, Inc.	New England Builders & Contractors, Inc. P.J. Dionne Company, Inc.
201101280085G	Haverhill	John G Whittier Middle School	Closeout	Repair - Accelerated	DBB	Vertex Construction Services	CSS Architects Incorporated	Russo Barr Associates, Inc.	New England Builders & Contractors, Inc.
201101280075G	Haverhill	Tilton Elementary School	Closeout	Repair - Accelerated	DBB	Vertex Construction Services	CSS Architects Incorporated	Russo Barr Associates, Inc.	Titan Roofing, Inc.
201101280080G	Haverhill	Walnut Square Elementary School	Closeout	Repair - Accelerated	DBB	Vertex Construction Services	CSS Architects Incorporated	RDK Engineers  Russo Barr Associates, Inc.	P.J. Dionne Company, Inc. Titan Roofing, Inc.
201201280035	Haverhill	Caleb Dustin Hunking Middle School	Feasibility Study			Joslin, Lesser + Associates Inc.	JCJ Architecture, PC		-
201001310410	Hingham	Hingham Middle School	Construction	New Construction	DBB	Knight, Bage & Anderson Inc.	Ai3 Architects LLC	Foreman Building Commissioning, LP	Brait Builders Corp.
200801330505	Holbrook	Holbrook Junior-Senior High School	Feasibility Study			Symmes Maini & McKee Associates, Inc.	Flansburgh Associates, Inc.		-
201201370015	Holyoke	Lt. McMahon Elementary School	Eligibility Period						
201201370605	Holyoke	Wm J Dean Voc Tech High	Project Completion	Science Lab		Skanska USA Building, Inc	Kaestle Boos Associates, Inc.	BVH Integrated Services, Inc.	-
201301380010	Hopedale	Memorial Elementary School	OPM Selection	Repair - Accelerated					
200801410410	Hudson	John F. Kennedy Middle School	Project Completion	New Construction	DBB	PMA Construction Services	OMR Architects, Inc.	WSP Flack + Kurtz	Bacon-Agostini Construction Joint Venture
200801530505	Leominster	Leominster Senior High School	Project Completion	Addition / Renovation	CM@R	Daedalus Projects Inc	Lamoureux Pagano & Associates, Inc.	Horizon Engineering Associates, LLP	S.O.M. Construction Ent., Inc.
201201530007	Leominster	Fall Brook	Project Completion	Repair - Accelerated		Compass Project Management, Inc.	Reinhardt Associates, Inc.	Horizon Engineering Associates, LLP	
201201530010	Leominster	Southeast School	Project Completion	Repair - Accelerated		Compass Project Management, Inc.	Reinhardt Associates, Inc.	Horizon Engineering Associates, LLP Russo Barr Associates, Inc.	
201101540005G	Leverett	Leverett Elementary School	Closeout	Repair - Accelerated	DBB	Potomac Capital Advisors	DiMarinisi & Wolfe Architects Urban Designers	Russo Barr Associates, Inc.	-
201101550010E	Lexington	Joseph Estabrook Elementary School	Construction	New Construction		RF Walsh Collaborative Partners	DiNisco Design Partnership, Limited	BVH Integrated Services, Inc.	Shawmut Design and Construction
200801590505	Longmeadow	Longmeadow High School	Project Completion	New Construction	CM@R	Joslin, Lesser + Associates Inc.	OMR Architects, Inc.	Foreman Building Commissioning, LP	Gilbane Building Company
201101600505G	Lowell	Lowell High School	Closeout	Repair - Accelerated	DBB	NETCO Construction Project Managers, Inc.	ICON architecture, inc.	Building Enclosure Associates	-
201101600027G	Lowell	Moody Elementary School	Closeout	Repair - Accelerated	DBB	NETCO Construction Project Managers, Inc.	ICON architecture, inc.	Building Enclosure Associates	Paul J. Rogan Co., Inc.
201101600055G	Lowell	Washington School	Closeout	Repair - Accelerated	DBB	NETCO Construction Project Managers, Inc.	ICON architecture, inc.	Building Enclosure Associates  RDK Engineers	Alpha Contracting Associates, Inc.
201101600040G	Lowell	Peter W Reilly School	Final Audit Approved	Repair - Accelerated	DBB	NETCO Construction Project Managers, Inc.	ICON architecture, inc.	Building Enclosure Associates	-
200801620505	Lunenburg	Lunenburg High School	Project Scope & Budget			Joslin, Lesser + Associates Inc.	Tappe Associates, Inc.		-
200901630305	Lynn	Thurgood Marshall Middle School	Design Development			Joslin, Lesser + Associates Inc.	Raymond Design Associates, Inc.		Walsh Brothers, Inc.
201201630405	Lynn	Breed Middle School	Project Completion	Repair - Accelerated		Diversified Project Management	Kaestle Boos Associates, Inc.	CBI Consulting Inc.	GVW Incorporated
201201630605	Lynn	Lynn Vocational Tech Institute	Project Completion	Repair - Accelerated		Diversified Project Management	Kaestle Boos Associates, Inc.	CBI Consulting Inc.	Gibson Roofs, Inc.
200901640505	Lynnfield	Lynnfield High School	Project Completion	Addition / Renovation	DBB	HEERY	Edward Rowse Architects, Inc.	Fitzemeyer & Tocci Associates, Inc.	E.A. Collangeli Construction Co., Inc.



MSBA ID	District	School	Phase	Project Scope	Procurement Type	OPM	Designer	Cx_Company	CMGC
200801680020	Marblehead	Glover Elementary School	Construction	New Construction	DBB	Municipal Building Consultants, Inc.	JCJ Architecture, PC	RDK Engineers	G & R Construction, Inc.
201101700505G	Marlborough	Marlborough High School	Closeout	Repair - Accelerated	DBB	RF Walsh Collaborative Partners	Baker/Wohl Architects, Inc.	RDK Engineers Building Enclosure Associates	A&A Window Products, Inc.  Feeley, McAnespie, Inc.  Veterans Development Corporation, Inc.
201101700008G	Marlborough	Francis J Kane Elementary School	Closeout	Repair - Accelerated	DBB	RF Walsh Collaborative Partners	Baker/Wohl Architects, Inc.	Building Enclosure Associates	A&A Window Products, Inc.
201101710505	Marshfield	Marshfield High School	Construction	New Construction	DBB	Compass Project Management, Inc.	Ai3 Architects LLC	Sebesta Blomberg & Associates, Inc.	Brait Builders Corp.
200801740505	Maynard	Maynard High School	Project Completion	New Construction	DBB	Municipal Building Consultants, Inc.	Tappe Associates, Inc.	WSP Flack + Kurtz	CTA Construction Co., Inc.
201201760505	Medford	Medford High School	Construction	Science Lab		Leftfield, LLC	DiNisco Design Partnership, Limited	Cannon Design	-
201301760505	Medford	Medford High School	OPM Selection	Repair - Accelerated					
200801770305	Medway	Medway Middle School	Closeout	Repair - Major	CM@R	Compass Project Management, Inc.	Knight, Bagge & Anderson, Inc.	Sebesta Blomberg & Associates, Inc.	Consigli Construction Company, Inc.
201201780505	Melrose	Melrose High School	Project Completion	Science Lab		CPI/Collaborative Partners	Ai3 Architects LLC	WSP Flack + Kurtz	-
201107100015G	Mendon-Upton	Miscoe Hill School	Closeout	Repair - Accelerated	DBB	Maguire Group Inc.	Habeeb & Associates Architects, Inc.	Sebesta Blomberg & Associates, Inc.	Greenwood Industries, Inc.
200801810505	Methuen	Methuen High School	Construction	Addition / Renovation	CM@R	KBA/Trident	Finegold Alexander and Associates Inc.	Environmental Health and Engineering	Dimeo Construction Company
201101820025G	Middleborough	Mary K. Goode Elementary School	Closeout	Repair - Accelerated	DBB	Maguire Group Inc.	Habeeb & Associates Architects, Inc.	Russo Barr Associates, Inc.	J.J. Cardosi, Inc.
200801840005	Middleton	Howe-Manning School	Final Audit Approved	New Construction	DBB	RF Walsh Collaborative Partners	DiNisco Design Partnership, Limited	Foreman Building Commissioning, LP	CTA Construction Co., Inc.
201101850090	Milford	Woodland Elementary School	Schematic Design			Joslin, Lesser + Associates Inc.	HMFH Architects, Inc.		Shawmut Design and Construction
200908300605	Minuteman Voc Tech	Minuteman Regional High School (Career Tech)	Feasibility Study			Skanska USA Building, Inc	Kaestle Boos Associates, Inc.		-
201107170005G	Mohawk Trail	Buckland-Shelburne Reg	Closeout	Repair - Accelerated	DBB	Potomac Capital Advisors	Bradley Architects, Inc.	Strategic Building Solutions, LLC	-
201107170010G	Mohawk Trail	Colrain Central School	Closeout	Repair - Accelerated	DBB	Potomac Capital Advisors	Bradley Architects, Inc.	Strategic Building Solutions, LLC	-
201107170505G	Mohawk Trail	Mohawk Trail Reg High School	Closeout	Repair - Accelerated	DBB	Potomac Capital Advisors	Bradley Architects, Inc.	Strategic Building Solutions, LLC	-
201122229999	Monomoy	Monomoy Regional High School	Construction	New Construction		Skanska USA Building, Inc	Mount Vernon Group Architects, Inc.	Sebesta Blomberg & Associates, Inc.	Fontaine Brothers, Inc.
201307150505	Mount Greylock Regional	Mount Greylock Regional High School	Eligibility Period						
201107200003G	Narragansett	Phillipston Memorial Elementary School	Closeout	Repair - Accelerated	DBB	Potomac Capital Advisors	DiMarinisi & Wolfe Architects Urban Designers	Rist-Frost-Shumway Engineering, P.C.	-
200807200020	Narragansett	Templeton Center School	Feasibility Study	Repair - Major		Strategic Building Solutions, LLC	Symmes Maini & McKee Associates, Inc.		-
200807250015	Nashoba	Pompsiticut Elementary School	Closeout	Addition / Renovation	DBB	Construction Monitoring Services, Inc.	Symmes Maini & McKee Associates, Inc.	Strategic Building Solutions, LLC	P.J. Stella Construction Corp.
200908520605G	Nashoba Valley Tech	Nashoba Valley Technical High School	Closeout	Repair - Accelerated	DBB	None	-	-	-
201308520605	Nashoba Valley Tech	Nashoba Valley Technical High School	OPM Selection	Repair - Accelerated					
200801980505	Natick	Natick High School	Closeout	New Construction	DBB	RF Walsh Collaborative Partners	Ai3 Architects LLC	Rist-Frost-Shumway Engineering, P.C.	-
201106600505G	Nauset	Nauset Regional High School	Closeout	Repair - Accelerated	DBB	NETCO Construction Project Managers, Inc.	Habeeb & Associates Architects, Inc.	CBI Consulting Inc.	Capeway Roofing Systems, Inc.  Modern Glass & Aluminum, Inc.
201306600305	Nauset	Nauset Regional Middle School	OPM Selection	Repair - Accelerated					
200901990050	Needham	Newman Elementary School	Closeout	Repair - Major	CM@R	Steven H. Popper - Town Employee	Drummeey Rosane Anderson, Inc.	Rist-Frost-Shumway Engineering, P.C.	Consigli Construction Company, Inc.  Triumph Leasing Corporation
201002010505	New Bedford	New Bedford High School	Closeout		DBB	-	-	-	-
200902010070	New Bedford	John Hannigan	OPM Selection			-	-	-	-
201102040005	Newburyport	Francis T Bresnahan Elementary School	Construction	New Construction		HEERY	HMFH Architects, Inc.	Fitzemeyer & Tocci Associates, Inc.	-



MSBA ID	District	School	Phase	Project Scope	Procurement Type	OPM	Designer	Cx_Company	CMGC
201002040305	Newburyport	Rupert A. Nock Middle School	Construction	Addition / Renovation	CM@R	HEERY	Miller Dyer Spears Inc.	Fitzemeyer & Tocci Associates, Inc.	-
201102070015G	Newton	Bowen	Closeout	Repair - Accelerated	DBB	STV Incorporated	Habeeb & Associates Architects, Inc.	-	-
201102070125G	Newton	Williams Elementary School	Closeout	Repair - Accelerated	DBB	STV Incorporated	Habeeb & Associates Architects, Inc.	-	-
201102070005	Newton	A E Angier Elementary School	Design Development			Joslin, Lesser + Associates Inc.	DiNisco Design Partnership, Limited	-	-
200802080005	Norfolk	Freeman-Kennedy Elementary School	Project Completion	New Construction	DBB	Joslin, Lesser + Associates Inc.	Flansburgh Associates, Inc.	WSP Flack + Kurtz	Fontaine Brothers, Inc.
200909150705	Norfolk County Agriculture	Norfolk County Agricultural High School	Construction	Addition / Renovation	DBB	Compass Project Management, Inc.	Turowski2 Architecture, Inc.	Rist-Frost-Shumway Engineering, P.C.	TLT Construction Corporation
200802090305	North Adams	Silvio O Conte Middle School	Design Development	Addition / Renovation		Strategic Building Solutions, LLC	Margo Jones Architects, Inc.	Rist-Frost-Shumway Engineering, P.C.	-
201102110018G	North Andover	Annie L Sargent School	Closeout	Repair - Accelerated	DBB	Municipal Building Consultants, Inc.	ICON architecture, inc.	Cannon Design	Variaka Construction, Inc.
201102110001G	North Andover	Atkinson School	Closeout	Repair - Accelerated	DBB	Municipal Building Consultants, Inc.	ICON architecture, inc.	Cannon Design	Paul J. Rogan Co., Inc.
201102110305G	North Andover	North Andover Middle School	Closeout	Repair - Accelerated	DBB	Municipal Building Consultants, Inc.	ICON architecture, inc.	Cannon Design	Stanley Roofing Company, Inc.
201202120015	North Attleborough	Roosevelt Avenue Elementary School	Construction	Repair - Accelerated		Skanska USA Building, Inc	Russo Barr Associates, Inc.	Gale Associates, Inc.	
201202120505	North Attleborough	North Attleboro High School	Project Completion	Science Lab		Skanska USA Building, Inc	Kaestle Boos Associates, Inc.	Consulting Engineering Services, LLC	-
201202150015	North Brookfield	North Brookfield Elementary School	Closeout	Repair - Accelerated		Strategic Building Solutions, LLC	CBI Consulting, Inc.	Simpson Gumpertz & Heger Inc.	
201102150015G	North Brookfield	North Brookfield Elementary School	Final Audit Approved	Repair - Accelerated	DBB	Vertex Construction Services	LPBA/ Architects, Inc.	Simpson Gumpertz & Heger Inc.	Lockheed Window Corporations
201107350010G	North Middlesex	Ashby Elementary School	Final Audit Approved	Repair - Accelerated	DBB	Compass Project Management, Inc.	Russo Barr Associates, Inc.	Building Enclosure Associates	Greenwood Industries, Inc.   GVV, Inc.
201107350005G	North Middlesex	Spaulding Memorial School	Final Audit Approved	Repair - Accelerated	DBB	Compass Project Management, Inc.	Russo Barr Associates, Inc.	Building Enclosure Associates	MDM Engineering
201107350505	North Middlesex	North Middlesex Regional High School	Schematic Design			HEERY	Symmes Maini & McKee Associates, Inc.	-	-
201002170505	North Reading	North Reading High School	Construction	Addition / Renovation	CM@R	PMA Construction Services	Dore & Whittier Architects, Inc.	Cannon Design	-
201102130003	Northborough	Lincoln Street Elementary School	Feasibility Study			Strategic Building Solutions, LLC	Lamoureux Pagano & Associates, Inc.	-	-
201202180015	Norton	J C Solmonese	Closeout	Repair - Accelerated		Joslin, Lesser + Associates Inc.	Habeeb & Associates Architects, Inc.	Simpson Gumpertz & Heger Inc.	Silktown Roofing
200902180505	Norton	Norton High School	Construction	Addition / Renovation	CM@R	Pinck & Co., Inc.	JCJ Architecture, PC	Rist-Frost-Shumway Engineering, P.C.	W. T. Rich Company Inc.
200908550605	Old Colony Reg Voc Tech	Vocational Technical High School	Closeout	Repair - Major		Vertex Construction Services	-	Consulting Engineering Services, LLC	J.D. Rivet & Company, Inc.
200802260405	Oxford	Oxford Middle School	Construction	Repair - Major		Diversified Project Management	CGKV Architects, Inc.	Cannon Design	S.O.M. Construction Ent., Inc.
201102270305G	Palmer	Converse Middle School	Closeout	Repair - Accelerated	DBB	Diversified Project Management	Tighe & Bond, Inc.	Strategic Building Solutions, LLC	Royal Steam Heater Co.   Titan Roofing, Inc.
201102270008G	Palmer	Old Mill Pond Elementary School	Closeout	Repair - Accelerated	DBB	Diversified Project Management	Tighe & Bond, Inc.	Strategic Building Solutions, LLC	Royal Steam Heater Co.
201102270505G	Palmer	Palmer High School	Closeout	Repair - Accelerated	DBB	Diversified Project Management	Tighe & Bond, Inc.	Strategic Building Solutions, LLC	Royal Steam Heater Co.   Titan Roofing, Inc.
201308600605	Pathfinder	Regional Vocational Technical High School	Schematic Design	Repair - Accelerated		exPERTcon, Inc.	Baker/Wohl Architects, Inc.		
201102290027G	Peabody	William A Welch Sr Elementary School	Closeout	Repair - Accelerated	DBB	Daedalus Projects Inc	LPBA/ Architects, Inc.	Sebesta Blomberg & Associates, Inc.	-
201102290007G	Peabody	John E Burke School	Closeout	Repair - Accelerated	DBB	Daedalus Projects Inc	LPBA/ Architects, Inc.	Sebesta Blomberg & Associates, Inc.	-
200802290305	Peabody	J Henry Higgins Middle School	Design Development	New Construction		Daedalus Projects Inc	DiNisco Design Partnership, Limited	BVH Integrated Services, Inc.	-
201302310010	Pembroke	Hobomock Elementary School	Schematic Design	Repair - Accelerated					
201302310015	Pembroke	North Pembroke Elementary School	Schematic Design	Repair - Accelerated					



MSBA ID	District	School	Phase	Project Scope	Procurement Type	OPM	Designer	Cx_Company	CMGC
201302310305	Pembroke	Pembroke Community Middle School	Schematic Design	Repair - Accelerated					
201302310505	Pembroke	Pembroke High School	Schematic Design	Repair - Accelerated					
201107450020G	Pentucket	Dr Frederick N Sweetsir School	Closeout	Repair - Accelerated	DBB	PMA Construction Services	Knight, Bagge & Anderson, Inc.	CBI Consulting Inc./RDK Engineers	E. Amanti & Sons, Inc.
201107450015G	Pentucket	Dr John C Page School	Closeout	Repair - Accelerated	DBB	PMA Construction Services	Knight, Bagge & Anderson, Inc.	CBI Consulting Inc./RDK Engineers	Capeway Roofing Systems, Inc.
201107450005G	Pentucket	Elmer S Bagnall	Closeout	Repair - Accelerated	DBB	PMA Construction Services	Knight, Bagge & Anderson, Inc.	CBI Consulting Inc./RDK Engineers	Gibson Roofs, Inc.
201307450405	Pentucket	Pentucket Regional Middle School	OPM Selection	Repair - Accelerated					
201107500008G	Pioneer Valley	Northfield Elementary Elementary School	Closeout	Repair - Accelerated	DBB	Diversified Project Management	CGKV Architects, Inc.	Strategic Building Solutions, LLC	-
201107500505G	Pioneer Valley	Pioneer Valley Reg Middle School/High School	Closeout	Repair - Accelerated	DBB	Diversified Project Management	CGKV Architects, Inc.	Strategic Building Solutions, LLC	-
201002360510	Pittsfield	Taconic High School	Feasibility Study				Skanska USA Building, Inc	-	-
201202390515	Plymouth	Plymouth South High School	Feasibility Study				Ted Gentry Associates, Inc	Ai3 Architects LLC	
200802390505	Plymouth	Plymouth North High School	Project Completion	New Construction - Model School	DBB	Ted Gentry Associates, Inc	Ai3 Architects LLC	Sebesta Blomberg & Associates, Inc.	J & J Contractors, Inc.
201207530030	Quabbin	Ruggles Lane Elementary School	Closeout	Repair - Accelerated	DBB	Vertex Construction Services	Turowski2 Architecture, Inc.	Simpson Gumpertz & Heger Inc.	PDS Engineering & Construction Inc.
201207780005	Quaboag	Warren Community Elementary School	Project Completion	Repair - Accelerated			Coast & Harbor Associates, Inc.	Lindgren & Sharples, Inc.	Strategic Building Solutions, LLC
200802430315	Quincy	Central Middle School	Project Completion	New Construction	DBB	Tishman Construction Corporation of MA	Ai3 Architects LLC	Sebesta Blomberg & Associates, Inc.	H.V. Collins Co., Inc.
201302430060	Quincy	Merrymount Elementary School	Schematic Design	Repair - Accelerated					
201302430510	Quincy	North Quincy High School	Schematic Design	Repair - Accelerated					
201302430110	Quincy	Wollaston Elementary School	Schematic Design	Repair - Accelerated					
201302440410	Randolph	Randolph Community Middle School	Schematic Design	Repair - Accelerated			NETCO Construction Project Managers, Inc.	Taylor & Burns, Inc.	
201302440505	Randolph	Randolph High School	Schematic Design	Repair - Accelerated			NETCO Construction Project Managers, Inc.		
201002480035	Revere	William McKinley Elementary School	Design Development	New Construction			RF Walsh Collaborative Partners	Drumey Rosane Anderson, Inc.	Rist-Frost-Shumway Engineering, P.C.
201102510025G	Rockland	R Stewart Esten Elementary School	Closeout	Repair - Accelerated	DBB	Daedalus Projects Inc	Habeeb & Associates Architects, Inc.	Russo Barr Associates, Inc.	Northeast Energy Control Systems
200802510305	Rockland	John W. Rogers Middle School	Project Completion	New Construction	CM@R	Daedalus Projects Inc	Dore & Whittier Architects, Inc.	Consulting Engineering Services, LLC	Agostini Construction Co., Inc.
200902580305G	Salem	Collins Middle School	Construction	Repair - Accelerated	CM@R	KV Associates, Inc.	Reinhardt Associates, Inc.	Rist-Frost-Shumway Engineering, P.C.	Gilbane Building Company
201002580050G	Salem	Saltonstall School	Project Completion	Repair - Accelerated	CM@R	KV Associates, Inc.	Reinhardt Associates, Inc.	Rist-Frost-Shumway Engineering, P.C.	Gilbane Building Company
201102610010G	Sandwich	Forestdale School	Closeout	Repair - Accelerated	DBB	NETCO Construction Project Managers, Inc.	Habeeb & Associates Architects, Inc.	Gale Associates, Inc.	Varieta Construction, Inc.
200902610025G	Sandwich	Oak Ridge School	Closeout	Repair - Accelerated	DBB	NETCO Construction Project Managers, Inc.	Habeeb & Associates Architects, Inc.	Gale Associates, Inc.	J.J. Cardosi, Inc.
201002620305	Saugus	Belmonte Middle School	Closeout	Repair - Major	CM@R	Skanska USA Building, Inc	Fletcher Thompson Architecture Engineering, LLC	Consulting Engineering Services, LLC	Consigli Construction Company, Inc.
201202640305	Scituate	Gates Intermediate School	Designer Selection				Daedalus Projects Inc		
200802660305	Sharon	Sharon Middle School	Closeout	Addition / Renovation	CM@R	Daedalus Projects Inc	Kaestle Boos Associates, Inc.	Horizon Engineering Associates, LLP	Consigli Construction Company, Inc.
201208710605	Shawsheen Valley Voc Tech	Shawsheen Valley Voc Tech High School	Closeout	Repair - Accelerated			Diversified Project Management	Shekar & Associates, Inc.	Fitzemeyer & Tocci Associates, Inc.
201102710035G	Shrewsbury	Spring Street Elementary School	Closeout	Repair - Accelerated	DBB	PMA Construction Services	Habeeb & Associates Architects, Inc.	Cannon Design	Lambrian Construction Corp.
200802710305	Shrewsbury	Sherwood Middle School	Project Completion	New Construction	CM@R	PMA Construction Services	Lamoureux Pagano & Associates, Inc.	RDK Engineers	Gilbane Building Company
20081119999	Somerset-Berkley	Somerset-Berkley High School	Construction	New Construction			Skanska USA Building, Inc	Ai3 Architects LLC	Horizon Engineering Associates, LLP



MSBA ID	District	School	Phase	Project Scope	Procurement Type	OPM	Designer	Cx_Company	CMGC
200902740111E	Somerville	East Somerville Community School at Cummings	Closeout	Addition / Renovation	CM@R	PMA Construction Services	Maguire Group, Inc.	Foreman Building Commissioning, LP	Gilbane Building Company
200902780015	South Hadley	Plains Elementary School	Design Development	New Construction		Arcadis	Margo Jones Architects, Inc.	Strategic Building Solutions, LLC	-
201308290605	South Middlesex Regional Voc Tech School District	Joseph P. Keefe Regional Technical High School	Schematic Design	Repair - Accelerated					
201202750005	Southampton	William E. Norris Elementary School	Construction	Repair - Accelerated		Tishman Construction Corporation of MA	Reinhardt Associates, Inc.	Building Enclosure Associates	
200802770505	Southbridge	Southbridge High School	Closeout	New Construction	CM@R	Joslin, Lesser + Associates Inc.	Tappe Associates, Inc.	Environmental Health and Engineering	Consigli Construction Company, Inc.
200908720605	Southeastern Reg Voc Tech	Southeastern Regional Vocational Technical School	Project Completion	Addition / Renovation	CM@R	RF Walsh Collaborative Partners	Drumme Rosane Anderson, Inc.	RDK Engineers	W. T. Rich Company Inc.
200908760605	Southern Worcester Cty VT	Vocational Technical High School	Construction	Addition / Renovation	DBB	HEERY	Kaestle Boos Associates, Inc.	RDK Engineers	Consigli Construction Company, Inc.
201107660505	Southwick-Tolland-Granville	Regional High School	Construction	Addition / Renovation		Strategic Building Solutions, LLC	JCJ Architecture, PC		BVH Integrated Services, Inc.
201102810125E	Springfield	Dryden Veterans Memorial Elementary School	Construction	Addition / Renovation	CM@R	Arcadis	Drumme Rosane Anderson, Inc.	BVH Integrated Services, Inc.	-
201202810500	Springfield	Central High School	Construction	Science Lab	CM@R	Leftfield, LLC	DiNisco Design Partnership, Limited	Horizon Engineering Associates, LLP	Morganti/Aquadro & Cerruti
201102810030E	Springfield	Elias Brookings Elementary School	Construction	New Construction	CM@R	Arcadis	Drumme Rosane Anderson, Inc.	BVH Integrated Services, Inc.	-
201302810310	Springfield	Chestnut Accelerated Middle School	OPM Selection				-	-	-
	Springfield	SCIPP Year 3	Project Completion						
W20014137	Springfield	Forest Park Middle School	Project Completion	Addition / Renovation	CM@R	Arcadis	Perkins Eastman	Foreman Building Commissioning, LP	Consigli Construction Company, Inc.
	Springfield	SCIPP Year 2	Project Completion						
W20054428	Springfield	Roger L. Putnam Vocational Technical High School	Project Completion	New Construction	CM@R	Pinnacle One, Inc.	Drumme Rosane Anderson Inc.	Strategic Building Solutions, LLC	Consigli/Morganti
201302810060	Springfield	Margaret C. Ellis School	Schematic Design	Repair - Accelerated		Atlantic Construction and Management, Inc.			
201302810550	Springfield	Springfield Public Day High School	Schematic Design	Repair - Accelerated		Atlantic Construction and Management, Inc.			
201302810530	Springfield	Springfield High School/Science-Tech	Schematic Design	Repair - Accelerated		Atlantic Construction and Management, Inc.			
201302810355	Springfield	South End Middle School	Schematic Design	Repair - Accelerated		Atlantic Construction and Management, Inc.			
200902840405	Stoneham	Stoneham Middle School	Construction	Addition / Renovation	CM@R	Joslin, Lesser + Associates Inc.	Tappe Associates, Inc.	RDK Engineers	Shawmut Design and Construction
201302850010	Stoughton	Helen Hansen Elementary School	Designer Selection	Repair- Accelerated					
201302850020	Stoughton	West Elementary School	Designer Selection	Repair - Accelerated					
201302850014	Stoughton	Joseph R. Dawe Jr. Elementary School	Schematic Design	Repair - Accelerated					
200802870005	Sturbridge	Burgess Elementary School	Project Completion	Addition / Renovation	DBB	Lamoureux Pagano & Associates, Inc.	Drumme Rosane Anderson, Inc.	Horizon Engineering Associates, LLP	Fontaine Brothers, Inc.
201202880025	Sudbury	General John Nixon Elementary School	Closeout	Repair - Accelerated		PMA Construction Services	ICON architecture, inc.	Gale Associates, Inc.	
200802900305	Sutton	Sutton Middle School	Construction	Addition / Renovation	DBB	Strategic Building Solutions, LLC	Flansburgh Associates, Inc.	RDK Engineers	TLT Construction Corporation
201102910010	Swampscott	Hadley Elementary School	Feasibility Study			Collaborative Partners	Mount Vernon Group Architects, Inc.		-
201202930057	Taunton	Harold H Galligan School	Closeout	Repair - Accelerated		Arcadis	Knight, Bagge & Anderson, Inc.	Gale Associates, Inc.	
200802950505	Tewksbury	Tewksbury Memorial High School	Project Completion	New Construction - Model School	DBB	HEERY	Symmes Maini & McKee Associates, Inc.	Sebesta Blomberg & Associates, Inc.	CTA Ventures
201208780605	Tri County	Tri County Reg Voc Tech High School	Project Completion	Science Lab		Collaborative Partners	Ai3 Architects LLC		-
201108790605G	Upper Cape Cod Voc Tech	Upper Cape Cod Voc Tech School	Final Audit Approved	Repair - Accelerated	DBB	NETCO Construction Project Managers, Inc.	Knight, Bagge & Anderson, Inc.	Gale Associates, Inc.	Modern Glass & Aluminum, Inc.



MSBA ID	District	School	Phase	Project Scope	Procurement Type	OPM	Designer	Cx_Company	CMGC
200803040505	Uxbridge	Uxbridge High School	Project Completion	New Construction	CM@R	Joslin, Lesser + Associates Inc.	Raymond Design Associates, Inc.	Turner Facilities Management Solutions	Shawmut Design and Construction
201107750035G	Wachusett	Naquag Elementary School	Closeout	Repair - Accelerated	DBB	Strategic Building Solutions, LLC	LPBA/ Architects, Inc.	Rist-Frost-Shumway Engineering, P.C.	MDM Engineering
201107750040G	Wachusett	Paxton Center School	Closeout	Repair - Accelerated	DBB	Strategic Building Solutions, LLC	LPBA/ Architects, Inc.	Rist-Frost-Shumway Engineering, P.C.	MDM Engineering
201107750045G	Wachusett	Thomas Prince School	Closeout	Repair - Accelerated	DBB	Strategic Building Solutions, LLC	LPBA/ Architects, Inc.	Rist-Frost-Shumway Engineering, P.C.	MDM Engineering
200907750305	Wachusett	Mountview Middle School	Design Development			<b>Gary Kaczmarek - Town Employee</b>	Lamoureux Pagano & Associates, Inc.		-
201003050310	Wakefield	Galvin Middle School	Construction	New Construction	CM@R	Joslin, Lesser + Associates Inc.	Tappe Associates, Inc.	B2Q Associates, Inc.	Bond Brothers, Inc.
201303070015	Walpole	Fisher Elementary School	OPM Selection						
201303100505	Wareham	Wareham Senior High School	OPM Selection						
200803150505	Wayland	Wayland High School	Final Audit Approved	New Construction	CM@R	KV Associates, Inc.	HMFH Architects, Inc.	WSP Flack + Kurtz	Shawmut Design and Construction
201203150305	Wayland	Wayland Middle School	Project Completion	Repair - Accelerated		Joslin, Lesser + Associates Inc.	DiMarinisi & Wolfe Architects Urban Designers	CBI Consulting Inc.	Capeway Roofing Systems, Inc.
200903160015	Webster	Park Avenue Elementary School	Construction	New Construction	DBB	RF Walsh Collaborative Partners	Dore & Whittier Architects, Inc.	Cannon Design	-
200803170505	Wellesley	Wellesley Senior High School	Closeout	New Construction	CM@R	<b>Ryegate, Inc.</b>	Symmes Maini & McKee Associates, Inc.	Rist-Frost-Shumway Engineering, P.C.	<b>Turner Construction Company</b>
201303180005	Wellfleet	Wellfleet Elementary School	OPM Selection	Repair - Accelerated					
201103220005G	West Boylston	Major Edwards Elementary	Closeout	Repair - Accelerated	DBB	URS Corporation	Reinhardt Associates, Inc.	Cannon Design	-
201003230505	West Bridgewater	West Bridgewater Middle-Senior High School	Construction	New Construction		Strategic Building Solutions, LLC	Flansburgh Associates, Inc.	Cannon Design	-
200903320505	West Springfield	West Springfield High School	Construction	New Construction	DBB	Strategic Building Solutions, LLC	Symmes Maini & McKee Associates, Inc.	Turner Facilities Management Solutions	Fontaine Brothers, Inc.
200903210305	Westborough	Gibbons Middle School	Feasibility Study			HEERY	Habeeb & Associates Architects, Inc.		-
201103250025G	Westfield	Highland Elementary School	Closeout	Repair - Accelerated	DBB	P3 Project Planning	Tighe & Bond, Inc.		
201103250036G	Westfield	Paper Mill Elementary School	Closeout	Repair - Accelerated	DBB	<b>P3 Project Planning</b>	<b>Tighe &amp; Bond, Inc.</b>	Strategic Building Solutions, LLC	R & H Roofing, LLP
201103250040G	Westfield	Southampton Road Elementary School	Closeout	Repair - Accelerated	DBB	P3 Inc.	Tighe & Bond, Inc.		
201103250505G	Westfield	Westfield High School	Closeout	Repair - Accelerated	DBB	<b>P3 Project Planning</b>	Tighe & Bond, Inc.	Strategic Building Solutions, LLC	-
201103250605G	Westfield	Westfield Voc Tech High School	Closeout	Repair - Accelerated	DBB	<b>P3 Project Planning</b>	<b>Tighe &amp; Bond, Inc.</b>	Strategic Building Solutions, LLC	-
200903250020	Westfield	Abner Gibbs Elementary School	Construction	New Construction - Model School	DBB	Skanska USA Building, Inc	Margo Jones Architects, Inc.	Horizon Engineering Associates, LLP	Fontaine Brothers, Inc.
201103250033E	Westfield	Munger Hill Elementary School	Project Completion	Repair - Accelerated		Vertex Construction Services	Knight, Bagge & Anderson, Inc.	Building Enclosure Associates	Allied Restoration Corporation
201203250036	Westfield	Paper Mill Elementary School	Project Completion	Repair - Accelerated		Vertex Construction Services	Knight, Bagge & Anderson, Inc.	Building Enclosure Associates	
201303260025	Westford	Colonel John Robinson School	OPM Selection	Repair - Accelerated					
201303260007	Westford	Norman E. Day Elementary School	OPM Selection	Repair - Accelerated					
201303270005	Westhampton	Westhampton Elementary School	Schematic Design	Repair - Accelerated					
200903300012	Weston	Field Elementary School	Construction	New Construction	DBB	Compass Project Management, Inc.	Jonathan Levi Architects LLC	Foreman Building Commissioning, LP	Colantonio, Inc.
201103300505G	Weston	Weston High School	Final Audit Approved	Repair - Accelerated	DBB	Compass Project Management, Inc.	Garcia Galuska DeSousa Consulting Engineers Inc.	RDK Engineers	-
201103310015G	Westport	Alice A Macomber Primary	Final Audit Approved	Repair - Accelerated	DBB	Pinck & Co., Inc.	CGKV Architects, Inc.	CBI Consulting Inc.	-
201103310505G	Westport	Westport High School	Final Audit Approved	Repair - Accelerated	DBB	Pinck & Co., Inc.	CGKV Architects, Inc.	CBI Consulting Inc.	-
201203360080	Weymouth	William Seach Primary	Project Completion	Repair - Accelerated		PMA Construction Services	BLW Engineers, Inc.	B2Q Associates, Inc.	Multitemp Mechanical Corporation





MSBA ID	District	School	Phase	Project Scope	Procurement Type	OPM	Designer	Cx_Company	CMGC
200907800025	Whitman-Hanson	Maquan Elementary School	Approved Project Vote Pending			Knight, Bagge & Anderson Inc.	Turowski2 Architecture, Inc.		-
200803400005	Williamsburg	Anne T. Dunphy School	Construction	Addition / Renovation	DBB	Arcadis	Drumme Rosane Anderson, Inc.	B2Q Associates, Inc.	Enfield Builders, Inc.
200903420505	Wilmington	Wilmington High School	Construction	New Construction	CM@R	Joslin, Lesser + Associates Inc.	Dore & Whittier Architects, Inc.	Symmes, Maini & McKee Associates	Gilbane Building Company
201203420060	Wilmington	North Intermediate	<b>Design Development</b>	Repair - Accelerated				CBI Consulting Inc.	
201003440505	Winchester	Winchester High School	Approved Project Vote Pending			Skanska USA Building, Inc	Symmes Maini & McKee Associates, Inc.		-
200803440025	Winchester	Vinson-Owen Elementary School	<b>Project Completion</b>	New Construction	DBB	Skanska USA Building, Inc	Tappe Associates, Inc.	Turner Facilities Management Solutions	CTA Construction Co., Inc.
200803460505	Winthrop	Winthrop Sr High School	Approved Project Vote Pending			Skanska USA Building, Inc Municipal Building Consultants, Inc.	HMFH Architects, Inc.		-
200803470015	Woburn	Goodyear Elementary School	Final Audit Approved	New Construction	CM@R		Tappe Associates, Inc.	Strategic Building Solutions, LLC	<b>Gilbane Building Company</b>
201203470060	Woburn	Wyman Elementary School	<b>OPM Selection</b>						
201203480052	Worcester	Chandler Magnet School	Construction	Repair - Accelerated		Tishman Construction Corporation of MA	Turowski2 Architecture, Inc.	Russo Barr Associates, Inc.	
201203488099	Worcester	Dr. James Caradonio Center	Construction	Repair - Accelerated		Tishman Construction Corporation of MA	Turowski2 Architecture, Inc.	Russo Barr Associates, Inc.   RDK Engineers	
201203480145	Worcester	Lake View School	Construction	Repair - Accelerated		Tishman Construction Corporation of MA	Turowski2 Architecture, Inc.	Russo Barr Associates, Inc.	
201203480175	Worcester	May Street School	Construction	Repair - Accelerated		Tishman Construction Corporation of MA	Turowski2 Architecture, Inc.	Russo Barr Associates, Inc.	
201203480200	Worcester	Nelson Place	Designer Selection			Tishman Construction Corporation of MA	-		-
201203480140	Worcester	Jacob Hiatt Magnet School	Project Completion	Repair - Accelerated		Tishman Construction Corporation of MA	Turowski2 Architecture, Inc.	RDK Engineers	
W20004048	Worcester	North High School	<b>Project Completion</b>	New Construction	CM@R	-	<b>Maguire Group, Inc.</b>	<b>Architectural Services</b>	<b>Gilbane Building Company</b>
201303480060	Worcester	Columbus Park Preparatory Academy	<b>Schematic Design</b>	Repair - Accelerated		Architectural Consulting Group, LLC	The S/L/A/M Collaborative		
201303480230	Worcester	Tatnuck Magnet School	<b>Schematic Design</b>	Repair - Accelerated		Architectural Consulting Group, LLC	The S/L/A/M Collaborative		
201303480225	Worcester	Worcester Arts Magnet School	<b>Schematic Design</b>	Repair - Accelerated		Architectural Consulting Group, LLC	The S/L/A/M Collaborative		
201303480420	Worcester	Worcester East Middle School	<b>Schematic Design</b>	Repair - Accelerated		Architectural Consulting Group, LLC	The S/L/A/M Collaborative		

### 2013 Estimated Bid Dates

Note bid dates are **Estimates ONLY**. Please contact Districts for exact information.

Total Project Budget denotes total District costs and does not denote the basis of the MSBA Total Facilities Grant.

■ - Denotes bid phase in progress or complete    
 ■ - Denotes estimated bid dates    
 ■ - Denotes estimated GMP dates

DISTRICT <small>*Projects Considering the CM @ Risk Method</small>	DESIGN BASIS FOR ENROLLMENT	PROJECT BUDGET <small>Shown in Millions</small>	CONSTRUCTION BUDGET <small>Shown in Millions</small>	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC
*LEXINGTON	540	\$40.8	\$31.1	Lexington: Estabrook ES (New Construction): Filed-Sub Bids rcv'd 12/19. GMP Issued January.											
NEWBURYPORT	660	\$37.3	\$31.1	Newburyport: Bresnahan ES (New Construction): Filed-Sub Bids rcv'd 1/16. G.C Bids rcv'd 2/1. NTP Issued March.											
MONOMOY RSD	700	\$64.7	\$52.9	Monomoy Regional HS (New Construction): Filed-Sub Bids rcv'd 1/9. G.C Bids rcv'd 1/30. NTP Issued February.											
MELROSE	1,026	\$6.5	\$4.9	Melrose HS (SLI): Filed-Sub Bids rcv'd 1/23. G.C Bids rcv'd 2/6. NTP Issued February.											
*STONEHAM	775	\$38.6	\$32.0	Stoneham MS (Addition/Renovation): Filed-Sub Bids rcv'd 1/17. GMP Issued March.											
*WILMINGTON	960	\$82.7	\$64.4	Wilmington HS (New Construction): Filed-Sub Bids rcv'd 1/18. GMP Issued June.											
NORTH ATTLEBOROUGH	1,209	\$6.2	\$4.7	North Attleborough HS (SLI): Filed-Sub Bids rcv'd 3/29. G.C. Bids rcv'd 4/5. NTP Issued April.											
GARDNER	636	\$3.8	\$2.9	Gardner HS (SLI): Filed-Sub Bids rcv'd 2/21. G.C. Bids rcv'd 2/28. NTP Issued March.											
ASSABET VALLEY RSD	1,000	\$62.4	\$50.8	Assabet Valley Regional HS (Repair): Filed-sub Bids rcv'd 3/1. G.C. Bids rcv'd 3/25. NTP Issued April.											
BLACKSTONE VALLEY RSD	573	\$1.0	\$0.7	Blackstone Valley Regional VTHS (SLI): Filed-Sub rcv'd 2/20. G.C. Bids rcv'd 3/6. NTP Issued March.											
HOLYOKE	404	\$6.9	\$5.4	Holyoke William J. Dean VTHS (SLI): Filed-Sub Bids rcv'd 3/1. G.C. Bids rcv'd 3/15. NTP Issued April.											
WILLIAMSBURG	170	\$12.0	\$9.6	Williamsburg Anne T. Dunphy IS (Addition/Renovation): Filed-Sub Bids rcv'd 2/12. G.C. Bids rcv'd 3/1. NTP Issued April.											
TRI COUNTY RSD	503	\$1.8	\$1.2	Tri-County Regional VTHS (SLI): Filed-Sub Bids rcv'd 3/5. G.C. Bids rcv'd 3/20. NTP Issued April.											
*NEWBURYPORT	845	\$26.9	\$21.8	Newburyport: Nock ES (Renovation): Filed-Sub Bids rcv'd 3/8. GMP Issued April.											
OLD COLONY RSD	570	\$2.7	\$2.2	Old Colony RVTHS (Repair/SLI): Filed-Sub Bids rcv'd 4/5. G.C. Bids rcv'd 4/12. NTP Issued June.											
*GREENFIELD	585	\$63.4	\$52.9	Greenfield HS (New Construction): Filed-Sub Bids rcv'd 4/24. GMP Issued August.											
*NORTH READING	1,370	\$103.4	\$86.3	North Reading HS (New Construction): Filed-Sub Bids rcv'd 4/4. GMP Issued June.											
*ANDOVER	680	\$44.7	\$34.5	Andover: Bancroft ES (New Construction): Filed-Sub Bids rcv'd 9/22. Non Filed-Sub Bids rcv'd 11/2. GMP issued July.											
MEDFORD	349	\$13.8	\$10.9	Medford HS (SLI): Filed-Sub Bids rcv'd 8/7. G.C. Bids rcv'd 8/21. NTP Targeted September.											
*WAKEFIELD	1,070	\$70.1	\$59.7	Wakefield: Galvin MS (New Construction): Filed-Sub Bids rcv'd 5/14. GMP Issued June.											

### 2013 Estimated Bid Dates

Note bid dates are **Estimates ONLY**. Please contact Districts for exact information.

Total Project Budget denotes total District costs and does not denote the basis of the MSBA Total Facilities Grant.

■ - Denotes bid phase in progress or complete    
 ■ - Denotes estimated bid dates    
 ■ - Denotes estimated GMP dates

DISTRICT <small>*Projects Considering the CM @ Risk Method</small>	DESIGN BASIS FOR ENROLLMENT	PROJECT BUDGET <small>Shown in Millions</small>	CONSTRUCTION BUDGET <small>Shown in Millions</small>	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC	
WEBSTER	720	\$44.9	\$35.8													Webster Park Ave ES (New Construction): Filed-Sub Bids rcv'd 5/30. G.C. Bids rcv'd 6/13. NTP Issued June.
*CONCORD-CARLISLE RSD	1,225	\$92.6	\$71.4													Concord-Carlisle HS (New Construction): Filed-Sub Bids rcv'd 5/24. GMP Issued August.
SOUTHWICK-TOLLAND-GRANVILLE PowderMill IS	545	\$18.5	\$14.8													Southwick-Tolland-Granville: PowderMill IS (Repair): Filed-Sub Bids rcv'd 5/1. G.C. rcv'd 5/30. NTP Issued June.
SOUTHWICK-TOLLAND-GRANVILLE Woodland ES	400	\$9.7	\$7.3													Southwick-Tolland-Granville: Woodland ES (Repair): Filed-Sub Bids rcv'd 5/1. G.C. rcv'd 5/30.
SOUTHWICK-TOLLAND-GRANVILLE STG Regional HS	790	\$40.7	\$31.4													Southwick-Tolland-Granville MS/HS (Addition/Renovation): Filed-Sub Bids rcv'd 7/10. G.C. rcv'd 7/25. NTP Issued August.
GREATER NEW BEDFORD	2,060	\$17.1	\$13.7													Greater New Bedford RVTHS (Addition/Renovation): Filed-Sub Bids rcv'd 8/27. G.C. Due 9/10. NTP Issued September.
SPRINGFIELD	408	\$32.1	\$25.7													Springfield: Central HS (SLI): Filed-Sub Bids rcv'd 8/16. GMP Issued September.
*SPRINGFIELD	320	\$27.9	\$22.7													Springfield: Brookings ES (New Construction): Filed-Sub Bids rcv'd 8/28. GMP Targeted November.
*SOUTHERN WORCESTER COUNTY	1,110	\$73.7	\$58.2													Bay Path RVTHS (Addition/Renovation): Filed-Sub Bids rcv'd 9/24. GMP Targeted November.
WEST BRIDGEWATER	625	\$63.7	\$49.7													West Bridgewater MS/HS (New Construction): Filed-Sub Bids Due 9/10. G.C. Due 9/24. NTP Issued September.
GEORGETOWN	770	\$46.2	\$37.0													Penn Brook ES (New Construction): Filed-Sub Bids Due 9/12. G.C. Bids rcv'd 9/19. NTP Issued September.
*AYER SHIRLEY RSD	495	\$56.5	\$44.4													Ayer Shirley RHS (Addition/Renovation): Filed-Sub Bids Due 9/25. GMP Targeted December.
<b>Subtotal</b>	<b>24,093</b>	<b>\$1,213</b>	<b>\$972.0</b>													
<b>GRAND TOTAL</b>	<b>24,093</b>	<b>\$1,213</b>	<b>\$972.0</b>													
<b>Number of Construction-Related Employment Opportunities Created</b>			<b>4,860</b>													

### 2014 Estimated Bid Dates

Note bid dates are **Estimates ONLY**. Please contact Districts for exact information.

Total Project Budget denotes total District costs and does not denote the basis of the MSBA Total Facilities Grant.

■ - Denotes bid phase in progress or complete    
 ■ - Denotes estimated bid dates    
 ■ - Denotes estimated GMP dates

DISTRICT <small>*Projects Considering the CM @ Risk Method</small>	DESIGN BASIS FOR ENROLLMENT	PROJECT BUDGET <small>Shown in Millions</small>	CONSTRUCTION BUDGET <small>Shown in Millions</small>	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC
<b>REVERE</b>	690	\$44.4	\$33.9	Revere: Hill (McKinley) ES (New Construction): Filed-Sub Bids Due 1/9. G.C. Bids Due 1/23. NTP Targeted February.											
<b>NORTH ADAMS</b>	310	\$29.7	\$21.9	North Adams: Conte MS (New Construction): Filed-Sub Bids Due 1/23. G.C. Bids Due 2/6. NTP Targeted March.											
<b>*GREATER LOWELL RSD</b>	1990	\$65.3	\$53.2	Greater Lowell RVTHS (Repair): Filed-Sub Bids Due 2/19. GMP Targeted March.											
<b>*AUBURN</b>	560	\$44.5	\$35.5	Auburn MS (New Construction): Filed-Sub Bids Due 3/31. GMP Targeted April.											
<b>WACHUSETT RSD</b>	800	\$54.3	\$43.1	Mountview MS (New Construction): Filed-Sub Bids Due 2/25. G.C. Bids Due 3/12. NTP Targeted March.											
<b>*CHICOPEE</b>	850	\$38.0	\$30.8	Chicopee Academy (Renovation): Filed-Sub Bids Due 3/3. GMP Targeted April.											
<b>SOUTH HADLEY</b>	270	\$28.2	\$21.6	South Hadley: Plains ES (New Construction): Filed-Sub Bids Due 4/3. G.C. Bids Due 4/17. NTP Targeted April.											
<b>PEABODY</b>	1,340	\$92.6	\$75.1	Peabody: Higgins MS (New Construction): Filed-Sub Bids Due 5/15. G.C. Bids Due 5/22. NTP Targeted June.											
<b>Subtotal</b>	<b>6,810</b>	<b>\$397</b>	<b>\$315.1</b>												
<b>GRAND TOTAL</b>	<b>6,810</b>	<b>\$397</b>	<b>\$315.1</b>												
<b>Number of Construction-Related Employment Opportunities Created</b>			<b>1,576</b>												

**Projects in Construction  
MSBA Grant Basis and Maximum Grant Amount  
Data Reported as of October 30, 2013**

New Program and Wait List Program Totals			\$2,802,391,994	58,553		11,364,412											*Includes Alternates	\$1,972,946,590		
Project	Grade	Contractor	Total Construction Cost*	Projected Enroll	PFA or Bid Data	Proposed Square Footage	Construction Cost per Square Foot	Building Cost	Building Cost per Square Foot	Project Type	Construction Start	Estimated Substantial Completion Date	Reporting Variance from Schedule	Physical Progress (%)	Change Orders (%)	Construction Status	Approximate Maximum Grant Amount *			
<b>CAPITAL PIPELINE PROJECTS IN CONSTRUCTION</b>																				
<b>New Program Totals</b>			<b>\$2,713,769,030</b>	<b>56,493</b>		<b>10,900,722</b>	<b>\$252</b>		<b>\$188</b>											<b>\$1,811,883,955</b>
Arlington	K-5	G&R Construction	\$15,340,026	380	Bid	57,614	\$266	\$12,403,811	\$215	Design/Bid/Build	7-Apr-12	21-Aug-13		98%	2.90%	The new building is in service. Resolution of a small number of punch list and commissioning items are in process. Final site work is nearing completion.	\$9,441,396			
Assabet Valley Reg Voc Tech	9-12	CTA Construction, Inc.	\$50,755,300	963	PFA	367,565	\$138	\$36,121,000	\$98	Design/Bid/Build	1-Apr-13	1-Aug-15		22%	-0.14%	This is a (10) phase project. Phase 1 and 2 are complete other than punch list items. Work included demo of ceiling tiles, demo of the Mechanical Room, HVAC work and abatement, MEP work, roofing, flooring and painting for these areas. Certificate of occupancy for Phase 2 was received which allowed students and staff back into the building in that location. Phase 3 is underway.	\$33,099,495			
Berlin-Boylston Tahanto Reg MS/HS	6-12	CTA	\$32,162,000	560	Bid	126,100	\$255	24,629,999	\$195	Design/Bid/Build	10-May-11	1-Jul-13		99%	3.19%	The new building is in service. Resolution of punch list and commissioning items are in process. Final site work is nearing completion. Installation of ceramic tile is planned to replace the blue stone exterior at the front entrance facade that was removed due to performance issues.	\$19,849,301			
Brookline Heath ES	K-8	Nauset	\$6,284,185	560	Bid	80,952	\$78	\$4,807,436	\$59	Design/Bid/Build	29-Sep-11	15-Aug-12		100%	4.70%	Project is complete and closeout is in process.	\$3,173,407			
Brookline Runkle ES	PK-8	G&R Construction	\$20,715,300	560	Bid	104,000	\$199	\$17,668,440	\$170	Design/Bid/Build	10-Nov-10	10-Sep-12		100%	8.22%	Project is complete and closeout is in process.	\$11,135,430			
Danvers Danvers HS	9-12	Bacon Construction	\$53,834,164	1,000	Bid	246,251	\$219	\$43,710,809	\$178	Design/Bid/Build	14-Nov-10	10-Jul-13	Approx. 113 days	100%	2.51%	Remaining Phase II punch list work is in progress. The contractor has begun submitting the remaining documents required for the achievement of substantial completion.	\$37,324,055			
Douglas Douglas ES	2-5	CTA	\$24,275,111	552	Bid	83,100	\$292	\$19,026,763	\$229	Design/Bid/Build	Mar-12	26-Aug-13		99%	0.00%	Site work continues. Exterior panel installation is nearing completion. Punch list is being completed during off hours while school is in session.	\$17,573,941			
Douglas Douglas IS	6-8	CTA	\$12,081,767	448	Bid	88,245	\$137	\$9,417,212	\$107	Design/Bid/Build	Mar-12	31-Jan-14	28 days	60%	0.00%	Site work continues. The Gym and Auditorium are complete. Window installations and abatement are complete. MEP rough-ins and structural steel are 50% complete. Demolition is nearing completion. Interior glass partitions are underway.	\$8,203,129			
Dracut Dracut HS	9-12	CTA	\$45,900,000	1,160	Bid	226,844	\$202	\$38,377,028	\$169	Design/Bid/Build	27-Aug-12	26-Aug-14		50%	0.78%	Phase II work is underway. Demolition, structural steel, MEP rough-in work, masonry are all underway. Site work continues.	\$35,838,072			
East Bridgewater E. Bridgewater Jr/Sr HS	7-12	Fontaine Brothers	\$65,409,000	950	Bid	213,544	\$306	\$47,684,117	\$223	Design/Bid/Build	10-Aug-11	24-Jun-13		89%	2.77%	The school has been turned over to the District and opened in September. Abatement of the existing HS and the additional field work are underway.	\$43,317,092			
Easthampton Easthampton HS	9-12	Fontaine Brothers	\$30,934,000	510	Bid	110,400	\$280	\$24,511,000	\$222	Design/Bid/Build	16-May-11	19-Feb-13	60 days	99%	2.20%	The new building is occupied. Demolition of the existing building is complete as well as site work and landscaping except for punch list items. Ten-month commissioning follow up is scheduled for January 2014.	\$24,104,384			
Fairhaven Rogers ES	K-5	CTA	\$19,099,606	370	Bid	77,871	\$245	\$14,996,521	\$193	Design/Bid/Build	21-May-12	28-Jul-13		99%	0.97%	The new building is in service. Resolution of punch list and commissioning items is in process. Final site work is complete.	\$13,994,641			
Fall River Morton MS	6-8	J&J Contractors	\$37,654,000	625	Bid	130,576	\$288	\$29,921,971	\$229	Design/Bid/Build	4-Nov-11	15-Jul-13		99%	8.97%	Building is substantially complete. Minor punch list work remaining.	\$38,251,808			
Franklin Franklin HS	9 - 12	Agostini/Bacon	\$86,778,700	1,650	Bid	306,543	\$283	\$73,191,801	\$238.77	Design/Bid/Build	16-Oct-12	15-Oct-14		55%	0.49%	The new student parking lot was turned over to the District on time for the start of school in September. Building is planned to be weather tight by November 15. All trades continue work throughout the building. There are presently 170-200 workers on site daily.	\$57,246,682			
Georgetown Penn Brook ES	K-6	Brait Builders Corp.	\$36,979,465	770	PFA	98,000	\$377	\$18,735,796	\$191.18	Design/Bid/Build	26-Sep-13			0%	0.00%	The contractor has recently mobilized.	\$20,348,437			
Greater New Bedford Regional Voc Tech HS	8-12	Agostini	\$13,669,847	2,060	PFA	487,530	\$28	\$9,627,841	\$20	Design/Bid/Build	13-Sep-13	22-Aug-14		1%	0.00%	The contractor has mobilized. Installation of perimeter fencing and erosion controls are being put in place.	\$13,543,920			
Hampden-Wilbraham Minnechaug HS	9-12	Fontaine Brothers	\$48,597,500	1,225	Bid	231,467	\$210	\$37,499,962	\$162	Design/Bid/Build	22-Jul-10	28-Jun-12		99%	2.29%	Remaining site work is scheduled to be completed by November which includes seeding one baseball field and loam and seed a soccer field.	\$34,863,838			
Hingham Hingham MS	6-8	Brait Builders Corp.	\$48,436,000	1,020	Bid	176,385	\$275	\$41,227,552	\$234	Design/Bid/Build	7-Jun-12	30-Dec-14		75%	0.26%	Work continues throughout the building. The classroom wing is 95% complete.	\$25,909,580			
Hudson John F Kennedy MS	5-7	Agostini/Bacon	\$35,102,573	715	Bid	118,846	\$295	\$28,373,294	\$239	Design/Bid/Build	28-Sep-11	22-Jun-13		98%	2.85%	The new building is complete and was open for use in August 2013. Demolition of existing building is complete and the new parking lot was paved before start of school. Final commissioning and site work scheduled to be complete in November.	\$24,005,749			
Lynnfield Lynnfield HS	9-12	E.A. Colangeli	\$3,110,346	740	Bid	10,950	\$284	\$2,322,687	\$212	Design/Bid/Build	25-Jun-12	28-Jun-13		99%	8.09%	Minor punch list work remaining.	\$1,828,473			
Marblehead Glover ES	K-3	G&R Construction	\$20,868,000	425	Bid	79,108	\$264	\$16,977,513	\$215	Design/Bid/Build	25-Jun-12	20-Dec-13		75%	2.24%	Building exterior is complete including windows and storefront. Permanent electric and gas has been installed. Interior finish work is in process including MEP, wallboard, ceilings, miscellaneous metal work, painting, cabinets, casework and interior glazing. Exterior work on retaining walls, parking and playground areas is progressing.	\$9,688,418			
Marshfield High School	9 - 12	Brait Brothers	\$84,980,000	1,310	Bid	267,469	\$318	\$64,604,850	\$242	Design/Bid/Build	Aug-12	7-Jul-14		66%	0.52%	Turnover of the stadium, track, fields, and concession building was completed on schedule in August and the facilities are in use by the District. Exterior masonry is complete in the courtyard and almost complete in the academic wing. Window installation is progressing and testing began in October. Roofing is nearing completion with all the membrane installed. Interior finish work continues with acoustical ceilings and drywall/plaster progressing, and finish carpentry just starting. MEP work is progressing throughout the building.	\$48,607,274			
Maynard Maynard HS	8-12	CTA	\$36,650,000	410	Bid	121,520	\$302	\$30,630,013	\$252	Design/Bid/Build	18-Aug-11	13-Dec-13		94%	1.27%	Punch list work is ongoing throughout the building. Work continues in the Auditorium. Site work is in progress with final grading and seeding underway.	\$23,483,860			
Monomoy Regional High School	9-12	Fontaine Brothers	\$49,374,000	700	Bid	168,000	\$294	\$41,433,695	\$247	Design/Bid/Build	11-Feb-13	30-Jun-14		38%	0.08%	Exterior masonry wall construction is progressing. Windows have been temporarily enclosed. The rough installation of the mechanical, electrical, plumbing, and fire-protection systems continue throughout the academic and administration areas.	\$29,696,270			
Newburyport Bresnahan ES	PK-3	CTA Construction, Inc.	\$27,405,000	660	Bid	112,517	\$244	\$20,842,000	\$185	Design/Bid/Build	14-Mar-13	30-Jun-14		43%	0.00%	Building envelope is nearing completion. Structural steel, roof and slabs are complete. MEP rough-ins are progressing on schedule.	\$15,676,427			
Norfolk County Agricultural HS	9-12	TLT Construction Corp.	\$21,508,952	550	Bid	114,816	\$187	\$15,546,739	\$135	Design/Bid/Build	27-Mar-12	9-May-14	133 days	75%	2.21%	Phase 1: Animal Science Building and Agricultural Mechanical Building punch list work is ongoing. Certificate of Occupancy issued on August 20, 2013. Equine Center is substantially complete with Certificate of Occupancy received on October 4, 2013. Equipment Garage is substantially complete with Certificate of Occupancy pending. Phase 2, renovation of existing labs and conversion of existing building to administration space, commenced on October 1, 2013 with demolition and abatement currently ongoing.	\$14,119,915			
Norfolk Freeman-Kennedy ES	3-6	Fontaine Brothers	\$25,354,966	585	Bid	96,410	\$263	\$20,023,001	\$208	Design/Bid/Build	9-Nov-10	13-Aug-12		98%	6.00%	The new building is complete and currently in use. Minor punch list items are ongoing.	\$15,861,760			
Old Colony: Old Colony Regional Voc Tech HS	9-12	J.D. Rivet % Co., Inc.	\$2,037,200	586	Bid	106,000	\$19	\$1,532,886	\$14	Design/Bid/Build	26-Jun-13	3-Sep-13		100%	0.00%	Minor punch list items for roof remain (adding a gutter at roof F). Science Lab punch list is complete. Closeout and commissioning are underway.	\$1,376,068			
Oxford Oxford MS	5-8	S.O.M./ J.J. Cardosi	\$5,085,217	652	Bid	117,000	\$43	\$5,085,217	\$43	Design/Bid/Build	1-Jun-12	31-Aug-14		45%	6.00%	Roof replacement completed in Summer 2012. Window project completed in Summer 2013. HVAC, ADA, and floor replacement work is currently being bid with construction to begin on May 1, 2014.	\$3,483,589			
Plymouth Plymouth HS	9-12	J&J Contractors	\$67,687,000	1,350	Bid	267,497	\$253	\$51,579,703	\$193	Design/Bid/Build	3-May-10	22-Jun-12	30 days	99%	5.49%	Installation of ball field lights scheduled to be installed by the end of November.	\$41,810,972			
Quincy Central MS	6-8	H.V. Collins Co. Inc.	\$32,540,712	620	Bid	114,975	\$283	\$27,057,118	\$235	Design/Bid/Build	24-May-12	5-Sep-13	43 days	90%	1.97%	Commissioning and punch list work are underway. The Auditorium is nearing completion. Substantial Completion and Certificate of Occupancy received October 18, 2013. School opened for classes on October 21, 2013.	\$32,780,403			
Somerset Berkley Somerset Berkley RHS	9-12	Bacon-Agostini	\$69,407,000	1,000	Bid	222,826	\$311	\$52,042,575	\$234	Design/Bid/Build	3-Jul-12	15-Aug-14	Approx. 113 days ahead	55%	0.39%	The first contract milestone, turnover of the track and fields in late August, was missed by 2 weeks. The track and fields have now been turned over and are presently in use by the District. The contractor is on schedule for the next milestone, substantial completion of the new school in June 2014. The building will be weather tight by the end of 2013 for finish work to proceed through the Winter. Masonry in the courtyard is nearing completion and 51% overall. All the high roof installation (academic area) is complete and work is ongoing in the lower roof areas. Work is progressing within the building with the 2nd floor being furthest ahead followed by the 3rd floor and then the first floor. The workforce is at 160/day average.	\$49,050,210			
Southwick-Tolland-Granville Regional HS	7-12	Fontaine Brothers	\$31,408,667	790	PFA	165,995	\$189	\$21,298,500	\$128	Design/Bid/Build	31-Jul-13	9/18/2015		9%	0.00%	Foundation and underground MEP scope for the Middle School addition is nearly complete. Excavation and foundation work has begun for High School addition. The new primary electrical duct-bank has been installed from the main road.	\$26,266,394			
Southwick-Tolland-Granville Powder Mill IS	3-6	PDS Engineering	\$14,747,586	545	PFA	95,775	\$154	\$10,420,350	\$109	Design/Bid/Build	24-Jul-13	14-Aug-15		19%	0.00%	Phase 1, renovation of the Cafeteria, Library, and district offices, is being completed with installation of lighting and casework that was not available prior to the start of the academic year. No work was scheduled during the current academic year. However, the contractor will begin preparing for electrical and mechanical work prior to the start of summer break.	\$9,878,462			
Southwick-Tolland-Granville Woodland ES	PK-2	PDS Engineering	\$7,328,004	400	PFA	67,800	\$108	\$5,218,390	\$77	Design/Bid/Build	24-Jul-13	14-Aug-15		36%	0.00%	Phase 2, renovation of North Wing, is underway with rough-ins complete and finishes ongoing. Phase 2 substantial completion is scheduled for 12/6/13. Delivery of windows has been delayed for Phase 2. Windows will be replaced during next phase.	\$5,194,158			
Sturbridge Burgess ES	K-6	Fontaine Brothers	\$22,946,000	860	Bid	131,630	\$174	\$17,591,000	\$134	Design/Bid/Build	10-Aug-10	30-Oct-12		99%	8.57%	The new school building addition and the adjacent existing school building renovation are complete and are in service. Final punch list items are being completed. Rubber floor tile adhesion failure in two areas of the renovated building is being investigated for cause and resolution.	\$16,616,077			
Sutton MS/HS	6-12	TLT Construction Corp.	\$41,230,800	840	Bid	179,040	\$230	\$32,998,403	\$184	Design/Bid/Build	1-Jul-11	31-Dec-14	180 days	73%	1.96%	The Middle School classroom wing, Media Center, Cafeteria and Kitchen have been turned over and students are occupying the building. Work continues in the Auditorium area.	\$27,837,016			

**Projects in Construction  
MSBA Grant Basis and Maximum Grant Amount  
Data Reported as of October 30, 2013**

Project	Grade	Contractor	Total Construction Cost*	Projected Enroll	PFA or Bid Data	Proposed Square Footage	Construction Cost per Square Foot	Building Cost	Building Cost per Square Foot	Project Type	Construction Start	Estimated Substantial Completion Date	Reporting Variance from Schedule	Physical Progress (%)	Change Orders (%)	Construction Status	Approximate Maximum Grant Amount *
Tewksbury Tewksbury HS	9-12	CTA/Methuen Construction Co.	\$51,600,000	1,100	Bid	218,781	\$236	\$40,159,651	\$184	Design/Bid/Build	15-Oct-10	3-Aug-12		98%	4.54%	The rubberized running track and tennis courts are scheduled to be complete in late Fall 2013.	\$36,622,570
Webster Park Ave Elem School	PK-4	CTA Construction, Inc.	\$32,370,000	720	Bid	109,597	\$295	\$25,725,914	\$235	Design/Bid/Build	27-Jun-13	1-Dec-14		10%	0.00%	Modular classrooms are set up. Demolition of existing building and connector are underway. Excavation, footing and foundation work continues. Steel erection began in October.	\$30,880,737
Westfield Abner Gibbs ES	K-5	Fontaine Brothers	\$25,578,000	600	Bid	95,573	\$268	\$21,444,000	\$224	Design/Bid/Build	24-Aug-12	N/A		7%	0.00%	Work stoppage regarding Article 97 "Protected Land". The City still does not have approval. General Contractor has demobilized from the site.	\$21,762,201
West Bridgewater	7-12	CTA Construction, Inc.	\$49,728,000	625	PFA	141,250	\$352	\$32,130,800	\$227	Design/Bid/Build	1-Oct-13	15-Jun-15		0%	0.00%	The contractor has mobilized. Erosion controls are in place and a perimeter fencing has been erected. Clearing and grubbing are complete. Demolition of the existing athletic fields and courts are complete. Topsoil has been stripped and stockpiled on site. The building footprint has been proof-rolled and structural fill is being placed.	\$47,584,652
West Springfield West Springfield HS	9-12	Fontaine Brothers	\$85,006,020	1,270	Bid	257,525	\$330	\$56,875,181	\$221	Design/Bid/Build	14-Dec-11	31-Dec-13		74%	2.18%	Electrical & plumbing finishes are ongoing in academic wings. Casework and countertop installations are ongoing on all floors. The main entry structures have been installed. Metal panels in the Gymnasium are complete. Pool deck slab has been placed.	\$68,808,290
Weston Field ES	4-5	Colantonio	\$24,537,966	355	Bid	65,390	\$375	\$19,872,289	\$304	Design/Bid/Build	21-Dec-12	15-May-14	5 days	43%	0.48%	Foundation has been poured throughout the building. Structural steel and door framing are complete. All mechanicals have been roughed in and sprinkler cuts began. Upper windows are being installed on the south side of the building. Roof flashing is ongoing and roof test cuts began late October. The contractor plans to have the building weather tight with temporary heat in place for the upcoming winter months.	\$8,610,302
Williamsburg Anne T. Dunphy ES	PK-6	Enfield	\$8,990,457	170	Bid	37,100	\$242	\$7,625,327	\$206	Design/Bid/Build	5-Apr-13	7-Apr-14		32%	1.35%	Demo and abatement are complete. Structural steel for the new classroom section is underway. Renovation of the existing kitchen, MEP rough-ins, earth work and underground utilities are all underway.	\$6,808,088
Winchester Vinson-Owen ES	K-5	CTA	\$20,446,000	420	Bid	74,774	\$273	17,767,598	\$238	Design/Bid/Build	17-Feb-12	26-Jul-13		99%	2.22%	Punch list work is ongoing.	\$10,292,465
Andover Bancroft ES	K-5	Skanska	\$44,077,007	680	Bid	106,486	\$414	27,101,717	\$255	CM-R	14-May-12	22-May-14		55%	0.11%	Exterior envelope construction continues. The building is scheduled to be weather tight by November 7, 2013. MEP rough-ins are underway and drywall installation has begun. Excavation for wetlands replication has commenced.	\$16,773,753
Ayer-Shirley Reg HS	9-12	Consigli	\$44,516,576	495	PFA	144,072	\$309	\$27,797,209	\$193	CM-R	19-Feb-13	1-Aug-15		5%	0.00%	Underground utility work up to the building is complete. Early foundation work is complete and steel erection is in progress at the new classroom wing and band/chorus addition.	\$37,174,694
Ashburnham Westminster JR Briggs ES	PK-5	Consigli	\$24,780,000	520	Bid	87,085	\$285	18,202,478	\$209	CM-R	9-Mar-12	30-Aug-13		96%	0.59%	The new school building is in service. Resolution of punch list and commissioning items are in process. Final site work is nearing completion.	\$16,353,447
Concord-Carlisle HS	9-12	Turner Construction	\$76,143,000	1,225	Bid	219,871	\$346	\$60,487,000	\$275	CM-R	20-Feb-13	15-Mar-15		16%	0.09%	Loop road binder course and foundations are complete. Slabs are ongoing with structural steel progressing on schedule. Roofing and building envelope are underway.	\$26,035,535
Duxbury HS	6-12	Dimeo	\$117,543,746	1,735	PFA	325,721	\$361	\$73,368,123	\$225	CM-R	9-Jul-12	3-Jul-14		58%	0.23%	Foundations, slabs and site underground utilities are complete. MEP rough-ins are complete including inspections/sign. The Field House was completed ahead of schedule on August 16, 2013. Roofing is approx. 95% complete. Curtain walls are 92% complete, plumbing is 75% complete, HVAC is 78% complete, and electrical is 46% complete. Drywall and CMU interior walls ongoing. Tiling has just begun.	\$50,363,184
Essex Technical High School	9-12	Gilbane	\$110,217,451	1,440	Bid	337,000	\$327	\$79,334,889	\$235	CM-R	7-May-12	30-Jun-14		62%	1.13%	Building facade work continues on main academy building. MEP rough-ins, CMU, drywall, taping, casework, and roof and window installations are ongoing. Work ongoing at detention ponds and main field. Loam and seed is being placed throughout the site. Concrete and bituminous sidewalks being installed.	\$77,500,000
Greenfield	8-12	Shawmut Design	\$52,487,924	585	PFA	160,649	\$327	\$37,812,150	\$235	CM-R	23-Mar-13	15-Aug-15		8%	-0.32%	Site utilities, foundations, structural steel and slabs on grade and decks are complete. Installation of metal wall studs, exterior sheathing, CMU blocking and electrical power cables are in process. Paving of areas needed for parking has been completed.	\$44,525,802
Leominster Leominster SHS	9-12	S.O.M.	\$33,794,797	1,825	Bid	295,859	\$114	\$25,382,707	\$86	CM-R	1-Jul-11	30-Aug-13		99%	5.76%	Punch list work, owner training, and commissioning activities are ongoing throughout the building.	\$30,693,543
Lexington Estabrook ES	K-5	Shawmut Design	\$32,792,348	540	Bid	91,840	\$357	\$22,795,606	\$248	CM-R	20-Jun-12	27-Jan-14		60%	0.16%	Phase I demo is 15% complete. Demo for Phase II starts after the new school is occupied in February of 2014. New building envelope, window installations and exterior masonry are complete. MEP rough-ins, framing and drywall nearing completion. Interior finishes have started. Site work is 50% complete.	\$12,148,495
Longmeadow Longmeadow HS	9-12	Gilbane	\$63,685,998	1,000	Bid	236,985	\$269	\$46,573,364	\$197	CM-R	Nov-10	1-Nov-13		96%	2.16%	Landscaping is underway. The remaining millwork is nearing completion with the installation of the display cases in the north Gym corridor. Punch list work continues throughout the building.	\$33,067,140
Methuen Methuen HS	9-12	Terminated Dimeo 12/31/2011. Consigli as of 5/21/2012	\$74,749,773	2,075	Bid	368,017	\$203	\$58,040,746	\$158	CM-R	21-Jul-11	Aug-14	30 days	65%	2.81%	Phase I was completed and occupied by students on September 5, 2013. Punch list and commissioning work continue for Phase I. The Auditorium is scheduled to be turned over in December. Phase II, renovation of the existing HS, demolition is 90% complete. MEP's and framing are all underway and on schedule.	\$64,503,232
Newburyport Nock MS / Molin ES	Nock MS 6-8 Molin ES 4-5	Gilbane	\$20,877,414	845	Bid	161,500	\$129	\$17,756,966	\$110	CM-R	18-Mar-13	21-Aug-14		39%	1.24%	Phase I work is complete except for punch list items which are ongoing. Phase II work is underway on a full time off-hours schedule (3-11 pm) now that school is back in session. Work in process includes selective demolition, installation of new data and power work, new sprinkler installation, installation of new masonry door openings and metal door frames, painting, installation of new windows, and other new MEP work. Window commissioning process is ongoing.	\$13,697,934
North Reading Middle/Senior High School	6-12	Gilbane	\$86,315,287	1,370	PFA	267,939	\$322	\$56,361,445	\$210	CM-R	02-Jul-12	21-Aug-14 (HS) 21-Aig-15 (MS)		35%	0.22%	Construction of the new High School is progressing with the plan to have the new high school entirely weather tight by the end of November 2013. Certain trades are working 6 days/week for increased progress. There are presently 200-215 workers on site daily.	\$49,323,123
Norton Norton HS	9-12	WT Rich	\$27,023,541	700	Bid	162,405	\$166	\$20,590,559	\$127	CMR	12-Mar-12	31-Dec-13		92%	4.32%	Phase 3 & 4 renovation work is complete and occupied. Work on the final phase is in progress including renovations to the Library, Auditorium, Band Rooms and misc. adjacent areas. Library and flex labs are scheduled for early turnover.	\$21,433,614
Rockland John Rogers MS/ HS	5-12	Agostini	\$66,362,037	1,525	Bid	275,700	\$241	\$47,724,091	\$173	CM-R	15-Nov-10	31-Dec-12		99%	6.00%	Miscellaneous punch list items remaining.	\$52,837,940
Shrewsbury Sherwood MS	5-6	Gilbane	\$33,986,286	900	Bid	129,378	\$263	\$22,823,030	\$176	CM-R	7-Mar-11	31-Oct-13		99%	-0.90%	The new school building is in service. Resolution of a small number of commissioning items are in process. Final site work is nearing completion.	\$22,369,828
Southern Worcester Bay Path Voc-Tech	9-12	Consigli	\$73,722,405	1,110	PFA	249,521	\$295	\$58,201,331	\$233	CM-R	2-Aug-13	1-Sep-15		3%	0.00%	Early packages released for earthwork, concrete and steel. Excavation and foundation formwork started. Steel projected to start in December 2013.	\$47,483,003
Southbridge Southbridge MS/HS	6-12	Consigli	\$59,307,632	1,050	Bid	199,740	\$297	\$41,487,200	\$208	CM-R	30-Nov-10	31-Jul-12		100%	-1.23%	Over seeding of the baseball and football fields is in progress. Project Closeout is in progress.	\$52,019,398
Southeastern Regional Voc Tech High School	9-12	WT Rich	\$27,200,000	1,370	Bid	308,250	\$88	\$19,996,609	\$65	CM-R	27-Jun-11	9-Sep-13		99%	2.28%	Renovations are complete and the building is in service. Punch list and commissioning items are being addressed.	\$25,988,607
Springfield Elias Brookings ES	PK-5	Morganti Aquadro & Cerruti	\$22,733,394	320	PFA	64,800	\$351	\$15,374,674	\$237	CM-R	1-Jul-13	20-Jan-15		1%	0.00%	Mobilization of subcontractors to the site is underway.	\$17,552,016
Springfield Dryden ES	PK-5	Morganti Aquadro & Cerruti	\$11,476,091	280	Bid	40,900	\$281	\$8,276,912	\$202	CM-R	28-Jun-12	1-Nov-13		90%	0.40%	Punch list work for Phases 1 and 2 are underway while work continues on the Phase 3 Gym and classrooms renovations.	\$8,169,913
Stoneham Middle School	5-8	Shawmut Design	\$33,086,864	775	Bid	136,410	\$243	\$21,209,275	\$155	CM-R	3-Dec-12	8-Aug-14		28%	0.21%	Foundations, structural steel, placement of slabs on deck and grade, and exterior wall construction for the new building is complete. Installation of exterior sheathing, vapor barrier, masonry and CMU is in process. The main renovations to the adjacent Central School are complete with the remainder of work scheduled to be completed in the Summer of 2014.	\$21,889,091
Uxbridge High School	9-12	Shawmut Design	\$37,293,765	600	Bid	123,000	\$303	\$27,562,625	\$224	CM-R	28-Feb-11	20-Jun-12		99%	2.93%	Miscellaneous punch list work remaining. Project is scheduled to be completed in the late Fall of 2013.	\$21,973,620
Wakefield	5-8	Bond Brothers	\$59,756,583	1,070	Bid	187,722	\$318	\$44,899,853	\$239	CM-R	18-Mar-13	15-Jun-15		11%	0.26%	Buildings A & B: Foundations, structural steel, placement of slabs on deck and grade, wall construction, exterior sheathing and vapor barrier installation is complete. Masonry and interior wall construction and MEP rough-ins are in process. Building C: GeoPier installation is complete and the foundation is partially complete.	\$34,547,827
Wilmington	9-12	Gilbane	\$65,690,437	960	Bid	192,443	\$341	\$47,966,002	\$249	CM-R	April 30-13	13-Feb-15		12%	0.00%	Gym and turf field are complete. Street and underground utility work are complete. Foundations are complete in Areas A through D and ongoing for Areas E & F. Perimeter foundation damp proofing and insulation are ongoing. Steel erection is about 70% complete. Elevator pit/formwork is complete. Under-slab plumbing and electrical work is ongoing. Building commissioning kick-off meeting took place and MEP submittals are being reviewed.	\$37,993,245
<b>** Excludes Field House</b>																	
<b>Wait List Program Totals</b>			<b>\$120,784,964</b>	<b>2,060</b>		<b>463,690</b>											<b>\$141,213,334</b>
Springfield Forest Park MS	6-8	Consigli	\$34,745,898	660	Bid	148,800	\$234	\$26,209,932	\$176	CM-R	26-Mar-12	1-Aug-13	25 days	98%	2.23%	Substantial completion achieved on August 26, 2013. Punch list work and project closeout are underway.	\$38,340,497

**Projects in Construction  
MSBA Grant Basis and Maximum Grant Amount  
Data Reported as of October 30, 2013**

Project	Grade	Contractor	Total Construction Cost*	Projected Enroll	PFA or Bid Data	Proposed Square Footage	Construction Cost per Square Foot	Building Cost	Building Cost per Square Foot	Project Type	Construction Start	Estimated Substantial Completion Date	Reporting Variance from Schedule	Physical Progress (%)	Change Orders (%)	Construction Status	Approximate Maximum Grant Amount *
Springfield Putnam Voc Tech HS	9-12	Consigli	\$86,039,066	1,400	Bid	314,890	\$273	\$62,949,742	\$200	CM-R	18-May-10	20-Jul-12		99%	-0.15%	Miscellaneous landscaping punch list work remaining.	\$102,872,837
Worcester North HS	9-12	Gilbane	\$49,145,638	1,200	Bid	239,570	\$205	\$40,860,983	\$171	CM-R	24-Sep-08	Jun-11		99%	3.20%	Phase 4, which includes paving the remaining parking lot and striping, is complete. Minor site punch list work to be completed.	\$45,911,881
