


Project Overview Report

January 9, 2013

A total of 331 projects that have received invitations from the Board of Directors (“Board”) to collaborate with the MSBA are currently in the MSBA’s Eligibility Period and Capital Pipeline. The following summary chart provides the number of projects in the Eligibility Period and each phase of the Capital Pipeline:

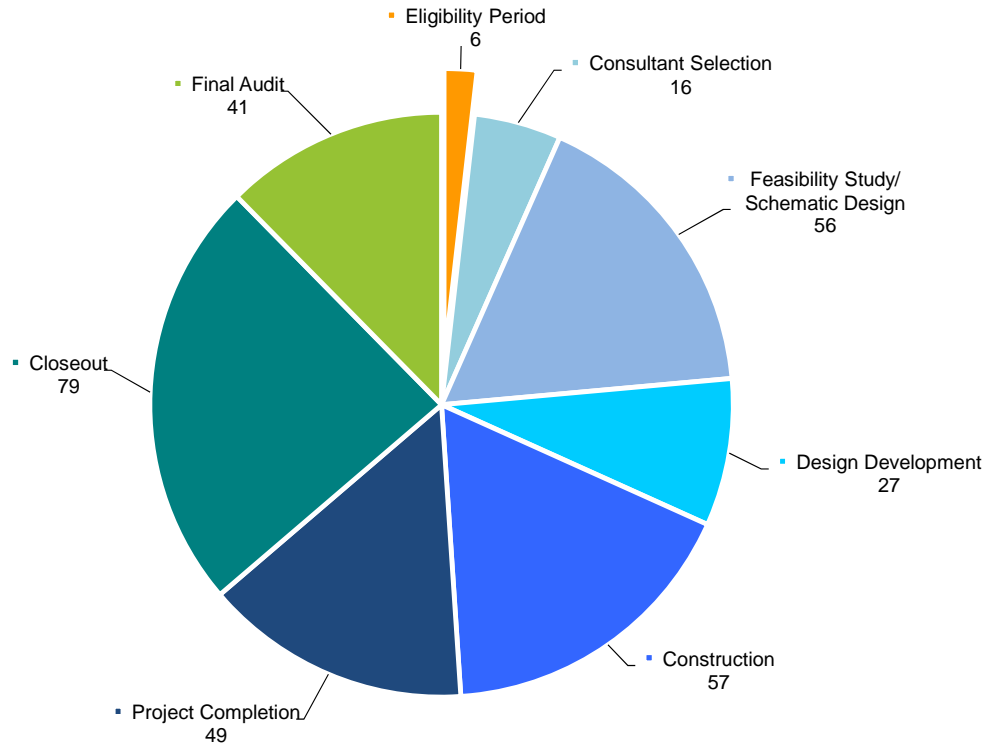

Statement of Interest (“SOI”) Review Status

The FY 2013 SOI Process opened on January 9, 2013. The submission process will close on April 10, 2013.

- To date 39 Districts have requested User Access

2012 SOI Overview

- 280 SOIs submitted:
 - 13 SOIs were filed for the Science Lab Initiative
 - 14 SOIs have been invited into the Eligibility Period
 - Two additional staff recommendations for invitations at the January Board meeting will bring the total to 16 SOIs invited into the Eligibility Period
 - 39 SOIs have been invited into the Accelerated Repair Program
 - 217 SOIs are being reviewed for the Core Program

Eleven of the 13 SOIs filed for the Science Lab Initiative have been invited into the Program. Joseph Case High School in Swansea and Saugus High School have requested removal of further consideration due to funding concerns.

Two of the 14 SOIs invited into the Eligibility Period have requested removal from further consideration due to funding concerns: the Clara Macy Elementary School in Bellingham and the Minot Forest Elementary School in Wareham.

Six of the 39 facilities invited into the Accelerated Repair Program have requested removal from further consideration due to funding concerns: the Rowe Elementary School in Rowe; the John A. Parker Elementary School in New Bedford; the Joseph Case Junior High School in Swansea; and three schools in the Bridgewater-Raynham Regional School District: the LaLiberte Elementary School, the L.B. Merrill School, and Bridgewater Middle School.

Eligibility Period

There are six districts in the Eligibility Period. No districts are seeking local funding and authorization within the next 60 days, and four of the six districts have secured funding. The remaining two districts have yet to confirm their dates for action.

An agreed-upon enrollment is a key pre-requisite for the MSBA to commence a Feasibility Study with a district. To begin the enrollment projection process, a district must file enrollment information utilizing the MSBA's online enrollment projection tool. Since the last report, two districts have completed the enrollment process.

Based upon the schedules anticipated by the districts for completion of the Eligibility Period requirements, staff anticipates recommending the six districts in Eligibility Period for an Invitation to Feasibility Study at upcoming Board meetings.

Capital Pipeline

Consultant Selection

After the district has completed all Eligibility Period requirements and received a Board Invitation to Feasibility Study, the district procures an Owner's Project Manager ("OPM"). There are four districts in the Capital Pipeline who need to procure an OPM.

After a district has selected and executed a contract with an OPM, it selects a Designer utilizing either a local designer selection process for projects under \$5 million or the MSBA's Designer Selection Panel ("DSP") for projects over \$5 million. There are 12 districts in the Capital Pipeline who are in the process of procuring a Designer.

Feasibility Study

Once a district has procured an OPM and Designer and a Feasibility Study Agreement has been executed, the district and its consultants must complete two Feasibility Study submittals, the Preliminary Design Program and the Preferred Schematic Report, prior to Board consideration to proceed into Schematic Design. Based on the

most recent data and schedules provided to the MSBA by districts, the MSBA anticipates that eight districts will present their preferred schematic designs to the Board at the upcoming April and June Board meetings.

Prior to consideration by the Board for Project Scope and Budget authorization, a district must submit a schematic design to the MSBA for review. Based on the most recent data and schedules provided to the MSBA by districts, the MSBA anticipates that eight districts will appear before the Board for Project Scope and Budget Agreement authorization at the upcoming April and June Board meetings.

Commissioning

Since the last report, the MSBA has assigned Commissioning Consultants to an additional 17 projects as presented in the table below. To date, the MSBA has executed 209 Commissioning Consultant contracts, totaling \$16.6 million; 36 contracts have been completed.

District	School	Estimated Const. Cost (million)	Commissioning Consultant	Contract Amount
Wilmington	North Intermediate - Accelerated Repair: Windows	\$1.21	CBI Consulting Inc.	\$30,200
Westfield	Munger Hill Elementary, Paper Mill Elementary - Accelerated Repair: Roofs	\$2.34	Building Enclosure Associates	\$46,800
North Attleborough	North Attleborough High School Science Lab Initiative	\$4.65	Consulting Engineering Services, LLC	\$24,350
Gardner	Gardner High School - Science Lab Initiative	\$2.93	Fitzemeyer & Tocci Associates, Inc.	\$18,300
Hamilton-Wenham Regional	Cutler Elementary - Accelerated Repair: Roof	\$0.55	Russo Barr Associates, Inc.	\$22,800
Springfield	Elias Brookings Elementary School	\$22.73	BVH Integrated Services, P.C.	\$76,465
Sudbury	Gen. John Nixon Elementary - Accelerated Repair: Roof	\$0.62	Gale Associates, Inc.	\$21,680
Shawshen Valley Voc Tech	Shawshen Valley Technical High School - Accelerated Repair:Boilers	\$0.74	Fitzemeyer & Tocci Associates, Inc.	\$6,400
North Attleborough	Roosevelt Avenue Elementary - Accelerated Repair: - Windows	\$0.77	Gale Associates, Inc.	\$29,270
North Brookfield	North Brookfield Elementary - Accelerated Repair: Windows (Phase 2)	\$0.27	Simpson Gumpertz & Heger Inc.	\$19,500
Georgetown	Penn Brook Elementary School	\$36.98	Rist-Frost-Shumway Engineering	\$91,139
Gardner	Gardner Middle School - Accelerated Repair: Boilers	\$0.44	Fitzemeyer & Tocci Associates, Inc.	\$10,240
Lynn	Breed Middle School, Lynn Vocational Technical Institute - Accelerated Repair: Roof, Windows	\$5.97	CBI Consulting Inc.	\$44,700
Easton	Easton Middle School - Accelerated Repair: Roof	\$1.85	Gale Associates, Inc.	\$21,680
Quabbin Regional	Ruggles Lane Elementary- Accelerated Repair: Roof, Windows	\$2.59	Simpson Gumpertz & Heger Inc.	\$42,100
Groton-Dunstable Regional	Groton-Dunstable Regional Middle School - Accelerated Repair: Roof	\$1.32	Russo Barr Associates, Inc.	\$24,300
Ayer-Shirley Regional	Ayer-Shirley Regional High School	\$44.37	WSP Flack + Kurtz	\$108,053

District	School	Estimated Const. Cost (million)	Commissioning Consultant	Contract Amount
Total		\$130.33 million	Total	
			\$637,977	

Design Development

Once a district has secured local funding and has entered into a Project Funding Agreement with the MSBA, it enters the Design Development phase. Currently there are 16 Core Program Projects in Design Development with a total estimated construction cost of \$655.1 million:

Elementary School Districts

Georgetown
 Newburyport (Bresnahan)
 Webster
 Williamsburg

Middle School Districts

Newburyport (Nock)
 Stoneham
 Springfield (Brookings)
 Wakefield

High School Districts

Assabet Valley Regional Technical
 Concord-Carlisle Regional
 Greater New Bedford Regional Technical
 Greenfield
 Monomoy Regional
 Southern Worcester Regional Technical
 Southwick-Tolland-Granville Regional
 West Bridgewater

Construction

When a district issues a Notice to Proceed, the project is advanced to the Construction Phase. Currently, there are 57 Projects in the Construction phase with a total estimated construction cost of \$2.9 billion: 13 Green Repair Projects, 43 Core Program Projects, and one Waitlist Project. The 43 Core Program Projects have a total estimated construction cost of \$2.78 billion and are listed below.

Elementary School Districts

Andover
 Arlington
 Ashburnham-Westminster Regional
 Douglas
 Fairhaven
 Lexington
 Marblehead
 Somerville
 Springfield (Dryden)
 Westfield
 Weston
 Winchester

Middle and Middle/High School Districts

Burlington
 Douglas
 Fall River
 Hingham
 Hudson
 Medway
 North Reading
 Oxford
 Quincy
 Rockland
 Saugus
 Sutton

High School Districts

Addition/Renovation
 Danvers
 Dracut
 Leominster
 Lynnfield
 Methuen
 Norfolk County Agricultural
 Norton
 Southeastern Regional Voc/Tech

New
 Easthampton
 Essex/North Shore Regional Voc/Tech
 Longmeadow
 Maynard
 Wilmington

Model
 Duxbury
 East Bridgewater
 Franklin
 Marshfield

Project Update

Green Repair – Schedule Extension Update

Eight of the 169 Green Repair Projects will not meet their anticipated construction completion deadline in 2012. Schedule delays can be attributed to bid protests, lead time for windows, and construction delays on site.

The MSBA granted each district a conditional extension to its Project Funding Agreement pending compliance with the following stipulations:

- The district must submit a detailed, revised construction timeline showing how the work will be completed at each school by no later than August 30, 2013;
- An Amendment to the Project Funding Agreement between the MSBA and the district must be executed to include the updated project schedule; and
- Any costs that may result from the district's requested extension of the construction schedule will be the sole responsibility of the district and are categorically ineligible for reimbursement by the MSBA.

Each of these projects has a revised construction schedule and will be complete by the beginning of the 2013-2014 school year. In no event has the extended schedule resulted in an increase to the estimated maximum Total Facilities Grant as authorized by the Board. Please note that staff reported on the schedule extensions for six of the projects shaded and shown below at previous Board meetings

District	School	Scope	Original Construction Completion Date	Updated Construction Completion Date	Reason for Schedule Extension
Brockton	Brockton High School	Windows and Roof	31-Dec-12	30-Aug-13	Construction fell behind schedule and the District did not want work being done in an occupied building. The roof work is complete.
Haverhill	Consentino Middle School	Windows and Boiler	31-Dec-12	31-May-13	Bid protests and lead times caused the window project to extend beyond the 2012 construction deadline. The boiler project is complete.
Haverhill	John G. Whittier Middle School	Windows	31-Dec-12	31-May-13	Bid protests and lead times caused the window project to extend beyond the 2012 construction deadline.
Lowell	Moody Elementary School	Windows	15-Aug-12	30-Aug-13	Construction fell behind schedule and the District did not want work being done in an occupied building.
Lowell	Washington Elementary School	Windows	15-Aug-12	30-Aug-13	Construction fell behind schedule and the District did not want work being done in an occupied building.
Shrewsbury	Spring Street Elementary School	Roof and Windows	24-Dec-12	31-Jan-13	The district issued a change order to add shrouds over the window wall unit ventilators.
Wachusett	Thomas Prince Elementary School	Roof	23-Mar-12	30-Apr-13	The district issued a change order to replace an existing skylight and due to lead times the work cannot be done until Spring 2013.
Westport	Westport High School	Roof	4-Sep-12	30-Apr-13	The district issued a change order to add scuppers to the roof and the work will be completed in Spring 2013.


Green Repair - Total Project Budget Update

Upon receiving the Board's approval of the Project Scope and Budget, the MSBA and participating districts enter into a Project Funding Agreement that establishes the Total Project Budget and the estimated maximum Total Facilities Grant for an approved project. Of the 169 grants authorized by the Board for the Green Repair Program, 11 projects have increased their Total Project Budgets due to acceptance of construction bids higher than the project estimates, or as a result of change orders issued on the project. In no event has the increase in budget resulted in an increase to the estimated maximum Total Facilities Grant as authorized by the Board. Please note that staff reported on the budget increases for the projects shaded and shown below at previous Board meetings. Westfield's Total Project Budget has increased since reported at the last Board meeting. Please also note that staff reported on the budget increases for 10 of the projects shaded and shown below at previous Board meetings (Arlington; Brockton - Hancock Elementary School and West Junior High School; Fitchburg; Florida; Hancock; Lexington; Narragansett; Pentucket; and Reading).

District	School Name	Scope	Project Funding Agreement		PFA Bid Amendment		Reason for Increase to Total Project Budget
			Total Project Budget	Total Maximum Facilities Grant	Total Project Budget	Total Maximum Facilities Grant	
Green Repair Program							
Arlington	M. Norcross Stratton Elementary School	Roof, Window, Boiler	\$2,445,395	\$739,336	\$2,445,395	\$739,336	Change Orders exhausted the construction contingency.
Brockton	Hancock Elementary School	Roof	\$2,292,164	\$1,814,937	\$2,422,742	\$1,814,937	District elected to accept the base bid that was higher than the approved budget. District appropriated additional funds to support overage.
Brockton	West Junior High School	Roof	\$2,742,386	\$2,171,001	\$3,069,905	\$2,171,001	District elected to accept the base bid that was higher than the approved budget. District appropriated additional funds to support overage.
Fitchburg	South Street Elementary School	Boiler	\$701,186	\$560,949	\$705,391	\$501,079	Change Orders exhausted the construction contingency.
Florida	Gabriel Abbott Memorial School	Roof	\$380,310	\$213,172	\$389,422	\$188,804	Project included \$80,153 in Change Orders that offset bid savings and exhausted the construction contingency.
Hancock	Hancock Elementary School	Roof/HVAC	\$277,450	\$125,740	\$400,805	\$125,740	District elected to accept the base bids in Phases 2 and 3 that were higher than the approved budget. District needs to appropriate the overage.
Lexington	Lexington High School	Roof	\$1,122,890	\$381,221	\$1,197,444	\$381,221	District elected to accept base bid and alternates. District appropriated additional funds to support overage.
Narragansett Regional	Philliptson Memorial Elementary School	Boiler	\$143,225	\$85,712	\$161,232	\$83,275	District elected to accept the base bid that was higher than the approved budget. District appropriated additional funds to support overage.
Pentucket Regional	Dr. John C. Page Elementary School	Roof, Window, Boiler	\$3,148,424	\$1,618,920	\$3,272,630	\$1,618,920	District elected to accept the base bid that was higher than the approved budget. District appropriated additional funds to support overage.
Reading	Birch Meadow Elementary School	Window	\$735,846	\$347,393	\$787,640	\$347,393	District elected to accept the base bid that was higher than the approved budget. Town Accountant certified that the FY2011 School Committee Operating Budget had an appropriation and encumbrance for the additional costs of the project.
Westfield	Westfield Vocational Technical High School	Roof, Window, Boiler	\$8,442,762	\$5,296,989	\$8,895,495	\$5,296,989	District elected to accept the base bid that was higher than the approved budget. District also approved an amendment to its Designer contract which increased the fee. District appropriated additional funds to support overage.


Status of Green Repair Program

169 projects participating in the Green Repair Program have received authorization to enter into a PFA, totaling \$366,647,226 in Total Project Costs and \$222,885,258 in MSBA grants.

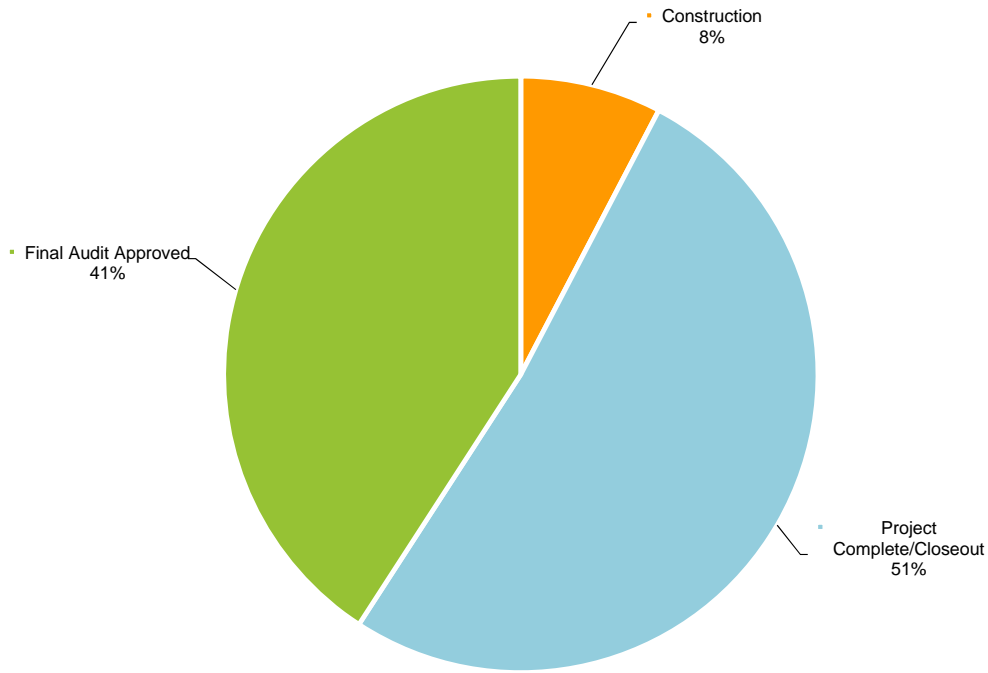

Status of Accelerated Repair Program

Currently there are a total of 23 districts, representing 33 projects, in the Accelerated Repair Program. All projects are under contract with consultants and have advanced into the preferred schematic or project scope and budget phases. At the January 30th meeting of the Board of Directors, MSBA staff will recommend a Project Funding Agreement (“PFA”) with 10 districts, representing 17 projects totaling \$31,061,270 in Total Project Costs. With the Board’s approval, 31 projects will have been authorized to enter into a PFA, totaling \$52,726,540 in Total Project Costs and \$33,004,220 in MSBA Total Facilities Grant funding.

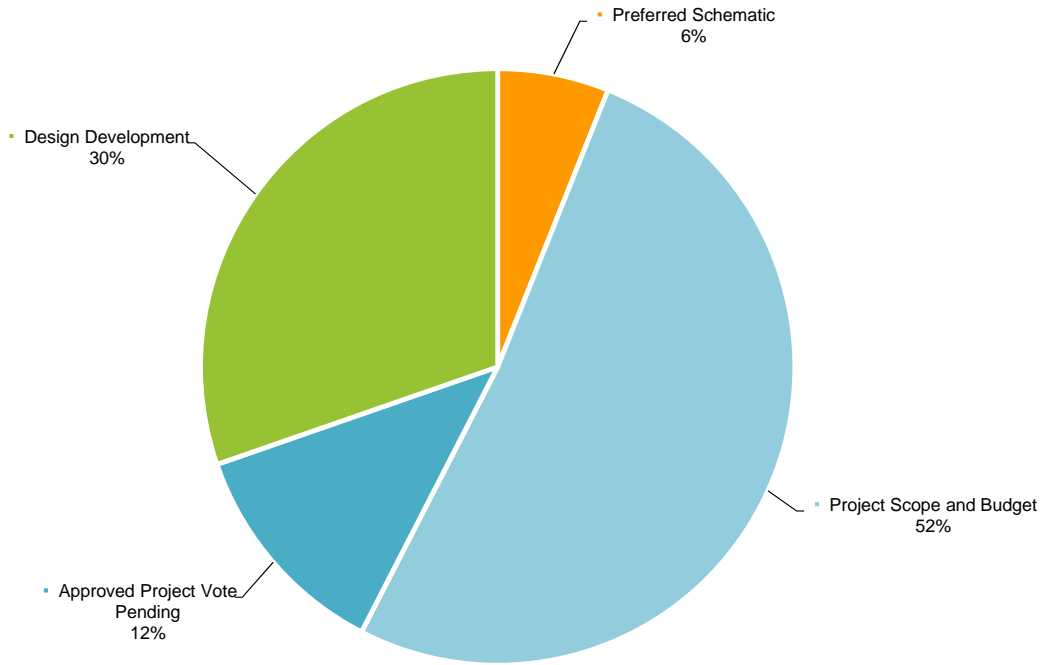

2012-2013 Eligibility Period Status

January 9, 2013

6 Projects in Eligibility Period




District	2012											2013							
	Mar	April	May	June	July	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	April	May	June	July	Aug	Sept
Brookline Devotion ES																			
Worcester Nelson Place ES																			
Georgetown Middle/High School																			
Holyoke Lt. McMahon ES																			
Scituate Gates IS																			
Woburn Wyman ES																			
District	Mar	April	May	June	July	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	April	May	June	July	Aug	Sept

*This project is a requirement in the Project Scope and Budget Agreement for the Penn Brook Elementary School. Therefore, the District's Maintenance Documentation and Enrollment Certification were completed prior to invitation to the Eligibility Period.

Project Status | January 9, 2013

Core Program:	97
Waitlist:	1
Green Repair:	13
Accelerated Repair:	33
Science Lab Initiative:	8
Project Complete / Substantial Completion:	49
Closeout:	79
Final Audit Approved:	41
Projects To be Removed	4
Total Projects:	325

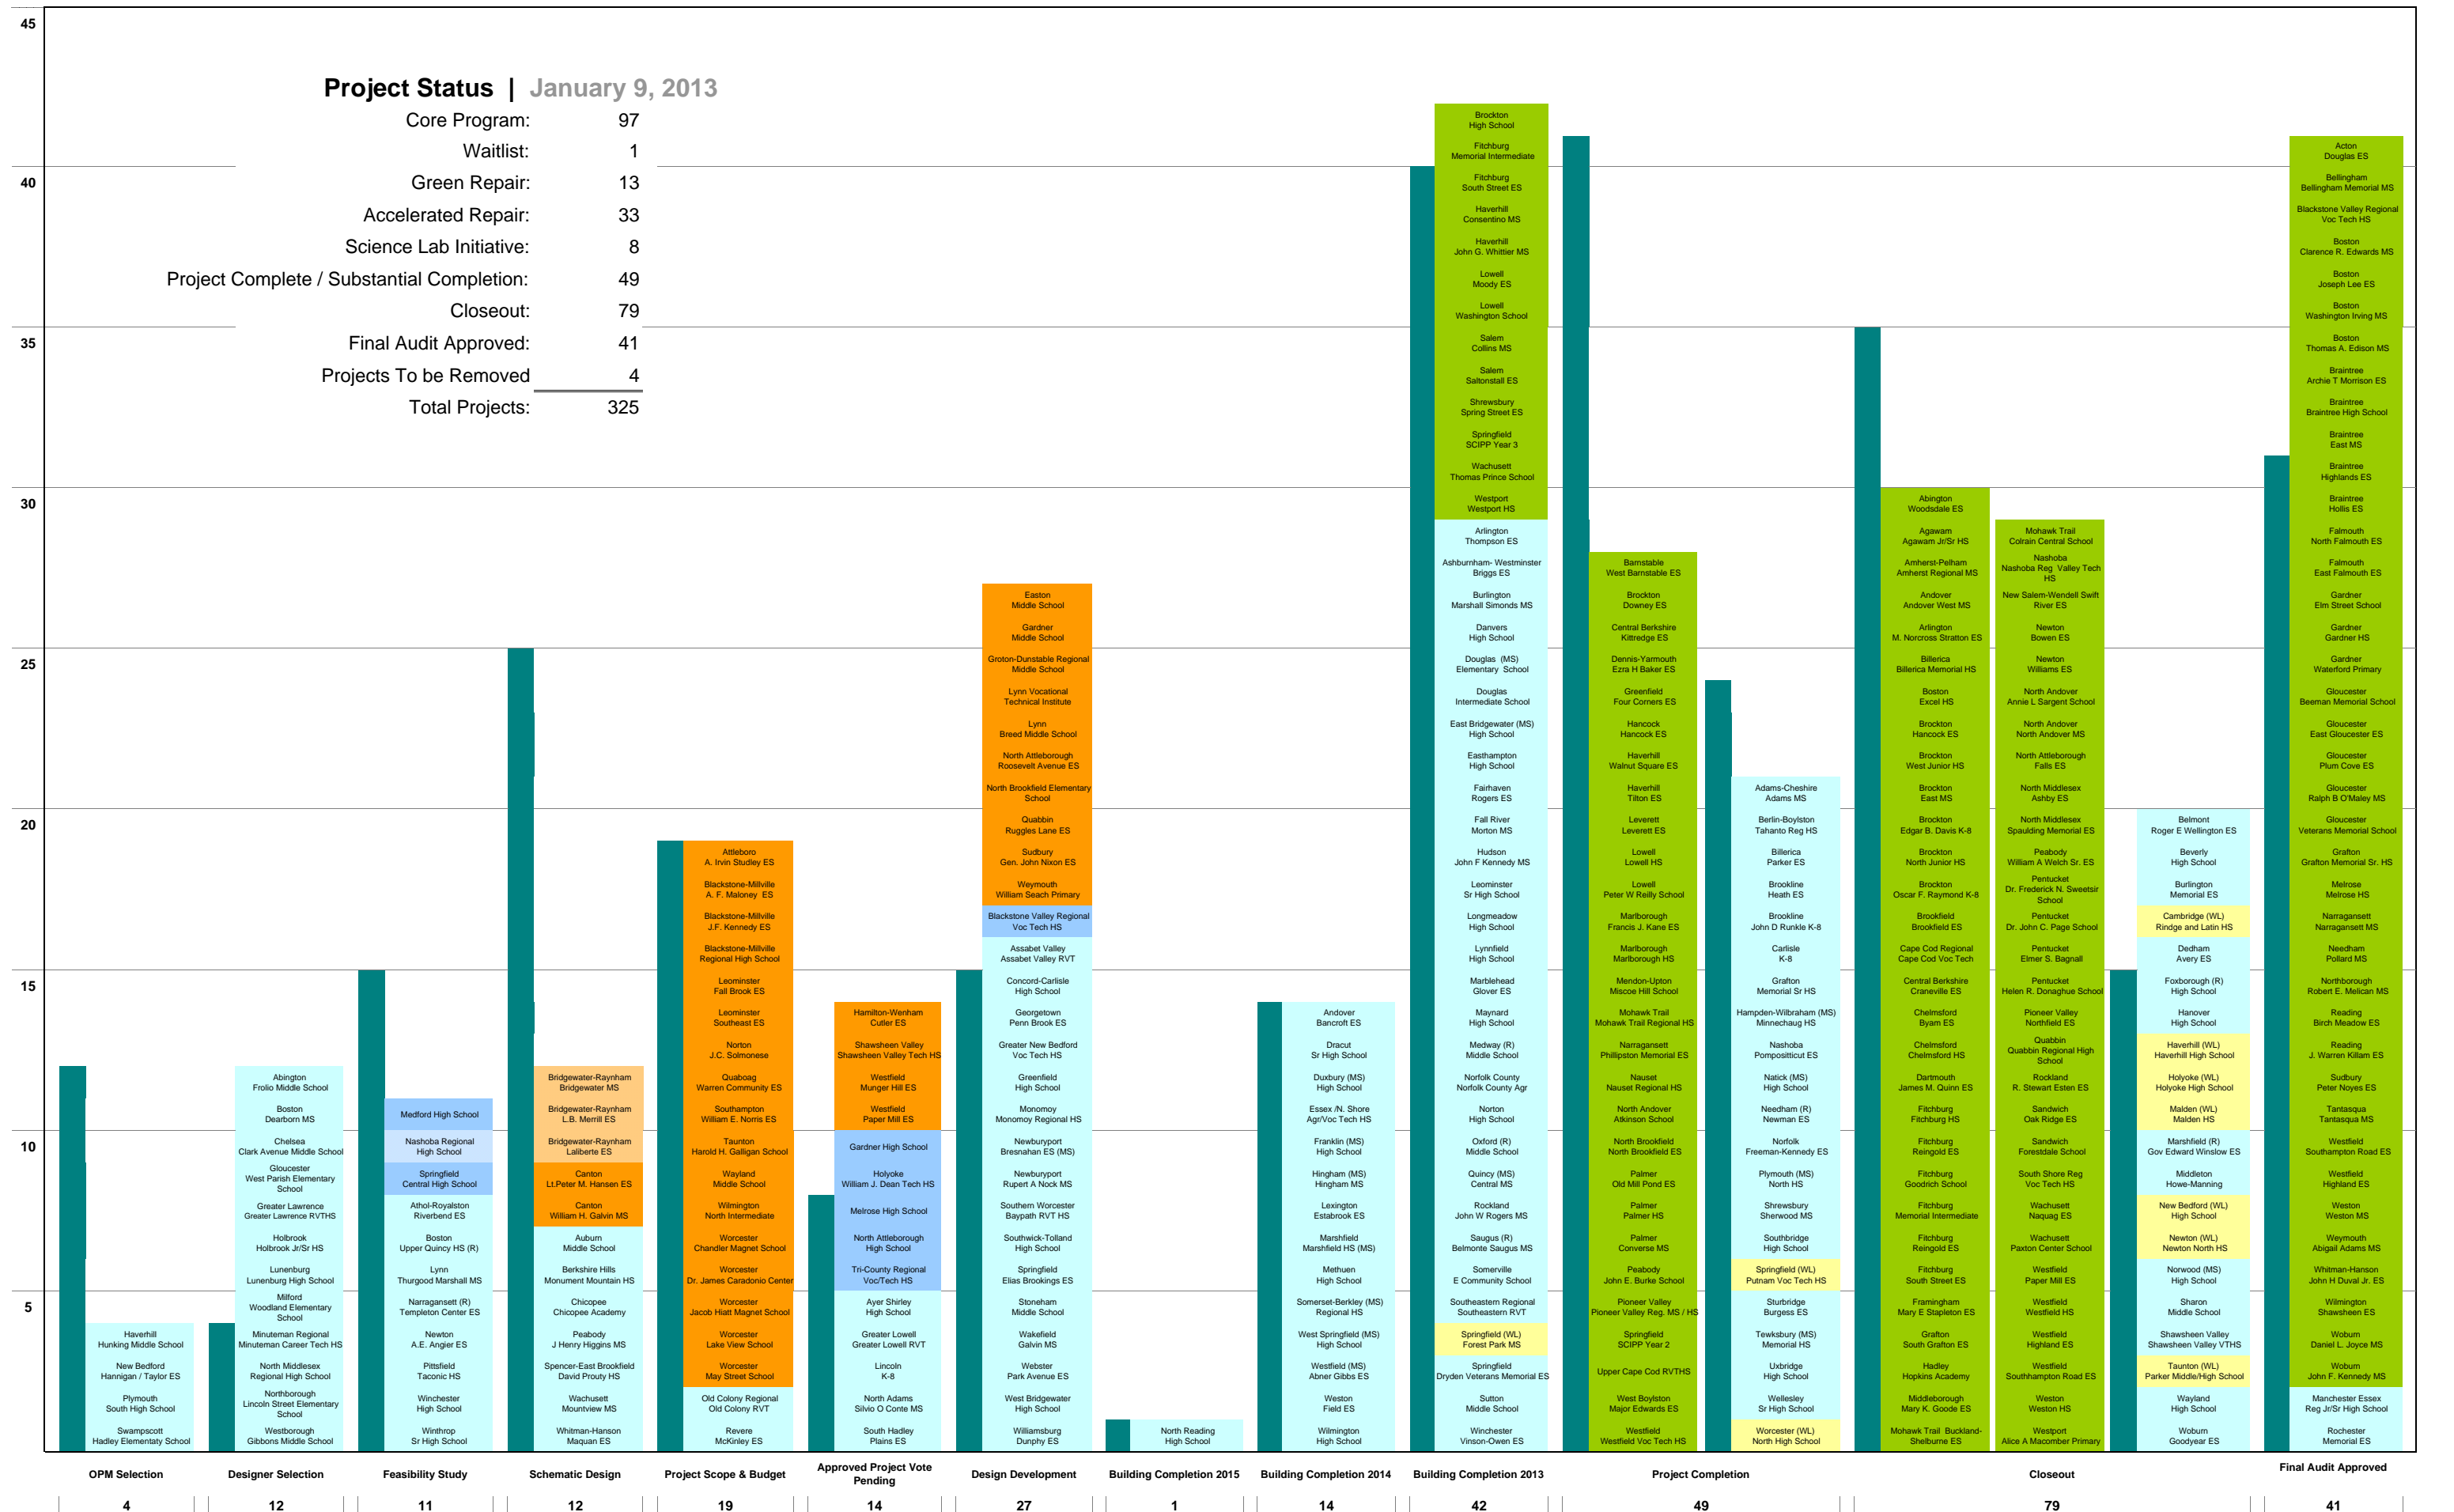

PROJECT STATUS

325
Total Active Projects

- Green Repair Program
- Accelerated Repair Program
- Accelerated Repair Program - To Be Removed
- New Program Project
- Science Lab Initiative Project
- Science Lab Initiative Project - To Be Removed
- Waitlist Projects
- Capital Pipeline Status Presented at November 14, 2012 Board of Directors Meeting

2013 Estimated Bid Dates

Note bid dates are **Estimates ONLY**. Please contact Districts for exact information.

Total Project Budget denotes total District costs and does not denote the basis of the MSBA Total Facilities Grant.

■ - Denotes bid phase in progress or complete
 ■ - Denotes estimated bid dates
 ■ - Denotes estimated GMP dates

DISTRICT	DESIGN BASIS FOR ENROLLMENT	PROJECT BUDGET <small>Shown in Millions</small>	CONSTRUCTION BUDGET <small>Shown in Millions</small>	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC
<small>*Projects Considering the CM @ Risk Method</small>															
*LEXINGTON	540	\$40.8	31.1	Lexington Estabrook ES New Construction : Filed-Sub Bids rcv'd 12/19. GMP Targeted January.											
NEWBURYPORT	660	\$37.3	\$31.1	Newburyport Bresnahan ES New Construction: Filed-Sub Bids Due 1/16. G.C Bids Due 1/30. NTP Targeted February.											
MONOMOY REGIONAL SCHOOL	700	\$64.7	\$52.9	Monomoy Regional HS New Construction: Filed-Sub Bids Due 1/9. G.C Bids Due 1/23. NTP Targeted February.											
*STONEHAM	775	\$38.6	\$32.0	Stoneham MS New Construction: Filed-Sub Bids Due 1/17. GMP Targeted February.											
*WILMINGTON	960	\$82.7	\$64.4	Wilmington HS New Construction: Filed-Sub Bids Due 1/18. GMP Targeted February.											
ASSABET VALLEY	1000	\$62.4	\$50.8	Assabet Valley Regional HS Repair: Filed-sub Bids Due 2/11. G.C. due 2/20. NTP Targeted March.											
WILLIAMSBURG	170	\$12.0	\$9.6	Williamsburg Anne T. Dunphy IS Addition/Renovation: Filed-Sub Bids Due 2/12. G.C. Due 2/26. NTP Targeted March.											
*NEWBURYPORT	845	\$26.9	\$21.8	Newburyport Nock ES Renovation: Filed-Sub Bids Due 3/8. GMP Targeted March.											
*GREENFIELD	585	\$63.4	\$52.9	Greenfield HS New Construction: Filed-Sub Bids Due 3/12. GMP Targeted April.											
*NORTH READING	1370	\$103.4	\$86.3	N.Reading HS New Construction: Filed-Sub Bids Due 2/8. GMP Targeted February.											
*ANDOVER	680	\$44.7	\$34.5	Andover Bancroft ES New Construction: Filed-Sub Bids rcv'd 9/22. Non Filed-Sub Bids rcv'd 11/2. GMP Targeted April.											
*WAKEFIELD	1070	\$70.1	\$59.7	Wakefield Galvin MS New Construction: Filed-Sub Bids Due 5/7. GMP Targeted May.											
WEBSTER	720	\$44.9	\$35.8	Webster Park Ave ES New Construction: Filed-Sub Bids Due 5/21. G.C. Bids Due 6/4. NTP Targeted June.											
*CONCORD/CARLISLE	1225	\$92.6	\$71.4	Concord/Carlisle HS New Construction: Filed-Sub Bids Due 7/5. GMP Targeted July.											
SOUTHWICK-TOLLAND-GRANVILLE PowderMill IS	545	\$18.5	\$14.8	PowderMill IS Repair: Filed-Sub Bids Due 4/30. G.C. Due 5/14. NTP Targeted May.											
SOUTHWICK-TOLLAND-GRANVILLE Woodland ES	400	\$9.7	\$7.3	Woodland ES Repair: Filed-Sub Bids Due 4/30. G.C. Due 5/14. NTP Targeted May.											
SOUTHWICK-TOLLAND-GRANVILLE STG Regional HS	790	\$40.7	\$31.4	STG MS/HS Addition/Renovation: Filed-Sub Bids Due 7/10. G.C. Due 7/31. NTP Targeted September.											
GREATER NEW BEDFORD	2060	\$17.1	\$13.7	GNBRVT HS Add/Reno: Filed-Sub Bids Due 8/7. G.C. Due 8/14. NTP Targeted August.											
*SPRINGFIELD	320	\$27.9	\$22.7	Springfield Brookings ES New Construction: Filed-Sub Bids Due 8/21. GMP Targeted September.											
WEST BRIDGEWATER	625	\$63.7	\$49.7	West Bridgewater MS/HS New Construction: Filed-Sub Bids Due 8/30. G.C. Due 9/16. NTP Targeted September.											
GEORGETOWN	770	\$46.2	\$37.0	Penn Brook ES New Construction: Filed-Sub Bids Due 9/27. G.C. Due 10/17. NTP Targeted October.											
*AYER-SHIRLEY	495	\$56.5	\$44.4	ASRHS Add/Reno: Filed-Sub Bids Due 10/4. GMP Targeted October.											
Subtotal	17,305	\$1,065	\$855.3												
GRAND TOTAL	17,305	\$1,065	\$855.3												
Number of Construction-Related Employment Opportunities Created			4,276												

2014 Estimated Bid Dates

Note bid dates are **Estimates ONLY**. Please contact Districts for exact information.

Total Project Budget denotes total District costs and does not denote the basis of the MSBA Total Facilities Grant.

■ - Denotes bid phase in progress or complete
 ■ - Denotes estimated bid dates
 ■ - Denotes estimated GMP dates

DISTRICT <small>*Projects Considering the CM @ Risk Method</small>	DESIGN BASIS FOR ENROLLMENT	PROJECT BUDGET <small>Shown in Millions</small>	CONSTRUCTION BUDGET <small>Shown in Millions</small>	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC
GREATER LOWELL	1990	\$65.3	\$53.2				GRTL RVTHS Repair: Filed-Sub Bids Due 2/19. GC. Bids Due 3/12. NTP Targeted April.								
Subtotal	1,990	\$65	\$53.2												
GRAND TOTAL	1,990	\$65	\$53.2												
Number of Construction-Related Employment Opportunities Created			266												



MSBA ID	District	School	Phase	Project Scope	Procurement Type	OPM	Designer	Cx Company	CMGC
20080010405	Abington	Frolio Middle School	Designer Selection			Knight, Bagge & Anderson Inc.	-		-
201100010015G	Abington	Woodsdale	Closeout	Repair - Accelerated	DBB	RF Walsh Collaborative Partners	Gale Associates, Inc.	Russo Barr Associates, Inc.	Lockheed Window Corporations
201000020020G	Acton	C. T. Douglas Elementary School	Final Audit Approved	Repair - Accelerated	DBB	-	CBI Consulting, Inc.		Gibson Roofs, Inc.
200806030305	Adams-Cheshire	Adams Memorial Middle School	Project Completion	Addition / Renovation	CM@R	URS Corporation	Tessier Associates, Inc.	Strategic Building Solutions, LLC	Gilbane Building Company
201100050405G	Agawam	Agawam Junior/Senior High	Closeout	Repair - Accelerated	DBB	Municipal Building Consultants, Inc.	CSS Architects Incorporated	Building Enclosure Associates	-
201106050405G	Amherst-Pelham	Amherst Regional Middle School	Closeout	Repair - Accelerated	DBB	Strategic Building Solutions, LLC	Bradley Architects, Inc.	Russo Barr Associates, Inc.	R&R Window Contractors, Inc.
201100090310G	Andover	Andover West Middle	Closeout	Repair - Accelerated	DBB	Skanska USA Building, Inc	Russo Barr Associates, Inc.	Simpson Gumpertz & Heger Inc.	Eagle Rivet Roof Services Corporation
200800090003	Andover	Bancroft Elementary School	Construction	New Construction	CM@R	Dore & Whittier Management Partners, Inc.	Symmes Maini & McKee Associates, Inc.	Sebesta Blomberg & Associates, Inc.	Skanska USA Building, Inc.
201100100055G	Arlington	M Norcross Stratton	Closeout	Repair - Accelerated	DBB	PMA Construction Services	Turowski2 Architecture, Inc.		Federal Construction Corp.] Unicon Inc.
200900100050	Arlington	Thompson Elementary School	Construction	New Construction	DBB	PMA Construction Services	HMFH Architects, Inc.	Consulting Engineering Services, LLC	G & R Construction, Inc.
200806100025	Ashburnham-Westminster	John R. Briggs Elementary School	Construction	New Construction	CM@R	STV Incorporated	Lamoureux Pagano & Associates, Inc.	Foreman Building Commissioning, LP	Consigli Construction Company, Inc.
200908010605	Assabet Valley	Assabet Valley Regional Technical High School	Design Development		DBB	Strategic Building Solutions, LLC	Design Partnership of Cambridge, Inc.	Symmes, Maini & McKee Associates	-
200906150020	Athol-Royalston	Riverbend School	Feasibility Study	Repair- Accelerated		Symmes Maini & McKee Associates, Inc.	Mount Vernon Group Architects, Inc.		-
201200160001	Attleboro	A. Irvin Studley Elementary School	Project Scope & Budget	Repair - Accelerated		Tishman Construction Corporation of MA	Gale Associates, Inc.		
200800170305	Auburn	Auburn Middle School	Schematic Design	New Construction		Skanska USA Building, Inc	Lamoureux Pagano & Associates, Inc.		-
9999	Ayer-Shirley	Ayer-Shirley Regional Middle/High School	Approved Project Vote Pending	Addition / Renovation		Dore and Whittier Architects, Inc.	Symmes Maini & McKee Associates, Inc.	WSP Flack + Kurtz	-
201100200005G	Barnstable	West Barnstable Elementary School	Project Completion	Repair - Accelerated	DBB	PMA Construction Services	Gale Associates, Inc.	CBI Consulting Inc.	Paul J. Rogan Co., Inc.
201100250315G	Bellingham	Bellingham Memorial Middle School	Final Audit Approved	Repair - Accelerated	DBB	Daedalus Projects Inc	Richard D. Kimball Company, Inc.	WSP Flack + Kurtz	General Air Conditioning & Heating, Inc.
200800260035	Belmont	Roger Wellington Elementary School	Closeout	New Construction	CM@R	PMA Construction Services	Jonathan Levi Architects LLC	Strategic Building Solutions, LLC	Skanska USA Building, Inc.
201006180505	Berkshire Hills	Monument Mountain Regional High School	Schematic Design			Strategic Building Solutions, LLC	Symmes Maini & McKee Associates, Inc.		-
200806200505	Berlin-Boylston	Tahanto Regional High School	Project Completion	New Construction	DBB	PMA Construction Services	HMFH Architects, Inc.	Strategic Building Solutions, LLC	CTA Construction Co., Inc.
200800300505	Beverly	Beverly HS	Closeout	Addition / Renovation		HEERY	Mount Vernon Group Architects, Inc.		CTA Construction Co., Inc.
200800310015	Billerica	Parker Elementary School	Project Completion	New Construction	DBB	Joslin, Lesser + Associates Inc.	Symmes Maini & McKee Associates, Inc.	Sebesta Blomberg & Associates, Inc.	CTA Construction Co., Inc. RS Hurford
201100310505G	Billerica	Memorial High School	Closeout	Repair		Municipal Building Consultants, Inc.	Knight, Bagge & Anderson, Inc.	Building Enclosure Associates	
201108050605G	Blackstone Valley Reg	Blackstone Valley Reional Voc Tech High School	Final Audit Approved	Repair - Accelerated	DBB	Strategic Building Solutions, LLC	Reinhardt Associates, Inc.	Cannon Design	Greenwood Industries, Inc.
201208050605	Blackstone Valley Reg	Blackstone Valley	Design Development	Science Lab		Compass Project Management, Inc.	Flansburgh Associates, Inc.	Horizon Engineering Associates, LLP	-
201206220015	Blackstone Valley - Millville	A.F. Maloney Elementary School	Project Scope & Budget	Repair- Accelerated					
201206220008	Blackstone Valley - Millville	J.F. Kennedy Elementary School	Project Scope & Budget	Repair- Accelerated					
201206220505	Blackstone Valley - Millville	Regional High School	Schematic Design	Repair - Accelerated				Cannon Design	
201100350430G	Boston	Clarence R Edwards Middle School	Final Audit Approved	Repair - Accelerated	DBB	Daedalus Projects Inc	BLW Engineers, Inc.	Rist-Frost-Shumway Engineering, P.C.	-
201100350522G	Boston	Excel High School	Closeout	Repair - Accelerated	DBB	Daedalus Projects Inc	BLW Engineers, Inc.	Simpson Gumpertz & Heger Inc.	-
201000350074	Boston	Henry Dearborn Middle School	Designer Selection			Compass Project Management, Inc.	-		-
201100350183G	Boston	Joseph Lee Elementary School	Final Audit Approved	Repair - Accelerated	DBB	Daedalus Projects Inc	BLW Engineers, Inc.	Simpson Gumpertz & Heger Inc.	Gale Associates, Inc.



MSBA ID	District	School	Phase	Project Scope	Procurement Type	OPM	Designer	Cx_Company	CMGC
201000350565	Boston	Quincy Upper School	Final Audit Approved			Maureen Anderson - City Employee	HMFH Architects, Inc.		-
201100350425G	Boston	Thomas A Edison Jr High School	Final Audit Approved	Repair - Accelerated	DBB	Daedalus Projects Inc	BLW Engineers, Inc.	Simpson Gumpertz & Heger Inc.	-
201100350445G	Boston	Washington Irving Middle School	Closeout	Repair - Accelerated	DBB	Daedalus Projects Inc	Gale Associates, Inc.	Simpson Gumpertz & Heger Inc.	-
201000400033G	Braintree	Archie T Morrison Elementary School	Final Audit Approved	Repair - Accelerated	DBB	RF Walsh Collaborative Partners	Habeeb & Associates Architects, Inc.	Cannon Design	Modern Glass & Aluminum, Inc.
201000400505G	Braintree	Braintree High School	Final Audit Approved	Repair - Accelerated	DBB	RF Walsh Collaborative Partners	Habeeb & Associates Architects, Inc.	Cannon Design	Gibson Roofs, Inc.
201000400305G	Braintree	East Middle School	Final Audit Approved	Repair - Accelerated	DBB	RF Walsh Collaborative Partners	Habeeb & Associates Architects, Inc.	Cannon Design	Modern Glass & Aluminum, Inc.
201000400015G	Braintree	Highlands Elementary School	Final Audit Approved	Repair - Accelerated	DBB	RF Walsh Collaborative Partners	Habeeb & Associates Architects, Inc.	Cannon Design	Modern Glass & Aluminum, Inc.
201000400005G	Braintree	Hollis Elementary School	Final Audit Approved	Repair - Accelerated	DBB	RF Walsh Collaborative Partners	Habeeb & Associates Architects, Inc.	Cannon Design	Modern Glass & Aluminum, Inc.
201206250320	Bridgewater-Raynham	Bridgewater Middle School	Schematic Design	Repair - Accelerated					
201206250020	Bridgewater-Raynham	L.B. Merrill Elementary School	Schematic Design	Repair - Accelerated					
201206250050	Bridgewater-Raynham	Laliberte Elementary School	Schematic Design	Repair - Accelerated					
201100440505G	Brockton	Brockton High School	Construction	Repair - Accelerated	DBB	Skanska USA Building, Inc	CSS Architects Incorporated	Simpson Gumpertz & Heger Inc.	Gibson Roofs, Inc.
201100440110G	Brockton	Downey Elementary School	Project Completion	Repair - Accelerated	DBB	Skanska USA Building, Inc	CSS Architects Incorporated	Simpson Gumpertz & Heger Inc.	Built-up Roofing Systems LLC
201100440405G	Brockton	East Junior High School	Closeout	Repair - Accelerated	DBB	Skanska USA Building, Inc	CSS Architects Incorporated	Rist-Frost-Shumway Engineering, P.C.	Reliable Roofing and Sheet Metal, LLC
201100440023G	Brockton	Edgar B Davis	Closeout	Repair - Accelerated	DBB	Skanska USA Building, Inc	CSS Architects Incorporated	Simpson Gumpertz & Heger Inc.	Reliable Roofing and Sheet Metal, LLC
201100440045G	Brockton	Hancock Elementary School	Closeout	Repair - Accelerated	DBB	Skanska USA Building, Inc	CSS Architects Incorporated	Simpson Gumpertz & Heger Inc.	Reliable Roofing and Sheet Metal, LLC
201100440410G	Brockton	North Junior High School	Closeout	Repair - Accelerated	DBB	Skanska USA Building, Inc	CSS Architects Incorporated	Rist-Frost-Shumway Engineering, P.C.	Arden Engineering Constructors, LLC
201100440078G	Brockton	Oscar F Raymond K-8	Closeout	Repair - Accelerated	DBB	Skanska USA Building, Inc	CSS Architects Incorporated	Simpson Gumpertz & Heger Inc.	Built-up Roofing Systems LLC
201100440420G	Brockton	West Junior High School	Closeout	Repair - Accelerated	DBB	Skanska USA Building, Inc	CSS Architects Incorporated	Simpson Gumpertz & Heger Inc.	Reliable Roofing and Sheet Metal, LLC
201100450005G	Brookfield	Brookfield Elementary School	Closeout	Repair - Accelerated	DBB	Diversified Project Management	Habeeb & Associates Architects, Inc.	Cannon Design	Northeast Energy Control Systems
201100460015	Brookline	Edward Devotion	Eligibility Period						
201000460025	Brookline	Heath Elementary School	Project Completion	Addition / Renovation	DBB	Town of Brookline Building Department	Miller Dyer Spears Inc.	Consulting Engineering Services, LLC	Nauset Construction Corporation
200800460045	Brookline	John D. Runkle School	Project Completion	Addition / Renovation	DBB	Town of Brookline Building Department	Design Partnership of Cambridge, Inc.	Consulting Engineering Services, LLC	G & R Construction, Inc.
201000480303	Burlington	Marshall Simonds Middle School	Construction	Addition / Renovation	DBB	Construction Monitoring Services, Inc.	Knight, Bagge & Anderson, Inc.	RDK Engineers	CTA Construction Co., Inc.
200800480015	Burlington	Memorial Elementary School	Closeout	New Construction	DBB	Construction Monitoring Services, Inc.	Knight, Bagge & Anderson, Inc.	Consulting Engineering Services, LLC	CTA Construction Co., Inc.
W20024323	Cambridge	Cambridge Rindge and Latin High School	Closeout	Addition / Renovation	DBB	-	HMFH Architects, Inc.		W. T. Rich Company Inc.
201200500012	Canton	Lt. Peter M. Hansen	Schematic Design	Repair - Accelerated		Vertex Construction Services	CSS Architects Incorporated		
201200500305	Canton	William H. Galvin Middle School	Schematic Design	Repair - Accelerated		Vertex Construction Services	CSS Architects Incorporated		
201008150605G	Cape Cod Region Voc Tech	Cape Cod Region Voc Tech	Closeout	Repair - Accelerated	DBB	URS Corporation	Garcia Galuska DeSousa Consulting Engineers Inc.	Fitzemeyer & Tocci Associates, Inc.	-
200800510025	Carlisle	Carlisle School	Project Completion	Addition / Renovation	DBB	Daedalus Projects Inc	HMFH Architects, Inc.	Horizon Engineering Associates, LLP	H.V. Collins Co., Inc.
201106350025G	Central Berkshire	Craneville Elementary School	Closeout	Repair - Accelerated	DBB	Daedalus Projects Inc	Bradley Architects, Inc.	Strategic Building Solutions, LLC	Titan Roofing, Inc.
201106350035G	Central Berkshire	Kittredge Elementary School	Project Completion	Repair - Accelerated	DBB	Daedalus Projects Inc	Bradley Architects, Inc.	Strategic Building Solutions, LLC	A.J. Schnopp Jr., Construction, Inc. Alpha Contracting Associates, Inc.
201100560030G	Chelmsford	Byam Elementary School	Closeout	Repair - Accelerated	DBB	Vertex Construction Services	Russo Barr Associates, Inc.	Simpson Gumpertz & Heger Inc.	S.O.M. Construction Ent., Inc.



MSBA ID	District	School	Phase	Project Scope	Procurement Type	OPM	Designer	Cx_Company	CMGC
201100560505G	Chelmsford	Chelmsford High School	Closeout	Repair - Accelerated	DBB	Vertex Construction Services	Russo Barr Associates, Inc.	Simpson Gumpertz & Heger Inc.	Lockheed Window Corporations
200800570050	Chelsea	Clark Avenue School	Designer Selection			Pinck & Co., Inc.	-		-
200900610021	Chicopee	Chicopee Academy	Schematic Design			Arcadis	Caolo & Bieniek Associates, Inc.		-
200906400505	Concord-Carlisle	Concord-Carlisle Regional High School	Design Development	New Construction	CM@R	KV Associates, Inc.	OMR Architects, Inc.	Strategic Building Solutions, LLC	Turner Construction Company
200800710505	Danvers	Danvers High School	Construction	Addition / Renovation	DBB	Construction Monitoring Services, Inc.	DiNisco Design Partnership, Limited	Turner Facilities Management Solutions	Bacon Construction Co, Inc.
201100720040G	Dartmouth	James M. Quinn Elementary School	Closeout	Repair - Accelerated	DBB	Vertex Construction Services	Russo Barr Associates, Inc.	Gale Associates, Inc.	Capeway Roofing Systems, Inc.
200800730010	Dedham	Avery Elementary School	Closeout	New Construction	CM@R	Construction Monitoring Services, Inc.	Dore & Whittier Architects, Inc.	WSP Flack + Kurtz	Consigli Construction Company, Inc.
201006450005G	Dennis-Yarmouth	Ezra Baker Elementary School	Project Completion	Repair - Accelerated	DBB	STV Incorporated	Knight, Bagge & Anderson, Inc.	CBI Consulting Inc.	Antonelli Construction Co., Inc.
200800770010	Douglas	Douglas Elementary School	Construction	New Construction		HEERY	DiNisco Design Partnership, Limited	Consulting Engineering Services, LLC	CTA Construction Co., Inc.
200800770100G	Douglas	Douglas Intermediate Elementary School	Construction	Repair - Accelerated	DBB	HEERY	DiNisco Design Partnership, Limited	Consulting Engineering Services, LLC	CTA Construction Co., Inc.
200800790505	Dracut	Dracut Senior High School	Construction	Addition / Renovation	DBB	RF Walsh Collaborative Partners	Mount Vernon Group Architects, Inc.	RDK Engineers	CTA Construction Co., Inc.
201000820505	Duxbury	Duxbury High School	Construction	New Construction	CM@R	KV Associates, Inc.	Mount Vernon Group Architects, Inc.	WSP Flack + Kurtz	Dimeo Construction Company
200900830505	East Bridgewater	East Bridgewater High School	Construction	New Construction	DBB	RF Walsh Collaborative Partners	Ai3 Architects LLC	Foreman Building Commissioning, LP	Fontaine Brothers, Inc.
200800860505	Easthampton	Easthampton High School	Construction	New Construction	DBB	Strategic Building Solutions, LLC	Caolo & Bieniek Associates, Inc.	Consulting Engineering Services, LLC	Fontaine Brothers, Inc.
201200880405	Easton	Easton Junior High School	Design Development	Repair - Accelerated		PMA Construction Services	Russo Barr Associates, Inc.	Gale Associates, Inc.	-
200809130705	Essex Agr Tech	Essex Agricultural and Technical High School	Construction	New Construction	CM@R	PMA Construction Services	Design Partnership of Cambridge, Inc.	Turner Facilities Management Solutions	Gilbane Building Company
200800940020	Fairhaven	Rogers Elementary School	Construction	New Construction	DBB	Daedalus Projects Inc	HMFH Architects, Inc.	Consulting Engineering Services, LLC	-
200900950315	Fall River	James Madison Morton Middle School	Construction	New Construction	DBB	Maguire Group Inc.	Mount Vernon Group Architects, Inc.	Sebesta Blomberg & Associates, Inc.	J & J Contractors, Inc.
201100960005G	Falmouth	East Falmouth Elementary School	Final Audit Approved	Repair - Accelerated	DBB	No OPM	Keenan and Kenny Architects, Ltd.	Gale Associates, Inc.	Meadows Construction Company LLC
201100960030G	Falmouth	North Falmouth Elementary School	Final Audit Approved	Repair - Accelerated	DBB	No OPM	Keenan and Kenny Architects, Ltd.	Gale Associates, Inc.	Meadows Construction Company LLC
201100970505G	Fitchburg	Fitchburg High School	Closeout	Repair - Accelerated	DBB	Compass Project Management, Inc.	BLW Engineers, Inc.	RDK Engineers	Ostrow Electrical Co., Inc.
201000970025G	Fitchburg	Goodrich Kindergarten	Closeout	Repair - Accelerated	DBB	Compass Project Management, Inc.	BLW Engineers, Inc.	RDK Engineers	CAM HVAC & Construction, Inc.
200900970048G	Fitchburg	Memorial Intermediate	Closeout	Repair - Accelerated	DBB	Compass Project Management, Inc.	BLW Engineers, Inc.	RDK Engineers	E. Amanti & Sons, Inc.
201100970048G	Fitchburg	Memorial Intermediate	Construction	Repair - Accelerated	DBB	Compass Project Management, Inc.	Knight, Bagge & Anderson, Inc.	Simpson Gumpertz & Heger Inc.	Lockheed Window Corporations
201100970043G	Fitchburg	Reingold Elementary School	Closeout	Repair - Accelerated	DBB	Compass Project Management, Inc.	Knight, Bagge & Anderson, Inc.	RDK Engineers	Lockheed Window Corporations
200900970043G	Fitchburg	Reingold Elementary School	Closeout	Repair - Accelerated	DBB	Compass Project Management, Inc.	BLW Engineers, Inc.	Simpson Gumpertz & Heger Inc.	E. Amanti & Sons, Inc.
200900970060G	Fitchburg	South Street Elementary	Closeout	Repair - Accelerated	DBB	Compass Project Management, Inc.	BLW Engineers, Inc.	RDK Engineers	CAM HVAC & Construction, Inc.
201100970060G	Fitchburg	South Street Elementary	Construction	Repair - Accelerated	DBB	Compass Project Management, Inc.	Knight, Bagge & Anderson, Inc.	Simpson Gumpertz & Heger Inc.	Lockheed Window Corporations
200800990505	Foxborough	Foxborough High School	Closeout	Repair - Major	DBB	Construction Monitoring Services, Inc.	Kaestle Boos Associates, Inc.	Consulting Engineering Services, LLC	CTA Construction Co., Inc.
201101000045G	Framingham	Mary E Stapleton Elementary School	Closeout	Repair - Accelerated	DBB	Bargmann, Flendrie & Archetype, Inc.	Russo Barr Associates, Inc.	CBI Consulting Inc.	-
200901010505	Franklin	Franklin High School	Construction	New Construction	DBB	Daedalus Projects Inc	Ai3 Architects LLC	Consulting Engineering Services, LLC	-
201101030001G	Gardner	Elm Street School	Final Audit Approved	Repair - Accelerated	DBB	P3 Inc.	Knight, Bagge & Anderson, Inc.	Building Enclosure Associates	Reliable Roofing and Sheet Metal, LLC
201101030505G	Gardner	Gardner High School	Final Audit Approved	Repair - Accelerated	DBB	P3 Inc.	Knight, Bagge & Anderson, Inc.	Building Enclosure Associates	Reliable Roofing and Sheet Metal, LLC



MSBA ID	District	School	Phase	Project Scope	Procurement Type	OPM	Designer	Cx Company	CMGC
201201030505	Gardner	Gardner High School	Approved Project Vote Pending	Science Lab		Pinck & Co., Inc.	Lamoureux Pagano & Associates, Inc.	Fitzemeyer & Tocci Associates, Inc.	-
201201030405	Gardner	Gardner Middle School	Design Development	Repair - Accelerated		Leftfield, LLC	Richard D. Kimball Company, Inc.	Fitzemeyer & Tocci Associates, Inc.	
200801030020G	Gardner	Waterford Street Primary Penn Brook Elementary School	Final Audit Approved	Repair - Accelerated	DBB	P3 Inc.	Knight, Bagge & Anderson, Inc.		Reliable Roofing and Sheet Metal, LLC
200901050010	Georgetown	Georgetown Middle/High School	Design Development	New Construction		Municipal Building Consultants, Inc.	Drumme Rosane Anderson, Inc.	Rist-Frost-Shumway Engineering, P.C.	-
200801050505	Georgetown		Eligibility Period						
201101070010G	Gloucester	Beeman Memorial School	Final Audit Approved	Repair - Accelerated	DBB	Knight, Bagge & Anderson Inc.	CGKV Architects, Inc.	Russo Barr Associates, Inc.	Built-up Roofing Systems LLC
201101070020G	Gloucester	East Gloucester Elementary School	Final Audit Approved	Repair - Accelerated	DBB	Knight, Bagge & Anderson Inc.	CGKV Architects, Inc.	Russo Barr Associates, Inc.	Stanley Roofing Company, Inc.
201101070042G	Gloucester	Plum Cove Elementary School	Final Audit Approved	Repair - Accelerated	DBB	Knight, Bagge & Anderson Inc.	CGKV Architects, Inc.	Russo Barr Associates, Inc.	Built-up Roofing Systems LLC
201101070305G	Gloucester	Ralph B O'Maley Middle	Final Audit Approved	Repair - Accelerated	DBB	Knight, Bagge & Anderson Inc.	CGKV Architects, Inc.	Russo Barr Associates, Inc.	Titan Roofing, Inc.
201101070045G	Gloucester	Veterans Memorial West Parish Elementary School	Final Audit Approved	Repair - Accelerated	DBB	Knight, Bagge & Anderson Inc.	CGKV Architects, Inc.	Russo Barr Associates, Inc.	Stanley Roofing Company, Inc.
200901070050	Gloucester		Designer Selection						-
200801100505	Grafton	Grafton Memorial Senior	Project Completion	New Construction	CM@R	Joslin, Lesser + Associates Inc.	Symmes Maini & McKee Associates, Inc.	Horizon Engineering Associates, LLP	Dimeo Construction Company
201101100505G	Grafton	Grafton Memorial Senior	Final Audit Approved	Repair - Accelerated	DBB	URS Corporation	CGKV Architects, Inc.	Horizon Engineering Associates, LLP	S.O.M. Construction Ent., Inc.
201101100005G	Grafton	South Grafton Elementary	Closeout	Repair - Accelerated	DBB	URS Corporation	CGKV Architects, Inc.	Horizon Engineering Associates, LLP	AAlanco Service Corporation
201108230605	Greater Lawrence RVT	Greater Lawrence Reg Voc Tech	Designer Selection	Repair - Major		Vertex Construction Services	-	-	-
200908280605	Greater Lowell Voc Tec	Greater Lowell Regional Technical High School	Approved Project Vote Pending	Repair - Major		Joslin, Lesser + Associates Inc.	Knight, Bagge & Anderson, Inc.		-
201008250605	Greater New Bedford	Vocational Technical High School	Design Development	Addition / Renovation		Construction Monitoring Services, Inc.	Drumme Rosane Anderson, Inc.		-
201101140025G	Greenfield	Four Corners	Project Completion	Repair - Accelerated	DBB	P3 Project Planning	Tighe & Bond, Inc.	Strategic Building Solutions, LLC	Five Star Building Corp.
200901140505	Greenfield	Greenfield High School	Design Development	New Construction	DBB	Construction Monitoring Services, Inc.	Dore & Whittier Architects, Inc.	BVH Integrated Services, Inc.	-
201206730305	Groton-Dunstable	Groton Dunstable Regional Middle School	Design Development	Repair - Accelerated		Collaborative Partners	ICON architecture, inc.	Russo Barr Associates, Inc.	-
201101170505G	Hadley	Hopkins Academy	Closeout	Repair - Accelerated	DBB	Strategic Building Solutions, LLC	CCS Presentation Systems	Russo Barr Associates, Inc.	MDM Engineering
201206750010	Hamilton-Wenham	Cutler School	Approved Project Vote Pending	Repair - Accelerated		Coast & Harbor Associates, Inc.	CBI Consulting, Inc.	Russo Barr Associates, Inc.	
200806800505	Hampden-Wilbraham	Minnechaug Regional High School	Project Completion	New Construction	DBB	Pinnacle One, Inc.	Mount Vernon Group Architects, Inc.	Horizon Engineering Associates, LLP	Fontaine Brothers, Inc.
201001210005G	Hancock	Hancock Elementary School	Project Completion	Repair - Accelerated	DBB	-	Westall Architects		Salco Construction Company, Inc.
200801220505	Hanover	Hanover High School	Closeout	New Construction	DBB	PMA Construction Services	HMFH Architects, Inc.	Horizon Engineering Associates, LLP	Callahan, Inc.
201201280035	Haverhill	Caleb Dustin Hunking	OPM Selection			-	-	-	-
201101280100G	Haverhill	Consentino Middle School	Construction	Repair - Accelerated	DBB	Vertex Construction Services	CSS Architects Incorporated	RDK Engineers Russo Barr Associates, Inc.	
201101280085G	Haverhill	High School	Closeout						
201101280075G	Haverhill	John G Whittier Middle School	Construction	Repair - Accelerated	DBB	Vertex Construction Services	CSS Architects Incorporated	Russo Barr Associates, Inc.	-
201101280075G	Haverhill	Tilton Elementary School	Project Completion	Repair - Accelerated	DBB	Vertex Construction Services	CSS Architects Incorporated	Russo Barr Associates, Inc.	-
201101280080G	Haverhill	Walnut Square Elementary School	Project Completion	Repair - Accelerated	DBB	Vertex Construction Services	CSS Architects Incorporated	RDK Engineers Russo Barr Associates, Inc.	-
201001310410	Hingham	Hingham Middle School	Construction	New Construction	DBB	Knight, Bagge & Anderson Inc.	Ai3 Architects LLC	Foreman Building Commissioning, LP	Brait Builders Corp.
200801330505	Holbrook	Holbrook Junior-Senior High School	Designer Selection			Symmes Maini & McKee Associates, Inc.	-	-	-



MSBA ID	District	School	Phase	Project Scope	Procurement Type	OPM	Designer	Cx_Company	CMGC
W20034396	Holyoke	Holyoke High School	Closeout	Repair - Major	DBB	-	Design Partnership of Cambridge, Inc.	-	-
201201370605	Holyoke	Wm J Dean Voc Tech High Lt. McMahon Elementary School	Approved Project Vote Pending	Science Lab		Skanska USA Building, Inc	Kaestle Boos Associates, Inc.	-	-
201201370015	Holyoke	John F. Kennedy Middle School	Eligibility Period						
200801410410	Hudson	Hudson High School	Construction	New Construction	DBB	PMA Construction Services	OMR Architects, Inc.	WSP Flack + Kurtz	Bacon-Agostini Construction Joint Venture
200801530505	Leominster	Leominster High School	Construction	Addition / Renovation	CM@R	Daedalus Projects Inc	Lamoureux Pagano & Associates, Inc.	Horizon Engineering Associates, LLP	S.O.M. Construction Ent., Inc.
201201530007	Leominster	Fall Brook	Project Scope & Budget	Repair - Accelerated					
201201530010	Leominster	Southeast School	Project Scope & Budget	Repair - Accelerated					
201101540005G	Leverett	Leverett Elementary School	Project Completion	Repair - Accelerated	DBB	Potomac Capital Advisors	DiMarinisi & Wolfe Architects Urban Designers	Russo Barr Associates, Inc.	-
201101550010E	Lexington	Joseph Estabrook Elementary School	Construction	New Construction		RF Walsh Collaborative Partners	DiNisco Design Partnership, Limited	BVH Integrated Services, Inc.	-
200901570025	Lincoln	Lincoln School	Approved Project Vote Pending	Addition / Renovation		Skanska USA Building, Inc	OMR Architects, Inc.	-	-
200801590505	Longmeadow	Longmeadow High School	Construction	New Construction	CM@R	Joslin, Lesser + Associates Inc.	OMR Architects, Inc.	Foreman Building Commissioning, LP	Gilbane Building Company
201101600505G	Lowell	Lowell High School	Project Completion	Repair - Accelerated	DBB	NETCO Construction Project Managers, Inc.	ICON architecture, inc.	Building Enclosure Associates	-
201101600027G	Lowell	Moody Elementary School	Construction	Repair - Accelerated	DBB	NETCO Construction Project Managers, Inc.	ICON architecture, inc.	Building Enclosure Associates	-
201101600040G	Lowell	Peter W Reilly School	Project Completion	Repair - Accelerated	DBB	NETCO Construction Project Managers, Inc.	ICON architecture, inc.	Building Enclosure Associates	-
201101600055G	Lowell	Washington School	Construction	Repair - Accelerated	DBB	NETCO Construction Project Managers, Inc.	ICON architecture, inc.	Building Enclosure Associates RDK Engineers	-
200801620505	Lunenburg	Lunenburg High School	Designer Selection			Joslin, Lesser + Associates Inc.	-	-	-
201201630405	Lynn	Breed Middle School	Design Development	Repair - Accelerated		Diversified Project Management	Kaestle Boos Associates, Inc.		
200901630305	Lynn	Thurgood Marshall Middle School	Feasibility Study			Joslin, Lesser + Associates Inc.	Raymond Design Associates, Inc.		-
201201630605	Lynn	Lynn Vocational Tech Institute	Design Development	Repair - Accelerated		Diversified Project Management	Kaestle Boos Associates, Inc.		
200901640505	Lynnfield	Lynnfield High School	Construction	Addition / Renovation	DBB	HEERY	Edward Rowse Architects, Inc.	Fitzemeyer & Tocci Associates, Inc.	E.A. Collangeli Construction Co., Inc.
W20024319	Malden	Malden High School	Closeout	Addition / Renovation	CM@R	URS Corporation	Flansburgh Associates, Inc.		Gilbane Building Company
200806980610	Manchester Essex Regional	Manchester Essex Regional High School	Final Audit Approved	New Construction	DBB	Design Technique Inc.	Mount Vernon Group Architects, Inc.		TLT Construction Corporation
200801680020	Marblehead	Glover Elementary School	Construction	New Construction	DBB	Municipal Building Consultants, Inc.	JCJ Architecture, PC	RDK Engineers	G & R Construction, Inc.
201101700008G	Marlborough	Francis J Kane Elementary School	Project Completion	Repair - Accelerated	DBB	RF Walsh Collaborative Partners	Baker/Wohl Architects, Inc.	Building Enclosure Associates	A&A Window Products, Inc.
201101700505G	Marlborough	Marlborough High School	Project Completion	Repair - Accelerated	DBB	RF Walsh Collaborative Partners	Baker/Wohl Architects, Inc.	RDK Engineers Building Enclosure Associates	McAnespie, Inc. Veterans Development Corporation, Inc.
200801710020	Marshfield	Governor Edward Winslow Elementary School	Closeout	Repair - Major	DBB	Vertex Construction Services	Knight, Bagge & Anderson, Inc.	RDK Engineers	Enterprise Equipment Co., Inc.
201101710505	Marshfield	Marshfield High School	Construction	New Construction	DBB	Compass Project Management, Inc.	Ai3 Architects LLC	Sebesta Blomberg & Associates, Inc.	-
200801740505	Maynard	Maynard High School	Construction	New Construction	DBB	Municipal Building Consultants, Inc.	Tappe Associates, Inc.	WSP Flack + Kurtz	CTA Construction Co., Inc.
201201760505	Medford	Medford High School	Feasibility Study	Science Lab		Leftfield, LLC	DiNisco Design Partnership, Limited		-
200801770305	Medway	Medway Middle School	Construction	Repair - Major	CM@R	Compass Project Management, Inc.	Knight, Bagge & Anderson, Inc.	Sebesta Blomberg & Associates, Inc.	Consigli Construction Company, Inc.
201201780505	Melrose	Melrose High School	Approved Project Vote Pending	Science Lab		CPI/Collaborative Partners	Ai3 Architects LLC		-
201101780505G	Melrose	Melrose High School	Final Audit Approved	Repair - Accelerated	DBB	Municipal Building Consultants, Inc.	Gale Associates, Inc.	Russo Barr Associates, Inc.	Commercial Roofing and Contracting, Inc.
201107100015G	Mendon-Upton	Miscoe Hill School	Project Completion	Repair - Accelerated	DBB	Maguire Group Inc.	Habeeb & Associates Architects, Inc.	Sebesta Blomberg & Associates, Inc.	Greenwood Industries, Inc.



MSBA ID	District	School	Phase	Project Scope	Procurement Type	OPM	Designer	Cx_Company	CMGC
200801810505	Methuen	Methuen High School	Construction	Addition / Renovation	CM@R	KBA/Trident	Finegold Alexander and Associates Inc.	Environmental Health and Engineering	Dimeo Construction Company
201101820025G	Middleborough	Mary K. Goode Elementary School	Closeout	Repair - Accelerated	DBB	Maguire Group Inc.	Habeeb & Associates Architects, Inc.	Russo Barr Associates, Inc.	J.J. Cardosi, Inc.
200801840005	Middleton	Howe-Manning School	Closeout	New Construction	DBB	RF Walsh Collaborative Partners	DiNisco Design Partnership, Limited	Foreman Building Commissioning, LP	CTA Construction Co., Inc.
201101850090	Milford	Woodland Elementary School	Designer Selection			Joslin, Lesser + Associates Inc.	-	-	-
200908300605	Minuteman Voc Tech	Minuteman Regional High School (Career Tech)	Designer Selection			Skanska USA Building, Inc	-	-	-
201107170005G	Mohawk Trail	Buckland-Shelburne Reg	Closeout	Repair - Accelerated	DBB	Potomac Capital Advisors	Bradley Architects, Inc.	Strategic Building Solutions, LLC	-
201107170010G	Mohawk Trail	Colrain Central School	Closeout	Repair - Accelerated	DBB	Potomac Capital Advisors	Bradley Architects, Inc.	Strategic Building Solutions, LLC	-
201107170505G	Mohawk Trail	Mohawk Trail Reg High School	Project Completion	Repair - Accelerated	DBB	Potomac Capital Advisors	Bradley Architects, Inc.	Strategic Building Solutions, LLC	-
201122229999	Monomoy	Monomoy Regional High School	Design Development	New Construction		Skanska USA Building, Inc	Mount Vernon Group Architects, Inc.	Sebesta Blomberg & Associates, Inc.	-
201107200305G	Narragansett	Narragansett Middle School	Final Audit Approved	Repair - Accelerated	DBB	Potomac Capital Advisors	DiMarinisi & Wolfe Architects Urban Designers	Rist-Frost-Shumway Engineering, P.C.	-
201107200003G	Narragansett	Phillipston Memorial Elementary School	Project Completion	Repair - Accelerated	DBB	Potomac Capital Advisors	DiMarinisi & Wolfe Architects Urban Designers	Rist-Frost-Shumway Engineering, P.C.	-
200807200020	Narragansett	Templeton Center School	Feasibility Study	Repair - Major		Strategic Building Solutions, LLC	Symmes Maini & McKee Associates, Inc.	-	-
201207250505	Nashoba	Nashoba Regional High School	Feasibility Study	Science Lab		Strategic Building Solutions, LLC	Symmes Maini & McKee Associates, Inc.	Strategic Building Solutions, LLC	P.J. Stella Construction Corp.
200807250015	Nashoba	Pompositicut Elementary School	Project Completion	Addition / Renovation	DBB	Construction Monitoring Services, Inc.	Symmes Maini & McKee Associates, Inc.	Strategic Building Solutions, LLC	P.J. Stella Construction Corp.
200908520605G	Nashoba Valley Tech	Nashoba Valley Technical High School	Closeout	Repair - Accelerated	DBB	-	-	-	-
200801980505	Natick	Natick High School	Project Completion	New Construction	DBB	RF Walsh Collaborative Partners	Ai3 Architects LLC	Rist-Frost-Shumway Engineering, P.C.	-
201106600505G	Nauset	Nauset Regional High School	Project Completion	Repair - Accelerated	DBB	NETCO Construction Project Managers, Inc.	Habeeb & Associates Architects, Inc.	CBI Consulting Inc.	Capeway Roofing Systems, Inc. Modern Glass & Aluminum, Inc. Consigli Construction Company, Inc. Triumph Leasing Corporation
200901990050	Needham	Newman Elementary School	Project Completion	Repair - Major	CM@R	Steven H. Popper - Town Employee	Drumme Rosane Anderson, Inc.	Rist-Frost-Shumway Engineering, P.C.	-
201101990405G	Needham	Pollard Middle	Final Audit Approved	Repair - Accelerated	DBB	STV Incorporated	Gale Associates, Inc.	CBI Consulting Inc.	Wayne Roofing Systems, LLC
200902010070	New Bedford	John Hannigan	OPM Selection			-	-	-	-
201002010505	New Bedford	New Bedford High School	Closeout		DBB	-	-	-	-
201107280015G	New Salem-Wendell	Swift River Elementary School	Closeout	Repair - Accelerated	DBB	Maguire Group Inc.	Bradley Architects, Inc.	Strategic Building Solutions, LLC	RAC Builders, Inc.
201102040005	Newburyport	Francis T Bresnahan Elementary School	Design Development	New Construction		HEERY	HMFH Architects, Inc.	Fitzmeyer & Tocci Associates, Inc.	-
201002040305	Newburyport	Rupert A. Nock Middle School	Design Development	Addition / Renovation		HEERY	Miller Dyer Spears Inc.	-	-
201102070005	Newton	A E Angier Elementary School	Feasibility Study			Joslin, Lesser + Associates Inc.	-	-	-
201102070015G	Newton	Bowen	Closeout	Repair - Accelerated	DBB	STV Incorporated	Habeeb & Associates Architects, Inc.	-	-
W20014216	Newton	Newton North High School	Closeout	New Construction	CM@R	Turner Construction Co.	Dore & Whittier Architects, Inc.	Dimeo Construction Company	-
201102070125G	Newton	Williams Elementary School	Closeout	Repair - Accelerated	DBB	STV Incorporated	Habeeb & Associates Architects, Inc.	-	-
200802080005	Norfolk	Freeman-Kennedy Elementary School	Project Completion	New Construction	DBB	Joslin, Lesser + Associates Inc.	Flansburgh Associates, Inc.	WSP Flack + Kurtz	Fontaine Brothers, Inc.
200909150705	Norfolk County Agriculture	Norfolk County Agricultural High School	Construction	Addition / Renovation	DBB	Compass Project Management, Inc.	Turowski2 Architecture, Inc.	Rist-Frost-Shumway Engineering, P.C.	TLT Construction Corporation
200802090305	North Adams	Silvio O Conte Middle School	Approved Project Vote Pending	Addition / Renovation		Strategic Building Solutions, LLC	Margo Jones Architects, Inc.	-	-
201102110018G	North Andover	Annie L Sargent School	Project Completion	Repair - Accelerated	DBB	Municipal Building Consultants, Inc.	ICON architecture, inc.	Cannon Design	Varioka Construction, Inc.
201102110001G	North Andover	Atkinson School	Project Completion	Repair - Accelerated	DBB	Municipal Building Consultants, Inc.	ICON architecture, inc.	Cannon Design	Paul J. Rogan Co., Inc.



MSBA ID	District	School	Phase	Project Scope	Procurement Type	OPM	Designer	Cx_Company	CMGC
201102110305G	North Andover	North Andover Middle School	Project Completion	Repair - Accelerated	DBB	Municipal Building Consultants, Inc.	ICON architecture, inc.	Cannon Design	Stanley Roofing Company, Inc.
201102120010G	North Attleborough	Falls Elementary School	Closeout	Repair - Accelerated	DBB	Atlantic Construction and Management, Inc.	CSS Architects Incorporated	Gale Associates, Inc.	Northeast Energy Control Systems
201202120505	North Attleborough	North Attleboro High	Approved Project Vote Pending	Science Lab		Skanska USA Building, Inc	Kaestle Boos Associates, Inc.		-
201202120015	North Attleborough	Rossvell Avenue Elementary School	Design Development	Repair - Accelerated		Skanska USA Building, Inc	Russo Barr Associates, Inc.		
201202150015	North Brookfield	North Brookfield Elementary School	Design Development	Repair - Accelerated		Strategic Building Solutions, LLC	CBI Consulting, Inc.		
201102150015G	North Brookfield	North Brookfield Elementary School	Project Completion	Repair - Accelerated	DBB	Vertex Construction Services	LPBA/ Architects, Inc.	Simpson Gumpertz & Heger Inc.	Lockheed Window Corporations
201107350010G	North Middlesex	Ashby Elementary	Closeout	Repair - Accelerated	DBB	Compass Project Management, Inc.	Russo Barr Associates, Inc.	Building Enclosure Associates	Greenwood Industries, Inc. GVVW, Inc.
201107350505	North Middlesex	North Middlesex Regional High School	Designer Selection			HEERY	-		-
201107350005G	North Middlesex	Spaulding Memorial	Closeout	Repair - Accelerated	DBB	Compass Project Management, Inc.	Russo Barr Associates, Inc.	Building Enclosure Associates	MDM Engineering
201002170505	North Reading	North Reading High School	Construction	Addition / Renovation	CM@R	PMA Construction Services	Dore & Whittier Architects, Inc.	Cannon Design	-
201102130003	Northborough	Lincoln Street	Designer Selection			Strategic Building Solutions, LLC	-		-
201102130305G	Northborough	Robert E. Melican Middle School	Final Audit Approved	Repair - Accelerated	DBB	Pinck & Co., Inc.	ICON architecture, inc.	Strategic Building Solutions, LLC	AAIanco Service Corporation
201202180015	Norton	J C Solmonese	Project Scope & Budget	Repair - Accelerated		Joslin, Lesser + Associates Inc.	Habeeb & Associates Architects, Inc.		
200902180505	Norton	Norton High School	Construction	Addition / Renovation	CM@R	Pinck & Co., Inc.	JCJ Architecture, PC	Rist-Frost-Shumway Engineering, P.C.	W. T. Rich Company Inc.
200802200505	Norwood	Norwood High School	Closeout	New Construction	DBB	Compass Project Management, Inc.	Ai3 Architects LLC		Agostini Construction Co., Inc.
200908550605	Old Colony Reg Voc Tech	Vocational Technical High School	Project Scope & Budget			Vertex Construction Services	-		-
200802260405	Oxford	Oxford Middle School	Construction	Repair - Major		Diversified Project Management	CGKV Architects, Inc.	Cannon Design	S.O.M. Construction Ent., Inc.
201102270305G	Palmer	Converse Middle School	Project Completion	Repair - Accelerated	DBB	Diversified Project Management	Tighe & Bond, Inc.	Strategic Building Solutions, LLC	Royal Steam Heater Co. Titan Roofing, Inc.
201102270008G	Palmer	Old Mill Pond Elementary School	Project Completion	Repair - Accelerated	DBB	Diversified Project Management	Tighe & Bond, Inc.	Strategic Building Solutions, LLC	Royal Steam Heater Co.
201102270505G	Palmer	Palmer High School	Project Completion	Repair - Accelerated	DBB	Diversified Project Management	Tighe & Bond, Inc.	Strategic Building Solutions, LLC	Royal Steam Heater Co. Titan Roofing, Inc.
200802290305	Peabody	J Henry Higgins Middle School	Schematic Design	New Construction		Daedalus Projects Inc	DiNisco Design Partnership, Limited		-
201102290007G	Peabody	John E Burke School	Project Completion	Repair - Accelerated	DBB	Daedalus Projects Inc	LPBA/ Architects, Inc.	Sebesta Blomberg & Associates, Inc.	-
201102290027G	Peabody	William A Welch Sr	Closeout	Repair - Accelerated	DBB	Daedalus Projects Inc	LPBA/ Architects, Inc.	Sebesta Blomberg & Associates, Inc.	-
201107450020G	Pentucket	Dr Frederick N Sweetsir	Closeout	Repair - Accelerated	DBB	PMA Construction Services	Knight, Bagge & Anderson, Inc.	CBI Consulting Inc.	E. Amanti & Sons, Inc.
201107450015G	Pentucket	Dr John C Page School	Closeout	Repair - Accelerated	DBB	PMA Construction Services	Knight, Bagge & Anderson, Inc.	RDK Engineers	Capeway Roofing Systems, Inc.
201107450005G	Pentucket	Elmer S Bagnall	Closeout	Repair - Accelerated	DBB	PMA Construction Services	Knight, Bagge & Anderson, Inc.	CBI Consulting Inc.	Gibson Roofs, Inc.
201107450010G	Pentucket	Helen R Donaghue School	Closeout	Repair - Accelerated	DBB	PMA Construction Services	Knight, Bagge & Anderson, Inc.	CBI Consulting Inc.	Gibson Roofs, Inc.
201107500008G	Pioneer Valley	Northfield Elementary School	Closeout	Repair - Accelerated	DBB	Diversified Project Management	CGKV Architects, Inc.	Strategic Building Solutions, LLC	-
201107500505G	Pioneer Valley	Pioneer Valley Reg Middle School/High School	Project Completion	Repair - Accelerated	DBB	Diversified Project Management	CGKV Architects, Inc.	Strategic Building Solutions, LLC	-
201002360510	Pittsfield	Taconic High School	Feasibility Study			Skanska USA Building, Inc	-		-
201202390515	Plymouth	Plymouth South High School	OPM Selection						
200802390505	Plymouth	Plymouth North High School	Project Completion	New Construction	DBB	Ted Gentry Associates, Inc	Ai3 Architects LLC	Sebesta Blomberg & Associates, Inc.	J & J Contractors, Inc.
201007530505G	Quabbin	Quabbin Regional High School	Closeout	Repair - Accelerated	DBB	Vertex Construction Services	LPBA/ Architects, Inc.	Building Enclosure Associates	Kronenberger & Sons Restoration, Inc.



MSBA ID	District	School	Phase	Project Scope	Procurement Type	OPM	Designer	Cx_Company	CMGC
201207530030	Quabbin	Ruggles Lane Elementary School	Design Development	Repair - Accelerated		Vertex Construction Services	Turowski2 Architecture, Inc.		
201207780005	Quaboag	Warren Community Elementary School	Project Scope & Budget	Repair - Accelerated		Coast & Harbor Associates, Inc.	Lindgren & Sharples, Inc.		
200802430315	Quincy	Central Middle School	Construction	New Construction	DBB	Tishman Construction Corporation of MA	Ai3 Architects LLC	Sebesta Blomberg & Associates, Inc.	H.V. Collins Co., Inc.
201102460005G	Reading	Birch Meadow Elementary School	Final Audit Approved	Repair - Accelerated	DBB	KBA Architects	LPBA/ Architects, Inc.	Russo Barr Associates, Inc.	Paul J. Rogan Co., Inc.
201102460017G	Reading	J Warren Killam Elementary School	Final Audit Approved	Repair - Accelerated	DBB	KBA Architects	LPBA/ Architects, Inc.	Russo Barr Associates, Inc.	Capeway Roofing Systems, Inc.
201002480035	Revere	William McKinley Elementary School	Project Scope & Budget			RF Walsh Collaborative Partners	Drumme Rosane Anderson, Inc.		-
200802500005	Rochester	Rochester Memorial School	Final Audit Approved	Addition / Renovation	CM@R	PMA Construction Services	Flansburgh Associates, Inc.	Horizon Engineering Associates, LLP	Gilbane Building Company
200802510305	Rockland	John W. Rogers Middle School	Construction	New Construction	CM@R	Daedalus Projects Inc	Dore & Whittier Architects, Inc.	Consulting Engineering Services, LLC	Agostini Construction Co., Inc.
201102510025G	Rockland	R Stewart Esten	Closeout	Repair - Accelerated	DBB	Daedalus Projects Inc	Habeeb & Associates Architects, Inc.	Russo Barr Associates, Inc.	Northeast Energy Control Systems
200902580305G	Salem	Collins Middle School	Construction	Repair - Accelerated	CM@R	KV Associates, Inc.	Reinhardt Associates, Inc.	Rist-Frost-Shumway Engineering, P.C.	-
201002580050G	Salem	Saltonstall School	Construction	Repair - Accelerated	CM@R	KV Associates, Inc.	Reinhardt Associates, Inc.	Rist-Frost-Shumway Engineering, P.C.	-
201102610010G	Sandwich	Forestdale School	Closeout	Repair - Accelerated	DBB	NETCO Construction Project Managers, Inc.	Habeeb & Associates Architects, Inc.	Gale Associates, Inc.	Variaka Construction, Inc.
200902610025G	Sandwich	Oak Ridge School	Closeout	Repair - Accelerated	DBB	NETCO Construction Project Managers, Inc.	Habeeb & Associates Architects, Inc.	Gale Associates, Inc.	J.J. Cardosi, Inc.
201002620305	Saugus	Belmonte Middle School	Construction	Repair - Major	CM@R	Skanska USA Building, Inc	Fletcher Thompson Architecture Engineering, LLC	Consulting Engineering Services, LLC	Consigli Construction Company, Inc.
201202640305	Scituate	Gates Intermediate School	Eligibility Period						
200802660305	Sharon	Sharon Middle School	Closeout	Addition / Renovation	CM@R	Daedalus Projects Inc	Kaestle Boos Associates, Inc.	Horizon Engineering Associates, LLP	Consigli Construction Company, Inc.
201008710605	Shawsheen Valley Voc Tech	Shawsheen Valley Voc Tech High School	Closeout	Addition / Renovation	DBB	Construction Monitoring Services, Inc.	Knight, Bagge & Anderson, Inc.		Colantonio, Inc.
201208710605	Shawsheen Valley Voc Tech	Shawsheen Valley Voc Tech High School	Approved Project Vote Pending	Repair - Accelerated		Diversified Project Management	Shekar & Associates, Inc.		
200802710305	Shrewsbury	Sherwood Middle School	Project Completion	New Construction	CM@R	PMA Construction Services	Lamoureux Pagano & Associates, Inc.	RDK Engineers	Gilbane Building Company
201102710035G	Shrewsbury	Spring Street Elementary School	Construction	Repair - Accelerated	DBB	PMA Construction Services	Habeeb & Associates Architects, Inc.	Cannon Design	Lambrian Construction Corp.
20081119999	Somerset-Berkley	Somerset-Berkley High School	Construction	New Construction		Skanska USA Building, Inc	Ai3 Architects LLC	Horizon Engineering Associates, LLP	Bacon-Agostini Construction Joint Venture
200902740111E	Somerville	East Somerville Community School at Cummings	Construction	Addition / Renovation	CM@R	PMA Construction Services	Maguire Group, Inc.	Foreman Building Commissioning, LP	Gilbane Building Company
200902780015	South Hadley	Plains School	Approved Project Vote Pending	New Construction		Arcadis	Margo Jones Architects, Inc.		-
200808730605G	South Shore Reg Voc Tech	South Shore Vocational Technical High School	Closeout	Repair - Accelerated	DBB	Vertex Construction Services	Gale Associates, Inc.	Building Enclosure Associates	-
200802770505	Southbridge	Southbridge High School	Project Completion	New Construction	CM@R	Joslin, Lesser + Associates Inc.	Tappe Associates, Inc.	Environmental Health and Engineering	Consigli Construction Company, Inc.
201202750005	Southampton	William E. Norris Elementary School	Project Scope & Budget	Repair - Accelerated					
200908720605	Southeastern Reg Voc Tech	Southeastern Regional Vocational Technical School	Construction	Addition / Renovation	CM@R	RF Walsh Collaborative Partners	Drumme Rosane Anderson, Inc.	RDK Engineers	W. T. Rich Company Inc.
200908760605	Southern Worcester City VT	Vocational Technical High School	Design Development	Addition / Renovation	DBB	HEERY	Kaestle Boos Associates, Inc.		-
201107660505	Southwick-Tolland	Regional High School	Design Development	Addition / Renovation		Strategic Building Solutions, LLC	JCJ Architecture, PC		BVH Integrated Services, Inc.
200807670505	Spencer-E Brookfield	David Prouty High School	Schematic Design	Addition / Renovation		Dore and Whittier Architects, Inc.	Design Partnership of Cambridge, Inc.		-
	Springfield	SCIPP Year 2	Project Completion						
	Springfield	SCIPP Year 3	Construction						
201102810125E	Springfield	Dryden Veterans Memorial Elementary School	Construction	Addition / Renovation		Arcadis	Drumme Rosane Anderson, Inc.	BVH Integrated Services, Inc.	-



MSBA ID	District	School	Phase	Project Scope	Procurement Type	OPM	Designer	Cx_Company	CMGC
201102810030E	Springfield	Elias Brookings Elementary School	Design Development	New Construction		Arcadis	Drumney Rosane Anderson, Inc.		-
W20014137	Springfield	Forest Park Middle School	Construction	Addition / Renovation	DBB	Arcadis	Perkins Eastman	Foreman Building Commissioning, LP	Consigli Construction Company, Inc.
W20054428	Springfield	Roger L. Putnam Vocational Technical High School	Project Completion	New Construction	CM@R	Pinnacle One, Inc.	Drumney Rosane Anderson Inc.	Strategic Building Solutions, LLC	Consigli/Morganti
201202810500	Springfield	Central High School	Feasibility Study	Science Lab		Leftfield, LLC	DiNisco Design Partnership, Limited		
200902840405	Stoneham	Stoneham Middle School	Design Development	Addition / Renovation	CM@R	Joslin, Lesser + Associates Inc.	Tappe Associates, Inc.	RDK Engineers	Shawmut Design and Construction
200802870005	Sturbridge	Burgess Elementary School	Project Completion	Addition / Renovation	DBB	Lamoureux Pagano & Associates, Inc.	Drumney Rosane Anderson, Inc.	Horizon Engineering Associates, LLP	Fontaine Brothers, Inc.
201102880030G	Sudbury	Peter Noyes Elementary School	Final Audit Approved	Repair - Accelerated	DBB	Compass Project Management, Inc.	Russo Barr Associates, Inc.	RDK Engineers	Gibson Roofs, Inc.
201202880025	Sudbury	General John Nixon Elementary School	Design Development	Repair - Accelerated					
200802900305	Sutton	Sutton Middle School	Construction	Addition / Renovation	DBB	Strategic Building Solutions, LLC	Flansburgh Associates, Inc.	RDK Engineers	TLT Construction Corporation
201102910010	Swampscott	Hadley Elementary School	OPM Selection			-	-		-
201107700405G	Tantasqua	Tantasqua Regional Jr High School	Final Audit Approved	Repair - Accelerated	DBB	Diversified Project Management	Habeeb & Associates Architects, Inc.		Greenwood Industries, Inc.
201202930057	Taunton	Harold H Galligan School	Project Scope & Budget	Repair - Accelerated					
W20014194	Taunton	Parker Middle/Taunton High School	Closeout	Addition / Renovation	CM@R	Gilbane Building Company	Design Partnership of Cambridge, Inc.		Bacon-Agostini Construction Joint Venture
200802950505	Tewksbury	Tewksbury Memorial High School	Project Completion	New Construction	DBB	HEERY	Symmes Maini & McKee Associates, Inc.	Sebesta Blomberg & Associates, Inc.	CTA Ventures
201208780605	Tri County	Tri County Reg Voc Tech	Approved Project Vote Pending	Science Lab		Collaborative Partners	Ai3 Architects LLC		-
201108790605G	Upper Cape Cod Voc Tech	Upper Cape Cod Voc Tech	Project Completion	Repair - Accelerated	DBB	NETCO Construction Project Managers, Inc.	Knight, Bagge & Anderson, Inc.	Gale Associates, Inc.	Modern Glass & Aluminum, Inc.
200803040505	Uxbridge	Uxbridge High School	Project Completion	New Construction	CM@R	Joslin, Lesser + Associates Inc.	Raymond Design Associates, Inc.	Turner Facilities Management Solutions	Shawmut Design and Construction
200907750305	Wachusett	Mountview Middle School	Schematic Design			Gary Kaczmarek - Town Employee	Lamoureux Pagano & Associates, Inc.		-
201107750035G	Wachusett	Naquag Elementary School	Closeout	Repair - Accelerated	DBB	Strategic Building Solutions, LLC	LPBA/ Architects, Inc.	Rist-Frost-Shumway Engineering, P.C.	MDM Engineering
201107750040G	Wachusett	Paxton Center School	Closeout	Repair - Accelerated	DBB	Strategic Building Solutions, LLC	LPBA/ Architects, Inc.	Rist-Frost-Shumway Engineering, P.C.	MDM Engineering
201107750045G	Wachusett	Thomas Prince School	Construction	Repair - Accelerated	DBB	Strategic Building Solutions, LLC	LPBA/ Architects, Inc.	Rist-Frost-Shumway Engineering, P.C.	MDM Engineering
201003050310	Wakefield	Galvin Middle School	Design Development	New Construction	DBB	Joslin, Lesser + Associates Inc.	Tappe Associates, Inc.	B2Q Associates, Inc.	-
201203150305	Wayland	Wayland Middle School	Project Scope & Budget	Repair - Accelerated		Joslin, Lesser + Associates Inc.	DiMarinisi & Wolfe Architects Urban Designers		
200803150505	Wayland	Wayland High School	Closeout	New Construction	CM@R	KV Associates, Inc.	HMFH Architects, Inc.	WSP Flack + Kurtz	Shawmut Design and Construction
200903160015	Webster	Park Avenue Elementary School	Design Development	New Construction	DBB	RF Walsh Collaborative Partners	Dore & Whittier Architects, Inc.		-
200803170505	Wellesley	Wellesley Senior High School	Project Completion	New Construction	CM@R	Ryegate, Inc.	Symmes Maini & McKee Associates, Inc.	Rist-Frost-Shumway Engineering, P.C.	Turner Construction Company
201103220005G	West Boylston	Major Edwards Elementary	Project Completion	Repair - Accelerated	DBB	URS Corporation	Reinhardt Associates, Inc.	Cannon Design	-
201003230505	West Bridgewater	West Bridgewater Middle-Senior High School	Design Development	New Construction		Strategic Building Solutions, LLC	Flansburgh Associates, Inc.		-
200903320505	West Springfield	West Springfield High School	Construction	New Construction	DBB	Strategic Building Solutions, LLC	Symmes Maini & McKee Associates, Inc.	Turner Facilities Management Solutions	Fontaine Brothers, Inc.
200903210305	Westborough	Gibbons Middle School	Designer Selection			-	-		-
200903250020	Westfield	Abner Gibbs Elementary School	Construction	New Construction	DBB	Skanska USA Building, Inc	Margo Jones Architects, Inc.	Horizon Engineering Associates, LLP	-
201103250025G	Westfield	Highland Elementary School	Closeout	Repair - Accelerated	DBB	P3 Project Planning	Tighe & Bond, Inc.		-
201003250025G	Westfield	Highland Elementary School	Final Audit Approved	Repair - Accelerated	DBB	P3 Project Planning	Tighe & Bond, Inc.	Strategic Building Solutions, LLC	-



MSBA ID	District	School	Phase	Project Scope	Procurement Type	OPM	Designer	Cx_Company	CMGC
201103250033E	Westfield	Munger Hill Elementary School	Approved Project Vote Pending	Repair - Accelerated		Vertex Construction Services	Knight, Bagge & Anderson, Inc.	Building Enclosure Associates	
201103250036G	Westfield	Paper Mill Elementary School	Closeout	Repair - Accelerated	DBB	P3 Project Planning	Tighe & Bond, Inc.	Strategic Building Solutions, LLC	-
201203250036	Westfield	Paper Mill Elementary School	Final Audit Approved	Repair - Accelerated		Vertex Construction Services	Knight, Bagge & Anderson, Inc.	Building Enclosure Associates	
201103250040G	Westfield	Southampton Road Elementary School	Final Audit Approved	Repair - Accelerated	DBB	P3 Inc.	Tighe & Bond, Inc.		
201003250040G	Westfield	Southampton Road Elementary School	Closeout	Repair - Accelerated	DBB	P3 Project Planning	Tighe & Bond, Inc.	Strategic Building Solutions, LLC	R & H Roofing
201103250505G	Westfield	Westfield High School	Closeout	Repair - Accelerated	DBB	P3 Project Planning	Tighe & Bond, Inc.	Strategic Building Solutions, LLC	-
201103250605G	Westfield	Westfield Voc Tech High School	Project Completion	Repair - Accelerated	DBB	P3 Project Planning	Tighe & Bond, Inc.	Strategic Building Solutions, LLC	-
200903300012	Weston	Field Elementary School	Construction	New Construction	DBB	Compass Project Management, Inc.	Jonathan Levi Architects LLC	Foreman Building Commissioning, LP	-
201103300505G	Weston	Weston High School	Closeout	Repair - Accelerated	DBB	Compass Project Management, Inc.	Garcia Galuska DeSousa Consulting Engineers Inc.	RDK Engineers	-
201103300305G	Weston	Weston Middle School	Final Audit Approved	Repair - Accelerated	DBB	Compass Project Management, Inc.	Russo Barr Associates, Inc.	RDK Engineers	Greenwood Industries, Inc.
201103310015G	Westport	Alice A Macomber Primary	Closeout	Repair - Accelerated	DBB	Pinck & Co., Inc.	CGKV Architects, Inc.	CBI Consulting Inc.	-
201103310505G	Westport	Westport High School	Construction	Repair - Accelerated	DBB	Pinck & Co., Inc.	CGKV Architects, Inc.	CBI Consulting Inc.	-
201103360310G	Weymouth	Abigail Adams Middle School	Final Audit Approved	Repair - Accelerated	DBB	KBA Architects	Gale Associates, Inc.	Cannon Design	Greenwood Industries, Inc.
201203360080	Weymouth	William Seach Primary	Design Development	Repair - Accelerated					
201107800030G	Whitman-Hanson	John H Duval Jr Elementary School	Final Audit Approved	Repair - Accelerated	DBB	-	BETA Group, Inc.		S.I. Services, Inc.
200907800025	Whitman-Hanson	Maquan Elementary School	Schematic Design			Knight, Bagge & Anderson Inc.	Turowski2 Architecture, Inc.		-
200803400005	Williamsburg	Anne T. Dunphy School	Design Development	Addition / Renovation	DBB	Arcadis	Drumme Rosane Anderson, Inc.	B2Q Associates, Inc.	-
201203420060	Wilmington	North Intermediate	Project Scope & Budget	Repair - Accelerated				CBI Consulting Inc.	
201103420025G	Wilmington	Shawsheen Elementary School	Final Audit Approved	Repair - Accelerated	DBB	P3 Inc.	Russo Barr Associates, Inc.	CBI Consulting Inc.	Lockheed Window Corporations
200903420505	Wilmington	Wilmington High School	Construction	New Construction	CM@R	Joslin, Lesser + Associates Inc.	Dore & Whittier Architects, Inc.	Symmes, Maini & McKee Associates	Gilbane Building Company
200803440025	Winchester	Vinson-Owen Elementary School	Construction	New Construction	DBB	Neil Foley - Town Employee	Tappe Associates, Inc.	Turner Facilities Management Solutions	CTA Construction Co., Inc.
201003440505	Winchester	Winchester High School	Feasibility Study			Skanska USA Building, Inc	Symmes Maini & McKee Associates, Inc.		-
200803460505	Winthrop	Winthrop Sr High School	Feasibility Study			Skanska USA Building, Inc	HMFH Architects, Inc.		-
201103470410G	Woburn	Daniel L Joyce Middle School	Final Audit Approved	Repair - Accelerated	DBB	Municipal Building Consultants, Inc.	Gale Associates, Inc.	Simpson Gumpertz & Heger Inc.	Reliable Roofing and Sheet Metal, LLC
200803470015	Woburn	Goodyear School	Closeout	New Construction	CM@R	Municipal Building Consultants, Inc.	Tappe Associates, Inc.	Strategic Building Solutions, LLC	Gilbane Building Company
201103470405G	Woburn	John F Kennedy Middle School	Final Audit Approved	Repair - Accelerated	DBB	Municipal Building Consultants, Inc.	Gale Associates, Inc.	Simpson Gumpertz & Heger Inc.	Greenwood Industries, Inc.
201203470060	Woburn	Wyman Elementary School	Eligibility Period						
201203480052	Worcester	Chandler Magnet School	Project Scope & Budget	Repair - Accelerated					
201203488099	Worcester	Dr. James Caradonio Center	Project Scope & Budget	Repair - Accelerated					
201203480140	Worcester	Jacob Hiatt Magnet School	Project Scope & Budget	Repair - Accelerated					
201203480145	Worcester	Lake View School	Project Scope & Budget	Repair - Accelerated					
201203480175	Worcester	May Street School	Project Scope & Budget	Repair - Accelerated					
201203480200	Worcester	Nelson Place	Eligibility Period			-	-	-	-



Massachusetts School Building Authority
You are Currently Viewing Active Projects.
Date of Report:1/9/13
Active Projects: 331

Green Repair **Accelerated Repair** **Waitlist** **Science Lab Initiative**

Last Updated: 1/9/13

MSBA ID	District	School	Phase	Project Scope	Procurement Type	OPM	Designer	Cx_Company	CMGC
W20004048	Worcester	North High School	Project Completion	New Construction	CM@R	-	Maguire Group, Inc.	Architectural Services	Gilbane Building Company

**Projects in Construction
MSBA Grant Basis and Maximum Grant Amount**

New Program and Wait List Program Totals			\$2,520,178,668	54,868		10,631,520											*Includes Alternates	\$1,762,708,267
Project	Grade	Contractor	Total Construction Cost*	Projected Enroll	PFA or Bid Data	Proposed Square Footage	Construction Cost per Square Foot	Building Cost	Building Cost per Square Foot	Project Type	Construction Start	Estimated Substantial Completion Date	Reporting Variance from Schedule	Physical Progress (%)	Change Orders (%)	Construction Status	Approximate Maximum Grant Amount *	
CAPITAL PIPELINE PROJECTS IN CONSTRUCTION																		
New Program Totals			\$2,431,555,704	52,808		10,167,830	\$237		\$178							\$1,601,645,632		
Arlington	K-5	G&R Construction	\$15,340,026	380	Bid	57,614	\$266	\$12,403,811	\$215	Design/Bid/Build	7-Apr-12	28-Jun-13		37%	0.72%	Exterior sheathing is progressing. Masonry has started at the North façade of the building. Temporary weather protection has been installed at window openings and roofing has been completed at Sections A & B of the building.	\$9,441,396	
Berlin-Boylston Tahanto Reg MS/HS	6-12	CTA	\$32,162,000	560	Bid	126,100	\$255	24,629,999	\$195	Design/Bid/Build	10-May-11	1-Jul-13		95%	2.02%	Students occupied the new school building on January 3, 2013. Punch list and Commissioning items are being completed after school hours. Abatement and demolition of the adjacent existing school will begin soon. Subsequently, ball field construction, final landscaping and site work will be completed.	\$19,849,301	
Billerica Parker ES	K-5	CTA	\$22,842,500	500	Bid	89,093	\$256	\$17,913,441	\$201	Design/Bid/Build	15-Sep-10	29-Aug-12	90 days	98%	-0.01%	The new building is substantially complete. Phase II, demolition and site work was completed November 21, 2012. Landscaping to be completed in the Spring.	\$15,851,020	
Brookline Heath ES	K-8	Nauset	\$6,284,185	560	Bid	80,952	\$78	\$4,807,436	\$59	Design/Bid/Build	29-Sep-11	15-Aug-12		98%	3.63%	Punch list work and commissioning remaining. Exterior punch list work to be completed in Spring.	\$3,173,407	
Brookline Runkle ES	PK-8	G&R Construction	\$20,715,300	560	Bid	104,000	\$199	\$17,668,440	\$170	Design/Bid/Build	10-Nov-10	10-Sep-12		95%	8.02%	Punch list work and commissioning remaining.	\$11,135,430	
Carlisle Carlisle K-8	K-8	H.V. Collins Co. Inc	\$15,277,344	700	Bid	140,312	\$109	\$11,342,751	\$81	Design/Bid/Build	9-Feb-11	31-Aug-12		99%	3.65%	Punch list work continues.	\$6,988,636	
Danvers Danvers HS	9-12	Bacon Construction	\$53,834,164	1,000	Bid	246,251	\$219	\$43,710,809	\$178	Design/Bid/Build	14-Nov-10	2-Jul-13		89%	2.15%	Phase I punch list work is ongoing. Phase II progress includes the completion of infrastructure and underground utilities as well as work in the cafeteria/lobby and kitchen. Work on the Central Offices and classrooms include completion of the MEP rough-ins and above ceiling work as well as commencement of drywall finishes.	\$37,324,055	
Douglas Douglas ES	2-5	CTA	\$23,857,111	552	Bid	83,100	\$287	\$19,026,763	\$229	Design/Bid/Build	Mar-12	9-Jun-13		26%	0.00%	Site work continues. Steel placement complete. MEP rough-ins, metal stud framing, exterior sheathing and roofing are underway.	\$17,573,941	
Douglas Douglas HS	6-8	CTA	\$12,081,767	448	Bid	88,245	\$137	\$9,417,212	\$107	Design/Bid/Build	Mar-12	31-Jan-14		20%	0.00%	Site work continues. No work is currently being performed while school is in session.	\$8,203,129	
Dracut Dracut HS	9-12	CTA	\$47,290,611	1,160	PFA	174,671	\$271	\$29,420,210	\$168	Design/Bid/Build	27-Aug-12	17-Dec-14		5%	0.00%	Site utilities, steel erection and MEP rough-ins are ongoing.	\$36,499,334	
East Bridgewater E. Bridgewater Jr/Sr HS	7-12	Fontaine Brothers	\$65,409,000	950	Bid	213,544	\$306	\$47,684,117	\$223	Design/Bid/Build	10-Aug-11	24-Jun-13		50%	0.91%	Site work drainage for Phase I is complete and the paving binder course has been placed. Window installation is complete except for the curtain walls. Drywall is complete in all classroom wings. Roof membrane is complete. Plastering and painting has begun.	\$43,317,092	
Easthampton Easthampton HS	9-12	Fontaine Brothers	\$30,934,000	510	Bid	110,400	\$280	\$24,511,000	\$222	Design/Bid/Build	16-May-11	25-Oct-13	21 days	89%	1.37%	Completing classroom finishes on first and second floors. MEP and fire protection finish work continues. Windows and exterior metal panels near completion. Completing all utility cable/fiber pulls to building. Substantial completion of building scheduled for January 15, 2013.	\$24,104,384	
Fairhaven Rogers ES	K-5	CTA	\$20,177,237	370	PFA	77,871	\$259	\$14,406,187	\$185	Design/Bid/Build	21-May-12	4-Jul-13		12%	0.00%	Structural steel erection and detailing for area B is complete and nearly complete in area A. Installation of sheathing is progressing. Plumbing and mechanical above ground has begun. Site work continues with installation of a new water service, drain manholes, catch basins and associated piping. Subgrade has been completed for parking lots and are ready for binder.	\$14,992,503	
Fall River Morton MS	6-8	J&J Contractors	\$37,654,000	625	Bid	130,576	\$288	\$29,921,971	\$229	Design/Bid/Build	4-Nov-11	15-Jun-13		56%	8.97%	Site work continues and binder course is complete. MEP rough-ins are underway. Window installation is scheduled to be completed by the end of January. Drywall completed on the 3rd floor and has begun on the 2nd floor. Temporary heat has been installed throughout the building.	\$38,251,808	
Foxborough Foxborough HS	9-12	CTA	\$11,469,333	885	Bid	218,500	\$52	\$8,845,000	\$40	Design/Bid/Build	25-Jan-10	31-Oct-11		100%	9.44%	Final completion achieved December 4, 2012.	\$7,226,509	
Franklin Franklin HS	9 - 12	Agostini/Bacon	\$87,914,728	1,650	PFA	325,000	\$271	\$62,777,616	\$193.16	Design/Bid/Build	16-Oct-12	15-Oct-14		2%	0.00%	Site work and utility installations underway. Footing and pier construction proceeding along with a substantial pending change order for removal of unsuitable soil materials.	\$54,558,408	
Hampden-Wilbraham Minnechaug HS	9-12	Fontaine Brothers	\$48,597,500	1,225	Bid	231,467	\$210	\$37,499,962	\$162	Design/Bid/Build	22-Jul-10	28-Jun-12		96%	2.29%	Work is completed except for misc. site work which will be completed in the Spring.	\$34,863,838	
Hingham Hingham MS	6-8	Brait Builders Corp.	\$50,432,439	1,020	PFA	176,385	\$286	\$38,006,989	\$215	Design/Bid/Build	7-Jun-12	30-Dec-14		25%	0.00%	Installation of under-slab plumbing and electrical systems continue. Steel erection has begun along with slab on grade placement.	\$25,909,580	
Hudson John F Kennedy MS	5-7	Agostini/Bacon	\$35,102,573	715	Bid	118,850	\$295	\$28,373,294	\$239	Design/Bid/Build	28-Sep-11	22-Nov-13		58%	1.37%	Interior drywall partitions are ongoing. Interior classroom mock ups are complete and moving towards build out.	\$24,005,749	
Lynnfield Lynnfield HS	9-12	E.A. Colangeli	\$2,886,991	740	Bid	10,950	\$264	\$2,322,687	\$212	Design/Bid/Build	25-Jun-12	1-Feb-13	7 days	60%	0.00%	Roof insulation, protection board, and EPDM rubber roof have been completed. Air vapor barrier has been installed to allow continued placement of brick veneer on all elevations. Expansion opening sealed and temporary heating installed to start drying process prior to finishes. MEP rough-ins are nearly complete on ground floor and continuing on first floor.	\$1,828,473	
Marblehead Glover ES	K-3	G&R Construction	\$20,868,000	425	Bid	79,108	\$264	\$16,977,513	\$215	Design/Bid/Build	25-Jun-12	9-Dec-13		12%	0.00%	Abatement and demolition of the existing elementary school is complete. Blasting and site prep is near completion. Footings and foundation work is in process.	\$9,688,418	
Marshfield High School	9 - 12	Brait Brothers	\$84,980,000	1,310	Bid	267,469	\$318	\$64,604,850	\$242	Design/Bid/Build	Aug-12	7-Jul-14		16%	0.10%	Underground utility work nearly complete. Construction of concrete foundations progressing and structural steel underway.	\$48,607,274	
Maynard Maynard HS	8-12	CTA	\$36,650,000	410	Bid	121,520	\$302	\$30,630,013	\$252	Design/Bid/Build	18-Aug-11	6-Dec-13		57%	0.81%	The installation of stairs and misc. metals are ongoing throughout the building. Curtain wall, storefront entrances and windows are near complete. Wall framing in Areas C & D and drywall finishes in areas C & B are ongoing.	\$23,483,860	
Middleton Howe-Manning ES	4-6	CTA	\$18,210,000	553	Bid	83,934	\$217	\$14,529,671	\$173	Design/Bid/Build	06-Apr-10	30-Jul-11		100%	6.93%	Final completion achieved November 30, 2012.	\$12,311,976	
Nashoba Pompositticut ES	K-5	P.J. Stella Construction/Brait Builders	\$23,640,900	600	Bid	98,030	\$241	\$18,427,425	\$188	Design/Bid/Build	15-Jun-10	31-Aug-12		100%	3.93%	Project is complete with a few remaining punch list items and minor control issues.	\$15,239,622	
Natick Natick HS	9-12	Brait Builders Corp.	\$63,303,452	1,300	Bid	254,225	\$249	\$53,213,182	\$209	Design/Bid/Build	13-Sep-10	15-Jun-12		94%	3.35%	Punch list work ongoing. Site work to be completed in the Spring.	\$38,209,033	
Norfolk County Agricultural HS	9-12	TLT Construction Corp.	\$21,508,952	550	PFA	114,816	\$187	\$15,546,739	\$135	Design/Bid/Build	27-Mar-12	9-May-14	14 days	35%	0.21%	Animal Science building's MEP work is ongoing while structural masonry and stairs are complete. Agricultural Mechanical building's MEP work and roof installation are ongoing. Pre-engineered buildings for Equine Building and Equipment Garage released to manufacturer to start work.	\$14,119,915	
Norfolk Freeman-Kennedy ES	3-6	Fontaine Brothers	\$25,354,966	585	Bid	96,410	\$263	\$20,023,001	\$208	Design/Bid/Build	9-Nov-10	10-Jun-12		98%	4.00%	Asbestos has been discovered in Phase III demo of the existing building and has caused a slight delay. Final paving and seeding to be completed in the Spring.	\$15,861,760	
Norwood Norwood HS	9-12	Agostini	\$54,400,480	1,100	Bid	227,374	\$239	\$42,573,646	\$187	Design/Bid/Build	19-May-09	13-May-11		100%	2.40%	The project is complete.	\$38,154,487	
Oxford Oxford MS	5-8	S.O.M.	\$5,085,217	652	Bid	117,000	\$43	\$5,085,217	\$43	Design/Bid/Build	1-Jun-12	26-Aug-13		25%	12.13%	Roof replacement complete. HVAC, window, and floor replacement work scheduled for Summer 2013.	\$3,483,589	
Plymouth Plymouth HS	9-12	J&J Contractors	\$67,687,000	1,350	Bid	267,497	\$253	\$51,579,703	\$193	Design/Bid/Build	3-May-10	22-Jun-12	30 days	98%	4.75%	Punch list work ongoing. Site work to be completed in the Spring.	\$41,810,972	
Quincy Central MS	6-8	H.V. Collins Co. Inc	\$32,699,769	620	PFA	114,975	\$284	\$27,182,118	\$236	Design/Bid/Build	24-May-12	5-Sep-13	14 days	18%	0.00%	Footings, foundations and structural steel are underway. Steel complete at bldg "A". Site utilities underway. Under-slab concrete placed at the gym.	\$32,949,685	
Somerset Berkley Somerset Berkley RHS	9-12	Bacon-Agostini	\$69,407,000	1,000	Bid	222,826	\$311	\$52,042,575	\$234	Design/Bid/Build	3-Jul-12	15-Aug-14		13%	0.28%	Most underground utility and building foundation work complete. Structural steel erection underway and anticipated to complete in January/February 2013.	\$49,050,210	
Sturbridge Burgess ES	K-6	Fontaine Brothers	\$22,946,000	860	Bid	131,630	\$174	\$17,591,000	\$134	Design/Bid/Build	10-Aug-10	1-Oct-12		98%	7.00%	Both the new addition and the adjacent building renovations are complete and in use. Abatement and demolition of the existing school have been completed. Construction of play area, ball fields and final landscaping are in process and are scheduled for completion in Spring 2013.	\$16,616,077	
Sutton MS/HS	6-12	TLT Construction Corp.	\$41,230,800	840	Bid	179,040	\$230	\$32,998,403	\$184	Design/Bid/Build	1-Jul-11	31-Dec-14	120 days	49%	0.49%	Boiler assembly is underway. Electrical work is ongoing. Drywall installation has commenced.	\$27,837,016	

**Projects in Construction
MSBA Grant Basis and Maximum Grant Amount**

Project	Grade	Contractor	Total Construction Cost*	Projected Enroll	PFA or Bid Data	Proposed Square Footage	Construction Cost per Square Foot	Building Cost	Building Cost per Square Foot	Project Type	Construction Start	Estimated Substantial Completion Date	Reporting Variance from Schedule	Physical Progress (%)	Change Orders (%)	Construction Status	Approximate Maximum Grant Amount *
Tewksbury Tewksbury HS	9-12	CTA/Methuen Construction Co.	\$51,600,000	1,100	Bid	218,781	\$236	\$40,159,651	\$184	Design/Bid/Build	15-Oct-10	3-Aug-12		88%	3.59%	Punch list work ongoing. Site work to be completed in the Spring.	\$36,622,570
West Springfield West Springfield HS	9-12	Fontaine Brothers	\$85,006,020	1,270	Bid	257,525	\$330	\$56,875,181	\$221	Design/Bid/Build	14-Dec-11	31-Dec-13		53%	0.15%	Exterior masonry continues at Bldg C & D. Interior framing and MEP rough-ins continue in Bldg A, B & C. Steel installation for the Natatorium is ongoing. Drywall installation has begun in Bldg A & B.	\$68,808,290
Weston Field ES	4-5	Colantonio	\$23,999,534	355	PFA	65,390	\$367	\$14,364,472	\$220	Design/Bid/Build	21-Dec-12	15-May-14		2%	0.15%	Early septic tank work complete. New building site work and foundations have begun. PCB encapsulation within existing building complete for continued occupation.	\$8,610,302
Winchester Vinson-Owen ES	K-5	CTA	\$21,290,000	420	PFA	74,774	\$285	17,586,599	\$235	Design/Bid/Build	17-Feb-12	13-May-13		39%	1.79%	Footings, foundations and structural steel are complete. Site utilities continue. Slabs-on-deck placed. Metal stud framing, sheathing and GWB underway.	\$10,292,465
Adams-Cheshire Hoosac Valley MSHS	6-12	Gilbane	\$33,474,193	805	Bid	174,758	\$192	24,009,952	\$137	CM-R	17-May-11	31-Jul-12		99%	2.29%	Commissioning is ongoing and is scheduled to be completed at the end of January. PV installation activated on December 28th. Punch list work continues.	\$28,243,131
Ashburnham Westminster, Briggs ES	PK-5	Consigli	\$24,780,000	520	Bid	87,085	\$285	18,202,478	\$209	CM-R	9-Mar-12	31-Dec-13		47%	0.09%	Phase I site work, site utilities and foundation work are substantially complete. Steel erection is complete, the building is framed, sheathed, waterproofed and masonry is complete. Roofing system is nearly complete. Mechanical, plumbing, electrical and fire protection rough-ins are ongoing on both floors with a majority of interior framing complete.	\$16,353,447
Burlington Marshall Simonds MS	6-8	CTA	\$24,612,440	880	Bid	151,000	\$163	\$18,988,987	\$126	CM-R	15-Apr-11	17-May-13	150 days ahead	95%	2.77%	Punch list work is in progress in the renovated areas. Athletic field work has commenced with the installation of underground infrastructure, drainage, electrical and light pole foundations.	\$16,933,103
Dedham Avery ES	K-5	Consigli	\$18,174,209	310	Bid	62,723	\$290	\$13,528,098	\$216	CM-R	15-Oct-10	1-Jan-12		99%	6.50%	Final punch list work is complete. Architect verification in process.	\$10,778,452
Duxbury HS	6-12	Dimeo	\$104,511,661	1,735	PFA	322,105	\$324	\$66,940,020	\$208	CM-R	9-Jul-12	9-Jun-14		13%	0.00%	Site work continues with excavation & backfill and placement of structural fill for building slabs. Main building foundation work has substantially completed with some work remaining in area D. Site utility work continues with drainage and gas service. Structural steel arrived on site and installations have commenced.	\$51,406,497
Essex North Shore Agricultural & Technical School	9-12	Gilbane	\$99,484,995	1,440	PFA	337,000	\$295	\$68,270,270	\$203	CM-R	7-May-12	30-Jun-14		20%	0.00%	Under-slab utilities ongoing. Slabs-on-deck nearly complete. Slabs-on-grade and roof installation started week of January 7th. Installing permanent power to farmstead area. Site development of upper Middleton fields, including retaining walls, continues.	\$77,500,000
Grafton Memorial Sr HS	9-12	Dimeo	\$54,881,977	900	Bid	186,000	\$295	\$41,783,110	\$225	CM-R	18-Aug-10	12-Jul-12		100%	5.80%	Project is complete and currently removing temporary access and barricades and completing punch list items. Continuing all required owner training.	\$36,108,679
Leominster Leominster SHS	9-12	S.O.M.	\$33,794,797	1,825	Bid	295,859	\$114	\$25,382,707	\$86	CM-R	1-Jul-11	30-Aug-13		79%	5.26%	Renovation work in the existing Science, Health Occupations, and Life Skills areas is ongoing. Rough installation of plumbing, underground plumbing, rough sprinkler, rough HVAC and temperature control wiring has been completed.	\$30,693,543
Lexington Estabrook ES	K-5	Shawmut Design	\$31,145,045	540	PFA	91,840	\$339	\$19,420,993	\$211	CM-R	20-Jun-12	15-Aug-14		7%	0.00%	Current activities include building foundation, water loop extension, and ductbank with temporary electrical. Early site work and site utilities complete.	\$13,132,418
Longmeadow Longmeadow HS	9-12	Gilbane	\$63,685,998	1,000	Bid	236,985	\$269	\$46,573,364	\$197	CM-R	Nov-10	1-Nov-13		68%	0.82%	Interior finish work and final cleaning are ongoing in the new section of the school. Furniture deliveries are ongoing. Work continues in the Auditorium and the Admin offices.	\$33,067,140
Medway MS	5-8	Consigli	\$18,211,824	800	Bid	223,780	\$81	\$12,885,464	\$58	CM-R	Oct-11	12.21.12	60 days ahead	93%	1.46%	This is a 4-phase project. Phase 1 and 2 were completed as scheduled and the Phase 1 area was turned over on April 18, 2012. Currently working on Phase 1 and 2 punch lists. Phase 3, to get the school ready for the students return, was completed on August 15, 2012. Substantial completion was issued on December 21, 2012 for the entire project phases 1-3. Punch list and project closeout are ongoing.	\$10,352,981
Methuen Methuen HS	9-12	Terminated Dimeo 12/31/2011. Consigli as of 5/21/2012	\$74,917,204	2,075	PFA	368,017	\$204	\$63,689,716	\$173	CM-R	21-Jul-11	Jun-14		20%	0.60%	MEP rough-in work is on going as well as asbestos abatement in the south wing, skylight opening preparation and roofing work. Steel erection at the addition is complete.	\$64,734,701
Needham Newman ES	K-5	Consigli	\$19,064,745	754	Bid	119,264	\$160	\$13,367,855	\$112	CM-R	16-Jun-10	27-Aug-12		99%	8.40%	Punch list work is ongoing.	\$8,598,929
Norton Norton HS	9-12	WT Rich	\$27,023,541	700	Bid	130,755	\$207	\$20,590,559	\$157	CM-R	12-Mar-12	27-Dec-13		40%	3.15%	Interior finishes are progressing in the addition. Food service equipment installations in the new kitchen are progressing. Piping for hot water heaters in the mechanical room is underway.	\$21,484,408
Rockland John Rogers MS/ HS	5-12	Agostini	\$66,362,037	1,525	Bid	275,700	\$241	\$47,724,091	\$173	CM-R	15-Jan-10	8/31/12 for MS 12/31/12 for HS		93%	4.41%	Phase 4 work continues in the High School. The Band Room, TV Studios, HS Administration Offices and HS/MS Art Classrooms are complete. Stair #5 work is ongoing. SPED classrooms and District School Offices demolition have commenced. Site work continues around the campus. All curbing is complete and all binder courses have been placed. Pedestrian walkways are 80% complete. Exterior tennis courts and basketball courts will be completed in the Spring. Punch list work related to Phase 2, 3 and 4 is being addressed.	\$52,837,940
Saugus Belmonte Middle School	6-8	Consigli	\$15,712,630	709	PFA	160,000	\$98	\$11,141,407	\$70	CM-R	23-May-12	23-Aug-13		35%	1.00%	Phase 1A and 1B are 100% complete. Phase 2 started January 1. Students and teachers moved from 2nd Floor to newly renovated classrooms on 1st floor over the Christmas break. 2nd floor is now well under construction with all abatement completed over the break. All windows have been removed from the 2nd floor and MEP rough-ins are proceeding well.	\$10,097,544
Shrewsbury Sherwood MS	5-6	Gilbane	\$33,986,286	900	Bid	129,378	\$263	\$22,823,030	\$176	CM-R	7-Mar-11	31-Oct-13		95%	2.00%	Punch list and commissioning activities are in process. Students will occupy the new school on January 23, 2013. Exterior landscaping and paving work is in process. Abatement and demolition of the old school building is expected to begin in early 2013.	\$22,369,828
Somerville E. Somerville Community School	K-8	Gilbane	\$32,590,244	500	Bid	121,100	\$269	\$24,613,842	\$203	CM-R	7-Nov-11	29-Mar-13		76%	0.30%	Interior finishes continue within the classrooms. MEP finishes have also begun. Binder course of paving has been completed.	\$15,237,996
Southbridge Southbridge MS/HS	6-12	Consigli	\$59,307,632	1,050	Bid	199,740	\$297	\$41,487,200	\$208	CM-R	30-Nov-10	18-Jun-12	77 days	99%	0.56%	Minor punch list and landscape maintenance work remaining to be completed in the Spring. Project closeout is in progress.	\$52,019,398
Southeastern Regional Voc Tech High School	9-12	WT Rich	\$26,576,567	1,370	PFA	308,250	\$86	\$17,611,703	\$57	CM-R	27-Jun-11	20-Jan-14		40%	0.20%	Phase II, Interior Renovation work, is complete. The new Gymnasium addition has also received a Certificate of Occupancy. Work is in process to complete the Dental Assisting Suite and Building 2 and 6 renovations. Roof top units are being connected to the building systems. Installation of the new elevator is in process. Final site landscaping work will be completed in Spring/Summer 2013.	\$25,988,607
Uxbridge High School	9-12	Shawmut Design	\$37,293,765	600	Bid	123,000	\$303	\$27,562,625	\$224	CM-R	28-Feb-11	20-Jun-12		93%	2.50%	Minor punch list work remaining within the building. Field work to be completed in the Spring.	\$21,973,620
Wayland ** Wayland HS	9-12	Shawmut Design	\$54,230,819	900	Bid	171,000	\$317	\$37,343,299	\$218	CM-R	28-Jun-10	1-Dec-11		99%	2.76%	Misc. punch list work to be completed during February vacation week. Misc. landscaping work to be completed in the Spring.	\$24,051,231
Wellesley Wellesley HS	9-12	Turner	\$82,942,222	1,500	Bid	280,000	\$296	\$55,814,300	\$199	CM-R	24-Aug-09	1-May-13		99%	4.59%	Remaining site and utility work is complete. Binder course paving, curbing and sidewalk installations have been completed. Punch work is ongoing.	\$40,117,222
** Excludes Field House																	
Wait List Program Totals			\$120,784,964	2,060		463,690											\$141,213,334
Springfield Forest Park MS	6-8	Consigli	\$34,745,898	660	Bid	148,800	\$234	\$26,209,932	\$176	CM-R	26-Mar-12	26-Jul-13		37%	0.00%	MEP work is ongoing on all floors. Window installation is in progress as well as roof work. Drywall has started on interior partition walls.	\$38,340,497
Springfield Putnam Voc Tech HS	9-12	Consigli	\$86,039,066	1,400	Bid	314,890	\$273	\$62,949,742	\$200	CM-R	18-May-10	20-Jul-12		93%	0.66%	Demolition of existing building is complete. Punch list work on new building is nearly complete. Paving for rear parking lot is complete. Binder was placed at Alton Street lot. All contaminated soil has been removed from site.	\$102,872,837
Worcester North HS	9-12	Gilbane	\$49,145,638	1,200	Bid	239,570	\$205	\$40,860,983	\$171	CM-R	24-Sep-08	Jun-11		99%	3.20%	Phase 4, which includes the parking lots and reconstruction of the ball fields, will be completed in the Spring.	\$45,911,881
