


Project Overview Report

May 22, 2013

A total of 331 projects that have received invitations from the Board of Directors (“Board”) to collaborate with the MSBA are currently in the MSBA’s Eligibility Period and Capital Pipeline. The following summary chart provides the number of projects in the Eligibility Period and each phase of the Capital Pipeline:

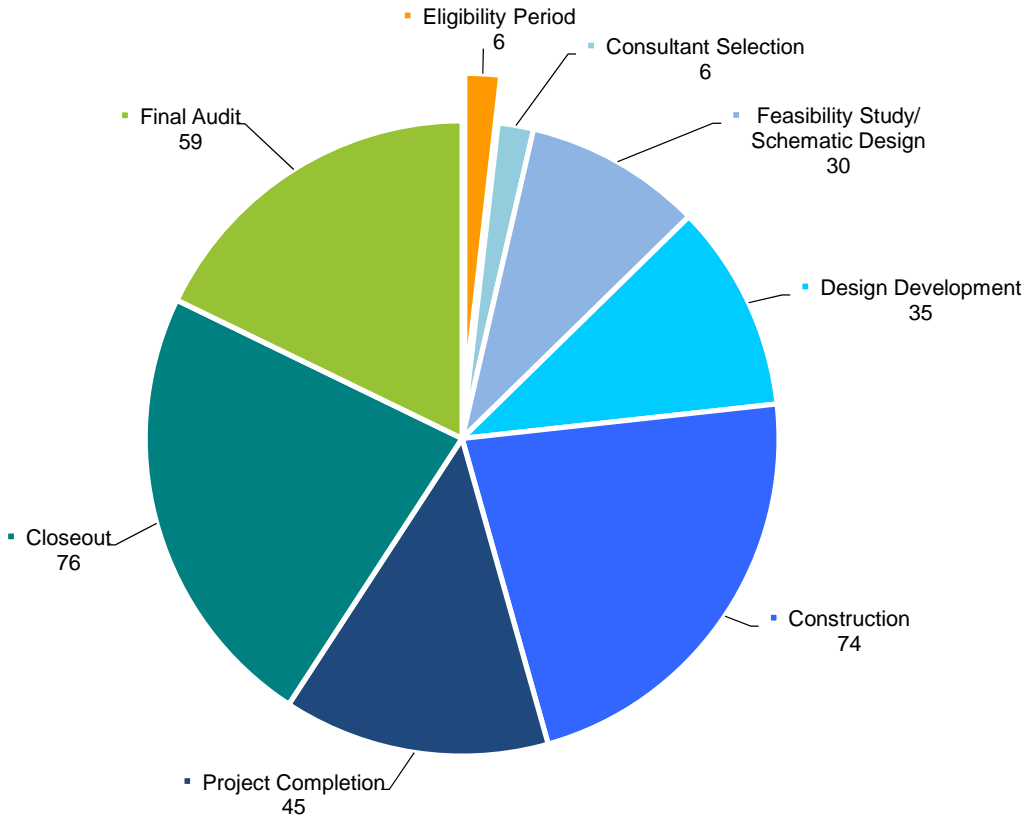

Statement of Interest (“SOI”) Review Status

The Fiscal Year 2013 Statement of Interest Process opened on January 9, 2013 and closed on April 10, 2013. 117 Districts submitted 201 Statements of Interest.

The Districts have identified the potential scope of the 201 SOIs as follows:

- 37 – New Construction
- 66 – Addition/Renovation
- 98 – Repair

In the coming weeks the MSBA will complete review of the SOI hard copy submissions to confirm that each SOI has been submitted properly with the required local votes, signatures of local officials, and other support documentation.

77 of the 201 SOIs are being considered for participation in the Accelerated Repair Program. 43 of these SOIs will be invited into the Accelerated Repair Program at the June Board meeting. Additional invitations into the 2013 Accelerated Repair Program may be made at the July Board meeting. SOIs that are not invited into the Accelerated Repair Program will be reviewed for potential participation in the Core Program.

Eligibility Period

There are six districts in the Eligibility Period. Three districts: Dedham, Granby and Holyoke, are seeking local funding and authorization within the next 60 days. Two of the six districts have already secured funding. The remaining district has yet to confirm its date for action.

An agreed-upon enrollment is a key prerequisite for the MSBA to commence a Feasibility Study with a district. To begin the enrollment projection process, a district must file enrollment information utilizing the MSBA's online enrollment projection tool. Since the last report, one district has completed the enrollment process.

Based upon the schedules anticipated by the districts for completion of the Eligibility Period requirements, staff anticipates recommending the six districts in Eligibility Period for an Invitation to Feasibility Study at upcoming Board meetings.

Capital Pipeline

Consultant Selection

After the district has completed all Eligibility Period requirements and has received a Board Invitation to Feasibility Study, the district procures an Owner's Project Manager ("OPM"). There are two districts in the Capital Pipeline that need to procure an OPM.

After a district has selected and executed a contract with an OPM, it selects a Designer utilizing either a local designer selection process for projects under \$5 million or the MSBA's Designer Selection Panel ("DSP") for projects over \$5 million. There are four districts in the Capital Pipeline that are in the process of procuring a Designer.

Feasibility Study

Once a district has procured an OPM and Designer and a Feasibility Study Agreement has been executed, the district and its consultants must complete two Feasibility Study submittals, the Preliminary Design Program and the Preferred Schematic Report, prior to Board consideration to proceed into Schematic Design. Based on the most recent data and schedules provided to the MSBA by districts, the MSBA anticipates that 10 districts will present their preferred schematic designs to the Board at the upcoming July and October Board meetings.

Prior to consideration by the Board for Project Scope and Budget Agreement authorization, a district must submit a schematic design to the MSBA for review. Based on the most recent data and schedules provided to the MSBA by districts, the MSBA anticipates that eight districts will appear before the Board for Project Scope and Budget Agreement authorization at the upcoming July and October Board meetings.

Commissioning

Since the last report, the MSBA has assigned Commissioning Consultants to an additional six projects as presented in the table below. To date, the MSBA has executed 231 Commissioning Consultant contracts, totaling \$17.9 million; 54 contracts have been completed.

District	School	Estimated Const. Cost (million)	Commissioning Consultant	Contract Amount
Revere	William McKinley Elementary School	\$40.00	RFS Engineering	\$92,248
South Hadley	Plains School	\$20.00	Strategic Building Solutions	\$74,784
Wachusett Regional	Mountainview Middle School	\$40.00	Fitzmeyer & Tocci	\$94,651
Canton	-Lt. Peter Hansen Elementary, Galvin Middle School – Accelerated Repair: Windows	\$1.75	Simpson Gumpertz & Heger	\$55,000
North Adams	Silvio O. Conte Middle School	\$28.00	RFS Engineering	\$83,589
Chicopee	Chicopee Academy	\$20.00	SMMA	\$132,318
Total		\$149.75 million	Total	\$532,590

Design Development

Once a district has secured local funding and has entered into a Project Funding Agreement with the MSBA, it enters the Design Development phase. Currently, there are 35 projects in the Design Development phase with a total estimated construction cost of \$482.8 million: 21 Accelerated Repair projects, one Science Lab Initiative project, and 13 Core Program projects. The 13 Core Program projects in Design Development have a total estimated construction cost of \$449.2 million:

Elementary School Districts

Georgetown
South Hadley
Webster

Middle School Districts

Auburn
North Adams
Springfield (Brookings)

High School Districts

Ayer Shirley Regional
Greater Lowell Regional Technical
Greater New Bedford Regional Technical
Old Colony Regional Technical
Southern Worcester Regional Technical
Southwick-Tolland-Granville Regional
West Bridgewater

Construction

When a district issues a Notice to Proceed, the project is advanced to the Construction Phase. Currently, there are 74 projects in the Construction phase with a total estimated construction cost of \$2.2 billion: seven Green Repair projects, 12 Accelerated Repair projects, seven Science Lab Initiative projects, 47 Core Program projects, and one Waiting List project. The 47 Core Program projects have a total estimated construction cost of \$2.04 billion and are listed below.

Elementary School Districts	Middle and Middle/High School Districts	High School Districts
Andover	Douglas	<u>Addition/Renovation</u>
Arlington	Fall River	Assabet Valley Regional Technical
Ashburnham-Westminster Regional	Hingham	Danvers
Douglas	Hudson	Dracut
Fairhaven	Newburyport (Nock)	Greenfield
Lexington	North Reading	Leominster
Marblehead	Oxford	Methuen
Newburyport (Bresnahan)	Quincy	Norfolk County Agricultural
Springfield (Dryden)	Rockland	Norton
Williamsburg	Saugus	Southeastern Regional Voc/Tech
Westfield	Stoneham	
Weston	Sutton	<u>New</u>
Winchester	Wakefield	Concord-Carlisle Regional
		Essex/North Shore Regional Voc/Tech
		Longmeadow
		Maynard
		Wilmington
		<u>Model</u>
		Duxbury
		East Bridgewater
		Franklin
		Marshfield
		Monomoy Regional
		Somerset-Berkley Regional
		West Springfield

Core Program – Total Project Budget Update

Upon receiving the Board’s approval of the Project Scope and Budget, the MSBA and participating districts enter into a Project Funding Agreement that establishes the Total Project Budget and the Estimated Maximum Total Facilities Grant for an approved project. Of the grants authorized by the Board, eight projects have increased their Total Project Budgets due to acceptance of construction bids higher than the project estimates. In no event has the increase in budget resulted in an increase to the Estimated Maximum Total Facilities Grant as authorized by the Board. Please also note that staff reported on the budget increases for the five projects shaded below at previous Board meetings.

District	School Name	Scope	Project Funding Agreement		PFA Bid Amendment		Reason for Increase to Total Project Budget
			Total Project Budget	Total Maximum Facilities Grant	Total Project Budget	Total Maximum Facilities Grant	
Core Program							
Andover	Bancroft Elementary School	New	\$44,659,837	\$16,773,753	\$50,374,837	TBD*	The District has appropriated additional funds to cover the costs associated with increased construction costs and additional contingencies for litigation/settlement costs and other ineligible costs.
Essex North Shore Agricultural & Technical School	Essex North Shore Agricultural & Technical School District	New	\$125,000,000	\$77,500,000	\$133,770,000	\$77,500,000	The Board was informed at the March 30, 2011 meeting that the Total Project Budget had increased due to additional ineligible scope that would be funded by DCAM.
Lexington	Estabrook Elementary School	New	\$40,792,248	\$12,250,739	\$42,554,862	TBD*	The District has executed a GMP that exceeds the Construction Budget of the PFA. The District is currently reviewing its project budget to determine the use of the additional appropriation funds it appropriated in excess of the Total Project Budget.
Somerville	East Somerville Community School	Add/Reno	\$33,185,258	\$15,237,996	\$38,006,621	\$15,237,996	At the March 28, 2012 Board Meeting, the Board approved an amendment to the PFA and a \$6.25M District loan.
Uxbridge	Uxbridge High School	New	\$43,000,000	\$22,362,328	\$44,986,479	\$22,362,328	The District has appropriated additional funds to cover the costs associated with the construction of athletic fields originally included in the PFA but which were not included in the bid as the District's construction contract would have exceeded the budget.


**A PFA Bid Amendment has not been developed to calculate a revised total facilities grant amount. The Total Maximum Facilities Grant will not exceed the Board authorized amount in the PFA but upon review may decrease.*

Further, MSBA staff notes that North Reading has reported construction costs higher than its project estimates. Staff is awaiting information from the district and will provide updates to the Board as they become available.

In the last report it was noted that Stoneham had reported construction costs higher than its project estimates, however, the District has informed the MSBA that no increase to its Total Project Budget is required at this time.

Status of Green Repair Program

169 projects participating in the Green Repair Program have received authorization to enter into a PFA, totaling \$366,647,226 in Total Project Costs and \$222,885,258 in MSBA grants.

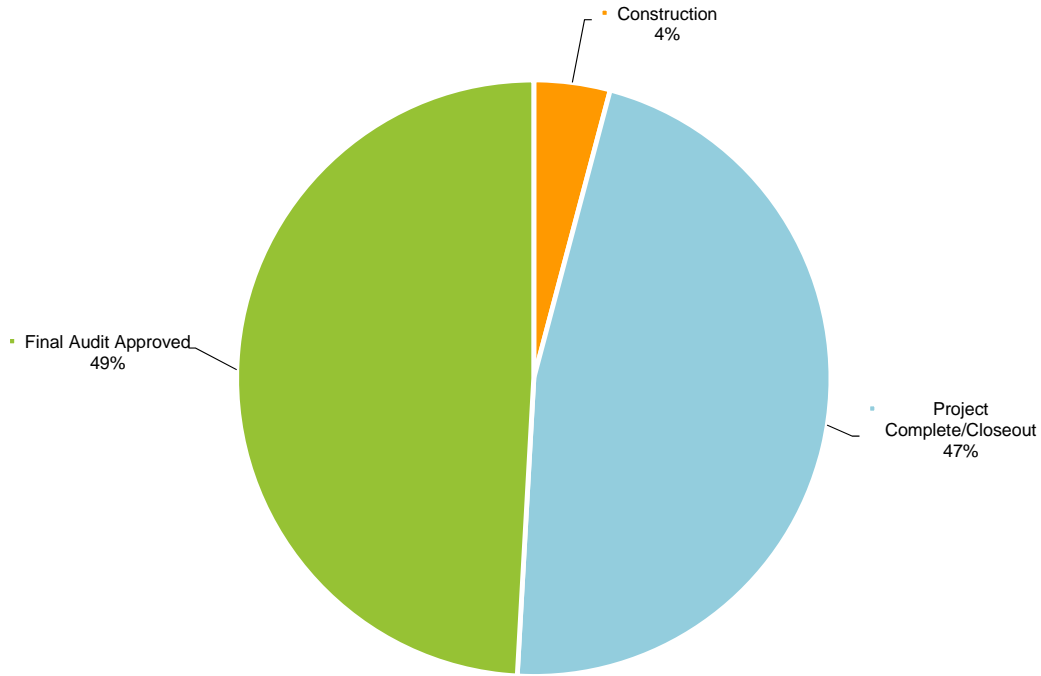

Green Repair – Schedule Extension Update

Eight of the 169 Green Repair Projects did not meet their anticipated construction completion deadline in 2012. Schedule delays can be attributed to bid protests, lead time for windows, and construction delays on site.

The MSBA granted each district a conditional extension to its Project Funding Agreement pending compliance with the following stipulations:

- The district must submit a detailed, revised construction timeline showing how the work will be completed at each school by no later than August 30, 2013;
- An Amendment to the Project Funding Agreement between the MSBA and the district must be executed to include the updated project schedule; and
- Any costs that may result from the district’s requested extension of the construction schedule will be the sole responsibility of the district and are categorically ineligible for reimbursement by the MSBA.

Each of these projects has a revised construction schedule and will be complete by the beginning of the 2013-2014 school year. In no event has the extended schedule resulted in an increase to the Estimated Maximum Total Facilities Grant as authorized by the Board. Please note that staff reported on the schedule extensions for the eight projects shaded below at previous Board meetings: ***No changes to this report.***

District	School	Scope	Original Construction Completion Date	Updated Construction Completion Date	Reason for Schedule Extension
Brockton	Brockton High School	Windows and Roof	31-Dec-12	30-Aug-13	Construction fell behind schedule and the District did not want work being done in an occupied building. The roof work is complete.
Haverhill	Consentino Middle School	Windows and Boiler	31-Dec-12	31-May-13	Bid protests and lead times caused the window project to extend beyond the 2012 construction deadline. The boiler project is complete.
Haverhill	John G. Whittier Middle School	Windows	31-Dec-12	31-May-13	Bid protests and lead times caused the window project to extend beyond the 2012 construction deadline.
Lowell	Moody Elementary School	Windows	15-Aug-12	30-Aug-13	Construction fell behind schedule and the District did not want work being done in an occupied building.
Lowell	Washington Elementary School	Windows	15-Aug-12	30-Aug-13	Construction fell behind schedule and the District did not want work being done in an occupied building.
Shrewsbury	Spring Street Elementary School	Roof and Windows	24-Dec-12	31-Jan-13	The district issued a change order to add shrouds over the window wall unit ventilators.
Wachusett Regional	Thomas Prince Elementary School	Roof	23-Mar-12	30-Apr-13	The district issued a change order to replace an existing skylight and due to lead times the work cannot be done until the spring of 2013.
Westport	Westport High School	Roof	4-Sep-12	30-Apr-13	The district issued a change order to add scuppers to the roof and the work will be completed in the spring of 2013.


Green Repair - Total Project Budget Update

Upon receiving the Board's approval of the Project Scope and Budget, the MSBA and participating districts enter into a Project Funding Agreement that establishes the Total Project Budget and the Estimated Maximum Total Facilities Grant for an approved project. Of the 169 grants authorized by the Board for the Green Repair Program, 15 projects have increased their Total Project Budgets due to acceptance of construction bids higher than the project estimates, or as a result of change orders issued on the project. In no event has the increase in budget resulted in an increase to the Estimated Maximum Total Facilities Grant as authorized by the Board. Please also note that staff reported on the budget increases for all 15 of the projects shaded and shown below at previous Board meetings. Last report, it was reported that the Boston, for its Excel High School project, had elected to accept and appropriate funds for a base bid that was higher than the approved budget. Since then, the project has exhausted the construction contingency with approved change orders resulting in an increase in the District's Total Project Budget.

District	School Name	Scope	Project Funding Agreement		PFA Bid Amendment		Reason for Increase to Total Project Budget
			Total Project Budget	Total Maximum Facilities Grant	Total Project Budget	Total Maximum Facilities Grant	
Green Repair Program							
Arlington	M. Norcross Stratton Elementary School	Roof, Window, Boiler	\$2,445,395	\$739,336	\$2,445,395	\$739,336	Change Orders exhausted the construction contingency.
Boston	Excel High School	Roof	\$1,227,180	\$908,850	\$1,454,735	\$908,850	District elected to accept the base bid that was higher than the approved budget. District appropriated additional funds to support overage.
Boston	Excel High School	Roof	\$1,454,735	\$908,850	\$1,544,018	\$908,850	Change Orders exhausted the construction contingency.
Brockton	Hancock Elementary School	Roof	\$2,292,164	\$1,814,937	\$2,422,742	\$1,814,937	District elected to accept the base bid that was higher than the approved budget. District appropriated additional funds to support overage.
Brockton	West Junior High School	Roof	\$2,742,386	\$2,171,001	\$3,069,905	\$2,171,001	District elected to accept the base bid that was higher than the approved budget. District appropriated additional funds to support overage.
Fitchburg	South Street Elementary School	Boiler	\$701,186	\$560,949	\$705,391	\$501,079	Change Orders exhausted the construction contingency.
Florida	Gabriel Abbott Memorial School	Roof	\$380,310	\$213,172	\$389,422	\$188,804	Project included \$80,153 in Change Orders that offset bid savings and exhausted the construction contingency.
Hancock	Hancock Elementary School	Roof/HVAC	\$277,450	\$125,740	\$400,805	\$125,740	District elected to accept the base bids in Phases 2 and 3 that were higher than the approved budget. District needs to appropriate the overage.
Lexington	Lexington High School	Roof	\$1,122,890	\$381,221	\$1,197,444	\$381,221	District elected to accept base bid and alternates. District appropriated additional funds to support overage.
Narragansett Regional	Phillipston Memorial Elementary School	Boiler	\$143,225	\$85,712	\$161,232	\$83,275	District elected to accept the base bid that was higher than the approved budget. District appropriated additional funds to support overage.
North Attleborough	Falls Elementary School	Windows	\$701,263	\$361,433	\$710,000	\$348,948	District elected to accept the base bid that was higher than the approved budget. District's original appropriation was for \$710,000; therefore the overage was covered.
Peabody	John E. Burke Elementary School	Roof, Window, Boiler	\$2,909,873	\$1,452,745	\$3,473,534	\$1,431,417	District elected to accept the base bid that was higher than the approved budget. District appropriated additional funds to support overage.
Peabody	William A. Welch Elementary School	Roof	\$1,280,511	\$646,728	\$1,437,800	\$630,732	District elected to accept the base bid that was higher than the approved budget. District appropriated additional funds to support overage.
Pentucket Regional	Dr. John C. Page Elementary School	Roof, Window, Boiler	\$3,148,424	\$1,618,920	\$3,272,630	\$1,618,920	District elected to accept the base bid that was higher than the approved budget. District appropriated additional funds to support overage.
Reading	Birch Meadow Elementary School	Window	\$735,846	\$347,393	\$787,640	\$347,393	District elected to accept the base bid that was higher than the approved budget. Town Accountant certified that the FY2011 School Committee Operating Budget had an appropriation and encumbrance for the additional costs of the project.
Westfield	Westfield Vocational Technical High School	Roof, Window, Boiler	\$8,442,762	\$5,296,989	\$8,895,495	\$5,296,989	District elected to accept the base bid that was higher than the approved budget. District also approved an amendment to its Designer contract which increased the fee. District appropriated additional funds to support overage.

Status of Accelerated Repair Program

Currently there are a total of 24 districts, representing 36 projects, in the Accelerated Repair Program. All projects are under contract with consultants and have advanced into the Preferred Schematic or Project Scope and Budget Phases. 36 projects have been authorized to enter into a PFA, totaling \$63,009,653 in Total Project Costs and a maximum of \$38,267,952 in MSBA Total Facilities Grant funding.

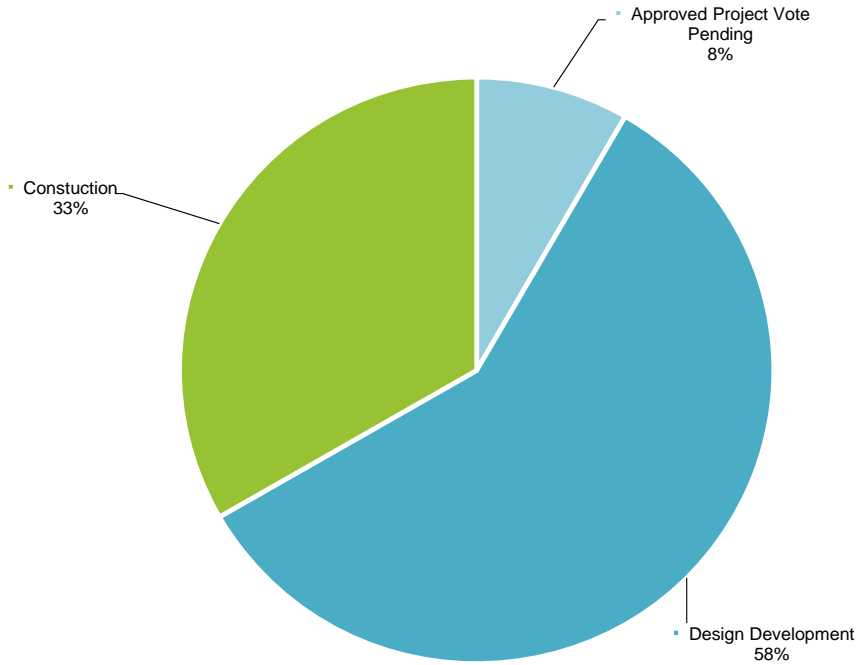


Of the 36 projects, 29 are scheduled to complete construction in 2013, and seven are scheduled to complete construction in 2014.

2012-2013 Eligibility Period Status

May 22, 2013

6 Projects in Eligibility Period

Task Remaining
 Partial Task Completed
 Invite / Completion Date
 Completed Task



District	2012		2013												2014		
	Nov	Dec	Jan	Feb	Mar	April	May	June	July	Aug	Sept	Oct	Nov	Dec	Jan	Feb	
Holyoke Lt. McMahon ES	11/14/12	11/28/12	12/28/12	1/28/13				5/27/13									
Scituate Gates IS																	
Woburn Wyman ES																	
Dedham Early Education Center				1/30/13	2/14/13	3/16/13	4/16/13	5/14/13		8/13/13							11/12/13
Granby West Street School																	
Spencer - East Brookfield David Prouty High School							4/3/13	4/17/13			7/16/13		10/14/13				1/13/14

45

Project Status | May 22, 2013

Core Program:	93
Waitlist:	1
Green Repair:	7
Accelerated Repair:	36
Science Lab Initiative:	8
Project Complete / Substantial Completion:	45
Closeout:	76
Final Audit Approved:	59
Total Projects:	325

Final Audit Approved / Removal

Abington Wooddale ES	Boston Thomas A. Edison MS	Fitchburg Fitchburg HS	Gloucester East Gloucester ES	Reading Birch Meadow ES	Wilmington Shawheen ES
Acton Douglas ES	Braintree Archie T. Morrison ES	Fitchburg Goodrich School	Gloucester Plum Cove ES	Reading J. Warren Kilam ES	Woburn Daniel L. Joyce MS
Amherst-Pelham Amherst Regional MS	Braintree Braintree High School	Fitchburg Memorial Intermediate	Gloucester Ralph B. O'Malley MS	South Shore Reg Voc Tech HS	Woburn John F. Kennedy MS
Arlington M. Norcross Stratton ES	Braintree East MS	Fitchburg Reingold ES	Gloucester Veterans Memorial School	Sudbury Peter Noyes ES	Holyoke (WL) Holyoke High School
Bellingham Bellingham Memorial MS	Braintree Highlands ES	Fitchburg South Street ES	Grafton Grafton Memorial Sr. HS	Tantasqua Tantasqua MS	Malden (WL) Malden HS
Billerica Billerica Memorial HS	Braintree Hollis ES	Frammingham Mary E. Stapleton ES	Melrose Melrose HS	Westfield Southampton Road ES	Manchester Essex Reg Jr/Sr High School
Blackstone Valley Regional Voc Tech HS	Central Berkshire Craneville ES	Gardner Elm Street School	Narragansett Narragansett MS	Westfield Highland ES	Marshfield (R) Gov Edward Winslow ES
Boston Clarence R. Edwards MS	Dartmouth James M. Quinn ES	Gardner Gardner HS	Needham Pollard MS	Weston Weston MS	Rochester Memorial ES
Boston Joseph Lee ES	Falmouth North Falmouth ES	Gardner Waterford Primary	Northborough Robert E. Melican MS	Weymouth Abigail Adams MS	Shawheen Valley Shawheen Valley VTHS
Boston Washington Irving MS	Falmouth East Falmouth ES	Gloucester Beeman Memorial School	Quabbin Quabbin Regional High School	Whitman-Hanson John H. Duval Jr. ES	

*As of this report, 59 projects have been approved for final MSBA approved grants and thus, with the fiscal year end, will be removed from future reports.

30


25

20

15

10

5

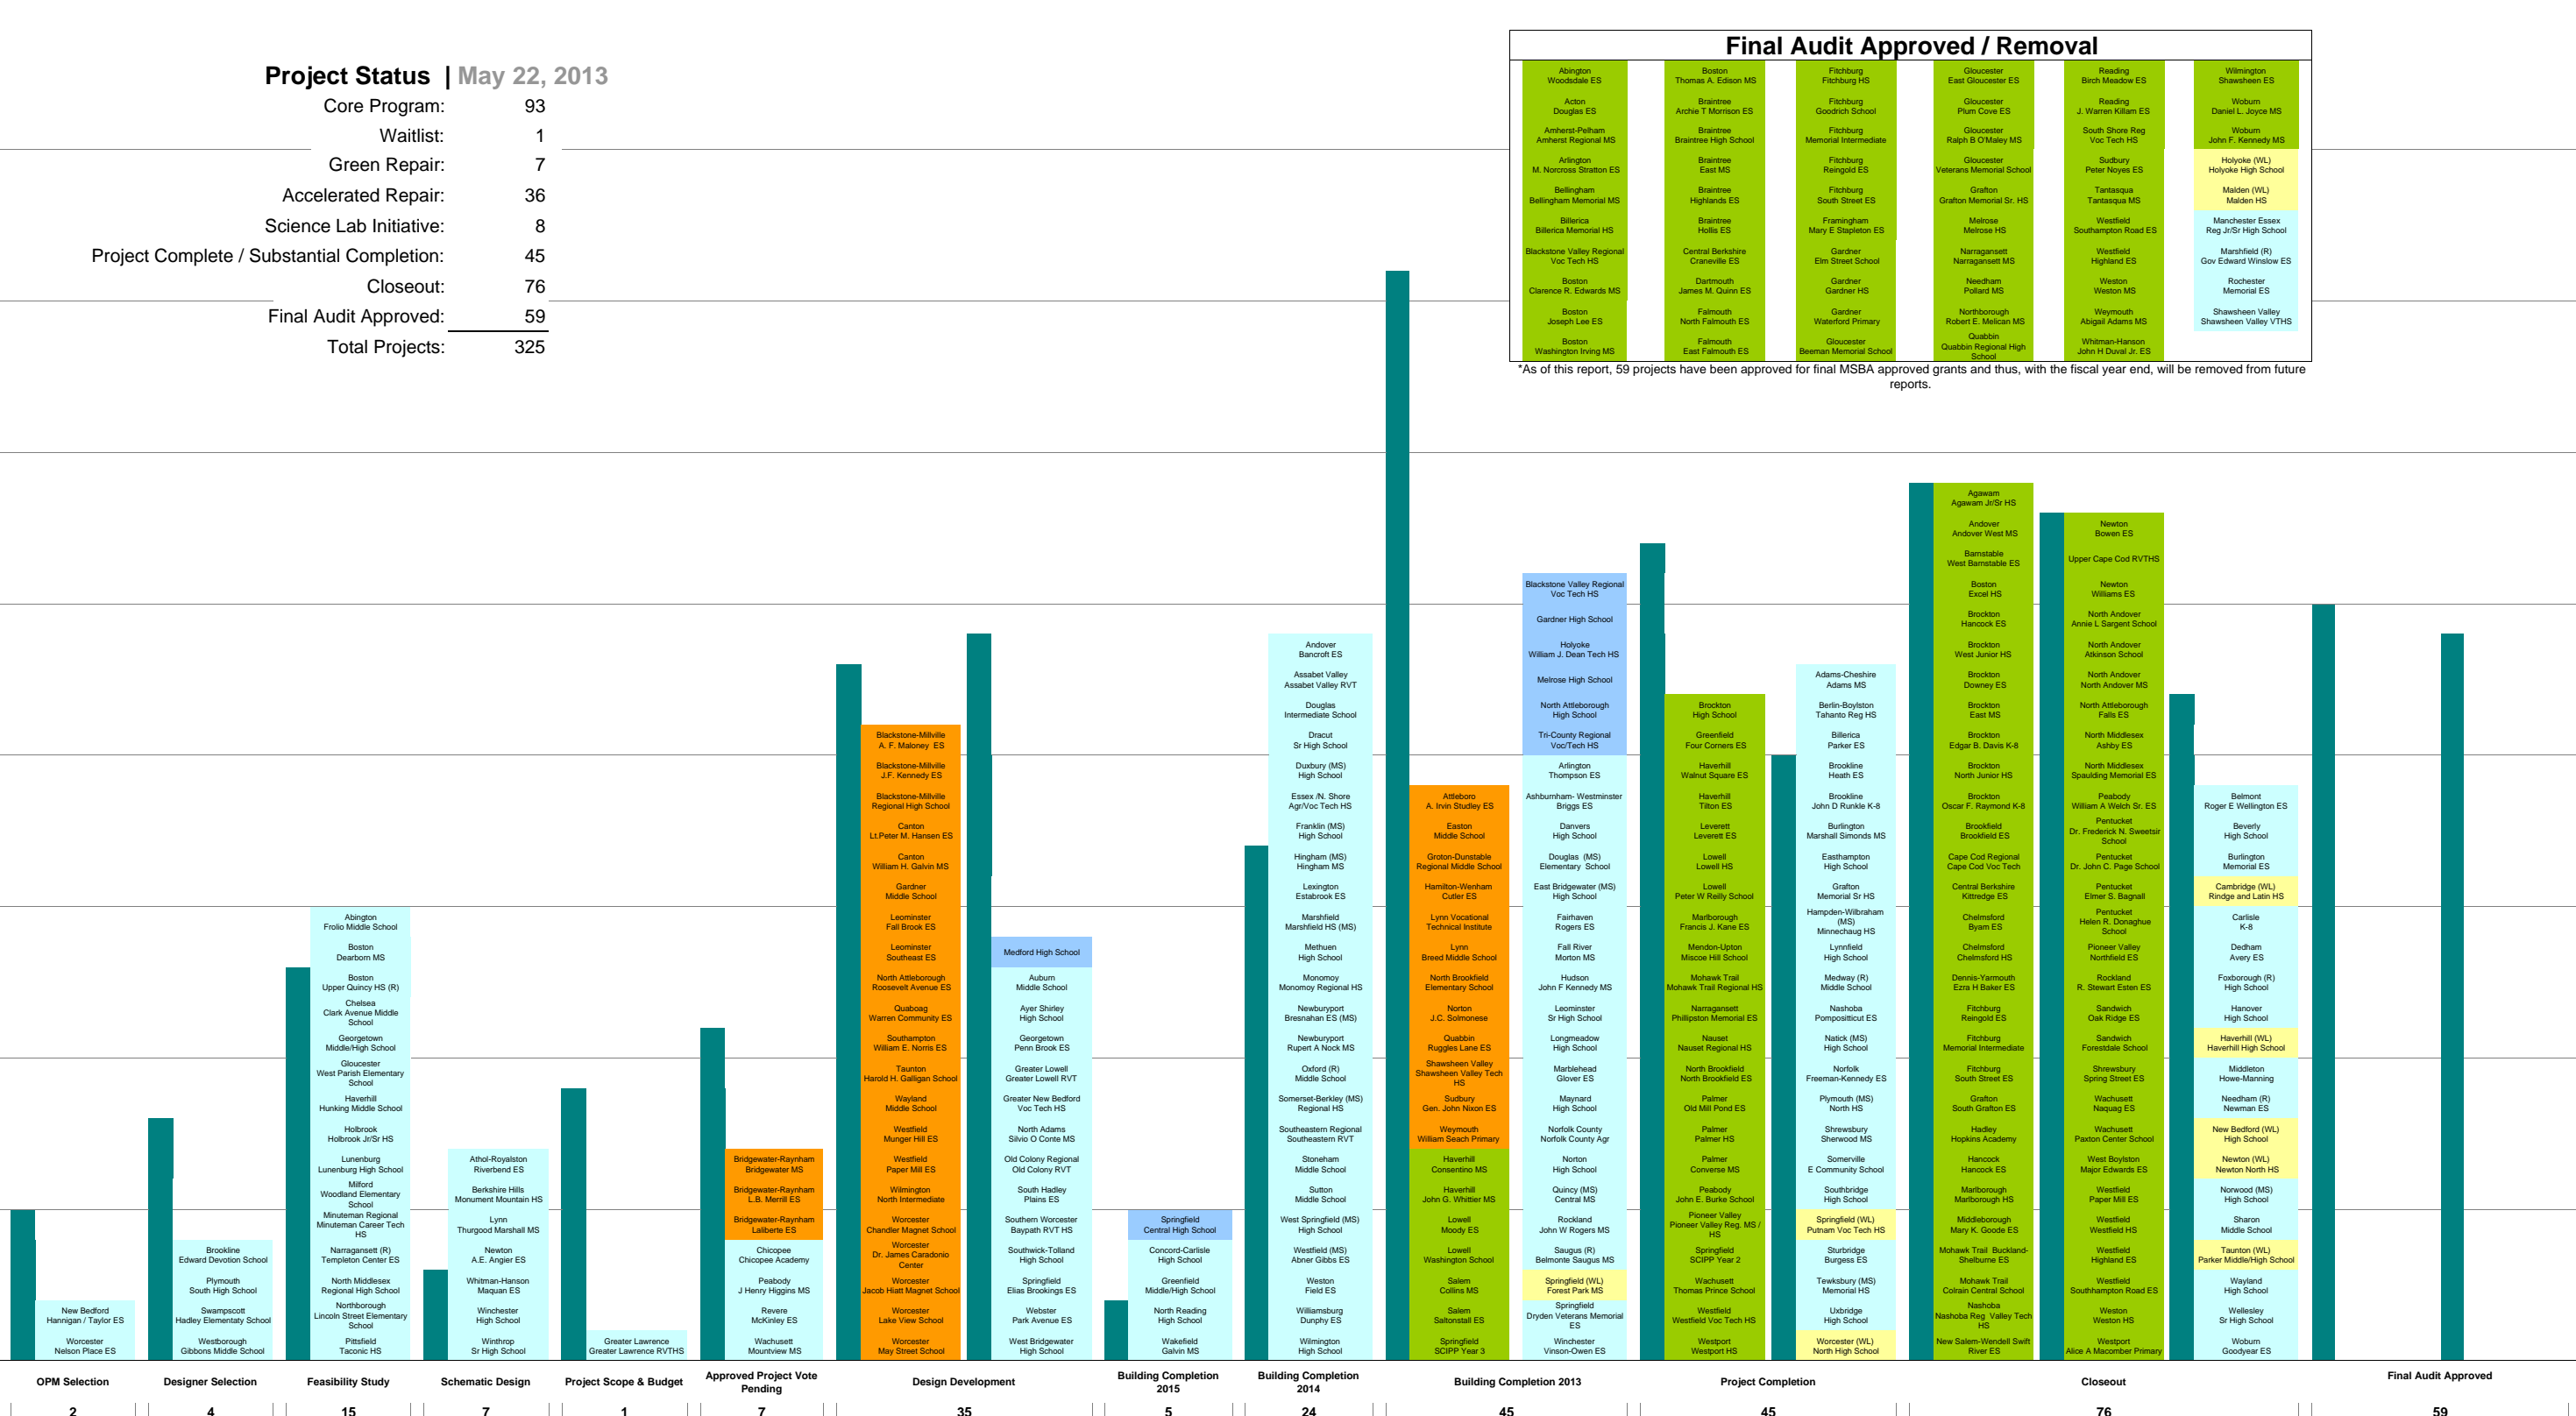

PROJECT STATUS

325 Total Active Projects

- Green Repair Program
- Accelerated Repair Program
- Science Lab Initiative Project
- Science Lab Initiative Project - To Be Removed
- Waitlist Projects
- Capital Pipeline Status Presented at January 30, 2013 Board of Directors Meeting

2013 Estimated Bid Dates

Note bid dates are **Estimates ONLY**. Please contact Districts for exact information.

Total Project Budget denotes total District costs and does not denote the basis of the MSBA Total Facilities Grant.

■ - Denotes bid phase in progress or complete
 ■ - Denotes estimated bid dates
 ■ - Denotes estimated GMP dates

DISTRICT <small>*Projects Considering the CM @ Risk Method</small>	DESIGN BASIS FOR ENROLLMENT	PROJECT BUDGET <small>Shown in Millions</small>	CONSTRUCTION BUDGET <small>Shown in Millions</small>	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC
*LEXINGTON	540	\$40.8	31.1	Lexington Estabrook ES New Construction : Filed-Sub Bids rcv'd 12/19. GMP Issued January.											
NEWBURYPORT	660	\$37.3	\$31.1	Newburyport Bresnhan ES New Construction: Filed-Sub Bids rcv'd 1/16. G.C Bids rcv'd 2/1. NTP Issued March.											
MONOMOY REGIONAL SCHOOL	700	\$64.7	\$52.9	Monomoy Regional HS New Construction: Filed-Sub Bids rcv'd 1/9. G.C Bids rcv'd 1/30. NTP Issued February.											
MELROSE	1026	\$6.5	\$4.9	Melrose HS SLI: Filed-Sub Bids rcv'd 1/23. G.C Bids rcv'd 2/6. NTP Issued February.											
*STONEHAM	775	\$38.6	\$32.0	Stoneham MS Add/Reno Construction: Filed-Sub Bids rcv'd 1/17. GMP Issued March.											
*WILMINGTON	960	\$82.7	\$64.4	Wilmington HS New Construction: Filed-Sub Bids rcv'd 1/18. GMP Targeted May.											
NORTH ATTLEBOROUGH	1209	\$6.2	\$4.7	North Attleborough HS SLI: Filed-Sub Bids rcv'd 3/29. G.C. Bids rcv'd 4/5. NTP Targeted April.											
GARDNER	636	\$3.8	\$2.9	Gardner HS SLI: Filed-Sub Bids rcv'd 2/21. G.C. Bids rcv'd 2/28. NTP Issued March.											
ASSABET VALLEY	1000	\$62.4	\$50.8	Assabet Valley Regional HS Repair: Filed-sub Bids rcv'd 3/1. G.C. Bids rcv'd 3/25. NTP Targeted April.											
BLACKSTONE VALLEY RSD	573	\$1.0	\$0.7	Blackstone Valley Regional VTHS SLI: Filed-Sub rcv'd 2/20. G.C. Bids rcv'd 3/6. NTP Issued March.											
HOLYOKE	404	\$6.9	\$5.4	Holyoke William J. Dean VTHS SLI: Filed-Sub Bids rcv'd 3/1. G.C. Bids rcv'd 3/15. NTP Issued April.											
WILLIAMSBURG	170	\$12.0	\$9.6	Williamsburg Anne T. Dunphy IS Addition/Renovation: Filed-Sub Bids rcv'd 2/12. G.C. Bids rcv'd 3/1. NTP Targeted April.											
TRI COUNTY RSD	503	\$1.8	\$1.2	Tri-County Regional VTHS SLI: Filed-Sub Bids rcv'd 3/5. G.C. Bids rcv'd 3/20. NTP Issued April.											
*NEWBURYPORT	845	\$26.9	\$21.8	Newburyport Nock ES Renovation: Filed-Sub Bids rcv'd 3/8. GMP Issued April.											
OLD COLONY	570	\$2.7	\$2.2	Old Colony RVTHS Repair/SLI: Filed-Sub Bids rcv'd 4/5. G.C. Bids rcv'd 4/12. NTP Targeted April.											
*GREENFIELD	585	\$63.4	\$52.9	Greenfield HS New Construction: Filed-Sub Bids Due 4/24. GMP Targeted June.											
*NORTH READING	1370	\$103.4	\$86.3	N.Reading HS New Construction: Filed-Sub Bids rcv'd 4/4. GMP Targeted June.											
*ANDOVER	680	\$44.7	\$34.5	Andover Bancroft ES New Construction: Filed-Sub Bids rcv'd 9/22. Non Filed-Sub Bids rcv'd 11/2. GMP Targeted June.											
MEDFORD	349	\$13.8	\$10.9	Medford HS SLI: Filed-Sub Bids Due 7/11. G.C. Bids Due 7/25. NTP Targeted August.											
*SOUTHERN WORCESTER COUNTY	1110	\$73.7	\$58.2	Bay Path VTHS Add/Reno: Filed-Sub Bids Due 5/31. GMP Targeted June.											
*WAKEFIELD	1070	\$70.1	\$59.7	Wakefield Galvin MS New Construction: Filed-Sub Bids rcv'd 5/14. GMP Targeted June.											

2013 Estimated Bid Dates

Note bid dates are **Estimates ONLY**. Please contact Districts for exact information.

Total Project Budget denotes total District costs and does not denote the basis of the MSBA Total Facilities Grant.

■ - Denotes bid phase in progress or complete
 ■ - Denotes estimated bid dates
 ■ - Denotes estimated GMP dates

DISTRICT <small>*Projects Considering the CM @ Risk Method</small>	DESIGN BASIS FOR ENROLLMENT	PROJECT BUDGET <small>Shown in Millions</small>	CONSTRUCTION BUDGET <small>Shown in Millions</small>	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC		
WEBSTER	720	\$44.9	\$35.8				■	■	Webster Park Ave ES New Construction: Filed-Sub Bids Due 5/30. G.C. Bids Due 6/13. NTP Targeted June.								
*CONCORD/CARLISLE	1225	\$92.6	\$71.4	Concord/Carlisle HS New Construction: Filed-Sub Bids Due 8/29. GMP Targeted October.			■	■	■								
SOUTHWICK-TOLLAND-GRANVILLE PowderMill IS	545	\$18.5	\$14.8				■	■	PowderMill IS Repair: Filed-Sub Bids Due 5/1. G.C. Due 5/30. NTP Targeted June.								
SOUTHWICK-TOLLAND-GRANVILLE Woodland ES	400	\$9.7	\$7.3				■	■	Woodland ES Repair: Filed-Sub Bids Due 5/1. G.C. Due 5/30. NTP Targeted June.								
SOUTHWICK-TOLLAND-GRANVILLE STG Regional HS	790	\$40.7	\$31.4						■	STG MS/HS Addition/Renovation: Filed-Sub Bids Due 7/10. G.C. Due 7/31. NTP Targeted September.							
GREATER NEW BEDFORD	2060	\$17.1	\$13.7							■	GNBRVT HS Add/Reno: Filed-Sub Bids Due 8/7. G.C. Due 8/14. NTP Targeted August.						
SPRINGFIELD	408	\$32.1	\$25.7							■	■	Springfield Central HS SLI: Filed-Sub Bids Due 8/16. GMP Targeted August.					
*SPRINGFIELD	320	\$27.9	\$22.7								■	■	Springfield Brookings ES New Construction: Filed-Sub Bids Due 8/21. GMP Targeted September.				
WEST BRIDGEWATER	625	\$63.7	\$49.7								■	West Bridgewater MS/HS New Construction: Filed-Sub Bids Due 8/30. G.C. Due 9/16. NTP Targeted September.					
GEORGETOWN	770	\$46.2	\$37.0								■	Penn Brook ES New Construction: Filed-Sub Bids Due 9/10. G.C. Due 10/4. NTP Targeted October					
*AYER-SHIRLEY	495	\$56.5	\$44.4								■	■	ASRHS Add/Reno: Filed-Sub Bids Due 9/24. GMP Targeted October				
Subtotal	24,093	\$1,213	\$972.0														
GRAND TOTAL	24,093	\$1,213	\$972.0														
Number of Construction-Related Employment Opportunities Created			4,860														

2014 Estimated Bid Dates

Note bid dates are **Estimates ONLY**. Please contact Districts for exact information.

Total Project Budget denotes total District costs and does not denote the basis of the MSBA Total Facilities Grant.

■ - Denotes bid phase in progress or complete
 ■ - Denotes estimated bid dates
 ■ - Denotes estimated GMP dates

DISTRICT <small>*Projects Considering the CM @ Risk Method</small>	DESIGN BASIS FOR ENROLLMENT	PROJECT BUDGET <small>Shown in Millions</small>	CONSTRUCTION BUDGET <small>Shown in Millions</small>	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC
SOUTH HADLEY	270	\$28.2	\$21.6	<div style="display: flex; align-items: center;"> <div style="width: 100%; height: 15px; background-color: green; margin-right: 5px;"></div> Plains ES New Construction: Filed-Sub Bids Due 2/6. G.C. Bids Due 2/27. NTP Targeted March. </div>											
*GREATER LOWELL	1990	\$65.3	\$53.2	<div style="display: flex; align-items: center;"> <div style="width: 100%; height: 15px; background-color: green; margin-right: 5px;"></div> <div style="width: 100%; height: 15px; background-color: orange; margin-right: 5px;"></div> GRTL RVTHS Repair: Filed-Sub Bids Due 2/19. GMP Targeted March. </div>											
*AUBURN	560	\$44.5	\$26.9	<div style="display: flex; align-items: center;"> <div style="width: 100%; height: 15px; background-color: green; margin-right: 5px;"></div> <div style="width: 100%; height: 15px; background-color: orange; margin-right: 5px;"></div> Auburn MS New Construction: Filed-Sub Bids Due 3/31. GMP Targeted April. </div>											
Subtotal	2,820	\$138	\$101.7												
GRAND TOTAL	2,820	\$138	\$101.7												
Number of Construction-Related Employment Opportunities Created			509												



MSBA ID	District	School	Phase	Project Scope	Procurement Type	OPM	Designer	Cx_Company	CM/GC
200800010405	Abington	Frolio Middle School	Feasibility Study			Knight, Bagge & Anderson Inc.	Ai3 Architects LLC		-
201100010015G	Abington	Woodsdale	Final Audit Approved	Repair - Accelerated	DBB	RF Walsh Collaborative Partners	Gale Associates, Inc.	Russo Barr Associates, Inc.	Lockheed Window Corporations
201000020020G	Acton	C. T. Douglas Elementary School	Final Audit Approved	Repair - Accelerated	DBB	-	CBI Consulting, Inc.		Gibson Roofs, Inc.
200806030305	Adams-Cheshire	Adams Memorial Middle School	Project Completion	Addition / Renovation	CM@R	URS Corporation	Tessier Associates, Inc.	Strategic Building Solutions, LLC	Gilbane Building Company
201100050405G	Agawam	Agawam Junior/Senior High	Closeout	Repair - Accelerated	DBB	Municipal Building Consultants, Inc.	CSS Architects Incorporated	Building Enclosure Associates	-
201106050405G	Amherst-Pelham	Amherst Regional Middle School	Final Audit Approved	Repair - Accelerated	DBB	Strategic Building Solutions, LLC	Bradley Architects, Inc.	Russo Barr Associates, Inc.	R&R Window Contractors, Inc.
201100090310G	Andover	Andover West Middle	Closeout	Repair - Accelerated	DBB	Skanska USA Building, Inc	Russo Barr Associates, Inc.	Simpson Gumpertz & Heger Inc.	Eagle Rivet Roof Services Corporation
200800090003	Andover	Bancroft Elementary School	Construction	New Construction	CM@R	Dore & Whittier Management Partners, Inc.	Symmes Maini & McKee Associates, Inc.	Sebesta Blomberg & Associates, Inc.	Skanska USA Building, Inc.
201100100055G	Arlington	M Norcross Stratton	Final Audit Approved	Repair - Accelerated	DBB	PMA Construction Services	Turowski2 Architecture, Inc.		Federal Construction Corp. Unicon Inc.
200900100050	Arlington	Thompson Elementary School	Construction	New Construction	DBB	PMA Construction Services	HMFH Architects, Inc.	Consulting Engineering Services, LLC	G & R Construction, Inc.
200806100025	Ashburnham-Westminster	John R. Briggs Elementary School	Construction	New Construction	CM@R	STV Incorporated	Lamoureux Pagano & Associates, Inc.	Foreman Building Commissioning, LP	Consigli Construction Company, Inc.
200908010605	Assabet Valley	Assabet Valley Regional Technical High School	Construction	Repair - Major	DBB	Strategic Building Solutions, LLC	Design Partnership of Cambridge, Inc.	Symmes, Maini & McKee Associates	-
200906150020	Athol-Royalston	Riverbend Elementary School	Schematic Design	Repair - Accelerated		Symmes Maini & McKee Associates, Inc.	Mount Vernon Group Architects, Inc.		-
201200160001	Attleboro	A. Irvin Studley Elementary School	Construction Approved Project Vote Pending	Repair - Accelerated		Tishman Construction Corporation of MA	Gale Associates, Inc.	CBI Consulting Inc.	
200800170305	Auburn	Auburn Middle School		New Construction		Skanska USA Building, Inc	Lamoureux Pagano & Associates, Inc.		-
9999	Ayer-Shirley	Ayer-Shirley Regional Middle/High School	Design Development	Addition / Renovation		Dore and Whittier Architects, Inc.	Symmes Maini & McKee Associates, Inc.	WSP Flack + Kurtz	-
201100200005G	Barnstable	West Barnstable Elementary School	Closeout	Repair - Accelerated	DBB	PMA Construction Services	Gale Associates, Inc.	CBI Consulting Inc.	Paul J. Rogan Co., Inc.
201100250315G	Bellingham	Bellingham Memorial Middle School	Final Audit Approved	Repair - Accelerated	DBB	Daedalus Projects Inc	Richard D. Kimball Company, Inc.	WSP Flack + Kurtz	General Air Conditioning & Heating, Inc.
200800260035	Belmont	Roger Wellington Elementary School	Closeout	New Construction	CM@R	PMA Construction Services	Jonathan Levi Architects LLC	Strategic Building Solutions, LLC	Skanska USA Building, Inc.
201006180505	Berkshire Hills	Monument Mountain Regional High School	Schematic Design			Strategic Building Solutions, LLC	Symmes Maini & McKee Associates, Inc.		-
200806200505	Berlin-Boylston	Tahanto Regional High School	Project Completion	New Construction	DBB	PMA Construction Services	HMFH Architects, Inc.	Strategic Building Solutions, LLC	CTA Construction Co., Inc.
200800300505	Beverly	Beverly HS	Closeout	Addition / Renovation		HEERY	Mount Vernon Group Architects, Inc.		CTA Construction Co., Inc.
200800310015	Billerica	Parker Elementary School	Project Completion	New Construction	DBB	Joslin, Lesser + Associates Inc.	Symmes Maini & McKee Associates, Inc.	Sebesta Blomberg & Associates, Inc.	CTA Construction Co., Inc. RS Hurford
201100310505G	Billerica	Memorial High School	Closeout	Repair - Accelerated		Municipal Building Consultants, Inc.	Knight, Bagge & Anderson, Inc.	Building Enclosure Associates	GVW, Inc.
201108050605G	Blackstone Valley Reg	Blackstone Valley Regional Voc Tech High School	Final Audit Approved	Repair - Accelerated	DBB	Strategic Building Solutions, LLC	Reinhardt Associates, Inc.	Cannon Design	Greenwood Industries, Inc.
201208050605	Blackstone Valley Reg	Blackstone Valley	Construction	Science Lab		Compass Project Management, Inc.	Flansburgh Associates, Inc.	Horizon Engineering Associates, LLP	-
201206220015	Blackstone Valley - Millville	A.F. Maloney Elementary School	Design Development	Repair - Accelerated					
201206220008	Blackstone Valley - Millville	J.F. Kennedy Elementary School	Design Development	Repair - Accelerated					
201206220505	Blackstone Valley - Millville	Regional High School	Design Development	Repair - Accelerated		Arcadis	DiMarinisi & Wolfe Architects Urban Designers	Gale Associates, Inc.	
201100350430G	Boston	Clarence R Edwards Middle School	Final Audit Approved	Repair - Accelerated	DBB	Daedalus Projects Inc	BLW Engineers, Inc.	Rist-Frost-Shumway Engineering, P.C.	-
201100350522G	Boston	Excel High School	Closeout	Repair - Accelerated	DBB	Daedalus Projects Inc	BLW Engineers, Inc.	Simpson Gumpertz & Heger Inc.	-
201000350074	Boston	Henry Dearborn Middle School	Feasibility Study			Daedalus Projects Inc	Jonathan Levi Architects LLC		-
201100350183G	Boston	Joseph Lee Elementary School	Final Audit Approved	Repair - Accelerated	DBB	Daedalus Projects Inc	BLW Engineers, Inc.	Simpson Gumpertz & Heger Inc.	Gale Associates, Inc.
201000350565	Boston	Quincy Upper School	Feasibility Study			Maureen Anderson - City Employee	HMFH Architects, Inc.		-



MSBA ID	District	School	Phase	Project Scope	Procurement Type	OPM	Designer	Cx_Company	CM/GC
201100350425G	Boston	Thomas A Edison Jr High School	Final Audit Approved	Repair - Accelerated	DBB	Daedalus Projects Inc	BLW Engineers, Inc.	Simpson Gumpertz & Heger Inc.	-
201100350445G	Boston	Washington Irving Middle School	Final Audit Approved	Repair - Accelerated	DBB	Daedalus Projects Inc	Gale Associates, Inc.	Simpson Gumpertz & Heger Inc.	-
201000400033G	Braintree	Archie T Morrison Elementary School	Final Audit Approved	Repair - Accelerated	DBB	RF Walsh Collaborative Partners	Habeeb & Associates Architects, Inc.	Cannon Design	Modern Glass & Aluminum, Inc.
201000400505G	Braintree	Braintree High School	Final Audit Approved	Repair - Accelerated	DBB	RF Walsh Collaborative Partners	Habeeb & Associates Architects, Inc.	Cannon Design	Gibson Roofs, Inc.
201000400305G	Braintree	East Middle School	Final Audit Approved	Repair - Accelerated	DBB	RF Walsh Collaborative Partners	Habeeb & Associates Architects, Inc.	Cannon Design	Modern Glass & Aluminum, Inc.
201000400015G	Braintree	Highlands Elementary School	Final Audit Approved	Repair - Accelerated	DBB	RF Walsh Collaborative Partners	Habeeb & Associates Architects, Inc.	Cannon Design	Modern Glass & Aluminum, Inc.
201000400005G	Braintree	Hollis Elementary School	Final Audit Approved	Repair - Accelerated	DBB	RF Walsh Collaborative Partners	Habeeb & Associates Architects, Inc.	Cannon Design	Modern Glass & Aluminum, Inc.
201206250320	Bridgewater-Raynham	Bridgewater Middle School	Approved Project Vote Pending	Repair - Accelerated			Pinck & Co., Inc.		
201206250020	Bridgewater-Raynham	L.B. Merrill Elementary School	Approved Project Vote Pending	Repair - Accelerated			Pinck & Co., Inc.		
201206250050	Bridgewater-Raynham	Laliberte Elementary School	Approved Project Vote Pending	Repair - Accelerated			Pinck & Co., Inc.		
201100440505G	Brockton	Brockton High School	Project Completion	Repair - Accelerated	DBB	Skanska USA Building, Inc	CSS Architects Incorporated	Simpson Gumpertz & Heger Inc.	Gibson Roofs, Inc.
201100440110G	Brockton	Downey Elementary School	Closeout	Repair - Accelerated	DBB	Skanska USA Building, Inc	CSS Architects Incorporated	Simpson Gumpertz & Heger Inc.	Built-up Roofing Systems LLC Reliable Roofing and Sheet Metal, LLC
201100440405G	Brockton	East Junior High School	Closeout	Repair - Accelerated	DBB	Skanska USA Building, Inc	CSS Architects Incorporated	Rist-Frost-Shumway Engineering, P.C.	Reliable Roofing and Sheet Metal, LLC
201100440023G	Brockton	Edgar B Davis	Closeout	Repair - Accelerated	DBB	Skanska USA Building, Inc	CSS Architects Incorporated	Simpson Gumpertz & Heger Inc.	Reliable Roofing and Sheet Metal, LLC
201100440045G	Brockton	Hancock Elementary School	Closeout	Repair - Accelerated	DBB	Skanska USA Building, Inc	CSS Architects Incorporated	Simpson Gumpertz & Heger Inc.	Arden Engineering Constructors, LLC Built-up Roofing Systems LLC
201100440410G	Brockton	North Junior High School	Closeout	Repair - Accelerated	DBB	Skanska USA Building, Inc	CSS Architects Incorporated	Rist-Frost-Shumway Engineering, P.C.	Reliable Roofing and Sheet Metal, LLC
201100440078G	Brockton	Oscar F Raymond K-8	Closeout	Repair - Accelerated	DBB	Skanska USA Building, Inc	CSS Architects Incorporated	Simpson Gumpertz & Heger Inc.	Reliable Roofing and Sheet Metal, LLC
201100440420G	Brockton	West Junior High School	Closeout	Repair - Accelerated	DBB	Skanska USA Building, Inc	CSS Architects Incorporated	Simpson Gumpertz & Heger Inc.	Reliable Roofing and Sheet Metal, LLC
201100450005G	Brookfield	Brookfield Elementary School	Closeout	Repair - Accelerated	DBB	Diversified Project Management	Habeeb & Associates Architects, Inc.	Cannon Design	Northeast Energy Control Systems
201100460015	Brookline	Edward Devotion	Designer Selection						
201000460025	Brookline	Heath Elementary School	Project Completion	Addition / Renovation	DBB	Town of Brookline Building Department	Miller Dyer Spears Inc.	Consulting Engineering Services, LLC	Nauset Construction Corporation
200800460045	Brookline	John D. Runkle School	Project Completion	Addition / Renovation	DBB	Town of Brookline Building Department	Design Partnership of Cambridge, Inc.	Consulting Engineering Services, LLC	G & R Construction, Inc.
201000480303	Burlington	Marshall Simonds Middle School	Project Completion	Addition / Renovation	DBB	Construction Monitoring Services, Inc.	Knight, Bagge & Anderson, Inc.	RDK Engineers	CTA Construction Co., Inc.
200800480015	Burlington	Memorial Elementary School	Closeout	New Construction	DBB	Construction Monitoring Services, Inc.	Knight, Bagge & Anderson, Inc.	Consulting Engineering Services, LLC	CTA Construction Co., Inc.
W20024323	Cambridge	Cambridge Rindge and Latin High School	Closeout	Addition / Renovation	DBB	-	HMFH Architects, Inc.		W. T. Rich Company Inc.
201200500012	Canton	Lt. Peter M. Hansen	Design Development	Repair - Accelerated		Vertex Construction Services	CSS Architects Incorporated		
201200500305	Canton	William H. Galvin Middle School	Design Development	Repair - Accelerated		Vertex Construction Services	CSS Architects Incorporated		
201008150605G	Cape Cod Region Voc Tech	Cape Cod Region Voc Tech	Closeout	Repair - Accelerated	DBB	URS Corporation	Garcia Galuska DeSousa Consulting Engineers Inc.	Fitzmeyer & Tocci Associates, Inc.	-
200800510025	Carlsle	Carlsle School	Closeout	Addition / Renovation	DBB	Daedalus Projects Inc	HMFH Architects, Inc.	Horizon Engineering Associates, LLP	H.V. Collins Co., Inc.
201106350025G	Central Berkshire	Craneville Elementary School	Final Audit Approved	Repair - Accelerated	DBB	Daedalus Projects Inc	Bradley Architects, Inc.	Strategic Building Solutions, LLC	Titan Roofing, Inc.
201106350035G	Central Berkshire	Kittredge Elementary School	Closeout	Repair - Accelerated	DBB	Daedalus Projects Inc	Bradley Architects, Inc.	Strategic Building Solutions, LLC	A.J. Schnopp Jr., Construction, Inc. Alpha Contracting Associates, Inc.
201100560030G	Chelmsford	Byam Elementary School	Closeout	Repair - Accelerated	DBB	Vertex Construction Services	Russo Barr Associates, Inc.	Simpson Gumpertz & Heger Inc.	S.O.M. Construction Ent., Inc.
201100560505G	Chelmsford	Chelmsford High School	Closeout	Repair - Accelerated	DBB	Vertex Construction Services	Russo Barr Associates, Inc.	Simpson Gumpertz & Heger Inc.	Lockheed Window Corporations
200800570050	Chelsea	Clark Avenue School	Feasibility Study				Pinck & Co., Inc.	HMFH Architects, Inc.	-
200900610021	Chicopee	Chicopee Academy	Approved Project Vote Pending			Arcadis	Caolo & Bieniek Associates, Inc.		-
200906400505	Concord-Carlisle	Concord-Carlisle Regional High School	Construction	New Construction	CM@R	KV Associates, Inc.	OMR Architects, Inc.	Strategic Building Solutions, LLC	Turner Construction Company



MSBA ID	District	School	Phase	Project Scope	Procurement Type	OPM	Designer	Cx_Company	CM/GC
200800710505	Danvers	Danvers High School	Construction	Addition / Renovation	DBB	Construction Monitoring Services, Inc.	DiNisco Design Partnership, Limited	Turner Facilities Management Solutions	Bacon Construction Co, Inc.
201100720040G	Dartmouth	James M. Quinn Elementary School	Final Audit Approved	Repair - Accelerated	DBB	Vertex Construction Services	Russo Barr Associates, Inc.	Gale Associates, Inc.	Capeway Roofing Systems, Inc.
200800730010	Dedham	Avery Elementary School	Closeout	New Construction	CM@R	Construction Monitoring Services, Inc.	Dore & Whittier Architects, Inc.	WSP Flack + Kurtz	Consigli Construction Company, Inc.
201200730005	Dedham	Early Childhood Education Center	Eligibility Period						
201006450005G	Dennis-Yarmouth	Ezra Baker Elementary School	Closeout	Repair - Accelerated	DBB	STV Incorporated	Knight, Bagge & Anderson, Inc.	CBI Consulting Inc.	Antonelli Construction Co., Inc.
200800770010	Douglas	Douglas Elementary School	Construction	New Construction		HEERY	DiNisco Design Partnership, Limited	Consulting Engineering Services, LLC	CTA Construction Co., Inc.
200800770100G	Douglas	Douglas Intermediate Elementary School	Construction	Repair - Accelerated	DBB	HEERY	DiNisco Design Partnership, Limited	Consulting Engineering Services, LLC	CTA Construction Co., Inc.
200800790505	Dracut	Dracut Senior High School	Construction	Addition / Renovation	DBB	RF Walsh Collaborative Partners	Mount Vernon Group Architects, Inc.	RDK Engineers	CTA Construction Co., Inc.
201000820505	Duxbury	Duxbury High School	Construction	New Construction	CM@R	KV Associates, Inc.	Mount Vernon Group Architects, Inc.	WSP Flack + Kurtz	Dimeo Construction Company
200900830505	East Bridgewater	East Bridgewater High School	Construction	New Construction	DBB	RF Walsh Collaborative Partners	Ai3 Architects LLC	Foreman Building Commissioning, LP	Fontaine Brothers, Inc.
200800860505	Easthampton	Easthampton High School	Project Completion	New Construction	DBB	Strategic Building Solutions, LLC	Caolo & Bieniek Associates, Inc.	Consulting Engineering Services, LLC	Fontaine Brothers, Inc.
201200880405	Easton	Easton Junior High School	Construction	Repair - Accelerated		PMA Construction Services	Russo Barr Associates, Inc.	Gale Associates, Inc.	-
200809130705	Essex Agr Tech	Essex Agricultural and Technical High School	Construction	New Construction	CM@R	PMA Construction Services	Design Partnership of Cambridge, Inc.	Turner Facilities Management Solutions	Gilbane Building Company
200800940020	Fairhaven	Rogers Elementary School	Construction	New Construction	DBB	Daedalus Projects Inc	HMFH Architects, Inc.	Consulting Engineering Services, LLC	CTA Construction Co., Inc.
200900950315	Fall River	James Madison Morton Middle School	Construction	New Construction	DBB	Maguire Group Inc.	Mount Vernon Group Architects, Inc.	Sebesta Blomberg & Associates, Inc.	J & J Contractors, Inc.
201100960005G	Falmouth	East Falmouth Elementary School	Final Audit Approved	Repair - Accelerated	DBB	No OPM	Keenan and Kenny Architects, Ltd.	Gale Associates, Inc.	Meadows Construction Company LLC
201100960030G	Falmouth	North Falmouth Elementary School	Final Audit Approved	Repair - Accelerated	DBB	No OPM	Keenan and Kenny Architects, Ltd.	Gale Associates, Inc.	Meadows Construction Company LLC
201100970505G	Fitchburg	Fitchburg High School	Final Audit Approved	Repair - Accelerated	DBB	Compass Project Management, Inc.	BLW Engineers, Inc.	RDK Engineers	Ostrow Electrical Co., Inc.
201000970025G	Fitchburg	Goodrich Kindergarten	Final Audit Approved	Repair - Accelerated	DBB	Compass Project Management, Inc.	BLW Engineers, Inc.	RDK Engineers	CAM HVAC & Construction, Inc.
200900970048G	Fitchburg	Memorial Intermediate	Final Audit Approved	Repair - Accelerated	DBB	Compass Project Management, Inc.	BLW Engineers, Inc.	RDK Engineers	E. Amanti & Sons, Inc.
201100970048G	Fitchburg	Memorial Intermediate	Closeout	Repair - Accelerated	DBB	Compass Project Management, Inc.	Knight, Bagge & Anderson, Inc.	Simpson Gumpertz & Heger Inc.	Lockheed Window Corporations
201100970043G	Fitchburg	Reingold Elementary School	Closeout	Repair - Accelerated	DBB	Compass Project Management, Inc.	Knight, Bagge & Anderson, Inc.	Simpson Gumpertz & Heger Inc.	Lockheed Window Corporations
200900970043G	Fitchburg	Reingold Elementary School	Final Audit Approved	Repair - Accelerated	DBB	Compass Project Management, Inc.	BLW Engineers, Inc.	RDK Engineers	E. Amanti & Sons, Inc.
200900970060G	Fitchburg	South Street Elementary	Final Audit Approved	Repair - Accelerated	DBB	Compass Project Management, Inc.	BLW Engineers, Inc.	RDK Engineers	Lockheed Window Corporations
201100970060G	Fitchburg	South Street Elementary	Closeout	Repair - Accelerated	DBB	Compass Project Management, Inc.	Knight, Bagge & Anderson, Inc.	Simpson Gumpertz & Heger Inc.	CAM HVAC & Construction, Inc.
200800990505	Foxborough	Foxborough High School	Closeout	Repair - Major	DBB	Construction Monitoring Services, Inc.	Kaestle Boos Associates, Inc.	Consulting Engineering Services, LLC	CTA Construction Co., Inc.
201101000045G	Framingham	Mary E Stapleton Elementary School	Final Audit Approved	Repair - Accelerated	DBB	Bargmann, Flendrie & Archetype, Inc.	Russo Barr Associates, Inc.	CBI Consulting Inc.	Lockheed Window Corporations
200901010505	Franklin	Franklin High School	Construction	New Construction	DBB	Daedalus Projects Inc	Ai3 Architects LLC	Consulting Engineering Services, LLC	Bacon-Agostini Construction Joint Venture
201101030001G	Gardner	Elm Street School	Final Audit Approved	Repair - Accelerated	DBB	P3 Inc.	Knight, Bagge & Anderson, Inc.	Building Enclosure Associates	Reliable Roofing and Sheet Metal, LLC
201101030050G	Gardner	Gardner High School	Final Audit Approved	Repair - Accelerated	DBB	P3 Inc.	Knight, Bagge & Anderson, Inc.	Building Enclosure Associates	Reliable Roofing and Sheet Metal, LLC
201201030505	Gardner	Gardner High School	Construction	Science Lab		Pinck & Co., Inc.	Lamoureux Pagano & Associates, Inc.	Fitzmeyer & Tocci Associates, Inc.	-
201201030405	Gardner	Gardner Middle School	Design Development	Repair - Accelerated		Leftfield, LLC	Richard D. Kimball Company, Inc.	Fitzmeyer & Tocci Associates, Inc.	-
200801030020G	Gardner	Waterford Street Primary	Final Audit Approved	Repair - Accelerated	DBB	P3 Inc.	Knight, Bagge & Anderson, Inc.	Building Enclosure Associates	Reliable Roofing and Sheet Metal, LLC
200901050010	Georgetown	Penn Brook Elementary School	Design Development	New Construction		Municipal Building Consultants, Inc.	Drumme Rosane Anderson, Inc.	Rist-Frost-Shumway Engineering, P.C.	-
200801050505	Georgetown	Georgetown Middle/High School	Feasibility Study			Municipal Building Consultants, Inc.	Drumme Rosane Anderson, Inc.		



MSBA ID	District	School	Phase	Project Scope	Procurement Type	OPM	Designer	Cx_Company	CM/GC
201101070010G	Gloucester	Beeman Memorial School	Final Audit Approved	Repair - Accelerated	DBB	Knight, Bagge & Anderson Inc.	CGKV Architects, Inc.	Russo Barr Associates, Inc.	Built-up Roofing Systems LLC
201101070020G	Gloucester	East Gloucester Elementary School	Final Audit Approved	Repair - Accelerated	DBB	Knight, Bagge & Anderson Inc.	CGKV Architects, Inc.	Russo Barr Associates, Inc.	Stanley Roofing Company, Inc.
201101070042G	Gloucester	Plum Cove Elementary School	Final Audit Approved	Repair - Accelerated	DBB	Knight, Bagge & Anderson Inc.	CGKV Architects, Inc.	Russo Barr Associates, Inc.	Built-up Roofing Systems LLC
201101070305G	Gloucester	Ralph B O'Maley Middle	Final Audit Approved	Repair - Accelerated	DBB	Knight, Bagge & Anderson Inc.	CGKV Architects, Inc.	Russo Barr Associates, Inc.	Titan Roofing, Inc.
201101070045G	Gloucester	Veterans Memorial School	Final Audit Approved	Repair - Accelerated	DBB	Knight, Bagge & Anderson Inc.	CGKV Architects, Inc.	Russo Barr Associates, Inc.	Stanley Roofing Company, Inc.
200901070050	Gloucester	West Parish Elementary School	Feasibility Study			Joslin, Lesser + Associates Inc.	Dore & Whittier Architects, Inc.		-
200801100505	Grafton	Grafton Memorial Senior	Project Completion	New Construction	CM@R	Symmes Maini & McKee Associates, Inc.		Horizon Engineering Associates, LLP	Dimeo Construction Company
201101100505G	Grafton	Grafton Memorial Senior	Final Audit Approved	Repair - Accelerated	DBB	URS Corporation	CGKV Architects, Inc.	Horizon Engineering Associates, LLP	S.O.M. Construction Ent., Inc.
201101100005G	Grafton	South Grafton Elementary	Closeout	Repair - Accelerated	DBB	URS Corporation	CGKV Architects, Inc.	Horizon Engineering Associates, LLP	AAanco Service Corporation
201201110010	Granby	West Street School	Eligibility Period						
201108230605	Greater Lawrence RVT	Greater Lawrence Reg Voc Tech	Project Scope & Budget	Repair - Major		Vertex Construction Services	Richard D. Kimball Company, Inc.		-
200908280605	Greater Lowell Voc Tec	Greater Lowell Regional Technical High School	Design Development	Repair - Major		Joslin, Lesser + Associates Inc.	Knight, Bagge & Anderson, Inc.	Horizon Engineering Associates, LLP	-
201008250605	Greater New Bedford	Greater New Bedford Vocational Technical High School	Design Development	Addition / Renovation		Construction Monitoring Services, Inc.	Drummeay Rosane Anderson, Inc.	Symmes, Maini & McKee Associates	-
201101140025G	Greenfield	Four Corners	Project Completion	Repair - Accelerated	DBB	P3 Project Planning	Tighe & Bond, Inc.	Strategic Building Solutions, LLC	Five Star Building Corp.
200901140505	Greenfield	Greenfield High School	Construction	New Construction	DBB	Construction Monitoring Services, Inc.	Dore & Whittier Architects, Inc.	BVH Integrated Services, Inc.	Shawmut Design and Construction
201206730305	Groton-Dunstable	Groton Dunstable Regional Middle School	Construction	Repair - Accelerated		Collaborative Partners	ICON architecture, inc.	Russo Barr Associates, Inc.	-
201101170505G	Hadley	Hopkins Academy	Closeout	Repair - Accelerated	DBB	Strategic Building Solutions, LLC	CCS Presentation Systems	Russo Barr Associates, Inc.	MDM Engineering
201206750010	Hamilton-Wenham	Cutler School	Construction	Repair - Accelerated		Coast & Harbor Associates, Inc.	CBI Consulting, Inc.	Russo Barr Associates, Inc.	
200806800505	Hampden-Wilbraham	Minnechaug Regional High School	Project Completion	New Construction	DBB	Pinnacle One, Inc.	Mount Vernon Group Architects, Inc.	Horizon Engineering Associates, LLP	Fontaine Brothers, Inc.
201001210005G	Hancock	Hancock Elementary School	Closeout	Repair - Accelerated	DBB	-	Westall Architects		Salco Construction Company, Inc.
200801220505	Hanover	Hanover High School	Closeout	New Construction	DBB	PMA Construction Services	HMFH Architects, Inc.	Horizon Engineering Associates, LLP	Callahan, Inc.
201201280035	Haverhill	Caleb Dustin Hunking Middle School	Feasibility Study			Joslin, Lesser + Associates Inc.	JCJ Architecture, PC		-
201101280100G	Haverhill	Consentino Middle School	Construction	Repair - Accelerated	DBB	Vertex Construction Services	CSS Architects Incorporated	RDK Engineers Russo Barr Associates, Inc.	New England Builders & Contractors, Inc. P.J. Dionne Company, Inc.
201101280085G	Haverhill	High School	Closeout						
201101280085G	Haverhill	John G Whittier Middle School	Construction	Repair - Accelerated	DBB	Vertex Construction Services	CSS Architects Incorporated	Russo Barr Associates, Inc.	New England Builders & Contractors, Inc.
201101280075G	Haverhill	Tilton Elementary School	Project Completion	Repair - Accelerated	DBB	Vertex Construction Services	CSS Architects Incorporated	Russo Barr Associates, Inc.	Titan Roofing, Inc.
201101280080G	Haverhill	Walnut Square Elementary School	Project Completion	Repair - Accelerated	DBB	Vertex Construction Services	CSS Architects Incorporated	RDK Engineers Russo Barr Associates, Inc.	P.J. Dionne Company, Inc. Titan Roofing, Inc.
201001310410	Hingham	Hingham Middle School	Construction	New Construction	DBB	Knight, Bagge & Anderson Inc.	Ai3 Architects LLC	Foreman Building Commissioning, LP	Brait Builders Corp.
200801330505	Holbrook	Holbrook Junior-Senior High School	Feasibility Study			Symmes Maini & McKee Associates, Inc.	Flansburgh Associates, Inc.		-
W20034396	Holyoke	Holyoke High School	Final Audit Approved	Repair - Major	DBB	-	Design Partnership of Cambridge, Inc.		-
201201370605	Holyoke	Wm J Dean Voc Tech High	Construction	Science Lab		Skanska USA Building, Inc	Kaestle Boos Associates, Inc.	BVH Integrated Services, Inc.	-
201201370015	Holyoke	Lt. McMahon Elementary School	Eligibility Period						
200801410410	Hudson	John F. Kennedy Middle School	Construction	New Construction	DBB	PMA Construction Services	OMR Architects, Inc.	WSP Flack + Kurtz	Bacon-Agostini Construction Joint Venture
200801530505	Leominster	Leominster High School	Construction	Addition / Renovation	CM@R	Lamoureux Pagano & Associates, Inc.		Horizon Engineering Associates, LLP	S.O.M. Construction Ent., Inc.
201201530007	Leominster	Fall Brook	Design Development	Repair - Accelerated		Daedalus Projects Inc	Reinhardt Associates, Inc.	Horizon Engineering Associates, LLP	
201201530010	Leominster	Southeast School	Design Development	Repair - Accelerated		Compass Project Management, Inc.	Reinhardt Associates, Inc.	Horizon Engineering Associates, LLP Russo Barr Associates, Inc.	



MSBA ID	District	School	Phase	Project Scope	Procurement Type	OPM	Designer	Cx_Company	CM/GC
201101540005G	Leverett	Leverett Elementary School	Project Completion	Repair - Accelerated	DBB	Potomac Capital Advisors	DiMarinisi & Wolfe Architects Urban Designers	Russo Barr Associates, Inc.	-
201101550010E	Lexington	Joseph Estabrook Elementary School	Construction	New Construction		RF Walsh Collaborative Partners	DiNisco Design Partnership, Limited	BVH Integrated Services, Inc.	Shawmut Design and Construction
200801590505	Longmeadow	Longmeadow High School	Construction	New Construction	CM@R	Joslin, Lesser + Associates Inc.	OMR Architects, Inc.	Foreman Building Commissioning, LP	Gilbane Building Company
201101600505G	Lowell	Lowell High School	Project Completion	Repair - Accelerated	DBB	NETCO Construction Project Managers, Inc.	ICON architecture, inc.	Building Enclosure Associates	-
201101600027G	Lowell	Moody Elementary School	Construction	Repair - Accelerated	DBB	NETCO Construction Project Managers, Inc.	ICON architecture, inc.	Building Enclosure Associates	Paul J. Rogan Co., Inc.
201101600040G	Lowell	Peter W Reilly School	Project Completion	Repair - Accelerated	DBB	NETCO Construction Project Managers, Inc.	ICON architecture, inc.	Building Enclosure Associates	-
201101600055G	Lowell	Washington School	Construction	Repair - Accelerated	DBB	NETCO Construction Project Managers, Inc.	ICON architecture, inc.	Building Enclosure Associates RDK Engineers	Alpha Contracting Associates, Inc.
200801620505	Lunenburg	Lunenburg High School	Feasibility Study			Joslin, Lesser + Associates Inc.	Tappe Associates, Inc.		-
201201630405	Lynn	Breed Middle School	Construction	Repair - Accelerated		Diversified Project Management	Kaestle Boos Associates, Inc.	CBI Consulting Inc.	
200901630305	Lynn	Thurgood Marshall Middle School	Schematic Design			Joslin, Lesser + Associates Inc.	Raymond Design Associates, Inc.		-
201201630605	Lynn	Lynn Vocational Tech Institute	Construction	Repair - Accelerated		Diversified Project Management	Kaestle Boos Associates, Inc.	CBI Consulting Inc.	
200901640505	Lynnfield	Lynnfield High School	Project Completion	Addition / Renovation	DBB	HEERY	Edward Rowse Architects, Inc.	Fitzmeyer & Tocci Associates, Inc.	E.A. Collangeli Construction Co., Inc.
W20024319	Malden	Malden High School	Closeout	Addition / Renovation	CM@R	URS Corporation	Flansburgh Associates, Inc.		Gilbane Building Company
200806980610	Manchester Essex Regional	Manchester Essex Regional High School	Final Audit Approved	New Construction	DBB	Design Technique Inc.	Mount Vernon Group Architects, Inc.		TLT Construction Corporation
200801680020	Marblehead	Glover Elementary School	Construction	New Construction	DBB	Municipal Building Consultants, Inc.	JCJ Architecture, PC	RDK Engineers	G & R Construction, Inc.
201101700008G	Marlborough	Francis J Kane Elementary School	Project Completion	Repair - Accelerated	DBB	RF Walsh Collaborative Partners	Baker/Wohl Architects, Inc.	Building Enclosure Associates	A&A Window Products, Inc.
201101700505G	Marlborough	Marlborough High School	Closeout	Repair - Accelerated	DBB	RF Walsh Collaborative Partners	Baker/Wohl Architects, Inc.	RDK Engineers Building Enclosure Associates	A&A Window Products, Inc. Feeley, McAnespie, Inc. Veterans Development Corporation, Inc.
200801710020	Marshfield	Governor Edward Winslow Elementary School	Final Audit Approved	Repair - Major	DBB	Vertex Construction Services	Knight, Bagge & Anderson, Inc.	RDK Engineers	Enterprise Equipment Co., Inc.
201101710505	Marshfield	Marshfield High School	Construction	New Construction	DBB	Compass Project Management, Inc.	Ai3 Architects LLC	Sebesta Blomberg & Associates, Inc.	Brait Builders Corp.
200801740505	Maynard	Maynard High School	Construction	New Construction	DBB	Municipal Building Consultants, Inc.	Tappe Associates, Inc.	WSP Flack + Kurtz	CTA Construction Co., Inc.
201201760505	Medford	Medford High School	Design Development	Science Lab		Leftfield, LLC	DiNisco Design Partnership, Limited	Cannon Design	-
200801770305	Medway	Medway Middle School	Project Completion	Repair - Major	CM@R	Compass Project Management, Inc.	Knight, Bagge & Anderson, Inc.	Sebesta Blomberg & Associates, Inc.	Consigli Construction Company, Inc.
201201780505	Melrose	Melrose High School	Construction	Science Lab		CPI/Collaborative Partners	Ai3 Architects LLC	WSP Flack + Kurtz	-
201101780505G	Melrose	Melrose High School	Final Audit Approved	Repair - Accelerated	DBB	Municipal Building Consultants, Inc.	Gale Associates, Inc.	Russo Barr Associates, Inc.	Commercial Roofing and Contracting, Inc.
201107100015G	Mendon-Upton	Miscoe Hill School	Project Completion	Repair - Accelerated	DBB	Maguire Group Inc.	Habeeb & Associates Architects, Inc.	Sebesta Blomberg & Associates, Inc.	Greenwood Industries, Inc.
200801810505	Methuen	Methuen High School	Construction	Addition / Renovation	CM@R	KBA/Trident	Finegold Alexander and Associates Inc.	Environmental Health and Engineering	Dimeo Construction Company
201101820025G	Middleborough	Mary K. Goode Elementary School	Closeout	Repair - Accelerated	DBB	Maguire Group Inc.	Habeeb & Associates Architects, Inc.	Russo Barr Associates, Inc.	J.J. Cardosi, Inc.
200801840005	Middleton	Howe-Manning School	Closeout	New Construction	DBB	RF Walsh Collaborative Partners	DiNisco Design Partnership, Limited	Foreman Building Commissioning, LP	CTA Construction Co., Inc.
201101850090	Milford	Woodland Elementary School	Feasibility Study			Joslin, Lesser + Associates Inc.	HMFH Architects, Inc.		-
200908300605	Minuteman Voc Tech	Minuteman Regional High School (Career Tech)	Feasibility Study			Skanska USA Building, Inc	Kaestle Boos Associates, Inc.		-
201107170005G	Mohawk Trail	Buckland-Shelburne Reg	Closeout	Repair - Accelerated	DBB	Potomac Capital Advisors	Bradley Architects, Inc.	Strategic Building Solutions, LLC	-
201107170010G	Mohawk Trail	Colrain Central School	Closeout	Repair - Accelerated	DBB	Potomac Capital Advisors	Bradley Architects, Inc.	Strategic Building Solutions, LLC	-
201107170505G	Mohawk Trail	Mohawk Trail Reg High School	Project Completion	Repair - Accelerated	DBB	Potomac Capital Advisors	Bradley Architects, Inc.	Strategic Building Solutions, LLC	-
201122229999	Monomoy	Monomoy Regional High School	Construction	New Construction		Skanska USA Building, Inc	Mount Vernon Group Architects, Inc.	Sebesta Blomberg & Associates, Inc.	Fontaine Brothers, Inc.
201107200305G	Narragansett	Narragansett Middle School	Final Audit Approved	Repair - Accelerated	DBB	Potomac Capital Advisors	DiMarinisi & Wolfe Architects Urban Designers	Rist-Frost-Shumway Engineering, P.C.	-
201107200003G	Narragansett	Phillipston Memorial Elementary School	Project Completion	Repair - Accelerated	DBB	Potomac Capital Advisors	DiMarinisi & Wolfe Architects Urban Designers	Rist-Frost-Shumway Engineering, P.C.	-



MSBA ID	District	School	Phase	Project Scope	Procurement Type	OPM	Designer	Cx_Company	CM/GC
200807200020	Narragansett	Templeton Center School	Feasibility Study	Repair - Major		Strategic Building Solutions, LLC	Symmes Maini & McKee Associates, Inc.		-
200807250015	Nashoba	Pompositticut Elementary School	Project Completion	Addition / Renovation	DBB	Construction Monitoring Services, Inc.	Symmes Maini & McKee Associates, Inc.	Strategic Building Solutions, LLC	P.J. Stella Construction Corp.
200908520605G	Nashoba Valley Tech	Nashoba Valley Technical High School	Closeout	Repair - Accelerated	DBB	-	-		-
200801980505	Natick	Natick High School	Project Completion	New Construction	DBB	RF Walsh Collaborative Partners	Ai3 Architects LLC	Rist-Frost-Shumway Engineering, P.C.	-
201106600505G	Nauset	Nauset Regional High School	Project Completion	Repair - Accelerated	DBB	NETCO Construction Project Managers, Inc.	Habeeb & Associates Architects, Inc.	CBI Consulting Inc.	Capeway Roofing Systems, Inc. Modern Glass & Aluminum, Inc.
200901990050	Needham	Newman Elementary School	Closeout	Repair - Major	CM@R	Steven H. Popper - Town Employee	Drummeey Rosane Anderson, Inc.	Rist-Frost-Shumway Engineering, P.C.	Consigli Construction Company, Inc. Triumph Leasing Corporation
201101990405G	Needham	Pollard Middle	Final Audit Approved	Repair - Accelerated	DBB	STV Incorporated	Gale Associates, Inc.	CBI Consulting Inc.	Wayne Roofing Systems, LLC
200902010070	New Bedford	John Hannigan	OPM Selection			-	-		-
201002010505	New Bedford	New Bedford High School	Closeout		DBB	-	-		-
201107280015G	New Salem-Wendell	Swift River Elementary School	Closeout	Repair - Accelerated	DBB	Maguire Group Inc.	Bradley Architects, Inc.	Strategic Building Solutions, LLC	RAC Builders, Inc.
201102040005	Newburyport	Francis T Bresnahan Elementary School	Construction	New Construction		HEERY	HMFH Architects, Inc.	Fitzmeyer & Tocci Associates, Inc.	-
201002040305	Newburyport	Rupert A. Nock Middle School	Construction	Addition / Renovation		HEERY	Miller Dyer Spears Inc.	Fitzmeyer & Tocci Associates, Inc.	-
201102070005	Newton	A E Angier Elementary School	Schematic Design			Joslin, Lesser + Associates Inc.	DiNisco Design Partnership, Limited		-
201102070015G	Newton	Bowen	Closeout	Repair - Accelerated	DBB	STV Incorporated	Habeeb & Associates Architects, Inc.		-
W20014216	Newton	Newton North High School	Closeout	New Construction	CM@R	Turner Construction Co.	Dore & Whittier Architects, Inc.	Dimeo Construction Company	-
201102070125G	Newton	Williams Elementary School	Closeout	Repair - Accelerated	DBB	STV Incorporated	Habeeb & Associates Architects, Inc.		-
200802080005	Norfolk	Freeman-Kennedy Elementary School	Project Completion	New Construction	DBB	Joslin, Lesser + Associates Inc.	Flansburgh Associates, Inc.	WSP Flack + Kurtz	Fontaine Brothers, Inc.
200909150705	Norfolk County Agriculture	Norfolk County Agricultural High School	Construction	Addition / Renovation	DBB	Compass Project Management, Inc.	Turowski2 Architecture, Inc.	Rist-Frost-Shumway Engineering, P.C.	TLT Construction Corporation
200802090305	North Adams	Silvio O Conte Middle School	Design Development	Addition / Renovation		Strategic Building Solutions, LLC	Margo Jones Architects, Inc.		-
201102110018G	North Andover	Annie L Sargent School	Closeout	Repair - Accelerated	DBB	Municipal Building Consultants, Inc.	ICON architecture, inc.	Cannon Design	Varioka Construction, Inc.
201102110001G	North Andover	Atkinson School	Closeout	Repair - Accelerated	DBB	Municipal Building Consultants, Inc.	ICON architecture, inc.	Cannon Design	Paul J. Rogan Co., Inc.
201102110305G	North Andover	North Andover Middle School	Closeout	Repair - Accelerated	DBB	Municipal Building Consultants, Inc.	ICON architecture, inc.	Cannon Design	Stanley Roofing Company, Inc.
201102120010G	North Attleborough	Falls Elementary School	Closeout	Repair - Accelerated	DBB	Atlantic Construction and Management, Inc.	CSS Architects Incorporated	Gale Associates, Inc.	Northeast Energy Control Systems
201202120505	North Attleborough	North Attleboro High	Construction	Science Lab		Skanska USA Building, Inc	Kaestle Boos Associates, Inc.	Consulting Engineering Services, LLC	-
201202120015	North Attleborough	Rossvelt Avenue Elementary School	Design Development	Repair- Accelerated		Skanska USA Building, Inc	Russo Barr Associates, Inc.	Gale Associates, Inc.	
201202150015	North Brookfield	North Brookfield Elementary School	Construction	Repair- Accelerated		Strategic Building Solutions, LLC	CBI Consulting, Inc.	Simpson Gumpertz & Heger Inc.	
201102150015G	North Brookfield	North Brookfield Elementary School	Project Completion	Repair - Accelerated	DBB	Vertex Construction Services	LPBA/ Architects, Inc.	Simpson Gumpertz & Heger Inc.	Lockheed Window Corporations
201107350010G	North Middlesex	Ashby Elementary	Closeout	Repair - Accelerated	DBB	Compass Project Management, Inc.	Russo Barr Associates, Inc.	Building Enclosure Associates	Greenwood Industries, Inc. GVV, Inc.
201107350505	North Middlesex	North Middlesex Regional High School	Feasibility Study			HEERY	Symmes Maini & McKee Associates, Inc.		-
201107350005G	North Middlesex	Spaulding Memorial	Closeout	Repair - Accelerated	DBB	Compass Project Management, Inc.	Russo Barr Associates, Inc.	Building Enclosure Associates	MDM Engineering
201002170505	North Reading	North Reading High School	Construction	Addition / Renovation	CM@R	PMA Construction Services	Dore & Whittier Architects, Inc.	Cannon Design	-
201102130003	Northborough	Lincoln Street Elementary School	Feasibility Study			Strategic Building Solutions, LLC	Lamoureux Pagano & Associates, Inc.		-
201102130305G	Northborough	Robert E. Melican Middle School	Final Audit Approved	Repair - Accelerated	DBB	Pinck & Co., Inc.	ICON architecture, inc.	Strategic Building Solutions, LLC	AAlanco Service Corporation
201202180015	Norton	J C Solmonese	Construction	Repair - Accelerated		Joslin, Lesser + Associates Inc.	Habeeb & Associates Architects, Inc.	Simpson Gumpertz & Heger Inc.	
200902180505	Norton	Norton High School	Construction	Addition / Renovation	CM@R	Pinck & Co., Inc.	JCJ Architecture, PC	Rist-Frost-Shumway Engineering, P.C.	W. T. Rich Company Inc.
200802200505	Norwood	Norwood High School	Closeout	New Construction	DBB	Compass Project Management, Inc.	Ai3 Architects LLC		Agostini Construction Co., Inc.
200908550605	Page Old Colony Reg Voc Tech	Old Colony Regional Vocational Technical High School	Design Development	Repair - Major		Vertex Construction Services	-	Consulting Engineering Services, LLC	-



MSBA ID	District	School	Phase	Project Scope	Procurement Type	OPM	Designer	Cx_Company	CM/GC
200802260405	Oxford	Oxford Middle School	Construction	Repair - Major		Diversified Project Management	CGKV Architects, Inc.	Cannon Design	S.O.M. Construction Ent., Inc.
201102270305G	Palmer	Converse Middle School	Project Completion	Repair - Accelerated	DBB	Diversified Project Management	Tighe & Bond, Inc.	Strategic Building Solutions, LLC	Royal Steam Heater Co. Titan Roofing, Inc.
201102270008G	Palmer	Old Mill Pond Elementary School	Project Completion	Repair - Accelerated	DBB	Diversified Project Management	Tighe & Bond, Inc.	Strategic Building Solutions, LLC	Royal Steam Heater Co.
201102270505G	Palmer	Palmer High School	Project Completion	Repair - Accelerated	DBB	Diversified Project Management	Tighe & Bond, Inc.	Strategic Building Solutions, LLC	Royal Steam Heater Co. Titan Roofing, Inc.
200802290305	Peabody	J Henry Higgins Middle School	Approved Project Vote Pending	New Construction		Daedalus Projects Inc	DiNisco Design Partnership, Limited		-
201102290007G	Peabody	John E Burke School	Project Completion	Repair - Accelerated	DBB	Daedalus Projects Inc	LPBA/ Architects, Inc.	Sebesta Blomberg & Associates, Inc.	-
201102290027G	Peabody	William A Welch Sr	Closeout	Repair - Accelerated	DBB	Daedalus Projects Inc	LPBA/ Architects, Inc.	Sebesta Blomberg & Associates, Inc.	-
201107450020G	Pentucket	Dr Frederick N Sweetsir	Closeout	Repair - Accelerated	DBB	PMA Construction Services	Knight, Bagge & Anderson, Inc.	CBI Consulting Inc./RDK Engineers	E. Amanti & Sons, Inc.
201107450015G	Pentucket	Dr John C Page School	Closeout	Repair - Accelerated	DBB	PMA Construction Services	Knight, Bagge & Anderson, Inc.	CBI Consulting Inc./RDK Engineers	Capeway Roofing Systems, Inc.
201107450005G	Pentucket	Elmer S Bagnall	Closeout	Repair - Accelerated	DBB	PMA Construction Services	Knight, Bagge & Anderson, Inc.	CBI Consulting Inc./RDK Engineers	Gibson Roofs, Inc.
201107450010G	Pentucket	Helen R Donaghue School	Closeout	Repair - Accelerated	DBB	PMA Construction Services	Knight, Bagge & Anderson, Inc.	CBI Consulting Inc.	Gibson Roofs, Inc.
201107500008G	Pioneer Valley	Northfield Elementary School	Closeout	Repair - Accelerated	DBB	Diversified Project Management	CGKV Architects, Inc.	Strategic Building Solutions, LLC	-
201107500505G	Pioneer Valley	Pioneer Valley Reg Middle School/High School	Project Completion	Repair - Accelerated	DBB	Diversified Project Management	CGKV Architects, Inc.	Strategic Building Solutions, LLC	-
201002360510	Pittsfield	Taconic High School	Feasibility Study			Skanska USA Building, Inc	-		-
201202390515	Plymouth	Plymouth South High School	Designer Selection				Ted Gentry Associates, Inc		
200802390505	Plymouth	Plymouth North High School	Project Completion	New Construction	DBB	Ted Gentry Associates, Inc	Ai3 Architects LLC	Sebesta Blomberg & Associates, Inc.	J & J Contractors, Inc.
201007530505G	Quabbin	Quabbin Regional High School	Final Audit Approved	Repair - Accelerated	DBB	Vertex Construction Services	LPBA/ Architects, Inc.	Building Enclosure Associates	Kronenberger & Sons Restoration, Inc.
201207530030	Quabbin	Ruggles Lane Elementary School	Construction	Repair - Accelerated	DBB	Vertex Construction Services	Turowski2 Architecture, Inc.	Simpson Gumpertz & Heger Inc.	
201207780005	Quaboag	Warren Community Elementary School	Construction	Repair - Accelerated		Coast & Harbor Associates, Inc.	Lindgren & Sharples, Inc.	Strategic Building Solutions, LLC	
200802430315	Quincy	Central Middle School	Construction	New Construction	DBB	Tishman Construction Corporation of MA	Ai3 Architects LLC	Sebesta Blomberg & Associates, Inc.	H.V. Collins Co., Inc.
201102460005G	Reading	Birch Meadow Elementary School	Final Audit Approved	Repair - Accelerated	DBB	KBA Architects	LPBA/ Architects, Inc.	Russo Barr Associates, Inc.	Paul J. Rogan Co., Inc.
201102460017G	Reading	J Warren Killam Elementary School	Final Audit Approved	Repair - Accelerated	DBB	KBA Architects	LPBA/ Architects, Inc.	Russo Barr Associates, Inc.	Capeway Roofing Systems, Inc.
201002480035	Revere	William McKinley Elementary School	Approved Project Vote Pending	New Construction		RF Walsh Collaborative Partners	Drumme Rosane Anderson, Inc.		-
200802500005	Rochester	Rochester Memorial School	Final Audit Approved	Addition / Renovation	CM@R	PMA Construction Services	Flansburgh Associates, Inc.	Horizon Engineering Associates, LLP	Gilbane Building Company
200802510305	Rockland	John W. Rogers Middle School	Construction	New Construction	CM@R	Daedalus Projects Inc	Dore & Whittier Architects, Inc.	Consulting Engineering Services, LLC	Agostini Construction Co., Inc.
201102510025G	Rockland	R Stewart Esten	Closeout	Repair - Accelerated	DBB	Daedalus Projects Inc	Habeeb & Associates Architects, Inc.	Russo Barr Associates, Inc.	Northeast Energy Control Systems
200902580305G	Salem	Collins Middle School	Construction	Repair - Accelerated	CM@R	KV Associates, Inc.	Reinhardt Associates, Inc.	Rist-Frost-Shumway Engineering, P.C.	Gilbane Building Company
201002580050G	Salem	Salt Stall School	Construction	Repair - Accelerated	CM@R	KV Associates, Inc.	Reinhardt Associates, Inc.	Rist-Frost-Shumway Engineering, P.C.	Gilbane Building Company
201102610010G	Sandwich	Forestdale School	Closeout	Repair - Accelerated	DBB	NETCO Construction Project Managers, Inc.	Habeeb & Associates Architects, Inc.	Gale Associates, Inc.	Varietka Construction, Inc.
200902610025G	Sandwich	Oak Ridge School	Closeout	Repair - Accelerated	DBB	NETCO Construction Project Managers, Inc.	Habeeb & Associates Architects, Inc.	Gale Associates, Inc.	J.J. Cardosi, Inc.
201002620305	Saugus	Belmonte Middle School	Construction	Repair - Major	CM@R	Skanska USA Building, Inc	Fletcher Thompson Architecture Engineering, LLC	Consulting Engineering Services, LLC	Consigli Construction Company, Inc.
201202640305	Scituate	Gates Intermediate School	Eligibility Period						
200802660305	Sharon	Sharon Middle School	Closeout	Addition / Renovation	CM@R	Daedalus Projects Inc	Kaestle Boos Associates, Inc.	Horizon Engineering Associates, LLP	Consigli Construction Company, Inc.
201008710605	Shawsheen Valley Voc Tech	Shawsheen Valley Voc Tech High School	Final Audit Approved	Addition / Renovation	DBB	Construction Monitoring Services, Inc.	Knight, Bagge & Anderson, Inc.		Colantonio, Inc.
201208710605	Shawsheen Valley Voc Tech	Shawsheen Valley Voc Tech High School	Construction	Repair - Accelerated		Diversified Project Management	Shekar & Associates, Inc.	Fitzmeyer & Tocci Associates, Inc.	
200802710305	Shrewsbury	Sherwood Middle School	Project Completion	New Construction	CM@R	PMA Construction Services	Lamoureux Pagano & Associates, Inc.	RDK Engineers	Gilbane Building Company
201102710035G	Shrewsbury	Spring Street Elementary School	Closeout	Repair - Accelerated	DBB	PMA Construction Services	Habeeb & Associates Architects, Inc.	Cannon Design	Lambrian Construction Corp.



MSBA ID	District	School	Phase	Project Scope	Procurement Type	OPM	Designer	Cx_Company	CM/GC
20081119999	Somerset-Berkley	Somerset-Berkley High School	Construction	New Construction		Skanska USA Building, Inc	Ai3 Architects LLC	Horizon Engineering Associates, LLP	Bacon-Agostini Construction Joint Venture
200902740111E	Somerville	East Somerville Community School at Cummings	Project Completion	Addition / Renovation	CM@R	PMA Construction Services	Maguire Group, Inc.	Foreman Building Commissioning, LP	Gilbane Building Company
200902780015	South Hadley	Plains School	Design Development	New Construction		Arcadis	Margo Jones Architects, Inc.		-
200808730605G	South Shore Reg Voc Tech	South Shore Vocational Technical High School	Final Audit Approved	Repair - Accelerated	DBB	Vertex Construction Services	Gale Associates, Inc.	Building Enclosure Associates	-
200802770505	Southbridge	Southbridge High School	Project Completion	New Construction	CM@R	Joslin, Lesser + Associates Inc.	Tappe Associates, Inc.	Environmental Health and Engineering	Consigli Construction Company, Inc.
201202750005	Southampton	William E. Norris Elementary School	Deisgn Development	Repair - Accelerated		Tishman Construction Corporation of MA	Reinhardt Associates, Inc.	Building Enclosure Associates	
200908720605	Southeastern Reg Voc Tech	Southeastern Regional Vocational Technical School	Construction	Addition / Renovation	CM@R	RF Walsh Collaborative Partners	Drummeey Rosane Anderson, Inc.	RDK Engineers	W. T. Rich Company Inc.
200908760605	Southern Worcester Cty VT	Bay Path Regional Vocational Technical High School	Design Development	Addition / Renovation	DBB	HEERY	Kaestle Boos Associates, Inc.	RDK Engineers	Consigli Construction Company, Inc.
201107660505	Southwick-Tolland	Regional High School	Design Development	Addition / Renovation		Strategic Building Solutions, LLC	JCJ Architecture, PC		BVH Integrated Services, Inc.
200807670505	Spencer-E Brookfield	David Prouty High School	Eligibility Period	Addition / Renovation		Dore and Whittier Architects, Inc.	Design Partnership of Cambridge, Inc.		-
	Springfield	SCIPP Year 2	Project Completion						
	Springfield	SCIPP Year 3	Construction						
201102810125E	Springfield	Dryden Veterans Memorial Elementary School	Construction	Addition / Renovation	CM@R	Arcadis	Drummeey Rosane Anderson, Inc.	BVH Integrated Services, Inc.	-
201102810030E	Springfield	Elias Brookings Elementary School	Design Development	New Construction	CM@R	Arcadis	Drummeey Rosane Anderson, Inc.	BVH Integrated Services, Inc.	-
W20014137	Springfield	Forest Park Middle School	Construction	Addition / Renovation	CM@R	Arcadis	Perkins Eastman	Foreman Building Commissioning, LP	Consigli Construction Company, Inc.
W20054428	Springfield	Roger L. Putnam Vocational Technical High School	Project Completion	New Construction	CM@R	Pinnacle One, Inc.	Drummeey Rosane Anderson Inc.	Strategic Building Solutions, LLC	Consigli/Morganti
201202810500	Springfield	Central High School	Construction	Science Lab		Leftfield, LLC	DiNisco Design Partnership, Limited	Horizon Engineering Associates, LLP	
200902840405	Stoneham	Stoneham Middle School	Design Development	Addition / Renovation	CM@R	Joslin, Lesser + Associates Inc.	Tappe Associates, Inc.	RDK Engineers	Shawmut Design and Construction
200802870005	Sturbridge	Burgess Elementary School	Project Completion	Addition / Renovation	DBB	Lamoureux Pagano & Associates, Inc.	Drummeey Rosane Anderson, Inc.	Horizon Engineering Associates, LLP	Fontaine Brothers, Inc.
201102880030G	Sudbury	Peter Noyes Elementary School	Final Audit Approved	Repair - Accelerated	DBB	Compass Project Management, Inc.	Russo Barr Associates, Inc.	RDK Engineers	Gibson Roofs, Inc.
201202880025	Sudbury	General John Nixon Elementary School	Design Development	Repair - Accelerated		PMA Construction Services	ICON architecture, inc.	Gale Associates, Inc.	
200802900305	Sutton	Sutton Middle School	Construction	Addition / Renovation	DBB	Strategic Building Solutions, LLC	Flansburgh Associates, Inc.	RDK Engineers	TLT Construction Corporation
201102910010	Swampscott	Hadley Elementary School	Designer Selection			-	-		-
201107700405G	Tantasqua	Tantasqua Regional Jr High School	Final Audit Approved	Repair - Accelerated	DBB	Diversified Project Management	Habeeb & Associates Architects, Inc.		Greenwood Industries, Inc.
201202930057	Taunton	Harold H Galligan School	Design Development	Repair - Accelerated		Arcadis	Knight, Bagge & Anderson, Inc.	Gale Associates, Inc.	
W20014194	Taunton	Parker Middle/Taunton High School	Closeout	Addition / Renovation	CM@R	Gilbane Building Company	Design Partnership of Cambridge, Inc.		Bacon-Agostini Construction Joint Venture
200802950505	Tewksbury	Tewksbury Memorial High School	Project Completion	New Construction	DBB	HEERY	Symmes Maini & McKee Associates, Inc.	Sebesta Blomberg & Associates, Inc.	CTA Ventures
201208780605	Tri County	Tri County Reg Voc Tech	Construction	Science Lab		Collaborative Partners	Ai3 Architects LLC		-
201108790605G	Upper Cape Cod Voc Tech	Upper Cape Cod Voc Tech	Closeout	Repair - Accelerated	DBB	NETCO Construction Project Managers, Inc.	Knight, Bagge & Anderson, Inc.	Gale Associates, Inc.	Modern Glass & Aluminum, Inc.
200803040505	Uxbridge	Uxbridge High School	Project Completion	New Construction	CM@R	Joslin, Lesser + Associates Inc.	Raymond Design Associates, Inc.	Turner Facilities Management Solutions	Shawmut Design and Construction
200907750305	Wachusett	Mountview Middle School	Approved Project Vote Pending			Gary Kaczmarek - Town Employee	Lamoureux Pagano & Associates, Inc.		-
201107750035G	Wachusett	Naquag Elementary School	Closeout	Repair - Accelerated	DBB	Strategic Building Solutions, LLC	LPBA/ Architects, Inc.	Rist-Frost-Shumway Engineering, P.C.	MDM Engineering
201107750040G	Wachusett	Paxton Center School	Closeout	Repair - Accelerated	DBB	Strategic Building Solutions, LLC	LPBA/ Architects, Inc.	Rist-Frost-Shumway Engineering, P.C.	MDM Engineering
201107750045G	Wachusett	Thomas Prince School	Project Completion	Repair - Accelerated	DBB	Strategic Building Solutions, LLC	LPBA/ Architects, Inc.	Rist-Frost-Shumway Engineering, P.C.	MDM Engineering
201003050310	Wakefield	Galvin Middle School	Construction	New Construction	CM@R	Joslin, Lesser + Associates Inc.	Tappe Associates, Inc.	B2Q Associates, Inc.	Bond Brothers, Inc.



MSBA ID	District	School	Phase	Project Scope	Procurement Type	OPM	Designer	Cx_Company	CM/GC
201203150305	Wayland	Wayland Middle School	Design Development	Repair - Accelerated		Joslin, Lesser + Associates Inc.	DiMarinisi & Wolfe Architects Urban Designers	CBI Consulting Inc.	
200803150505	Wayland	Wayland High School	Closeout	New Construction	CM@R	KV Associates, Inc.	HMFH Architects, Inc.	WSP Flack + Kurtz	Shawmut Design and Construction
200903160015	Webster	Park Avenue Elementary School	Design Development	New Construction	DBB	RF Walsh Collaborative Partners	Dore & Whittier Architects, Inc.	Cannon Design	-
200803170505	Wellesley	Wellesley Senior High School	Closeout	New Construction	CM@R	Ryegate, Inc.	Symmes Maini & McKee Associates, Inc.	Rist-Frost-Shumway Engineering, P.C.	Turner Construction Company
201103220005G	West Boylston	Major Edwards Elementary	Closeout	Repair - Accelerated	DBB	URS Corporation	Reinhardt Associates, Inc.	Cannon Design	-
201003230505	West Bridgewater	West Bridgewater Middle-Senior High School	Design Development	New Construction		Strategic Building Solutions, LLC	Flansburgh Associates, Inc.	Cannon Design	-
200903320505	West Springfield	West Springfield High School	Construction	New Construction	DBB	Strategic Building Solutions, LLC	Symmes Maini & McKee Associates, Inc.	Turner Facilities Management Solutions	Fontaine Brothers, Inc.
200903210305	Westborough	Gibbons Middle School	Designer Selection			HEERY	-		-
200903250020	Westfield	Abner Gibbs Elementary School	Construction	New Construction	DBB	Skanska USA Building, Inc	Margo Jones Architects, Inc.	Horizon Engineering Associates, LLP	-
201103250025G	Westfield	Highland Elementary School	Closeout	Repair - Accelerated	DBB	P3 Project Planning	Tighe & Bond, Inc.		
201003250025G	Westfield	Highland Elementary School	Final Audit Approved	Repair - Accelerated	DBB	P3 Project Planning	Tighe & Bond, Inc.	Strategic Building Solutions, LLC	-
201103250033E	Westfield	Munger Hill Elementary School	Design Development	Repair - Accelerated		Vertex Construction Services	Knight, Bagge & Anderson, Inc.	Building Enclosure Associates	
201103250036G	Westfield	Paper Mill Elementary School	Closeout	Repair - Accelerated	DBB	P3 Project Planning	Tighe & Bond, Inc.	Strategic Building Solutions, LLC	-
201203250036	Westfield	Paper Mill Elementary School	Design Development	Repair - Accelerated		Vertex Construction Services	Knight, Bagge & Anderson, Inc.	Building Enclosure Associates	
201103250040G	Westfield	Southampton Road Elementary School	Closeout	Repair - Accelerated	DBB	P3 Inc.	Tighe & Bond, Inc.		
201003250040G	Westfield	Southampton Road Elementary School	Final Audit Approved	Repair - Accelerated	DBB	P3 Project Planning	Tighe & Bond, Inc.	Strategic Building Solutions, LLC	R & H Roofing
201103250505G	Westfield	Westfield High School	Closeout	Repair - Accelerated	DBB	P3 Project Planning	Tighe & Bond, Inc.	Strategic Building Solutions, LLC	-
201103250605G	Westfield	Westfield Voc Tech High School	Project Completion	Repair - Accelerated	DBB	P3 Project Planning	Tighe & Bond, Inc.	Strategic Building Solutions, LLC	-
200903300012	Weston	Field Elementary School	Construction	New Construction	DBB	Compass Project Management, Inc.	Jonathan Levi Architects LLC	Foreman Building Commissioning, LP	Colantonio, Inc.
201103300505G	Weston	Weston High School	Closeout	Repair - Accelerated	DBB	Compass Project Management, Inc.	Garcia Galuska DeSousa Consulting Engineers Inc.	RDK Engineers	-
201103300305G	Weston	Weston Middle School	Final Audit Approved	Repair - Accelerated	DBB	Compass Project Management, Inc.	Russo Barr Associates, Inc.	RDK Engineers	Greenwood Industries, Inc.
201103310015G	Westport	Alice A Macomber Primary	Closeout	Repair - Accelerated	DBB	Pinck & Co., Inc.	CGKV Architects, Inc.	CBI Consulting Inc.	-
201103310505G	Westport	Westport High School	Project Completion	Repair - Accelerated	DBB	Pinck & Co., Inc.	CGKV Architects, Inc.	CBI Consulting Inc.	-
201103360310G	Weymouth	Abigail Adams Middle School	Final Audit Approved	Repair - Accelerated	DBB	KBA Architects	Gale Associates, Inc.	Cannon Design	Greenwood Industries, Inc.
201203360080	Weymouth	William Seach Primary	Construction	Repair - Accelerated				B2Q Associates, Inc.	
201107800030G	Whitman-Hanson	John H Duval Jr Elementary School	Final Audit Approved	Repair - Accelerated	DBB	-	BETA Group, Inc.		S.I. Services, Inc.
200907800025	Whitman-Hanson	Maquan Elementary School	Schematic Design			Knight, Bagge & Anderson Inc.	Turowski2 Architecture, Inc.		-
200803400005	Williamsburg	Anne T. Dunphy School	Design Development	Addition / Renovation	DBB	Arcadis	Drummeey Rosane Anderson, Inc.	B2Q Associates, Inc.	-
201203420060	Wilmington	North Intermediate	Design Development	Repair - Accelerated				CBI Consulting Inc.	
201103420025G	Wilmington	Shawshen Elementary School	Final Audit Approved	Repair - Accelerated	DBB	P3 Inc.	Russo Barr Associates, Inc.	CBI Consulting Inc.	Lockheed Window Corporations
200903420505	Wilmington	Wilmington High School	Construction	New Construction	CM@R	Joslin, Lesser + Associates Inc.	Dore & Whittier Architects, Inc.	Symmes, Maini & McKee Associates	Gilbane Building Company
200803440025	Winchester	Vinso-Owen Elementary School	Construction	New Construction	DBB	Skanska USA Building, Inc	Tappe Associates, Inc.	Turner Facilities Management Solutions	CTA Construction Co., Inc.
201003440505	Winchester	Winchester High School	Schematic Design			Skanska USA Building, Inc	Symmes Maini & McKee Associates, Inc.		-
200803460505	Winthrop	Winthrop Sr High School	Schematic Design			Skanska USA Building, Inc	HMFH Architects, Inc.		-
201103470410G	Woburn	Daniel L Joyce Middle School	Final Audit Approved	Repair - Accelerated	DBB	Municipal Building Consultants, Inc.	Gale Associates, Inc.	Simpson Gumpertz & Heger Inc.	Reliable Roofing and Sheet Metal, LLC
200803470015	Woburn	Goodyear School	Closeout	New Construction	CM@R	Municipal Building Consultants, Inc.	Tappe Associates, Inc.	Strategic Building Solutions, LLC	Gilbane Building Company
201103470405G	Woburn	John F Kennedy Middle School	Final Audit Approved	Repair - Accelerated	DBB	Municipal Building Consultants, Inc.	Gale Associates, Inc.	Simpson Gumpertz & Heger Inc.	Greenwood Industries, Inc.
201203470060	Woburn	Wyman Elementary School	Eligibility Period						
201203480052	Worcester	Chandler Magnet School	Design Development	Repair - Accelerated		Tishman Construction Corporation of MA	Turowski2 Architecture, Inc.	Russo Barr Associates, Inc.	RDK Engineers



MSBA ID	District	School	Phase	Project Scope	Procurement Type	OPM	Designer	Cx_Company	CM/GC
201203488099	Worcester	Dr. James Caradonio Center	Design Development	Repair - Accelerated		Tishman Construction Corporation of MA	Turowski2 Architecture, Inc.	Russo Barr Associates, Inc. RDK Engineers	
201203480140	Worcester	Jacob Hiatt Magnet School	Design Development	Repair - Accelerated		Tishman Construction Corporation of MA	Turowski2 Architecture, Inc.	RDK Engineers	
201203480145	Worcester	Lake View School	Design Development	Repair - Accelerated		Tishman Construction Corporation of MA	Turowski2 Architecture, Inc.	Russo Barr Associates, Inc.	
201203480175	Worcester	May Street School	Design Development	Repair - Accelerated		Tishman Construction Corporation of MA	Turowski2 Architecture, Inc.	Russo Barr Associates, Inc.	
201203480200	Worcester	Nelson Place	OPM Selection			-	-		-
W20004048	Worcester	North High School	Project Completion	New Construction	CM@R	-	Maguire Group, Inc.	Architectural Services	Gilbane Building Company

**Projects in Construction
MSBA Grant Basis and Maximum Grant Amount
Data Reported as of February 28, 2013**

New Program and Wait List Program Totals			\$2,841,389,011	59,774		11,489,069											*Includes Alternates	\$1,962,448,339
Project	Grade	Contractor	Total Construction Cost*	Projected Enroll	PFA or Bid Data	Proposed Square Footage	Construction Cost per Square Foot	Building Cost	Building Cost per Square Foot	Project Type	Construction Start	Estimated Substantial Completion Date	Reporting Variance from Schedule	Physical Progress (%)	Change Orders (%)	Construction Status	Approximate Maximum Grant Amount *	
CAPITAL PIPELINE PROJECTS IN CONSTRUCTION																		
New Program Totals			\$2,752,766,047	57,714		11,025,379	\$250		\$191							\$1,801,385,704		
Arlington	K-5	G&R Construction	\$15,340,026	380	Bid	57,614	\$266	\$12,403,811	\$215	Design/Bid/B uild	7-Apr-12	28-Jun-13	10 days	80%	2.59%	The new school building exterior is complete. Interior work is progressing. Site work is in process.	\$9,441,396	
Assabet Valley Reg Voc Tech		CTA Construction, Inc.	\$50,755,300	963	PFA	367,565	\$138	\$36,121,000	\$98	Design/Bid/B uild	1-Apr-13	1-Aug-15		7%	0.00%	The GC has been working nights getting started on the demo and abatement as well as removing the ceiling tiles in certain areas. This is a (10) phase project which has just begun.	\$33,099,495	
Berlin-Boylston Tahanto Reg MS/HS	6-12	CTA	\$32,162,000	560	Bid	126,100	\$255	24,629,999	\$195	Design/Bid/B uild	10-May-11	1-Jul-13		98%	3.15%	The new school building is in service. Punch list and commissioning items are being completed after school hours. Demo and abatement of the adjacent existing school is complete. Remaining work includes small sections of access road & parking lot, ball field construction, final landscaping to be completed in the Fall of 2013.	\$19,849,301	
Billerica Parker ES	K-5	CTA	\$22,842,500	500	Bid	89,093	\$256	\$17,913,441	\$201	Design/Bid/B uild	15-Sep-10	29-Aug-12	90 days	98%	-0.01%	The new building is substantially complete. Phase II, demolition and site work was completed November 21, 2012. Punch list, warranty work and commissioning nearly complete.	\$15,851,020	
Brookline Heath ES	K-8	Nauset	\$6,284,185	560	Bid	80,952	\$78	\$4,807,436	\$59	Design/Bid/B uild	29-Sep-11	15-Aug-12		99%	4.70%	Misc. punch list work remaining. Commissioning nearly complete.	\$3,173,407	
Brookline Runkle ES	PK-8	G&R Construction	\$20,715,300	560	Bid	104,000	\$199	\$17,668,440	\$170	Design/Bid/B uild	10-Nov-10	10-Sep-12		96%	7.94%	Misc. punch list work remaining.	\$11,135,430	
Danvers Danvers HS	9-12	Bacon Construction	\$53,834,164	1,000	Bid	246,251	\$219	\$43,710,809	\$178	Design/Bid/B uild	14-Nov-10	10-Jul-13		93%	2.50%	Work continues on Phase I punch list items. Phase II work in the District Offices includes completion of flooring and commencement of punch work and final cleaning. Phase II work at the cafeteria and foyer areas includes the installation of kitchen equipment, flooring, wall finishes, ceiling finishes and MEP finishes.	\$37,324,055	
Douglas Douglas ES	2-5	CTA	\$23,857,111	552	Bid	83,100	\$287	\$19,026,763	\$229	Design/Bid/B uild	Mar-12	22-Jun-13		78%	0.10%	Site work, curbing, sidewalks and fields continue. Interior finishes 90%, except flooring @ 5% because of slab moisture issue. Kitchen equipment and elevator installed. Exterior panels underway. MEP and window commissioning underway.	\$17,611,449	
Douglas Douglas IS	6-8	CTA	\$12,081,767	448	Bid	88,245	\$137	\$9,417,212	\$107	Design/Bid/B uild	Mar-12	31-Jan-14		32%	0.00%	Site work continues. Gym and auditorium complete. No work is currently being performed while school is in session.	\$8,203,129	
Dracut Dracut HS	9-12	CTA	\$45,900,000	1,160	Bid	174,671	\$263	\$38,377,028	\$220	Design/Bid/B uild	27-Aug-12	26-Aug-14		35%	0.29%	Brick veneer work ongoing at C wing. Window installations and window testing continue. MEP/FP progressing in C wing. Storm drainage system excavation and installation are in progress. Demolition and reconstruction of the boiler room is underway.	\$35,838,072	
East Bridgewater E. Bridgewater Jr/Sr HS	7-12	Fontaine Brothers	\$65,409,000	950	Bid	213,544	\$306	\$47,684,117	\$223	Design/Bid/B uild	10-Aug-11	24-Jun-13		81%	0.70%	Millwork and casework have begun on all floors. All finishes are underway. Mechanical contractor is falling behind schedule but other work is being accelerated to mitigate schedule impact.	\$43,317,092	
Easthampton Easthampton HS	9-12	Fontaine Brothers	\$30,934,000	510	Bid	110,400	\$280	\$24,511,000	\$222	Design/Bid/B uild	16-May-11	15-Jan-13		95%	1.38%	FF&E and technology installations ongoing. Site work continues. Interior demolition of existing building has begun.	\$24,104,384	
Fairhaven Rogers ES	K-5	CTA	\$19,099,606	370	Bid	77,871	\$245	\$14,996,521	\$193	Design/Bid/B uild	21-May-12	4-Jul-13		86%	1.36%	The new school building exterior is complete. Interior work is nearing completion with main remaining work being completion of wall tile, ceiling tile, VCT flooring, doors, and lockers. Site work in progress includes parking lot, retention pond construction, and grading with stockpiled soils. Final landscaping and planting to be completed by the Fall of 2013.	\$13,994,641	
Fall River Morton MS	6-8	J&J Contractors	\$37,654,000	625	Bid	130,576	\$288	\$29,921,971	\$229	Design/Bid/B uild	4-Nov-11	15-Jul-13		80%	8.97%	Millwork and casework have begun on all floors. All finishes are underway. Site work continues.	\$38,251,808	
Foxborough Foxborough HS	9-12	CTA	\$12,961,769	885	Bid	218,500	\$59	\$10,337,436	\$47	Design/Bid/B uild	25-Jan-10	31-Oct-11		100%	9.26%	Final completion achieved December 4, 2012.	\$7,226,509	
Franklin Franklin HS	9 - 12	Agostini/Bacon	\$86,778,700	1,650	Bid	306,543	\$283	\$73,191,801	\$238.77	Design/Bid/B uild	16-Oct-12	15-Oct-14		18%	0.37%	Project is on schedule with footings, walls, and steel erection progressing. Elevated slab placements have progressed, along with underslab plumbing and electrical work in support of slab on grade placements. Interior masonry construction focusing on stairway areas.	\$57,246,682	
Hampden-Wilbraham Minnechaug HS	9-12	Fontaine Brothers	\$48,597,500	1,225	Bid	231,467	\$210	\$37,499,962	\$162	Design/Bid/B uild	22-Jul-10	28-Jun-12		99%	2.29%	Remaining site work is scheduled to be completed in the Spring/Summer of 2013.	\$34,863,838	
Hingham Hingham MS	6-8	Brait Builders Corp.	\$50,432,439	1,020	PFA	176,385	\$286	\$38,006,989	\$215	Design/Bid/B uild	7-Jun-12	30-Dec-14		55%	0.00%	Masonry installation has begun and interior framing started in Phase I. Roof installation complete on the classroom wing.	\$25,909,580	
Hudson John F Kennedy MS	5-7	Agostini/Bacon	\$35,102,573	715	Bid	118,850	\$295	\$28,373,294	\$239	Design/Bid/B uild	28-Sep-11	22-Nov-13		85%	1.70%	Work continues on interior finishes throughout the building and site work. Exterior metal panels nearing completion.	\$24,005,749	
Lynnfield Lynnfield HS	9-12	E.A. Colangeli	\$2,886,991	740	Bid	10,950	\$264	\$2,322,687	\$212	Design/Bid/B uild	25-Jun-12	24-May-13		97%	5.90%	Punch list work on the addition is ongoing. The site contractor has re-mobilized to complete work in the parking areas.	\$1,828,473	
Marblehead Glover ES	K-3	G&R Construction	\$20,868,000	425	Bid	79,108	\$264	\$16,977,513	\$215	Design/Bid/B uild	25-Jun-12	9-Dec-13		28%	0.84%	Demolition of the existing elementary school is complete. New school footing and foundation work is nearly complete. Installation of under-slab drainage and plumbing is nearly complete. Steel frame is complete and slab placements are progressing.	\$9,688,418	
Marshfield High School	9 - 12	Brait Brothers	\$84,980,000	1,310	Bid	267,469	\$318	\$64,604,850	\$242	Design/Bid/B uild	Aug-12	7-Jul-14		38%	0.38%	School building work on schedule. Structural steel and interior concrete placements complete. Interior masonry 75% complete and trade work underway. Underground utility work complete and binder being placed. Phase I, exterior site work, is on schedule for required August 2013 completion.	\$48,607,274	
Maynard Maynard HS	8-12	CTA	\$36,650,000	410	Bid	121,520	\$302	\$30,630,013	\$252	Design/Bid/B uild	18-Aug-11	13-Dec-13		76%	1.08%	Interior finish work is well underway. Installation of millwork and cabinetry are ongoing. Locker installations are progressing. Installation of exterior slate building panels are nearing completion. Site work has commenced.	\$23,483,860	
Middleton Howe-Manning ES	4-6	CTA	\$18,210,000	553	Bid	83,934	\$217	\$14,529,671	\$173	Design/Bid/B uild	06-Apr-10	30-Jul-11		100%	6.93%	Final completion achieved November 30, 2012.	\$12,311,976	
Monomoy Regional High School	9-12	Fontaine Brothers	\$49,374,000	700	Bid	168,000	\$294	\$41,433,695	\$247	Design/Bid/B uild	11-Feb-13	30-Jun-14		7%	0.00%	Site work is underway. Foundation walls, footings and piers have commenced. Underground utility work has begun.	\$29,696,270	
Nashoba Pompsiticut ES	K-5	P.J. Stella Construction/Brait Builders	\$23,640,900	600	Bid	98,030	\$241	\$18,427,425	\$188	Design/Bid/B uild	15-Jun-10	31-Aug-12		100%	4.35%	Project is complete with a few remaining punch list items and minor control issues.	\$15,239,622	
Natick Natick HS	9-12	Brait Builders Corp.	\$63,303,452	1,300	Bid	254,225	\$249	\$53,213,182	\$209	Design/Bid/B uild	13-Sep-10	15-Jun-12		99%	3.28%	Tennis court surfacing will be completed in June after the tennis season.	\$38,209,033	
Newburyport Bresnahan ES	PK-3	CTA Construction, Inc.	\$28,190,000	660	Bid	112,517	\$251	\$20,841,759	\$185	Design/Bid/B uild	14-Mar-13	30-Jun-14		8%	0.00%	Phase I demo complete. Foundations are 95% complete. Underground utilities are 50% complete and grading is 80% complete.	\$15,757,413	
Norfolk County Agricultural HS	9-12	TLT Construction Corp.	\$21,508,952	550	Bid	114,816	\$187	\$15,546,739	\$135	Design/Bid/B uild	27-Mar-12	9-May-14	30 days	56%	0.52%	Animal Science Building: Framing, dry wall framing, and painting continue. MEP finish work has begun. Agricultural Mechanical Building: Exterior siding continues. MEP finish work and spray acoustical insulation have started. Equine Center and Equipment Garage: Framing of Equine Center continues.	\$14,119,915	
Norfolk Freeman-Kennedy ES	3-6	Fontaine Brothers	\$25,354,966	585	Bid	96,410	\$263	\$20,023,001	\$208	Design/Bid/B uild	9-Nov-10	13-Aug-12		93%	6.00%	New building is complete and currently in use. Final punch list items are ongoing. Final paving, seeding, as well as miscellaneous landscaping to be completed in May/June of 2013.	\$15,861,760	
Oxford Oxford MS	5-8	S.O.M./ J.J. Cardosi	\$5,085,217	652	Bid	117,000	\$43	\$5,085,217	\$43	Design/Bid/B uild	1-Jun-12	29-Aug-14		25%	5.16%	Roof replacement complete. Window project scheduled for Summer 2013. HVAC, ADA, and floor replacement work scheduled for Summer 2014.	\$3,483,589	
Plymouth Plymouth HS	9-12	J&J Contractors	\$67,687,000	1,350	Bid	267,497	\$253	\$51,579,703	\$193	Design/Bid/B uild	3-May-10	22-Jun-12	30 days	98%	5.49%	Field work ongoing.	\$41,810,972	
Quincy Central MS	6-8	H.V. Collins Co. Inc	\$32,540,712	620	Bid	114,975	\$283	\$27,057,118	\$235	Design/Bid/B uild	24-May-12	5-Sep-13		35%	0.49%	Foundations and structural steel complete. Metal studs, drywall and MEP rough-ins complete. Interior finishes are underway. Exterior densglas, CMU and site utilities continue. Roofing is 95% complete.	\$32,780,403	
Somerset Berkley Somerset Berkley RHS	9-12	Bacon-Agostini	\$69,407,000	1,000	Bid	222,826	\$311	\$52,042,575	\$234	Design/Bid/B uild	3-Jul-12	15-Aug-14		28%	0.32%	Building envelope construction underway with exterior masonry about to begin. Elevated concrete slabs complete and roof installation at 75% completion. Completion of track and fields by required August 2013 deadline will be aggressive. Site contractor has rework to be done to a portion of the field. Tennis courts complete and available for acceptance.	\$49,050,210	
Sturbridge Burgess ES	K-6	Fontaine Brothers	\$22,946,000	860	Bid	131,630	\$174	\$17,591,000	\$134	Design/Bid/B uild	10-Aug-10	1-Oct-12		99%	7.42%	Both the new addition and the adjacent building renovations are substantially complete and the areas are in service. Abatement and demolition of the existing school have been completed. Remaining work includes ball fields and final landscaping which are scheduled for completion in the Fall of 2013.	\$16,616,077	
Sutton MS/HS	6-12	TLT Construction Corp.	\$41,230,800	840	Bid	179,040	\$230	\$32,998,403	\$184	Design/Bid/B uild	1-Jul-11	31-Dec-14	60 days	66%	1.65%	Interior finish work is ongoing. Floor tile, interior wall panel installations and painting are underway.	\$27,837,016	
Tewksbury Tewksbury HS	9-12	CTA/Methuen Construction Co.	\$51,600,000	1,100	Bid	218,781	\$236	\$40,159,651	\$184	Design/Bid/B uild	15-Oct-10	3-Aug-12		95%	4.54%	Punch list work is ongoing. Site work to be completed in Spring/Summer of 2013.	\$36,622,570	
Westfield Abner Gibbs ES	9-12	Fontaine Brothers	\$25,178,000	600	Bid	95,573	\$263	\$21,444,000	\$224	Design/Bid/B uild	24-Aug-12	25-Mar-14		6%	0.00%	Work stoppage regarding Article 97 "Protected Land". The City hopes to have approval in June to allow time for a City vote and a vote by the Legislation as well.	\$21,762,201	
West Springfield West Springfield HS	9-12	Fontaine Brothers	\$85,006,020	1,270	Bid	257,525	\$330	\$56,875,181	\$221	Design/Bid/B uild	14-Dec-11	31-Dec-13		70%	0.34%	Exterior framing for the gym and pool continues. Interior painting and ceiling grid installations are underway in Bldg A & B. Millwork has begun in Bldg. A & B.	\$68,808,290	
Weston Field ES	4-5	Colantonio	\$24,537,966	355	PFA	65,390	\$375	\$19,872,289	\$304	Design/Bid/B uild	21-Dec-12	15-May-14		11%	0.37%	Building mass site excavation is complete. Foundation pours are ongoing. Temporary parking lots and bus loop are in place.	\$8,610,302	

**Projects in Construction
MSBA Grant Basis and Maximum Grant Amount
Data Reported as of February 28, 2013**

Project	Grade	Contractor	Total Construction Cost*	Projected Enroll	PFA or Bid Data	Proposed Square Footage	Construction Cost per Square Foot	Building Cost	Building Cost per Square Foot	Project Type	Construction Start	Estimated Substantial Completion Date	Reporting Variance from Schedule	Physical Progress (%)	Change Orders (%)	Construction Status	Approximate Maximum Grant Amount *
Williamsburg Anne T. Dunphy ES	PK-6	Enfield	\$8,990,457	170	PFA	37,100	\$242	\$7,625,327	\$206	Design/Bid/Build	5-Apr-13	7-Apr-14		5%	0.79%	Abatement is complete with demolition ongoing.	\$7,485,572
Winchester Vinson-Owen ES	K-5	CTA	\$21,290,000	420	PFA	74,774	\$285	17,586,598	\$235	Design/Bid/Build	17-Feb-12	21-Jun-13		89%	1.98%	Site work and interior finishes are approximately 90% complete. Elevator and kitchen equipment installation are 99%. Final cleaning and commissioning are underway. Curtain wall and exterior wall panels are 95% complete.	\$10,252,465
Adams-Cheshire Hoosac Valley MSHS	6-12	Gilbane	\$33,474,193	805	Bid	174,758	\$192	24,009,952	\$137	CM-R	17-May-11	31-Jul-12		99%	2.46%	Misc. punch list work remaining.	\$28,243,131
Andover Bancroft ES	K-5	Skanska	\$34,527,063	680	PFA	67,600	\$511	21,966,698	\$325	CM-R	14-May-12	27-Oct-14		35%	0.00%	Exterior wall envelope has begun and is on schedule to be enclosed by the Fall. Site work continues.	\$16,773,753
Ashburnham Westminister, JR Briggs ES	PK-5	Consigli	\$24,780,000	520	Bid	87,085	\$285	18,202,478	\$209	CM-R	9-Mar-12	31-Dec-13		75%	0.47%	The new school building exterior is complete except for canopies. Interior is nearing completion including MEP, FP, ceramic wall tiles, VCT flooring, carpet, and gym floor. Abatement and demo of the adjacent existing school will be completed in the Summer 2013 followed by final grading and landscaping.	\$16,353,447
Burlington Marshall Simonds MS	6-8	CTA	\$24,612,440	880	Bid	151,000	\$163	\$18,988,987	\$126	CM-R	15-Apr-11	17-May-13		100%	3.74%	Remaining punch list items are nearing completion in the building. Final site grading, loam and seeding are in progress at the location of the modular classrooms. Athletic Field operations include the processing and placement of subgrade materials and the installation of the field lighting.	\$16,933,103
Concord-Carlisle HS	9-12	Turner Construction	\$71,365,015	1,225	PFA	219,871	\$325	\$61,213,812	\$278	CM-R	20-Feb-13	6-Mar-15		1%	0.00%	The CM-R has mobilized. Demo, abatement, site, electric, concrete and steel are all underway.	\$28,587,347
Dedham Avery ES	K-5	Consigli	\$18,174,209	310	Bid	62,723	\$290	\$13,528,098	\$216	CM-R	15-Oct-10	1-Jan-12		100%	6.70%	The new school building is complete and in service. Project closeout is in process.	\$10,778,452
Duxbury HS	6-12	Dimeo	\$105,369,106	1,735	Bid	322,105	\$327	\$72,739,123	\$226	CM-R	9-Jul-12	3-Jul-14		27%	0.11%	School building: steel detailing and deck placement continues on areas C & D, slab-on-deck placement for floors 2 & 3 on area B and slab on-grade in area B. CMU stairwells completed. Spray fireproofing ongoing, HVAC ductwork installation and other rough MEP work in areas A & B have begun. Curtain wall framing underway. Roofing work ongoing in areas B & C. Building envelope work continues including start of exterior masonry. Field House work continues with roofing, interior masonry walls and exterior brick veneer, slab on grade placement, metal windows and continued rough MEP installation.	\$51,406,497
Essex North Shore Agricultural & Technical High School	9-12	Gilbane	\$110,217,451	1,440	PFA	337,000	\$327	\$79,334,889	\$235	CM-R	7-May-12	30-Jun-14		32%	0.24%	Site work, exterior masonry, MEP rough-ins, and roof and window installations continue. Framing and drywall installations are ongoing throughout academy buildings. Work on pre-engineered buildings continues.	\$77,500,000
Grafton Memorial Sr HS	9-12	Dimeo	\$54,881,977	900	Bid	186,000	\$295	\$41,783,110	\$225	CM-R	18-Aug-10	10-Jul-12		100%	6.05%	The new building is complete and currently in use. Minor punch list items remaining. Commissioning is ongoing.	\$36,108,679
Greenfield	8-12	Shawmut Design	\$52,487,924	585	PFA	149,823	\$350	\$34,742,646	\$232	CM-R	1-May-13	15-Aug-15		1%	0.00%	The CM-R has mobilized to perform early site enabling work.	\$44,525,802
Leominster Leominster SHS	9-12	S.O.M.	\$33,794,797	1,825	Bid	295,859	\$114	\$25,382,707	\$86	CM-R	1-Jul-11	30-Aug-13		93%	5.76%	The project is in its 6th of 7 phases. Renovations are underway in the Administration, Art/Music Wing and the remaining C Wing classrooms. Work includes fire alarm/security/camera installation, drywall installation, ceiling grid and flooring installations.	\$30,693,543
Lexington Estabrook ES	K-5	Shawmut Design	\$32,792,348	540	PFA	91,840	\$357	\$22,795,606	\$248	CM-R	20-Jun-12	21-Feb-14		22%	0.00%	Slab on deck placements continue. Exterior framing, sheathing, air vapor barrier installations and MEP rough-ins are ongoing. Installation of masonry insulation continues.	\$13,132,418
Longmeadow Longmeadow HS	9-12	Gilbane	\$63,685,998	1,000	Bid	236,985	\$269	\$46,573,364	\$197	CM-R	Nov-10	1-Nov-13		81%	1.53%	Demolition of the main existing building is nearing completion. Renovation work continues in the Central Administration offices and other District spaces. Site work has commenced and grading for new parking lot is underway.	\$33,067,140
Medway MS	5-8	Consigli	\$18,211,824	800	Bid	223,780	\$81	\$12,885,464	\$58	CM-R	Oct-11	21-Dec-12	60 days ahead	99%	4.00%	The 4-phase project is substantially complete. Final punch list work is ongoing and commissioning is nearly complete. The goal is to have the project 100% complete by the end of May including all change orders and GMP items.	\$10,352,981
Methuen Methuen HS	9-12	Terminated Dimeo 12/31/2011. Consigli as of 5/21/2012	\$74,749,773	2,075	Bid	368,017	\$203	\$58,040,746	\$158	CM-R	21-Jul-11	Aug-14		45%	88.00%	Finishes continue in the existing academic wing that is currently being renovated and scheduled for turnover the end of July. The Phase I addition work which is also slated to turnover the end of July is falling behind due to the cafeteria and auditorium being behind schedule.	\$64,503,232
Newburyport Nock MS / Molin ES	Nock MS 6-8 Molin ES 4-5	Gilbane	\$20,942,293	845	PFA	161,500	\$130			CM-R	18-Mar-13	21-Aug-14		12%	0.00%	OPM & CM-R construction trailers in place. Phase I demo and VAT abatement complete at Phase I (9 classrooms). Air monitoring ongoing.	\$13,697,934
North Reading Middle/Senior High School	6-12	Gilbane	\$86,315,287	1,370	PFA	267,939	\$322	\$56,361,445	\$210	CM-R	02-Jul-12	21-Aug-14 (HS) 21-Aug-15 (MS)		12%	0.00%	Site work is underway. Concrete foundations are being placed. Steel is in fabrication and scheduled for delivery and installation starting late May or early June.	\$49,323,123
Norton Norton HS	9-12	WT Rich	\$27,023,541	700	Bid	130,755	\$207	\$20,590,559	\$157	CM-R	12-Mar-12	31-Dec-13		62%	2.69%	Phase 2 renovation of first floor classrooms and administration offices was completed after April school vacation. Phase 3 demolition completed. Drywall installation and taping are underway.	\$21,484,408
Rockland John Rogers MS/ HS	5-12	Agostini	\$66,362,037	1,525	Bid	275,700	\$241	\$47,724,091	\$173	CM-R	15-Jan-10	8/31/12 for MS May 2013 for HS		97%	5.59%	Work in the Phase IV Woodshop and misc. site work are ongoing. Punch list work related to Phase 2, 3 and 4 is ongoing.	\$52,837,940
Saugus Belmonte Middle School	6-8	Consigli	\$15,712,630	709	PFA	160,000	\$98	\$11,141,407	\$70	CM-R	23-May-12	3-Sep-13		63%	3.00%	This is a 4-phase project. Phase 1A and 1B are complete. Phase 1 punch list items are in process and near completion. Phase 2 is complete and punch list items are ongoing. Phase 3 started over April vacation and is 50% complete. The CM-R was able to start some of the Phase 4 work during April vacation and at nights which was originally scheduled to start in June when the school session completed. Phase 4 is 15% complete.	\$10,097,544
Shrewsbury Sherwood MS	5-6	Gilbane	\$33,986,286	900	Bid	129,378	\$263	\$22,823,030	\$176	CM-R	7-Mar-11	31-Oct-13		97%	2.04%	The new school building is in service. Punch list and commissioning items are being completed after school hours. Abatement and demolition of the adjacent existing school has been completed. Final site work to be completed by the Fall of 2013 including the balance of the access road and parking lot, ball field construction, and final grading & landscaping utilizing stockpiled soils and plantings.	\$22,369,828
Somerville E. Somerville Community School	K-8	Gilbane	\$32,590,244	500	Bid	121,100	\$269	\$24,613,842	\$203	CM-R	7-Nov-11	29-Mar-13		95%	0.32%	HVAC testing and balancing is underway. Classroom wings are ready for FF&E which will arrive in June. Landscaping to be completed as soon as the playground equipment arrives. Commissioning is underway. Project has received a TCO to occupy the building and anticipate a C of O once the playground equipment is installed.	\$15,237,996
Southbridge Southbridge MS/HS	6-12	Consigli	\$59,307,632	1,050	Bid	199,740	\$297	\$41,487,200	\$208	CM-R	30-Nov-10	31-Jul-12		99%	0.84%	Warranty work is being performed. Site work is being monitored to confirm the success of plant growth, site stabilization, and storm water work related to the sports fields.	\$52,019,398
Southeastern Regional Voc Tech High School	9-12	WT Rich	\$27,200,000	1,370	Bid	308,250	\$88	\$19,996,609	\$65	CM-R	27-Jun-11	20-Jan-14		68%	1.38%	Phase II interior renovation work, the new Gymnasium addition, elevator, the new media center, classrooms, labs, and copy room created from renovation of the existing gym are complete and are in service. Demolition and renovation of the cafeteria is in process. Final site landscaping work and installation of a new roof on the existing school will be completed in Spring/Summer 2013.	\$25,988,607
Springfield Dryden ES	PK-5	Morganti Aquadro & Cerruti	\$10,720,901	280	PFA	38,850	\$276	\$7,217,800	\$186	CM-R	28-Jun-12	1-Nov-13		35%	0.00%	Phase I exterior enclosure and all interior work have been completed. Mechanical work is complete. Punch list work is currently ongoing.	\$8,287,993
Stoneham Middle School	5-8	Shawmut Design	\$33,086,864	775	Bid	136,410	\$243	\$21,209,275	\$155	CM-R	3-Dec-12	25-Jul-14		1%	0.00%	The CM-R has mobilized and early site work is being performed.	\$22,386,455
Uxbridge High School	9-12	Shawmut Design	\$37,293,765	600	Bid	123,000	\$303	\$27,562,625	\$224	CM-R	28-Feb-11	20-Jun-12		99%	2.93%	Field work ongoing. District added bleachers to the project.	\$21,973,620
Wakefield	5-8	Bond Brothers	\$59,756,583	1,070	PFA	187,773	\$318	\$41,169,028	\$219	CM-R	18-Mar-13	15-May-15		1%	0.00%	CM-R performing early site enabling work.	\$34,689,576
Wayland ** Wayland HS	9-12	Shawmut Design	\$54,230,819	900	Bid	171,000	\$317	\$37,343,299	\$218	CM-R	28-Jun-10	1-Dec-11		100%	2.76%	Project is complete and close out is in progress	\$24,051,231
Wilmington	9-12	Gilbane	\$64,408,261	960	PFA	192,443	\$335	\$46,525,282	\$242	CM-R	April 30-13	13-Feb-15		<1%	0.00%	Site mobilization and early site work recently started.	\$37,993,245
** Excludes Field House																	
Wait List Program Totals			\$120,784,964	2,060		463,690											\$141,213,334
Springfield Forest Park MS	6-8	Consigli	\$34,745,898	660	Bid	148,800	\$234	\$26,209,932	\$176	CM-R	26-Mar-12	1-Aug-13		72%	0.00%	MEP work is in progress on all floors. Casework and countertop work continue on all floors. Toilet partitions and accessories are installed. Millwork and wood flooring installation have started. Linoleum Flooring continues to progress. Plaster patching and elevator work continues to progress. Commissioning for MEP equipment is in progress.	\$38,340,497
Springfield Putnam Voc Tech HS	9-12	Consigli	\$86,039,066	1,400	Bid	314,890	\$273	\$62,949,742	\$200	CM-R	18-May-10	20-Jul-12	60 days ahead	96%	0.66%	Site work nearly complete.	\$102,872,837
Worcester North HS	9-12	Gilbane	\$49,145,638	1,200	Bid	239,570	\$205	\$40,860,983	\$171	CM-R	24-Sep-08	Jun-11		99%	3.20%	Phase 4, which includes the parking lots and reconstruction of the ball fields, will be completed by the Fall of 2013.	\$45,911,881
