


# Project Overview Report

## July 10, 2013

A total of 315 projects that have received invitations from the Board of Directors (“Board”) to collaborate with the MSBA are currently in the MSBA’s Eligibility Period and Capital Pipeline. The following summary chart provides the number of projects in the Eligibility Period and each phase of the Capital Pipeline:

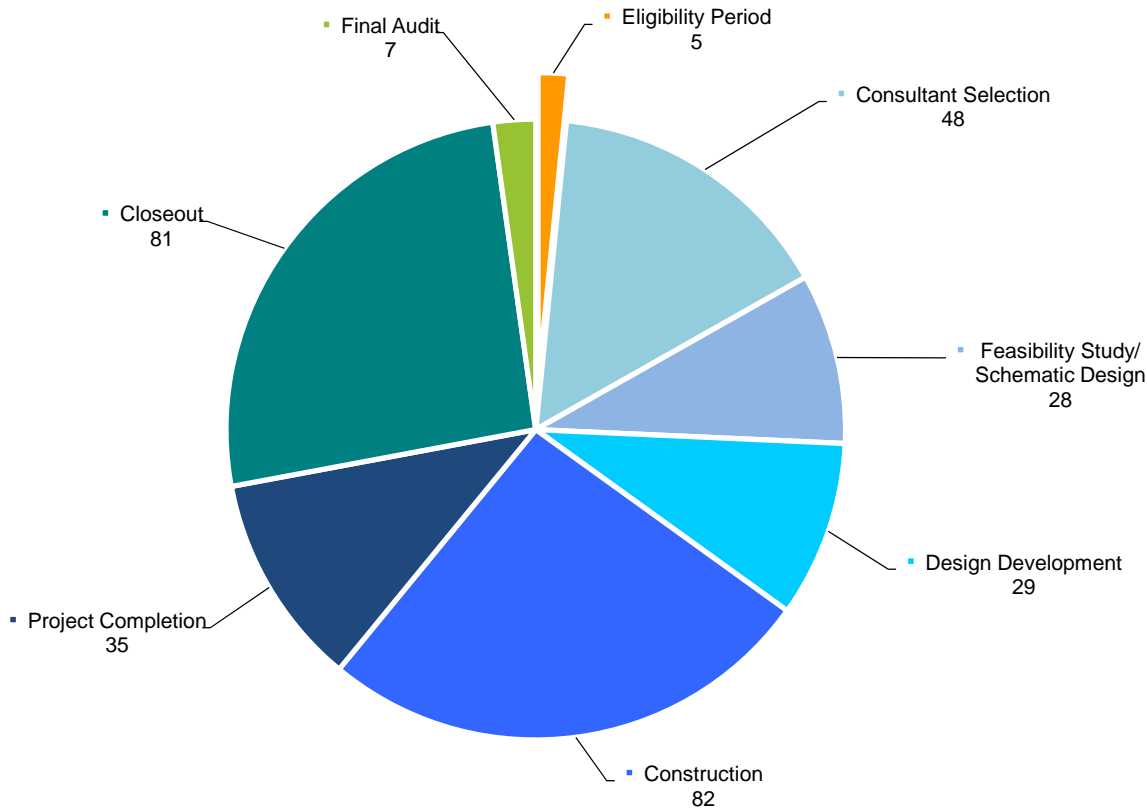

### Statement of Interest (“SOI”) Review Status

The Fiscal Year 2013 Statement of Interest Process opened on January 9, 2013 and closed on April 10, 2013. 117 Districts submitted 201 Statements of Interest for consideration in FY2013.

The Districts have identified the potential scope of the 201 SOIs as follows:

- 37 – New Construction
- 66 – Addition/Renovation
- 98 – Repair

77 of the 201 SOIs have been considered for participation in the Accelerated Repair Program. 43 of these SOIs were invited into the Program at the June Board meeting and six additional SOIs will be brought to the Board for consideration at the July Board meeting, closing invites into the Accelerated Repair Program for FY2013. Core Program SOI review will continue through the summer and into the fall, with Eligibility Period invites anticipated at the late fall/winter Board meetings.

### **Eligibility Period**

There are five districts in the Eligibility Period. One district is seeking local funding and authorization within the next 90 days, and three of the five districts have already secured funding. The remaining district has yet to confirm its date for action.

An agreed-upon enrollment is a key prerequisite for the MSBA to commence a Feasibility Study with a district. To begin the enrollment projection process, a district must file enrollment information utilizing the MSBA's online enrollment projection tool. Since the last report, one district has completed the enrollment process.

Based upon the schedules anticipated by the districts for completion of the Eligibility Period requirements, staff anticipates recommending the five districts in Eligibility Period for an Invitation to Feasibility Study at upcoming Board meetings.

### **Capital Pipeline**

#### **Consultant Selection**

After the district has completed all Eligibility Period requirements and has received a Board Invitation to Feasibility Study, the district procures an Owner's Project Manager ("OPM"). There are three districts in the Capital Pipeline that need to procure an OPM.

After a district has selected and executed a contract with an OPM, it selects a Designer utilizing either a local designer selection process for projects estimated to cost under \$5 million or the MSBA's Designer Selection Panel ("DSP") for projects estimated to cost over \$5 million. There are two districts in the Capital Pipeline that are in the process of procuring a Designer.

#### **Feasibility Study**

Once a district has procured an OPM and Designer and a Feasibility Study Agreement has been executed, the district and its consultants must complete two Feasibility Study submittals. These submittals are the Preliminary Design Program and the Preferred Schematic Report, which must be submitted prior to Board consideration to proceed into Schematic Design. Based on the most recent data and schedules provided to the MSBA by districts, the MSBA anticipates that nine districts will present their preferred schematic designs to the Board at the upcoming October and November Board meetings.

Prior to consideration by the Board for Project Scope and Budget authorization, a district must submit a schematic design to the MSBA for review. Based on the most recent data and schedules provided to the MSBA by districts, the MSBA anticipates that six districts will appear before the Board for Project Scope and Budget Agreement authorization at the upcoming October and November Board meetings.

## Commissioning

Since the last report, the MSBA has assigned Commissioning Consultants to an additional two projects as presented in the table below. To date, the MSBA has executed 233 Commissioning Consultant contracts, totaling \$18.2 million; 69 contracts have been completed.

District	School	Estimated Const. Cost (million)	Commissioning Consultant	Contract Amount
Auburn	Auburn Middle School	\$36.40	WSP Flack + Kurtz	\$89,352
Peabody	J. Henry Higgins Middle School	\$76.70	BVH Integrated Services	\$166,138
<b>Total</b>		<b>\$113.10 million</b>	<b>Total</b>	<b>\$255,490</b>

## Design Development

Once a district has secured local funding and has entered into a Project Funding Agreement with the MSBA, it enters the Design Development phase. Currently, there are 29 projects in the Design Development phase with a total combined estimated construction cost of \$624.8 million: 13 Accelerated Repair projects, One Science Lab Initiative project, and 15 Core Program projects. The 15 Core Program projects in Design Development have a total combined estimated construction cost of \$594.1 million:

### Elementary School Districts

Georgetown  
 South Hadley  
 Springfield (Brookings)  
 Revere

### Middle School Districts

Auburn  
 North Adams  
 Chicopee  
 Peabody  
 Wachusett Regional

### High School Districts

Ayer Shirley Regional  
 Greater Lowell Regional Technical  
 Greater New Bedford Voc/Tech  
 Southern Worcester Regional Technical  
 Southwick-Tolland-Granville Regional  
 West Bridgewater

## Construction

When a district issues a Notice to Proceed, the project is advanced to the Construction Phase. Currently, there are 82 projects in the Construction phase with a total combined estimated construction cost of \$2.194 billion: seven Green Repair projects, 20 Accelerated Repair projects, seven Science Lab Initiative projects, 47 Core Program projects, and one Waitlist project. The 47 Core Program projects have a total estimated construction cost of \$2.042 billion and are listed below. This does not include the 35 projects that have reached substantial completion and are currently in the Project Completion phase.

### Elementary School Districts

Andover  
Arlington  
Douglas  
Fairhaven  
Lexington  
Marblehead  
Newburyport (Bresnahan)  
Springfield (Dryden)  
Webster  
Westfield  
Weston  
Williamsburg  
Winchester

### Middle and Middle/High School Districts

Douglas  
Fall River  
Greenfield  
Hingham  
Newburyport (Nock)  
Oxford  
Quincy  
Rockland  
Saugus  
Stoneham  
Sutton  
Wakefield

### High School Districts

#### Addition/Renovation

Assabet Valley Regional Technical  
Danvers  
Dracut  
Leominster  
Methuen  
Norfolk County Agricultural  
North Reading  
Norton  
Old Colony Regional Voc/Tech  
Southeastern Regional Voc/Tech

#### New

Concord-Carlisle Regional  
Essex/North Shore Regional Voc/Tech  
Longmeadow  
Maynard  
Wilmington

#### Model

Duxbury  
East Bridgewater  
Franklin  
Marshfield  
Monomoy Regional  
Somerset-Berkley Regional  
West Springfield

## Core Program – Total Project Budget Update

Upon receiving the Board’s approval of the Project Scope and Budget, the MSBA and participating districts enter into a Project Funding Agreement that establishes the Total Project Budget and the Estimated Maximum Total Facilities Grant for an approved project. Of the grants authorized by the Board, eight projects have increased their Total Project Budgets due to acceptance of construction bids higher than the project estimates. In no event has the increase in budget resulted in an increase to the Estimated Maximum Total Facilities Grant as authorized by the Board. Please note that staff reported on the budget increases for the five projects shaded below at previous Board meetings. *There have been no changes this report.*


District	School Name	Scope	Project Funding Agreement		PFA Bid Amendment		Reason for Increase to Total Project Budget
			Total Project Budget	Total Maximum Facilities Grant	Total Project Budget	Total Maximum Facilities Grant	
<b>Core Program</b>							
Andover	Bancroft Elementary School	New	\$44,659,837	\$16,773,753	\$50,374,837	TBD*	The District has appropriated additional funds to cover the costs associated with increased construction costs and additional contingencies for litigation/settlement costs and other ineligible costs.
Essex North Shore Agricultural & Technical School	Essex North Shore Agricultural & Technical School District	New	\$125,000,000	\$77,500,000	\$133,770,000	\$77,500,000	The Board was informed at the March 30, 2011 meeting that the Total Project Budget had increased due to additional ineligible scope that would be funded by DCAM.
Lexington	Estabrook Elementary School	New	\$40,792,248	\$12,250,739	\$42,554,862	TBD*	The District has executed a GMP that exceeds the Construction Budget of the PFA. The District is currently reviewing its project budget to determine the use of the additional funds it appropriated in excess of the Total Project Budget.
Somerville	East Somerville Community School	Add/Reno	\$33,185,258	\$15,237,996	\$38,006,621	\$15,237,996	At the March 28, 2012 Board Meeting, the Board approved an amendment to the PFA and a \$6.25M District loan.
Uxbridge	Uxbridge High School	New	\$43,000,000	\$22,362,328	\$44,986,479	\$22,362,328	The District has appropriated additional funds to cover the costs associated with the construction of athletic fields originally included in the PFA but which were not included in the bid as the District's construction contract would have exceeded the budget.

\*PFA Bid Amendment has not been developed to calculate a revised total facilities grant amount. The Total Maximum Facilities Grant will not exceed the Board authorized amount in the PFA but, upon review, may decrease.

Further, MSBA staff notes that North Reading has reported construction costs higher than its project estimates. Staff is awaiting information from the district and will provide updates to the Board as they become available.

**Status of Green Repair Program**

169 projects participating in the Green Repair Program have received authorization to enter into a PFA, totaling \$366,647,226 in Total Project Costs and \$222,885,258 in MSBA grants.

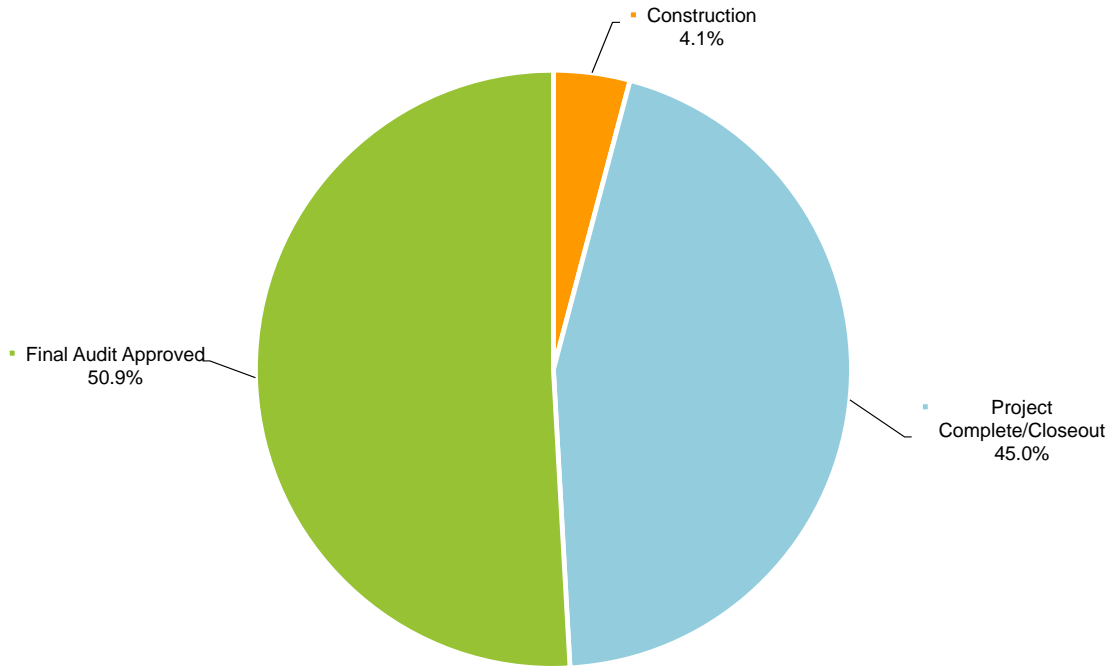

## Green Repair – Schedule Extension Update

Eight of the 169 Green Repair Projects did not meet their anticipated construction completion deadline in 2012. Schedule delays can be attributed to bid protests, lead time for windows, and construction delays on site.

The MSBA granted each district a conditional extension to its Project Funding Agreement pending compliance with the following stipulations:

- The district must submit a detailed, revised construction timeline showing how the work will be completed at each school by no later than August 30, 2013;
- An Amendment to the Project Funding Agreement between the MSBA and the district must be executed to include the updated project schedule; and
- Any costs that may result from the district's requested extension of the construction schedule will be the sole responsibility of the district and are categorically ineligible for reimbursement by the MSBA.

Each of these projects has a revised construction schedule and will be complete by the beginning of the 2013-2014 school year. In no event has the extended schedule resulted in an increase to the Estimated Maximum Total Facilities Grant as authorized by the Board. Please note that staff reported on the schedule extensions for the eight projects shaded below at previous Board meetings. Since the last report, three of these projects have reached substantial completion.

District	School	Scope	Original Construction Completion Date	Updated Construction Completion Date	Reason for Schedule Extension
Brockton	Brockton High School	Windows and Roof	31-Dec-12	30-Aug-13	Construction fell behind schedule and the District did not want work being done in an occupied building. The roof work is complete.
Haverhill	Consentino Middle School	Windows and Boiler	31-Dec-12	30-Aug-13	Bid protests and lead times caused the window project to extend beyond the 2012 construction deadline. The boiler project is complete.
Haverhill	John G. Whittier Middle School	Windows	31-Dec-12	30-Aug-13	Bid protests and lead times caused the window project to extend beyond the 2012 construction deadline.
Lowell	Moody Elementary School	Windows	15-Aug-12	30-Aug-13	Construction fell behind schedule and the District did not want work being done in an occupied building.
Lowell	Washington Elementary School	Windows	15-Aug-12	30-Aug-13	Construction fell behind schedule and the District did not want work being done in an occupied building.
Shrewsbury	Spring Street Elementary School	Roof and Windows	24-Dec-12	Complete Feb - 2013	The District issued a change order to add shrouds over the window wall unit ventilators.
Wachusett Regional	Thomas Prince Elementary School	Roof	23-Mar-12	Complete April - 2013	The District issued a change order to replace an existing skylight and, due to lead times, the work was not done until the spring of 2013.
Westport	Westport High School	Roof	4-Sep-12	Complete April - 2013	The District issued a change order to add scuppers to the roof and the work was not completed until the spring of 2013.

## Green Repair - Total Project Budget Update

Upon receiving the Board's approval of the Project Scope and Budget, the MSBA and participating districts enter into a Project Funding Agreement that establishes the Total Project Budget and the Estimated Maximum Total Facilities Grant for an approved project. Of the 169 grants authorized by the Board for the Green Repair Program, 17 projects have increased their Total Project Budgets due to acceptance of construction bids higher than the project estimates or as a result of change orders issued on the project. In no event has the increase in budget resulted in an increase to the Estimated Maximum Total Facilities Grant as authorized by the Board. Please also note that staff reported on the budget increases for all 17 of the projects shaded and shown below at previous Board meetings. West Barnstable Elementary School has exhausted the construction contingency with approved change orders resulting in an increase in the District's Total Project Budget.

District	School Name	Scope	Project Funding Agreement		PFA Bid Amendment		Reason for Increase to Total Project Budget
			Total Project Budget	Total Maximum Facilities Grant	Total Project Budget	Total Maximum Facilities Grant	
<b>Green Repair Program</b>							
Arlington	M. Norcross Stratton Elementary School	Roof, Window, Boiler	\$2,445,395	\$739,336	\$2,445,395	\$739,336	Change Orders exhausted the construction contingency.
Barnstable	West Barnstable Elementary School	Windows	\$1,173,175	\$437,829	\$1,239,205	\$437,829	Change Orders exhausted the construction contingency.
Boston	Excel High School*	Roof	\$1,227,180	\$908,850	\$1,454,735	\$908,850	District elected to accept the base bid that was higher than the approved budget. District appropriated additional funds to support overage.
Boston	Excel High School*	Roof	\$1,454,735	\$908,850	\$1,544,018	\$908,850	Change Orders exhausted the construction contingency.
Brockton	Hancock Elementary School	Roof	\$2,292,164	\$1,814,937	\$2,422,742	\$1,814,937	District elected to accept the base bid that was higher than the approved budget. District appropriated additional funds to support overage.
Brockton	West Junior High School	Roof	\$2,742,386	\$2,171,001	\$3,069,905	\$2,171,001	District elected to accept the base bid that was higher than the approved budget. District appropriated additional funds to support overage.
Fitchburg	South Street Elementary School	Boiler	\$701,186	\$560,949	\$705,391	\$501,079	Change Orders exhausted the construction contingency.
Florida	Gabriel Abbott Memorial School	Roof	\$380,310	\$213,172	\$389,422	\$188,804	Project included \$80,153 in Change Orders that offset bid savings and exhausted the construction contingency.
Hancock	Hancock Elementary School	Roof/HVAC	\$277,450	\$125,740	\$400,805	\$125,740	District elected to accept the base bids in Phases 2 and 3 that were higher than the approved budget. District needs to appropriate the overage.
Lexington	Lexington High School	Roof	\$1,122,890	\$381,221	\$1,197,444	\$381,221	District elected to accept base bid and alternates. District appropriated additional funds to support overage.
Narragansett Regional	Phillipston Memorial Elementary School	Boiler	\$143,225	\$85,712	\$161,232	\$83,275	District elected to accept the base bid that was higher than the approved budget. District appropriated additional funds to support overage.
North Attleborough	Falls Elementary School	Windows	\$701,263	\$361,433	\$710,000	\$348,948	District elected to accept the base bid that was higher than the approved budget. District's original appropriation was for \$710,000; therefore the overage was covered.
Peabody	John E. Burke Elementary School	Roof, Window, Boiler	\$2,909,873	\$1,452,745	\$3,473,534	\$1,431,417	District elected to accept the base bid that was higher than the approved budget. District appropriated additional funds to support overage.
Peabody	William A. Welch Elementary School	Roof	\$1,280,511	\$646,728	\$1,437,800	\$630,732	District elected to accept the base bid that was higher than the approved budget. District appropriated additional funds to support overage.
Pentucket Regional	Dr. John C. Page Elementary School	Roof, Window, Boiler	\$3,148,424	\$1,618,920	\$3,272,630	\$1,618,920	District elected to accept the base bid that was higher than the approved budget. District appropriated additional funds to support overage.
Reading	Birch Meadow Elementary School	Window	\$735,846	\$347,393	\$787,640	\$347,393	District elected to accept the base bid that was higher than the approved budget. Town Accountant certified that the FY2011 School Committee Operating Budget had an appropriation and encumbrance for the additional costs of the project.
Westfield	Westfield Vocational Technical High School	Roof, Window, Boiler	\$8,442,762	\$5,296,989	\$8,895,495	\$5,296,989	District elected to accept the base bid that was higher than the approved budget. District also approved an amendment to its Designer contract which increased the fee. District appropriated additional funds to support overage.

\*Excel High School is listed twice to capture two different incidences.




## **Status of Accelerated Repair Program**

Currently there are a total of 45 districts, representing 79 projects, in the Accelerated Repair Program.

### **2012 Accelerated Repair Program**

All 24 districts, representing 36 projects, approved in 2012 are under contract with consultants and have been authorized to enter into a Project Funding Agreement. The combined totals are \$63,009,653 in Total Project Costs and a maximum of \$38,267,952 in MSBA Total Facilities Grant funding. Of the 36 projects, 29 are scheduled to complete construction in 2013, and seven are scheduled to complete construction in 2014. The chart below represents the progress of the 36 projects approved in 2012.

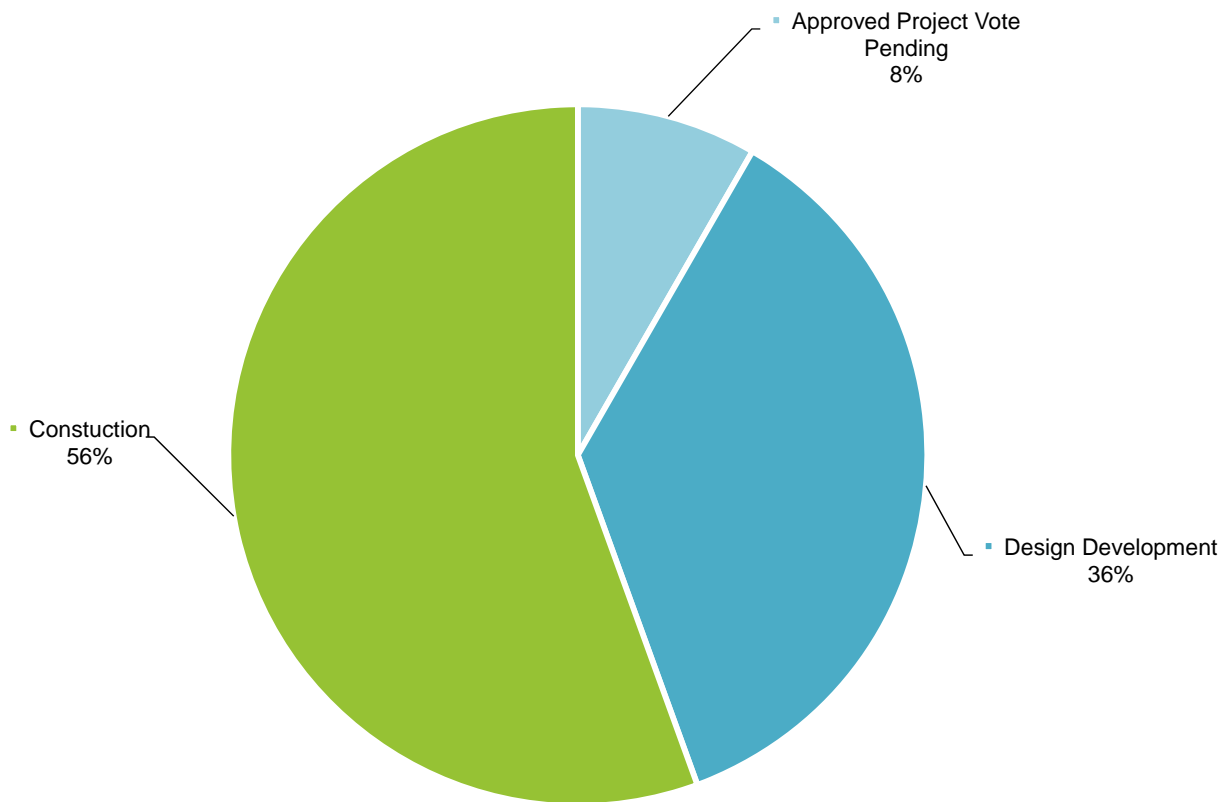


### **2013 Accelerated Repair Program**

At the June 5, 2013 Board, 25 districts, representing 43 projects, were invited into the Accelerated Repair Program. All 43 projects are currently in the OPM Selection Phase.

# 2012-2013 Eligibility Period Status

July 10, 2013  
5 Projects in Eligibility Period

Task Remaining    
  Partial Task Completed  
 Invite / Completion Date    
  Completed Task




District	2012		2013												2014							
	Nov	Dec	Jan	Feb	Mar	April	May	June	July	Aug	Sept	Oct	Nov	Dec	Jan	Feb						
Holyoke Lt. McMahon ES	11/14/12		11/28/12		12/28/12		1/28/13		5/27/13		8/26/13											
	ICC (30 days)		SBC (60 days)		Maintenance Docs		Enrollment Certification		Local Authorization		FSA (270 days)											
Woburn Wyman ES	11/14/12		11/28/12		12/28/12		1/28/13		5/27/13		8/26/13											
	ICC (30 days)		SBC (60 days)		Maintenance Docs		Enrollment Certification		Local Authorization / FSA (270 days)													
Dedham Early Education Center	11/14/12		11/28/12		12/28/12		1/30/13		2/14/13		3/16/13		4/16/13		5/14/13		8/13/13		11/12/13			
	ICC (30 days)		SBC (60 days)		Online Enrollment Projection Info		Maintenance Docs		Enrollment Certification		Local Authorization / FSA (270 days)											
Granby West Street School	11/14/12		11/28/12		12/28/12		1/30/13		2/14/13		3/16/13		4/16/13		5/14/13		8/13/13		11/12/13			
	ICC (30 days)		SBC (60 days)		Online Enrollment Projection Info		Maint Docs / Enroll Certification (180 days)		Local Authorization		FSA (270 days)											
Spencer - East Brookfield David Prouty High School	11/14/12		11/28/12		12/28/12		1/30/13		2/14/13		3/16/13		4/3/13		4/17/13		7/16/13		10/14/13		1/13/14	
	ICC / SBC / Online Enrollment Projection Info (90 days)		Maint Docs / Enroll Certification (180 days)		Local Authorization / FSA (270 days)																	

### Project Status | July 10, 2013

Core Program:	92
Waitlist:	1
Green Repair:	7
Accelerated Repair:	79
Science Lab Initiative:	8
Project Complete / Substantial Completion:	35
Closeout:	81
Final Audit Approved:	7
<b>Total Projects:</b>	<b>310</b>

Final Audit Approved / Removal		
New Salem-Windell Swift River ES	Cambridge (WL) Rindge and Latin HS	Norwood (MS) High School
North Attaborough Falls ES	Newton (WL) Newton North HS	
Pentucket Helen R. Donoghue Middle School	Taunton (WL) Parker Middle/High School	

\*As of this report, 7 projects have been approved for final MSBA approved grants and thus, with the fiscal year end, will be removed from future reports.

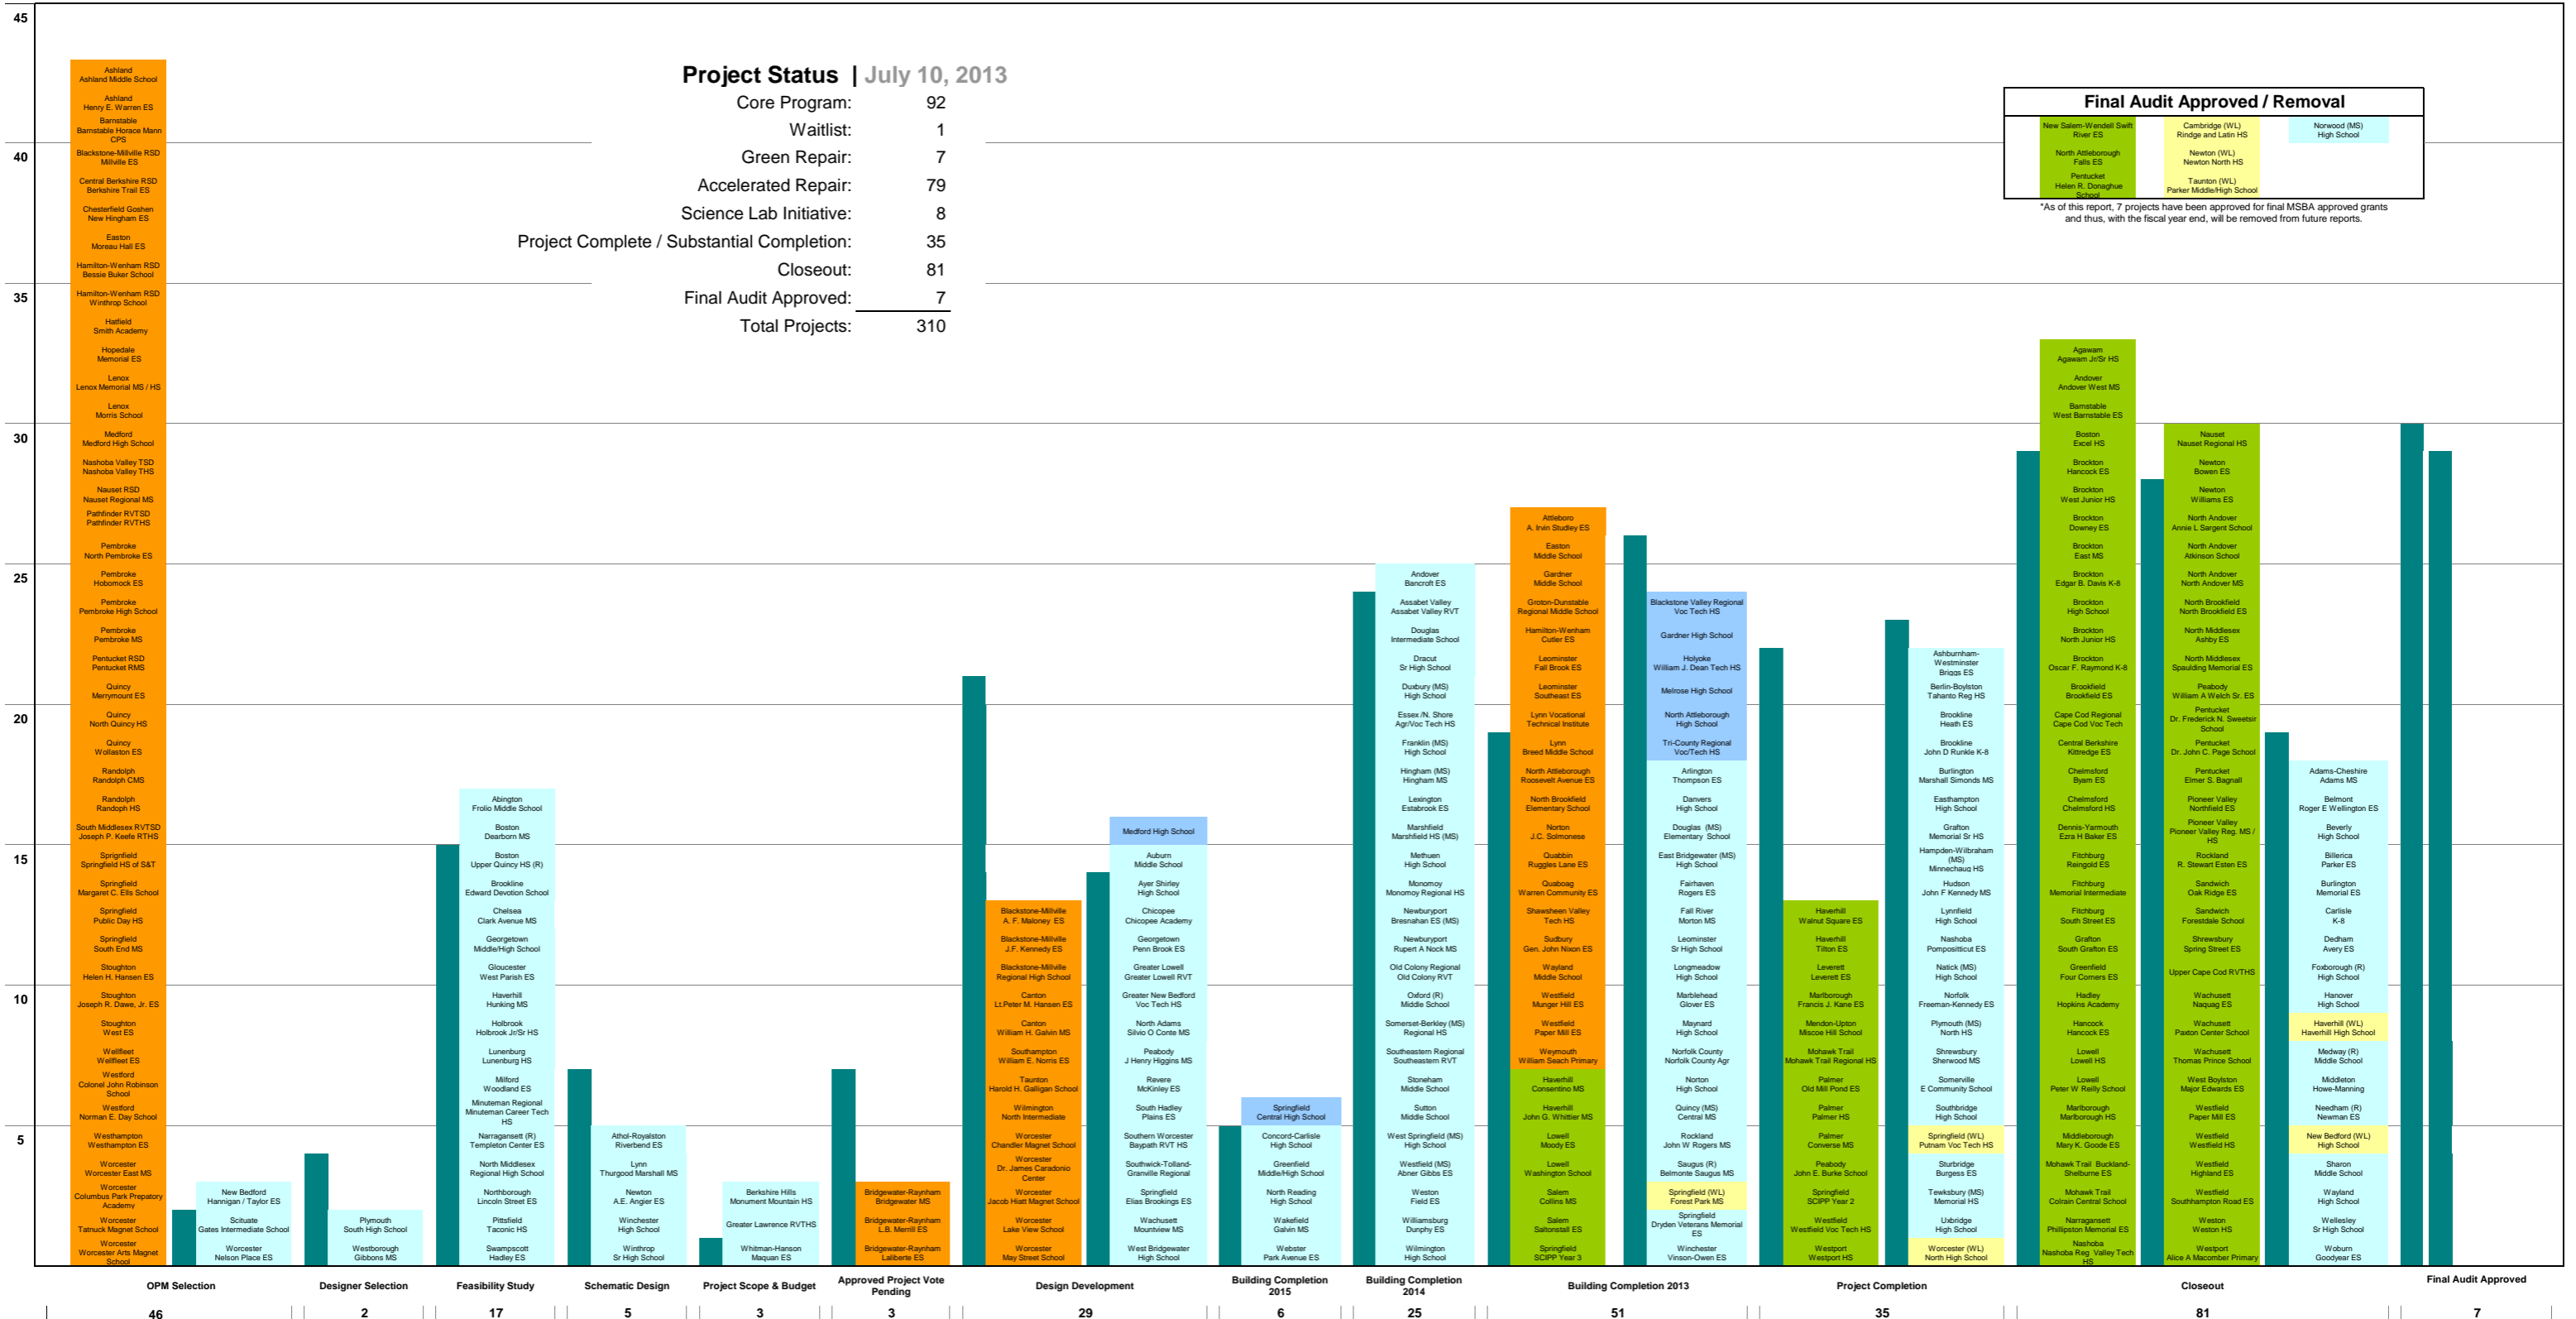

# PROJECT STATUS

310  
Total Active  
Projects

- Green Repair Program
- Accelerated Repair Program
- Accelerated Repair Program - To Be Removed

- New Program Project
- Science Lab Initiative Project
- Science Lab Initiative Project - To Be Removed

- Waitlist Projects
- Capital Pipeline Status Presented at June 5, 2013 Board of Directors Meeting



MSBA ID	District	School	Phase	Project Scope	Procurement Type	OPM	Designer	Cx_Company	CM/GC
200800010405	Abington	Frolio Middle School	Feasibility Study			Knight, Bagge & Anderson Inc.	Ai3 Architects LLC		-
200806030305	Adams-Cheshire	Adams Memorial Middle School	Closeout	Addition / Renovation	CM@R	URS Corporation	Tessier Associates, Inc.	Strategic Building Solutions, LLC	Gilbane Building Company
201100050405G	Agawam	Agawam Junior/Senior High	Closeout	Repair - Accelerated	DBB	Municipal Building Consultants, Inc.	CSS Architects Incorporated	Building Enclosure Associates	-
201100090310G	Andover	Andover West Middle	Closeout	Repair - Accelerated	DBB	Skanska USA Building, Inc	Russo Barr Associates, Inc.	Simpson Gumpertz & Heger Inc.	Eagle Rivet Roof Services Corporation
200800090003	Andover	Bancroft Elementary School	Construction	New Construction	CM@R	Dore & Whittier Management Partners, Inc.	Symmes Maini & McKee Associates, Inc.	Sebesta Blomberg & Associates, Inc.	Skanska USA Building, Inc.
200900100050	Arlington	Thompson Elementary School	Construction	New Construction	DBB	PMA Construction Services	HMFH Architects, Inc.	Consulting Engineering Services, LLC	G & R Construction, Inc.
200806100025	Ashburnham-Westminster	John R. Briggs Elementary School	Project Completion	New Construction	CM@R	STV Incorporated	Lamoureux Pagano & Associates, Inc.	Foreman Building Commissioning, LP	Consigli Construction Company, Inc.
201300140405	Ashland	Ashland Middle School	OPM Selection	Repair - Accelerated					
201300140010	Ashland	Henry E Warren Elementary School	OPM Selection	Repair - Accelerated					
200908010605	Assabet Valley	Assabet Valley Regional Technical High School	Construction	Repair - Major	DBB	Strategic Building Solutions, LLC	Design Partnership of Cambridge, Inc.	Symmes, Maini & McKee Associates	-
200906150020	Athol-Royalston	Riverbend Elementary School	Schematic Design	Repair- Accelerated		Symmes Maini & McKee Associates, Inc.	Mount Vernon Group Architects, Inc.		-
201200160001	Attleboro	A. Irvin Studley Elementary School	Construction	Repair - Accelerated		Tishman Construction Corporation of MA	Gale Associates, Inc.	CBI Consulting Inc.	
200800170305	Auburn	Auburn Middle School	Design Development	New Construction		Skanska USA Building, Inc	Lamoureux Pagano & Associates, Inc.	WSP Flack + Kurtz	-
9999	Ayer-Shirley	Ayer-Shirley Regional Middle/High School	Design Development	Addition / Renovation	CM@R	Dore and Whittier Architects, Inc.	Symmes Maini & McKee Associates, Inc.	WSP Flack + Kurtz	Consigli Construction Company, Inc.
201100200005G	Barnstable	West Barnstable Elementary School	Closeout	Repair - Accelerated	DBB	PMA Construction Services	Gale Associates, Inc.	CBI Consulting Inc.	Paul J. Rogan Co., Inc.
201300200010	Barnstable	Horace Mann Charter School	OPM Selection	Repair - Accelerated					
200800260035	Belmont	Roger Wellington Elementary School	Closeout	New Construction	CM@R	PMA Construction Services	Jonathan Levi Architects LLC	Strategic Building Solutions, LLC	Skanska USA Building, Inc.
201006180505	Berkshire Hills	Monument Mountain Regional High School	Project Scope & Budget			Strategic Building Solutions, LLC	Symmes Maini & McKee Associates, Inc.		-
200806200505	Berlin-Boylston	Tahanto Regional High School	Project Completion	New Construction	DBB	PMA Construction Services	HMFH Architects, Inc.	Strategic Building Solutions, LLC	CTA Construction Co., Inc.
200800300505	Beverly	Beverly HS	Closeout	Addition / Renovation		HEERY	Mount Vernon Group Architects, Inc.		
200800310015	Billerica	Parker Elementary School	Closeout	New Construction	DBB	Joslin, Lesser + Associates Inc.	Symmes Maini & McKee Associates, Inc.	Sebesta Blomberg & Associates, Inc.	CTA Construction Co., Inc.   RS Hurford
201306220010	Blackstone - Millville	Millville Elementary School	OPM Selection	Repair - Accelerated					
201206220015	Blackstone Valley - Millville	A.F. Maloney Elementary School	Design Development	Repair- Accelerated		Arcadis	DiMarinisi & Wolfe Architects Urban Designers	Gale Associates, Inc.	
201206220008	Blackstone Valley - Millville	J.F. Kennedy Elementary School	Design Development	Repair- Accelerated		Arcadis	DiMarinisi & Wolfe Architects Urban Designers	Gale Associates, Inc.	
201206220505	Blackstone Valley - Millville	Regional High School	Design Development	Repair - Accelerated		Arcadis	DiMarinisi & Wolfe Architects Urban Designers	Gale Associates, Inc.	
201208050605	Blackstone Valley Reg	Blackstone Valley	Construction	Science Lab		Compass Project Management, Inc.	Flansburgh Associates, Inc.	Horizon Engineering Associates, LLP	Pergola Constrion Company, Inc.
201100350522G	Boston	Excel High School	Closeout	Repair - Accelerated	DBB	Daedalus Projects Inc	BLW Engineers, Inc.	Simpson Gumpertz & Heger Inc.	-
201000350074	Boston	Henry Dearborn Middle School	Feasibility Study			Daedalus Projects Inc	Jonathan Levi Architects LLC		-



MSBA ID	District	School	Phase	Project Scope	Procurement Type	OPM	Designer	Cx_Company	CM/GC
201000350565	Boston	Quincy Upper School	Feasibility Study			<b>Maureen Anderson - City Employee</b>	HMFH Architects, Inc.		-
201206250320	Bridgewater-Raynham	Bridgewater Middle School	<b>Approved Project Vote Pending</b>	Repair - Accelerated		Pinck & Co., Inc.			
201206250020	Bridgewater-Raynham	L.B. Merrill Elementary School	<b>Approved Project Vote Pending</b>	Repair - Accelerated		Pinck & Co., Inc.			
201206250050	Bridgewater-Raynham	Laliberte Elementary School	<b>Approved Project Vote Pending</b>	Repair - Accelerated		Pinck & Co., Inc.			
201100440110G	Brockton	Downey Elementary School	<b>Closeout</b>	Repair - Accelerated	DBB	Skanska USA Building, Inc	CSS Architects Incorporated	Simpson Gumpertz & Heger Inc.	Built-up Roofing Systems LLC
201100440405G	Brockton	East Junior High School	Closeout	Repair - Accelerated	DBB	Skanska USA Building, Inc	CSS Architects Incorporated	Rist-Frost-Shumway Engineering, P.C.	Reliable Roofing and Sheet Metal, LLC
201100440023G	Brockton	Edgar B Davis	Closeout	Repair - Accelerated	DBB	Skanska USA Building, Inc	CSS Architects Incorporated	Simpson Gumpertz & Heger Inc.	Reliable Roofing and Sheet Metal, LLC
201100440045G	Brockton	Hancock Elementary School	Closeout	Repair - Accelerated	DBB	Skanska USA Building, Inc	CSS Architects Incorporated	Simpson Gumpertz & Heger Inc.	Reliable Roofing and Sheet Metal, LLC
201100440410G	Brockton	North Junior High School	Closeout	Repair - Accelerated	DBB	Skanska USA Building, Inc	CSS Architects Incorporated	Rist-Frost-Shumway Engineering, P.C.	Arden Engineering Constructors, LLC   Built-up Roofing Systems LLC
201100440078G	Brockton	Oscar F Raymond K-8	Closeout	Repair - Accelerated	DBB	Skanska USA Building, Inc	CSS Architects Incorporated	Simpson Gumpertz & Heger Inc.	Reliable Roofing and Sheet Metal, LLC
201100440420G	Brockton	West Junior High School	Closeout	Repair - Accelerated	DBB	Skanska USA Building, Inc	CSS Architects Incorporated	Simpson Gumpertz & Heger Inc.	Reliable Roofing and Sheet Metal, LLC
201100440505G	Brockton	Brockton High School	<b>Closeout</b>	Repair - Accelerated	DBB	Skanska USA Building, Inc	CSS Architects Incorporated	Simpson Gumpertz & Heger Inc.	Gibson Roofs, Inc.
201100450005G	Brookfield	Brookfield Elementary School	Closeout	Repair - Accelerated	DBB	Diversified Project Management	<b>Habeeb &amp; Associates Architects, Inc.</b>	Cannon Design	Northeast Energy Control Systems
201100460015	Brookline	Edward Devotion	Feasibility Study			<b>Anthony Guigli - Town Employee</b>	<b>HMFH Architects, Inc.</b>		
201000460025	Brookline	Heath Elementary School	<b>Project Completion</b>	Addition / Renovation	DBB	Town of Brookline Building Department	Miller Dyer Spears Inc.	Consulting Engineering Services, LLC	Nauset Construction Corporation
200800460045	Brookline	John D. Runkle School	<b>Project Completion</b>	Addition / Renovation	DBB	Town of Brookline Building Department	Design Partnership of Cambridge, Inc.	Consulting Engineering Services, LLC	G & R Construction, Inc.
200800480015	Burlington	Memorial Elementary School	Closeout	New Construction	DBB	Construction Monitoring Services, Inc.	Knight, Bagge & Anderson, Inc.	Consulting Engineering Services, LLC	CTA Construction Co., Inc.
201000480303	Burlington	Marshall Simonds Middle School	<b>Project Completion</b>	Addition / Renovation	DBB	Construction Monitoring Services, Inc.	Knight, Bagge & Anderson, Inc.	RDK Engineers	CTA Construction Co., Inc.
W20024323	Cambridge	Cambridge Rindge and Latin High School	Final Audit Approved	Addition / Renovation	DBB	-	HMFH Architects, Inc.		W. T. Rich Company Inc.
201200500012	Canton	Lt. Peter M. Hansen	<b>Design Development</b>	Repair - Accelerated		Vertex Construction Services	CSS Architects Incorporated		
201200500305	Canton	William H. Galvin Middle School	<b>Design Development</b>	Repair - Accelerated		<b>Vertex Construction Services</b>	CSS Architects Incorporated		
201008150605G	Cape Cod Region Voc Tech	Cape Cod Region Voc Tech	Closeout	Repair - Accelerated	DBB	<b>URS Corporation</b>	<b>Garcia Galuska DeSousa Consulting Engineers Inc.</b>	Fitzemeyer & Tocci Associates, Inc.	-
200800510025	Carlisle	Carlisle School	<b>Closeout</b>	Addition / Renovation	DBB	Daedalus Projects Inc	HMFH Architects, Inc.	Horizon Engineering Associates, LLP	H.V. Collins Co., Inc.
201106350035G	Central Berkshire	Kittredge Elementary School	<b>Closeout</b>	Repair - Accelerated	DBB	Daedalus Projects Inc	Bradley Architects, Inc.	Strategic Building Solutions, LLC	A.J. Schnopp Jr., Construction, Inc.   Alpha Contracting Associates, Inc.
201306350010	Central Berkshire	Berkshire Trail Elementary School	<b>OPM Selection</b>	Repair - Accelerated					
201100560030G	Chelmsford	Byam Elementary School	Closeout	Repair - Accelerated	DBB	Vertex Construction Services	Russo Barr Associates, Inc.	Simpson Gumpertz & Heger Inc.	S.O.M. Construction Ent., Inc.
201100560505G	Chelmsford	Chelmsford High School	Closeout	Repair - Accelerated	DBB	Vertex Construction Services	<b>Russo Barr Associates, Inc.</b>	Simpson Gumpertz & Heger Inc.	Lockheed Window Corporations
	Chelmsford - Goshen	New Hingham Elementary School	<b>OPM Selection</b>	Repair - Accelerated					



MSBA ID	District	School	Phase	Project Scope	Procurement Type	OPM	Designer	Cx_Company	CM/GC
200800570050	Chelsea	Clark Avenue School	Feasibility Study			Pinck & Co., Inc.	HMFH Architects, Inc.		-
200900610021	Chicopee	Chicopee Academy	Design Development			Arcadis	Caolo & Bieniek Associates, Inc.	Symmes, Maini & McKee Associates	-
200906400505	Concord-Carlisle	Concord-Carlisle Regional High School	Construction	New Construction	CM@R	KV Associates, Inc.	OMR Architects, Inc.	Strategic Building Solutions, LLC	Turner Construction Company
200800710505	Danvers	Danvers High School	Construction	Addition / Renovation	DBB	Construction Monitoring Services, Inc.	DiNisco Design Partnership, Limited	Turner Facilities Management Solutions	Bacon Construction Co, Inc.
200800730010	Dedham	Avery Elementary School	Closeout	New Construction	CM@R	Construction Monitoring Services, Inc.	Dore & Whittier Architects, Inc.	WSP Flack + Kurtz	Consigli Construction Company, Inc.
201200730005	Dedham	Early Childhood Education Center	Eligibility Period						
201006450005G	Dennis-Yarmouth	Ezra Baker Elementary School	Closeout	Repair - Accelerated	DBB	STV Incorporated	Knight, Bagge & Anderson, Inc.	CBI Consulting Inc.	Antonelli Construction Co., Inc.
200800770010	Douglas	Douglas Elementary School	Construction	New Construction		HEERY	DiNisco Design Partnership, Limited	Consulting Engineering Services, LLC	CTA Construction Co., Inc.
200800770100G	Douglas	Douglas Intermediate School	Construction	Repair - Accelerated	DBB	HEERY	DiNisco Design Partnership, Limited	Consulting Engineering Services, LLC	CTA Construction Co., Inc.
200800790505	Dracut	Dracut Senior High School	Construction	Addition / Renovation	DBB	RF Walsh Collaborative Partners	Mount Vernon Group Architects, Inc.	RDK Engineers	CTA Construction Co., Inc.
201000820505	Duxbury	Duxbury High School	Construction	New Construction	CM@R	KV Associates, Inc.	Mount Vernon Group Architects, Inc.	WSP Flack + Kurtz	Dimeo Construction Company
200900830505	East Bridgewater	East Bridgewater High School	Construction	New Construction	DBB	RF Walsh Collaborative Partners	Ai3 Architects LLC	Foreman Building Commissioning, LP	Fontaine Brothers, Inc.
200800860505	Easthampton	Easthampton High School	Project Completion	New Construction	DBB	Strategic Building Solutions, LLC	Caolo & Bieniek Associates, Inc.	Consulting Engineering Services, LLC	Fontaine Brothers, Inc.
201200880405	Easton	Easton Junior High School	Construction	Repair - Accelerated		PMA Construction Services	Russo Barr Associates, Inc.	Gale Associates, Inc.	-
201300880020	Easton	Moreau Hall Elementary School	OPM Selection	Repair - Accelerated					
200809130705	Essex Agr Tech	Essex Agricultural and Technical High School	Construction	New Construction	CM@R	PMA Construction Services	Design Partnership of Cambridge, Inc.	Turner Facilities Management Solutions	Gilbane Building Company
200800940020	Fairhaven	Rogers Elementary School	Construction	New Construction	DBB	Daedalus Projects Inc	HMFH Architects, Inc.	Consulting Engineering Services, LLC	CTA Construction Co., Inc.
200900950315	Fall River	James Madison Morton Middle School	Construction	New Construction	DBB	Maguire Group Inc.	Mount Vernon Group Architects, Inc.	Sebesta Blomberg & Associates, Inc.	J & J Contractors, Inc.
201100970048G	Fitchburg	Memorial Intermediate	Closeout	Repair - Accelerated	DBB	Compass Project Management, Inc.	Knight, Bagge & Anderson, Inc.	Simpson Gumpertz & Heger Inc.	Lockheed Window Corporations
201100970043G	Fitchburg	Reingold Elementary School	Closeout	Repair - Accelerated	DBB	Compass Project Management, Inc.	Knight, Bagge & Anderson, Inc.	Simpson Gumpertz & Heger Inc.	Lockheed Window Corporations
201100970060G	Fitchburg	South Street Elementary	Closeout	Repair - Accelerated	DBB	Compass Project Management, Inc.	Knight, Bagge & Anderson, Inc.	Simpson Gumpertz & Heger Inc.	CAM HVAC & Construction, Inc.
200800990505	Foxborough	Foxborough High School	Closeout	Repair - Major	DBB	Construction Monitoring Services, Inc.	Kaestle Boos Associates, Inc.	Consulting Engineering Services, LLC	CTA Construction Co., Inc.
200901010505	Franklin	Franklin High School	Construction	New Construction	DBB	Daedalus Projects Inc	Ai3 Architects LLC	Consulting Engineering Services, LLC	Bacon-Agostini Construction Joint Venture
201201030505	Gardner	Gardner High School	Construction	Science Lab		Pinck & Co., Inc.	Lamoureux Pagano & Associates, Inc.	Fitzemeyer & Tocci Associates, Inc.	-
201201030405	Gardner	Gardner Middle School	Construction	Repair - Accelerated		Leftfield, LLC	Richard D. Kimball Company, Inc.	Fitzemeyer & Tocci Associates, Inc.	
200901050010	Georgetown	Penn Brook Elementary School	Design Development	New Construction		Municipal Building Consultants, Inc.	Drummey Rosane Anderson, Inc.	Rist-Frost-Shumway Engineering, P.C.	-
200801050505	Georgetown	Georgetown Middle/High School	Feasibility Study			Municipal Building Consultants, Inc.	Drummey Rosane Anderson, Inc.		
200901070050	Gloucester	West Parish Elementary School	Feasibility Study			Knight, Bagge & Anderson Inc.	Dore & Whittier Architects, Inc.		-



MSBA ID	District	School	Phase	Project Scope	Procurement Type	OPM	Designer	Cx_Company	CM/GC
20110110005G	Grafton	South Grafton Elementary	Closeout	Repair - Accelerated	DBB	URS Corporation	CGKV Architects, Inc.	Horizon Engineering Associates, LLP	AAlanco Service Corporation
200801100505	Grafton	Grafton Memorial Senior	Project Completion	New Construction	CM@R	Joslin, Lesser + Associates Inc.	Symmes Maini & McKee Associates, Inc.	Horizon Engineering Associates, LLP	Dimeo Construction Company
201201110010	Granby	West Street School	Eligibility Period						
201108230605	Greater Lawrence RVT	Greater Lawrence Reg Voc Tech	Project Scope & Budget	Repair - Major		Vertex Construction Services	Richard D. Kimball Company, Inc.		-
200908280605	Greater Lowell Voc Tec	Greater Lowell Regional Technical High School	Design Development	Repair - Major		Joslin, Lesser + Associates Inc.	Knight, Bagge & Anderson, Inc.	Horizon Engineering Associates, LLP	Consigli Construction Company, Inc.
201008250605	Greater New Bedford	Vocational Technical High School	Design Development	Addition / Renovation		Construction Monitoring Services, Inc.	Drummeey Rosane Anderson, Inc.	Symmes, Maini & McKee Associates	-
201101140025G	Greenfield	Four Corners	Closeout	Repair - Accelerated	DBB	P3 Project Planning	Tighe & Bond, Inc.	Strategic Building Solutions, LLC	Five Star Building Corp.
200901140505	Greenfield	Greenfield Middle/High School	Construction	New Construction	DBB	Construction Monitoring Services, Inc.	Dore & Whittier Architects, Inc.	BVH Integrated Services, Inc.	Shawmut Design and Construction
201206730305	Groton-Dunstable	Groton Dunstable Regional Middle School	Construction	Repair - Accelerated		Collaborative Partners	ICON architecture, inc.	Russo Barr Associates, Inc.	-
201101170505G	Hadley	Hopkins Academy	Closeout	Repair - Accelerated	DBB	Strategic Building Solutions, LLC	CCS Presentation Systems	Russo Barr Associates, Inc.	MDM Engineering
201206750010	Hamilton-Wenham	Cutler School	Construction	Repair - Accelerated		Coast & Harbor Associates, Inc.	CBI Consulting, Inc.	Russo Barr Associates, Inc.	
201306750007	Hamilton-Wenham	Bessie Buker Elementary School	OPM Selection	Repair - Accelerated					
201306750015	Hamilton-Wenham	Winthrop School	OPM Selection	Repair - Accelerated					
200806800505	Hampden-Wilbraham	Minnechaug Regional High School	Project Completion	New Construction	DBB	Pinnacle One, Inc.	Mount Vernon Group Architects, Inc.	Horizon Engineering Associates, LLP	Fontaine Brothers, Inc.
201001210005G	Hancock	Hancock Elementary School	Closeout	Repair - Accelerated	DBB	-	Westall Architects		Salco Construction Company, Inc.
200801220505	Hanover	Hanover High School	Closeout	New Construction	DBB	PMA Construction Services	HMFH Architects, Inc.	Horizon Engineering Associates, LLP	Callahan, Inc.
201301270505	Hatfield	Smith Academy	OPM Selection	Repair - Accelerated					
	Haverhill	High School	Closeout						
201101280100G	Haverhill	Consentino Middle School	Construction	Repair - Accelerated	DBB	Vertex Construction Services	CSS Architects Incorporated	RDK Engineers  Russo Barr Associates, Inc.	New England Builders & Contractors, Inc. P.J. Dionne Company, Inc.
201101280085G	Haverhill	John G Whittier Middle School	Construction	Repair - Accelerated	DBB	Vertex Construction Services	CSS Architects Incorporated	Russo Barr Associates, Inc.	New England Builders & Contractors, Inc.
201201280035	Haverhill	Caleb Dustin Hunking Middle School	Feasibility Study			Joslin, Lesser + Associates Inc.	JCJ Architecture, PC		-
201101280075G	Haverhill	Tilton Elementary School	Project Completion	Repair - Accelerated	DBB	Vertex Construction Services	CSS Architects Incorporated	Russo Barr Associates, Inc.	Titan Roofing, Inc.
201101280080G	Haverhill	Walnut Square Elementary School	Project Completion	Repair - Accelerated	DBB	Vertex Construction Services	CSS Architects Incorporated	RDK Engineers  Russo Barr Associates, Inc.	P.J. Dionne Company, Inc. Titan Roofing, Inc.
201001310410	Hingham	Hingham Middle School	Construction	New Construction	DBB	Knight, Bagge & Anderson Inc.	Ai3 Architects LLC	Foreman Building Commissioning, LP	Brait Builders Corp.
200801330505	Holbrook	Holbrook Junior-Senior High School	Feasibility Study			Symmes Maini & McKee Associates, Inc.	Flansburgh Associates, Inc.		-
201201370605	Holyoke	Wm J Dean Voc Tech High	Construction	Science Lab		Skanska USA Building, Inc	Kaestle Boos Associates, Inc.	BVH Integrated Services, Inc.	-
201201370015	Holyoke	Lt. McMahon Elementary School	Eligibility Period						
201301380010	Hopedale	Memorial Elementary School	OPM Selection	Repair - Accelerated					



MSBA ID	District	School	Phase	Project Scope	Procurement Type	OPM	Designer	Cx_Company	CM/GC
200801410410	Hudson	John F. Kennedy Middle School	Project Completion	New Construction	DBB	PMA Construction Services	OMR Architects, Inc.	WSP Flack + Kurtz	Bacon-Agostini Construction Joint Venture
201301520505	Lenox	Lenox Memorial Middle/High School	OPM Selection	Repair - Accelerated					
201301520015	Lenox	Morris School	OPM Selection	Repair - Accelerated					
200801530505	Leominster	Leominster High School	Construction	Addition / Renovation	CM@R	Daedalus Projects Inc	Lamoureux Pagano & Associates, Inc.	Horizon Engineering Associates, LLP	S.O.M. Construction Ent., Inc.
201201530007	Leominster	Fall Brook	Construction	Repair - Accelerated		Compass Project Management, Inc.	Reinhardt Associates, Inc.	Horizon Engineering Associates, LLP	
201201530010	Leominster	Southeast School	Construction	Repair - Accelerated		Compass Project Management, Inc.	Reinhardt Associates, Inc.	Horizon Engineering Associates, LLP Russo Barr Associates, Inc.	
201101540005G	Leverett	Leverett Elementary School	Project Completion	Repair - Accelerated	DBB	Potomac Capital Advisors	DiMarinisi & Wolfe Architects Urban Designers	Russo Barr Associates, Inc.	-
201101550010E	Lexington	Joseph Estabrook Elementary School	Construction	New Construction		RF Walsh Collaborative Partners	DiNisco Design Partnership, Limited	BVH Integrated Services, Inc.	Shawmut Design and Construction
200801590505	Longmeadow	Longmeadow High School	Construction	New Construction	CM@R	Joslin, Lesser + Associates Inc.	OMR Architects, Inc.	Foreman Building Commissioning, LP	Gilbane Building Company
201101600505G	Lowell	Lowell High School	Closeout	Repair - Accelerated	DBB	NETCO Construction Project Managers, Inc.	ICON architecture, inc.	Building Enclosure Associates	-
201101600040G	Lowell	Peter W Reilly School	Closeout	Repair - Accelerated	DBB	NETCO Construction Project Managers, Inc.	ICON architecture, inc.	Building Enclosure Associates	-
201101600027G	Lowell	Moody Elementary School	Construction	Repair - Accelerated	DBB	NETCO Construction Project Managers, Inc.	ICON architecture, inc.	Building Enclosure Associates	Paul J. Rogan Co., Inc.
201101600055G	Lowell	Washington School	Construction	Repair - Accelerated	DBB	NETCO Construction Project Managers, Inc.	ICON architecture, inc.	Building Enclosure Associates  RDK Engineers	Alpha Contracting Associates, Inc.
200801620505	Lunenburg	Lunenburg High School	Feasibility Study			Joslin, Lesser + Associates Inc.	Tappe Associates, Inc.		-
201201630405	Lynn	Breed Middle School	Construction	Repair - Accelerated		Diversified Project Management	Kaestle Boos Associates, Inc.	CBI Consulting Inc.	
201201630605	Lynn	Lynn Vocational Tech Institute	Construction	Repair - Accelerated		Diversified Project Management	Kaestle Boos Associates, Inc.	CBI Consulting Inc.	
200901630305	Lynn	Thurgood Marshall Middle School	Schematic Design			Joslin, Lesser + Associates Inc.	Raymond Design Associates, Inc.		-
200901640505	Lynnfield	Lynnfield High School	Project Completion	Addition / Renovation	DBB	HEERY	Edward Rowse Architects, Inc.	Fitzmeyer & Tocci Associates, Inc.	E.A. Collangeli Construction Co., Inc.
200801680020	Marblehead	Glover Elementary School	Construction	New Construction	DBB	Municipal Building Consultants, Inc.	JCJ Architecture, PC	RDK Engineers	G & R Construction, Inc.
201101700505G	Marlborough	Marlborough High School	Closeout	Repair - Accelerated	DBB	RF Walsh Collaborative Partners	Baker/Wohl Architects, Inc.	RDK Engineers Building Enclosure Associates	McAnespie, Inc.  Veterans Development Corporation, Inc.
201101700008G	Marlborough	Francis J Kane Elementary School	Project Completion	Repair - Accelerated	DBB	RF Walsh Collaborative Partners	Baker/Wohl Architects, Inc.	Building Enclosure Associates	A&A Window Products, Inc.
201101710505	Marshfield	Marshfield High School	Construction	New Construction	DBB	Compass Project Management, Inc.	Ai3 Architects LLC	Sebesta Blomberg & Associates, Inc.	Brait Builders Corp.
200801740505	Maynard	Maynard High School	Construction	New Construction	DBB	Municipal Building Consultants, Inc.	Tappe Associates, Inc.	WSP Flack + Kurtz	CTA Construction Co., Inc.
201201760505	Medford	Medford High School	Design Development	Science Lab		Leftfield, LLC	DiNisco Design Partnership, Limited	Cannon Design	-
201301760505	Medford	Medford High School	OPM Selection	Repair - Accelerated					
200801770305	Medway	Medway Middle School	Closeout	Repair - Major	CM@R	Compass Project Management, Inc.	Knight, Bagge & Anderson, Inc.	Sebesta Blomberg & Associates, Inc.	Consigli Construction Company, Inc.
201201780505	Melrose	Melrose High School	Construction	Science Lab		CPI/Collaborative Partners	Ai3 Architects LLC	WSP Flack + Kurtz	-
201107100015G	Mendon-Upton	Miscoe Hill School	Project Completion	Repair - Accelerated	DBB	Maguire Group Inc.	Habeeb & Associates Architects, Inc.	Sebesta Blomberg & Associates, Inc.	Greenwood Industries, Inc.





MSBA ID	District	School	Phase	Project Scope	Procurement Type	OPM	Designer	Cx_Company	CM/GC
200801810505	Methuen	Methuen High School	Construction	Addition / Renovation	CM@R	KBA/Trident	Finegold Alexander and Associates Inc.	Environmental Health and Engineering	Dimeo Construction Company
201101820025G	Middleborough	Mary K. Goode Elementary School	Closeout	Repair - Accelerated	DBB	Maguire Group Inc.	Habeeb & Associates Architects, Inc.	Russo Barr Associates, Inc.	J.J. Cardosi, Inc.
200801840005	Middleton	Howe-Manning School	Closeout	New Construction	DBB	RF Walsh Collaborative Partners	DiNisco Design Partnership, Limited	Foreman Building Commissioning, LP	CTA Construction Co., Inc.
201101850090	Milford	Woodland Elementary School	Feasibility Study				Joslin, Lesser + Associates Inc.	HMFH Architects, Inc.	-
200908300605	Minuteman Voc Tech	Minuteman Regional High School (Career Tech)	Feasibility Study			Skanska USA Building, Inc		Kaestle Boos Associates, Inc.	-
201107170005G	Mohawk Trail	Buckland-Shelburne Reg	Closeout	Repair - Accelerated	DBB	Potomac Capital Advisors	Bradley Architects, Inc.	Strategic Building Solutions, LLC	-
201107170010G	Mohawk Trail	Colrain Central School	Closeout	Repair - Accelerated	DBB	Potomac Capital Advisors	Bradley Architects, Inc.	Strategic Building Solutions, LLC	-
201107170505G	Mohawk Trail	Mohawk Trail Reg High School	Project Completion	Repair - Accelerated	DBB	Potomac Capital Advisors	Bradley Architects, Inc.	Strategic Building Solutions, LLC	-
201122229999	Monomoy	Monomoy Regional High School	Construction	New Construction		Skanska USA Building, Inc	Mount Vernon Group Architects, Inc.	Sebesta Blomberg & Associates, Inc.	Fontaine Brothers, Inc.
201107200003G	Narragansett	Phillipston Memorial Elementary School	Closeout	Repair - Accelerated	DBB	Potomac Capital Advisors	DiMarinisi & Wolfe Architects Urban Designers	Rist-Frost-Shumway Engineering, P.C.	-
200807200020	Narragansett	Templeton Center School	Feasibility Study	Repair - Major		Strategic Building Solutions, LLC	Symmes Maini & McKee Associates, Inc.		-
200807250015	Nashoba	Pompositicut Elementary School	Project Completion	Addition / Renovation	DBB	Construction Monitoring Services, Inc.	Symmes Maini & McKee Associates, Inc.	Strategic Building Solutions, LLC	P.J. Stella Construction Corp.
200908520605G	Nashoba Valley Tech	Nashoba Valley Technical High School	Closeout	Repair - Accelerated	DBB	-	-		-
201308520605	Nashoba Valley Tech	Nashoba Valley Technical High School	OPM Selection	Repair - Accelerated					
200801980505	Natick	Natick High School	Project Completion	New Construction	DBB	RF Walsh Collaborative Partners	Ai3 Architects LLC	Rist-Frost-Shumway Engineering, P.C.	-
201106600505G	Nauset	Nauset Regional High School	Closeout	Repair - Accelerated	DBB	NETCO Construction Project Managers, Inc.	Habeeb & Associates Architects, Inc.	CBI Consulting Inc.	Capeway Roofing Systems, Inc.   Modern Glass & Aluminum, Inc.
201306600305	Nauset	Nauset Regional Middle School	OPM Selection	Repair - Accelerated					
200901990050	Needham	Newman Elementary School	Closeout	Repair - Major	CM@R	Steven H. Popper - Town Employee	Drummey Rosane Anderson, Inc.	Rist-Frost-Shumway Engineering, P.C.	Consigli Construction Company, Inc.   Triumph Leasing Corporation
201002010505	New Bedford	New Bedford High School	Closeout		DBB	-	-		-
200902010070	New Bedford	John Hannigan	OPM Selection			-	-		-
201107280015G	New Salem-Wendell	Swift River Elementary School	Final Audit Approved	Repair - Accelerated	DBB	Maguire Group Inc.	Bradley Architects, Inc.	Strategic Building Solutions, LLC	RAC Builders, Inc.
201102040005	Newburyport	Francis T Bresnahan Elementary School	Construction	New Construction		HEERY	HMFH Architects, Inc.	Fitzmeyer & Tocci Associates, Inc.	-
201002040305	Newburyport	Rupert A. Nock Middle School	Construction	Addition / Renovation	CM@R	HEERY	Miller Dyer Spears Inc.	Fitzmeyer & Tocci Associates, Inc.	-
201102070015G	Newton	Bowen	Closeout	Repair - Accelerated	DBB	STV Incorporated	Habeeb & Associates Architects, Inc.		-
201102070125G	Newton	Williams Elementary School	Closeout	Repair - Accelerated	DBB	STV Incorporated	Habeeb & Associates Architects, Inc.		-
W20014216	Newton	Newton North High School	Final Audit Approved	New Construction	CM@R	Turner Construction Co.	Dore & Whittier Architects, Inc.	Dimeo Construction Company	-
201102070005	Newton	A E Angier Elementary School	Schematic Design			Joslin, Lesser + Associates Inc.	DiNisco Design Partnership, Limited		-
200802080005	Norfolk	Freeman-Kennedy Elementary School	Project Completion	New Construction	DBB	Joslin, Lesser + Associates Inc.	Flansburgh Associates, Inc.	WSP Flack + Kurtz	Fontaine Brothers, Inc.



MSBA ID	District	School	Phase	Project Scope	Procurement Type	OPM	Designer	Cx_Company	CM/GC
200909150705	Norfolk County Agriculture	Norfolk County Agricultural High School	Construction	Addition / Renovation	DBB	Compass Project Management, Inc.	Turowski2 Architecture, Inc.	Rist-Frost-Shumway Engineering, P.C.	TLT Construction Corporation
200802090305	North Adams	Silvio O Conte Middle School	Design Development	Addition / Renovation		Strategic Building Solutions, LLC	Margo Jones Architects, Inc.	Rist-Frost-Shumway Engineering, P.C.	-
201102110018G	North Andover	Annie L Sargent School	Closeout	Repair - Accelerated	DBB	Municipal Building Consultants, Inc.	ICON architecture, inc.	Cannon Design	Varieka Construction, Inc.
201102110001G	North Andover	Atkinson School	Closeout	Repair - Accelerated	DBB	Municipal Building Consultants, Inc.	ICON architecture, inc.	Cannon Design	Paul J. Rogan Co., Inc.
201102110305G	North Andover	North Andover Middle School	Closeout	Repair - Accelerated	DBB	Municipal Building Consultants, Inc.	ICON architecture, inc.	Cannon Design	Stanley Roofing Company, Inc.
201202120505	North Attleborough	North Attleboro High	Construction	Science Lab		Skanska USA Building, Inc	Kaestle Boos Associates, Inc.	Consulting Engineering Services, LLC	-
201202120015	North Attleborough	Rossevelt Avenue Elementary School	Construction	Repair- Accelerated		Skanska USA Building, Inc	Russo Barr Associates, Inc.	Gale Associates, Inc.	
201102120010G	North Attleborough	Falls Elementary School	Final Audit Approved	Repair - Accelerated	DBB	Atlantic Construction and Management, Inc.	CSS Architects Incorporated	Gale Associates, Inc.	Northeast Energy Control Systems
201102150015G	North Brookfield	North Brookfield Elementary School	Closeout	Repair - Accelerated	DBB	Vertex Construction Services	LPBA/ Architects, Inc.	Simpson Gumpertz & Heger Inc.	Lockheed Window Corporations
201202150015	North Brookfield	North Brookfield Elementary School	Construction	Repair- Accelerated		Strategic Building Solutions, LLC	CBI Consulting, Inc.	Simpson Gumpertz & Heger Inc.	
201107350010G	North Middlesex	Ashby Elementary	Closeout	Repair - Accelerated	DBB	Compass Project Management, Inc.	Russo Barr Associates, Inc.	Building Enclosure Associates	Greenwood Industries, Inc.   GVW, Inc.
201107350005G	North Middlesex	Spaulding Memorial	Closeout	Repair - Accelerated	DBB	Compass Project Management, Inc.	Russo Barr Associates, Inc.	Building Enclosure Associates	MDM Engineering
201107350505	North Middlesex	North Middlesex Regional High School	Feasibility Study			HEERY	Symmes Maini & McKee Associates, Inc.		-
201002170505	North Reading	North Reading High School	Construction	Addition / Renovation	CM@R	PMA Construction Services	Dore & Whittier Architects, Inc.	Cannon Design	-
201102130003	Northborough	Lincoln Street Elementary School	Feasibility Study			Strategic Building Solutions, LLC	Lamoureux Pagano & Associates, Inc.		-
201202180015	Norton	J C Solmonese	Construction	Repair - Accelerated		Joslin, Lesser + Associates Inc.	Habeeb & Associates Architects, Inc.	Simpson Gumpertz & Heger Inc.	Silktown Roofing
200902180505	Norton	Norton High School	Construction	Addition / Renovation	CM@R	Pinck & Co., Inc.	JCJ Architecture, PC	Rist-Frost-Shumway Engineering, P.C.	W. T. Rich Company Inc.
200802200505	Norwood	Norwood High School	Final Audit Approved	New Construction	DBB	Compass Project Management, Inc.	Ai3 Architects LLC		Agostini Construction Co., Inc.
200908550605	Old Colony Reg Voc Tech	Vocational Technical High School	Construction	Repair - Major		Vertex Construction Services -		Consulting Engineering Services, LLC	J.D. Rivet & Company, Inc.
200802260405	Oxford	Oxford Middle School	Construction	Repair - Major		Diversified Project Management	CGKV Architects, Inc.	Cannon Design	S.O.M. Construction Ent., Inc.
201102270305G	Palmer	Converse Middle School	Project Completion	Repair - Accelerated	DBB	Diversified Project Management	Tighe & Bond, Inc.	Strategic Building Solutions, LLC	Royal Steam Heater Co.   Titan Roofing, Inc.
201102270008G	Palmer	Old Mill Pond Elementary School	Project Completion	Repair - Accelerated	DBB	Diversified Project Management	Tighe & Bond, Inc.	Strategic Building Solutions, LLC	Royal Steam Heater Co.
201102270505G	Palmer	Palmer High School	Project Completion	Repair - Accelerated	DBB	Diversified Project Management	Tighe & Bond, Inc.	Strategic Building Solutions, LLC	Royal Steam Heater Co.   Titan Roofing, Inc.
201308600605	Pathfinder	Regional Vocational Technical High School	OPM Selection	Repair - Accelerated					
201102290027G	Peabody	William A Welch Sr	Closeout	Repair - Accelerated	DBB	Daedalus Projects Inc	LPBA/ Architects, Inc.	Sebesta Blomberg & Associates, Inc.	-
200802290305	Peabody	J Henry Higgins Middle School	Design Development	New Construction		Daedalus Projects Inc	DiNisco Design Partnership, Limited	BVH Integrated Services, Inc.	-
201102290007G	Peabody	John E Burke School	Project Completion	Repair - Accelerated	DBB	Daedalus Projects Inc	LPBA/ Architects, Inc.	Sebesta Blomberg & Associates, Inc.	-
201302310010	Pembroke	Hobomock Elementary School	OPM Selection	Repair - Accelerated					



MSBA ID	District	School	Phase	Project Scope	Procurement Type	OPM	Designer	Cx_Company	CM/GC
201302310015	Pembroke	North Pembroke Elementary School	OPM Selection	Repair - Accelerated					
201302310305	Pembroke	Pembroke Community Middle School	OPM Selection	Repair - Accelerated					
201302310505	Pembroke	Pembroke High School	OPM Selection	Repair - Accelerated					
201107450020G	Pentucket	Dr Frederick N Sweetsir	Closeout	Repair - Accelerated	DBB	PMA Construction Services	Knight, Bagge & Anderson, Inc.	CBI Consulting Inc./RDK Engineers	E. Amanti & Sons, Inc.
201107450015G	Pentucket	Dr John C Page School	Closeout	Repair - Accelerated	DBB	PMA Construction Services	Knight, Bagge & Anderson, Inc.	CBI Consulting Inc./RDK Engineers	Capeway Roofing Systems, Inc.
201107450005G	Pentucket	Elmer S Bagnall	Closeout	Repair - Accelerated	DBB	PMA Construction Services	Knight, Bagge & Anderson, Inc.	CBI Consulting Inc./RDK Engineers	Gibson Roofs, Inc.
201107450010G	Pentucket	Helen R Donaghue School	Final Audit Approved	Repair - Accelerated	DBB	PMA Construction Services	Knight, Bagge & Anderson, Inc.	CBI Consulting Inc.	Gibson Roofs, Inc.
201307450405	Pentucket	Pentucket Regional Middle School	OPM Selection	Repair - Accelerated					
201107500008G	Pioneer Valley	Northfield Elementary School	Closeout	Repair - Accelerated	DBB	Diversified Project Management	CGKV Architects, Inc.	Strategic Building Solutions, LLC	-
201107500505G	Pioneer Valley	Pioneer Valley Reg Middle School/High School	Closeout	Repair - Accelerated	DBB	Diversified Project Management	CGKV Architects, Inc.	Strategic Building Solutions, LLC	-
201002360510	Pittsfield	Taconic High School	Feasibility Study			Skanska USA Building, Inc	-		-
201202390515	Plymouth	Plymouth South High School	Designer Selection			Ted Gentry Associates, Inc			
200802390505	Plymouth	Plymouth North High School	Project Completion	New Construction - Model School	DBB	Ted Gentry Associates, Inc	Ai3 Architects LLC	Sebesta Blomberg & Associates, Inc.	J & J Contractors, Inc.
201207530030	Quabbin	Ruggles Lane Elementary School	Construction	Repair - Accelerated	DBB	Vertex Construction Services	Turowski2 Architecture, Inc.	Simpson Gumpertz & Heger Inc.	PDS Engineering & Construction Inc.
201207780005	Quaboag	Warren Community Elementary School	Construction	Repair - Accelerated		Coast & Harbor Associates, Inc.	Lindgren & Sharples, Inc.	Strategic Building Solutions, LLC	AAlanco Service Corporation
200802430315	Quincy	Central Middle School	Construction	New Construction	DBB	Tishman Construction Corporation of MA	Ai3 Architects LLC	Sebesta Blomberg & Associates, Inc.	H.V. Collins Co., Inc.
201302430060	Quincy	Merrymount Elementary School	OPM Selection	Repair - Accelerated					
201302430510	Quincy	North Quincy High School	OPM Selection	Repair - Accelerated					
201302430110	Quincy	Wollaston Elementary School	OPM Selection	Repair - Accelerated					
201302440410	Randolph	Randolph Community Middle School	OPM Selection	Repair - Accelerated					
201302440505	Randolph	Randolph High School	OPM Selection	Repair - Accelerated					
201002480035	Revere	William McKinley Elementary School	Design Development	New Construction		RF Walsh Collaborative Partners	Drumme Rosane Anderson, Inc.	Rist-Frost-Shumway Engineering, P.C.	-
201102510025G	Rockland	R Stewart Esten	Closeout	Repair - Accelerated	DBB	Daedalus Projects Inc	Habeeb & Associates Architects, Inc.	Russo Barr Associates, Inc.	Northeast Energy Control Systems
200802510305	Rockland	John W. Rogers Middle School	Construction	New Construction	CM@R	Daedalus Projects Inc	Dore & Whittier Architects, Inc.	Consulting Engineering Services, LLC	Agostini Construction Co., Inc.
200902580305G	Salem	Collins Middle School	Construction	Repair - Accelerated	CM@R	KV Associates, Inc.	Reinhardt Associates, Inc.	Rist-Frost-Shumway Engineering, P.C.	Gilbane Building Company
201002580050G	Salem	Saltonstall School	Construction	Repair - Accelerated	CM@R	KV Associates, Inc.	Reinhardt Associates, Inc.	Rist-Frost-Shumway Engineering, P.C.	Gilbane Building Company
201102610010G	Sandwich	Forestdale School	Closeout	Repair - Accelerated	DBB	NETCO Construction Project Managers, Inc.	Habeeb & Associates Architects, Inc.	Gale Associates, Inc.	Varioka Construction, Inc.
200902610025G	Sandwich	Oak Ridge School	Closeout	Repair - Accelerated	DBB	NETCO Construction Project Managers, Inc.	Habeeb & Associates Architects, Inc.	Gale Associates, Inc.	J.J. Cardosi, Inc.



MSBA ID	District	School	Phase	Project Scope	Procurement Type	OPM	Designer	Cx_Company	CM/GC
201002620305	Saugus	Belmonte Middle School	Construction	Repair - Major	CM@R	Skanska USA Building, Inc	Fletcher Thompson Architecture Engineering, LLC	Consulting Engineering Services, LLC	Consigli Construction Company, Inc.
201202640305	Scituate	Gates Intermediate School	OPM Selection						
200802660305	Sharon	Sharon Middle School	Closeout	Addition / Renovation	CM@R	Daedalus Projects Inc	Kaestle Boos Associates, Inc.	Horizon Engineering Associates, LLP	Consigli Construction Company, Inc.
201208710605	Shawsheen Valley Voc Tech	Shawsheen Valley Voc Tech High School	Construction	Repair- Accelerated		Diversified Project Management	Shekar & Associates, Inc.	Fitzemeyer & Tocci Associates, Inc.	
201102710035G	Shrewsbury	Spring Street Elementary School	Closeout	Repair - Accelerated	DBB	PMA Construction Services	Habeeb & Associates Architects, Inc.	Cannon Design	Lambrian Construction Corp.
200802710305	Shrewsbury	Sherwood Middle School	Project Completion	New Construction	CM@R	PMA Construction Services	Lamoureux Pagano & Associates, Inc.	RDK Engineers	Gilbane Building Company
200811119999	Somerset-Berkley	Somerset-Berkley High School	Construction	New Construction		Skanska USA Building, Inc	Ai3 Architects LLC	Horizon Engineering Associates, LLP	Bacon-Agostini Construction Joint Venture
200902740111E	Somerville	East Somerville Community School at Cummings	Project Completion	Addition / Renovation	CM@R	PMA Construction Services	Maguire Group, Inc.	Foreman Building Commissioning, LP	Gilbane Building Company
200902780015	South Hadley	Plains School	Design Development	New Construction		Arcadis	Margo Jones Architects, Inc.	Strategic Building Solutions, LLC	-
201308290605	South Middlesex Regional Voc Tech School District	Joseph P. Keefe Regional Technical High School	OPM Selection	Repair - Accelerated					
201202750005	Southampton	William E. Norris Elementary School	Design Development	Repair - Accelerated		Tishman Construction Corporation of MA	Reinhardt Associates, Inc.	Building Enclosure Associates	
200802770505	Southbridge	Southbridge High School	Project Completion	New Construction	CM@R	Joslin, Lesser + Associates Inc.	Tappe Associates, Inc.	Environmental Health and Engineering	Consigli Construction Company, Inc.
200908720605	Southeastern Reg Voc Tech	Southeastern Regional Vocational Technical School	Construction	Addition / Renovation	CM@R	RF Walsh Collaborative Partners	Drumme Rosane Anderson, Inc.	RDK Engineers	W. T. Rich Company Inc.
200908760605	Southern Worcester Cty VT	Bay Path Regional Vocational Technical High School	Design Development	Addition / Renovation	DBB	HEERY	Kaestle Boos Associates, Inc.	RDK Engineers	Consigli Construction Company, Inc.
201107660505	Southwick-Tolland	Regional High School	Design Development	Addition / Renovation		Strategic Building Solutions, LLC	JCJ Architecture, PC		BVH Integrated Services, Inc.
200807670505	Spencer-E Brookfield	David Prouty High School	Eligibility Period	Addition / Renovation		Dore and Whittier Architects, Inc.	Design Partnership of Cambridge, Inc.		-
	<b>Springfield</b>	<b>SCIPP Year 3</b>	<b>Construction</b>						
201102810125E	Springfield	Dryden Veterans Memorial Elementary School	Construction	Addition / Renovation	CM@R	Arcadis	Drumme Rosane Anderson, Inc.	BVH Integrated Services, Inc.	-
W20014137	Springfield	Forest Park Middle School	Construction	Addition / Renovation	CM@R	Arcadis	Perkins Eastman	Foreman Building Commissioning, LP	Consigli Construction Company, Inc.
201202810500	Springfield	Central High School	Construction	Science Lab	CM@R	Lefffield, LLC	DiNisco Design Partnership, Limited	Horizon Engineering Associates, LLP	Morganti/Aquadro & Cerruti
201102810030E	Springfield	Elias Brookings Elementary School	Design Development	New Construction	CM@R	Arcadis	Drumme Rosane Anderson, Inc.	BVH Integrated Services, Inc.	-
201302810060	Springfield	Margaret C. Ellis School	OPM Selection	Repair - Accelerated					
201302810550	Springfield	Springfield Public Day high School	OPM Selection	Repair - Accelerated					
201302810530	Springfield	Springfield High School/Science-Tech	OPM Selection	Repair - Accelerated					
201302810355	Springfield	South End Middle School	OPM Selection	Repair - Accelerated					
	<b>Springfield</b>	<b>SCIPP Year 2</b>	<b>Project Completion</b>						
W20054428	Springfield	Roger L. Putnam Vocational Technical High School	Project Completion	New Construction	CM@R	Pinnacle One, Inc.	Drumme Rosane Anderson Inc.	Strategic Building Solutions, LLC	Consigli/Morganti



MSBA ID	District	School	Phase	Project Scope	Procurement Type	OPM	Designer	Cx_Company	CM/GC
200902840405	Stoneham	Stoneham Middle School	Construction	Addition / Renovation	CM@R	Joslin, Lesser + Associates Inc.	Tappe Associates, Inc.	RDK Engineers	Shawmut Design and Construction
201302850010	Stoughton	Helen Hansen Elementary School	OPM Selection	Repair- Accelerated					
201302850014	Stoughton	Joseph R. Dawe Jr. Elementary School	OPM Selection	Repair - Accelerated					
201302850020	Stoughton	West Elementary School	OPM Selection	Repair - Accelerated					
200802870005	Sturbridge	Burgess Elementary School	Project Completion	Addition / Renovation	DBB	Lamoureux Pagano & Associates, Inc.	Drumme Rosane Anderson, Inc.	Horizon Engineering Associates, LLP	Fontaine Brothers, Inc.
201202880025	Sudbury	General John Nixon Elementary School	Construction	Repair - Accelerated		PMA Construction Services Strategic Building Solutions, LLC	ICON architecture, inc.	Gale Associates, Inc.	
200802900305	Sutton	Sutton Middle School	Construction	Addition / Renovation	DBB		Flansburgh Associates, Inc.	RDK Engineers	TLT Construction Corporation
201102910010	Swampscott	Hadley Elementary School	Feasibility Study			Collaborative Partners	Mount Vernon Group Architects, Inc.		-
201202930057	Taunton	Harold H Galligan School	Design Development	Repair - Accelerated		Arcadis	Knight, Bagge & Anderson, Inc.	Gale Associates, Inc.	
W20014194	Taunton	Parker Middle/Taunton High School	Final Audit Approved	Addition / Renovation	CM@R	Gilbane Building Company	Design Partnership of Cambridge, Inc.		Bacon-Agostini Construction Joint Venture
200802950505	Tewksbury	Tewksbury Memorial High School	Project Completion	New Construction	DBB	HEERY	Symmes Maini & McKee Associates, Inc.	Sebesta Blomberg & Associates, Inc.	CTA Ventures
201208780605	Tri County	Tri County Reg Voc Tech	Construction	Science Lab		Collaborative Partners	Ai3 Architects LLC		-
201108790605G	Upper Cape Cod Voc Tech	Upper Cape Cod Voc Tech	Closeout	Repair - Accelerated	DBB	NETCO Construction Project Managers, Inc.	Knight, Bagge & Anderson, Inc.	Gale Associates, Inc.	Modern Glass & Aluminum, Inc.
200803040505	Uxbridge	Uxbridge High School	Project Completion	New Construction	CM@R	Joslin, Lesser + Associates Inc.	Raymond Design Associates, Inc.	Turner Facilities Management Solutions	Shawmut Design and Construction
201107750035G	Wachusett	Naquag Elementary School	Closeout	Repair - Accelerated	DBB	Strategic Building Solutions, LLC	LPBA/ Architects, Inc.	Rist-Frost-Shumway Engineering, P.C.	MDM Engineering
201107750040G	Wachusett	Paxton Center School	Closeout	Repair - Accelerated	DBB	Strategic Building Solutions, LLC	LPBA/ Architects, Inc.	Rist-Frost-Shumway Engineering, P.C.	MDM Engineering
201107750045G	Wachusett	Thomas Prince School	Closeout	Repair - Accelerated	DBB	Strategic Building Solutions, LLC	LPBA/ Architects, Inc.	Rist-Frost-Shumway Engineering, P.C.	MDM Engineering
200907750305	Wachusett	Mountview Middle School	Design Development			<b>Gary Kaczmarek - Town Employee</b>	Lamoureux Pagano & Associates, Inc.		-
201003050310	Wakefield	Galvin Middle School	Construction	New Construction	CM@R	Joslin, Lesser + Associates Inc.	Tappe Associates, Inc.	B2Q Associates, Inc.	Bond Brothers, Inc.
200803150505	Wayland	Wayland High School	Closeout	New Construction	CM@R	KV Associates, Inc.	HMFH Architects, Inc.	WSP Flack + Kurtz	Shawmut Design and Construction
201203150305	Wayland	Wayland Middle School	Construction	Repair - Accelerated		Joslin, Lesser + Associates Inc.	DiMarinisi & Wolfe Architects Urban Designers	CBI Consulting Inc.	Capeway Roofing Systems, Inc.
200903160015	Webster	Park Avenue Elementary School	Construction	New Construction	DBB	RF Walsh Collaborative Partners	Dore & Whittier Architects, Inc.	Cannon Design	-
200803170505	Wellesley	Wellesley Senior High School	Closeout	New Construction	CM@R	<b>Ryegate, Inc.</b>	Symmes Maini & McKee Associates, Inc.	Rist-Frost-Shumway Engineering, P.C.	Turner Construction Company
201303180005	Wellfleet	Wellfleet Elementary School	OPM Selection	Repair - Accelerated					
201103220005G	West Boylston	Major Edwards Elementary	Closeout	Repair - Accelerated	DBB	URS Corporation	Reinhardt Associates, Inc.	Cannon Design	-
201003230505	West Bridgewater	West Bridgewater Middle-Senior High School	Design Development	New Construction		Strategic Building Solutions, LLC	Flansburgh Associates, Inc.	Cannon Design	-
200903320505	West Springfield	West Springfield High School	Construction	New Construction	DBB	Strategic Building Solutions, LLC	Symmes Maini & McKee Associates, Inc.	Turner Facilities Management Solutions	Fontaine Brothers, Inc.
200903210305	Westborough	Gibbons Middle School	Designer Selection			HEERY	-		-



MSBA ID	District	School	Phase	Project Scope	Procurement Type	OPM	Designer	Cx_Company	CM/GC
201103250025G	Westfield	Highland Elementary School	Closeout	Repair - Accelerated	DBB	P3 Project Planning	Tighe & Bond, Inc.		
201103250036G	Westfield	Paper Mill Elementary School	Closeout	Repair - Accelerated	DBB	P3 Project Planning	Tighe & Bond, Inc.	Strategic Building Solutions, LLC	R & H Roofing, LLP
201103250040G	Westfield	Southampton Road Elementary School	Closeout	Repair - Accelerated	DBB	P3 Inc.	Tighe & Bond, Inc.		
201103250505G	Westfield	Westfield High School	Closeout	Repair - Accelerated	DBB	P3 Project Planning	Tighe & Bond, Inc.	Strategic Building Solutions, LLC	-
200903250020	Westfield	Abner Gibbs Elementary School	Construction	New Construction - Model School	DBB	Skanska USA Building, Inc	Margo Jones Architects, Inc.	Horizon Engineering Associates, LLP	Fontaine Brothers, Inc.
201103250033E	Westfield	Munger Hill Elementary School	Construction	Repair - Accelerated		Vertex Construction Services	Knight, Bagge & Anderson, Inc.	Building Enclosure Associates	Allied Restoration Corporation
201203250036	Westfield	Paper Mill Elementary School	Construction	Repair - Accelerated		Vertex Construction Services	Knight, Bagge & Anderson, Inc.	Building Enclosure Associates	
201103250605G	Westfield	Westfield Voc Tech High School	Project Completion	Repair - Accelerated	DBB	P3 Project Planning	Tighe & Bond, Inc.	Strategic Building Solutions, LLC	-
201303260025	Westford	Colonel John Robinson School	OPM Selection	Repair - Accelerated					
201303260007	Westford	Norman E. Day Elementary School	OPM Selection	Repair - Accelerated					
201303270005	Westhampton	Westhampton Elementary School	OPM Selection	Repair - Accelerated					
201103300505G	Weston	Weston High School	Closeout	Repair - Accelerated	DBB	Compass Project Management, Inc.	Garcia Galuska DeSousa Consulting Engineers Inc.	RDK Engineers	-
200903300012	Weston	Field Elementary School	Construction	New Construction	DBB	Compass Project Management, Inc.	Jonathan Levi Architects LLC	Foreman Building Commissioning, LP	Colantonio, Inc.
201103310015G	Westport	Alice A Macomber Primary	Closeout	Repair - Accelerated	DBB	Pinck & Co., Inc.	CGKV Architects, Inc.	CBI Consulting Inc.	-
201103310505G	Westport	Westport High School	Project Completion	Repair - Accelerated	DBB	Pinck & Co., Inc.	CGKV Architects, Inc.	CBI Consulting Inc.	-
201203360080	Weymouth	William Seach Primary	Construction	Repair - Accelerated		PMA Construction Services	BLW Engineers, Inc.	B2Q Associates, Inc.	Multitemp Mechanical Corporation
200907800025	Whitman-Hanson	Maquan Elementary School	Project Scope & Budget			Knight, Bagge & Anderson Inc.	Turowski2 Architecture, Inc.		-
200803400005	Williamsburg	Anne T. Dunphy School	Construction	Addition / Renovation	DBB	Arcadis	Drummey Rosane Anderson, Inc.	B2Q Associates, Inc.	Enfield Builders, Inc.
200903420505	Wilmington	Wilmington High School	Construction	New Construction	CM@R	Joslin, Lesser + Associates Inc.	Dore & Whittier Architects, Inc.	Symmes, Maini & McKee Associates	Gilbane Building Company
201203420060	Wilmington	North Intermediate	Design Development	Repair - Accelerated				CBI Consulting Inc.	
200803440025	Winchester	Vinson-Owen Elementary School	Construction	New Construction	DBB	Skanska USA Building, Inc	Tappe Associates, Inc.	Turner Facilities Management Solutions	CTA Construction Co., Inc.
201003440505	Winchester	Winchester High School	Schematic Design			Skanska USA Building, Inc	Symmes Maini & McKee Associates, Inc.		-
200803460505	Winthrop	Winthrop Sr High School	Schematic Design			Skanska USA Building, Inc	HMFH Architects, Inc.		-
200803470015	Woburn	Goodyear School	Closeout	New Construction	CM@R	Municipal Building Consultants, Inc.	Tappe Associates, Inc.	Strategic Building Solutions, LLC	Gilbane Building Company
201203470060	Woburn	Wyman Elementary School	Eligibility Period						
201203480052	Worcester	Chandler Magnet School	Design Development	Repair - Accelerated		Tishman Construction Corporation of MA	Turowski2 Architecture, Inc.	Russo Barr Associates, Inc.	
201203488099	Worcester	Dr. James Caradonio Center	Design Development	Repair - Accelerated		Tishman Construction Corporation of MA	Turowski2 Architecture, Inc.	Russo Barr Associates, Inc.	RDK Engineers
201203480140	Worcester	Jacob Hiatt Magnet School	Design Development	Repair - Accelerated		Tishman Construction Corporation of MA	Turowski2 Architecture, Inc.	RDK Engineers	



MSBA ID	District	School	Phase	Project Scope	Procurement Type	OPM	Designer	Cx_Company	CM\GC
201203480145	Worcester	Lake View School	Design Development	Repair - Accelerated		Tishman Construction Corporation of MA	Turowski2 Architecture, Inc.	Russo Barr Associates, Inc.	
201203480175	Worcester	May Street School	Design Development	Repair - Accelerated		Tishman Construction Corporation of MA	Turowski2 Architecture, Inc.	Russo Barr Associates, Inc.	
201303480060	Worcester	Columbus Park Preparatory Academy	<b>OPM Selection</b>	Repair - Accelerated					
201303480230	Worcester	Tatnuck Magnet School	<b>OPM Selection</b>	Repair - Accelerated					
201303480225	Worcester	Worcester Arts Magnet School	<b>OPM Selection</b>	Repair - Accelerated					
201303480420	Worcester	Worcester East Middle School	<b>OPM Selection</b>	Repair - Accelerated					
201203480200	Worcester	Nelson Place	OPM Selection			-	-		-
W20004048	Worcester	North High School	<b>Project Completion</b>	New Construction	CM@R	-	<b>Maguire Group, Inc.</b>	<b>Architectural Services</b>	<b>Gilbane Building Company</b>

### 2013 Estimated Bid Dates

Note bid dates are **Estimates ONLY**. Please contact Districts for exact information.

Total Project Budget denotes total District costs and does not denote the basis of the MSBA Total Facilities Grant.

■ - Denotes bid phase in progress or complete    
 ■ - Denotes estimated bid dates    
 ■ - Denotes estimated GMP dates

DISTRICT <small>*Projects Considering the CM @ Risk Method</small>	DESIGN BASIS FOR ENROLLMENT	PROJECT BUDGET <small>Shown in Millions</small>	CONSTRUCTION BUDGET <small>Shown in Millions</small>	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC
*LEXINGTON	540	\$40.8	\$31.1	Lexington Estabrook ES New Construction: Filed-Sub Bids rcv'd 12/19. GMP Issued January.											
NEWBURYPORT	660	\$37.3	\$31.1	Newburyport Bresnahan ES New Construction: Filed-Sub Bids rcv'd 1/16. G.C Bids rcv'd 2/1. NTP Issued March.											
MONOMOY REGIONAL SCHOOL	700	\$64.7	\$52.9	Monomoy Regional HS New Construction: Filed-Sub Bids rcv'd 1/9. G.C Bids rcv'd 1/30. NTP Issued February.											
MELROSE	1026	\$6.5	\$4.9	Melrose HS SLI: Filed-Sub Bids rcv'd 1/23. G.C Bids rcv'd 2/6. NTP Issued February.											
*STONEHAM	775	\$38.6	\$32.0	Stoneham MS Add/Reno Construction: Filed-Sub Bids rcv'd 1/17. GMP Issued March.											
*WILMINGTON	960	\$82.7	\$64.4	Wilmington HS New Construction: Filed-Sub Bids rcv'd 1/18. GMP Issued June.											
NORTH ATTLEBOROUGH	1209	\$6.2	\$4.7	North Attleborough HS SLI: Filed-Sub Bids rcv'd 3/29. G.C. Bids rcv'd 4/5. NTP Issued April.											
GARDNER	636	\$3.8	\$2.9	Gardner HS SLI: Filed-Sub Bids rcv'd 2/21. G.C. Bids rcv'd 2/28. NTP Issued March.											
ASSABET VALLEY	1000	\$62.4	\$50.8	Assabet Valley Regional HS Repair: Filed-sub Bids rcv'd 3/1. G.C. Bids rcv'd 3/25. NTP Issued April.											
BLACKSTONE VALLEY RSD	573	\$1.0	\$0.7	Blackstone Valley Regional VTHS SLI: Filed-Sub rcv'd 2/20. G.C. Bids rcv'd 3/6. NTP Issued March.											
HOLYOKE	404	\$6.9	\$5.4	Holyoke William J. Dean VTHS SLI: Filed-Sub Bids rcv'd 3/1. G.C. Bids rcv'd 3/15. NTP Issued April.											
WILLIAMSBURG	170	\$12.0	\$9.6	Williamsburg Anne T. Dunphy IS Addition/Renovation: Filed-Sub Bids rcv'd 2/12. G.C. Bids rcv'd 3/1. NTP Issued April.											
TRI COUNTY RSD	503	\$1.8	\$1.2	Tri-County Regional VTHS SLI: Filed-Sub Bids rcv'd 3/5. G.C. Bids rcv'd 3/20. NTP Issued April.											
*NEWBURYPORT	845	\$26.9	\$21.8	Newburyport Nock ES Renovation: Filed-Sub Bids rcv'd 3/8. GMP Issued April.											
OLD COLONY	570	\$2.7	\$2.2	Old Colony RVTHS Repair/SLI: Filed-Sub Bids rcv'd 4/5. G.C. Bids rcv'd 4/12. NTP Issued June.											
*GREENFIELD	585	\$63.4	\$52.9	Greenfield HS New Construction: Filed-Sub Bids rcv'd 4/24. GMP Targeted July.											
*NORTH READING	1370	\$103.4	\$86.3	N.Reading HS New Construction: Filed-Sub Bids rcv'd 4/4. GMP Issued June.											
*ANDOVER	680	\$44.7	\$34.5	Andover Bancroft ES New Construction: Filed-Sub Bids rcv'd 9/22. Non Filed-Sub Bids rcv'd 11/2. GMP issued July.											
MEDFORD	349	\$13.8	\$10.9	Medford HS SLI: Filed-Sub Bids Due 7/31. G.C. Bids Due 8/14. NTP Targeted August.											
*WAKEFIELD	1070	\$70.1	\$59.7	Wakefield Galvin MS New Construction: Filed-Sub Bids rcv'd 5/14. GMP Issued June.											



### 2013 Estimated Bid Dates

Note bid dates are **Estimates ONLY**. Please contact Districts for exact information.

Total Project Budget denotes total District costs and does not denote the basis of the MSBA Total Facilities Grant.

■ - Denotes bid phase in progress or complete    
 ■ - Denotes estimated bid dates    
 ■ - Denotes estimated GMP dates

DISTRICT <small>*Projects Considering the CM @ Risk Method</small>	DESIGN BASIS FOR ENROLLMENT	PROJECT BUDGET <small>Shown in Millions</small>	CONSTRUCTION BUDGET <small>Shown in Millions</small>	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC
WEBSTER	720	\$44.9	\$35.8				████████████████████								
*CONCORD/CARLISLE	1225	\$92.6	\$71.4					████████████████████		██████████					
SOUTHWICK-TOLLAND-GRANVILLE PowderMill IS	545	\$18.5	\$14.8				████████████████████								
SOUTHWICK-TOLLAND-GRANVILLE Woodland ES	400	\$9.7	\$7.3				████████████████████								
SOUTHWICK-TOLLAND-GRANVILLE STG Regional HS	790	\$40.7	\$31.4						████████████████████	██████████					
GREATER NEW BEDFORD	2060	\$17.1	\$13.7								██████████				
SPRINGFIELD	408	\$32.1	\$25.7								██████████	██████████			
*SPRINGFIELD	320	\$27.9	\$22.7									██████████	██████████		
*SOUTHERN WORCESTER COUNTY	1110	\$73.7	\$58.2									██████████	██████████		
WEST BRIDGEWATER	625	\$63.7	\$49.7									████████████████████			
GEORGETOWN	770	\$46.2	\$37.0									████████████████████			
*AYER-SHIRLEY	495	\$56.5	\$44.4									██████████	██████████		
REVERE	690	\$44.4	\$33.9												████████████████████
<b>Subtotal</b>	<b>24,783</b>	<b>\$1,258</b>	<b>\$1,005.9</b>												
<b>GRAND TOTAL</b>	<b>24,783</b>	<b>\$1,258</b>	<b>\$1,005.9</b>												
<b>Number of Construction-Related Employment Opportunities Created</b>			<b>5,030</b>												

### 2014 Estimated Bid Dates

Note bid dates are **Estimates ONLY**. Please contact Districts for exact information.

Total Project Budget denotes total District costs and does not denote the basis of the MSBA Total Facilities Grant.

■ - Denotes bid phase in progress or complete    
 ■ - Denotes estimated bid dates    
 ■ - Denotes estimated GMP dates

DISTRICT <small>*Projects Considering the CM @ Risk Method</small>	DESIGN BASIS FOR ENROLLMENT	PROJECT BUDGET <small>Shown in Millions</small>	CONSTRUCTION BUDGET <small>Shown in Millions</small>	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC
SOUTH HADLEY	270	\$28.2	\$21.6	<div style="display: flex; align-items: center;"> <div style="width: 100%; height: 15px; background-color: green; margin-right: 5px;"></div> <span>Plains ES New Construction: Filed-Sub Bids Due 2/6. G.C. Bids Due 2/27. NTP Targeted March.</span> </div>											
*GREATER LOWELL	1990	\$65.3	\$53.2	<div style="display: flex; align-items: center;"> <div style="width: 100%; height: 15px; background-color: green; margin-right: 5px;"></div> <div style="width: 100%; height: 15px; background-color: orange; margin-right: 5px;"></div> <span>GLRVTHS Repair: Filed-Sub Bids Due 2/19. GMP Targeted March.</span> </div>											
*AUBURN	560	\$44.5	\$35.5	<div style="display: flex; align-items: center;"> <div style="width: 100%; height: 15px; background-color: green; margin-right: 5px;"></div> <div style="width: 100%; height: 15px; background-color: orange; margin-right: 5px;"></div> <span>Auburn MS New Construction: Filed-Sub Bids Due 3/31. GMP Targeted April.</span> </div>											
WACHUSETT RSD	800	\$54.3	\$43.1	<div style="display: flex; align-items: center;"> <div style="width: 100%; height: 15px; background-color: green; margin-right: 5px;"></div> <span>Mountview MS New Construction: Filed-Sub Bids Due 3/10. G.C. Bids Due 3/17. NTP Targeted March.</span> </div>											
NORTH ADAMS	310	\$29.7	\$21.9	<div style="display: flex; align-items: center;"> <div style="width: 100%; height: 15px; background-color: green; margin-right: 5px;"></div> <span>Conte MS New Construction: Filed-Sub Bids Due 3/24. G.C. Bids Due 4/14. NTP Targeted May.</span> </div>											
PEABODY	1340	\$92.6	\$75.1	<div style="display: flex; align-items: center;"> <div style="width: 100%; height: 15px; background-color: green; margin-right: 5px;"></div> <span>Higgins MS New Construction: Filed-Sub Bids Due 5/15. G.C. Bids Due 5/22. NTP Targeted June.</span> </div>											
<b>Subtotal</b>	<b>5,270</b>	<b>\$315</b>	<b>\$250.4</b>												
<b>GRAND TOTAL</b>	<b>5,270</b>	<b>\$315</b>	<b>\$250.4</b>												
<b>Number of Construction-Related Employment Opportunities Created</b>				<b>1,252</b>											

**Projects in Construction  
MSBA Grant Basis and Maximum Grant Amount  
Data Reported as of July 10, 2013**

New Program and Wait List Program Totals			\$2,792,123,805	58,742		11,232,752											*Includes Alternates	\$1,949,621,280
Project	Grade	Contractor	Total Construction Cost*	Projected Enroll	PFA or Bid Data	Proposed Square Footage	Construction Cost per Square Foot	Building Cost	Building Cost per Square Foot	Project Type	Construction Start	Estimated Substantial Completion Date	Reporting Variance from Schedule	Physical Progress (%)	Change Orders (%)	Construction Status	Approximate Maximum Grant Amount *	
<b>CAPITAL PIPELINE PROJECTS IN CONSTRUCTION</b>																		
<b>New Program Totals</b>			<b>\$2,703,500,841</b>	<b>56,682</b>		<b>10,769,062</b>	<b>\$250</b>		<b>\$190</b>								<b>\$1,788,558,645</b>	
Arlington	K-5	G&R Construction	\$15,340,026	380	Bid	57,614	\$266	\$12,403,811	\$215	Design/Bid/Build	7-Apr-12	12-Jul-13	10 days	88%	2.59%	The building exterior is complete. Interior work in areas A & B are substantially complete. Interior work is progressing in Areas C & D. Site work is in process.	\$9,441,396	
Assabet Valley Reg Voc Tech		CTA Construction, Inc.	\$50,755,300	963	PFA	367,565	\$138	\$36,121,000	\$98	Design/Bid/Build	1-Apr-13	1-Aug-15		9%	0.00%	The GC has been working nights getting started on the demo and abatement as well as removing the ceiling tiles in certain areas. This is a (10) phase project which has just begun. Phase 1 includes demo of the ceiling tiles, demo of the mechanical room, HVAC work and abatement. Phase 2 is scheduled to begin on July 1, 2013.	\$33,099,495	
Berlin-Boylston Tahanto Reg MS/HS	6-12	CTA	\$32,162,000	560	Bid	126,100	\$255	24,629,999	\$195	Design/Bid/Build	10-May-11	1-Jul-13		98%	3.19%	The new building is in service. Punch list and commissioning items in the new building are progressing. Demo and abatement of the adjacent existing school is complete. Remaining work includes maintenance of hydro seeded playing fields, completion of irrigation system installation, and continuation of site work for west side playing field and parking area. CTA's updated schedule reflect Project completion by the 8-27-13 deadline.	\$19,849,301	
Billerica Parker ES	K-5	CTA	\$22,842,500	500	Bid	89,093	\$256	\$17,913,441	\$201	Design/Bid/Build	15-Sep-10	29-Aug-12	90 days	100%	-0.01%	Project is complete and close out is in process.	\$15,851,020	
Brookline Heath ES	K-8	Nauset	\$6,284,185	560	Bid	80,952	\$78	\$4,807,436	\$59	Design/Bid/Build	29-Sep-11	15-Aug-12		99%	4.70%	Misc. punch list work remaining.	\$3,173,407	
Brookline Runkle ES	PK-8	G&R Construction	\$20,715,300	560	Bid	104,000	\$199	\$17,668,440	\$170	Design/Bid/Build	10-Nov-10	10-Sep-12		99%	8.22%	Misc. punch list work remaining.	\$11,135,430	
Danvers Danvers HS	9-12	Bacon Construction	\$53,834,164	1,000	Bid	246,251	\$219	\$43,710,809	\$178	Design/Bid/Build	14-Nov-10	10-Jul-13		94%	2.51%	Work is nearing completion at the cafeteria and foyer areas. Remaining work includes the installation of kitchen equipment, flooring, wall finishes and MEP finishes.	\$37,324,055	
Douglas Douglas ES	2-5	CTA	\$23,857,111	552	Bid	83,100	\$287	\$19,026,763	\$229	Design/Bid/Build	Mar-12	22-Jun-13		88%	0.10%	Site work, curbing, sidewalks and fields continue. Interior finishes are 90% complete except flooring is 5% complete due to a slab moisture issue. Kitchen equipment and elevator installed. Exterior panels underway. MEP and window commissioning underway.	\$17,611,449	
Douglas Douglas IS	6-8	CTA	\$12,081,767	448	Bid	88,245	\$137	\$9,417,212	\$107	Design/Bid/Build	Mar-12	31-Jan-14		32%	0.00%	Site work continues. Gym and auditorium complete. No work is currently being performed while school is in session.	\$8,203,129	
Dracut Dracut HS	9-12	CTA	\$45,900,000	1,160	Bid	174,671	\$263	\$38,377,028	\$220	Design/Bid/Build	27-Aug-12	26-Aug-14		40%	0.29%	Window installations are in progress. Casework installations are ongoing in the lower and upper C wing. Installation of ceiling grid and elevator in the C wing are underway.	\$35,838,072	
East Bridgewater E. Bridgewater Jr/Sr HS	7-12	Fontaine Brothers	\$65,409,000	950	Bid	213,544	\$306	\$47,684,117	\$223	Design/Bid/Build	10-Aug-11	24-Jun-13	14 days	89%	0.70%	FF&E installation has begun. The Gym and the Auditorium will be completed by the end of July. Paving around the building is underway. Administration is scheduled to move into their spaces on the 15th of July.	\$43,317,092	
Easthampton Easthampton HS	9-12	Fontaine Brothers	\$30,934,000	510	Bid	110,400	\$280	\$24,511,000	\$222	Design/Bid/Build	16-May-11	19-Feb-13		96%	1.86%	New building occupied after April vacation. Demolition of old school is underway.	\$24,104,384	
Fairhaven Rogers ES	K-5	CTA	\$19,099,606	370	Bid	77,871	\$245	\$14,996,521	\$193	Design/Bid/Build	21-May-12	28-Jul-13		90%	1.29%	The new building exterior is complete. Interior work is nearing completion with main remaining work being completion of wall tile, ceiling tile, VCT flooring, doors, and lockers. Site work in progress includes parking lot, retention pond construction, and grading with stockpiled soils. Final landscaping and planting to be completed by the Fall of 2013.	\$13,994,641	
Fall River Morton MS	6-8	J&J Contractors	\$37,654,000	625	Bid	130,576	\$288	\$29,921,971	\$229	Design/Bid/Build	4-Nov-11	15-Jul-13		95%	8.97%	All finishes are underway. Site work continues.	\$38,251,808	
Franklin Franklin HS	9 - 12	Agostini/Bacon	\$86,778,700	1,650	Bid	306,543	\$283	\$73,191,801	\$238.77	Design/Bid/Build	16-Oct-12	15-Oct-14		23%	0.35%	Steel erection is complete and remaining concrete slabs in the auditorium and cafeteria projected for completion in July. Roofing is 60% complete, spray fireproofing is 50% complete, and exterior wall envelope construction is progressing. Interior mechanical-electrical work is just underway.	\$57,246,682	
Hampden-Wilbraham Minnechaug HS	9-12	Fontaine Brothers	\$48,597,500	1,225	Bid	231,467	\$210	\$37,499,962	\$162	Design/Bid/Build	22-Jul-10	28-Jun-12		99%	2.29%	Remaining site work is scheduled to be completed by end of Summer of 2013.	\$34,863,838	
Hingham Hingham MS	6-8	Brait Builders Corp.	\$47,881,000	1,020	Bid	176,385	\$271	\$41,227,552	\$234	Design/Bid/Build	7-Jun-12	30-Dec-14		60%	0.19%	Interior masonry installation is 80% complete and window installation is 30% complete. Painting has begun as well as the floor epoxy application in areas identified to be needed.	\$25,909,580	
Hudson John F Kennedy MS	5-7	Agostini/Bacon	\$35,102,573	715	Bid	118,850	\$295	\$28,373,294	\$239	Design/Bid/Build	28-Sep-11	1-Jun-13		86%	1.67%	Final cleaning and miscellaneous interior finishes in progress. District has begun to move into administrative spaces. Demolition of existing school and site work are in progress.	\$24,005,749	
Lynnfield Lynnfield HS	9-12	E.A. Colangeli	\$2,886,991	740	Bid	10,950	\$264	\$2,322,687	\$212	Design/Bid/Build	25-Jun-12	28-Jun-13		97%	8.09%	Minor punch list work remaining. Site work is still in progress.	\$1,828,473	
Marblehead Glover ES	K-3	G&R Construction	\$20,868,000	425	Bid	79,108	\$264	\$16,977,513	\$215	Design/Bid/Build	25-Jun-12	13-Dec-13		45%	1.34%	Demolition of existing elementary school is complete. New school footings, foundation, under slab plumbing, slab placements, and steel erection is complete. Exterior wall framing, sheathing and MEP rough-in work are in process. CMU has been installed for the elevator and duct shaft in Area 1 and is progressing in the Gym. The Gym roof is complete and sloped roof work is in process.	\$9,688,418	
Marshfield High School	9 - 12	Brait Brothers	\$84,980,000	1,310	Bid	267,469	\$318	\$64,604,850	\$242	Design/Bid/Build	Aug-12	7-Jul-14		44%	0.38%	Community field, athletic field, and concession building nearing completion and turnover to the District. Work has progressed on sidewalks, parking areas, and the connector road with dense grade and binder pavement placement. Work continues on the interior masonry walls and exterior masonry in the courtyard. All concrete slabs are complete. Trade work inside the building is also progressing along with spray fireproofing installation.	\$48,607,274	
Maynard Maynard HS	8-12	CTA	\$36,650,000	410	Bid	121,520	\$302	\$30,630,013	\$252	Design/Bid/Build	18-Aug-11	13-Dec-13		85%	1.08%	Site grading work is underway. Sidewalks and site retaining wall work have commenced. Final connections and finishes for Elevator No. 1 and No. 2 continue.	\$23,483,860	
Monomoy Regional High School	9-12	Fontaine Brothers	\$49,374,000	700	Bid	168,000	\$294	\$41,433,695	\$247	Design/Bid/Build	11-Feb-13	30-Jun-14		16%	0.00%	Remaining foundation, footing and pier installations for the building are nearing completion. Steel installations are nearing completion. Underground utility work continues in zones C and A. Track and field work is ongoing.	\$29,696,270	
Nashoba Pompositticut ES	K-5	P.J. Stella Construction/Brait Builders	\$23,640,900	600	Bid	98,030	\$241	\$18,427,425	\$188	Design/Bid/Build	15-Jun-10	31-Aug-12		100%	4.35%	Punch list work ongoing.	\$15,239,622	
Natick Natick HS	9-12	Brait Builders Corp.	\$63,303,452	1,300	Bid	254,225	\$249	\$53,213,182	\$209	Design/Bid/Build	13-Sep-10	15-Jun-12		99%	3.28%	Warranty work addressing exterior panels to be completed in July.	\$38,209,033	
Newburyport Bresnahan ES	PK-3	CTA Construction, Inc.	\$28,190,000	660	Bid	112,517	\$251	\$21,734,937	\$193	Design/Bid/Build	14-Mar-13	30-Jun-14		22%	0.00%	Phase I demo complete. Foundations are 95% complete. Underground utilities are 50% complete and grading is 80% complete.	\$15,757,413	
Norfolk County Agricultural HS	9-12	TLT Construction Corp.	\$21,508,952	550	Bid	114,816	\$187	\$15,546,739	\$135	Design/Bid/Build	27-Mar-12	9-May-14		68%	1.35%	Animal Science Building: Finishes and MEP finish work continue. Agricultural Mechanical Building: Finishes and MEP finish work continue. Equine Center: Framing and roof sheathing substantially complete. Slab on grade in the stable portion is complete. Phase 3 site work has begun for new entrance from Route 1A.	\$14,119,915	
Norfolk Freeman-Kennedy ES	3-6	Fontaine Brothers	\$25,354,966	585	Bid	96,410	\$263	\$20,023,001	\$208	Design/Bid/Build	9-Nov-10	13-Aug-12		96%	6.00%	New building is complete and currently in use. Final punch list items are ongoing. Final paving, seeding, as well as miscellaneous landscaping to be completed in the Summer of 2013.	\$15,861,760	
Old Colony: Old Colony Regional Vocational Tech. HS	9-12		\$2,179,947	586	PFA	106,000	\$21	\$1,396,806	\$13	Design/Bid/Build	26-Jun-13	16-Oct-13		<1%	0.00%	GC mobilized on June 26, 2013.		
Oxford Oxford MS	5-8	S.O.M./J.J. Cardosi	\$5,085,217	652	Bid	117,000	\$43	\$5,085,217	\$43	Design/Bid/Build	1-Jun-12	29-Aug-14		25%	5.16%	Roof replacement complete. Window project scheduled for Summer 2013. HVAC, ADA, and floor replacement work scheduled for Summer 2014.	\$3,483,589	
Plymouth Plymouth HS	9-12	J&J Contractors	\$67,687,000	1,350	Bid	267,497	\$253	\$51,579,703	\$193	Design/Bid/Build	3-May-10	22-Jun-12	30 days	99%	5.49%	Installation of ballfield lights scheduled to be installed by the end of the Summer of 2013.	\$41,810,972	
Quincy Central MS	6-8	H.V. Collins Co. Inc	\$32,540,712	620	Bid	114,975	\$283	\$27,057,118	\$235	Design/Bid/Build	24-May-12	5-Sep-13		35%	0.49%	Foundations and structural steel complete. Metal studs, drywall and MEP rough-ins complete. Interior finishes are underway. Exterior densglas, CMU and site utilities continue. Roofing is 95% complete.	\$32,780,403	
Somerset Berkley Somerset Berkley RHS	9-12	Bacon-Agostini	\$69,407,000	1,000	Bid	222,826	\$311	\$52,042,575	\$234	Design/Bid/Build	3-Jul-12	15-Aug-14		33%	0.39%	Work on the track and field facilities continues which are required for completion in August 2013. Wall construction, interior masonry and exterior masonry in the courtyard continues. Rough-in of mechanical, electrical, and fire protection systems continues on the second and third floors of the new school. Work also progressed on the concession stand and maintenance building.	\$49,050,210	
Sturbridge Burgess ES	K-6	Fontaine Brothers	\$22,946,000	860	Bid	131,630	\$174	\$17,591,000	\$134	Design/Bid/Build	10-Aug-10	1-Oct-12		99%	7.42%	Both the new addition and the adjacent building renovations are substantially complete and the areas are in service. Abatement and demolition of the existing school have been completed. Remaining work includes ball fields and final landscaping which are scheduled for completion in the Fall of 2013.	\$16,616,077	
Sutton MS/HS	6-12	TLT Construction Corp.	\$41,230,800	840	Bid	179,040	\$230	\$32,998,403	\$184	Design/Bid/Build	1-Jul-11	31-Dec-14	60 days	68%	1.65%	Site work continues at the covered canopy between buildings. Finish paving in the courtyard has begun. Interior finish work continues at the Cafeteria and Media Center. Rough framing is ongoing at the Auditorium.	\$27,837,016	
Tewksbury Tewksbury HS	9-12	CTA/Methuen Construction Co.	\$51,600,000	1,100	Bid	218,781	\$236	\$40,159,651	\$184	Design/Bid/Build	15-Oct-10	3-Aug-12		98%	4.54%	Site work to be completed by the end of the Summer of 2013.	\$36,622,570	
Webster Park Ave Elem School	PK-4	CTA	\$35,840,565	720	PFA	109,067	\$329	\$24,180,000	\$222	Design/Bid/Build	2-Jul-13	1-Dec-14		0%	0.00%	The contractor is mobilizing. Modular classrooms are being set up.	\$30,880,737	

**Projects in Construction  
MSBA Grant Basis and Maximum Grant Amount  
Data Reported as of July 10, 2013**

Project	Grade	Contractor	Total Construction Cost*	Projected Enroll	PFA or Bid Data	Proposed Square Footage	Construction Cost per Square Foot	Building Cost	Building Cost per Square Foot	Project Type	Construction Start	Estimated Substantial Completion Date	Reporting Variance from Schedule	Physical Progress (%)	Change Orders (%)	Construction Status	Approximate Maximum Grant Amount *
Westfield Abner Gibbs ES	9-12	Fontaine Brothers	\$25,178,000	600	Bid	95,573	\$263	\$21,444,000	\$224	Design/Bid/Build	24-Aug-12	25-Mar-14		6%	0.00%	Work stoppage regarding Article 97 "Protected Land". The City still does not have approval. General Contractor has demobilized from the site.	\$21,762,201
West Springfield West Springfield HS	9-12	Fontaine Brothers	\$85,006,020	1,270	Bid	257,525	\$330	\$56,875,181	\$221	Design/Bid/Build	14-Dec-11	31-Dec-13		74%	0.34%	Exterior framing for the gym and pool continues. Interior painting and ceiling grid installations are underway in Bldg A & B. Millwork has begun in Bldg. A & B.	\$68,808,290
Weston Field ES	4-5	Colantonio	\$24,537,966	355	PFA	65,390	\$375	\$19,872,289	\$304	Design/Bid/Build	21-Dec-12	15-May-14		17%	0.48%	Foundation and underground piping nearing completion. Completing steel erection with steel decking to follow.	\$8,610,302
Williamsburg Anne T. Dunphy ES	PK-6	Enfield	\$8,990,457	170	PFA	37,100	\$242	\$7,625,327	\$206	Design/Bid/Build	5-Apr-13	7-Apr-14		13%	0.79%	Abatement is complete with demolition ongoing.	\$7,485,572
Winchester Vinson-Owen ES	K-5	CTA	\$21,290,000	420	Bid	74,774	\$285	17,767,598	\$238	Design/Bid/Build	17-Feb-12	21-Jun-13		98%	1.98%	Site work and interior finishes are approximately 90% complete. Elevator and kitchen equipment installation are 99% complete. Final cleaning and commissioning are underway. Curtain wall and exterior wall panels are 95% complete.	\$10,252,465
Adams-Cheshire Hoosac Valley MSHS	6-12	Gilbane	\$33,474,193	805	Bid	174,758	\$192	24,009,952	\$137	CM-R	17-May-11	31-Jul-12		100%	2.46%	Project is complete and close out is in progress	\$28,243,131
Andover Bancroft ES	K-5	Skanska	\$34,527,063	680	PFA	67,600	\$511	21,966,698	\$325	CM-R	14-May-12	27-Oct-14		35%	0.00%	Exterior wall envelope has begun and is on schedule to be enclosed by the Fall. MEP above ceiling work underway. Site work continues.	\$16,773,753
Ashburnham Westminster, Briggs ES	PK-5	Consigli	\$24,780,000	520	Bid	87,085	\$285	18,202,478	\$209	CM-R	9-Mar-12	31-Dec-13		84%	0.47%	The new school building exterior is substantially complete. Punch list work in the new building is in process. Abatement and demo of the adjacent existing school is in process.	\$16,353,447
Burlington Marshall Simonds MS	6-8	CTA	\$24,612,440	880	Bid	151,000	\$163	\$18,988,987	\$126	CM-R	15-Apr-11	17-May-13		100%	10.36%	Project is complete and closeout is in progress.	\$16,933,103
Concord-Carlisle HS	9-12	Turner Construction	\$71,365,015	1,225	PFA	219,871	\$325	\$61,213,812	\$278	CM-R	20-Feb-13	6-Mar-15		13%	0.00%	The CM-R has mobilized. Demo, abatement, site, electric, concrete and steel are all underway.	\$28,587,347
Dedham Avery ES	K-5	Consigli	\$18,174,209	310	Bid	62,723	\$290	\$13,528,098	\$216	CM-R	15-Oct-10	1-Jan-12		100%	6.70%	The new school building is complete and is in service. Project closeout is in process.	\$10,778,452
Duxbury HS	6-12	Dimeo	\$105,369,106	1,735	Bid	322,105	\$327	\$72,739,123	\$226	CM-R	9-Jul-12	3-Jul-14		39%	0.16%	Foundations, steel erection and elevated slabs complete. Brick veneer, roofing, spray fireproofing, metal frame and overhead MEP rough-ins are all underway. Curtain walls are being installed. Under slab plumbing almost complete. Slab-on-grade prep has begun. CMU almost complete for 1st and 2nd floors. Field House: roofing and CMU complete. Rough overhead MEP nearly complete. Interior finishes and underground utilities are ongoing.	\$51,406,497
Essex Technical High School	9-12	Gilbane	\$110,217,451	1,440	Bid	337,000	\$327	\$79,334,889	\$235	CM-R	7-May-12	30-Jun-14		38%	0.24%	Site work, exterior masonry, MEP rough-ins, and roof and window installations continue. Framing and drywall installations are ongoing throughout academy buildings. Work on pre-engineered buildings continues. Doors, frames and windows complete at Animal Science Bldg.	\$77,500,000
Grafton Memorial Sr HS	9-12	Dimeo	\$54,881,977	900	Bid	186,000	\$295	\$41,783,110	\$225	CM-R	18-Aug-10	10-Jul-12		100%	6.05%	The new building is complete and currently in use. Minor punch list items remaining. Commissioning is ongoing.	\$36,108,679
Greenfield	8-12	Shawmut Design	\$52,487,924	585	PFA	149,823	\$350	\$34,742,646	\$232	CM-R	1-May-13	15-Aug-15		1%	0.00%	The CM-R has mobilized to perform early site enabling work.	\$44,525,802
Leominster Leominster SHS	9-12	S.O.M.	\$33,794,797	1,825	Bid	295,859	\$114	\$25,382,707	\$86	CM-R	1-Jul-11	30-Aug-13		94%	5.76%	Renovations are nearing completion in the 6th of the 7 phases of the project. Demobilization of the modular classrooms is underway.	\$30,693,543
Lexington Estabrook ES	K-5	Shawmut Design	\$32,792,348	540	PFA	91,840	\$357	\$22,795,606	\$248	CM-R	20-Jun-12	21-Feb-14		40%	0.04%	Slab on deck placements continue. Exterior framing, sheathing, air vapor barrier installations and MEP rough-ins are ongoing. Installation of masonry insulation continues.	\$13,132,418
Longmeadow Longmeadow HS	9-12	Gilbane	\$63,685,998	1,000	Bid	236,985	\$269	\$46,573,364	\$197	CM-R	Nov-10	1-Nov-13		90%	1.53%	Renovation work continues in the Central Administration offices and other District spaces. Site work is ongoing.	\$33,067,140
Medway MS	5-8	Consigli	\$18,211,824	800	Bid	223,780	\$81	\$12,885,464	\$58	CM-R	Oct-11	21-Dec-12	60 days ahead	100%	3.57%	Project is complete and closeout is in process.	\$10,352,981
Methuen Methuen HS	9-12	Terminated Dimeo 12/31/2011. Consigli as of 5/21/2012	\$74,749,773	2,075	Bid	368,017	\$203	\$58,040,746	\$158	CM-R	21-Jul-11	Aug-14	30 days	57%	0.88%	Finishes continue in the existing academic wing that is currently being renovated and scheduled for turnover the end of July. The Phase I addition work which is also slated to turnover the end of July is falling behind due to the cafeteria and auditorium being behind schedule. PH II demolition has begun in the existing HS classrooms.	\$64,503,232
Newburyport Nock MS / Molin ES	Nock MS 6-8 Molin ES 4-5	Gilbane	\$20,942,293	845	PFA	161,500	\$130	\$14,924,391	\$92	CM-R	18-Mar-13	21-Aug-14		17%	0.00%	Phase IA and IB work are underway on a full time schedule now that school is out of session. Work includes selective demolition, installation of new data and power work, new sprinkler installation, installation of new masonry door openings and metal door frames, and painting.	\$13,697,934
North Reading Middle/Senior High School	6-12	Gilbane	\$86,315,287	1,370	PFA	267,939	\$322	\$56,361,445	\$210	CM-R	02-Jul-12	21-Aug-14 (HS) 21-Aug-15 (MS)		20%	0.00%	Steel erection is complete in the High School wing, auditorium, and cafeteria. Slabs on deck have been placed on the 2nd and 3rd floors, and throughout the elevated walkway. Underground utilities have progressed for slab on grade construction. Exterior building framing is underway. Site utility installations are also underway and on schedule.	\$49,323,123
Norton Norton HS	9-12	WT Rich	\$27,023,541	700	Bid	130,755	\$207	\$20,590,559	\$157	CM-R	12-Mar-12	31-Dec-13		65%	2.69%	Work continues on Phase 3. Exterior insulation and finishes are underway at exterior masonry walls. Drywall work is ongoing at locker rooms.	\$21,484,408
Rockland John Rogers MS/ HS	5-12	Agostini	\$66,362,037	1,525	Bid	275,700	\$241	\$47,724,091	\$173	CM-R	15-Jan-10	8/31/12 for MS May 2013 for HS		97%	5.59%	Misc. site work and punch list work underway.	\$52,837,940
Saugus Belmonte Middle School	6-8	Consigli	\$15,625,749	709	Bid	160,000	\$98	\$12,017,522	\$75	CM-R	23-May-12	3-Sep-13		63%	3.00%	This is a 4-phase project which is 75% complete. Phase 1, 2 and 3 are complete. Phase 1 and 2 punch list items are 99% complete. Phase 3 punch list items are 80% complete. Phase 4 work is ongoing and will be done during the summer months.	\$10,097,544
Shrewsbury Sherwood MS	5-6	Gilbane	\$33,986,286	900	Bid	129,378	\$263	\$22,823,030	\$176	CM-R	7-Mar-11	31-Oct-13		97%	2.12%	The new school building is in service. Punch list and commissioning items are being completed. Abatement and demolition of the adjacent existing school has been completed. Final site work to be completed by the Fall of 2013 including the balance of the access road and parking lot, ball field construction, and final grading & landscaping utilizing stockpiled soils and plantings.	\$22,369,828
Somerville E. Somerville Community School	K-8	Gilbane	\$32,590,244	500	Bid	121,100	\$269	\$24,613,842	\$203	CM-R	7-Nov-11	29-Mar-13		97%	0.32%	Classroom wings are ready for FF&E which will arrive in July/August. Landscaping to be completed as soon as the playground equipment arrives. Commissioning is underway. Project has received a TCO to occupy the building and anticipate a C of O once the playground equipment is installed.	\$15,237,996
Southbridge Southbridge MS/HS	6-12	Consigli	\$59,307,632	1,050	Bid	199,740	\$297	\$41,487,200	\$208	CM-R	30-Nov-10	31-Jul-12		99%	0.84%	Project is complete and closeout is in progress.	\$52,019,398
Southeastern Regional Voc Tech High School	9-12	WT Rich	\$27,200,000	1,370	Bid	308,250	\$88	\$19,996,609	\$65	CM-R	27-Jun-11	20-Jan-14		70%	2.28%	Phase 2 interior renovation work, the new Gymnasium addition, elevator, the new media center, classrooms, labs, and copy room created from renovation of the existing gym are complete and are in service. Demolition and renovation of the cafeteria is in process. Final site landscaping work and installation of a new roof on the existing school will be completed in Summer of 2013.	\$25,988,607
Springfield Dryden ES	PK-5	Morganti Aquadro & Cerruti	\$11,476,091	280	Bid	40,900	\$281	\$8,276,912	\$202	CM-R	28-Jun-12	1-Nov-13		51%	0.00%	Phase 2 construction is underway with selective demolition and most abatement complete. The Summer 2013 phase work in the gym, cafeteria, kitchen, administrative offices and lobby is underway with most selective demolition complete and infrastructure work has commenced. Phase 3 selective demolition and abatement is underway.	\$8,169,913
Stoneham Middle School	5-8	Shawmut Design	\$33,086,864	775	Bid	136,410	\$243	\$21,209,275	\$155	CM-R	3-Dec-12	25-Jul-14		7%	0.11%	The CM-R has mobilized and early site work is being performed.	\$22,386,455
Uxbridge High School	9-12	Shawmut Design	\$37,293,765	600	Bid	123,000	\$303	\$27,562,625	\$224	CM-R	28-Feb-11	20-Jun-12		99%	2.93%	Repairs are being performed to address a roof leak. Fields are being re-seeded in certain areas.	\$21,973,620
Wakefield	5-8	Bond Brothers	\$59,756,583	1,070	PFA	187,773	\$318	\$41,169,028	\$219	CM-R	18-Mar-13	15-May-15		2%	0.00%	Early site enabling work being performed.	\$34,689,576
Wilmington	9-12	Gilbane	\$64,408,261	960	PFA	192,443	\$335	\$46,525,282	\$242	CM-R	April 30-13	13-Feb-15		6%	0.00%	Abatement and demolition of Gym completed. Building foundation and site utility work has begun. Site preparation is underway at field & track, as well as perimeter field draining installation is underway at football field.	\$37,993,245
** Excludes Field House																	
<b>Wait List Program Totals</b>			<b>\$120,784,964</b>	<b>2,060</b>		<b>463,690</b>											<b>\$141,213,334</b>
Springfield Forest Park MS	6-8	Consigli	\$34,745,898	660	Bid	148,800	\$234	\$26,209,932	\$176	CM-R	26-Mar-12	1-Aug-13		80%	0.00%	Final painting is underway. Wood and terrazzo floor installations are ongoing. MEP start up, site work and asphalt installation are in progress.	\$38,340,497
Springfield Putnam Voc Tech HS	9-12	Consigli	\$86,039,066	1,400	Bid	314,890	\$273	\$62,949,742	\$200	CM-R	18-May-10	20-Jul-12	60 days ahead	99%	-0.15%	Parking lots completed. Only punch list work remaining.	\$102,872,837
Worcester North HS	9-12	Gilbane	\$49,145,638	1,200	Bid	239,570	\$205	\$40,860,983	\$171	CM-R	24-Sep-08	Jun-11		99%	3.20%	Phase 4, which includes paving the remaining parking lot and play surfaces, is scheduled to be completed by the end of August.	\$45,911,881
