


Project Overview Report

March 5, 2014

A total of 328 projects that have received invitations from the Board of Directors (“Board”) to collaborate with the MSBA are currently in the MSBA’s Eligibility Period and Capital Pipeline. The following summary chart provides the number of projects in the Eligibility Period and each phase of the Capital Pipeline:

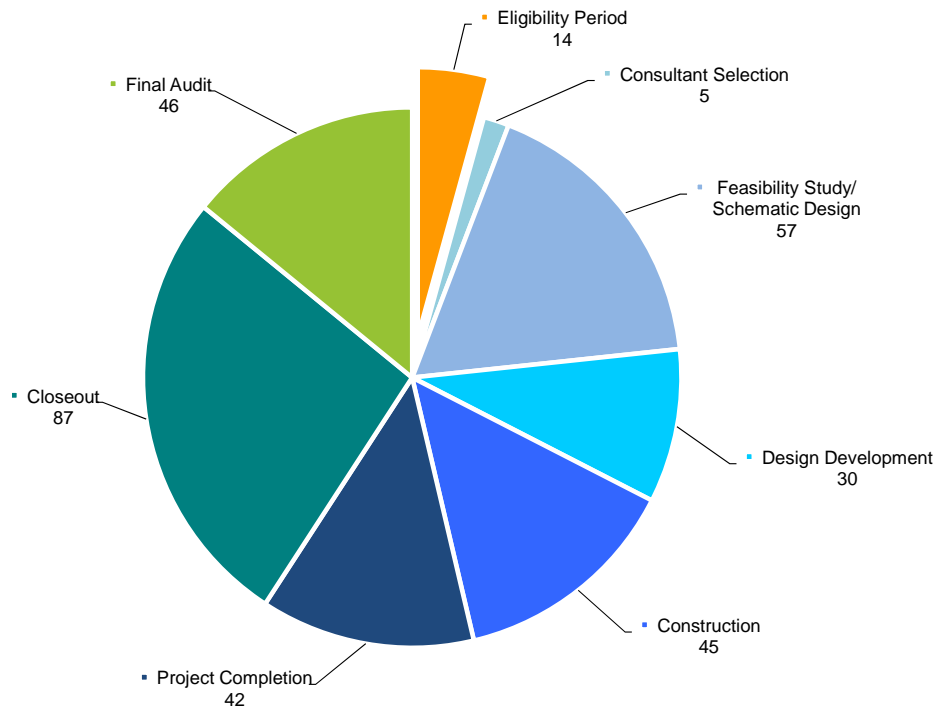

Statement of Interest (“SOI”)

2014 SOI Process

The Fiscal Year 2014 SOI filing period opened on **January 10, 2014**. The deadline to file SOIs for consideration in the Accelerated Repair Program (“ARP”) was Friday, February 14, 2014. Submission of SOIs for consideration in the 2014 ARP is now closed.

The SOI closing date for districts submitting for consideration in the Core Program, which is primarily for projects beyond the scope of Accelerated Repair, including extensive repairs, renovations, addition/renovations, and new school construction, is **April 11, 2014**.

As of the February 14th deadline the MSBA received 117 ARP SOIs, submitted by 59 Districts. ARP review for proper submission, and content is underway. Invitations into ARP are anticipated for the June Board of Directors meeting.

Eligibility Period

There are 14 districts in the Eligibility Period. Four of the 14 districts have already secured funding. The remaining 10 districts have yet to confirm their date for action.

An agreed-upon enrollment is a key prerequisite for the MSBA to commence a Feasibility Study with a district. To begin the enrollment projection process, a district must file enrollment information utilizing the MSBA's online enrollment projection tool. Since the last report, one district has completed the enrollment process.

Based upon the schedules anticipated by the districts for completion of the Eligibility Period requirements, staff anticipate recommending the 14 districts in Eligibility Period for an Invitation to Feasibility Study at upcoming Board meetings.

Capital Pipeline

Consultant Selection

After the district has completed all Eligibility Period requirements and has received a Board Invitation to Feasibility Study, the district procures an Owner's Project Manager ("OPM"). There are four districts in the Capital Pipeline that need to procure an OPM.

After a district has selected and executed a contract with an OPM, it selects a Designer utilizing either a local designer selection process for projects under \$5 million or the MSBA's Designer Selection Panel ("DSP") for projects over \$5 million. There is one district in the Capital Pipeline that is in the process of procuring a Designer.

Feasibility Study

Once a district has procured an OPM and Designer and a Feasibility Study Agreement has been executed, the district and its consultants must complete two Feasibility Study submittals, the Preliminary Design Program and the Preferred Schematic Report, prior to Board consideration to proceed into Schematic Design. Based on the most recent data and schedules provided to the MSBA by districts, the MSBA anticipates that five districts will present their preferred schematic designs to the Board at the upcoming June and July Board meetings.

Prior to consideration by the Board for Project Scope and Budget authorization, a district must submit a schematic design to the MSBA for review. Based on the most recent data and schedules provided to the MSBA by districts, the MSBA anticipates that four districts will appear before the Board for Project Scope and Budget Agreement authorization at the upcoming June and July Board meetings.

Commissioning

Since the last report, the MSBA has assigned Commissioning Consultants to an additional 23 projects presented in the table below. To date, the MSBA has executed 267 Commissioning Consultant contracts, totaling \$20.0 million; 91 contracts have been completed.

District	School	Estimated Const. Cost (million)	Commissioning Consultant	Contract Amount
Ashland	2013 ARP Roofs	\$5.25	Gale Associates	\$52,940
Barnstable	2013 ARP Roof	\$0.94	CBI Consulting	\$27,500
Blackstone-Millville	2013 ARP Millville ES Roofs	\$1.27	Simpson Gumpertz & Heger	\$26,000
Central Berkshire	Berkshire Trail ES 2013 ARP Roof	\$0.68	Building Enclosure Associates	\$23,500
Dighton-Rehoboth	2013 ARP Roofing - 4 schools	\$11.34	Gale Associates	\$118,400
Easton	2013 ARP Moreau Hall Roof	\$0.69	Gale Associates	\$22,500
Greater Lawrence RVT	Greater Lawrence Reg Voc Tech Repairs	\$4.40	WSP	\$16,500
Hamilton-Wenham	2013 ARP Boilers - 2 schools	\$1.35	Strategic Building Solutions	\$18,346
Hamilton-Wenham	ARP Winthrop ES Windows	\$1.05	CBI Consulting	\$24,000
Hatfield	Smith Academy 2013 ARP Roof Window	\$1.80	Building Enclosure Associates	\$28,000
Hopedale	2013 ARP Memorial ES Roof	\$0.41	Simpson Gumpertz & Heger	\$22,500
Medford	Medford HS ARP Boilers	\$1.89	Symmes, Maini & McKee Associates	\$18,600
Nashoba Valley Tech	Nashoba Valley THS 2013 ARP Roof	\$2.08	CBI Consulting	\$20,000
Nauset	Nauset Reg MS 2013 ARP Roofs	\$2.08	Russo Barr Associates	\$32,965
Pathfinder Voc Tech	Pathfinder Voc Tech 2013 ARP	\$2.83	Building Enclosure Associates	\$29,000
Pentucket	Pentucket RMS 2013 APR Boilers	\$0.84	Strategic Building Solutions	\$9,931
Quincy	2013 ARP Windows	\$4.36	Simpson Gumpertz & Heger	\$90,000
Randolph	2013 ARP Community MS Boilers	\$0.38	Consulting Engineering Services	\$17,450
So Middlesex Voc Tech Reg	South Middlesex 2013 ARP	\$5.13	Russo Barr Associates	\$34,965
Stoughton	2013 ARP	\$3.01	Building Enclosure Associates	\$73,000
Wellfleet	Wellfleet ES 2013 ARP Roof	\$0.34	Russo Barr Associates	\$22,450
Westhampton	Westhampton ES 2013 ARP Roofs Windows	\$0.82	Building Enclosure Associates	\$29,000
Worcester	2013 ARP Worcester East MS boilers	\$2.18	RDK Engineers	\$10,520
Total		\$55.11 M	Total	\$768,067

The table below represents the status of commissioning assignments sorted by the fiscal year in which the commissioning work orders were issued.

Fiscal Year	No. Work Orders Issued	Value of Work Orders Issued	Total Invoiced	Percent Complete
FY10	31	\$4,231,376	\$4,179,663.87	98.78%
FY11	95	\$6,328,287	\$5,219,543.50	82.48%
FY12	52	\$4,459,061	\$2,611,370.41	58.56%
FY13	55	\$3,386,847	\$1,184,413.57	34.97%
FY14	34	\$1,821,717	\$34,680.91	1.90%

Design Development

Once a district has secured local funding and has entered into a Project Funding Agreement with the MSBA, it enters the Design Development phase. Currently, there are 30 projects in the Design Development phase with a total estimated construction cost of approximately \$602.06 million: 17 Accelerated Repair projects and 13 Core Program projects. The 13 Core Program projects in Design Development have a total estimated construction cost of approximately \$578.3 million:

Elementary School Districts

Athol-Royalston
Gloucester
Newton
South Hadley

Middle School Districts

Chicopee
Lynn
North Adams
Peabody
Wachusett Regional

High School Districts

Greater Lawrence Regional Voc/Tech
Lunenburg
Winchester
Winthrop

Construction

When a district issues a Notice to Proceed, the project is advanced to the Construction phase. Currently, there are 45 projects in the Construction phase with a total estimated construction cost of \$1.802 billion: six Accelerated Repair projects, two Science Lab Initiative projects, and 37 Core Program projects. The 37 Core Program projects have a total estimated construction cost of \$1.763 billion and are listed below. This does not include the 42 projects that have reached substantial completion and are currently in the Project Completion phase.

Elementary School Districts

Andover
Georgetown
Newburyport (Bresnahan)
Revere
Springfield (Brookings)
Webster
Westfield
Weston
Williamsburg

Middle and Middle/High School Districts

Auburn
Douglas
Greenfield
Hingham
Newburyport (Nock)
Oxford
Stoneham
Sutton
Wakefield

High School Districts

Addition/Renovation
Assabet Valley Regional Technical
Ayer Shirley Regional
Dracut
Greater Lowell Regional Voc/Tech
Greater New Bedford Voc/Tech
Methuen
Norfolk County Agricultural
North Reading
Southern Worcester Regional Voc/Tech
Southwick-Tolland-Granville Regional
New
Concord-Carlisle Regional
Essex/North Shore Regional Voc/Tech
West Bridgewater
Wilmington
Model
Duxbury
Franklin
Marshfield
Monomoy Regional
Somerset-Berkley Regional

Summary of Bid Data

These numbers are based on preliminary information received from the District and are subject to further review and calculation.

Year	Number of Projects	Design Basis for Enrollment	Project Budget	Construction Budget
2014	13	10,815	\$632.0 M	\$493.0 M
2015	1	970	\$80.2 M	\$62.0 M
Grand Total	14	11,785	\$712.2 M	\$555.0 M

Core Program – Total Project Budget Update


Upon receiving the Board’s approval of the Project Scope and Budget, the MSBA and participating districts enter into a Project Funding Agreement that establishes the Total Project Budget and the Estimated Maximum Total Facilities Grant for an approved project. Of the grants authorized by the Board, nine projects have increased their Total Project Budgets due to acceptance of construction bids higher than the project estimates, and one project has increased its Total Project Budget due to an increase in its site acquisition cost budget. In no event has the increase in budget resulted in an increase to the Estimated Maximum Total Facilities Grant as authorized by the Board. Please note that staff reported on these budget increases for the seven projects shaded below at previous Board meetings.

District	School Name	Scope	Project Funding Agreement		PFA Bid Amendment		Reason for Increase to Total Project Budget
			Total Project Budget	Total Maximum Facilities Grant	Total Project Budget	Total Maximum Facilities Grant	
Core Program							
Andover	Bancroft Elementary School	New	\$44,659,837	\$16,773,753	\$50,374,837	TBD*	The District has appropriated additional funds to cover the costs associated with increased construction costs and additional contingencies for litigation/settlement costs and other ineligible costs.
Essex North Shore Agricultural & Technical School	Essex North Shore Agricultural & Technical School District	New	\$125,000,000	\$77,500,000	\$133,770,000	\$77,500,000	The Board was informed at the March 30, 2011 meeting that the Total Project Budget had increased due to additional ineligible scope that would be funded by DCAM.
Essex North Shore Agricultural & Technical School	Essex North Shore Agricultural & Technical School	New	\$125,000,000	\$77,500,000	\$134,501,368	\$77,500,000	The District has appropriated additional funds to cover the costs associated with increased construction costs for horse tack barn renovations.
Lexington	Estabrook Elementary School	New	\$40,792,248	\$12,250,739	\$42,554,862	TBD*	The District has executed a GMP that exceeds the Construction Budget of the PFA. The District is currently reviewing its project budget to determine the use of the additional appropriation funds it appropriated in excess of the Total Project Budget.
North Reading	North Reading Middle /High School	Add/Reno	\$107,727,074	\$49,323,123	\$123,227,074	\$49,323,123	This is a CMR project. The estimated, reconciled construction costs tracked over budget at DD (\$9,746,655 over), 60% (\$4,655,965 over), and 90% (\$15,136,846 over). A Town override vote in March 2013 obtained an additional \$15,500,000 in local funding to proceed.
Revere	Staff Sergeant James J. Hill Elementary School (currently the McKinley ES)	New	\$45,402,396	\$29,551,048	TBD*	\$29,551,048	At Project Scope and Budget, the Total Project Budget was approved at \$44,382,396. The City of Revere has increased the land acquisition budget. Therefore, the projected total project budget at PFA has increased to \$45,402,396. Note that the MSBA grant has not changed since the Project Scope and Budget Agreement.
Somerville	East Somerville Community School	Add/Reno	\$33,185,258	\$15,237,996	\$38,006,621	\$15,237,996	At the March 28, 2012 Board Meeting, the Board approved an amendment to the PFA and a \$6.25M District loan.
Uxbridge	Uxbridge High School	New	\$43,000,000	\$22,362,328	\$44,986,479	\$22,362,328	The District has appropriated additional funds to cover the costs associated with the construction of athletic fields originally included in the PFA but which were not included in the bid as the District's construction contract would have exceeded the budget.

*PFA Bid Amendment has not been developed to calculate a revised total facilities grant amount. The Total Maximum Facilities Grant will not exceed the Board authorized amount in the PFA but upon review may decrease.

Status of Green Repair Program

Since the January report, five additional projects have had a Final Audit Approved, no projects remain in construction.

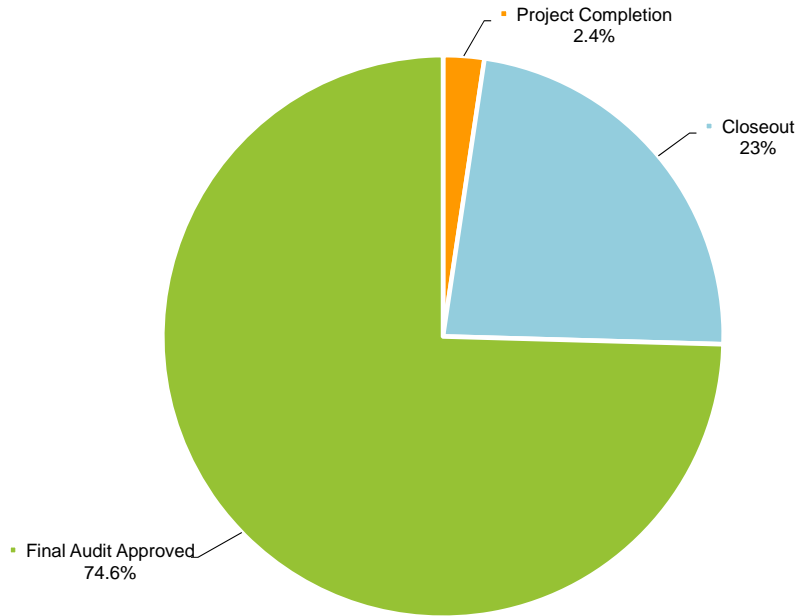


169 projects participating in the Green Repair Program have received authorization to enter into a PFA, totaling \$366,647,226 in Total Project Costs and \$222,885,258 in MSBA grants.

Status of Accelerated Repair Program

Currently there are a total of 45 districts, representing 83 projects, in the Accelerated Repair Program.


2012 Accelerated Repair Program

All 24 districts, representing 36 projects, approved in 2012 are under contract with consultants and have been authorized to enter into a PFA, totaling \$63,009,653 in Total Project Costs and a maximum of \$38,267,952 in MSBA Total Facilities Grant funding. Of the 36 projects, 27 are scheduled to complete construction in 2013, and nine are scheduled to complete construction in 2014. The chart below represents the progress of the 36 projects approved in 2012.

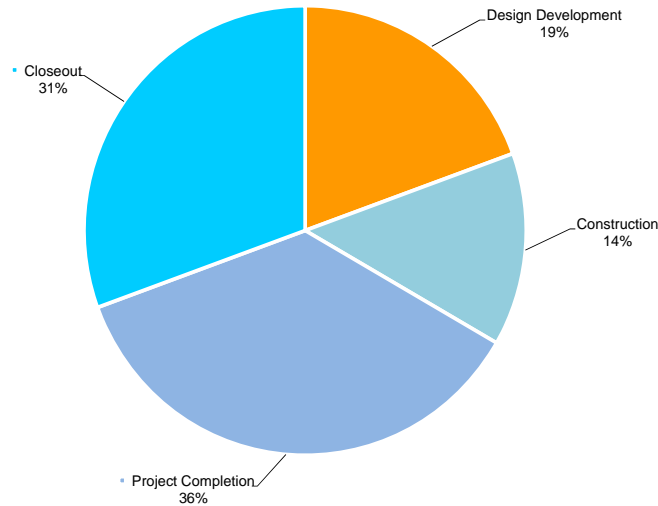

2013 Accelerated Repair Program

The 2013 Accelerated Repair Program has 47 projects represented by 26 districts. At the November and January Board Meetings, 38 projects representing 21 districts were approved for Project Funding Agreements. Of the total 47 projects, an additional eight projects representing six districts are seeking approval for Project Funding Agreements at the March Board Meeting. With the Board's authorization at the March Board Meeting, the 2013 Accelerated Repair Program will have \$99,801,495 in Total Project Costs and a maximum of \$57,759,742 in MSBA Total Facilities Grant funding.

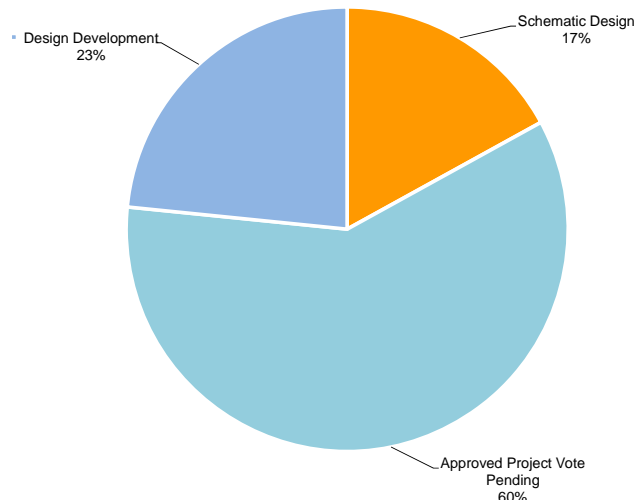

2012 Accelerated Repair Projects – Construction Estimate vs. 2013 Bid Amount

- Out of 36 projects, 32 bids were received in 2013.
- Of the 32, 30 bids have been reported.
- Of the 30 projects, 25 bids came within the estimated budget.

District	School	Scope	Project Type	Bid Date	Construction Estimate **	Bid Amount **	Variance from Construction Estimate	Reimbursement Rate	Potential Grant Variance *
				Total	\$41,438,114	\$32,257,385	\$9,180,729	-	\$6,108,260
Weymouth	William Seach PS	Boiler	DBB	Dec-12	\$425,213	\$459,104	-\$33,891	54.16%	\$0
Groton-Dunstable RSD	Gronton-Dunstable MS	Roof	DBB	Feb-13	\$1,316,890	\$942,000	\$374,890	45.74%	\$171,475
Hamilton-Wenham	Cutler ES	Roof	DBB	Feb-13	\$547,326	\$444,150	\$103,176	43.42%	\$44,799
North Brookfield	North Brookfield ES	Windows	DBB	Feb-13	\$274,254	\$199,400	\$74,854	62.67%	\$46,911
Shawsheen Valley Voc/Tech.	Shawsheen Valley VTHS	Boiler	DBB	Mar-13	\$805,423	\$535,000	\$270,423	52.06%	\$140,782
Sudbury	Gen. John Nixon ES	Roof	DBB	Mar-13	\$621,554	\$542,775	\$78,779	36.89%	\$29,062
Easton	Easton Jr. HS	Roof	DBB	Mar-13	\$1,850,830	\$1,889,000	-\$38,170	50.16%	\$0
Norton	Solmonese ES	Roof	DBB	Mar-13	\$1,166,044	\$986,000	\$180,044	55.63%	\$100,158
Attleborough	Irvin Studley ES	Roof	DBB	Mar-13	\$773,363	\$489,000	\$284,363	57.74%	\$164,191
Lynn	Breed MS	Windows	DBB	Mar-13	\$1,796,674	\$2,167,300	-\$370,626	80.00%	\$0
Lynn	Lynn Voc. Tech	Roof	DBB	Mar-13	\$4,173,000	\$3,097,000	\$1,076,000	80.00%	\$860,800
Worcester	Chandler Magnet	Windows	DBB	Mar-13	\$3,723,463	\$3,142,320	\$581,143	80.00%	\$464,914
Worcester	Jacob Hiatt Magnet	Boiler	DBB	Mar-13	\$298,877	\$321,703	-\$22,826	80.00%	\$0
Worcester	James Caradonio Center	Windows & Boiler	DBB	Mar-13	\$1,021,820	\$1,007,132	\$14,688	80.00%	\$11,750
Worcester	Lake View	Windows	DBB	Mar-13	\$1,127,970	\$789,398	\$338,572	80.00%	\$270,858
Worcester	May Street	Windows	DBB	Mar-13	\$1,655,289	\$1,548,167	\$107,122	80.00%	\$85,698
Gardner	Gardner MS	Boiler	DBB	Apr-13	\$438,439	\$396,100	\$42,339	78.95%	\$33,427
North Attleborough	Roosevelt Ave. ES	Windows	DBB	Apr-13	\$768,000	\$656,483	\$111,517	52.06%	\$58,056
Quabaog RSD	Warren ES	Boiler	DBB	Apr-13	\$207,000	\$182,444	\$24,556	68.34%	\$16,782
Quabbin	Ruggles Lane ES	Roof & Windows	DBB	Apr-13	\$2,588,409	\$2,287,836	\$300,573	57.74%	\$173,551
Leominster	Fall Brook ES	Boiler	DBB	Apr-13	\$949,550	\$684,000	\$265,550	73.38%	\$194,861
Leominster	Southeast ES	Roof & Boiler	DBB	Apr-13	\$3,146,097	\$1,948,000	\$1,198,097	73.38%	\$879,164
Westfield	Munger Hill ES	Roof	DBB	Apr-13	\$1,170,735	\$593,499	\$577,236	59.84%	\$345,418
Westfield	Paper Mill ES	Roof	DBB	Apr-13	\$1,170,735	\$562,525	\$608,210	59.84%	\$363,953
Southampton	William Norris ES	Roof	DBB	May-13	\$1,504,147	\$922,000	\$582,147	55.00%	\$320,181
Taunton	Galligan School	Roof	DBB	May-13	\$543,570	\$486,600	\$56,970	73.95%	\$42,129
Wayland	Wayland MS	Roof	DBB	May-13	\$2,445,767	\$1,965,800	\$479,967	36.89%	\$177,060
Blackstone-Milville RSD	Maloney ES	Roof	DBB	Sep-13	\$1,405,656	\$702,000	\$703,656	57.74%	\$406,291
Blackstone-Milville RSD	J.F.Kennedy ES	Roof	DBB	Sep-13	\$2,315,707	\$1,093,000	\$1,222,707	57.74%	\$705,991
Wilmington	North IS	Windows	DBB	Nov-13	\$1,206,312	\$1,217,649	-\$11,337	49.94%	\$0

*These numbers are based on preliminary information received from the district and are subject to further review and calculation.

**The construction estimate and bid amount do not include pre-construction services and alternatives.

Accelerated Repair Projects – Schedule Extension Update

9 of the 36 2012 Accelerated Repair Projects have not met their anticipated construction completion dates. Schedule delays can be attributed to local funding issues, lead time for windows, and construction delays on site.

The MSBA granted each district a conditional extension to its Project Funding Agreement pending compliance with the following stipulations:

- The district needed to submit a detailed, revised construction timeline showing how the work will be completed at each school; and
- Any costs that may result from the district’s requested extension of the construction schedule will be the sole responsibility of the district and are categorically ineligible for reimbursement by the MSBA.


Each of these projects has a revised construction schedule and is scheduled to be complete by the beginning of the 2014-2015 school year. In no event has the extended schedule resulted in an increase to the Estimated Maximum Total Facilities Grant as authorized by the Board.

District	School	Scope	Original Construction Completion Date	Updated Construction Completion Date	Reason for Schedule Extension
Blackstone-Millville	Blackstone Millville RHS	Roof	26-Dec-13	1-Sep-14	The District fell behind schedule due to local funding issues.
Bridgewater-Raynham	Bridgewater MS	Roof	1-Sep-13	1-Sep-14	The District fell behind schedule as a result to local issues funding issues and incorporation of new OPM to project team.
Bridgewater-Raynham	Laliberte ES	Roof	1-Sep-13	1-Sep-14	The District fell behind schedule as a result to local issues funding issues and incorporation of new OPM to project team.
Bridgewater-Raynham	L.B. Merrill ES	Roof	1-Sep-13	1-Sep-14	The District fell behind schedule as a result to local issues funding issues and incorporation of new OPM to project team.
North Attleborough	Roosevelt Ave. ES	Windows	27-Sep-13	31-Mar-14	Construction fell behind schedule due to material delivery delays. Corrective work continues to ensure windows pass commissioning tests.
Taunton	Galligan School	Roof	13-Nov-13	31-Dec-13	District issued a Change Order for installation of tapered insulation and membrane overlay to prevent ponding around the chimney area.
Worcester	Lake View School	Windows/Doors	13-Sep-13	14-Feb-14	Construction fell behind schedule due to material delivery delays.
Worcester	May Street School	Windows/Doors	14-Sep-13	15-Mar-14	Construction fell behind schedule due to material delivery delays.
Worcester	New Citizens Center School	Windows/Doors & Boilers	13-Sep-14	14-Feb-13	Construction fell behind schedule due to material delivery delays. Boiler scope completed per baseline schedule.

2013-2014 Eligibility Period Status

March 5, 2014
14 Projects in Eligibility Period


Task Remaining
 Partial Task Completed
 Invite / Completion Date
 Completed Task



District	2013				2014												
	Sept	Oct	Nov	Dec	Jan	Feb	Mar	April	May	June	July	Aug	Sept	Oct	Nov	Dec	
Beverly Briscoe Middle School		10/2/13	10/16/13	11/15/13	12/16/13	1/14/14	Maintenance Docs / Enroll Certification (180 days)			Local Authorization		FSA (270 days)					
			ICC (30 days)	SBC (60 days)	Online Enrollment Projection Info												
Mount Greylock RSD Mount Greylock RHS			ICC (30 days)	SBC (60 days)	Online Enrollment Projection Info	Maintenance Docs / Enroll Certification (180 days)			Local Authorization / FSA (270 days)								
Amherst Wildwood Elementary School			11/20/13	12/4/13	1/3/14	2/3/14	3/4/14	Maintenance Docs / Enroll Certification (180 days)			Local Authorization / FSA (270 days)			9/1/2014			
				ICC (30 days)	SBC (60 days)	Online Enrollment Projection Info											
Braintree East Middle School				ICC (30 days)	SBC (60 days)	Online Enrollment Projection Info	Maintenance Docs / Enroll Certification (180 days)			Local Authorization / FSA (270 days)							
Hopkinton Center Elementary School				ICC (30 days)	SBC (60 days)	Online Enrollment Projection Info	Maintenance Docs / Enroll Certification (180 days)			Local Authorization		FSA (270 days)					
Needham Hillside Elementary School				ICC (30 days)	SBC (60 days)	Online Enrollment Projection Info	Maintenance Docs / Enroll Certification (180 days)			Local Authorization		FSA (270 days)					
Newton Cabot Elementary School				ICC (30 days)	SBC (60 days)	Online Enrollment Projection Info	Maintenance Docs		Enroll Certification (180 days)		Local Authorization		FSA (270 days)				
Billerica Billerica Memorial High School						1/29/14	2/12/2014	3/4/2014	4/3/2014	5/5/2014	8/1/2014			10/30/2014			
							ICC (30 days)	SBC (60 days)	Online Enrollment Projection Info / Ed Profile Questionnaire (90 days)	Maintenance Docs / Enroll Certification (180 days)			Local Authorization / FSA (270 days)				
Carver Carver Elementary School							ICC (30 days)	SBC (60 days)	Online Enrollment Projection Info / Ed Profile Questionnaire (90 days)	Maintenance Docs / Enroll Certification (180 days)			Local Authorization / FSA (270 days)				
Hanover Sylvester Elementary School							ICC (30 days)	SBC (60 days)	Online Enrollment Projection Info / Ed Profile Questionnaire (90 days)	Maintenance Docs / Enroll Certification (180 days)			Local Authorization / FSA (270 days)				
Provincetown Provincetown Schools							ICC (30 days)	SBC (60 days)	Online Enrollment Projection Info / Ed Profile Questionnaire (90 days)	Maintenance Docs / Enroll Certification (180 days)			Local Authorization / FSA (270 days)				
Quincy Reay E. Sterling Middle School							ICC (30 days)	SBC (60 days)	Online Enrollment Projection Info / Ed Profile Questionnaire (90 days)	Maintenance Docs / Enroll Certification (180 days)			Local Authorization / FSA (270 days)				
Somerville Somerville High School							ICC (30 days)	SBC (60 days)	Online Enrollment Projection Info / Ed Profile Questionnaire (90 days)	Maintenance Docs / Enroll Certification (180 days)			Local Authorization / FSA (270 days)				
Stoughton Stoughton High School							ICC (30 days)	SBC (60 days)	Online Enrollment Projection Info / Ed Profile Questionnaire (90 days)	Maintenance Docs / Enroll Certification (180 days)			Local Authorization / FSA (270 days)				
District	Sept	Oct	Nov	Dec	Jan	Feb	Mar	April	May	June	July	Aug	Sept	Oct	Nov	Dec	

Project Status | March 5, 2014

Core Program:	134
Waitlist:	5
Green Repair:	84
Accelerated Repair:	83
Science Lab Initiative:	8
Total Projects:	314

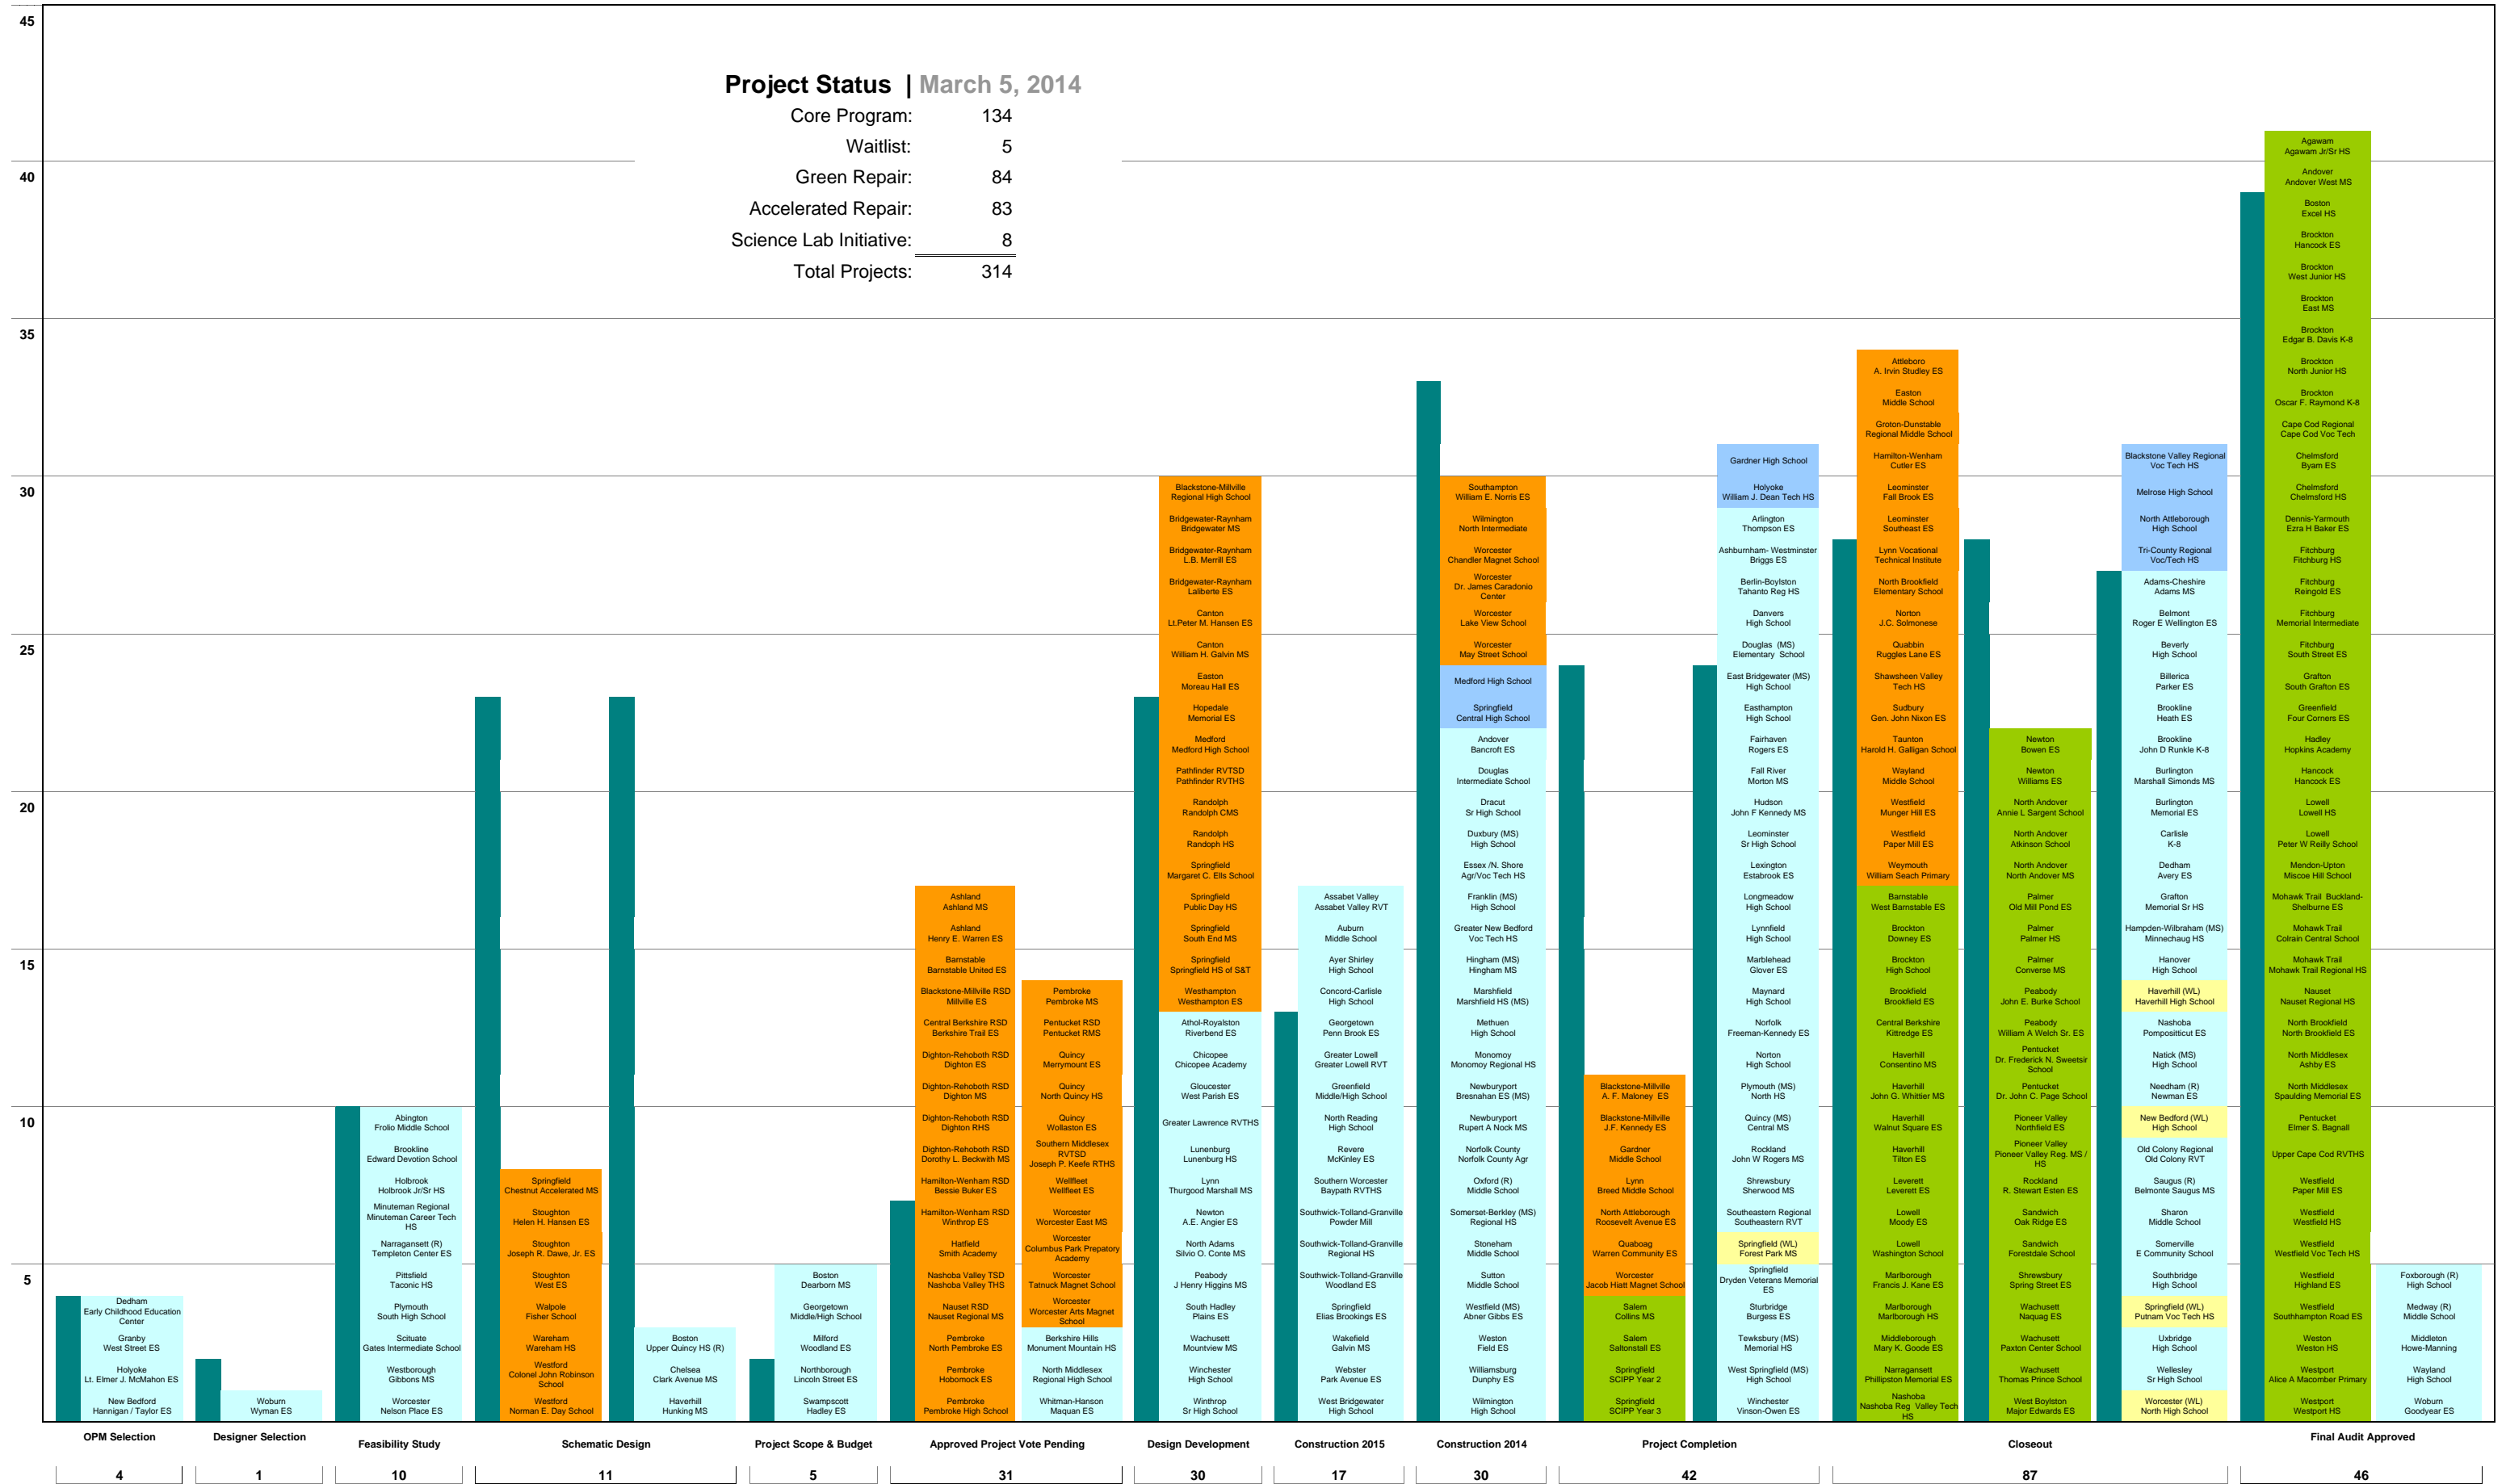

PROJECT STATUS 314 Total Active Projects

■ Green Repair Program
■ Accelerated Repair Program
■ Core Program Project
■ Science Lab Initiative Project
■ Waitlist Project
■ Capital Pipeline Status Presented at January 29, 2014 Board of Directors Meeting

Date of Report: 3/5/2014

Total Projects: 328

MSBA ID	District	School	Phase	Project Scope	Procurement Type	OPM	Designer	CM/GC	Commissioning Consultant
200800010405	Abington	Frolio Middle School	Feasibility Study			Knight, Bagge & Anderson Inc.	Ai3 Architects LLC	-	-
200806030505	Adams-Cheshire	Hoosac Valley High School	Closeout	Addition / Renovation	CM@R	URS Corporation	Tessier Associates, Inc.	Gilbane Building Company	Strategic Building Solutions, LLC
201100050405G	Agawam	Agawam Junior High	Final Audit Approved	Repair - Accelerated	DBB	Municipal Building Consultants, Inc.	CSS Architects Incorporated	Capeway Roofing Systems, Inc. Chandler Architectural Products, Inc.	Building Enclosure Associates, LLC
201300080050	Amherst	Wildwood Elementary	Eligibility Period			-	-	-	-
201100090310G	Andover	Andover West Middle	Final Audit Approved	Repair - Accelerated	DBB	Skanska USA Building, Inc	Russo Barr Associates, Inc.	Eagle Rivet Roof Services Corporation	Simpson Gumpertz & Heger Inc.
200800090003	Andover	Bancroft Elementary School	Construction	New Construction	CM@R	Dore & Whittier Management Partners, Inc.	Symmes Maini & McKee Associates, Inc.	Skanska USA Building, Inc.	Sebesta Blomberg & Associates, Inc.
200900100050	Arlington	Thompson Elementary School	Project Completion	New Construction	DBB	PMA Construction Services	HMFH Architects, Inc.	G & R Construction, Inc.	Consulting Engineering Services, LLC
200806100025	Ashburnham-Westminster	John R. Briggs Elementary School	Project Completion	New Construction	CM@R	STV Incorporated	Lamoureux Pagano & Associates, Inc.	Consigli Construction Company, Inc.	Foreman Building Commissioning, LP
201300140405	Ashland	Ashland Middle	Approved Project Vote Pending	Repair - Accelerated		Arcadis U.S., Inc.	Raymond Design Associates, Inc.	-	Gale Associates, Inc.
201300140010	Ashland	Henry E Warren Elem	Approved Project Vote Pending	Repair - Accelerated		Arcadis U.S., Inc.	Raymond Design Associates, Inc.	-	Gale Associates, Inc.
200908010605	Assabet Valley	Assabet Valley Regional Technical High School	Construction	Repair - Major	DBB	Strategic Building Solutions, LLC	Design Partnership of Cambridge, Inc.	CTA Construction Co., Inc.	Symmes, Maini & McKee Associates
200906150020	Athol-Royalston	Riverbend School	Design Development			Symmes Maini & McKee Associates	Mount Vernon Group Architects, Inc.	-	Strategic Building Solutions, LLC
201200160001	Attleboro	A. Irvin Studley Elementary School	Closeout	Repair - Accelerated		Tishman Construction Corporation of MA	Gale Associates, Inc.	Titan Roofing, Inc.	CBI Consulting Inc.
200800170305	Auburn	Auburn Middle	Construction	New Construction		Skanska USA Building, Inc	Lamoureux Pagano & Associates, Inc.	Fontaine Brothers, Inc.	WSP Flack + Kurtz
9999	Ayer-Shirley	Ayer-Shirley Regional Middle/High School	Construction	Addition / Renovation	CM@R	Dore and Whittier Architects, Inc.	Symmes Maini & McKee Associates, Inc.	Consigli Construction Company, Inc.	WSP Flack + Kurtz
201300200010	Barnstable	Barnstable United Elementary School	Approved Project Vote Pending	Repair - Accelerated		exPERTcon, Inc.	Gale Associates, Inc.	-	-
201100200005G	Barnstable	West Barnstable Elem	Closeout	Repair - Accelerated	DBB	PMA Construction Services	-	Paul J. Rogan Co., Inc.	CBI Consulting Inc.
200800260035	Belmont	Roger Wellington Elementary School	Closeout	New Construction	CM@R	PMA Construction Services	Jonathan Levi Architects LLC	Skanska USA Building, Inc.	Strategic Building Solutions, LLC
201006180505	Berkshire Hills	Monument Mountain Regional High School	Approved Project Vote Pending	Addition / Renovation		Strategic Building Solutions, LLC	Symmes Maini & McKee Associates, Inc.	-	-
200806200505	Berlin-Boylston	Tahanto Regional High School	Project Completion	New Construction	DBB	PMA Construction Services	HMFH Architects, Inc.	CTA Construction Co., Inc.	Strategic Building Solutions, LLC
200800300505	Beverly	Beverly High School	Closeout	Addition / Renovation	DBB	HEERY	-	-	-
201300300305	Beverly	Briscoe Middle	Eligibility Period			-	-	-	-
201300310505	Billerica	Billerica Memorial High School	Eligibility Period			-	-	-	-
200800310015	Billerica	Parker Elementary School	Closeout	New Construction	DBB	Joslin, Lesser + Associates Inc.	Symmes Maini & McKee Associates, Inc.	CTA Construction Co., Inc.	Sebesta Blomberg & Associates, Inc.
201208050605	Blackstone Valley Reg	Blackstone Valley	Closeout	Addition / Renovation		Compass Project Management, Inc.	Flansburgh Associates, Inc.	Pergola Construction Co., Inc.	Horizon Engineering Associates, LLP

201206220015	Blackstone-Millville	A F Maloney	Project Completion	Repair - Accelerated		Arcadis U.S., Inc.	DiMarinisi & Wolfe Architects Urban Designers	Greenwood Industries, Inc.	Gale Associates, Inc.
201206220505	Blackstone-Millville	Blackstone Millville RHS	Design Development	Repair - Accelerated		Arcadis U.S., Inc.	DiMarinisi & Wolfe Architects Urban Designers	-	Gale Associates, Inc.
201206220008	Blackstone-Millville	John F Kennedy Elem	Project Completion	Repair - Accelerated		Arcadis U.S., Inc.	DiMarinisi & Wolfe Architects Urban Designers	Greenwood Industries, Inc.	Gale Associates, Inc.
201306220010	Blackstone-Millville	Millville Elem	Approved Project Vote Pending	Repair - Accelerated		Pinck & Co., Inc.	CBI Consulting Inc.	-	-
201100350522G	Boston	Excel High School	Final Audit Approved	Repair - Accelerated	DBB	Daedalus Projects Inc	-	-	Simpson Gumpertz & Heger Inc.
201000350074	Boston	Henry Dearborn Middle School	Project Scope & Budget			Daedalus Projects Inc	Jonathan Levi Architects LLC	-	-
201000350565	Boston	Quincy Upper School	Schematic Design			City Employee - Maureen Anderson Skanska USA Building, Inc.	HMFH Architects, Inc.	-	-
201300400305	Braintree	East Middle School	Eligibility Period			-	-	-	-
201206250320	Bridgewater-Raynham	Bridgewater Middle School	Design Development	Repair - Accelerated		Vertex Construction Services	-	-	CBI Consulting Inc.
201206250050	Bridgewater-Raynham	Laliberte Elementary School	Design Development	Repair - Accelerated		Vertex Construction Services	Raymond Design Associates, Inc.	-	CBI Consulting Inc.
201206250020	Bridgewater-Raynham	Merrill Elementary School	Design Development	Repair - Accelerated		Vertex Construction Services	Raymond Design Associates, Inc.	-	CBI Consulting Inc.
201100440505G	Brockton	Brockton High	Closeout	Repair - Accelerated	DBB	Skanska USA Building, Inc	CSS Architects Incorporated	Gibson Roofs, Inc.	Simpson Gumpertz & Heger Inc.
201100440110G	Brockton	Downey	Closeout	Repair - Accelerated	DBB	Skanska USA Building, Inc	CSS Architects Incorporated	Built-up Roofing Systems LLC	Simpson Gumpertz & Heger Inc.
201100440405G	Brockton	East Junior High	Final Audit Approved	Repair - Accelerated	DBB	Skanska USA Building, Inc	CSS Architects Incorporated	Reliable Roofing and Sheet Metal, LLC	Rist-Frost-Shumway Engineering, P.C.
201100440023G	Brockton	Edgar B Davis	Final Audit Approved	Repair - Accelerated	DBB	Skanska USA Building, Inc	CSS Architects Incorporated	Reliable Roofing and Sheet Metal, LLC	Simpson Gumpertz & Heger Inc.
201100440045G	Brockton	Hancock	Final Audit Approved	Repair - Accelerated	DBB	Skanska USA Building, Inc	CSS Architects Incorporated	Reliable Roofing and Sheet Metal, LLC	Simpson Gumpertz & Heger Inc.
201100440410G	Brockton	North Junior High	Final Audit Approved	Repair - Accelerated	DBB	Skanska USA Building, Inc	-	Arden Engineering Constructors, LLC Built-up Roofing Systems LLC	Rist-Frost-Shumway Engineering, P.C.
201100440078G	Brockton	Oscar F Raymond	Final Audit Approved	Repair - Accelerated	DBB	Skanska USA Building, Inc	CSS Architects Incorporated	Reliable Roofing and Sheet Metal, LLC	Simpson Gumpertz & Heger Inc.
201100440420G	Brockton	West Junior High	Final Audit Approved	Repair - Accelerated	DBB	Skanska USA Building, Inc	CSS Architects Incorporated	Reliable Roofing and Sheet Metal, LLC	Simpson Gumpertz & Heger Inc.
201100450005G	Brookfield	Brookfield Elementary	Closeout	Repair - Accelerated	DBB	Diversified Project Management	-	Northeast Energy Control Systems	Cannon Design
201100460015	Brookline	Edward Devotion	Feasibility Study			Town Employee - Anthony Guigli	HMFH Architects, Inc.	-	-
201000460025	Brookline	Heath School	Closeout	Addition / Renovation	DBB	Town of Brookline Building Department	Miller Dyer Spears Inc.	Nauset Construction Corporation	Consulting Engineering Services, LLC
200800460045	Brookline	John D. Runkle School	Closeout	Addition / Renovation	DBB	Town of Brookline Building Department	Design Partnership of Cambridge, Inc.	G & R Construction, Inc.	Consulting Engineering Services, LLC
201000480303	Burlington	Marshall Simonds Middle School	Closeout	Addition / Renovation	CM@R	Construction Monitoring Services, Inc.	Knight, Bagge & Anderson, Inc.	CTA Construction Co., Inc.	RDk Engineers
200800480015	Burlington	Memorial Elementary School	Closeout	New Construction	DBB	Construction Monitoring Services, Inc.	Knight, Bagge & Anderson, Inc.	CTA Construction Co., Inc.	Consulting Engineering Services, LLC

201200500012	Canton	Lt Peter M Hansen	Design Development	Repair - Accelerated		Vertex Construction Services	CSS Architects Incorporated	-	Simpson Gumpertz & Heger Inc.
201200500305	Canton	Wm H Galvin Middle	Design Development	Repair - Accelerated		Vertex Construction Services	CSS Architects Incorporated	-	Simpson Gumpertz & Heger Inc.
201008150605G	Cape Cod Region Voc Tech	Cape Cod Region Voc Tech	Final Audit Approved	Repair - Accelerated	DBB	URS Corporation	-	-	Fitzmeyer & Tocci Associates, Inc.
200800510025	Carlisle	Carlisle School	Closeout	Addition / Renovation	DBB	Daedalus Projects Inc	HMFH Architects, Inc.	H.V. Collins Co., Inc.	Horizon Engineering Associates, LLP
201300520015	Carver	Carver Elementary School	Eligibility Period			-	-	-	-
201306350010	Central Berkshire	Berkshire Trail Elem	Approved Project Vote Pending	Repair - Accelerated		Strategic Building Solutions, LLC	Tighe & Bond, Inc.	-	-
201106350035G	Central Berkshire	Kittredge	Closeout	Repair - Accelerated	DBB	Daedalus Projects Inc	Bradley Architects, Inc.	Alpha Contracting Associates, Inc.	Strategic Building Solutions, LLC
201100560030G	Chelmsford	Byam School	Final Audit Approved	Repair - Accelerated	DBB	Vertex Construction Services	Russo Barr Associates, Inc.	S.O.M. Construction Ent., Inc.	Simpson Gumpertz & Heger Inc.
201100560505G	Chelmsford	Chelmsford High	Final Audit Approved	Repair - Accelerated	DBB	Vertex Construction Services	Russo Barr Associates, Inc.	Lockheed Window Corporations	Simpson Gumpertz & Heger Inc.
200800570050	Chelsea	Clark Avenue School	Schematic Design			Pinck & Co., Inc.	HMFH Architects, Inc.	-	-
200900610021	Chicopee	Chicopee Academy	Design Development	Addition / Renovation		Arcadis U.S., Inc.	Caolo & Bieniek Associates, Inc.	-	Symmes, Maini & McKee Associates
200906400505	Concord-Carlisle	Concord-Carlisle Regional High School	Construction	New Construction	CM@R	KV Associates, Inc.	OMR Architects, Inc.	Turner Construction Company	Strategic Building Solutions, LLC
200800710505	Danvers	Danvers High School	Project Completion	Addition / Renovation	DBB	Construction Monitoring Services, Inc.	DiNisco Design Partnership, Limited	Bacon Construction Co, Inc.	Turner Facilities Management Solutions
200800730010	Dedham	Avery Elementary School	Closeout	New Construction	CM@R	Construction Monitoring Services, Inc.	Dore & Whittier Architects, Inc.	Consigli Construction Company, Inc.	WSP Flack + Kurtz
201200730005	Dedham	Early Childhood Center	OPM Selection			-	-	-	-
201006450005G	Dennis-Yarmouth	Ezra H Baker	Final Audit Approved	Repair - Accelerated	DBB	STV Incorporated	Knight, Bagge & Anderson, Inc.	Antonelli Construction Co., Inc.	CBI Consulting Inc.
201306500005	Dighton-Rehoboth	Dighton Elementary	Approved Project Vote Pending	Repair - Accelerated		-	-	-	-
201306500305	Dighton-Rehoboth	Dighton Middle School	Approved Project Vote Pending	Repair - Accelerated		-	-	-	-
201306500505	Dighton-Rehoboth	Dighton-Rehoboth Rhs	Approved Project Vote Pending	Repair - Accelerated		-	-	-	-
201306500310	Dighton-Rehoboth	Dorothy L Beckwith	Approved Project Vote Pending	Repair - Accelerated		-	-	-	-
200800770010	Douglas	Douglas Elementary	Project Completion	New Construction - Model School	DBB	HEERY	DiNisco Design Partnership, Limited	CTA Construction Co., Inc.	Consulting Engineering Services, LLC
200800770100G	Douglas	Douglas Intermediate Elementary School	Construction	Addition / Renovation	DBB	HEERY	DiNisco Design Partnership, Limited	CTA Construction Co., Inc.	Consulting Engineering Services, LLC
200800790505	Dracut	Dracut Senior High School	Construction	Addition / Renovation	DBB	Collaborative Partners f/k/a RF Walsh Collab Ptnrs	Mount Vernon Group Architects, Inc.	CTA Construction Co., Inc.	RDK Engineers
201000820505	Duxbury	Duxbury High School	Construction	New Construction - Model School	CM@R	KV Associates, Inc.	Mount Vernon Group Architects, Inc.	Dimeo Construction Company	WSP Flack + Kurtz
200900830505	East Bridgewater	East Bridgewater High School	Project Completion	New Construction - Model School	DBB	Collaborative Partners f/k/a RF Walsh Collab Ptnrs	Ai3 Architects LLC	Fontaine Brothers, Inc.	Foreman Building Commissioning, LP
200800860505	Easthampton	Easthampton High School	Project Completion	New Construction	DBB	Strategic Building Solutions, LLC	Caolo & Bieniek Associates, Inc.	Fontaine Brothers, Inc.	Consulting Engineering Services, LLC
201200880405	Easton	Easton Junior High	Closeout	Repair - Accelerated		PMA Construction Services	Russo Barr Associates, Inc.	Gibson Roofs, Inc.	Gale Associates, Inc.
201300880020	Easton	Moreau Hall	Design Development	Repair - Accelerated		Skanska USA Building, Inc	Baker/Wohl Architects, Inc.	-	Gale Associates, Inc.

200809130705	Essex Agr Tech	Essex Agricultural and Technical High School	Construction	New Construction	CM@R	PMA Construction Services	Design Partnership of Cambridge, Inc.	Gilbane Building Company	Turner Facilities Management Solutions
200800940020	Fairhaven	Rogers Elementary School	Project Completion	New Construction - Model School	DBB	Daedalus Projects Inc	HMFH Architects, Inc.	CTA Construction Co., Inc.	Consulting Engineering Services, LLC
200900950315	Fall River	James Madison Morton Middle School	Project Completion	New Construction	DBB	Maguire Group Inc.	Mount Vernon Group Architects, Inc.	J & J Contractors, Inc.	Sebesta Blomberg & Associates, Inc.
201100970505G	Fitchburg	Fitchburg High	Final Audit Approved	Repair - Accelerated	DBB	Compass Project Management, Inc.	BLW Engineers, Inc.	Ostrow Electrical Co., Inc.	RDK Engineers
201100970048G	Fitchburg	Memorial Intermediate	Final Audit Approved	Repair - Accelerated	DBB	Compass Project Management, Inc.	Knight, Bagge & Anderson, Inc.	Lockheed Window Corporations	Simpson Gumpertz & Heger Inc.
201100970043G	Fitchburg	Reingold Elementary	Final Audit Approved	Repair - Accelerated	DBB	Compass Project Management, Inc.	Knight, Bagge & Anderson, Inc.	Lockheed Window Corporations	Simpson Gumpertz & Heger Inc.
201100970060G	Fitchburg	South Street Elementary	Final Audit Approved	Repair - Accelerated	DBB	Compass Project Management, Inc.	Knight, Bagge & Anderson, Inc.	Lockheed Window Corporations	Simpson Gumpertz & Heger Inc.
200800990505	Foxborough	Foxborough High School	Final Audit Approved	Repair - Major	DBB	Construction Monitoring Services, Inc.	Kaestle Boos Associates, Inc.	CTA Construction Co., Inc.	Consulting Engineering Services, LLC
200901010505	Franklin	Franklin High School	Construction	New Construction - Model School	DBB	Daedalus Projects Inc	Ai3 Architects LLC	Bacon-Agostini Construction Joint Venture	Consulting Engineering Services, LLC
201201030505	Gardner	Gardner High	Project Completion	Addition / Renovation		Pinck & Co., Inc.	Lamoureux Pagano & Associates, Inc.	Five Star Building Corp.	Fitzmeyer & Tocci Associates, Inc.
201201030405	Gardner	Gardner Middle School	Project Completion	Repair - Accelerated		Leftfield, LLC	Richard D. Kimball Company, Inc.	Royal Steam Heater Co.	Fitzmeyer & Tocci Associates, Inc.
200801050505	Georgetown	Georgetown Middle/High School	Project Scope & Budget	Addition / Renovation		Municipal Building Consultants, Inc.	Drummey Rosane Anderson, Inc.	-	-
200901050010	Georgetown	Penn Brook Elementary School	Construction	New Construction	DBB	Municipal Building Consultants, Inc.	Drummey Rosane Anderson, Inc.	Brait Builders Corp.	Rist-Frost-Shumway Engineering, P.C.
200901070050	Gloucester	West Parish Elementary School	Design Development			Knight, Bagge & Anderson Inc.	Dore & Whittier Architects, Inc.	-	-
200801100505	Grafton	Grafton Memorial Senior	Closeout	New Construction	CM@R	Joslin, Lesser + Associates Inc.	Symmes Maini & McKee Associates, Inc.	Dimeo Construction Company	Horizon Engineering Associates, LLP
201101100005G	Grafton	South Grafton Elementary	Final Audit Approved	Repair - Accelerated	DBB	URS Corporation	CGKV Architects, Inc.	AAlanco Service Corporation	Horizon Engineering Associates, LLP
201201110010	Granby	West St	OPM Selection			-	-	-	-
201108230605	Greater Lawrence RVT	Gr Lawrence Reg Voc Tech	Design Development	Repair - Major		Vertex Construction Services	Richard D. Kimball Company, Inc.	-	WSP Flack + Kurtz
200908280605	Greater Lowell Voc Tec	Greater Lowell Regional Technical High School	Construction	Addition / Renovation	CM@R	Joslin, Lesser + Associates Inc.	Knight, Bagge & Anderson, Inc.	Consigli Construction Company, Inc.	Horizon Engineering Associates, LLP
201008250605	Greater New Bedford	Greater New Bedford Vocational Technical High School	Construction	Addition / Renovation	DBB	Construction Monitoring Services, Inc.	Drummey Rosane Anderson, Inc.	Agostini Construction Co., Inc.	Symmes, Maini & McKee Associates
201101140025G	Greenfield	Four Corners	Final Audit Approved	Repair - Accelerated	DBB	P3 Inc.	-	Five Star Building Corp.	Strategic Building Solutions, LLC
200901140505	Greenfield	Greenfield High School	Construction	New Construction	CM@R	Construction Monitoring Services, Inc.	Dore & Whittier Architects, Inc.	Shawmut Design and Construction	BVH Integrated Services, P.C.
201206730305	Groton-Dunstable	Groton/Dun Reg'l Middle	Closeout	Repair - Accelerated		Collaborative Partners f/k/a RF Walsh Collab Ptnrs	ICON architecture, inc.	Greenwood Industries, Inc.	Russo Barr Associates, Inc.
201101170505G	Hadley	Hopkins Academy	Final Audit Approved	Repair - Accelerated		Strategic Building Solutions, LLC	CSS Architects Incorporated	MDM Engineering	Russo Barr Associates, Inc.
201306750007	Hamilton-Wenham	Bessie Buker Elementary	Approved Project Vote Pending	Repair - Accelerated		NETCO Construction Project Managers, Inc.	Habeeb & Associates Architects, Inc.	-	-
201206750010	Hamilton-Wenham	Cutler School	Closeout	Repair - Accelerated		Coast and Harbor Association, Inc.	CBI Consulting Inc.	Stanley Roofing Company, Inc.	Russo Barr Associates, Inc.
201306750015	Hamilton-Wenham	Winthrop School	Approved Project Vote Pending	Repair - Accelerated		NETCO Construction Project Managers, Inc.	Habeeb & Associates Architects, Inc.	-	-

200806800505	Hampden-Wilbraham	Minnechaug Regional High School	Closeout	New Construction - Model School	DBB	Pinnacle One, Inc.	Mount Vernon Group Architects, Inc.	Fontaine Brothers, Inc.	Horizon Engineering Associates, LLP
201001210005G	Hancock	Hancock Elementary School	Final Audit Approved	Repair - Accelerated	DBB	-	-	Salco Construction Company, Inc.	-
200801220505	Hanover	Hanover High School	Closeout	New Construction	DBB	PMA Construction Services	HMFH Architects, Inc.	Callahan, Inc.	Horizon Engineering Associates, LLP
201301220015	Hanover	Sylvester	Eligibility Period			-	-	-	-
201301270505	Hatfield	Smith Academy	Approved Project Vote Pending	Repair - Accelerated		Collaborative Partners f/k/a RF Walsh Collab Ptnrs	Civitects	-	-
201201280035	Haverhill	Caleb Dustin Hunking	Schematic Design			Joslin, Lesser + Associates Inc.	JCJ Architecture, PC	-	-
201101280100G	Haverhill	Consentino	Closeout	Repair - Accelerated	DBB	Vertex Construction Services	CSS Architects Incorporated	New England Builders & Contractors, Inc.	RDK Engineers Russo Barr Associates, Inc.
	Haverhill	Haverhill High School	Closeout			-	-	-	-
201101280085G	Haverhill	John G Whittier	Closeout	Repair - Accelerated	DBB	Vertex Construction Services	CSS Architects Incorporated	New England Builders & Contractors, Inc.	Russo Barr Associates, Inc.
201101280075G	Haverhill	Tilton	Closeout	Repair - Accelerated	DBB	Vertex Construction Services	CSS Architects Incorporated	Titan Roofing, Inc.	Russo Barr Associates, Inc.
201101280080G	Haverhill	Walnut Square	Closeout	Repair - Accelerated	DBB	Vertex Construction Services	CSS Architects Incorporated	Titan Roofing, Inc.	RDK Engineers Russo Barr Associates, Inc.
201001310410	Hingham	Hingham Middle School	Construction	New Construction - Model School	DBB	Knight, Bagge & Anderson Inc.	Ai3 Architects LLC	Brait Builders Corp.	Foreman Building Commissioning, LP
200801330505	Holbrook	Holbrook Junior-Senior High School	Feasibility Study			Symmes Maini & McKee Associates, Inc.	Flansburgh Associates, Inc.	-	-
201201370015	Holyoke	Lt Elmer J McMahon Elem	OPM Selection			-	-	-	-
201201370605	Holyoke	Wm J Dean Voc Tech High	Project Completion	Addition / Renovation		Skanska USA Building, Inc	Kaestle Boos Associates, Inc.	RAC Builders, Inc.	BVH Integrated Services, P.C.
201301380010	Hopedale	Memorial	Design Development	Repair - Accelerated		Atlantic Construction and Management, Inc.	Civitects	-	Simpson Gumpertz & Heger Inc.
201301390005	Hopkinton	Center	Eligibility Period			-	-	-	-
200801410410	Hudson	John F. Kennedy Middle School	Project Completion	New Construction	DBB	PMA Construction Services	OMR Architects, Inc.	Bacon-Agostini Construction Joint Venture	WSP Flack + Kurtz
201201530007	Leominster	Fall Brook	Closeout	Repair - Accelerated		Compass Project Management, Inc.	Reinhardt Associates, Inc.	NB Kenney Company, Inc	Horizon Engineering Associates, LLP
200801530505	Leominster	Leominster High School	Project Completion	Addition / Renovation	CM@R	Daedalus Projects Inc	Lamoureux Pagano & Associates, Inc.	S.O.M. Construction Ent., Inc.	Horizon Engineering Associates, LLP
201201530010	Leominster	Southeast School	Closeout	Repair - Accelerated		Compass Project Management, Inc.	Reinhardt Associates, Inc.	NB Kenney Company, Inc	Horizon Engineering Associates, LLP Russo Barr Associates, Inc.
201101540005G	Leverett	Leverett Elementary	Closeout	Repair - Accelerated	DBB	Potomac Capital Advisors	DiMarinisi & Wolfe Architects Urban Designers	-	Russo Barr Associates, Inc.
201101550010E	Lexington	Joseph Estabrook	Project Completion	New Construction	CM@R	Collaborative Partners f/k/a RF Walsh Collab Ptnrs	DiNisco Design Partnership, Limited	Shawmut Design and Construction	BVH Integrated Services, P.C.
200801590505	Longmeadow	Longmeadow High School	Project Completion	New Construction	CM@R	Joslin, Lesser + Associates Inc.	OMR Architects, Inc.	Gilbane Building Company	Foreman Building Commissioning, LP
201101600505G	Lowell	Lowell High	Final Audit Approved	Repair - Accelerated	DBB	NETCO Construction Project Managers, Inc.	ICON architecture, inc.	-	Building Enclosure Associates, LLC
201101600027G	Lowell	Moody Elem	Closeout	Repair - Accelerated	DBB	NETCO Construction Project Managers, Inc.	ICON architecture, inc.	Paul J. Rogan Co., Inc.	Building Enclosure Associates, LLC
201101600040G	Lowell	Peter W Reilly	Final Audit Approved	Repair - Accelerated	DBB	NETCO Construction Project Managers, Inc.	ICON architecture, inc.	-	Building Enclosure Associates, LLC

201101600055G	Lowell	Washington	Closeout	Repair - Accelerated	DBB	NETCO Construction Project Managers, Inc.	ICON architecture, inc.	Alpha Contracting Associates, Inc.	Building Enclosure Associates, LLC RDK Engineers
201001620505	Lunenburg	Lunenburg High School	Design Development	New Construction		Joslin, Lesser + Associates Inc.	Tappe Associates, Inc.	Shawmut Design and Construction	-
201201630405	Lynn	Breed Middle School	Project Completion	Repair - Accelerated		Diversified Project Management	Kaestle Boos Associates, Inc.	GVW, Inc.	CBI Consulting Inc.
201201630605	Lynn	Lynn Voc Tech Institute	Closeout	Repair - Accelerated		Diversified Project Management	Kaestle Boos Associates, Inc.	Gibson Roofs, Inc.	CBI Consulting Inc.
200901630305	Lynn	Thurgood Marshall Middle School	Design Development	New Construction		Joslin, Lesser + Associates Inc.	Raymond Design Associates, Inc.	Walsh Brothers, Inc.	Rist-Frost-Shumway Engineering, P.C.
200901640505	Lynnfield	Lynnfield High School	Project Completion	Addition / Renovation	DBB	HEERY	Edward Rowse Architects, Inc.	E.A. Colangeli Construction Co. Inc	Fitzmeyer & Tocci Associates, Inc.
200801680020	Marblehead	Glover School	Project Completion	New Construction	DBB	Municipal Building Consultants, Inc.	JCJ Architecture, PC	G & R Construction, Inc.	RDK Engineers
201101700008G	Marlborough	Francis J Kane	Closeout	Repair - Accelerated	DBB	Collaborative Partners f/k/a RF Walsh Collab Ptnrs	Baker/Wohl Architects, Inc.	A&A Window Products, Inc.	Building Enclosure Associates, LLC
201101700505G	Marlborough	Marlborough High	Closeout	Repair - Accelerated	DBB	Collaborative Partners f/k/a RF Walsh Collab Ptnrs	Baker/Wohl Architects, Inc.	A&A Window Products, Inc. Feeley, McAnespie, Inc. Veterans Development Corporation, Inc.	Building Enclosure Associates, LLC RDK Engineers
201101710505	Marshfield	Marshfield High	Construction	New Construction - Model School	DBB	Compass Project Management, Inc.	Ai3 Architects LLC	Brait Builders Ventures	Sebesta Blomberg & Associates, Inc.
200801740505	Maynard	Maynard High School	Construction	New Construction	DBB	Municipal Building Consultants, Inc.	Tappe Associates, Inc.	CTA Construction Co., Inc.	WSP Flack + Kurtz
201201760505	Medford	Medford High	Construction	Addition / Renovation		Leftfield, LLC	DiNisco Design Partnership, Limited	G & R Construction, Inc.	Cannon Design
201301760505	Medford	Medford High	Design Development	Repair - Accelerated		Architectural Consulting Group, LLC	Dietz & Company Architects, Inc.	-	Symmes, Maini & McKeefe Associates
200801770305	Medway	Medway Middle School	Final Audit Approved	Repair - Major	CM@R	Compass Project Management, Inc.	Knight, Bagge & Anderson, Inc.	Consigli Construction Company, Inc.	Sebesta Blomberg & Associates, Inc.
201201780505	Melrose	Melrose High	Closeout	Addition / Renovation		Collaborative Partners f/k/a RF Walsh Collab Ptnrs	Ai3 Architects LLC	G & R Construction, Inc.	WSP Flack + Kurtz
201107100015G	Mendon-Upton	Miscoe Hill School	Final Audit Approved	Repair - Accelerated	DBB	CDR Maguire formerly known as Maguire Group Inc.	Habeeb & Associates Architects, Inc.	Greenwood Industries, Inc.	Sebesta Blomberg & Associates, Inc.
200801810505	Methuen	Methuen High School	Construction	Addition / Renovation	CM@R	KBA/Trident	Finegold Alexander and Associates Inc.	Dimeo Construction Company	Environmental Health and Engineering
201101820025G	Middleborough	Mary K. Goode Elementary School	Closeout	Repair - Accelerated	DBB	CDR Maguire formerly known as Maguire Group Inc.	Habeeb & Associates Architects, Inc.	J.J. Cardosi, Inc.	Russo Barr Associates, Inc.
200801840005	Middleton	Howe-Manning School	Final Audit Approved	New Construction	DBB	Collaborative Partners f/k/a RF Walsh Collab Ptnrs	DiNisco Design Partnership, Limited	CTA Construction Co., Inc.	Foreman Building Commissioning, LP
201101850090	Milford	Woodland	Project Scope & Budget			Joslin, Lesser + Associates Inc.	HMFH Architects, Inc.	Shawmut Design and Construction	-
200908300605	Minuteman Voc Tech	Minuteman Regional High School	Feasibility Study			Skanska USA Building, Inc	Kaestle Boos Associates, Inc.	-	-
201107170005G	Mohawk Trail	Buckland-Shelburne Reg	Final Audit Approved	Repair - Accelerated	DBB	Potomac Capital Advisors	Bradley Architects, Inc.	-	Strategic Building Solutions, LLC
201107170010G	Mohawk Trail	Colrain Central	Final Audit Approved	Repair - Accelerated	DBB	Potomac Capital Advisors	Bradley Architects, Inc.	-	Strategic Building Solutions, LLC
201107170505G	Mohawk Trail	Mohawk Trail Reg High	Final Audit Approved	Repair - Accelerated	DBB	Potomac Capital Advisors	Bradley Architects, Inc.	-	Strategic Building Solutions, LLC
201107129999	Monomoy	Monomoy Regional High School	Construction	New Construction - Model School	DBB	Skanska USA Building, Inc	Mount Vernon Group Architects, Inc.	Fontaine Brothers, Inc.	Sebesta Blomberg & Associates, Inc.
201307150505	Mount Greylock	Mt Greylock Reg High	Eligibility Period			-	-	-	-

201107200003G	Narragansett	Phillipston Memorial	Closeout	Repair - Accelerated	DBB	Potomac Capital Advisors	DiMarinisi & Wolfe Architects Urban Designers -		Rist-Frost-Shumway Engineering, P.C.
200807200020	Narragansett	Templeton Center School	Feasibility Study			Strategic Building Solutions, LLC	Symmes Maini & McKee Associates, Inc.	-	-
200807250015	Nashoba	Pompositticut Elementary School	Closeout	Addition / Renovation	DBB	Construction Monitoring Services, Inc.	Symmes Maini & McKee Associates, Inc.	P.J. Stella Construction Corp.	Strategic Building Solutions, LLC
200908520605G	Nashoba Valley Tech	Nashoba Valley Tech H S	Closeout	Repair - Accelerated	DBB	STV Incorporated	-	-	-
201308520605	Nashoba Valley Tech	Nashoba Valley Tech H S	Approved Project Vote Pending	Repair - Accelerated		-	-	-	-
200801980505	Natick	Natick High School	Closeout	New Construction - Model School	DBB	Collaborative Partners f/k/a RF Walsh Collab Ptnrs	Ai3 Architects LLC	Brait Builders Corp.	Rist-Frost-Shumway Engineering, P.C.
201306600305	Nauset	Nauset Reg Middle	Approved Project Vote Pending	Repair - Accelerated		Strategic Building Solutions, LLC	ICON architecture, inc.	-	Russo Barr Associates, Inc.
201106600505G	Nauset	Nauset Regional High	Final Audit Approved	Repair - Accelerated	DBB	NETCO Construction Project Managers, Inc.	Habeeb & Associates Architects, Inc.	Modern Glass & Aluminum, Inc.	CBI Consulting Inc.
201301990035	Needham	Hillside Elementary	Eligibility Period			-	-	-	-
200901990050	Needham	Newman Elementary School	Closeout	Repair - Major	CM@R	-	Drummey Rosane Anderson, Inc.	Consigli Construction Company, Inc.	Rist-Frost-Shumway Engineering, P.C.
200902010070	New Bedford	John Hannigan	OPM Selection			-	-	-	-
W201002010505	New Bedford	New Bedford High	Closeout	Repair - Major	DBB	-	-	-	-
201102040005	Newburyport	Francis T Bresnahan Elem	Construction	New Construction - Model School	DBB	HEERY	HMFH Architects, Inc.	CTA Construction Co., Inc.	Fitzemeyer & Tocci Associates, Inc.
201002040305	Newburyport	Rupert A. Nock Middle School	Construction	Addition / Renovation	CM@R	HEERY	Miller Dyer Spears Inc.	Gilbane Building Company	Fitzemeyer & Tocci Associates, Inc.
201102070005	Newton	A E Angier	Design Development	New Construction		Joslin, Lesser + Associates Inc.	DiNisco Design Partnership, Limited	-	Fitzemeyer & Tocci Associates, Inc.
201102070015G	Newton	Bowen	Closeout	Repair - Accelerated	DBB	-	Habeeb & Associates Architects, Inc.	-	-
201302070025	Newton	Cabot	Eligibility Period			-	-	-	-
201102070125G	Newton	Williams	Closeout	Repair - Accelerated	DBB	-	-	-	-
200802080005	Norfolk	Freeman-Kennedy Elementary School	Project Completion	New Construction	DBB	Joslin, Lesser + Associates Inc.	Flansburgh Associates, Inc.	Fontaine Brothers, Inc.	WSP Flack + Kurtz
200909150705	Norfolk County Agriculture	Norfolk County Agr	Construction	Addition / Renovation	DBB	Compass Project Management, Inc.	Turowski2 Architecture, Inc.	TLT Construction Corporation	Rist-Frost-Shumway Engineering, P.C.
200802090305	North Adams	Silvio O Conte Middle School	Design Development	Addition / Renovation		Strategic Building Solutions, LLC	Margo Jones Architects, Inc.	-	Rist-Frost-Shumway Engineering, P.C.
201102110018G	North Andover	Annie L Sargent School	Closeout	Repair - Accelerated	DBB	Municipal Building Consultants, Inc.	ICON architecture, inc.	Varioka Construction, Inc.	Cannon Design
201102110001G	North Andover	Atkinson	Closeout	Repair - Accelerated	DBB	Municipal Building Consultants, Inc.	ICON architecture, inc.	Paul J. Rogan Co., Inc.	Cannon Design
201102110305G	North Andover	North Andover Middle	Closeout	Repair - Accelerated	DBB	Municipal Building Consultants, Inc.	ICON architecture, inc.	Stanley Roofing Company, Inc.	Cannon Design
201202120505	North Attleborough	North Attleboro High	Closeout	Addition / Renovation		Skanska USA Building, Inc	Kaestle Boos Associates, Inc.	M. O'Connor Contracting, Inc.	Consulting Engineering Services, LLC
201202120015	North Attleborough	Roosevelt Avenue	Project Completion	Repair - Accelerated		Skanska USA Building, Inc	Russo Barr Associates, Inc.	Evergreen Construction Corporataion	Gale Associates, Inc.
201102150015G	North Brookfield	North Brookfield Elem	Final Audit Approved	Repair - Accelerated	DBB	Vertex Construction Services	-	Lockheed Window Corporations	Simpson Gumpertz & Heger Inc.
201202150015	North Brookfield	North Brookfield Elem	Closeout	Repair - Accelerated		Strategic Building Solutions, LLC	CBI Consulting Inc.	Garland Construction Corp.	Simpson Gumpertz & Heger Inc.
201107350010G	North Middlesex	Ashby Elementary	Final Audit Approved	Repair - Accelerated	DBB	Compass Project Management, Inc.	Russo Barr Associates, Inc.	GVW, Inc.	Building Enclosure Associates, LLC
201107350505	North Middlesex	North Middlesex Reg	Approved Project Vote Pending			HEERY	Symmes Maini & McKee Associates, Inc.	-	-

201107350005G	North Middlesex	Spaulding Memorial	Final Audit Approved	Repair - Accelerated	DBB	Compass Project Management, Inc.	Russo Barr Associates, Inc.	MDM Engineering	Building Enclosure Associates, LLC
201002170505	North Reading	North Reading High School	Construction	Addition / Renovation	CM@R	PMA Construction Services	Dore & Whittier Architects, Inc.	Gilbane Building Company	Cannon Design
201102130003	Northborough	Lincoln Street	Project Scope & Budget			Strategic Building Solutions, LLC	Lamoureux Pagano & Associates, Inc.	-	-
201202180015	Norton	J C Solmonese	Closeout	Repair - Accelerated		Joslin, Lesser + Associates Inc.	Habeeb & Associates Architects, Inc.	Silktown Roofing	Simpson Gumpertz & Heger Inc.
200902180505	Norton	Norton High School	Project Completion	Addition / Renovation	CM@R	Pinck & Co., Inc.	JCJ Architecture, PC	W. T. Rich Company Inc.	Rist-Frost-Shumway Engineering, P.C.
200908550605		Old Colony Reg Voc Tech	Closeout	Repair - Major	DBB	Vertex Construction Services	Habeeb & Associates Architects, Inc.	J.D. Rivet & Co., Inc.	Consulting Engineering Services, LLC
200802260405	Oxford	Oxford Middle School	Construction	Repair - Major	DBB	Diversified Project Management	CGKV Architects, Inc.	J.J. Cardosi, Inc.	Cannon Design
201102270305G	Palmer	Converse Middle	Closeout	Repair - Accelerated	DBB	Diversified Project Management	-	Royal Steam Heater Co. Titan Roofing, Inc.	Strategic Building Solutions, LLC
201102270008G	Palmer	Old Mill Pond	Closeout	Repair - Accelerated	DBB	Diversified Project Management	-	Royal Steam Heater Co. Titan Roofing, Inc.	Strategic Building Solutions, LLC
201102270505G	Palmer	Palmer High	Closeout	Repair - Accelerated	DBB	Diversified Project Management	-	Royal Steam Heater Co. Titan Roofing, Inc.	Strategic Building Solutions, LLC
201308600605	Pathfinder Voc Tech	Pathfinder Voc Tech	Design Development	Repair - Accelerated		exPERTcon, Inc.	Baker/Wohl Architects, Inc.	-	Building Enclosure Associates, LLC
200802290305	Peabody	Higgins Middle School	Design Development			Daedalus Projects Inc	DiNisco Design Partnership, Limited	-	BVH Integrated Services, P.C.
201102290007G	Peabody	John E Burke	Closeout	Repair - Accelerated	DBB	Daedalus Projects Inc	LPBA/ Architects, Inc.	-	Sebesta Blomberg & Associates, Inc.
201102290027G	Peabody	William A Welch Sr	Closeout	Repair - Accelerated	DBB	Daedalus Projects Inc	LPBA/ Architects, Inc.	-	Sebesta Blomberg & Associates, Inc.
201302310010	Pembroke	Hobomock Elementary	Approved Project Vote Pending	Repair - Accelerated		Pinck & Co., Inc.	The S/L/A/M Collaborative	-	CBI Consulting Inc.
201302310015	Pembroke	North Pembroke Elem	Approved Project Vote Pending	Repair - Accelerated		Pinck & Co., Inc.	The S/L/A/M Collaborative	-	CBI Consulting Inc.
201302310305	Pembroke	Pembroke Community Middle School	Approved Project Vote Pending	Repair - Accelerated		Pinck & Co., Inc.	The S/L/A/M Collaborative	-	CBI Consulting Inc.
201302310505	Pembroke	Pembroke High School	Approved Project Vote Pending	Repair - Accelerated		Pinck & Co., Inc.	The S/L/A/M Collaborative	-	CBI Consulting Inc.
201107450020G	Pentucket	Dr Frederick N Sweetsir	Closeout	Repair - Accelerated	DBB	PMA Construction Services Inc.	Knight, Bagge & Anderson, Inc.	E. Amanti & Sons, Inc.	CBI Consulting Inc. RDK Engineers
201107450015G	Pentucket	Dr John C Page School	Closeout	Repair - Accelerated	DBB	PMA Construction Services Inc.	Knight, Bagge & Anderson, Inc.	Capeway Roofing Systems, Inc.	CBI Consulting Inc. RDK Engineers
201107450005G	Pentucket	Elmer S Bagnall	Final Audit Approved	Repair - Accelerated	DBB	PMA Construction Services Inc.	Knight, Bagge & Anderson, Inc.	Gibson Roofs, Inc.	CBI Consulting Inc. RDK Engineers
201307450405	Pentucket	Pentucket Reg Middle	Approved Project Vote Pending	Repair - Accelerated		Arcadis U.S., Inc.	CGKV Architects, Inc.	-	Strategic Building Solutions, LLC
201107500008G	Pioneer Valley	Northfield Elementary	Closeout	Repair - Accelerated	DBB	Diversified Project Management	CGKV Architects, Inc.	-	Strategic Building Solutions, LLC
201107500505G	Pioneer Valley	Pioneer Valley Reg	Closeout	Repair - Accelerated	DBB	Diversified Project Management	CGKV Architects, Inc.	-	Strategic Building Solutions, LLC
201002360510	Pittsfield	Taconic High School	Feasibility Study			Skanska USA Building, Inc	Drummey Rosane Anderson, Inc.	-	-
200802390505	Plymouth	Plymouth North High School	Project Completion	New Construction - Model School	DBB	Ted Gentry Associates, Inc	Ai3 Architects LLC	-	Sebesta Blomberg & Associates, Inc.
201202390515	Plymouth	Plymouth South High	Feasibility Study			Ted Gentry Associates, Inc	Ai3 Architects LLC	-	-
201302420505	Provincetown	Provincetown High	Eligibility Period			-	-	-	-
201207530030	Quabbin	Ruggles Lane	Closeout	Repair - Accelerated	DBB	Vertex Construction Services	Turowski2 Architecture, Inc.	PDS Engineering and Construction, Inc.	Simpson Gumpertz & Heger Inc.

201207780005	Quaboag Regional	Warren Elementary	Project Completion	Repair - Accelerated		Coast and Harbor Association, Inc.	Lindgren & Sharples, Inc.	AAlanco Service Corporation	Strategic Building Solutions, LLC
200802430315	Quincy	Central Middle School	Project Completion	New Construction - Model School	DBB	Tishman Construction Corporation of MA	Ai3 Architects LLC	H.V. Collins Co., Inc.	Sebesta Blomberg & Associates, Inc.
201302430060	Quincy	Merrymount	Approved Project Vote Pending	Repair - Accelerated		Skanska USA Building, Inc	Habeeb & Associates Architects, Inc.	-	-
201302430510	Quincy	North Quincy High	Approved Project Vote Pending	Repair - Accelerated		Skanska USA Building, Inc	Habeeb & Associates Architects, Inc.	-	-
201302430320	Quincy	Reay E Sterling Middle	Eligibility Period			-	-	-	-
201302430110	Quincy	Wollaston School	Approved Project Vote Pending	Repair - Accelerated		Skanska USA Building, Inc	Habeeb & Associates Architects, Inc.	-	-
201302440410	Randolph	Randolph Community Middle	Design Development	Repair - Accelerated		NETCO Construction Project Managers, Inc.	Taylor & Burns, Inc.	-	Consulting Engineering Services, LLC
201302440505	Randolph	Randolph High	Design Development	Repair - Accelerated		NETCO Construction Project Managers, Inc.	-	-	Gale Associates, Inc.
201002480035	Revere	Staff Sergeant James J. Hill School	Construction	New Construction		Collaborative Partners f/k/a RF Walsh Collab Ptnrs	-	-	Rist-Frost-Shumway Engineering, P.C.
200802510305	Rockland	John W. Rogers Middle School	Project Completion	New Construction	CM@R	Daedalus Projects Inc	Dore & Whittier Architects, Inc.	Agostini Construction Co., Inc.	Consulting Engineering Services, LLC
201102510025G	Rockland	R Stewart Esten	Closeout	Repair - Accelerated	DBB	Daedalus Projects Inc	Habeeb & Associates Architects, Inc.	Northeast Energy Control Systems	Russo Barr Associates, Inc.
200902580305G	Salem	Collins Middle School	Project Completion	Repair - Accelerated	CM@R	KV Associates, Inc.	Reinhardt Associates, Inc.	Gilbane Building Company	Rist-Frost-Shumway Engineering, P.C.
201002580050G	Salem	Saltonstall School	Project Completion	Repair - Accelerated	CM@R	KV Associates, Inc.	Reinhardt Associates, Inc.	Gilbane Building Company	Rist-Frost-Shumway Engineering, P.C.
201102610010G	Sandwich	Forestdale	Closeout	Repair - Accelerated	DBB	NETCO Construction Project Managers, Inc.	Habeeb & Associates Architects, Inc.	Varieka Construction, Inc.	Gale Associates, Inc.
200902610025G	Sandwich	Oak Ridge School	Closeout	Repair - Accelerated	DBB	NETCO Construction Project Managers, Inc.	Habeeb & Associates Architects, Inc.	J.J. Cardosi, Inc.	Gale Associates, Inc.
201002620305	Saugus	Belmonte Middle School	Closeout	Repair - Major	CM@R	Skanska USA Building, Inc	Fletcher Thompson Architecture Engineering, LLC	Consigli Construction Company, Inc.	Consulting Engineering Services, LLC
201202640305	Scituate	Gates Intermediate School	Feasibility Study			Daedalus Projects Inc	Dore & Whittier Architects, Inc.	-	-
200802660305	Sharon	Sharon Middle School	Closeout	Addition / Renovation	CM@R	Daedalus Projects Inc	Kaestle Boos Associates, Inc.	Consigli Construction Company, Inc.	Horizon Engineering Associates, LLP
201208710605	Shawsheen Valley Voc Tech	Shawsheen Valley Voc Tech High School	Closeout	Repair - Accelerated		Diversified Project Management	Shekar & Associates, Inc.	NB Kenney Company, Inc	Fitzmeyer & Tocchi Associates, Inc.
200802710305	Shrewsbury	Sherwood Middle School	Project Completion	New Construction	CM@R	PMA Construction Services	Lamoureux Pagano & Associates, Inc.	Gilbane Building Company	RDK Engineers
201102710035G	Shrewsbury	Spring Street	Closeout	Repair - Accelerated	DBB	PMA Construction Services	Habeeb & Associates Architects, Inc.	Lambrian Construction Corp.	Cannon Design
201308290605	So Middlesex Voc Tech Reg	Joseph P Keefe Tech HS	Approved Project Vote Pending	Repair - Accelerated		PMA Construction Services	Raymond Design Associates, Inc.	-	Russo Barr Associates, Inc.
20081119999	Somerset-Berkley	Somerset-Berkley High	Construction	New Construction - Model School	DBB	Skanska USA Building, Inc	Ai3 Architects LLC	Bacon-Agostini Construction Joint Venture	Horizon Engineering Associates, LLP
200902740111E	Somerville	East Somerville Community School at Cummings	Closeout	Addition / Renovation	CM@R	PMA Construction Services	Maguire Group Inc.	Gilbane Building Company	Foreman Building Commissioning, LP
201302740505	Somerville	Somerville High	Eligibility Period			-	-	-	-
200902780015	South Hadley	Plains School	Design Development	New Construction		Arcadis U.S., Inc.	Margo Jones Architects, Inc.	-	Strategic Building Solutions, LLC
201202750005	Southampton	William E Norris	Construction	Repair - Accelerated		Tishman Construction Corporation of MA	Reinhardt Associates, Inc.	Greenwood Industries, Inc.	Building Enclosure Associates, LLC

200802770505	Southbridge	Southbridge High School	Closeout	New Construction	CM@R	Joslin, Lesser + Associates Inc.	Tappe Associates, Inc.	Consigli Construction Company, Inc.	Environmental Health and Engineering
200908720605	Southeastern Reg Voc Tech	Southeastern Regional Vocational Technical School	Project Completion	Addition / Renovation	CM@R	Collaborative Partners f/k/a RF Walsh Collab Ptnrs	Drummeey Rosane Anderson, Inc.	W. T. Rich Company Inc.	RDK Engineers
200908760605	Southern Worcester Cty VT	Bay Path Regional Vocational Technical High School	Construction	Addition / Renovation	CM@R	HEERY	Kaestle Boos Associates, Inc.	Consigli Construction Company, Inc.	RDK Engineers
201107660305	Southwick-Tolland	Powder Mill	Construction	Repair - Major	DBB	Strategic Building Solutions, LLC	JCJ Architecture, PC	PDS Engineering and Construction, Inc.	BVH Integrated Services, P.C.
201107660505	Southwick-Tolland	Southwick-Tolland Regional High	Construction	Addition / Renovation	DBB	Strategic Building Solutions, LLC	JCJ Architecture, PC	Fontaine Brothers, Inc.	BVH Integrated Services, P.C.
200807660010	Southwick-Tolland	Woodland Elementary School	Construction	Addition / Renovation	DBB	Strategic Building Solutions, LLC	JCJ Architecture, PC	PDS Engineering and Construction, Inc.	BVH Integrated Services, P.C.
	Springfield	SCIPP Year 2	Project Completion	Repair - Accelerated	-	-	-	-	Building Enclosure Associates, LLC
	Springfield	SCIPP Year 3	Project Completion	Repair - Accelerated	-	-	-	-	-
201302810310	Springfield	Chestnut Accelerated Middle School	Schematic Design	Repair - Accelerated	-	-	-	-	-
201102810125E	Springfield	Dryden Memorial	Project Completion	Addition / Renovation	CM@R	Arcadis U.S., Inc.	Drummeey Rosane Anderson, Inc.	Morganti/Aquadro & Cerruti	BVH Integrated Services, P.C.
201102810030E	Springfield	Elias Brookings	Construction	New Construction	CM@R	Arcadis U.S., Inc.	Drummeey Rosane Anderson, Inc.	Morganti/Aquadro & Cerruti	BVH Integrated Services, P.C.
W20014137	Springfield	Forest Park Middle School	Project Completion	Addition / Renovation	CM@R	Arcadis U.S., Inc.	Perkins Eastman	Consigli Construction Company, Inc.	Foreman Building Commissioning, LP
201302810530	Springfield	High School/Science-Tech	Design Development	Repair - Accelerated	-	Atlantic Construction and Management, Inc.	CBI Consulting Inc.	-	Building Enclosure Associates, LLC
201302810060	Springfield	Margaret C Ells	Design Development	Repair - Accelerated	-	Atlantic Construction and Management, Inc.	CBI Consulting Inc.	-	Building Enclosure Associates, LLC
W20054428	Springfield	Roger L. Putnam Vocational Technical High School	Closeout	New Construction	CM@R	Pinnacle One, Inc.	Drummeey Rosane Anderson, Inc.	Consigli/Morganti	Strategic Building Solutions, LLC
201302810355	Springfield	South End Middle School	Design Development	Repair - Accelerated	-	Atlantic Construction and Management, Inc.	CBI Consulting Inc.	-	Building Enclosure Associates, LLC
201202810500	Springfield	Springfield Central High	Construction	Addition / Renovation	CM@R	Leftfield, LLC	DINisco Design Partnership, Limited	Morganti/Aquadro & Cerruti	Horizon Engineering Associates, LLP
201302810550	Springfield	Springfield Public Day High School	Design Development	Repair - Accelerated	-	Atlantic Construction and Management, Inc.	CBI Consulting Inc.	-	Building Enclosure Associates, LLC
200902840405	Stoneham	Stoneham Middle School	Construction	Addition / Renovation	CM@R	Joslin, Lesser + Associates Inc.	Tappe Associates, Inc.	Shawmut Design and Construction	RDK Engineers
201302850010	Stoughton	Helen Hansen Elementary	Schematic Design	Repair - Accelerated	-	Collaborative Partners f/k/a RF Walsh Collab Ptnrs	Taylor & Burns, Inc.	-	-
201302850014	Stoughton	Joseph R Dawe Jr Elem	Schematic Design	Repair - Accelerated	-	Collaborative Partners f/k/a RF Walsh Collab Ptnrs	Taylor & Burns, Inc.	-	-
201302850505	Stoughton	Stoughton High	Eligibility Period	-	-	-	-	-	-
201302850020	Stoughton	West Elementary	Schematic Design	Repair - Accelerated	-	Collaborative Partners f/k/a RF Walsh Collab Ptnrs	Taylor & Burns, Inc.	-	-
200802870005	Sturbridge	Burgess Elementary School	Project Completion	Addition / Renovation	DBB	Lamoureux Pagano & Associates, Inc.	Drummeey Rosane Anderson, Inc.	Fontaine Brothers, Inc.	Horizon Engineering Associates, LLP
201202880025	Sudbury	General John Nixon Elem	Closeout	Repair - Accelerated	-	PMA Construction Services	ICON architecture, inc.	Silktown Roofing	Gale Associates, Inc.
200802900305	Sutton	Sutton Middle School	Construction	Addition / Renovation	DBB	Strategic Building Solutions, LLC	Flansburgh Associates, Inc.	TLT Construction Corporation	RDK Engineers
201102910010	Swampscott	Hadley	Project Scope & Budget	-	-	Collaborative Partners f/k/a RF Walsh Collab Ptnrs	Mount Vernon Group Architects, Inc.	-	-

201202930057	Taunton	H H Galligan	Closeout	Repair - Accelerated		Arcadis U.S., Inc.	Knight, Bagge & Anderson, Inc.	Capeway Roofing Systems, Inc.	Gale Associates, Inc.
200802950505	Tewksbury	Tewksbury Memorial High School	Project Completion	New Construction - Model School	DBB	HEERY	Symmes Maini & McKee Associates, Inc.	CTA Ventures	Sebesta Blomberg & Associates, Inc.
201208780605	Tri County	Tri County Reg Voc Tech	Closeout	Repair - Accelerated		Collaborative Partners f/k/a RF Walsh Collab Ptnrs	Ai3 Architects LLC	Federal Construction Corp.	-
201108790605G	Upper Cape Cod Voc Tech	Upper Cape Cod Voc Tech	Final Audit Approved	Repair - Accelerated	DBB	NETCO Construction Project Managers, Inc.	Knight, Bagge & Anderson, Inc.	Modern Glass & Aluminum, Inc.	Gale Associates, Inc.
200803040505	Uxbridge	Uxbridge High	Closeout	New Construction	CM@R	Joslin, Lesser + Associates Inc.	Raymond Design Associates, Inc.	Shawmut Design and Construction	Turner Facilities Management Solutions
200907750305	Wachusett	Mountview Middle School	Design Development	New Construction		Gary Kaczmarek - Town Employee	Lamoureux Pagano & Associates, Inc.	-	Fitzmeyer & Tocci Associates, Inc.
201107750035G	Wachusett	Naquag Elementary	Closeout	Repair - Accelerated	DBB	Strategic Building Solutions, LLC	LPBA/ Architects, Inc.	MDM Engineering	Rist-Frost-Shumway Engineering, P.C.
201107750040G	Wachusett	Paxton Center	Closeout	Repair - Accelerated	DBB	Strategic Building Solutions, LLC	LPBA/ Architects, Inc.	MDM Engineering	Rist-Frost-Shumway Engineering, P.C.
201107750045G	Wachusett	Thomas Prince	Closeout	Repair - Accelerated	DBB	Strategic Building Solutions, LLC	LPBA/ Architects, Inc.	MDM Engineering	Rist-Frost-Shumway Engineering, P.C.
201003050310	Wakefield	Galvin Middle School	Construction	New Construction	CM@R	Joslin, Lesser + Associates Inc.	Tappe Associates, Inc.	Bond Brothers, Inc.	B2Q Associates, Inc.
201303070015	Walpole	Fisher	Schematic Design	Repair - Accelerated		-	-	-	-
201303100505	Wareham	Wareham Senior High	Schematic Design	Repair - Accelerated		Collaborative Partners f/k/a RF Walsh Collab Ptnrs	Tighe & Bond, Inc.	-	-
200803150505	Wayland	Wayland High School	Final Audit Approved	New Construction	CM@R	KV Associates, Inc.	HMFH Architects, Inc.	Shawmut Design and Construction	WSP Flack + Kurtz
201203150305	Wayland	Wayland Middle School	Closeout	Repair - Accelerated		Joslin, Lesser + Associates Inc.	DiMarinisi & Wolfe Architects Urban Designers	Capeway Roofing Systems, Inc.	CBI Consulting Inc.
200903160015	Webster	Park Avenue Elementary School	Construction	New Construction	DBB	Collaborative Partners f/k/a RF Walsh Collab Ptnrs	Dore & Whittier Architects, Inc.	CTA Construction Co., Inc.	Cannon Design
200803170505	Wellesley	Wellesley Senior School	Closeout	New Construction	CM@R	-	Symmes Maini & McKee Associates, Inc.	-	Rist-Frost-Shumway Engineering, P.C.
201303180005	Wellfleet	Wellfleet Elementary	Approved Project Vote Pending	Repair - Accelerated		Architectural Consulting Group, LLC	CSS Architects Incorporated	-	-
201103220005G	West Boylston	Major Edwards Elementary	Closeout	Repair - Accelerated	DBB	URS Corporation	Reinhardt Associates, Inc.	-	Cannon Design
201003230505	West Bridgewater	West Bridgewater Middle-Senior High School	Construction	New Construction	DBB	Strategic Building Solutions, LLC	Flansburgh Associates, Inc.	CTA Construction Co., Inc.	Cannon Design
200903320505	West Springfield	West Springfield High School	Project Completion	New Construction - Model School	DBB	Strategic Building Solutions, LLC	Symmes Maini & McKee Associates, Inc.	Fontaine Brothers, Inc.	Turner Facilities Management Solutions
200903210305	Westborough	Gibbons Middle School	Feasibility Study			HEERY	Habeeb & Associates Architects, Inc.	-	-
200903250020	Westfield	Abner Gibbs Elementary School	Construction	New Construction - Model School	DBB	Skanska USA Building, Inc	Margo Jones Architects, Inc.	Fontaine Brothers, Inc.	Horizon Engineering Associates, LLP
201003250025G	Westfield	Highland	Final Audit Approved	Repair - Accelerated	DBB	-	-	-	Strategic Building Solutions, LLC
201103250033E	Westfield	Munger Hill	Closeout	Repair - Accelerated		Vertex Construction Services	Knight, Bagge & Anderson, Inc.	Allied Restoration Corporation	Building Enclosure Associates, LLC
201103250036G	Westfield	Paper Mill	Final Audit Approved	Repair - Accelerated	DBB	-	Tighe & Bond, Inc.	-	Strategic Building Solutions, LLC
201203250036	Westfield	Paper Mill	Closeout	Repair - Accelerated		Vertex Construction Services	Knight, Bagge & Anderson, Inc.	R & H Roofing, LLP	Building Enclosure Associates, LLC

2011003250040G	Westfield	Southampton Road	Final Audit Approved	Repair - Accelerated	DBB	-	-	-	Strategic Building Solutions, LLC Strategic Building Solutions, LLC
201103250505G	Westfield	Westfield High	Final Audit Approved	Repair - Accelerated	DBB	-	Tighe & Bond, Inc.	-	Strategic Building Solutions, LLC
201103250605G	Westfield	Westfield Voc Tech High	Final Audit Approved	Repair - Accelerated	DBB	-	-	-	Strategic Building Solutions, LLC
201303260025	Westford	Col John Robinson	Schematic Design	Repair - Accelerated			Strategic Building Solutions, LLC	Gale Associates, Inc.	-
201303260007	Westford	Day Elementary	Schematic Design	Repair - Accelerated			Strategic Building Solutions, LLC	Gale Associates, Inc.	-
201303270005	Westhampton	Westhampton Elem School	Design Development	Repair - Accelerated			Atlantic Construction and Management, Inc.	CSS Architects Incorporated	-
200903300012	Weston	Field Elementary School	Construction	New Construction	DBB		Compass Project Management, Inc.	Jonathan Levi Architects LLC	Colantonio, Inc.
201103300505G	Weston	Weston High	Final Audit Approved	Repair - Accelerated	DBB		Compass Project Management, Inc.	Garcia Galuska DeSousa Consulting Engineers Inc.	-
201103310015G	Westport	Alice A Macomber	Final Audit Approved	Repair - Accelerated	DBB		Pinck & Co., Inc.	CGKV Architects, Inc.	-
201103310505G	Westport	Westport High	Final Audit Approved	Repair - Accelerated	DBB		Pinck & Co., Inc.	CGKV Architects, Inc.	-
201203360080	Weymouth	William Seach	Closeout	Repair - Accelerated			PMA Construction Services	BLW Engineers, Inc.	Multitemp Mechanical Corporation
200907800025	Whitman-Hanson	Maquan Elementary School	Approved Project Vote Pending	New Construction			Knight, Bagge & Anderson Inc.	Turowski2 Architecture, Inc.	-
200803400005	Williamsburg	Anne T. Dunphy School	Construction	Addition / Renovation	DBB		Arcadis U.S., Inc.	Drummeys Rosane Anderson, Inc.	Enfield Builders, Inc.
201203420060	Wilmington	North Intermediate	Construction	Repair - Accelerated			Diversified Project Management	-	-
200903420505	Wilmington	Wilmington High School	Construction	New Construction	CM@R		Joslin, Lesser + Associates Inc.	Dore & Whittier Architects, Inc.	Gilbane Building Company
200803440025	Winchester	Vinson-Owen Elementary School	Project Completion	New Construction	DBB		Skanska USA Building, Inc	Tappe Associates, Inc.	CTA Construction Co., Inc.
201003440505	Winchester	Winchester High School	Design Development	Addition / Renovation			Skanska USA Building, Inc	Symmes Maini & McKee Associates, Inc.	-
200803460505	Winthrop	Winthrop High School	Design Development				Skanska USA Building, Inc	HMFH Architects, Inc.	-
200803470015	Woburn	Goodyear School	Final Audit Approved	New Construction	CM@R		Municipal Building Consultants, Inc.	Tappe Associates, Inc.	-
201203470060	Woburn	Wyman	Designer Selection				Municipal Building Consultants, Inc.	-	-
201203480052	Worcester	Chandler Magnet	Construction	Repair - Accelerated			Tishman Construction Corporation of MA	Turowski2 Architecture, Inc.	J.J. Cardosi, Inc.
201303480060	Worcester	Columbus Park	Approved Project Vote Pending	Repair - Accelerated			Architectural Consulting Group, LLC	The S/L/A/M Collaborative	-
201203488099	Worcester	Dr. James Caradonio Center	Construction	Repair - Accelerated			Tishman Construction Corporation of MA	Turowski2 Architecture, Inc.	CAM HVAC & Construction, Inc.
201203480140	Worcester	Jacob Hiatt Magnet	Project Completion	Repair - Accelerated			Tishman Construction Corporation of MA	Turowski2 Architecture, Inc.	CAM HVAC & Construction, Inc.
201203480145	Worcester	Lake View	Construction	Repair - Accelerated			Tishman Construction Corporation of MA	Turowski2 Architecture, Inc.	J.J. Cardosi, Inc.
201203480175	Worcester	May Street	Construction	Repair - Accelerated			Tishman Construction Corporation of MA	Turowski2 Architecture, Inc.	J.J. Cardosi, Inc.
201203480200	Worcester	Nelson Place	Feasibility Study				Tishman Construction Corporation of MA	Lamoureux Pagano & Associates, Inc.	-

W20004048	Worcester	North High School	Closeout	New Construction	CM@R	-	-	-	-
201303480230	Worcester	Tatnuck	Approved Project Vote Pending	Repair - Accelerated		Architectural Consulting Group, LLC	The S/L/A/M Collaborative	-	Russo Barr Associates, Inc.
201303480225	Worcester	Worcester Arts Magnet Sch	Approved Project Vote Pending	Repair - Accelerated		Architectural Consulting Group, LLC	The S/L/A/M Collaborative	-	Russo Barr Associates, Inc.
201303480420	Worcester	Worcester East Middle	Approved Project Vote Pending	Repair - Accelerated		Architectural Consulting Group, LLC	The S/L/A/M Collaborative	-	-

2014 Estimated Bid Dates

Note bid dates are **Estimates ONLY**. Please contact Districts for exact information.

Total Project Budget denotes total District costs and does not denote the basis of the MSBA Total Facilities Grant.

■ - Denotes bid phase in progress or complete
 ■ - Denotes estimated bid dates
 ■ - Denotes estimated GMP dates

DISTRICT <small>*Projects Considering the CM @ Risk Method</small>	DESIGN BASIS FOR ENROLLMENT	PROJECT BUDGET <small>Shown in Millions</small>	CONSTRUCTION BUDGET <small>Shown in Millions</small>	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC
*AYER SHIRLEY RSD	495	\$56.5	\$44.4	■				■ Ayer Shirley RHS - Addition/Renovation: Filed-Sub Bids Due 9/25. GMP Targeted March.							
REVERE	690	\$44.4	\$33.9	■				Staff Sergeant James J. Hill (McKinley) ES - New Construction: Filed-Sub Bids recieved 1/14. G.C. Bids recieved 1/23. NTP Targeted March.							
NORTH ADAMS	310	\$29.7	\$21.9	■				Silvio O. Conte MS - New Construction: Filed-Sub Bids recieved 2/24. G.C. Bids recieved 3/6. NTP Targeted March.							
*GREATER LOWELL RVTSD	1990	\$65.3	\$53.2	■				■ Greater Lowell RVTHS - Repair: Filed-Sub Bids recieved 2/21. GMP Targeted March.							
*AUBURN	560	\$44.5	\$35.5	■				■ Auburn MS - New Construction: Filed-Sub Bids Due 3/31. GMP Targeted April.							
WACHUSETT RSD	800	\$54.3	\$43.1	■				■ Mountview MS - New Construction: Filed-Sub Bids Due 4/10. G.C. Bids Due 4/24. NTP Targeted May.							
CHICOPEE	850	\$38.0	\$30.8	■				■ Chicopee Academy - Renovation: Filed-Sub Bids Due 4/23. GMP Targeted June.							
SOUTH HADLEY	270	\$28.2	\$21.6	■				■ Plains ES - New Construction: Filed-Sub Bids Due 4/3. G.C. Bids Due 4/17. NTP Targeted April.							
PEABODY	1340	\$92.6	\$75.1	■				■ Higgins MS - New Construction: Filed-Sub Bids Due 5/15. G.C. Bids Due 5/27. NTP Targeted June.							
GREATER LAWRENCE RVTSD	1400	\$5.2	\$4.4	■				■ Greater Lawrence RVTHS - Repair: Filed-Sub Bids Due 4/30. G.C. Bids Due 5/7. NTP Targeted June.							
*LYNN	1100	\$92.0	\$67.7	■				■ Thurgood Marshall MS - New Construction: Filed-Sub Bids Due 9/26. GMP Targeted October. ■							
*NEWTON	465	\$37.5	\$26.2	■				■ Angier ES - New Construction: Filed-Sub Bids Due 10/6. GMP Targeted October. ■							
ATHOL-ROYALSTON RSD	545	\$43.9	\$35.2	■				■ Riverbend ES - New Construction: Filed-Sub Bids Due 10/15. G.C. Bids Due 10/31. NTP Targeted November. ■							
Subtotal	10,815	\$632.1	\$493.0												
GRAND TOTAL	10,815	\$632.1	\$493.0												

2015 Estimated Bid Dates

Note bid dates are **Estimates ONLY**. Please contact Districts for exact information.

Total Project Budget denotes total District costs and does not denote the basis of the MSBA Total Facilities Grant.

■ - Denotes bid phase in progress or complete
 ■ - Denotes estimated bid dates
 ■ - Denotes estimated GMP dates

DISTRICT <small>*Projects Considering the CM @ Risk Method</small>	DESIGN BASIS FOR ENROLLMENT	PROJECT BUDGET <small>Shown in Millions</small>	CONSTRUCTION BUDGET <small>Shown in Millions</small>	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC
*WINTHROP	970	\$80.2	\$61.9				Winthrop MS/HS - New Construction: Filed-Sub Bids Due 2/25. GMP Targeted April.								
Subtotal	970	\$80.2	\$61.9												
GRAND TOTAL	970	\$80.2	\$61.9												

**Projects in Construction
MSBA Grant Basis and Estimated Maximum Grant Amount
Data Reported as of March 5, 2014**

New Program and Wait List Program Totals			\$2,653,141,931	55,812		10,915,397											*Includes Alternates	\$1,755,149,795		
Project	Grade	Contractor	Total Construction Cost*	Projected Enroll	PFA or Bid Data	Proposed Square Footage	Construction Cost per Square Foot	Building Cost	Building Cost per Square Foot	Project Type	Construction Start	Estimated Substantial Completion Date	Reporting Variance from Schedule	Physical Progress (%)	Change Orders (%)	Construction Status	Estimated Maximum Total Facilities Grant *			
CAPITAL PIPELINE PROJECTS IN CONSTRUCTION																				
New Program Totals			\$2,650,558,033	55,152		10,766,597	\$258		\$193											\$1,700,352,018
Arlington	K-5	G&R Construction	\$15,340,026	380	Bid	57,614	\$266	\$12,403,811	\$215	Design/Bid/Build	7-Apr-12	21-Aug-13		100%	3.09%	The new school building is in service. Roof IR scan to be performed when weather conditions permit. Final site work is complete except minor work to be completed in the Spring of 2014.	\$8,996,284			
Assabet Valley Reg Voc Tech	9-12	CTA Construction, Inc.	\$46,764,740	963	Bid	367,565	\$127	\$41,523,764	\$113	Design/Bid/Build	1-Apr-13	1-Aug-15		32%	0.06%	This is a (10) phase project. Phase 1 ,2 and 3 are complete other than punch list items in Phase 2 and 3. Work includes demo of ceiling tiles, demo of the Mechanical Room, HVAC work and abatement, MEP work, windows, roofing, flooring and painting for these areas. Certificate of Occupancy for Phase 2 was received which allowed students and staff back into the building in that location. Phase 4 began on December 1st, 2013 and is scheduled for completion in March of 2014.	\$28,790,301			
Berlin-Boylston Tahanto Reg MS/HS	6-12	CTA	\$32,162,000	560	Bid	126,100	\$255	24,629,999	\$195	Design/Bid/Build	10-May-11	1-Jul-13		99%	3.19%	The new school building is in service. Resolution of punch list and Commissioning Consultant action items are in process. Final site work is complete except minor work to be completed in the Spring of 2014. Installation of ceramic tile is planned to replace the blue stone exterior at the front entrance facade that was removed due to performance issues.	\$18,717,193			
Danvers Danvers HS	9-12	Bacon Construction	\$53,834,164	1,000	Bid	246,251	\$219	\$43,710,809	\$178	Design/Bid/Build	14-Nov-10	10-Jul-13		100%	2.51%	Project closeout is in process.	\$34,409,979			
Douglas Douglas ES	2-5	CTA	\$24,275,111	552	Bid	83,100	\$292	\$19,026,763	\$229	Design/Bid/Build	Mar-12	26-Aug-13		99%	0.00%	Punch list is being completed during off hours while school is in session.	\$17,611,449			
Douglas Douglas IS	6-8	CTA	\$12,081,767	448	Bid	88,245	\$137	\$9,417,212	\$107	Design/Bid/Build	Mar-12	1-Jul-14		85%	1.99%	Site, demo, concrete, masonry, steel, roof, windows and interior glass partitions are complete. Interior finishes are ongoing. MEP/FP finishes are ongoing.	\$7,170,485			
Dracut Dracut HS	9-12	CTA	\$45,900,000	1,160	Bid	226,844	\$202	\$38,377,028	\$169	Design/Bid/Build	27-Aug-12	26-Aug-14		58%	0.66%	OPM reports the project did not meet the February interim milestone schedule. The overall schedule is being evaluated. Structural work for Phase II continues in the Auditorium area as well as plumbing and miscellaneous work in the Cafeteria and finishes in the new classrooms.	\$35,838,072			
East Bridgewater E. Bridgewater Jr/Sr HS	7-12	Fontaine Brothers	\$65,409,000	950	Bid	213,544	\$306	\$47,684,117	\$223	Design/Bid/Build	10-Aug-11	16-Aug-13		95%	2.77%	The school has been turned over to the District and opened in September. Abatement is completed and demolition of the existing HS is nearly complete. Field work to resume in the Spring of 2014.	\$43,317,092			
Easthampton Easthampton HS	9-12	Fontaine Brothers	\$30,934,000	510	Bid	110,400	\$280	\$24,511,000	\$222	Design/Bid/Build	16-May-11	19-Feb-13		99%	2.70%	Remaining work consists of warranty items and commissioning completion including the infrared scan which will be scheduled when the roof is clear of snow. Project closeout will follow.	\$22,859,504			
Fairhaven Rogers ES	K-5	CTA	\$19,099,606	370	Bid	77,871	\$245	\$14,996,521	\$193	Design/Bid/Build	21-May-12	26-Jun-13		100%	0.97%	The new school building is in service. All punch list work is complete. Resolution of Commissioning Consultant action items is in process. Final site work is complete except minor work to be completed in the Spring of 2014.	\$13,431,486			
Fall River Morton MS	6-8	J&J Contractors	\$37,654,000	625	Bid	130,576	\$288	\$29,921,971	\$229	Design/Bid/Build	4-Nov-11	15-Jul-13		99%	13.29%	Building is substantially complete. Minor punch list work remaining.	\$38,251,808			
Franklin Franklin HS	9 - 12	Agostini/Bacon	\$86,778,700	1,650	Bid	306,543	\$283	\$73,191,801	\$238.77	Design/Bid/Build	16-Oct-12	25-Jul-14		75%	0.60%	Exterior envelope nearing completion with the exception of storefront installation. Interior finishes progressing on the 2nd and 3rd floors with plaster, painting, ceiling grid installations, and bathroom tile complete; 1st floor progress is behind the upper floors. HVAC, plumbing, and electrical work progressing throughout the building.	\$54,558,408			
Georgetown Penn Brook ES	K-6	Brait Builders Corp.	\$36,979,465	770	PFA	98,000	\$377	\$18,735,796	\$191.18	Design/Bid/Build	26-Sep-13	20-May-16		12%	0.00%	Foundations and steel being installed.	\$20,348,437			
Greater New Bedford Regional Voc Tech HS	8-12	Agostini	\$12,181,500	2,060	Bid	487,530	\$25	\$10,757,696	\$22	Design/Bid/Build	13-Sep-13	19-Dec-14		13%	1.14%	Foundations are complete and structural steel is being erected. Underground plumbing and electrical is in process.	\$12,736,352			
Hingham Hingham MS	6-8	Brait Builders Corp.	\$48,436,000	1,020	Bid	176,385	\$275	\$41,227,552	\$234	Design/Bid/Build	7-Jun-12	30-Dec-14		90%	0.26%	Finish work continues throughout the building. FFE scheduled for delivery in April of 2014.	\$25,909,580			
Hudson John F Kennedy MS	5-7	Agostini/Bacon	\$35,102,573	715	Bid	118,846	\$295	\$28,373,294	\$239	Design/Bid/Build	28-Sep-11	22-Jun-13		99%	2.92%	The project is complete with the exception of minor site work which will be completed in the Spring.	\$22,932,938			
Lynnfield Lynnfield HS	9-12	E.A. Colangeli	\$3,110,346	740	Bid	10,950	\$284	\$2,322,687	\$212	Design/Bid/Build	25-Jun-12	28-Jun-13		99%	8.98%	Minor punch list work remaining.	\$1,828,473			
Marblehead Glover ES	K-3	G&R Construction	\$20,868,000	425	Bid	79,108	\$264	\$16,977,513	\$215	Design/Bid/Build	25-Jun-12	20-Dec-13	28 days	98%	3.13%	Building is complete with the exception of punch list items and Commissioning Consultant action items. Final site work will be completed in the Spring of 2014.	\$8,759,441			
Marshfield High School	9 - 12	Brait Brothers	\$84,980,000	1,310	Bid	267,469	\$318	\$64,604,850	\$242	Design/Bid/Build	16-Aug-12	25-Jul-14	30 days ahead	87%	0.70%	Finish work is well underway, equipment installation beginning in the kitchen and gym, auditorium seating installation nearing completion. Project is trending for early substantial completion in advance of the July 25, 2014 contract date.	\$46,550,599			
Maynard Maynard HS	8-12	CTA	\$36,650,000	410	Bid	121,520	\$302	\$30,630,013	\$252	Design/Bid/Build	18-Aug-11	13-Dec-13		100%	0.85%	Punch list work and commissioning activities are being completed.	\$22,095,036			
Monomoy Regional High School	9-12	Fontaine Brothers	\$49,374,000	700	Bid	168,000	\$294	\$41,433,695	\$247	Design/Bid/Build	11-Feb-13	30-Jun-14		65%	0.32%	Exterior masonry, roofing and window installations are nearing completion. Wall tile finishes are underway in the bathrooms. Interior priming and painting is in progress in the academic areas. Interior masonry wall block installation has commenced in the cafeteria and servery.	\$27,654,507			
Newburyport Bresnahan ES	PK-3	CTA Construction, Inc.	\$28,190,000	660	Bid	112,517	\$251	\$20,842,000	\$185	Design/Bid/Build	14-Mar-13	30-Jun-14	45 days	70%	0.00%	Building envelope is complete except the exterior storefront construction. Metal stud and drywall as well as MEP rough-ins are complete. Temporary heat is being utilized. Interior finishes are ongoing, as well as Commissioning.	\$15,676,427			
Norfolk County Agricultural HS	9-12	Brait Builders. Terminated TLT Construction Corp. 12/26/2013.	\$21,508,952	550	Bid	114,816	\$187	\$15,546,739	\$135	Design/Bid/Build	29-Mar-12	9-May-14	21 days	77%	2.61%	Phase 1: Animal Science Building, Agricultural Mechanical Building, Equine Center, and Equipment Garage are substantially complete. Phase 3: Site work is substantially complete. Phase 2: Replacement General Contractor Brait Builders mobilized and started to coordinate Phase 2 work. OPM reports that Phase 2 completion is estimated to be by the end of May 2014; however, the estimate is dependent on the efficiency of the Surety in ratifying subcontractors.	\$13,493,272			
Norfolk Freeman-Kennedy ES	3-6	Fontaine Brothers	\$25,354,966	585	Bid	96,410	\$263	\$20,023,001	\$208	Design/Bid/Build	9-Nov-10	13-Aug-12		98%	6.00%	The new building is complete and currently in use. Minor punch list items are ongoing.	\$15,861,760			
Oxford Oxford MS	5-8	S.O.M./ J.J. Cardosi/ R.A.C. Builders	\$5,085,217	652	Bid	117,000	\$43	\$5,085,217	\$43	Design/Bid/Build	1-Jun-12	30-Aug-14		45%	2.37%	Roof replacement completed in the Summer of 2012. Window project completed in the Summer of 2013. HVAC/ADA/flooring contract has been awarded. General Contractor started limited demolition on February 18, 2014.	\$3,369,847			
Plymouth Plymouth HS	9-12	J&J Contractors	\$67,687,000	1,350	Bid	267,497	\$253	\$51,579,703	\$193	Design/Bid/Build	3-May-10	22-Jun-12		99%	6.86%	Irrigation of the new ball field to be completed and commissioning in the Spring of 2014.	\$41,810,972			
Quincy Central MS	6-8	H.V. Collins Co. Inc.	\$32,540,712	620	Bid	114,975	\$283	\$27,057,118	\$235	Design/Bid/Build	18-Jun-12	5-Sep-13		98%	1.97%	Commissioning and punch list work are ongoing. The Auditorium is nearing completion. Substantial Completion and Certificate of Occupancy received October 18, 2013. School opened for classes on October 21, 2013. Site retaining wall will be completed in the Spring.	\$29,726,120			
Revere SS James J. Hill ES	PK-5	CTA	\$33,897,336	690	PFA	103,650	\$327	\$26,943,250	\$260	Design/Bid/Build	18-Feb-14	16-Jun-15		0%	0.00%	Notice to Proceed issued February 18, 2014.	\$28,099,048			
Somerset Berkley Somerset Berkley RHS	9-12	Bacon-Agostini	\$69,407,000	1,000	Bid	222,826	\$311	\$52,553,676	\$236	Design/Bid/Build	16-Jul-12	20-Jun-14		75%	0.61%	Finish work ongoing in the 2nd and 3rd floors of the academic wing including lighting and ceiling grids. Construction also progressing in the auditorium/stage and adjacent areas, interior masonry in the gym and locker room areas. Exterior installation of storefront, curtain wall, and trim proceeding when weather is permitting.	\$46,722,150			
Southwick-Tolland-Granville Regional HS	7-12	Fontaine Brothers	\$31,408,667	790	PFA	165,995	\$189	\$21,298,500	\$128	Design/Bid/Build	5-Aug-13	18-Sep-15		19%	0.40%	Metal framing and exterior sheathing are complete at the Middle School addition with MEP rough-ins underway. Roofing has started at both Middle School and High School additions and continues weather permitting. Structural steel is complete at the High School addition with the exception of the west connector which is being left open for access to the courtyard. Metal framing of exterior walls are just beginning at the High School addition. Sewer and sanitary work outside the High School addition is largely complete.	\$19,572,669			
Southwick-Tolland-Granville Powder Mill IS	3-6	PDS Engineering	\$14,747,586	545	PFA	95,775	\$154	\$10,420,350	\$109	Design/Bid/Build	7-Jun-13	14-Aug-15		23%	0.08%	No work was scheduled during this school year. However, work is expected to start early in the Summer of 2014 to prepare some of the electrical and mechanical scope for the upcoming school year. The new primary electric conduits, transformer pad, and secondary conduits have been installed with the new switchgear in place. Electrical feeders have been run in corridors. Installation of the new boilers and related equipment is currently underway while tie-ins will begin after the heating season.	\$8,437,002			
Southwick-Tolland-Granville Woodland ES	PK-2	PDS Engineering	\$7,328,004	400	PFA	67,800	\$108	\$5,218,390	\$77	Design/Bid/Build	7-Jun-13	14-Aug-15		49%	0.12%	Phase 3 (West wing) of Woodland School is under construction. Demolition, abatement, and underground plumbing has been completed. MEP rough-in is well underway as well as the installation of windows. Work in Phase 3 is scheduled to be substantially complete by May 30, 2014. Window installation for Phase 2, which was originally scheduled for the Fall of 2013, will be completed during the April school vacation week.	\$4,620,410			
Sturbridge Burgess ES	K-6	Fontaine Brothers	\$22,946,000	860	Bid	131,630	\$174	\$17,591,000	\$134	Design/Bid/Build	10-Aug-10	31-Oct-12		100%	8.57%	The new school building addition and the adjacent existing school building renovation are complete and in service. The OPM's and Contractor's independent consultants have completed an investigation of a rubber floor tile adhesion failure in the Cafeteria and Band Room which are located in the renovated building. Reports are currently under review. Failure of one Roof Top Unit (RTU) to restart after power loss, as required, is being investigated to determine a resolution.	\$14,764,380			
Sutton MS/HS	6-12	TLT Construction Corp.	\$41,230,800	840	Bid	179,040	\$230	\$32,998,403	\$184	Design/Bid/Build	1-Jul-11	31-Dec-14	240 days	73%	2.67%	Commencement of construction work is pending mobilization of the new general contractor.	\$25,646,928			
Tewksbury Tewksbury HS	9-12	CTA/Methuen Construction Co.	\$51,600,000	1,100	Bid	218,781	\$236	\$40,159,651	\$184	Design/Bid/Build	15-Oct-10	3-Aug-12		99%	5.28%	The rubberized running track and tennis courts will be completed in the Spring of 2014.	\$36,622,570			

Projects in Construction
MSBA Grant Basis and Estimated Maximum Grant Amount
Data Reported as of March 5, 2014

Project	Grade	Contractor	Total Construction Cost*	Projected Enroll	PFA or Bid Data	Proposed Square Footage	Construction Cost per Square Foot	Building Cost	Building Cost per Square Foot	Project Type	Construction Start	Estimated Substantial Completion Date	Reporting Variance from Schedule	Physical Progress (%)	Change Orders (%)	Construction Status	Estimated Maximum Total Facilities Grant *
Webster Park Ave Elem School	PK-4	CTA Construction, Inc.	\$32,370,000	720	Bid	109,597	\$295	\$24,910,914	\$227	Design/Bid/Build	8-Jul-13	12-Dec-14	11 Days	37%	-0.01%	Steel erection is complete and installation of roof and fascia has commenced. Ongoing work includes installation of slabs-on-grade and elevated slabs, installation of exterior metal wall framing, sheathing/air-vapor barrier, window blocking, interior partitions, and rough mechanical, electrical and plumbing work.	\$28,102,666
Westfield Abner Gibbs ES	K-5	Fontaine Brothers	\$25,578,000	600	Bid	95,573	\$268	\$21,444,000	\$224	Design/Bid/Build	24-Aug-12	25-Mar-14		7%	0.00%	Work stoppage regarding Article 97 "Protected Land". The City still does not have approval. General Contractor has demobilized from the site.	\$20,004,642
West Bridgewater	7-12	CTA Construction, Inc.	\$49,728,000	625	PFA	141,250	\$352	\$49,727,766	\$352	Design/Bid/Build	1-Oct-13	15-Jun-15		10%	0.00%	Demolition of the existing athletic fields and courts are complete. Top soil has been stripped and stockpiled on site. Foundations complete. Structural steel erection ongoing.	\$27,015,896
West Springfield West Springfield HS	9-12	Fontaine Brothers	\$85,006,020	1,270	Bid	257,525	\$330	\$56,875,181	\$221	Design/Bid/Build	22-Nov-11	31-Dec-13		93%	2.18%	Students occupied the new High School after February vacation. Abatement of the existing building has begun. Minor punch list remains.	\$68,808,290
Weston Field ES	4-5	Colantonio	\$24,537,966	355	Bid	65,390	\$375	\$19,872,289	\$304	Design/Bid/Build	21-Dec-12	19-Jun-14	25 days	76%	2.67%	Roof work is mostly complete. Windows are approximately 90% complete. The Mechanical Room has been completely framed and the boiler, hot water heater and pump have all been installed. Sprinkler work is complete. Duct work and electrical are approximately 90% complete. Dry wall and ceiling painting have begun in several classrooms. The building is currently weather tight.	\$8,004,886
Williamsburg Anne T. Dunphy ES	PK-6	Enfield	\$8,990,457	170	Bid	37,859	\$237	\$7,625,327	\$201	Design/Bid/Build	5-Apr-13	7-Apr-14	30 days	70%	2.45%	Demo and abatement are complete. Building "A" structural steel is complete. Building envelope is enclosed. Metal studs, drywall and MEP/FP rough-ins are ongoing. Building "B" building envelope is complete. Temp heat is in place. Interior finishes and MEP/FP finish are underway. Earth work and underground utilities are ongoing.	\$6,808,088
Winchester Vinson-Owen ES	K-5	CTA	\$21,290,000	420	Bid	74,820	\$285	17,767,598	\$237	Design/Bid/Build	17-Feb-12	26-Jul-13		99%	2.22%	Punch list work is nearing completion and being performed after school hours. Site work items are scheduled to be completed during the April 2014 vacation, weather permitting.	\$9,812,209
Andover Bancroft ES	K-5	Skanska	\$44,077,007	680	Bid	106,904	\$412	27,101,717	\$254	CM-R	14-May-12	22-May-14		80%	0.31%	Phenolic siding installation is nearly complete on the building exterior. Final finishes are underway in classroom wings. Millwork, casework, and door & hardware installations are in progress. Ceiling grid and light fixtures are being installed. Commissioning of the mechanical systems is being coordinated.	\$15,731,353
Auburn Middle School	6-8	Fontaine Brothers	\$35,474,676	560	PFA	100,395	\$353	\$23,350,958	\$233	CM-R	27-Feb-14	5-Jun-15		0%	0.00%	Early sitework package was released with concrete and steel packages to follow.	\$33,721,125
Ayer-Shirley Reg HS	9-12	Consigli	\$44,372,576	495	PFA	144,072	\$308	\$27,797,209	\$193	CM-R	19-Feb-13	26-Aug-15		17%	0.00%	Phase 1A, swing space prep, is complete and in use. Phase 1B, construction of the new classroom wing, is underway. The roof is in place, exterior sheathing is installed, and the building is temporarily enclosed with temp heat operational. Concrete slabs-on-grade and slabs-on-deck are complete. Metal stud framing, drywall, and MEP rough-ins are underway. Steel erection is in progress for Phase 1C band/chorus renovation/addition. Utility work continues in the new mechanical room.	\$34,926,694
Ashburnham Westminster JR Briggs ES	PK-5	Consigli	\$24,780,000	520	Bid	87,085	\$285	18,202,478	\$209	CM-R	9-Mar-12	1-Aug-13		100%	0.24%	The new school building is in service. Resolution of punch list and Commissioning Consultant action items is in process. Final site work is complete except minor work to be completed in the Spring of 2014.	\$16,187,237
Concord-Carlisle HS	9-12	Turner Construction	\$76,143,000	1,225	PFA	219,871	\$346	\$47,562,547	\$216	CM-R	20-Feb-13	15-Mar-15		25%	2.22%	Foundations, structural steel and slabs are complete. Roof and exterior walls are 50% complete. Building enclosed with temp heat running. Interior framing at 25%. MEP/FP rough-ins are at 15%. Building site work (Phase I) is 90% complete.	\$27,098,682
Duxbury HS	6-12	Dimeo	\$105,475,520	1,735	Bid	325,721	\$324	\$73,368,123	\$225	CM-R	12-Sep-12	3-Jul-14		78%	1.23%	Entire building envelope is approximately 98% complete including curtain walls and windows. Interior drywall is 95% complete. Finish flooring is ongoing. Electrical overhead rough-ins are ongoing. Fireproofing is complete. MEP rough-ins and finish work advancing. Lockers and casework/millwork installation are underway. Building commissioning is ongoing.	\$48,141,830
Essex Technical High School	9-12	Gilbane	\$110,217,451	1,440	Bid	337,000	\$327	\$79,334,889	\$235	CM-R	7-May-12	30-Jun-14		76%	1.52%	The new Animal Barn has been completed. The roof is nearly complete and the siding is half done for the Auto Tech. and Collision Building (Bldg E). Steel erection has recently begun on Building G (Masonry, Landscape & Carpentry). The last section of roof for the Main Academy (Bldg D) is being installed. Flooring is being installed in Buildings A and B on the main and upper levels. Painting continues throughout the Main Academy as well as MEP finishes.	\$72,471,233
Greater Lowell Regional Voc Tech HS	9-12	Consigli	\$53,165,631	1,990	PFA	505,766	\$105	\$36,613,853	\$72	CM-R	2-Oct-13	19-Aug-15		1%	0.00%	Building addition footings and foundations are complete. Structural steel was delivered in February. Misc site activities, including utility layout and steel erection at existing building entrance are ongoing. Early release packages included site, concrete and steel.	\$47,584,652
Greenfield	8-12	Shawmut Design	\$53,507,787	585	Bid	160,649	\$333	\$37,812,150	\$235	CM-R	27-Mar-13	15-Dec-15		40%	-0.31%	Phase 1 work is on schedule for July 31, 2014 Substantial Completion with occupancy in September of 2014. The building exterior is complete except minor finish work and installation. All windows are installed. Roof Top Units will be installed in the Spring of 2014. MEP rough-ins are 90% complete. Wallboard installation is 80% complete and painting of finished areas is in process. Main electrical feeds are installed and switchgear installation is pending receipt of new switch gear.	\$42,194,483
Leominster Leominster SHS	9-12	S.O.M.	\$33,794,797	1,825	Bid	295,859	\$114	\$25,382,707	\$86	CM-R	1-Jul-11	30-Aug-13		100%	7.08%	Remaining punch list work is being completed and project closeout is in process.	\$27,337,956
Lexington Estabrook ES	K-5	Shawmut Design	\$32,838,998	540	Bid	91,840	\$358	\$22,795,606	\$248	CM-R	20-Jun-12	27-Jan-14		84%	1.24%	New building complete and occupied in February. Temporary Certificate of Occupancy received January 22, 2014. Commissioning ongoing and nearing completion. Site work is 50% complete. Phase I demolition is 15% complete. Phase II demo will be ongoing in March.	\$12,148,490
Longmeadow Longmeadow HS	9-12	Gilbane	\$63,685,998	1,000	Bid	236,985	\$269	\$46,573,364	\$197	CM-R	Nov-10	1-Nov-13		99%	2.35%	Remaining punch list work is being completed and project closeout is in process.	\$31,297,686
Methuen Methuen HS	9-12	Terminated Dimeo 12/31/2011. Consigli as of 5/21/2012	\$74,749,773	2,075	Bid	368,017	\$203	\$58,040,746	\$158	CM-R	21-Jul-11	26-Jun-14		85%	2.81%	The Auditorium was turned over at the end of January. Phase II, renovation of the remaining existing High School, including drywall, painting and millwork, have begun.	\$64,503,232
Newburyport Nock MS / Molin ES	Nock MS 6-8 Molin ES 4-5	Gilbane	\$20,877,414	845	Bid	161,500	\$129	\$15,975,491	\$99	CM-R	18-Mar-13	21-Aug-14		65%	3.33%	Phase 3A and 3B work are underway and include mechanical, electrical, plumbing, fire protection, ceiling tile, flooring, lighting and casework installations. Most work is occurring during 2nd shift. Phase 2 punch list work and commissioning continues.	\$12,785,667
North Reading Middle/Senior High School	6-12	Gilbane	\$101,328,363	1,370	Bid	267,939	\$378	\$66,726,592	\$249	CM-R	15-Jan-13	31-Aug-14 (HS) 31-Aug-15 (MS)		44%	0.91%	High School window installation is complete. Finish work is underway in the high school academic wing, including drywall and painting, bathroom tile installation, and ceiling grid installation. Radiator installations are underway and will be placed into service as installed for temporary heating. Masonry construction in the gym area is progressing.	\$47,071,882
Norton Norton HS	9-12	WT Rich	\$27,023,541	700	Bid	162,405	\$166	\$20,590,559	\$127	CM-R	12-Mar-12	31-Jan-14		99%	4.41%	Work on the final phase is complete with only minor punch list work remaining. Temporary occupancy of the Auditorium has been granted. Certificate of Occupancy is pending AAB variance approval. RTU noise issue is being resolved.	\$20,634,829
Rockland John Rogers MS/ HS	5-12	Agostini	\$66,362,037	1,525	Bid	275,700	\$241	\$47,724,091	\$173	CM-R	15-Nov-10	1-Aug-13		99%	6.00%	Minor Spring 2014 site work remaining.	\$49,488,478
Shrewsbury Sherwood MS	5-6	Gilbane	\$33,986,286	900	Bid	129,378	\$263	\$22,823,030	\$176	CM-R	7-Mar-11	31-Oct-12		100%	-3.03%	The new school building is in service. Final site work is complete except minor work to be completed in the Spring of 2014.	\$20,964,674
Southern Worcester Bay Path Voc-Tech	9-12	Consigli	\$58,201,331	1,110	PFA	249,521	\$233	\$33,021,768	\$132	CM-R	2-Aug-13	1-Sep-15		7%	0.00%	Unforeseen asbestos was uncovered by the area where the new addition is to be built which caused some delay. The Contractor has implemented a recovery schedule. No delay has been reported in the overall schedule. Excavation and foundation formwork are ongoing.	\$44,510,177
Southeastern Regional Voc Tech High School	9-12	WT Rich	\$27,200,000	1,370	Bid	308,250	\$88	\$19,996,609	\$65	CM-R	27-Jun-11	9-Sep-13		99%	3.27%	Renovations are complete and the building is in service. Resolution of Commissioning Consultant action items are being addressed.	\$24,659,109
Springfield Elias Brookings ES	PK-5	Morganti Aquadro & Cerruti	\$22,733,394	320	PFA	64,800	\$351	\$15,374,674	\$237	CM-R	1-Jul-13	20-Jan-15		15%	-0.43%	Footing and foundation installations are nearing completion. Subgrade utility work and steel erection is underway.	\$16,448,816
Springfield Dryden ES	PK-5	Morganti Aquadro & Cerruti	\$11,476,091	280	Bid	40,900	\$281	\$8,276,912	\$202	CM-R	28-Jun-12	1-Nov-13		99%	2.37%	Remaining punch list and commissioning work is being completed and project closeout is in process.	\$7,221,300
Stoneham Middle School	5-8	Shawmut Design	\$33,086,864	775	Bid	136,410	\$243	\$21,209,275	\$155	CM-R	1-Nov-12	8-Aug-14		60%	0.29%	Roofing activities are nearly complete, most brick veneer has been placed, metal windows have been installed, air vapor barrier has been applied, and curtain wall system installation is ongoing. Interior mechanical, electrical, plumbing, and fire protection rough-ins are all ongoing.	\$21,346,937
Wakefield	5-8	Bond Brothers	\$59,756,583	1,070	Bid	187,722	\$318	\$44,899,853	\$239	CM-R	18-Mar-13	30-Jun-15		30%	1.39%	Building A windows have been installed on the north side of the building. Masonry continues on the south side. MEP rough-ins on the upper floors are 80-90% complete. Framing is almost complete on the 1st floor and drywall installation will begin shortly. The underground utilities and roofing are in progress for Building B. Structural steel is completed for Building C and installation of decking is in progress.	\$32,631,618
Wilmington	9-12	Gilbane	\$67,558,835	960	Bid	192,443	\$351	\$48,060,314	\$250	CM-R	April 30-13	13-Feb-15		21%	0.00%	Steel work in Area C is complete. Area E is 10% complete and Areas A,B and D are 90% complete. Roofing in Areas A & B is 90% complete. Fireproofing, mechanical rough-ins and ductwork are in progress. Internal masonry work continues at stairways. Interior finish work is ongoing.	\$35,622,158
Wait List Program Totals			\$34,745,898	660		148,800											\$36,080,584
Springfield Forest Park MS	6-8	Consigli	\$34,745,898	660	Bid	148,800	\$234	\$26,209,932	\$176	CM-R	26-Mar-12	1-Aug-13	25 days	99%	2.23%	Remaining punch list work is being completed and project closeout is in process.	\$36,080,584
