


Project Overview Report

June 4, 2014

A total of 341 projects that have received invitations from the Board of Directors (“Board”) to collaborate with the MSBA are currently in the MSBA’s Eligibility Period and Capital Pipeline. The following summary chart provides the number of projects in the Eligibility Period and each phase of the Capital Pipeline:

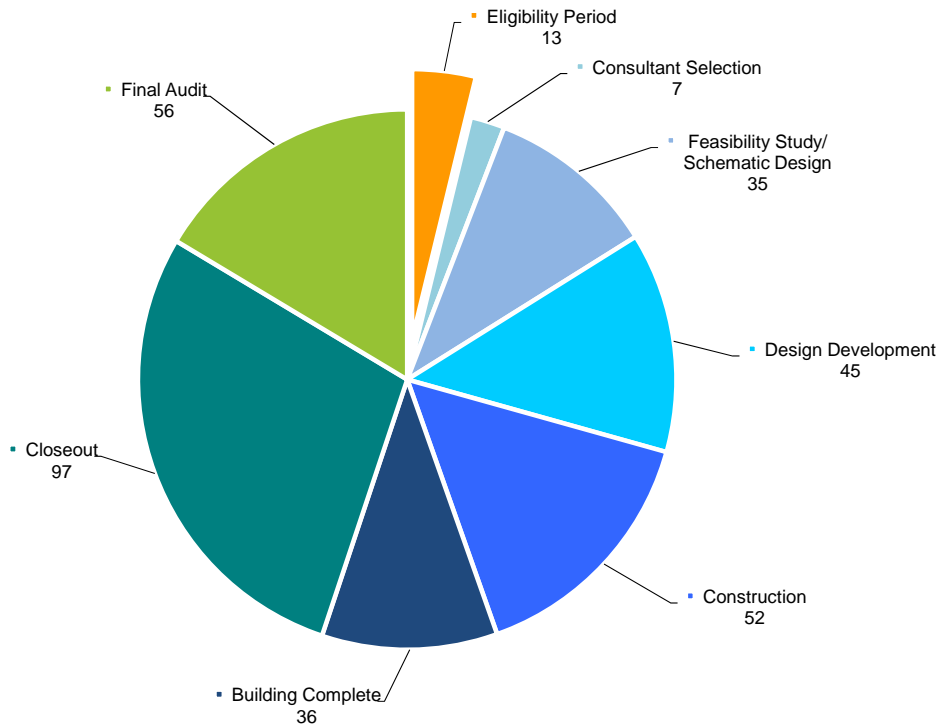

Statement of Interest (“SOI”)

2014 SOI Process

The Fiscal Year 2014 SOI filing period opened on **January 10, 2014**. The deadline to file SOIs for consideration in the Accelerated Repair Program (“ARP”) was Friday, February 14, 2014. The MSBA received 119 SOIs, submitted by 60 districts for consideration in the ARP. Invites into the ARP are anticipated for the June 4, 2014 Board of Directors Meeting.

The SOI closing date for districts submitting for consideration in the Core Program, which is primarily for projects beyond the scope of Accelerated Repair, including extensive repairs, renovations, addition/renovations, and new school construction, was **April 11, 2014**. As of the April 11th deadline, the MSBA received 108 Core SOIs. The review process for these SOIs will last throughout the summer, and the MSBA anticipates invites into the Eligibility Period at the Fall 2014/Winter 2015 Board of Directors Meetings.

Eligibility Period

There are 13 districts in the Eligibility Period. Of the 13, one district has already secured funding. The remaining 12 districts have yet to confirm their date for action.

An agreed-upon enrollment is a key prerequisite for the MSBA to commence a Feasibility Study with a district. To begin the enrollment projection process, a district must file enrollment information utilizing the MSBA's online enrollment projection tool. Since the last report, seven districts have completed the enrollment process.

Based upon the schedules anticipated by the districts for completion of the Eligibility Period requirements, staff anticipates recommending the 13 districts in the Eligibility Period for an Invitation to Feasibility Study at upcoming Board meetings.

Capital Pipeline

Consultant Selection

After the district has completed all Eligibility Period requirements and has received a Board Invitation to Feasibility Study, the district procures an Owner's Project Manager ("OPM"). There are five districts in the Capital Pipeline that need to procure an OPM.

After a district has selected and executed a contract with an OPM, it selects a Designer utilizing either a local designer selection process for projects under \$5 million or the MSBA's Designer Selection Panel ("DSP") for projects over \$5 million. There are two districts in the Capital Pipeline that are in the process of procuring a Designer.

Feasibility Study

Once a district has procured an OPM and Designer and a Feasibility Study Agreement has been executed, the district and its consultants must complete two Feasibility Study submittals, the Preliminary Design Program and the Preferred Schematic Report, prior to Board consideration to proceed into Schematic Design. Based on the most recent data and schedules provided to the MSBA by districts, the MSBA anticipates that six districts will present their preferred schematic designs to the Board at the upcoming July and September Board meetings.

Prior to consideration by the Board for Project Scope and Budget authorization, a district must submit a Schematic Design to the MSBA for review. Based on the most recent data and schedules provided to the MSBA by districts, the MSBA anticipates that five districts will appear before the Board for Project Scope and Budget Agreement authorization at the upcoming July and September Board meetings.

Commissioning

Since the last report, the MSBA has assigned Commissioning Consultants to an additional seven projects presented in the table below. To date, the MSBA has executed 274 Commissioning Consultant contracts, totaling \$20.5 million; 110 contracts have been completed.

District	School	Estimated Const. Cost (million)	Commissioning Consultant	Contract Amount
Gloucester	West Parish Elementary School	\$30.00	Fitzemeyer & Tocci	\$74,873
Springfield	Chestnut Acc. MS (2013 ARP: Roofing)	\$3.70	Building Enclosure Associates	\$28,500
Westford	Robinson ES (2013 ARP: Windows)	\$1.40	CBI Consulting	\$26,900
Quincy	Merrymount ES, N. Quincy HS, Wollaston ES (2013 ARP: Windows)	\$4.40	Simpson Gumpertz & Heger	\$90,000
Milford	Woodland Elementary School	\$65.00	Consulting Engineering Services	\$99,404
North Middlesex	North Middlesex Regional High School	\$69.20	Horizon Engineering Associates	\$135,398
Lunenburg	Lunenburg Middle/High School	\$59.60	Cannon Design	\$126,765
Total		\$230.50 M	Total	\$518,440

The table below represents the status of commissioning assignments sorted by the fiscal year in which the commissioning work orders were issued.

Fiscal Year	No. Work Orders Issued	Value of Work Orders Issued	Total Invoiced	Percent Complete
FY10	31	\$4,231,376	\$4,188,548.87	98.99%
FY11	95	\$6,328,287	\$5,337,494.28	84.34%
FY12	52	\$4,459,061	\$2,832,214.00	63.52%
FY13	55	\$3,386,847	\$1,331,524.66	39.31%
FY14	34	\$2,168,147	\$180,223.65	8.31%

Design Development

Once a district has secured local funding and has entered into a Project Funding Agreement with the MSBA, it enters the Design Development phase. Currently, there are 45 projects in the Design Development phase with a total estimated construction cost of approximately \$730.34 million: 30 Accelerated Repair projects and 15 Core Program projects. The 15 Core Program projects in Design Development have a total estimated construction cost of approximately \$676.23 million:

Elementary School Districts

Athol-Royalston Regional
Gloucester
Milford
Newton
Northborough

Middle School Districts

Chicopee
Georgetown
Lynn
Peabody
Wachusett Regional

High School Districts

Greater Lawrence Regional Voc/Tech
Lunenburg
North Middlesex Regional
Winchester
Winthrop

Construction

When a district issues a Notice to Proceed, the project is advanced to the Construction phase. Currently, there are 52 projects in the Construction phase with a total estimated construction cost of \$1.85 billion: one Green Repair project, nine Accelerated Repair projects, two Science Lab Initiative projects, and 40 Core Program projects. The 40 Core Program projects have a total estimated construction cost of \$1.79 billion and are listed below. This does not include the 36 projects that have reached substantial completion and are currently in the Building Complete phase.

Elementary School Districts

Andover
Georgetown
Newburyport (*Bresnahan*)
Revere
Springfield (*Brookings*)
South Hadley
Southwick-Tolland-Granville
Regional (*Woodland*)
Webster
Westfield
Weston
Williamsburg

Middle and Middle/High School Districts

Auburn
Greenfield
Hingham
Newburyport (*Nock*)
North Adams
Oxford
Southwick-Tolland-Granville
Regional (*Powder Mill*)
Stoneham
Sutton
Wakefield

High School Districts

Addition/Renovation
Assabet Valley Regional Technical
Ayer Shirley Regional
Dracut
Greater Lowell Regional Voc/Tech
Greater New Bedford Voc/Tech
Methuen
Norfolk County Agricultural
North Reading
Southern Worcester Regional Voc/Tech
Southwick-Tolland-Granville Regional

New

Concord-Carlisle Regional
Essex/North Shore Regional Voc/Tech
West Bridgewater
Wilmington

Model

Duxbury
Franklin
Marshfield
Monomoy Regional
Somerset-Berkley Regional

Summary of Bid Data

These numbers are based on preliminary information received from the district and are subject to further review and calculation.

Year	Number of Projects	Design Basis for Enrollment	Project Budget	Construction Budget
2014	14	12,185	\$762.0 M	\$593.9 M
2015	3	1,960	\$114.0 M	\$86.0 M
Grand Total	17	14,145	\$876.0 M	\$679.9 M

Core Program – Total Project Budget Update

Upon receiving the Board’s approval of the Project Scope and Budget, the MSBA and participating districts enter into a Project Funding Agreement that establishes the Total Project Budget and the Estimated Maximum Total Facilities Grant for an approved project. Of the grants authorized by the Board, nine projects have increased their Total Project Budgets due to acceptance of construction bids higher than the project estimates, and one project has increased its Total Project Budget due to an increase in its site acquisition cost budget. In no event has the increase in budget resulted in an increase to the Estimated Maximum Total Facilities Grant as authorized by the Board. Please note that staff reported on these budget increases for the seven projects shaded below at previous Board meetings.

District	School Name	Scope	Project Funding Agreement		PFA Bid Amendment		Reason for Increase to Total Project Budget
			Total Project Budget	Total Maximum Facilities Grant	Total Project Budget	Total Maximum Facilities Grant	
Core Program							
Andover	Bancroft Elementary School	New	\$44,659,837	\$16,773,753	\$50,374,837	TBD*	The District has appropriated additional funds to cover the costs associated with increased construction costs and additional contingencies for litigation/settlement costs and other ineligible costs.
Essex North Shore Agricultural & Technical School	Essex North Shore Agricultural & Technical School District	New	\$125,000,000	\$77,500,000	\$133,770,000	\$77,500,000	The Board was informed at the March 30, 2011 meeting that the Total Project Budget had increased due to additional ineligible scope that would be funded by DCAM.
Essex North Shore Agricultural & Technical School	Essex North Shore Agricultural & Technical School	New	\$125,000,000	\$77,500,000	\$134,501,368	\$77,500,000	The District has appropriated additional funds to cover the costs associated with increased construction costs for horse tack barn renovations.
Lexington	Estabrook Elementary School	New	\$40,792,248	\$12,250,739	\$42,554,862	TBD*	The District has executed a GMP that exceeds the Construction Budget of the PFA. The District is currently reviewing its project budget to determine the use of the additional appropriation funds it appropriated in excess of the Total Project Budget.
North Reading	North Reading Middle /High School	Add/Reno	\$107,727,074	\$49,323,123	\$123,227,074	\$49,323,123	This is a CMR project. The estimated, reconciled construction costs tracked over budget at DD (\$9,746,655 over), 60% (\$4,655,965 over), and 90% (\$15,136,846 over). A Town override vote in March 2013 obtained an additional \$15,500,000 in local funding to proceed.
Revere	Staff Sergeant James J. Hill Elementary School (currently the McKinley ES)	New	\$45,402,396	\$29,551,048	TBD*	\$29,551,048	At Project Scope and Budget, the Total Project Budget was approved at \$44,382,396. The City of Revere has increased the land acquisition budget. Therefore, the projected total project budget at PFA has increased to \$45,402,396. Note that the MSBA grant has not changed since the Project Scope and Budget Agreement.
Somerville	East Somerville Community School	Add/Reno	\$33,185,258	\$15,237,996	\$38,006,621	\$15,237,996	At the March 28, 2012 Board Meeting, the Board approved an amendment to the PFA and a \$6.25M District loan.
Uxbridge	Uxbridge High School	New	\$43,000,000	\$22,362,328	\$44,986,479	\$22,362,328	The District has appropriated additional funds to cover the costs associated with the construction of athletic fields originally included in the PFA but which were not included in the bid as the District’s construction contract would have exceeded the budget.

*PFA Bid Amendment has not been developed to calculate a revised total facilities grant amount. The Total Maximum Facilities Grant will not exceed the Board authorized amount in the PFA but, upon review, may decrease.

Status of Accelerated Repair Program


Currently there are a total of 45 districts, representing 81 projects, in the Accelerated Repair Program.

2014 Accelerated Repair Program

Following a review of 2014 Accelerated Repair Statements of Interest, the MSBA completed site visits for potential Program invitations.


2013 Accelerated Repair Program

Prior to the June 2014 Board Meeting, 46 projects representing 26 districts were approved for Project Funding Agreements. One remaining project is seeking approval for a Project Funding Agreement at the June 2014 Board Meeting. Subsequent to the March 2014 Board Meeting, two districts authorized Declarations of Removal of a Statement of Interest and removed their potential projects from the Program. Following the June 2014 Board meeting, assuming the one additional project is approved, the Program total will be 45 projects represented by 25 districts. With the Board's authorization at the June 2014 Board Meeting, the 2013 Accelerated Repair Program will have \$94,605,790 in Total Project Costs and a maximum of \$54,662,710 in MSBA Total Facilities Grant funding.

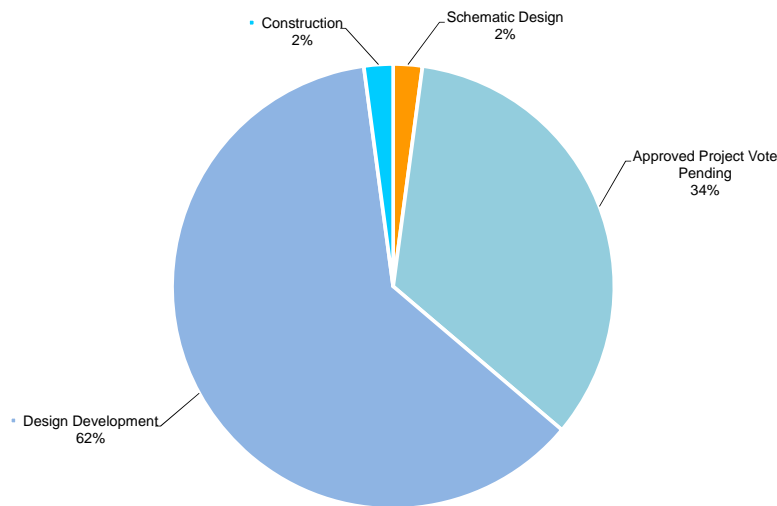

2012 Accelerated Repair Program

All 24 districts, representing 36 projects, approved in 2012 are under contract with consultants and have been authorized to enter into a Project Funding Agreement, totaling \$63,009,653 in Total Project Costs and a maximum of \$38,267,952 in MSBA Total Facilities Grant funding. Of the 36 projects, 27 are scheduled to complete construction in 2013, and nine are scheduled to complete construction in 2014. The chart below represents the progress of the 36 projects approved in 2012.

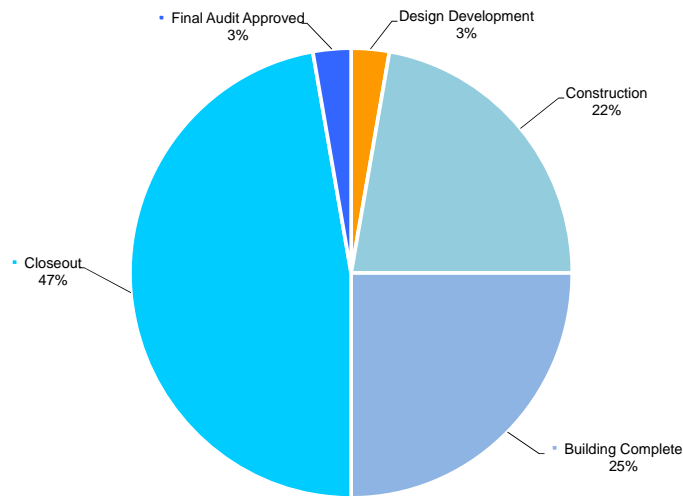

Status of Green Repair Program

The Green Repair Program has resulted in PFA authorizations totaling \$366,647,226 in Total Project Costs and \$222,885,258 in MSBA grants. One project, Douglas Intermediate School, remains in construction with substantial completion scheduled for July 1, 2014.

2012 Accelerated Repair Projects – Construction Estimate vs. 2013 Bid Amount

- Out of 36 projects, 35 bids have been received.
- Of the 35, 33 bids have been reported.
- Of the 33 projects, 28 bids came within the estimated budget.

District	School	Scope	Project Type	Bid Date	Construction Estimate **	Bid Amount **	Variance from Construction Estimate	Reimbursement Rate	Potential Grant Variance *
				Total	\$45,975,629	\$35,256,185	\$10,719,444	-	\$6,939,841
Weymouth	William Seach PS	Boiler	DBB	Dec-12	\$425,213	\$459,104	-\$33,891	54.16%	\$0
Groton-Dunstable RSD	Gronton-Dunstable MS	Roof	DBB	Feb-13	\$1,316,890	\$942,000	\$374,890	45.74%	\$171,475
Hamilton-Wenham	Cutler ES	Roof	DBB	Feb-13	\$547,326	\$444,150	\$103,176	43.42%	\$44,799
North Brookfield	North Brookfield ES	Windows	DBB	Feb-13	\$274,254	\$199,400	\$74,854	62.67%	\$46,911
Shawsheen Valley Voc/Tech.	Shawsheen Valley VTHS	Boiler	DBB	Mar-13	\$805,423	\$535,000	\$270,423	52.06%	\$140,782
Sudbury	Gen. John Nixon ES	Roof	DBB	Mar-13	\$621,554	\$542,775	\$78,779	36.89%	\$29,062
Easton	Easton Jr. HS	Roof	DBB	Mar-13	\$1,850,830	\$1,889,000	-\$38,170	50.16%	\$0
Norton	Solmonese ES	Roof	DBB	Mar-13	\$1,166,044	\$986,000	\$180,044	55.63%	\$100,158
Attleborough	Irvin Studley ES	Roof	DBB	Mar-13	\$773,363	\$489,000	\$284,363	57.74%	\$164,191
Lynn	Breed MS	Windows	DBB	Mar-13	\$1,796,674	\$2,167,300	-\$370,626	80.00%	\$0
Lynn	Lynn Voc. Tech	Roof	DBB	Mar-13	\$4,173,000	\$3,097,000	\$1,076,000	80.00%	\$860,800
Worcester	Chandler Magnet	Windows	DBB	Mar-13	\$3,723,463	\$3,142,320	\$581,143	80.00%	\$464,914
Worcester	Jacob Hiatt Magnet	Boiler	DBB	Mar-13	\$298,877	\$321,703	-\$22,826	80.00%	\$0
Worcester	James Caradonio Center	Windows & Boiler	DBB	Mar-13	\$1,021,820	\$1,007,132	\$14,688	80.00%	\$11,750
Worcester	Lake View School	Windows	DBB	Mar-13	\$1,127,970	\$789,398	\$338,572	80.00%	\$270,858
Worcester	May Street School	Windows	DBB	Mar-13	\$1,655,289	\$1,548,167	\$107,122	80.00%	\$85,698
Gardner	Gardner MS	Boiler	DBB	Apr-13	\$438,439	\$396,100	\$42,339	78.95%	\$33,427
North Attleborough	Roosevelt Ave. ES	Windows	DBB	Apr-13	\$768,000	\$656,483	\$111,517	52.06%	\$58,056
Quabaog RSD	Warren ES	Boiler	DBB	Apr-13	\$207,000	\$182,444	\$24,556	68.34%	\$16,782
Quabbin	Ruggles Lane ES	Roof & Windows	DBB	Apr-13	\$2,588,409	\$2,287,836	\$300,573	57.74%	\$173,551
Leominster	Fall Brook ES	Boiler	DBB	Apr-13	\$949,550	\$684,000	\$265,550	73.38%	\$194,861
Leominster	Southeast ES	Roof & Boiler	DBB	Apr-13	\$3,146,097	\$1,948,000	\$1,198,097	73.38%	\$879,164
Westfield	Munger Hill ES	Roof	DBB	Apr-13	\$1,170,735	\$593,499	\$577,236	59.84%	\$345,418
Westfield	Paper Mill ES	Roof	DBB	Apr-13	\$1,170,735	\$562,525	\$608,210	59.84%	\$363,953
Southampton	William Norris ES	Roof	DBB	May-13	\$1,504,147	\$922,000	\$582,147	55.00%	\$320,181
Taunton	Galligan School	Roof	DBB	May-13	\$543,570	\$486,600	\$56,970	73.95%	\$42,129
Wayland	Wayland MS	Roof	DBB	May-13	\$2,445,767	\$1,965,800	\$479,967	36.89%	\$177,060
Blackstone-Millville RSD	Maloney ES	Roof	DBB	Sep-13	\$1,405,656	\$702,000	\$703,656	57.74%	\$406,291
Blackstone-Millville RSD	J.F.Kennedy ES	Roof	DBB	Sep-13	\$2,315,707	\$1,093,000	\$1,222,707	57.74%	\$705,991
Wilmington	North IS	Windows	DBB	Nov-13	\$1,206,312	\$1,217,649	-\$11,337	49.94%	\$0
Canton	Peter Hanson School	Windows	DBB	Dec-13	\$734,414	\$660,200	\$74,214	45.11%	\$33,478
Canton	William Galvin MS	Windows	DBB	Dec-13	\$1,014,385	\$856,600	\$157,785	45.11%	\$71,177
Bridgewater-Raynham	Bridgewater MS	Roof	DBB	Mar-14	\$2,788,716	\$1,482,000	\$1,306,716	55.63%	\$726,926

*These numbers are based on preliminary information received from the district and are subject to further review and calculation.

**The construction estimate and bid amount do not include pre-construction services and alternatives.

Accelerated Repair Projects – Schedule Extension Update

The MSBA has granted districts conditional extensions to their Project Funding Agreements pending compliance with the following stipulations:

- The district needed to submit a detailed, revised construction timeline showing how the work will be completed at each school; and
- Any costs that may result from the district's requested extension of the construction schedule will be the sole responsibility of the district and are categorically ineligible for reimbursement by the MSBA.

Schedule delays for these districts can be attributed to local funding issues, lead time for windows, and construction delays on site. In no event have the extended schedules resulted in an increase to the Estimated Maximum Total Facilities Grant as authorized by the Board.

Nine of the 36 2012 Accelerated Repair Projects have not met their anticipated construction completion dates. Each of these projects has a revised construction schedule and is scheduled to be complete by the beginning of the 2014-2015 school year.

District	School	Scope	Original Construction Completion Date	Updated Construction Completion Date	Reason for Schedule Extension
Blackstone-Millville	Blackstone-Millville RHS	Roof	26-Dec-13	1-Sep-14	The District fell behind schedule due to local funding issues.
Bridgewater-Raynham	Bridgewater MS	Roof	1-Sep-13	1-Sep-14	The District fell behind schedule as a result to local issues funding issues and incorporation of new OPM to project team.
Bridgewater-Raynham	Laliberte ES	Roof	1-Sep-13	1-Sep-14	The District fell behind schedule as a result to local issues funding issues and incorporation of new OPM to project team.
Bridgewater-Raynham	L.B. Merrill ES	Roof	1-Sep-13	1-Sep-14	The District fell behind schedule as a result to local issues funding issues and incorporation of new OPM to project team.
North Attleborough	Roosevelt Ave. ES	Windows	27-Sep-13	31-Mar-14	Construction fell behind schedule due to material delivery delays. Corrective work continues to ensure windows pass commissioning tests.
Taunton	Galligan School	Roof	13-Nov-13	31-Dec-13	District issued a Change Order for installation of tapered insulation and membrane overlay to prevent ponding around the chimney area.
Worcester	Lake View School	Windows/Doors	13-Sep-13	14-Feb-14	Construction fell behind schedule due to material delivery delays.
Worcester	May Street School	Windows/Doors	14-Sep-13	15-Mar-14	Construction fell behind schedule due to material delivery delays.
Worcester	New Citizens Center School	Windows/Doors & Boilers	13-Sep-14	14-Feb-13	Construction fell behind schedule due to material delivery delays. Boiler scope completed per baseline schedule.


One of the 45 2013 Accelerated Repair Projects will not meet its anticipated construction completion date in 2014. The project has a revised construction schedule and is scheduled to be completed by the beginning of the 2015-2016 school year.

District	School	Scope	Original Construction Completion Date	Updated Construction Completion Date	Reason for Schedule Extension
Hamilton-Wenham	Winthrop ES	Windows	15-Sep-14	13-Aug-15	The District and its consultants have determined that the estimated lead time for windows requires construction to be scheduled for 2015.

PROJECT STATUS

Total Number of Projects: 328

Wednesday, May 14, 2014

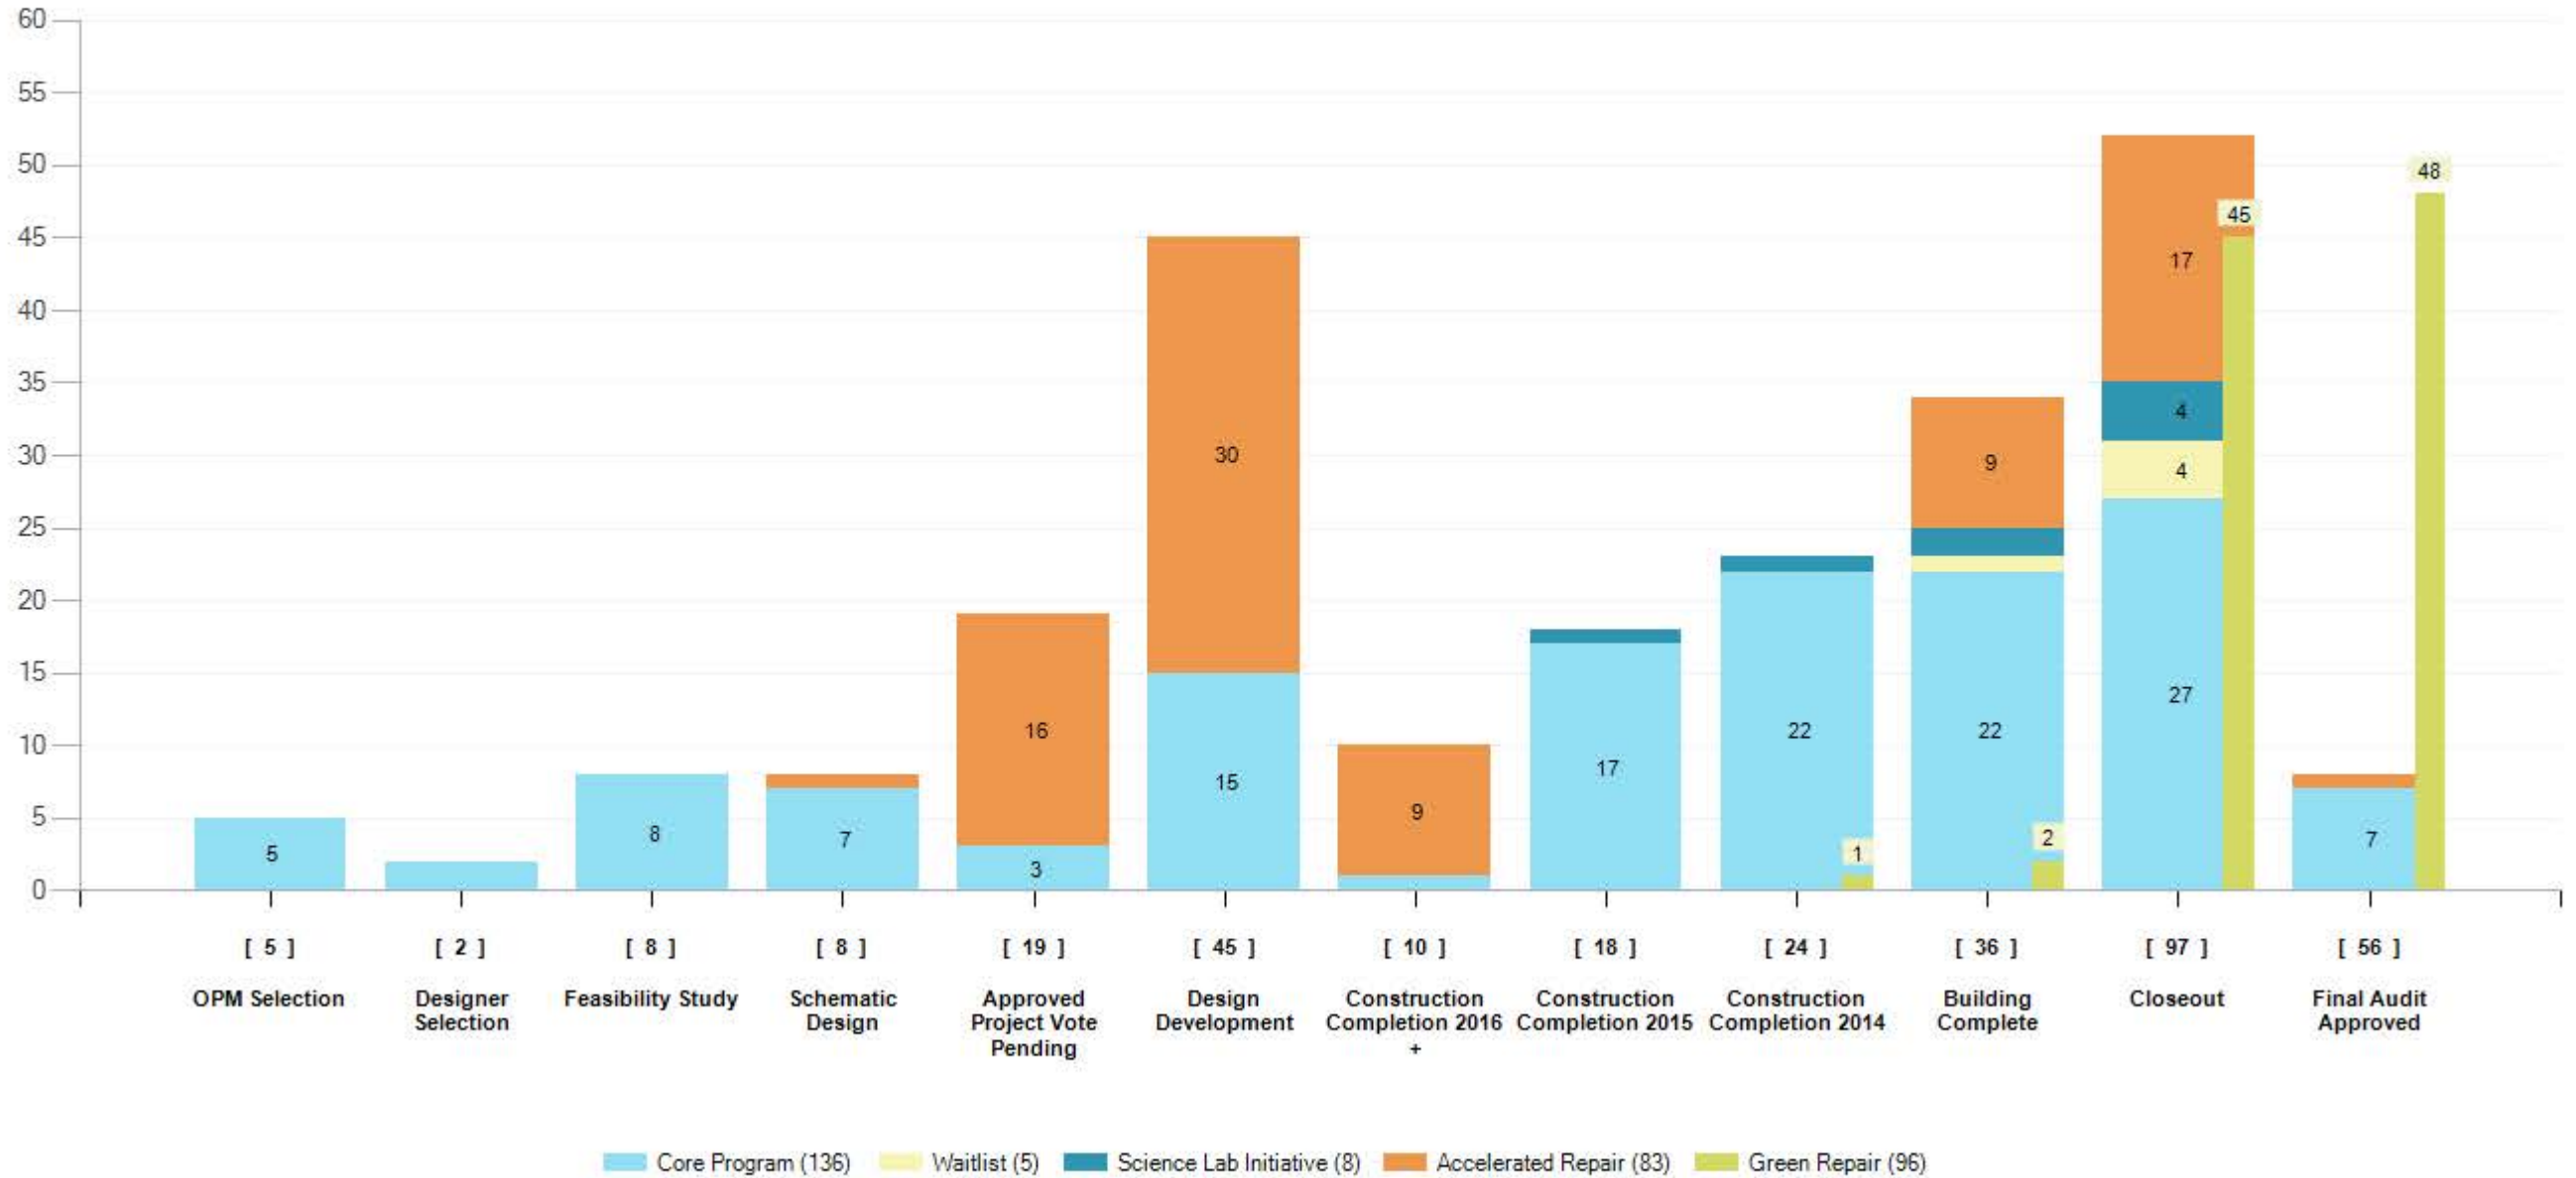

Number less than 3 is not shown in the chart

Date of Report: 5/14/2014

Total Projects: 341

MSBA ID	District	School	Project Phase	Project Type	Project Scope	Procurement Type	OPM	Designer	CM/GC	Commissioning Consultant
20080010405	Abington	Frolio Middle School	Schematic Design	Core Program	New Construction		Knight, Bagge & Anderson Inc.	Ai3 Architects LLC	-	-
200806030505	Adams-Cheshire	Hoosac Valley High School	Closeout	Core Program	Addition / Renovation	CM@R	URS Corporation	Tessier Associates, Inc.	Gilbane Building Company	Strategic Building Solutions, LLC
201100050405G	Agawam	Agawam Junior High	Final Audit Approved	Green Repair		DBB	Municipal Building Consultants, Inc.	CSS Architects Incorporated	Capeway Roofing Systems, Inc. Chandler Architectural Products, Inc.	Building Enclosure Associates, LLC
201300080050	Amherst	Wildwood Elementary	Eligibility Period	Core Program			-	-	-	-
201100090310G	Andover	Andover West Middle	Final Audit Approved	Green Repair		DBB	Skanska USA Building, Inc.	Russo Barr Associates, Inc.	Eagle Rivet Roof Services Corporation	Simpson Gumpertz & Heger Inc.
200800090003	Andover	Bancroft Elementary School	Construction	Core Program	New Construction	CM@R	Dore & Whittier Management Partners, Inc.	Symmes Maini & McKee Associates, Inc.	Skanska USA Building, Inc.	Sebesta Blomberg & Associates, Inc.
200900100050	Arlington	Thompson Elementary School	Building Complete	Core Program	New Construction	DBB	PMA Construction Services	HMFH Architects, Inc.	G & R Construction, Inc.	Consulting Engineering Services, LLC
200806100025	Ashburnham-Westminster	John R. Briggs Elementary School	Building Complete	Core Program	New Construction	CM@R	STV Incorporated	Lamoureux Pagano & Associates, Inc.	Consigli Construction Company, Inc.	Foreman Building Commissioning, LP
201300140405	Ashland	Ashland Middle	Design Development	Accelerated Repair			Arcadis U.S., Inc.	Raymond Design Associates, Inc.	-	Gale Associates, Inc.
201300140010	Ashland	Henry E Warren Elem	Design Development	Accelerated Repair			Arcadis U.S., Inc.	Raymond Design Associates, Inc.	-	Gale Associates, Inc.
200908010605	Assabet Valley	Assabet Valley Regional Technical High School	Construction	Core Program	Repair - Major	DBB	Strategic Building Solutions, LLC	Design Partnership of Cambridge, Inc.	CTA Construction Co., Inc.	Symmes, Maini & McKee Associates
200906150020	Athol-Royalston	Riverbend School	Design Development	Core Program	New Construction		Symmes Maini & McKee Associates	Mount Vernon Group Architects, Inc.	-	Strategic Building Solutions, LLC
201200160001	Attleboro	A. Irvin Studley Elementary School	Closeout	Accelerated Repair			Tishman Construction Corporation of MA	Gale Associates, Inc.	Titan Roofing, Inc.	CBI Consulting Inc.
200800170305	Auburn	Auburn Middle	Construction	Core Program	New Construction	CM@R	Skanska USA Building, Inc.	Lamoureux Pagano & Associates, Inc.	Fontaine Brothers, Inc.	WSP Flack + Kurtz
200806160505	Ayer-Shirley	Ayer-Shirley Regional Middle/High School	Construction	Core Program	Addition / Renovation	CM@R	Dore and Whittier Architects, Inc.	Symmes Maini & McKee Associates, Inc.	Consigli Construction Company, Inc.	WSP Flack + Kurtz
201300200010	Barnstable	Barnstable United Elementary School	Approved Project Vote Pending	Accelerated Repair			exPERTcon, Inc.	Gale Associates, Inc.	-	Russo Barr Associates, Inc.
201100200005G	Barnstable	West Barnstable Elem	Closeout	Green Repair		DBB	PMA Construction Services	-	Paul J. Rogan Co., Inc.	CBI Consulting Inc.
200800260035	Belmont	Roger Wellington Elementary School	Closeout	Core Program	New Construction	CM@R	PMA Construction Services	Jonathan Levi Architects LLC	Skanska USA Building, Inc.	Strategic Building Solutions, LLC
201006180505	Berkshire Hills	Monument Mountain Regional High School	Approved Project Vote Pending	Core Program	Addition / Renovation		Strategic Building Solutions, LLC	Symmes Maini & McKee Associates, Inc.	-	-
200806200505	Berlin-Boylston	Tahanto Regional High School	Building Complete	Core Program	New Construction	DBB	PMA Construction Services	HMFH Architects, Inc.	CTA Construction Co., Inc.	Strategic Building Solutions, LLC
200800300505	Beverly	Beverly High School	Closeout	Core Program	Addition / Renovation	DBB	HEERY	-	-	-
201300300305	Beverly	Briscoe Middle	OPM Selection	Core Program			-	-	-	-
201300310505	Billerica	Billerica Memorial High School	Eligibility Period	Core Program			-	-	-	-
200800310015	Billerica	Parker Elementary School	Closeout	Core Program	New Construction	DBB	Joslin, Lesser + Associates Inc.	Symmes Maini & McKee Associates, Inc.	CTA Construction Co., Inc.	Sebesta Blomberg & Associates, Inc.
201208050605	Blackstone Valley Reg	Blackstone Valley	Closeout	Science Lab Initiative	Addition / Renovation		Compass Project Management, Inc.	Flansburgh Associates, Inc.	Pergola Construction Co., Inc.	Horizon Engineering Associates, LLP
201206220015	Blackstone-Millville	A F Maloney	Building Complete	Accelerated Repair			Arcadis U.S., Inc.	DiMarinisi & Wolfe Architects Urban Designers	Greenwood Industries, Inc.	Gale Associates, Inc.
201206220505	Blackstone-Millville	Blackstone Millville RHS	Design Development	Accelerated Repair			Arcadis U.S., Inc.	DiMarinisi & Wolfe Architects Urban Designers	-	Gale Associates, Inc.

201206220008	Blackstone-Millville	John F Kennedy Elem	Building Complete	Accelerated Repair			Arcadis U.S., Inc.	DiMarinisi & Wolfe Architects Urban Designers	Greenwood Industries, Inc.	Gale Associates, Inc.
201306220010	Blackstone-Millville	Millville Elem	Approved Project Vote Pending	Accelerated Repair			Pinck & Co., Inc.	CBI Consulting Inc.	-	Simpson Gumpertz & Heger Inc.
201100350522G	Boston	Excel High School	Final Audit Approved	Green Repair		DBB	Daedalus Projects Inc	-	-	Simpson Gumpertz & Heger Inc.
201000350074	Boston	Henry Dearborn Middle School	Approved Project Vote Pending	Core Program	New Construction		Daedalus Projects Inc	Jonathan Levi Architects LLC	-	-
201000350565	Boston	Quincy Upper School	Schematic Design	Core Program			Skanska USA Building, Inc	HMFH Architects, Inc.	-	-
201300400305	Braintree	East Middle School	Eligibility Period	Core Program			-	-	-	-
201206250320	Bridgewater-Raynham	Bridgewater Middle School	Construction	Accelerated Repair			Vertex Construction Services	-	-	CBI Consulting Inc.
201206250050	Bridgewater-Raynham	Laliberte Elementary School	Construction	Accelerated Repair			Vertex Construction Services	Raymond Design Associates, Inc.	-	CBI Consulting Inc.
201206250020	Bridgewater-Raynham	Merrill Elementary School	Construction	Accelerated Repair			Vertex Construction Services	Raymond Design Associates, Inc.	-	CBI Consulting Inc.
201100440505G	Brockton	Brockton High	Final Audit Approved	Green Repair		DBB	Skanska USA Building, Inc	CSS Architects Incorporated	Gibson Roofs, Inc.	Simpson Gumpertz & Heger Inc.
201100440110G	Brockton	Downey	Final Audit Approved	Green Repair		DBB	Skanska USA Building, Inc	CSS Architects Incorporated	Built-up Roofing Systems LLC	Simpson Gumpertz & Heger Inc.
201100440405G	Brockton	East Junior High	Final Audit Approved	Green Repair		DBB	Skanska USA Building, Inc	CSS Architects Incorporated	Reliable Roofing and Sheet Metal, LLC	Rist-Frost-Shumway Engineering, P.C.
201100440023G	Brockton	Edgar B Davis	Final Audit Approved	Green Repair		DBB	Skanska USA Building, Inc	CSS Architects Incorporated	Reliable Roofing and Sheet Metal, LLC	Simpson Gumpertz & Heger Inc.
201100440045G	Brockton	Hancock	Final Audit Approved	Green Repair		DBB	Skanska USA Building, Inc	CSS Architects Incorporated	Reliable Roofing and Sheet Metal, LLC	Simpson Gumpertz & Heger Inc.
201100440410G	Brockton	North Junior High	Final Audit Approved	Green Repair		DBB	Skanska USA Building, Inc	-	Arden Engineering Constructors, LLC Built-up Roofing Systems LLC	Rist-Frost-Shumway Engineering, P.C.
201100440078G	Brockton	Oscar F Raymond	Final Audit Approved	Green Repair		DBB	Skanska USA Building, Inc	CSS Architects Incorporated	Reliable Roofing and Sheet Metal, LLC	Simpson Gumpertz & Heger Inc.
201100440420G	Brockton	West Junior High	Final Audit Approved	Green Repair		DBB	Skanska USA Building, Inc	CSS Architects Incorporated	Reliable Roofing and Sheet Metal, LLC	Simpson Gumpertz & Heger Inc.
201100450005G	Brookfield	Brookfield Elementary	Closeout	Green Repair		DBB	Diversified Project Management	-	Northeast Energy Control Systems	Cannon Design
201100460015	Brookline	Edward Devotion	Feasibility Study	Core Program			-	HMFH Architects, Inc.	-	-
201000460025	Brookline	Heath School	Final Audit Approved	Core Program	Addition / Renovation	DBB	Town of Brookline Building Department	Miller Dyer Spears Inc.	Nauset Construction Corporation	Consulting Engineering Services, LLC
200800460045	Brookline	John D. Runkle School	Final Audit Approved	Core Program	Addition / Renovation	DBB	Town of Brookline Building Department	Design Partnership of Cambridge, Inc.	G & R Construction, Inc.	Consulting Engineering Services, LLC
201000480303	Burlington	Marshall Simonds Middle School	Closeout	Core Program	Addition / Renovation	CM@R	Construction Monitoring Services, Inc.	Knight, Bagge & Anderson, Inc.	CTA Construction Co., Inc.	RDK Engineers
200800480015	Burlington	Memorial Elementary School	Closeout	Core Program	New Construction	DBB	Construction Monitoring Services, Inc.	Knight, Bagge & Anderson, Inc.	CTA Construction Co., Inc.	Consulting Engineering Services, LLC
201200500012	Canton	Lt Peter M Hansen	Construction	Accelerated Repair			Vertex Construction Services	CSS Architects Incorporated	-	Simpson Gumpertz & Heger Inc.
201200500305	Canton	Wm H Galvin Middle	Construction	Accelerated Repair			Vertex Construction Services	CSS Architects Incorporated	-	Simpson Gumpertz & Heger Inc.
201008150605G	Cape Cod Region Voc Tech	Cape Cod Region Voc Tech	Final Audit Approved	Green Repair		DBB	URS Corporation	-	-	Fitzmeyer & Tocci Associates, Inc.
200800510025	Carlisle	Carlisle School	Closeout	Core Program	Addition / Renovation	DBB	Daedalus Projects Inc	HMFH Architects, Inc.	H.V. Collins Co., Inc.	Horizon Engineering Associates, LLP
201300520015	Carver	Carver Elementary School	Eligibility Period	Core Program			-	-	-	-
201306350010	Central Berkshire	Berkshire Trail Elem	Approved Project Vote Pending	Accelerated Repair			Strategic Building Solutions, LLC	Tighe & Bond, Inc.	-	Building Enclosure Associates, LLC
201106350035G	Central Berkshire	Kittredge	Closeout	Green Repair		DBB	Daedalus Projects Inc	Bradley Architects, Inc.	Alpha Contracting Associates, Inc.	Strategic Building Solutions, LLC

201100560030G	Chelmsford	Byam School	Final Audit Approved	Green Repair		DBB	Vertex Construction Services	Russo Barr Associates, Inc.	S.O.M. Construction Ent., Inc.	Simpson Gumpertz & Heger Inc.
201100560505G	Chelmsford	Chelmsford High	Final Audit Approved	Green Repair		DBB	Vertex Construction Services	Russo Barr Associates, Inc.	Lockheed Window Corporations	Simpson Gumpertz & Heger Inc.
200800570050	Chelsea	Clark Avenue School	Schematic Design	Core Program			Pinck & Co., Inc.	HMFH Architects, Inc.	-	-
200900610021	Chicopee	Chicopee Academy	Design Development	Core Program	Addition / Renovation		Arcadis U.S., Inc.	Caolo & Bieniek Associates, Inc.	-	Symmes, Maini & McKee Associates
200906400505	Concord-Carlisle	Concord-Carlisle Regional High School	Construction	Core Program	New Construction	CM@R	KV Associates, Inc.	OMR Architects, Inc.	Turner Construction Company	Strategic Building Solutions, LLC
200800710505	Danvers	Danvers High School	Building Complete	Core Program	Addition / Renovation	DBB	Construction Monitoring Services, Inc.	DiNisco Design Partnership, Limited	Bacon Construction Co, Inc.	Turner Facilities Management Solutions
200800730010	Dedham	Avery Elementary School	Closeout	Core Program	New Construction	CM@R	Construction Monitoring Services, Inc.	Dore & Whittier Architects, Inc.	Consigli Construction Company, Inc.	WSP Flack + Kurtz
201200730005	Dedham	Early Childhood Center	Designer Selection	Core Program			-	-	-	-
201006450005G	Dennis-Yarmouth	Ezra H Baker	Final Audit Approved	Green Repair		DBB	STV Incorporated	Knight, Bagge & Anderson, Inc.	Antonelli Construction Co., Inc.	CBI Consulting Inc.
201306500005	Dighton-Rehoboth	Dighton Elementary	Design Development	Accelerated Repair			-	-	-	Gale Associates, Inc.
201306500305	Dighton-Rehoboth	Dighton Middle School	Design Development	Accelerated Repair			-	-	-	Gale Associates, Inc.
201306500505	Dighton-Rehoboth	Dighton-Rehoboth Rhs	Approved Project Vote Pending	Accelerated Repair			-	-	-	Gale Associates, Inc.
201306500310	Dighton-Rehoboth	Dorothy L Beckwith	Design Development	Accelerated Repair			-	-	-	Gale Associates, Inc.
200800770010	Douglas	Douglas Elementary	Building Complete	Core Program	New Construction - Model School	DBB	HEERY	DiNisco Design Partnership, Limited	CTA Construction Co., Inc.	Consulting Engineering Services, LLC
200800770100G	Douglas	Douglas Intermediate Elementary School	Construction	Green Repair	Addition / Renovation	DBB	HEERY	DiNisco Design Partnership, Limited	CTA Construction Co., Inc.	Consulting Engineering Services, LLC
200800790505	Dracut	Dracut Senior High School	Construction	Core Program	Addition / Renovation	DBB	Hill International Company	Mount Vernon Group Architects, Inc.	CTA Construction Co., Inc.	RDK Engineers
201000820505	Duxbury	Duxbury High School	Construction	Core Program	New Construction - Model School	CM@R	KV Associates, Inc.	Mount Vernon Group Architects, Inc.	Dimeo Construction Company	WSP Flack + Kurtz
200900830505	East Bridgewater	East Bridgewater High School	Building Complete	Core Program	New Construction - Model School	DBB	Hill International Company	Ai3 Architects LLC	Fontaine Brothers, Inc.	Foreman Building Commissioning, LP
200800860505	Easthampton	Easthampton High School	Building Complete	Core Program	New Construction	DBB	Strategic Building Solutions, LLC	Caolo & Bieniek Associates, Inc.	Fontaine Brothers, Inc.	Consulting Engineering Services, LLC
201200880405	Easton	Easton Junior High	Closeout	Accelerated Repair			PMA Construction Services	Russo Barr Associates, Inc.	Gibson Roofs, Inc.	Gale Associates, Inc.
201300880020	Easton	Moreau Hall	Design Development	Accelerated Repair			Skanska USA Building, Inc	Baker/Wohl Architects, Inc.	-	Gale Associates, Inc.
200809130705	Essex Agr Tech	Essex Agricultural and Technical High School	Construction	Core Program	New Construction	CM@R	PMA Construction Services	Design Partnership of Cambridge, Inc.	Gilbane Building Company	Turner Facilities Management Solutions
200800940020	Fairhaven	Rogers Elementary School	Building Complete	Core Program	New Construction - Model School	DBB	Daedalus Projects Inc	HMFH Architects, Inc.	CTA Construction Co., Inc.	Consulting Engineering Services, LLC
200900950315	Fall River	James Madison Morton Middle School	Closeout	Core Program	New Construction	DBB	Maguire Group Inc.	Mount Vernon Group Architects, Inc.	J & J Contractors, Inc.	Sebesta Blomberg & Associates, Inc.
201100970505G	Fitchburg	Fitchburg High	Final Audit Approved	Green Repair		DBB	Compass Project Management, Inc.	BLW Engineers, Inc.	Ostrow Electrical Co., Inc.	RDK Engineers
201100970048G	Fitchburg	Memorial Intermediate	Final Audit Approved	Green Repair		DBB	Compass Project Management, Inc.	Knight, Bagge & Anderson, Inc.	Lockheed Window Corporations	Simpson Gumpertz & Heger Inc.
201100970043G	Fitchburg	Reingold Elementary	Final Audit Approved	Green Repair		DBB	Compass Project Management, Inc.	Knight, Bagge & Anderson, Inc.	Lockheed Window Corporations	Simpson Gumpertz & Heger Inc.
201100970060G	Fitchburg	South Street Elementary	Final Audit Approved	Green Repair		DBB	Compass Project Management, Inc.	Knight, Bagge & Anderson, Inc.	Lockheed Window Corporations	Simpson Gumpertz & Heger Inc.
200800990505	Foxborough	Foxborough High School	Final Audit Approved	Core Program	Repair - Major	DBB	Construction Monitoring Services, Inc.	Kaestle Boos Associates, Inc.	CTA Construction Co., Inc.	Consulting Engineering Services, LLC

200901010505	Franklin	Franklin High School	Construction	Core Program	New Construction - Model School	DBB	Daedalus Projects Inc	Ai3 Architects LLC	Bacon-Agostini Construction Joint Venture	Consulting Engineering Services, LLC
201201030505	Gardner	Gardner High	Building Complete	Science Lab Initiative	Addition / Renovation		Pinck & Co., Inc.	Lamoureux Pagano & Associates, Inc.	Five Star Building Corp.	Fitzmeyer & Tocci Associates, Inc.
201201030405	Gardner	Gardner Middle School	Closeout	Accelerated Repair			Leftfield, LLC	Richard D. Kimball Company, Inc.	Royal Steam Heater Co.	Fitzmeyer & Tocci Associates, Inc.
200801050505	Georgetown	Georgetown Middle/High School	Design Development	Core Program	Addition / Renovation		Municipal Building Consultants, Inc.	Drummey Rosane Anderson, Inc.	-	-
200901050010	Georgetown	Penn Brook Elementary School	Construction	Core Program	New Construction	DBB	Municipal Building Consultants, Inc.	Drummey Rosane Anderson, Inc.	Brait Builders Corp.	Rist-Frost-Shumway Engineering, P.C.
200901070050	Gloucester	West Parish Elementary School	Design Development	Core Program	New Construction		Knight, Bagge & Anderson Inc.	Dore & Whittier Architects, Inc.	-	Fitzmeyer & Tocci Associates, Inc.
200801100505	Grafton	Grafton Memorial Senior	Closeout	Core Program	New Construction	CM@R	Joslin, Lesser + Associates Inc.	Symmes Maini & McKee Associates, Inc.	Dimeo Construction Company	Horizon Engineering Associates, LLP
201101100005G	Grafton	South Grafton Elementary	Final Audit Approved	Green Repair		DBB	URS Corporation	CGKV Architects, Inc.	AAlanco Service Corporation	Horizon Engineering Associates, LLP
201201110010	Granby	West St	OPM Selection	Core Program			Hill International Company	-	-	-
201108230605	Greater Lawrence RVT	Gr Lawrence Reg Voc Tech	Design Development	Core Program	Repair - Major		Vertex Construction Services	Richard D. Kimball Company, Inc.	-	WSP Flack + Kurtz
200908280605	Greater Lowell Voc Tec	Greater Lowell Regional Technical High School	Construction	Core Program	Addition / Renovation	CM@R	Joslin, Lesser + Associates Inc.	Knight, Bagge & Anderson, Inc.	Consigli Construction Company, Inc.	Horizon Engineering Associates, LLP
201008250605	Greater New Bedford	Greater New Bedford Vocational Technical High School	Construction	Core Program	Addition / Renovation	DBB	Construction Monitoring Services, Inc.	Drummey Rosane Anderson, Inc.	Agostini Construction Co., Inc.	Symmes, Maini & McKee Associates
201101140025G	Greenfield	Four Corners	Final Audit Approved	Green Repair		DBB	P3 Inc.	-	Five Star Building Corp.	Strategic Building Solutions, LLC
200901140505	Greenfield	Greenfield High School	Construction	Core Program	New Construction	CM@R	Construction Monitoring Services, Inc.	Dore & Whittier Architects, Inc.	Shawmut Design and Construction	BVH Integrated Services, P.C.
201206730305	Groton-Dunstable	Groton/Dun Reg'l Middle	Closeout	Accelerated Repair			Hill International Company	ICON architecture, inc.	Greenwood Industries, Inc.	Russo Barr Associates, Inc.
201101170505G	Hadley	Hopkins Academy	Final Audit Approved	Green Repair			Strategic Building Solutions, LLC	CSS Architects Incorporated	MDM Engineering	Russo Barr Associates, Inc.
201306750007	Hamilton-Wenham	Bessie Buker Elementary	Design Development	Accelerated Repair			NETCO Construction Project Managers, Inc.	Habeeb & Associates Architects, Inc.	-	Strategic Building Solutions, LLC
201206750010	Hamilton-Wenham	Cutler School	Final Audit Approved	Accelerated Repair			Coast and Harbor Association, Inc.	CBI Consulting Inc.	Stanley Roofing Company, Inc.	Russo Barr Associates, Inc.
201306750015	Hamilton-Wenham	Winthrop School	Design Development	Accelerated Repair			NETCO Construction Project Managers, Inc.	Habeeb & Associates Architects, Inc.	-	CBI Consulting Inc. Strategic Building Solutions, LLC
200806800505	Hampden-Wilbraham	Minnechaug Regional High School	Closeout	Core Program	New Construction - Model School	DBB	Pinnacle One, Inc.	Mount Vernon Group Architects, Inc.	Fontaine Brothers, Inc.	Horizon Engineering Associates, LLP
201001210005G	Hancock	Hancock Elementary School	Final Audit Approved	Green Repair		DBB	-	-	Salco Construction Company, Inc.	-
200801220505	Hanover	Hanover High School	Closeout	Core Program	New Construction	DBB	PMA Construction Services	HMFH Architects, Inc.	Callahan, Inc.	Horizon Engineering Associates, LLP
201301220015	Hanover	Sylvester	Eligibility Period	Core Program			-	-	-	-
201301270505	Hatfield	Smith Academy	Approved Project Vote Pending	Accelerated Repair			Hill International Company	Civitects	-	Building Enclosure Associates, LLC
201201280035	Haverhill	Caleb Dustin Hunking	Schematic Design	Core Program			Joslin, Lesser + Associates Inc.	JCJ Architecture, PC	-	-
201101280100G	Haverhill	Consentino	Closeout	Green Repair		DBB	Vertex Construction Services	CSS Architects Incorporated	New England Builders & Contractors, Inc.	RDK Engineers Russo Barr Associates, Inc.
W20034393	Haverhill	Haverhill High School	Closeout	Waitlist	Repair - Major		-	-	-	-
201101280085G	Haverhill	John G Whittier	Closeout	Green Repair		DBB	Vertex Construction Services	CSS Architects Incorporated	New England Builders & Contractors, Inc.	Russo Barr Associates, Inc.
201101280075G	Haverhill	Tilton	Closeout	Green Repair		DBB	Vertex Construction Services	CSS Architects Incorporated	Titan Roofing, Inc.	Russo Barr Associates, Inc.
201101280080G	Haverhill	Walnut Square	Closeout	Green Repair		DBB	Vertex Construction Services	CSS Architects Incorporated	Titan Roofing, Inc.	RDK Engineers Russo Barr Associates, Inc.

201001310410	Hingham	Hingham Middle School	Construction	Core Program	New Construction - Model School	DBB	Knight, Bagge & Anderson Inc.	Ai3 Architects LLC	Brait Builders Corp.	Foreman Building Commissioning, LP
200801330505	Holbrook	Holbrook Junior-Senior High School	Schematic Design	Core Program	New Construction		Symmes Maini & McKee Associates, Inc.	Flansburgh Associates, Inc.	-	-
201201370015	Holyoke	Lt Elmer J McMahon Elem	OPM Selection	Core Program			-	-	-	-
201201370605	Holyoke	Wm J Dean Voc Tech High	Building Complete	Science Lab Initiative	Addition / Renovation		Skanska USA Building, Inc	Kaestle Boos Associates, Inc.	RAC Builders, Inc.	BVH Integrated Services, P.C.
201301380010	Hopedale	Memorial	Design Development	Accelerated Repair			Atlantic Construction and Management, Inc.	Civitects	-	Simpson Gumpertz & Heger Inc.
201301390005	Hopkinton	Center	OPM Selection	Core Program			-	-	-	-
200801410410	Hudson	John F. Kennedy Middle School	Building Complete	Core Program	New Construction	DBB	PMA Construction Services	OMR Architects, Inc.	Bacon-Agostini Construction Joint Venture	WSP Flack + Kurtz
201201530007	Leominster	Fall Brook	Closeout	Accelerated Repair			Compass Project Management, Inc.	Reinhardt Associates, Inc.	NB Kenney Company, Inc	Horizon Engineering Associates, LLP
200801530505	Leominster	Leominster High School	Building Complete	Core Program	Addition / Renovation	CM@R	Daedalus Projects Inc	Lamoureux Pagano & Associates, Inc.	S.O.M. Construction Ent., Inc.	Horizon Engineering Associates, LLP
201201530010	Leominster	Southeast School	Closeout	Accelerated Repair			Compass Project Management, Inc.	Reinhardt Associates, Inc.	NB Kenney Company, Inc	Horizon Engineering Associates, LLP Russo Barr Associates, Inc.
201101540005G	Leverett	Leverett Elementary	Closeout	Green Repair		DBB	Potomac Capital Advisors	DiMarinisi & Wolfe Architects Urban Designers	-	Russo Barr Associates, Inc.
201101550010E	Lexington	Joseph Estabrook	Building Complete	Core Program	New Construction	CM@R	Hill International Company	DiNisco Design Partnership, Limited	Shawmut Design and Construction	BVH Integrated Services, P.C.
200801590505	Longmeadow	Longmeadow High School	Building Complete	Core Program	New Construction	CM@R	Joslin, Lesser + Associates Inc.	OMR Architects, Inc.	Gilbane Building Company	Foreman Building Commissioning, LP
201101600505G	Lowell	Lowell High	Final Audit Approved	Green Repair		DBB	NETCO Construction Project Managers, Inc.	ICON architecture, inc.	-	Building Enclosure Associates, LLC
201101600027G	Lowell	Moody Elem	Closeout	Green Repair		DBB	NETCO Construction Project Managers, Inc.	ICON architecture, inc.	Paul J. Rogan Co., Inc.	Building Enclosure Associates, LLC
201101600040G	Lowell	Peter W Reilly	Final Audit Approved	Green Repair		DBB	NETCO Construction Project Managers, Inc.	ICON architecture, inc.	-	Building Enclosure Associates, LLC
201101600055G	Lowell	Washington	Closeout	Green Repair		DBB	NETCO Construction Project Managers, Inc.	ICON architecture, inc.	Alpha Contracting Associates, Inc.	Building Enclosure Associates, LLC RDK Engineers
201001620505	Lunenburg	Lunenburg High School	Design Development	Core Program	New Construction		Joslin, Lesser + Associates Inc.	Tappe Associates, Inc.	Shawmut Design and Construction	Cannon Design
201201630405	Lynn	Breed Middle School	Building Complete	Accelerated Repair			Diversified Project Management	Kaestle Boos Associates, Inc.	GVW, Inc.	CBI Consulting Inc.
201201630605	Lynn	Lynn Voc Tech Institute	Closeout	Accelerated Repair			Diversified Project Management	Kaestle Boos Associates, Inc.	Gibson Roofs, Inc.	CBI Consulting Inc.
200901630305	Lynn	Thurgood Marshall Middle School	Design Development	Core Program	New Construction		Joslin, Lesser + Associates Inc.	Raymond Design Associates, Inc.	Walsh Brothers, Inc.	Rist-Frost-Shumway Engineering, P.C.
200901640505	Lynnfield	Lynnfield High School	Building Complete	Core Program	Addition / Renovation	DBB	HEERY	Edward Rowse Architects, Inc.	E.A. Colangeli Construction Co. Inc	Fitzmeyer & Tocci Associates, Inc.
200801680020	Marblehead	Glover School	Building Complete	Core Program	New Construction	DBB	Municipal Building Consultants, Inc.	JCJ Architecture, PC	G & R Construction, Inc.	RDK Engineers
201101700008G	Marlborough	Francis J Kane	Closeout	Green Repair		DBB	Hill International Company	Baker/Wohl Architects, Inc.	A&A Window Products, Inc.	Building Enclosure Associates, LLC
201101700505G	Marlborough	Marlborough High	Closeout	Green Repair		DBB	Hill International Company	Baker/Wohl Architects, Inc.	A&A Window Products, Inc. Feeley, McAnespie, Inc. Veterans Development Corporation, Inc.	Building Enclosure Associates, LLC RDK Engineers
201101710505	Marshfield	Marshfield High	Construction	Core Program	New Construction - Model School	DBB	Compass Project Management, Inc.	Ai3 Architects LLC	Brait Builders Ventures	Sebesta Blomberg & Associates, Inc.
200801740505	Maynard	Maynard High School	Building Complete	Core Program	New Construction	DBB	Municipal Building Consultants, Inc.	Tappe Associates, Inc.	CTA Construction Co., Inc.	WSP Flack + Kurtz
201201760505	Medford	Medford High	Construction	Science Lab Initiative	Addition / Renovation		Leftfield, LLC	DiNisco Design Partnership, Limited	G & R Construction, Inc.	Cannon Design

201301760505	Medford	Medford High	Design Development	Accelerated Repair			Architectural Consulting Group, LLC	Dietz & Company Architects, Inc.	-	Symmes, Maini & McKee Associates
200801770305	Medway	Medway Middle School	Final Audit Approved	Core Program	Repair - Major	CM@R	Compass Project Management, Inc.	Knigh, Bagge & Anderson, Inc.	Consigli Construction Company, Inc.	Sebesta Blomberg & Associates, Inc.
201201780505	Melrose	Melrose High	Closeout	Science Lab Initiative	Addition / Renovation		Hill International Company	Ai3 Architects LLC	G & R Construction, Inc.	WSP Flack + Kurtz
201107100015G	Mendon-Upton	Miscoe Hill School	Final Audit Approved	Green Repair		DBB	CDR Maguire formerly known as Maguire Group Inc.	Habeeb & Associates Architects, Inc.	Greenwood Industries, Inc.	Sebesta Blomberg & Associates, Inc.
200801810505	Methuen	Methuen High School	Construction	Core Program	Addition / Renovation	CM@R	KBA/Trident	Finegold Alexander and Associates Inc.	Consigli Construction Company, Inc.	Environmental Health and Engineering
201101820025G	Middleborough	Mary K. Goode Elementary School	Closeout	Green Repair		DBB	CDR Maguire formerly known as Maguire Group Inc.	Habeeb & Associates Architects, Inc.	J.J. Cardosi, Inc.	Russo Barr Associates, Inc.
200801840005	Middleton	Howe-Manning School	Final Audit Approved	Core Program	New Construction	DBB	Hill International Company	DiNisco Design Partnership, Limited	CTA Construction Co., Inc.	Foreman Building Commissioning, LP
201101850090	Milford	Woodland	Design Development	Core Program	New Construction		Joslin, Lesser + Associates Inc.	HMFH Architects, Inc.	Shawmut Design and Construction	Consulting Engineering Services, LLC
200908300605	Minuteman Voc Tech	Minuteman Regional High School	Feasibility Study	Core Program			Skanska USA Building, Inc	Kaestle Boos Associates, Inc.	-	-
201107170005G	Mohawk Trail	Buckland-Shelburne Reg	Final Audit Approved	Green Repair		DBB	Potomac Capital Advisors	Bradley Architects, Inc.	-	Strategic Building Solutions, LLC
201107170010G	Mohawk Trail	Colrain Central	Final Audit Approved	Green Repair		DBB	Potomac Capital Advisors	Bradley Architects, Inc.	-	Strategic Building Solutions, LLC
201107170505G	Mohawk Trail	Mohawk Trail Reg High	Final Audit Approved	Green Repair		DBB	Potomac Capital Advisors	Bradley Architects, Inc.	-	Strategic Building Solutions, LLC
201107129999	Monomoy	Monomoy Regional High School	Construction	Core Program	New Construction - Model School	DBB	Skanska USA Building, Inc	Mount Vernon Group Architects, Inc.	Fontaine Brothers, Inc.	Sebesta Blomberg & Associates, Inc.
201307150505	Mount Greylock	Mt Greylock Reg High	Eligibility Period	Core Program	Addition / Renovation		-	-	-	-
201107200003G	Narragansett	Phillipston Memorial	Closeout	Green Repair		DBB	Potomac Capital Advisors	DiMarinisi & Wolfe Architects Urban Designers	-	Rist-Frost-Shumway Engineering, P.C.
200807200020	Narragansett	Templeton Center School	Feasibility Study	Core Program			Strategic Building Solutions, LLC	Symmes Maini & McKee Associates, Inc.	-	-
200807250015	Nashoba	Pompositicut Elementary School	Closeout	Core Program	Addition / Renovation	DBB	Construction Monitoring Services, Inc.	Symmes Maini & McKee Associates, Inc.	P.J. Stella Construction Corp.	Strategic Building Solutions, LLC
200908520605G	Nashoba Valley Tech	Nashoba Valley Tech H S	Closeout	Green Repair		DBB	-	-	-	-
201308520605	Nashoba Valley Tech	Nashoba Valley Tech H S	Approved Project Vote Pending	Accelerated Repair			STV Incorporated	CGKV Architects, Inc.	-	CBI Consulting Inc.
200801980505	Natick	Natick High School	Closeout	Core Program	New Construction - Model School	DBB	Hill International Company	Ai3 Architects LLC	Brait Builders Corp.	Rist-Frost-Shumway Engineering, P.C.
201306600305	Nauset	Nauset Reg Middle	Approved Project Vote Pending	Accelerated Repair			Strategic Building Solutions, LLC	ICON architecture, inc.	-	Russo Barr Associates, Inc.
201106600505G	Nauset	Nauset Regional High	Final Audit Approved	Green Repair		DBB	NETCO Construction Project Managers, Inc.	Habeeb & Associates Architects, Inc.	Modern Glass & Aluminum, Inc.	CBI Consulting Inc.
201301990035	Needham	Hillside Elementary	Eligibility Period	Core Program			-	-	-	-
200901990050	Needham	Newman Elementary School	Closeout	Core Program	Repair - Major	CM@R	-	Drumme Rosane Anderson, Inc.	Consigli Construction Company, Inc.	Rist-Frost-Shumway Engineering, P.C.
200902010070	New Bedford	John Hannigan	Designer Selection	Core Program			Daedalus Projects Inc	-	-	-
W201002010505	New Bedford	New Bedford High	Closeout	Waitlist	Repair - Major	DBB	-	-	-	-
201102040005	Newburyport	Francis T Bresnahan Elem	Construction	Core Program	New Construction - Model School	DBB	HEERY	HMFH Architects, Inc.	CTA Construction Co., Inc.	Fitzemeyer & Tocci Associates, Inc.
201002040305	Newburyport	Rupert A. Nock Middle School	Construction	Core Program	Addition / Renovation	CM@R	HEERY	Miller Dyer Spears Inc.	Gilbane Building Company	Fitzemeyer & Tocci Associates, Inc.
201102070005	Newton	A E Angier	Design Development	Core Program	New Construction		Joslin, Lesser + Associates Inc.	DiNisco Design Partnership, Limited	-	Fitzemeyer & Tocci Associates, Inc.
201102070015G	Newton	Bowen	Final Audit Approved	Green Repair		DBB	-	Habeeb & Associates Architects, Inc.	-	-
201302070025	Newton	Cabot	OPM Selection	Core Program			-	-	-	-
201102070125G	Newton	Williams	Final Audit Approved	Green Repair		DBB	-	-	-	-

200802080005	Norfolk	Freeman-Kennedy Elementary School	Closeout	Core Program	New Construction	DBB	Joslin, Lesser + Associates Inc.	Flansburgh Associates, Inc.	Fontaine Brothers, Inc.	WSP Flack + Kurtz
200909150705	Norfolk County Agriculture	Norfolk County Agr Silvio O Conte Middle School	Construction	Core Program	Addition / Renovation	DBB	Compass Project Management, Inc.	Turowski2 Architecture, Inc.	TLT Construction Corporation	Rist-Frost-Shumway Engineering, P.C.
200802090305	North Adams	Silvio O Conte Middle School	Construction	Core Program	Addition / Renovation		Strategic Building Solutions, LLC	Margo Jones Architects, Inc.	-	Rist-Frost-Shumway Engineering, P.C.
201102110018G	North Andover	Annie L Sargent School	Final Audit Approved	Green Repair		DBB	Municipal Building Consultants, Inc.	ICON architecture, inc.	Varieka Construction, Inc.	Cannon Design
201102110001G	North Andover	Atkinson	Final Audit Approved	Green Repair		DBB	Municipal Building Consultants, Inc.	ICON architecture, inc.	Paul J. Rogan Co., Inc.	Cannon Design
201102110305G	North Andover	North Andover Middle	Final Audit Approved	Green Repair		DBB	Municipal Building Consultants, Inc.	ICON architecture, inc.	Stanley Roofing Company, Inc.	Cannon Design
201202120505	North Attleborough	North Attleboro High	Closeout	Science Lab Initiative	Addition / Renovation		Skanska USA Building, Inc	Kaestle Boos Associates, Inc.	M. O'Connor Contracting, Inc.	Consulting Engineering Services, LLC
201202120015	North Attleborough	Roosevelt Avenue	Building Complete	Accelerated Repair			Skanska USA Building, Inc	Russo Barr Associates, Inc.	Evergreen Construction Corporaation	Gale Associates, Inc.
201102150015G	North Brookfield	North Brookfield Elem	Final Audit Approved	Green Repair		DBB	Vertex Construction Services	-	Lockheed Window Corporations	Simpson Gumpertz & Heger Inc.
201202150015	North Brookfield	North Brookfield Elem	Closeout	Accelerated Repair			Strategic Building Solutions, LLC	CBI Consulting Inc.	Garland Construction Corp.	Simpson Gumpertz & Heger Inc.
201107350010G	North Middlesex	Ashby Elementary	Final Audit Approved	Green Repair		DBB	Compass Project Management, Inc.	Russo Barr Associates, Inc.	GVW, Inc.	Horizon Engineering Associates, LLC
201107350505	North Middlesex	North Middlesex Reg	Design Development	Core Program			HEERY	Symmes Maini & McKee Associates, Inc.	-	Building Enclosure Associates, LLC
201107350005G	North Middlesex	Spaulding Memorial	Final Audit Approved	Green Repair		DBB	Compass Project Management, Inc.	Russo Barr Associates, Inc.	MDM Engineering	Building Enclosure Associates, LLC
201002170505	North Reading	North Reading High School	Construction	Core Program	Addition / Renovation	CM@R	PMA Construction Services	Dore & Whittier Architects, Inc.	Gilbane Building Company	Cannon Design
201102130003	Northborough	Lincoln Street	Design Development	Core Program	Addition / Renovation		Strategic Building Solutions, LLC	Lamoureux Pagano & Associates, Inc.	-	-
201202180015	Norton	J C Solmonese	Closeout	Accelerated Repair			Joslin, Lesser + Associates Inc.	Habeeb & Associates Architects, Inc.	Silktown Roofing	Simpson Gumpertz & Heger Inc.
200902180505	Norton	Norton High School	Building Complete	Core Program	Addition / Renovation	CM@R	Pinck & Co., Inc.	JCJ Architecture, PC	W. T. Rich Company Inc.	Rist-Frost-Shumway Engineering, P.C.
200908550605	Orange	Old Colony Reg Voc Tech	Closeout	Core Program	Repair - Major	DBB	Vertex Construction Services	Habeeb & Associates Architects, Inc.	J.D. Rivet & Co., Inc.	Consulting Engineering Services, LLC
201302230010	Orange	Dexter Park	Eligibility Period	Core Program			-	-	-	-
200802260405	Oxford	Oxford Middle School	Construction	Core Program	Repair - Major	DBB	Diversified Project Management	CGKV Architects, Inc.	J.J. Cardosi, Inc.	Cannon Design
201102270305G	Palmer	Converse Middle	Closeout	Green Repair		DBB	Diversified Project Management	-	Royal Steam Heater Co. Titan Roofing, Inc.	Strategic Building Solutions, LLC
201102270008G	Palmer	Old Mill Pond	Closeout	Green Repair		DBB	Diversified Project Management	-	Royal Steam Heater Co.	Strategic Building Solutions, LLC
201102270505G	Palmer	Palmer High	Closeout	Green Repair		DBB	Diversified Project Management	-	Royal Steam Heater Co. Titan Roofing, Inc.	Strategic Building Solutions, LLC
201308600605	Pathfinder Voc Tech	Pathfinder Voc Tech	Approved Project Vote Pending	Accelerated Repair			exPERTcon, Inc.	Baker/Wohl Architects, Inc.	-	Building Enclosure Associates, LLC
200802290305	Peabody	Higgins Middle School	Design Development	Core Program			Daedalus Projects Inc	DiNisco Design Partnership, Limited	-	BVH Integrated Services, P.C.
201102290007G	Peabody	John E Burke	Closeout	Green Repair		DBB	Daedalus Projects Inc	LPBA/ Architects, Inc.	-	Sebesta Blomberg & Associates, Inc.
201102290027G	Peabody	William A Welch Sr	Closeout	Green Repair		DBB	Daedalus Projects Inc	LPBA/ Architects, Inc.	-	Sebesta Blomberg & Associates, Inc.
201302310010	Pembroke	Hobomock Elementary	Design Development	Accelerated Repair			Pinck & Co., Inc.	The S/L/A/M Collaborative	-	CBI Consulting Inc.
201302310015	Pembroke	North Pembroke Elem	Design Development	Accelerated Repair			Pinck & Co., Inc.	The S/L/A/M Collaborative	-	CBI Consulting Inc.
201302310305	Pembroke	Pembroke Community Middle School	Design Development	Accelerated Repair			Pinck & Co., Inc.	The S/L/A/M Collaborative	-	CBI Consulting Inc.
201302310505	Pembroke	Pembroke High School	Design Development	Accelerated Repair			Pinck & Co., Inc.	The S/L/A/M Collaborative	-	CBI Consulting Inc.

201107450020G	Pentucket	Dr Frederick N Sweetsir	Closeout	Green Repair		DBB	PMA Construction Services	Knight, Bagge & Anderson, Inc.	E. Amanti & Sons, Inc.	CBI Consulting Inc. RDK Engineers
201107450015G	Pentucket	Dr John C Page School	Closeout	Green Repair		DBB	PMA Construction Services	Knight, Bagge & Anderson, Inc.	Capeway Roofing Systems, Inc.	CBI Consulting Inc. RDK Engineers
201107450005G	Pentucket	Elmer S Bagnall	Final Audit Approved	Green Repair		DBB	PMA Construction Services	Knight, Bagge & Anderson, Inc.	Gibson Roofs, Inc.	CBI Consulting Inc. RDK Engineers
201307450405	Pentucket	Pentucket Reg Middle	Design Development	Accelerated Repair			Arcadis U.S., Inc.	CGKV Architects, Inc.	-	CBI Consulting Inc. Strategic Building Solutions, LLC
201107500008G	Pioneer Valley	Northfield Elementary	Closeout	Green Repair		DBB	Diversified Project Management	CGKV Architects, Inc.	-	Strategic Building Solutions, LLC
201107500505G	Pioneer Valley	Pioneer Valley Reg	Closeout	Green Repair		DBB	Diversified Project Management	CGKV Architects, Inc.	-	Strategic Building Solutions, LLC
201002360510	Pittsfield	Taconic High School	Feasibility Study	Core Program			Skanska USA Building, Inc	Drummey Rosane Anderson, Inc.	-	-
200802390505	Plymouth	Plymouth North High School	Closeout	Core Program	New Construction - Model School	DBB	Ted Gentry Associates, Inc	Ai3 Architects LLC	-	Sebesta Blomberg & Associates, Inc.
201202390515	Plymouth	Plymouth South High	Schematic Design	Core Program	New Construction		Ted Gentry Associates, Inc	Ai3 Architects LLC	-	-
201302420505	Provincetown	Provincetown High	Eligibility Period	Core Program			-	-	-	-
201207530030	Quabbin	Ruggles Lane	Closeout	Accelerated Repair		DBB	Vertex Construction Services	Turowski2 Architecture, Inc.	PDS Engineering and Construction, Inc.	Simpson Gumpertz & Heger Inc.
201207780005	Quabog Regional	Warren Elementary	Building Complete	Accelerated Repair			Coast and Harbor Association, Inc.	Lindgren & Sharples, Inc.	AAlanco Service Corporation	Strategic Building Solutions, LLC
200802430315	Quincy	Central Middle School	Building Complete	Core Program	New Construction - Model School	DBB	Tishman Construction Corporation of MA	Ai3 Architects LLC	H.V. Collins Co., Inc.	Sebesta Blomberg & Associates, Inc.
201302430060	Quincy	Merrymount	Design Development	Accelerated Repair			Skanska USA Building, Inc	Habeeb & Associates Architects, Inc.	-	Simpson Gumpertz & Heger Inc.
201302430510	Quincy	North Quincy High	Design Development	Accelerated Repair			Skanska USA Building, Inc	Habeeb & Associates Architects, Inc.	-	Simpson Gumpertz & Heger Inc.
201302430320	Quincy	Reay E Sterling Middle	Eligibility Period	Core Program			-	-	-	-
201302430110	Quincy	Wollaston School	Design Development	Accelerated Repair			Skanska USA Building, Inc	Habeeb & Associates Architects, Inc.	-	Simpson Gumpertz & Heger Inc.
201302440410	Randolph	Randolph Community Middle	Design Development	Accelerated Repair			NETCO Construction Project Managers, Inc.	Taylor & Burns, Inc.	-	Consulting Engineering Services, LLC
201302440505	Randolph	Randolph High	Design Development	Accelerated Repair			NETCO Construction Project Managers, Inc.	-	-	Gale Associates, Inc.
201002480035	Revere	Staff Sergeant James J. Hill School	Construction	Core Program	New Construction		Hill International Company	-	CTA Construction Co., Inc.	Rist-Frost-Shumway Engineering, P.C.
200802510305	Rockland	John W. Rogers Middle School	Closeout	Core Program	New Construction	CM@R	Daedalus Projects Inc	Dore & Whittier Architects, Inc.	Agostini Construction Co., Inc.	Consulting Engineering Services, LLC
201102510025G	Rockland	R Stewart Esten	Closeout	Green Repair		DBB	Daedalus Projects Inc	Habeeb & Associates Architects, Inc.	Northeast Energy Control Systems	Russo Barr Associates, Inc.
200902580305G	Salem	Collins Middle School	Building Complete	Green Repair		CM@R	KV Associates, Inc.	Reinhardt Associates, Inc.	Gilbane Building Company	Rist-Frost-Shumway Engineering, P.C.
201002580050G	Salem	Saltonstall School	Building Complete	Green Repair		CM@R	KV Associates, Inc.	Reinhardt Associates, Inc.	Gilbane Building Company	Rist-Frost-Shumway Engineering, P.C.
201102610010G	Sandwich	Forestdale	Closeout	Green Repair		DBB	NETCO Construction Project Managers, Inc.	Habeeb & Associates Architects, Inc.	Varieka Construction, Inc.	Gale Associates, Inc.
200902610025G	Sandwich	Oak Ridge School	Closeout	Green Repair		DBB	NETCO Construction Project Managers, Inc.	Habeeb & Associates Architects, Inc.	J.J. Cardosi, Inc.	Gale Associates, Inc.
201002620305	Saugus	Belmonte Middle School	Closeout	Core Program	Repair - Major	CM@R	Skanska USA Building, Inc	Fletcher Thompson Architecture Engineering, LLC	Consigli Construction Company, Inc.	Consulting Engineering Services, LLC
201202640305	Scituate	Gates Intermediate School	Feasibility Study	Core Program			Daedalus Projects Inc	-	-	-
200802660305	Sharon	Sharon Middle School	Closeout	Core Program	Addition / Renovation	CM@R	Daedalus Projects Inc	Kaestle Boos Associates, Inc.	Consigli Construction Company, Inc.	Horizon Engineering Associates, LLP
201208710605	Shawsheen Valley	Shawsheen Valley Voc Tech High School	Closeout	Accelerated Repair			Diversified Project Management	Shekar & Associates, Inc.	NB Kenney Company, Inc	Fitzmeyer & Tocci Associates, Inc.
201302710005	Shrewsbury	Beal School	Eligibility Period	Core Program			-	-	-	-

200802710305	Shrewsbury	Sherwood Middle School	Building Complete	Core Program	New Construction	CM@R	PMA Construction Services	Lamoureux Pagano & Associates, Inc.	Gilbane Building Company	RDK Engineers
201102710035G	Shrewsbury	Spring Street	Closeout	Green Repair		DBB	PMA Construction Services	Habeeb & Associates Architects, Inc.	Lambrian Construction Corp.	Cannon Design
201308290605	So Middlesex Voc Tech Reg	Joseph P Keefe Tech HS	Design Development	Accelerated Repair			PMA Construction Services	Raymond Design Associates, Inc.	-	Russo Barr Associates, Inc.
200811119999	Somerset-Berkley	Somerset-Berkley High	Construction	Core Program	New Construction - Model School	DBB	Skanska USA Building, Inc	Ai3 Architects LLC	Bacon-Agostini Construction Joint Venture	Horizon Engineering Associates, LLP
200902740111E	Somerville	East Somerville Community School at Cummings	Closeout	Core Program	Addition / Renovation	CM@R	PMA Construction Services	Maguire Group Inc.	Gilbane Building Company	Foreman Building Commissioning, LP
201302740505	Somerville	Somerville High	Eligibility Period	Core Program			-	-	-	-
200902780015	South Hadley	Plains School	Construction	Core Program	New Construction		Arcadis U.S., Inc.	Margo Jones Architects, Inc.	-	Strategic Building Solutions, LLC
201202750005	Southampton	William E Norris	Construction	Accelerated Repair			Tishman Construction Corporation of MA	Reinhardt Associates, Inc.	Greenwood Industries, Inc.	Building Enclosure Associates, LLC
200802770505	Southbridge	Southbridge High School	Closeout	Core Program	New Construction	CM@R	Joslin, Lesser + Associates Inc.	Tappe Associates, Inc.	Consigli Construction Company, Inc.	Environmental Health and Engineering
200908720605	Southeastern Reg Voc Tech	Southeastern Regional Vocational Technical School	Closeout	Core Program	Addition / Renovation	CM@R	Hill International Company	Drummey Rosane Anderson, Inc.	Greenwood Industries, Inc. W. T. Rich Company Inc.	RDK Engineers
200908760605	Southern Worcester Cty VT	Bay Path Regional Vocational Technical High School	Construction	Core Program	Addition / Renovation	CM@R	HEERY	Kaestle Boos Associates, Inc.	Consigli Construction Company, Inc.	RDK Engineers
201107660305	Southwick-Tolland	Powder Mill	Construction	Core Program	Repair - Major	DBB	Strategic Building Solutions, LLC	JCJ Architecture, PC	PDS Engineering and Construction, Inc.	BVH Integrated Services, P.C.
201107660505	Southwick-Tolland	Southwick-Tolland Regional High	Construction	Core Program	Addition / Renovation	DBB	Strategic Building Solutions, LLC	JCJ Architecture, PC	Fontaine Brothers, Inc.	BVH Integrated Services, P.C.
200807660010	Southwick-Tolland	Woodland Elementary School	Construction	Core Program	Addition / Renovation	DBB	Strategic Building Solutions, LLC	JCJ Architecture, PC	PDS Engineering and Construction, Inc.	BVH Integrated Services, P.C.
201102810175G	Springfield	Alice B Beal Elem	Closeout	Green Repair			-	-	-	Building Enclosure Associates, LLC
200902810165G	Springfield	Arthur T Talmadge	Closeout	Green Repair			-	-	-	-
201302810310	Springfield	Chestnut Accelerated Middle School	Design Development	Accelerated Repair			-	-	-	Building Enclosure Associates, LLC
201102810125E	Springfield	Dryden Memorial	Building Complete	Core Program	Addition / Renovation	CM@R	Arcadis U.S., Inc.	Drummey Rosane Anderson, Inc.	Morganti/Aquadro & Cerruti	BVH Integrated Services, P.C.
201102810030E	Springfield	Elias Brookings	Construction	Core Program	New Construction	CM@R	Arcadis U.S., Inc.	Drummey Rosane Anderson, Inc.	Morganti/Aquadro & Cerruti	BVH Integrated Services, P.C.
W20014137	Springfield	Forest Park Middle School	Building Complete	Waitlist	Addition / Renovation	CM@R	Arcadis U.S., Inc.	Perkins Eastman	Consigli Construction Company, Inc.	Foreman Building Commissioning, LP
200902810075G	Springfield	Frank H Freedman	Closeout	Green Repair			-	-	-	Building Enclosure Associates, LLC
200902810068G	Springfield	Glickman Elementary	Closeout	Green Repair			-	-	-	Building Enclosure Associates, LLC
201302810530	Springfield	High School/Science-Tech	Construction	Accelerated Repair			Atlantic Construction and Management, Inc.	CBI Consulting Inc.	-	Building Enclosure Associates, LLC
200902810320G	Springfield	John J Duggan Middle	Closeout	Green Repair			-	-	-	Building Enclosure Associates, LLC
200902810330G	Springfield	M Marcus Kiley Middle	Closeout	Green Repair			-	-	-	Building Enclosure Associates, LLC
200802810060G	Springfield	Margaret C Ells	Closeout	Green Repair			-	-	-	Building Enclosure Associates, LLC
201302810060	Springfield	Margaret C Ells	Design Development	Accelerated Repair			Atlantic Construction and Management, Inc.	CBI Consulting Inc.	-	Building Enclosure Associates, LLC
200902810140G	Springfield	Mary M Lynch	Closeout	Green Repair			-	-	-	Building Enclosure Associates, LLC
200902810155G	Springfield	Mary M Walsh	Closeout	Green Repair			-	-	-	Building Enclosure Associates, LLC
200902810023G	Springfield	Milton Bradley School	Closeout	Green Repair			-	-	-	Building Enclosure Associates, LLC

W20054428	Springfield	Roger L. Putnam Vocational Technical High School	Closeout	Waitlist	New Construction	CM@R	Pinnacle One, Inc.	Drumme Rosane Anderson, Inc.	Consigli/Morganti	Strategic Building Solutions, LLC
201302810355	Springfield	South End Middle School	Design Development	Accelerated Repair			Atlantic Construction and Management, Inc.	CBI Consulting Inc.	-	Building Enclosure Associates, LLC
201202810500	Springfield	Springfield Central High	Construction	Science Lab Initiative	Addition / Renovation	CM@R	Leftfield, LLC	DiNisco Design Partnership, Limited	Morganti/Aquadro & Cerruti	Horizon Engineering Associates, LLP
201302810550	Springfield	Springfield Public Day High School	Design Development	Accelerated Repair			Atlantic Construction and Management, Inc.	CBI Consulting Inc.	-	Building Enclosure Associates, LLC
200902810180G	Springfield	Warner	Closeout	Green Repair			-	-	-	Building Enclosure Associates, LLC
200902810185G	Springfield	Washington	Closeout	Green Repair			-	-	-	Building Enclosure Associates, LLC
200902810190G	Springfield	White Street	Closeout	Green Repair			-	-	-	Building Enclosure Associates, LLC
200902840405	Stoneham	Stoneham Middle School	Construction	Core Program	Addition / Renovation	CM@R	Joslin, Lesser + Associates Inc.	Tappe Associates, Inc.	Shawmut Design and Construction	RDK Engineers
201302850010	Stoughton	Helen Hansen Elementary	Approved Project Vote Pending	Accelerated Repair			Hill International Company	Taylor & Burns, Inc.	-	-
201302850014	Stoughton	Joseph R Dawe Jr Elem	Approved Project Vote Pending	Accelerated Repair			Hill International Company	Taylor & Burns, Inc.	-	-
201302850505	Stoughton	Stoughton High	Eligibility Period	Core Program			-	-	-	-
201302850020	Stoughton	West Elementary	Approved Project Vote Pending	Accelerated Repair			Hill International Company	Taylor & Burns, Inc.	-	-
200802870005	Sturbridge	Burgess Elementary School	Building Complete	Core Program	Addition / Renovation	DBB	Lamoureux Pagano & Associates, Inc.	Drumme Rosane Anderson, Inc.	Fontaine Brothers, Inc.	Horizon Engineering Associates, LLP
201202880025	Sudbury	General John Nixon Elem	Closeout	Accelerated Repair			PMA Construction Services	ICON architecture, inc.	Silktown Roofing	Gale Associates, Inc.
200802900305	Sutton	Sutton Middle School	Construction	Core Program	Addition / Renovation	DBB	Strategic Building Solutions, LLC	Flansburgh Associates, Inc.	Brait Builders Corp.	RDK Engineers
201102910010	Swampscott	Hadley	Schematic Design	Core Program	New Construction		Hill International Company	Mount Vernon Group Architects, Inc.	-	-
201202930057	Taunton	H H Galligan	Closeout	Accelerated Repair			Arcadis U.S., Inc.	Knight, Bagge & Anderson, Inc.	Capeway Roofing Systems, Inc.	Gale Associates, Inc.
200802950505	Tewksbury	Tewksbury Memorial High School	Closeout	Core Program	New Construction - Model School	DBB	HEERY	Symmes Maini & McKee Associates, Inc.	CTA Ventures	Sebesta Blomberg & Associates, Inc.
201208780605	Tri County	Tri County Reg Voc Tech	Closeout	Science Lab Initiative			Hill International Company	Ai3 Architects LLC	Federal Construction Corp.	-
201108790605G	Upper Cape Cod Voc Tech	Upper Cape Cod Voc Tech	Final Audit Approved	Green Repair		DBB	NETCO Construction Project Managers, Inc.	Knight, Bagge & Anderson, Inc.	Modern Glass & Aluminum, Inc.	Gale Associates, Inc.
200803040505	Uxbridge	Uxbridge High	Closeout	Core Program	New Construction	CM@R	Joslin, Lesser + Associates Inc.	Raymond Design Associates, Inc.	Shawmut Design and Construction	Turner Facilities Management Solutions
200907750305	Wachusett	Mountview Middle School	Design Development	Core Program	New Construction		-	Lamoureux Pagano & Associates, Inc.	-	Fitzmeyer & Tocci Associates, Inc.
201107750035G	Wachusett	Naquag Elementary	Closeout	Green Repair		DBB	Strategic Building Solutions, LLC	LPBA/ Architects, Inc.	MDM Engineering	Rist-Frost-Shumway Engineering, P.C.
201107750040G	Wachusett	Paxton Center	Closeout	Green Repair		DBB	Strategic Building Solutions, LLC	LPBA/ Architects, Inc.	MDM Engineering	Rist-Frost-Shumway Engineering, P.C.
201107750045G	Wachusett	Thomas Prince	Closeout	Green Repair		DBB	Strategic Building Solutions, LLC	LPBA/ Architects, Inc.	MDM Engineering	Rist-Frost-Shumway Engineering, P.C.
201003050310	Wakefield	Galvin Middle School	Construction	Core Program	New Construction	CM@R	Joslin, Lesser + Associates Inc.	Tappe Associates, Inc.	Bond Brothers, Inc.	B2Q Associates, Inc.
201303070015	Walpole	Fisher	Design Development	Accelerated Repair			-	-	-	Gale Associates, Inc.
201303100505	Wareham	Wareham Senior High	Design Development	Accelerated Repair			Hill International Company	Tighe & Bond, Inc.	-	Russo Barr Associates, Inc.
200803150505	Wayland	Wayland High School	Final Audit Approved	Core Program	New Construction	CM@R	KV Associates, Inc.	HMFH Architects, Inc.	Shawmut Design and Construction	WSP Flack + Kurtz
201203150305	Wayland	Wayland Middle School	Closeout	Accelerated Repair			Joslin, Lesser + Associates Inc.	DiMarinisi & Wolfe Architects Urban Designers	Capeway Roofing Systems, Inc.	CBI Consulting Inc.
200903160015	Webster	Park Avenue Elementary School	Construction	Core Program	New Construction	DBB	Hill International Company	Dore & Whittier Architects, Inc.	CTA Construction Co., Inc.	Cannon Design

200803170505	Wellesley	Wellesley Senior School	Closeout	Core Program	New Construction	CM@R	-	Symmes Maini & McKee Associates, Inc.	-	Rist-Frost-Shumway Engineering, P.C.
201303180005	Wellfleet	Wellfleet Elementary	Approved Project Vote Pending	Accelerated Repair			Architectural Consulting Group, LLC	CSS Architects Incorporated	-	Russo Barr Associates, Inc.
201103220005G	West Boylston	Major Edwards Elementary	Closeout	Green Repair			URS Corporation	Reinhardt Associates, Inc.	-	Cannon Design
201003230505	West Bridgewater	West Bridgewater Middle-Senior High School	Construction	Core Program	New Construction	DBB	Strategic Building Solutions, LLC	Flansburgh Associates, Inc.	CTA Construction Co., Inc.	Cannon Design
200903230505	West Springfield	West Springfield High School	Building Complete	Core Program	New Construction - Model School	DBB	Strategic Building Solutions, LLC	Symmes Maini & McKee Associates, Inc.	Fontaine Brothers, Inc.	Turner Facilities Management Solutions
200903210305	Westborough	Gibbons Middle School	Feasibility Study	Core Program			HEERY	Habeeb & Associates Architects, Inc.	-	-
200903250020	Westfield	Abner Gibbs Elementary School	Construction	Core Program	New Construction - Model School	DBB	Skanska USA Building, Inc.	Margo Jones Architects, Inc.	Fontaine Brothers, Inc.	Horizon Engineering Associates, LLP
201003250025G	Westfield	Highland	Final Audit Approved	Green Repair			-	-	-	Strategic Building Solutions, LLC
201103250033E	Westfield	Munger Hill	Closeout	Accelerated Repair			Vertex Construction Services	Knight, Bagge & Anderson, Inc.	Allied Restoration Corporation	Building Enclosure Associates, LLC
201103250036G	Westfield	Paper Mill	Final Audit Approved	Green Repair			-	Tighe & Bond, Inc.	-	Strategic Building Solutions, LLC
201203250036	Westfield	Paper Mill	Closeout	Accelerated Repair			Vertex Construction Services	Knight, Bagge & Anderson, Inc.	R & H Roofing, LLP	Building Enclosure Associates, LLC
201003250040G	Westfield	Southampton Road	Final Audit Approved	Green Repair			-	-	-	Strategic Building Solutions, LLC Strategic Building Solutions, LLC
201103250505G	Westfield	Westfield High	Final Audit Approved	Green Repair			-	Tighe & Bond, Inc.	-	Strategic Building Solutions, LLC
201103250605G	Westfield	Westfield Voc Tech High	Final Audit Approved	Green Repair			-	-	-	Strategic Building Solutions, LLC
201303260025	Westford	Col John Robinson	Design Development	Accelerated Repair			Strategic Building Solutions, LLC	Gale Associates, Inc.	-	CBI Consulting Inc.
201303260007	Westford	Day Elementary	Schematic Design	Accelerated Repair			Strategic Building Solutions, LLC	Gale Associates, Inc.	-	-
201303270005	Westhampton	Westhampton Elem School	Design Development	Accelerated Repair			Atlantic Construction and Management, Inc.	CSS Architects Incorporated	-	Building Enclosure Associates, LLC
200903300012	Weston	Field Elementary School	Construction	Core Program	New Construction	DBB	Compass Project Management, Inc.	Jonathan Levi Architects LLC	Colantonio, Inc.	Foreman Building Commissioning, LP
201103300505G	Weston	Weston High	Final Audit Approved	Green Repair			Compass Project Management, Inc.	Garcia Galuska DeSousa Consulting Engineers Inc.	-	RDK Engineers
201103310015G	Westport	Alice A Macomber	Final Audit Approved	Green Repair			Pinck & Co., Inc.	CGKV Architects, Inc.	-	CBI Consulting Inc.
201103310505G	Westport	Westport High	Final Audit Approved	Green Repair			Pinck & Co., Inc.	CGKV Architects, Inc.	-	CBI Consulting Inc.
201203360080	Weymouth	William Seach	Closeout	Accelerated Repair			PMA Construction Services	BLW Engineers, Inc.	Multitemp Mechanical Corporation	B2Q Associates, Inc.
200907800025	Whitman-Hanson	Maquan Elementary School	Approved Project Vote Pending	Core Program	New Construction		Knight, Bagge & Anderson Inc.	Turoski2 Architecture, Inc.	-	-
200803400005	Williamsburg	Anne T. Dunphy School	Construction	Core Program	Addition / Renovation	DBB	Arcadis U.S., Inc.	Drummeey Rosane Anderson, Inc.	Enfield Builders, Inc.	B2Q Associates, Inc.
201203420060	Wilmington	North Intermediate	Construction	Accelerated Repair			Diversified Project Management	-	-	CBI Consulting Inc.
200903420505	Wilmington	Wilmington High School	Construction	Core Program	New Construction	CM@R	Joslin, Lesser + Associates Inc.	Dore & Whittier Architects, Inc.	Gilbane Building Company	Symmes, Maini & McKee Associates
200803440025	Winchester	Vinson-Owen Elementary School	Building Complete	Core Program	New Construction	DBB	Skanska USA Building, Inc	Tappe Associates, Inc.	CTA Construction Co., Inc.	Turner Facilities Management Solutions
201003440505	Winchester	Winchester High School	Design Development	Core Program	Addition / Renovation		Skanska USA Building, Inc	Symmes Maini & McKee Associates, Inc.	-	RDK Engineers
200803460505	Winthrop	Winthrop High School	Design Development	Core Program			Skanska USA Building, Inc	HMFH Architects, Inc.	-	WSP Flack + Kurtz
200803470015	Woburn	Goodyear School	Final Audit Approved	Core Program	New Construction	CM@R	Municipal Building Consultants, Inc.	Tappe Associates, Inc.	-	Strategic Building Solutions, LLC

201203470060	Woburn	Wyman	Feasibility Study	Core Program			Municipal Building Consultants, Inc.	DiNisco Design Partnership, Limited	-	-
201203480052	Worcester	Chandler Magnet	Construction	Accelerated Repair			Tishman Construction Corporation of MA	Turowski2 Architecture, Inc.	J.J. Cardosi, Inc.	Russo Barr Associates, Inc.
201303480060	Worcester	Columbus Park	Approved Project Vote Pending	Accelerated Repair			Architectural Consulting Group, LLC	The S/L/A/M Collaborative	-	RDK Engineers Russo Barr Associates, Inc.
201203488099	Worcester	Dr. James Caradonio Center	Building Complete	Accelerated Repair			Tishman Construction Corporation of MA	Turowski2 Architecture, Inc.	CAM HVAC & Construction, Inc.	RDK Engineers Russo Barr Associates, Inc.
201203480140	Worcester	Jacob Hiatt Magnet	Building Complete	Accelerated Repair			Tishman Construction Corporation of MA	Turowski2 Architecture, Inc.	CAM HVAC & Construction, Inc.	RDK Engineers
201203480145	Worcester	Lake View	Building Complete	Accelerated Repair			Tishman Construction Corporation of MA	Turowski2 Architecture, Inc.	J.J. Cardosi, Inc.	Russo Barr Associates, Inc.
201203480175	Worcester	May Street	Building Complete	Accelerated Repair			Tishman Construction Corporation of MA	Turowski2 Architecture, Inc.	J.J. Cardosi, Inc.	Russo Barr Associates, Inc.
201203480200	Worcester	Nelson Place	Feasibility Study	Core Program			Tishman Construction Corporation of MA	Lamoureux Pagano & Associates, Inc.	-	-
W20004048	Worcester	North High School	Closeout	Waitlist	New Construction	CM@R	-	-	-	-
201303480230	Worcester	Tatnuck	Approved Project Vote Pending	Accelerated Repair			Architectural Consulting Group, LLC	The S/L/A/M Collaborative	-	Russo Barr Associates, Inc.
201303480225	Worcester	Worcester Arts Magnet Sch	Approved Project Vote Pending	Accelerated Repair			Architectural Consulting Group, LLC	The S/L/A/M Collaborative	-	Russo Barr Associates, Inc.
201303480420	Worcester	Worcester East Middle	Approved Project Vote Pending	Accelerated Repair			Architectural Consulting Group, LLC	The S/L/A/M Collaborative	-	RDK Engineers

2014 Estimated Bid Dates

Note bid dates are **Estimates ONLY**. Please contact Districts for exact information.

Total Project Budget denotes total District costs and does not denote the basis of the MSBA Total Facilities Grant.

■ - Denotes bid phase in progress or complete
 ■ - Denotes estimated bid dates
 ■ - Denotes estimated GMP dates

DISTRICT <small>*Projects Considering the CM @ Risk Method</small>	DESIGN BASIS FOR ENROLLMENT	PROJECT BUDGET <small>Shown in Millions</small>	CONSTRUCTION BUDGET <small>Shown in Millions</small>	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC
*AYER SHIRLEY RSD	495	\$56.5	\$44.4					Ayer Shirely RHS - Addition/Renovation: Filed-Sub Bids Due 9/25. GMP Issued March.							
REVERE	690	\$44.4	\$33.9					Staff Sergeant James J. Hill (McKinley) ES - New Construction: Filed-Sub Bids received 1/14. G.C. Bids received 1/23. NTP Issued March.							
NORTH ADAMS	310	\$29.7	\$21.9					Silvio O. Conte MS - New Construction: Filed-Sub Bids received 2/24. G.C. Bids received 3/17. NTP Issued April.							
*GREATER LOWELL RSD	1990	\$65.3	\$53.2					Greater Lowell RVTHS - Repair: Filed-Sub Bids received 2/21. GMP Issued March.							
*AUBURN	560	\$44.5	\$35.5					Auburn MS - New Construction: Filed-Sub Bids received 4/24. GMP Targeted June.							
WACHUSETT RSD	800	\$54.3	\$43.1					Mountview MS - New Construction: Filed-Sub Bids received 4/10. G.C. Bids Due 5/13. NTP Targeted May.							
CHICOPEE	850	\$38.0	\$30.8					Chicopee Academy - Renovation: Filed-Sub Bids received 4/23. G.C. Bids Due 5/14. NTP Targeted May.							
SOUTH HADLEY	270	\$28.2	\$21.6					Plains ES - New Construction: Filed-Sub Bids received 4/10. G.C. Bids received 4/22. NTP Targeted May.							
PEABODY	1340	\$92.6	\$75.1					Higgins MS - New Construction: Filed-Sub Bids Due 5/15. G.C. Bids Due 5/27. NTP Targeted June.							
GREATER LAWRENCE RVTSD	1400	\$5.2	\$4.4					Greater Lawrence RVTHS - Repair: Filed-Sub Bids Due 5/21. G.C. Bids Due 5/29. NTP Targeted June.							
*LYNN	1100	\$92.0	\$67.7					Thurgood Marshall MS - New Construction: Filed-Sub Bids Due 9/26. GMP Targeted October.							
*NEWTON	465	\$37.5	\$26.2					Angier ES - New Construction: Filed-Sub Bids Due 10/6. GMP Targeted October.							
ATHOL-ROYALSTON RSD	545	\$43.9	35.2					Riverbend ES - New Construction: Filed-Sub Bids Due 10/15. G.C. Bids Due 10/31. NTP Targeted November.							
*WINCHESTER	1370	\$129.9	100.9					Winchester HS - Addition/Renovation: Filed-Sub Bids Due 10/20. GMP Targeted November.							
Subtotal	12,185	\$762.0	\$593.9												
GRAND TOTAL	12,185	\$762.0	\$593.9												

2015 Estimated Bid Dates

Note bid dates are **Estimates ONLY**. Please contact Districts for exact information.

Total Project Budget denotes total District costs and does not denote the basis of the MSBA Total Facilities Grant.

■ - Denotes bid phase in progress or complete
 ■ - Denotes estimated bid dates
 ■ - Denotes estimated GMP dates

DISTRICT <small>*Projects Considering the CM @ Risk Method</small>	DESIGN BASIS FOR ENROLLMENT	PROJECT BUDGET <small>Shown in Millions</small>	CONSTRUCTION BUDGET <small>Shown in Millions</small>	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC
*WINTHROP	970	\$80.2	\$61.9												
NORTHBOROUGH	270	\$25.5	\$18.2												
GEORGETOWN	720	\$7.8	\$5.9												
Subtotal	1,960	\$113.5	\$86.0												
GRAND TOTAL	1,960	\$113.5	\$86.0												

**Projects in Construction
MSBA Grant Basis and Maximum Grant Amount
Data Reported as of May 14, 2014**

Core Program and Waitlist Totals			\$2,555,152,746	52,252		10,344,717												*Includes Alternates	\$1,622,710,664
Project	Grade	Contractor	Total Construction Cost*	Projected Enrollment	PFA or Bid Data	Proposed Sq.Ft.	Construction Cost/Sq.Ft.	Building Cost	Building Cost/Sq.Ft.	Procurement Type	Construction Start Date	Substantial Completion	Schedule Variance (days)	Physical Progress	Change Orders	Change Orders %	Construction Status	Estimated Max Total Facilities Grant	
CAPITAL PIPELINE PROJECTS IN CONSTRUCTION																			
Core Program Totals			\$2,520,406,848	51,592		10,195,917												\$1,583,703,811	
Arlington Thompson	Elementary School	G & R Construction, Inc.	\$15,340,026	380	Bid	57,614	\$266	\$12,403,811	\$215	Design/Bid/Build	07-Apr-12	21-Aug-13	0	100%	\$473,245	3.085%	The new school building is in service. Final site work is complete except minor landscaping work to be completed by the end of June 2014.	\$8,996,284	
Assabet Valley Assabet Valley Voc H S	Vocational / Technical	CTA Construction Co., Inc.	\$46,764,740	963	Bid	367,565	\$127	\$41,523,764	\$113	Design/Bid/Build	01-Apr-13	01-Aug-15	0	40%	\$371,205	0.794%	This is a (10) phase project. Ph 1 ,2 ,3 and 4 are complete. Punch list items in Ph 2 & 3 are 90% complete and punch list for Ph 4 is ongoing. Work includes demo of ceiling tiles, demo of the Mechanical Room, HVAC work and abatement, MEP work, windows, roofing, flooring and painting for these areas. Certificate of Occupancy for Ph 2 was received which allowed students and staff back into the building in that location. Ph 5 has begun and is scheduled for completion on June 30, 2014.	\$28,790,301	
Berlin-Boylston Tahanto Reg High	High School	CTA Construction Co., Inc.	\$32,162,000	560	Bid	126,100	\$255	\$24,629,999	\$195	Design/Bid/Build	10-May-11	01-Jul-13	0	99%	\$1,026,723	3.282%	The new school building is in service. Resolution of a few remaining landscaping and commissioning punch list items are in process and are forecast for completion by June 30, 2014. A contract has been awarded for installation of ceramic tile rain screen which is scheduled to be substantially complete by August 25, 2014.	\$18,717,193	
Danvers Danvers High	High School	Bacon Construction Co, Inc.	\$53,834,164	1,000	Bid	246,251	\$219	\$43,710,809	\$178	Design/Bid/Build	14-Nov-10	10-Jul-13	0	100%	\$1,350,044	2.508%	Final site punch list items are ongoing. Project Closeout is in process.	\$34,409,979	
Douglas Douglas Elementary	Elementary School	CTA Construction Co., Inc.	\$24,275,111	552	Bid	83,100	\$292	\$19,026,763	\$229	Design/Bid/Build	02-Mar-12	26-Aug-13	0	99%	\$303,336	1.272%	Punch list is being completed during off hours while school is in session.	\$15,297,961	
Dracut Dracut Senior High	High School	CTA Construction Co., Inc.	\$45,900,000	1,160	Bid	226,844	\$202	\$38,377,028	\$169	Design/Bid/Build	27-Aug-12	26-Aug-14	90 behind	80%	\$282,540	0.616%	Work continues in several areas including the library, locker rooms, renovated C academic wing, admin wing, auditorium & site. Work also continues on punch list items of all turned over phases. Next milestone is turnover of the library & locker rm wing by July 31, 2014. After that the Admin wing, Remodeled C wing and site will be turned over in August and the final Milestone is for the auditorium area, which the owner is requesting by Mid-September but the contractor is noting November 2014.	\$34,137,202	
East Bridgewater East Bridgewater High	High School	Fontaine Brothers, Inc.	\$65,409,000	950	Bid	213,544	\$306	\$47,684,117	\$223	Design/Bid/Build	10-Aug-11	25-Jun-13	0	95%	\$2,171,759	3.557%	Demo of existing HS is complete. Site crew working on bringing the site up to grade to complete the remaining ball fields and parking. Overall project complete 7/1/14.	\$40,164,584	
Easthampton Easthampton High	High School	Fontaine Brothers, Inc.	\$30,934,000	510	Bid	110,400	\$280	\$24,511,000	\$222	Design/Bid/Build	16-May-11	19-Feb-13	0	99%	\$911,700	2.994%	Remaining work consists of warranty items and commissioning completion. Project closeout will follow.	\$22,859,504	
Fairhaven Rogers	Elementary School	CTA Construction Co., Inc.	\$19,099,606	370	Bid	77,871	\$245	\$14,996,521	\$193	Design/Bid/Build	21-May-12	26-Jun-13	0	100%	\$217,798	1.140%	The new school building is in service. All punch list and commissioning consultant action items are complete. Final site work is complete except minor landscaping to be completed by June 30, 2014.	\$13,431,486	
Franklin Franklin High	High School	Bacon-Agostini Construction Joint Venture	\$86,778,700	1,650	Bid	306,543	\$283	\$73,191,801	\$239	Design/Bid/Build	16-Oct-12	25-Jul-14	0	81%	\$802,171	0.924%	Building envelope is nearing completion. Classroom finishes are nearing completion on the 2nd and 3rd floors, less advanced in the 1st floor classrooms. Gym equipment installation is proceeding, as is the auditorium theater rigging installation. Exterior site work has resumed. Equipment testing and startups are proceeding through the month of May.	\$54,558,408	
Georgetown Penn Brook	Elementary School	Brait Builders Corp.	\$32,875,975	770	Bid	98,000	\$335	\$26,976,145	\$275	Design/Bid/Build	26-Sep-13	20-May-16	0	25%	\$2,142,894	6.518%	Cleared and graded Access Road including water line connections. Concrete prep for slabs on grade Steel erection of B wing complete and A wing erection has begun.	\$18,864,538	
Greater New Bedford Gr New Bedford Voc Tech	Vocational / Technical	Agostini Construction Co., Inc.	\$12,181,500	2,060	PFA	464,300	\$26	\$10,757,696	\$23	Design/Bid/Build	13-Sep-13	19-Dec-14	0	25%	\$138,950	1.141%	Steel erection of B Wing is complete and A Wing erection has begun.	\$12,736,352	
Hingham Hingham Middle School	Middle School	Brait Builders Corp.	\$48,436,000	1,020	Bid	176,385	\$275	\$41,227,552	\$234	Design/Bid/Build	07-Jun-12	30-Dec-14	0	95%	\$378,225	0.790%	Minor work left to complete. FFE deliveries and installation are underway.	\$22,503,315	
Hudson John F Kennedy	Middle School	Bacon-Agostini Construction Joint Venture	\$35,102,573	715	Bid	118,846	\$295	\$28,373,294	\$239	Design/Bid/Build	28-Sep-11	22-Jun-13	0	100%	\$1,303,523	3.714%	The new school building is in service. Closeout of Commissioning is in process. Final site work is complete.	\$22,932,938	
Lynnfield Lynnfield High	High School	E.A. Colangeli Construction Co. Inc	\$3,110,346	740	Bid	10,950	\$284	\$2,322,687	\$212	Design/Bid/Build	25-Jun-12	28-Jun-13	0	99%	\$259,285	8.981%	Minor punch list work remaining.	\$1,743,071	
Marblehead Glover	Elementary School	G & R Construction, Inc.	\$20,868,000	425	Bid	79,108	\$264	\$16,977,513	\$215	Design/Bid/Build	25-Jun-12	20-Dec-13	0	99%	\$722,339	3.462%	The new school building is complete and in service. A small number of punch list items and Commissioning Consultant action items are being resolved. Site work is complete with the exception of final landscaping that will be completed by June 30, 2014.	\$8,759,441	
Marshfield Marshfield High	High School	Brait Builders Ventures	\$84,980,000	1,310	Bid	267,469	\$318	\$64,604,850	\$242	Design/Bid/Build	16-Aug-12	25-Jul-14	30 ahead	92%	\$609,982	0.766%	Finishes are being completed throughout the new school including carpentry and millwork, hardwood flooring installation in the gym, and washing and waxing of floors. Technology installation and startups proceeding along with equipment startups.	\$46,550,599	
Maynard Maynard High	High School	CTA Construction Co., Inc.	\$36,650,000	410	Bid	121,520	\$302	\$30,630,013	\$252	Design/Bid/Build	18-Aug-11	13-Dec-13	0	99%	\$311,462	0.850%	Punch list activities continue. Exterior landscaping and final grading and seeding of the lawn in front of the school is ongoing.	\$22,095,036	
Monomoy Monomoy Regional High School	High School	Fontaine Brothers, Inc.	\$49,374,000	700	Bid	168,000	\$294	\$41,433,695	\$247	Design/Bid/Build	11-Feb-13	30-Jun-14	0	80%	\$363,501	0.757%	Casework installations on the first and second floor of Building A academic areas are ongoing. Ceiling tile installation continues in building A. CMU block in the locker rooms and all of the exterior masonry has been completed. The curtain wall installation is nearing completion at the main entrance. The main parking lot construction by the track and field has started.	\$27,654,507	
Newburyport Francis T Bresnahan Elem	Elementary School	CTA Construction Co., Inc.	\$28,190,000	660	Bid	112,517	\$251	\$20,841,757	\$185	Design/Bid/Build	14-Mar-13	30-Jun-14	14 behind	81%	\$665,420	2.428%	Building envelope is complete. Metal stud, drywall and MEP rough-ins are complete. Interior finishes are 95% complete. MEP finishes are 70% complete. The elevator is complete. Demo of existing building will commence after school session ends in June, 2014. Site work is approximately 75% complete.	\$15,676,427	
Norfolk County Agriculture Norfolk County Agr	Vocational / Technical	TLT Construction Corporation	\$21,508,952	550	Bid	114,816	\$187	\$15,546,739	\$135	Design/Bid/Build	29-Mar-12	09-May-14	83 behind	80%	\$617,249	2.999%	Phase 1: Animal Science Building, Agricultural Mechanical Building, Equine Center, and Equipment Garage are substantially complete. Phase 3: Site work is substantially complete. Phase 2: Replacement General Contractor Brait Builders is completing renovation and site Phase 2 work. OPM reports that Phase 2 completion is estimated to be by the end of July 2014. However, the estimate is dependent on the efficiency of the Surety coming to a contract agreement with Brait Builders.	\$13,493,272	
North Adams Silvio O Conte Middle	Middle School	PDS Engineering and Construction, Inc.	\$21,853,267	310	PFA	78,119	\$280	\$14,521,110	\$186	Design/Bid/Build	28-Apr-14	17-Jul-15	0	0%	\$0	0.000%	The contractor has recently mobilized.	\$20,632,054	
Oxford Oxford Middle	Middle School	J.J. Cardosi, Inc.	\$5,085,217	652	PFA	117,000	\$43	\$5,085,217	\$43	Design/Bid/Build	01-Jun-12	22-Aug-14	0	48%	\$139,512	2.744%	Roof replacement completed in the Summer of 2012. Window project completed in the Summer of 2013. HVAC/ADA contract has been awarded. General Contractor is completing demolition, abatement, and piping on 2nd shift until end of school year.	\$3,369,847	
Quincy Central Middle	Middle School	H.V. Collins Co., Inc.	\$32,540,712	620	Bid	114,975	\$283	\$27,057,118	\$235	Design/Bid/Build	18-Jun-12	18-Oct-13	0	99%	\$828,830	2.547%	Commissioning and punch list work nearing completion.	\$28,962,549	
Revere Staff Sergeant James J. Hill School	Elementary School	CTA Construction Co., Inc.	\$33,897,336	690	PFA	103,650	\$327	\$24,309,968	\$235	Design/Bid/Build	25-Mar-14	16-Jun-15	0	8%	\$428,348	1.264%	Demolition of the three existing houses on the new school site is ongoing. The Contractor is currently installing ground improvement. The foundation has been poured in two major sections and is approximately 50% complete.	\$28,099,048	
Somerset-Berkley Somerset-Berkley High	High School	Bacon-Agostini Construction Joint Venture	\$69,407,000	1,000	Bid	222,826	\$311	\$52,553,676	\$236	Design/Bid/Build	16-Jul-12	20-Jun-14	0	85%	\$480,476	0.730%	Finish work complete on the 2nd and 3rd floors in the academic areas, and nearing completion on the 1st floor. Wood flooring installation and seating proceeding in the auditorium. Finishes completed in the lobby areas and main corridor.	\$46,363,361	
South Hadley Plains Elementary	Elementary School	Fontaine Brothers, Inc.	\$25,918,550	270	PFA	63,377	\$409	\$14,664,281	\$231	Design/Bid/Build	08-May-14	15-Jul-15	0	0%	\$0	0.000%	The general contractor has mobilized.	\$13,874,014	
Southwick-Tolland Powder Mill	Middle School	PDS Engineering and Construction, Inc.	\$13,556,194	545	Bid	95,775	\$142	\$11,289,029	\$118	Design/Bid/Build	07-Jun-13	14-Aug-15	0	27%	(\$15,257)	-0.113%	New primary electric conduits, secondary conduits, and transformer pad have been installed. The new switchgear is in place. Electrical feeders have been run in corridors after school hours. Installation of the new boilers as well as related equipment is currently underway. Floor and ceiling demolition was completed during April school vacation in the area to be renovated in the Summer of 2014.	\$8,437,002	

Projects in Construction
MSBA Grant Basis and Maximum Grant Amount
Data Reported as of May 14, 2014

Core Program and Waitlist Totals			\$2,555,152,746	52,252		10,344,717												*Includes Alternates	\$1,622,710,664
Project	Grade	Contractor	Total Construction Cost*	Projected Enrollment	PFA or Bid Data	Proposed Sq.Ft.	Construction Cost/Sq.Ft.	Building Cost	Building Cost/Sq.Ft.	Procurement Type	Construction Start Date	Substantial Completion	Schedule Variance (days)	Physical Progress	Change Orders	Change Orders %	Construction Status	Estimated Max Total Facilities Grant	
CAPITAL PIPELINE PROJECTS IN CONSTRUCTION																			
Core Program Totals			\$2,520,406,848	51,592		10,195,917													\$1,583,703,811
Southwick-Tolland Southwick-Tolland Regional High	High School	Fontaine Brothers, Inc.	\$25,307,990	790	Bid	165,995	\$152	\$19,838,420	\$120	Design/Bid/Build	05-Aug-13	18-Sep-15	0	29%	\$445,870	1.799%	Roofing has been completed at both the Middle School and High School additions. Interior and exterior masonry in both additions is nearing completion. Window installation and MEP rough-ins at both additions are ongoing. Excavation for drainage and underground utilities at the High School addition is largely complete. Abatement of corridor tile and installation of electrical feeders in the existing building were completed during April school vacation.	\$19,572,669	
Southwick-Tolland Woodland Elementary	Elementary School	PDS Engineering and Construction, Inc.	\$7,172,052	400	Bid	67,800	\$106	\$6,077,790	\$90	Design/Bid/Build	07-Jun-13	14-Aug-15	0	65%	\$65,599	0.915%	Phase 3 (West wing) is in construction. MEP rough-ins and window installation have been completed. Painting and finishes are underway. Phase 3 is scheduled to be substantially complete by May 30, 2014. Phase 2 windows were installed during April school vacation. Boiler removal and flooring abatement for summer 2014 work have been completed early.	\$4,620,410	
Sturbridge Burgess Elementary	Elementary School	Fontaine Brothers, Inc.	\$22,946,000	860	Bid	131,630	\$174	\$17,591,000	\$134	Design/Bid/Build	10-Aug-10	30-Oct-10	0	100%	\$1,966,295	8.575%	The new school building addition and renovations are complete and in service. An investigation of a rubber floor tile adhesion failure in the Cafeteria and Band Room in the renovated building has been completed. Floor replacement in these areas is being planned for the Summer of 2014. A report of the result of Investigations in other areas is in process. Punch list work continues.	\$14,764,380	
Sutton Sutton Middle School	Middle School	Brait Builders Corp.	\$41,230,800	840	Bid	179,040	\$230	\$32,998,403	\$184	Design/Bid/Build	01-Jul-11	31-Dec-14	240 behind	75%	\$1,099,287	2.736%	The new completion contractor has mobilized and completed abatement activities. The original project Substantial Completion date of December 31, 2014 is now scheduled for June 30, 2015. Selective demolition within the core building is complete. Demolition of the existing High School is nearing completion. Corrective work within the new Auditorium has begun with the removal of sprinkler lines to allow for the installation of stage rigging. Previous phase punch list work has commenced.	\$25,646,928	
Webster Park Avenue Elementary	Elementary School	CTA Construction Co., Inc.	\$32,370,001	720	Bid	109,597	\$295	\$24,190,915	\$221	Design/Bid/Build	08-Jul-13	12-Dec-14	11 behind	53%	\$223,121	0.705%	Ongoing work includes installation of slabs-on-grades at Cafeteria and Gymnasium, installation of exterior envelope (roof & walls), metal wall framing, sheathing/air-vapor barrier and brick veneer, window blocking and metal roof & fascia. Installation of interior partitions and rough mechanical, electrical, plumbing and fire protection systems continue, and utility trenching work has begun.	\$28,102,666	
West Bridgewater West Bridgewater Jr-Sr	High School	CTA Construction Co., Inc.	\$46,267,000	625	Bid	141,250	\$328	\$34,404,274	\$244	Design/Bid/Build	01-Oct-13	15-Jun-15	25 behind	15%	\$0	0.000%	Erosion controls are in place. Demolition of the existing athletic fields and courts are complete. Top soil is stockpiled on site. Structural steel and masonry are complete. Under slab piping and slabs are complete. Steel stairs are 50% complete. Metal studs and mechanical/electrical rough-ins are underway. Site work and site utilities are ongoing.	\$26,034,563	
West Springfield West Springfield High	High School	Fontaine Brothers, Inc.	\$85,006,020	1,270	Bid	257,525	\$330	\$56,875,181	\$221	Design/Bid/Build	22-Nov-11	31-Dec-13	0	94%	\$2,458,648	3.489%	Students occupied the new High School after February vacation. Abatement of the existing building has begun and half of the existing HS has been demolished. Minor punch list remains.	\$60,722,795	
Westfield Abner Gibbs	Elementary School	Fontaine Brothers, Inc.	\$25,578,000	600	Bid	95,573	\$268	\$21,444,000	\$224	Design/Bid/Build	24-Aug-12	25-Mar-14	0	7%	\$0	0.000%	Work stoppage regarding Article 97 "Protected Land". The City still does not have approval. General Contractor has demobilized from the site.	\$20,004,642	
Weston Field Elem School	Elementary School	Colantonio, Inc.	\$24,537,966	355	Bid	65,390	\$375	\$19,872,289	\$304	Design/Bid/Build	21-Dec-12	19-Jun-14	0	80%	\$830,186	3.383%	Roof work is mostly complete except for minor metal work. Windows are complete and undergoing final commissioning testing. The boiler, hot water heater and pump have all been installed and sprinkler work is complete. Duct work and electrical are complete except for punch list. Drywall and ceiling painting are complete in the majority of the building including classrooms. Mock-ups have begun for the classroom floor installation.	\$8,004,886	
Williamsburg Anne T Dunphy	Elementary School	Enfield Builders, Inc.	\$8,990,457	170	Bid	37,859	\$237	\$7,625,327	\$201	Design/Bid/Build	05-Apr-13	15-May-14	53 behind	90%	\$403,022	4.483%	Building envelope complete. Metal studs, drywall and MEP/FP rough-in complete. Interior finishes and MEP/FP finishes are nearly complete (approx. 90%). Earth work and underground utilities are ongoing.	\$6,808,088	
Winchester Vinson-Owen	Elementary School	CTA Construction Co., Inc.	\$21,289,999	420	Bid	74,820	\$285	\$17,586,598	\$235	Design/Bid/Build	17-Feb-12	26-Jul-13	0	100%	\$473,296	2.247%	Punch list work is nearing completion and being performed after school hours.	\$9,091,823	
Andover Bancroft Elementary	Elementary School	Skanska USA Building, Inc.	\$40,077,007	680	Bid	106,904	\$375	\$27,101,717	\$254	CM-at-Risk	14-May-12	22-May-14	0	90%	\$169,186	0.422%	Minor work remains on exterior envelope. Final finishes and millwork installations are nearing completion in the academic wings. Carpet flooring to be installed in Admin area and Library. Finish work remains in Gym & Cafeterium. FF&E installations are scheduled for the beginning of June. Site work is ongoing. Demo of existing building to begin in June.	\$15,731,353	
Ashburnham-Westminster Briggs Elem	Elementary School	Consigli Construction Company, Inc.	\$24,780,000	520	Bid	87,085	\$285	\$18,202,478	\$209	CM-at-Risk	09-Mar-12	30-Aug-13	0	100%	\$27,896	0.113%	The new school building is in service. A small number of punch list and commissioning consultant action items are being resolved. Final site work is complete except minor landscaping to be completed by June 30, 2014.	\$16,187,237	
Auburn Auburn Middle	Middle School	Fontaine Brothers, Inc.	\$36,612,806	560	PFA	100,395	\$365	\$23,550,958	\$235	CM-at-Risk	27-Feb-14	05-Jun-15	0	7%	\$0	0.000%	Contractor mobilized, set up temporary facilities and erosion controls, and performed initial survey. Topsoil was stripped and civil site work has begun.	\$19,763,951	
Ayer-Shirley Ayer-Shirley Regional Middle/High School	High School	Consigli Construction Company, Inc.	\$44,516,576	495	PFA	144,072	\$309	\$32,082,505	\$223	CM-at-Risk	19-Feb-13	26-Aug-15	0	25%	\$71,574	0.161%	At the new classroom wing, exterior masonry has commenced, MEP rough-ins are complete, drywall installation is ongoing on all three floors and finish work has commenced in the bathrooms. The band & chorus addition slabs-on-grade have been placed, exterior walls have been framed, the roof is installed and interior rough-ins have commenced. Demolition has begun in Auditorium, Gym, and locker rooms. Footings were excavated and concrete placed in the courtyard.	\$34,926,694	
Concord-Carlisle Concord Carlisle High	High School	Turner Construction Company	\$76,143,704	1,225	PFA	219,871	\$346	\$53,607,000	\$244	CM-at-Risk	20-Feb-13	15-Mar-15	0	45%	\$347,370	0.456%	Loop road binder course and foundations are complete. Slabs, structural steel and roofing are complete. Building envelope, metal studs, drywall and painting are ongoing. MEP/FP rough-ins are ongoing.	\$26,795,748	
Duxbury Duxbury High	High School	Dimeo Construction Company	\$105,475,520	1,735	Bid	322,105	\$327	\$73,368,123	\$228	CM-at-Risk	12-Sep-12	03-Jul-14	0	86%	\$2,112,102	2.121%	The gym floors have been installed. The kitchen equipment installation is substantially complete. MEP finish work is ongoing and includes air balancing in Building Area A. Interior cleaning has started in Building Area A and B. Initial punch list has been completed in building Area A and is underway in Building B.	\$48,141,830	
Essex Agr Tech Essex Agr and Tech Inst	Vocational / Technical	Gilbane Building Company	\$110,217,451	1,440	Bid	337,000	\$327	\$79,334,889	\$235	CM-at-Risk	07-May-12	30-Jun-14	0	87%	\$1,762,649	1.599%	Ph I Farmstead- Punch list and site work remaining. Ph II Farmstead- Agr. Storage Bldg (Hoop House) erected and slab poured. MEP's ready to connect to permanent power. Existing farm bldgs are abated and demolished. Site work is ongoing. Academy- Auto Tech & Collision fit-out nearly complete. Windows and overhead doors being installed. Landscape/Mason Bldg metal panel system and slabs complete. CMU, framing and MEP's ongoing. Mn Academy- Painting and final cleaning ongoing.	\$72,471,233	
Greater Lowell Voc Tec Gr Lowell Reg Voc Tech	Vocational / Technical	Consigli Construction Company, Inc.	\$52,472,010	1,990	PFA	505,766	\$104	\$38,997,643	\$77	CM-at-Risk	04-Nov-13	31-Aug-15	90 ahead	10%	\$0	0.000%	Building Addition: Foundations and structural steel complete. Under slab piping and slab are complete. Roofing is underway. Mechanical piping is underway. Existing renovations to begin at the close of the school year.	\$46,002,209	
Greenfield Greenfield High	High School	Shawmut Design and Construction	\$53,507,787	585	Bid	160,649	\$333	\$37,812,150	\$235	CM-at-Risk	27-Mar-13	15-Dec-15	0	45%	\$182,412	0.341%	Phase 1 work is on schedule for July 31, 2014 Substantial Completion with occupancy in September of 2014. The building exterior is complete except minor finish work. Interior construction is progressing on schedule with MEP rough-ins and wallboard installation nearing completion. Painting of finished areas, ceiling grid installation, and installation of Marmoleum flooring is in process.	\$42,194,483	
Leominster Leominster Senior High	High School	S.O.M. Construction Ent., Inc.	\$33,794,797	1,825	Bid	295,859	\$114	\$25,382,707	\$86	CM-at-Risk	01-Jul-11	30-Aug-13	0	100%	\$2,478,803	7.335%	Remaining punch list work is being completed and project closeout is in process.	\$27,337,956	
Lexington Joseph Estabrook	Elementary School	Shawmut Design and Construction	\$32,792,348	540	Bid	91,840	\$357	\$22,795,606	\$248	CM-at-Risk	12-Jun-12	27-Jan-14	0	90%	\$721,021	2.199%	The new building is occupied. Abatement of existing building is complete. Site work is ongoing.	\$12,148,491	
Longmeadow Longmeadow High	High School	Gilbane Building Company	\$63,685,998	1,000	Bid	236,985	\$269	\$46,573,364	\$197	CM-at-Risk	01-Nov-10	01-Nov-13	0	99%	\$1,532,738	2.437%	Remaining punch list work is being completed and project closeout is in process.	\$31,297,686	
Methuen Methuen High	High School	Consigli Construction Company, Inc.	\$74,749,773	2,075	Bid	324,424	\$230	\$58,040,776	\$179	CM-at-Risk	12-Jul-11	26-Jun-14	0	95%	\$2,690,031	3.599%	Millwork is underway on all floors of the Ph 2 Bldg. Painting and completing ACT ceilings continue. Cleaning is scheduled for June and turnover of Ph 2 is scheduled for June 24, 2014.	\$61,544,094	
Newburyport Rupert A Nock Middle	Middle School	Gilbane Building Company	\$20,877,414	845	Bid	161,500	\$129	\$14,924,391	\$92	CM-at-Risk	18-Mar-13	21-Aug-14	0	70%	\$741,298	3.551%	Phase 4 work has begun. Punch list and commissioning work continue on Phases 1-3. Phase 4 work includes mechanical, electrical, plumbing, fire protection, ceiling tile, flooring, lighting and casework installations. The Auditorium HVAC work is also underway. Most work is presently occurring during 2nd shift, but the CM-R will transfer to a regular day schedule upon the end of school year. The roof replacement work will be completed during the summer months.	\$12,785,667	

**Projects in Construction
MSBA Grant Basis and Maximum Grant Amount
Data Reported as of May 14, 2014**

Core Program and Waitlist Totals			\$2,555,152,746	52,252		10,344,717												*Includes Alternates	\$1,622,710,664
Project	Grade	Contractor	Total Construction Cost*	Projected Enrollment	PFA or Bid Data	Proposed Sq.Ft.	Construction Cost/Sq.Ft.	Building Cost	Building Cost/Sq.Ft.	Procurement Type	Construction Start Date	Substantial Completion	Schedule Variance (days)	Physical Progress	Change Orders	Change Orders %	Construction Status	Estimated Max Total Facilities Grant	
CAPITAL PIPELINE PROJECTS IN CONSTRUCTION																			
Core Program Totals			\$2,520,406,848	51,592		10,195,917													\$1,583,703,811
North Reading North Reading High	High School	Gilbane Building Company	\$101,328,353	1,370	Bid	267,939	\$378	\$66,726,592	\$249	CM-at-Risk	15-Jan-13	31-Aug-14	0	58%	\$1,162,595	1.147%	Finishes nearing completion in the HS academic building. Finish electrical and high level finishes nearing completion in the auditorium so the temporary floor staging can be removed. Wood flooring in the gym to be delivered and installed in May. Equipment and finishes have also been installed in the kitchen and the HS and MS serving areas. Testing of the Wastewater Treatment Plant is scheduled for mid-May. The HS phase is scheduled to be completed by August 31, 2014. The next phase, renovation of the MS, will commence during the Summer of 2014 and is scheduled to be completed by August 31, 2015. Demo of the existing HS will begin during the Summer of 2015.	\$47,071,882	
Norton Norton High	High School	W. T. Rich Company Inc.	\$27,023,541	700	Bid	162,405	\$166	\$20,590,559	\$127	CM-at-Risk	12-Mar-12	31-Jan-14	0	100%	\$1,366,532	5.131%	Punch list work is 100% complete. An extension has been granted for temp. occupancy of the Auditorium through May 11, 2014. RTU noise issue and floor finish issue are being resolved.	\$20,634,829	
Shrewsbury Sherwood Middle School	Middle School	Gilbane Building Company	\$33,986,286	900	Bid	129,378	\$263	\$22,823,030	\$176	CM-at-Risk	07-Mar-11	31-Oct-12	0	100%	(\$1,033,847)	-3.061%	The new school building is in service. Final minor landscaping work is forecast for completion by June 30, 2014.	\$20,964,674	
Southern Worcester Cty VT Bay Path Reg Voc Tech H S	Vocational / Technical	Consigli Construction Company, Inc.	\$57,024,455	1,110	Bid	249,521	\$229	\$41,468,049	\$166	CM-at-Risk	02-Aug-13	01-Sep-15	0	15%	\$256,075	0.452%	The project is currently in Phase 1 of an 11-Phase project. Phase 1 is the addition of the new Media Center, Science Classrooms and Typical Classrooms. Phase 1 is approx. 40% complete. Phase 1 is scheduled to be turned over to the District on September 1, 2014. Scope in additional phases includes the replacement of multiple building systems throughout the building as well as site work.	\$44,510,177	
Springfield Dryden Memorial	Elementary School	Morganti/Aquadro & Cerruti	\$11,476,091	280	Bid	40,900	\$281	\$8,276,912	\$202	CM-at-Risk	28-Jun-12	01-Nov-13	0	99%	\$271,991	2.370%	Remaining site punch list and commissioning work is being completed and project closeout is in process.	\$10,344,789	
Springfield Elias Brookings	Elementary School	Morganti/Aquadro & Cerruti	\$22,733,394	320	PFA	64,800	\$351	\$18,337,328	\$283	CM-at-Risk	01-Jul-13	20-Jan-15	56 behind	26%	\$256,355	1.128%	Foundations have been completed. Steel erection and detailing are underway. Subsurface plumbing and electric are ongoing.	\$25,563,992	
Stoneham Stoneham Middle School	Middle School	Shawmut Design and Construction	\$33,086,864	775	Bid	136,410	\$243	\$23,430,771	\$172	CM-at-Risk	01-Nov-12	08-Aug-14	0	70%	\$329,931	0.997%	The new school building's exterior masonry is nearly complete. Roofing is complete with nine RTUs installed. Interior work is progressing with drywall nearly complete, painting and ceiling grid placement close to 50% complete, and floor tile installation in process.	\$21,346,937	
Wakefield Galvin Middle School	Middle School	Bond Brothers, Inc.	\$59,756,584	1,070	Bid	187,722	\$318	\$44,899,853	\$239	CM-at-Risk	18-Mar-13	30-Jun-15	0	50%	\$1,142,745	1.912%	The new school building is being completed in three phases (A, B & C) working from upper to lower floors. Phase A exterior and interior construction is nearing completion. Framing of walls in Phase B is progressing and MEP rough-ins are beginning. Phase C slab placement has been completed. Permanent power is in place and boilers, water heaters, and switchgear are on site for installation.	\$32,631,618	
Wilmington Wilmington High	High School	Gilbane Building Company	\$67,558,835	960	PFA	192,443	\$351		\$250	CM-at-Risk	30-Apr-13	13-Feb-15	0	32%	\$0	0.000%	Structural steel work overall is 88% complete. All MEP rough-ins are well underway. Site work continues including utility work and the installation of the drainage system.	\$35,822,158	
Waitlist Totals			\$34,745,898	660		148,800	\$234		\$176									\$39,006,853	
Springfield Forest Park Middle	Middle School	Consigli Construction Company, Inc.	\$34,745,898	660	Bid	148,800	\$234	\$26,209,932	\$176	CM-at-Risk	26-Mar-12	01-Aug-13	0	99%	\$1,048,807	3.019%	Minor punch list remaining. Project closeout is in process.	\$36,080,584	
