

Massachusetts School Building Authority

# CAPITAL PLANNING PROJECT OVERVIEW REPORT

January 8, 2016


# TABLE OF CONTENTS

<b>Capital Pipeline Overview .....</b>	<b>2</b>
<b>Statements of Interest (SOIs) .....</b>	<b>3</b>
<b>Core Program .....</b>	<b>4 - 11</b>
Eligibility Period .....	4
Consultant Selection .....	5 - 6
Feasibility Study .....	7
Schematic Design .....	8
Commissioning .....	9
Design Development .....	10
Summary of Bid Data.....	10
Construction .....	11
<b>Accelerated Repair Program .....</b>	<b>12 - 15</b>
<b>Project Variances .....</b>	<b>16</b>
<i>Appendix</i>	
(A) <i>Project Status List</i>	
(B) <i>2016 Estimated Bid Dates</i>	
(C) <i>Construction Status Report</i>	

# CAPITAL PIPELINE OVERVIEW

## Current Projects Status

A total of 306 projects that have received invitations from the Board of Directors (“Board”) to collaborate with the MSBA are currently in the MSBA’s Eligibility Period and Capital Pipeline. The summary chart provides the number of projects in Eligibility Period and each phase of the Capital Pipeline. For a detailed look at the Capital Pipeline projects, please go to [www.massschoolbuildings.org/building](http://www.massschoolbuildings.org/building) and select “Capital Pipeline Status Chart”.

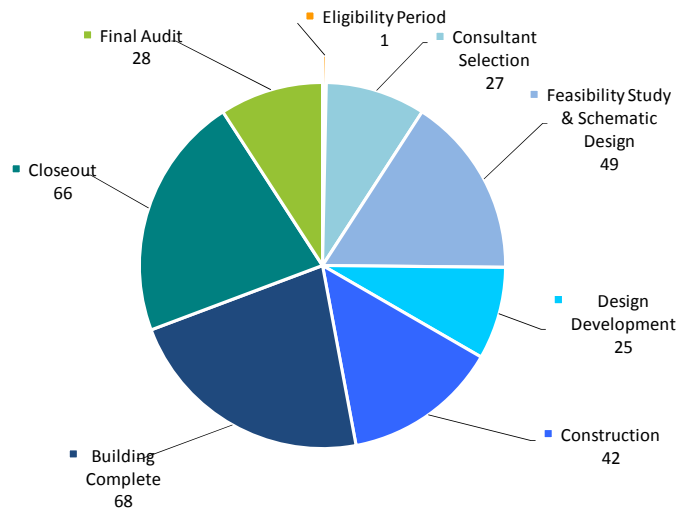

## 2015 Progress Report

- SOI 2015
  - 97 Core Program SOIs were received; and recommendations for the 2015 SOI opening are anticipated at the January 2016 Board meeting.
  - 2015 ARP SOIs were finalized with recommendations for invitation issued for 24 districts, representing 44 projects, at the June 3, 2015 Board meeting.
- SOI 2016
  - The SOI System for SOI consideration in 2016 opened on January 8, 2016.
- Eligibility Period
  - The remaining district in Eligibility Period is being recommended for an invitation to Feasibility Study at the January Board meeting.
- Feasibility Study/Schematic Design
  - One district received MSBA approval for selection of an Owner’s Project Manager (“OPM”).
  - Two districts have completed their designer selection.
- Accelerated Repair Program
  - From the 2015 SOI opening, all districts have completed preliminary requirements and have been assigned consultants. One district was recommended for a Project Funding Agreement at the November 2015 Board meeting, 15 districts are anticipated at the January Board meeting, with the remaining eight districts being presented at the March and May Board meetings.
- Construction Costs – Core Program
  - Of the 14 bids and/or executions of a GMP in 2015, 13 have been reported to date.
  - Of the 13, 10 bids came in within the estimated budget.
- Substantial Completion
  - Of the 24 districts anticipating substantial completion in 2015, 23 have declared substantial completion as of this report.
  - 13 projects are projecting substantial completion in 2016.

# STATEMENTS OF INTEREST (SOIs)

## **2016 SOI Process**

The Fiscal Year 2016 SOI filing period opens on January 8, 2016. The deadline to file SOIs for consideration in the Accelerated Repair Program (“ARP”) is Friday, February 12, 2016.

The SOI filing period for districts submitting for consideration in the Core Program, which is primarily for projects beyond the scope of Accelerated Repair, including extensive repairs, renovations, addition/renovations, and new school construction, is Friday, April 8, 2016.

# CORE PROGRAM

## Eligibility Period

There is one district remaining in Eligibility Period, and it has secured funding.

An agreed-upon enrollment is a key pre-requisite for the MSBA to commence a Feasibility Study with a district. To begin the enrollment projection process, a district must file enrollment information utilizing the MSBA’s online enrollment projection tool. The remaining district has completed its online enrollment projection information and has signed its enrollment certification.

Based upon the schedule anticipated by the district for completion of Eligibility Period requirements, staff anticipates recommending this district in Eligibility Period for an Invitation to Feasibility Study at the January Board meeting.

District	School	Date of Invitation to Eligibility Period	30 days	60 days	90 days		180 days		270 days	Date of Invitation to Feasibility Study (Estimated)
			ICC	SBC	Online Enrollment Projection Info	Ed Profile Questionnaire	Maintenance Documents	Enrollment Certification	Local Authorization	
Everett	George Keverian School	3/25/15	x	x	x	x	x	x	x	1/27/16

Staff will be recommending SOI’s from the SOI 2015 submittals for Invitation to Eligibility Period at the January 2016 Board meeting.

## Consultant Selection

### OPM Selection

After the district has completed all Eligibility Period requirements and has received a Board Invitation to Feasibility Study, the district procures an Owner's Project Manager ("OPM"). Since the last report, one district has completed its OPM selection as shown shaded in the table below. Currently, there are 15 districts in the Capital Pipeline that are in the process of procuring an OPM.

District	School	Anticipated Selection
Saugus	Saugus HS	December 2015
Westport	Westport MS	January 2016
Lynn	Pickering MS	January 2016
Waltham	Waltham HS	January 2016
Boston	Boston Arts Academy	February 2016
Cape Cod RVTSD	Cape Cod RTHS	February 2016
Worcester	South High Community School	February 2016
Easthampton	Maple ES	March 2016
Attleboro	Attleboro HS	April 2016
Middleborough	Middleborough HS	April 2016
Lowell	Lowell HS	April 2016
Taunton	Mulcahey ES	April 2016
Bristol County Agricultural	Bristol County Agricultural HS	May 2016
Clarksburg	Clarksburg ES	May 2016
Fall River	BMC Durfee HS	June 2016
Holyoke	Lt. Elmer J. McMahon ES	TBD

### Designer Selection

After a district has selected and executed a contract with an OPM, it selects a Designer utilizing either a local designer selection process for projects under \$5 million or the MSBA’s Designer Selection Panel (“DSP”) for projects over \$5 million. Since the last report, two districts have completed their Designer selection as shown shaded in the table below. There is currently one district in the Capital Pipeline that is in the process of procuring a Designer.

District	School	Anticipated Selection
Millis	Clyde F. Brown ES	November 2015
Ipswich	Winthrop ES	December 2015
Saugus	Saugus HS	February 2016

For additional information on the selected consultant teams, see Appendix A.

**Feasibility Study**

Once a district has procured an OPM and Designer, the district and its consultants must complete two Feasibility Study submittals, the Preliminary Design Program and the Preferred Schematic Report, prior to Board consideration to proceed into Schematic Design. Based on the most recent data and schedules provided to the MSBA by districts, the MSBA anticipates that eight districts will present their preferred schematic designs to the Board at the upcoming January, March, and May Board meetings.

District	School	Anticipated PS Board Date
Needham	Hillside ES	January 27, 2016
Stoughton	Stoughton HS	January 27, 2016
Amherst	Wildwood ES	March 30, 2016
Boston	Quincy Upper School	March 30, 2016
Hanover	Sylvester ES	March 30, 2016
Bourne	Peebles ES	May 25, 2016
Braintree	East MS	May 25, 2016
Millis	Clyde F. Brown ES	May 25, 2016



## **Schematic Design**

Prior to consideration by the Board for Project Scope and Budget authorization, a district must submit a Schematic Design to the MSBA for review. Based on the most recent data and schedules provided to the MSBA by districts, the MSBA anticipates that eight districts will appear before the Board for Project Scope and Budget Agreement authorization at the upcoming January, March, and May Board meetings.

District	School	Anticipated PS&B Board Date
Billerica	Memorial HS	January 27, 2016
Granby	West Street ES	January 27, 2016
Minuteman RVTSD	Minuteman RVTHS	January 27, 2016
Mount Greylock RSD	Mount Greylock RHS	January 27, 2016
Dedham	Early Childhood Center	March 30, 2016
Newton	Cabot ES	March 30, 2016
Stoughton	Stoughton HS	May 25, 2016
Quincy	Sterling MS	May 25, 2016

**Commissioning**

The MSBA assigns a Commissioning Consultant once a district has secured local funding for the Board approved project. Since the last report, the MSBA has assigned Commissioning Consultants to nine additional projects presented in the table below.

District	School	Program	Estimated Const. Cost (million)	Commissioning Consultant	Contract Amount
Leicester	Leicester HS (Roof)	2015 ARP	\$2.10	Russo Barr Associates	\$47,435
Provincetown	Provincetown K-8 (Repairs)	Core	\$5.71	BVH Integrated Services	\$43,840
Hopkinton	Center ES	Core	\$35.14	RDK Engineers	\$89,915
Chicopee	2 schools (Roofs)	2015 ARP	\$3.13	Building Enclosure Associates	\$52,500
Springfield	4 Schools	2015 ARP	\$5.24	Building Enclosure Associates	\$97,000
Cambridge	Kennedy Longfellow (Roof)	2015 ARP	\$2.80	Thompson & Lichtner	\$34,270
North Reading	E. Ethel Little School (Roof)	2015 ARP	\$1.42	Thompson & Lichtner	\$33,270
West Bridgewater	Spring Street School (Roof)	2015 ARP	\$1.11	Thompson & Lichtner	\$31,100
Greenfield	Federal Street School	2015 ARP	\$4.70	Colliers International	\$59,851

To date, the MSBA has executed 340 Commissioning Consultant contracts, totaling \$24.4 million. To date, 184 contracts have been completed.

The table below represents the status of commissioning assignments sorted by the fiscal year in which the commissioning work orders were issued.

Fiscal Year	No. Work Orders Issued	Value of Work Orders Issued	Total Invoiced	Percent Complete
FY10	31	\$4,231,376	\$4,273,277	100%
FY11	95	\$6,132,890	\$6,046,179	99%
FY12	52	\$4,450,761	\$4,265,048	96%
FY13	55	\$3,364,697	\$2,937,419	87%
FY14	47	\$2,604,062	\$1,656,620	64%
FY15	44	\$2,277,711	\$809,013	36%
FY16	16	\$1,315,773	\$15,768	1%

**Design Development**

Once a district has secured local funding and has entered into a Project Funding Agreement with the MSBA, it enters into the Design Development phase. Currently, there are 25 projects in the Design Development phase with a total estimated construction cost of approximately \$497.3 million: 15 Accelerated Repair projects and 10 Core Program projects. The 10 Core Program projects in Design Development have a total estimated construction cost of approximately \$474.6 million and are listed below.

Elementary School Districts	Middle School Districts	High School Districts	Other Grade Configurations
Carver (PK-5) Hopkinton (PK-1) Narragansett (PK-5) New Bedford (PK-5) Woburn (K-5)	<b><u>Middle School Districts</u></b> Beverly (5-8) Westborough (7-8)	Pittsfield (9-12)	Brookline (K-8) Provincetown (K-8)

**Summary of Bid Data**

Based on the most recent data and schedules provided by the districts, the MSBA anticipates 14 projects will bid in 2015 and 11 projects will bid in 2016.

Year	Number of Projects	Design Basis for Enrollment	Project Budget	Construction Budget
2015	14	10,654	\$887.9 M	\$700.9 M
2016	11	5,500	\$639.3 M	\$526.1 M
<b>Totals</b>	<b>25</b>	<b>16,154</b>	<b>\$1.53 B</b>	<b>\$1.23 B</b>

*Note: These numbers are based on preliminary information received from the District and are subject to further review and calculation.*

Anticipated Bids in 2016:

- January – N/A
- February – Westborough (CMR)

For additional information on each of these projects, see Appendix B.

**Construction**

When a district issues a Notice to Proceed, the project is advanced to the Construction phase. Currently, there are 42 projects in the Construction phase with a total estimated construction cost of \$1.17 billion: 21 Accelerated Repair projects, one waitlist project, and 20 Core Program projects. This does not include the 68 projects that have reached substantial completion and are currently in the Building Complete phase. The 20 Core Program projects have a total estimated construction cost of \$1.12 billion and are listed below.

Elementary School Districts	Middle and Middle/High School Districts	High School Districts	Other Grade Configurations
Athol-Royalston RSD (PK-4) Gloucester (K-5) Milford (3-5) Northborough (K-5) Westfield* (K-5)	<p><b><u>Middle School Districts</u></b></p> Chelsea (5-8) Lynn (6-8) Peabody (6-8) Scituate (6-8) Wachusett RSD (6-8)	North Middlesex RSD (9-12) Plymouth (9-12) Winchester (9-12)	Abington (PK; 5-12) Haverhill (K-8) Holbrook (PK-12) Worcester (PK-6)
	<p><b><u>Middle/High School Districts</u></b></p> Boston - Dearborn MS (6-12) Lunenburg (6-12) Winthrop (6-12)		

*\*Note: Westfield, Abner Gibbs Elementary School, stopped construction in December of 2012 due to a preliminary injunction based upon project site status as Article 97 "Protected Land".*

For additional information on the construction status for each of these projects, see Appendix C.

# ACCELERATED REPAIR PROGRAM

Currently there are a total of 83 districts, representing 172 projects, either active or completed in the Accelerated Repair Program. All new information that has been updated since the last report has been emphasized in italics.

Repair Program	Number of Districts	Number of Projects	Total Project Budgets	Maximum Facility Grants	Number of Projects Final Audit Approved
2015 Accelerated*	24	44	\$2,529,730	\$1,497,853	0
2014 Accelerated	34	47	\$108,410,084	\$65,388,035	0
2013 Accelerated	25	45	\$94,724,781	\$54,702,981	9
2012 Accelerated	24	36	\$63,009,653	\$38,267,952	28
Green	93	189	\$366,654,266	\$222,889,218	180


\*Totals reflect projects approved for Project Funding Agreements as of the November 18, 2015 Board of Directors' Meeting.

## 2015 Accelerated Repair Program

- Invitations – 24 districts, representing 44 projects
  - Scope includes 22 roofs, 26 windows/doors and nine boilers
- Approved for Project Funding Agreements – one district, representing one project
- *Total Project Budgets - \$2,529,730*
- *MSBA Total Facilities Grants - \$1,497,853*
- *15 districts, representing 28 projects, are seeking PFA approval at the January 27, 2016 Board of Director's Meeting*
  - *The proposed combined Total Project Budgets and Maximum Facility Grants are \$85,334,092 and \$60,142,331 respectively.*

## 2014 Accelerated Repair Program


- Invitations – 36 districts, representing 51 projects
- SOI Removal – two districts, representing four projects
- Current 2014 ARP projects – 34 districts, representing 47 projects
  - Scope includes 20 roofs, 25 windows/doors and 13 boilers
- Approved for Project Funding Agreements – 34 districts, representing 47 projects
- Total Project Budgets - \$108,410,084
- MSBA Total Facilities Grants - \$65,388,035
- Four districts, representing six projects, required schedule extensions following PFA approval
- *86% of reporting projects bid within estimated budget*

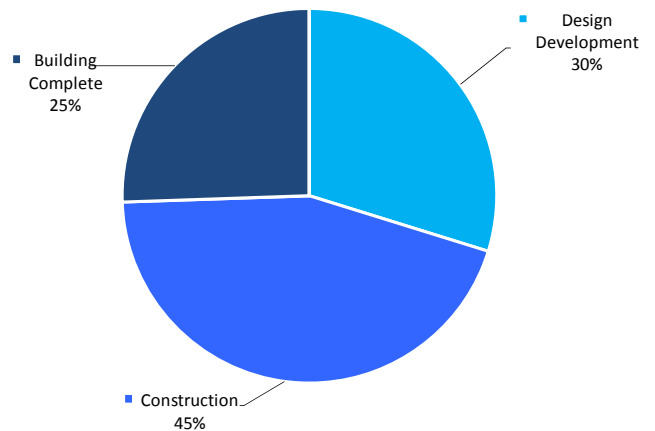

2014 ARP Status Chart

### 2013 Accelerated Repair Program


- Invitations – 28 districts, representing 50 projects
- SOI Removals – four districts, representing five projects
- Approved for Project Funding Agreements – 26 districts, representing 47 projects
- Active Projects – 25 districts, representing 45 projects
  - Scope includes 30 roofs, 13 windows/doors and seven boilers
- Total Project Budgets – \$94,724,781
- MSBA Total Facilities Grants – \$54,702,981
- Four districts, representing seven projects, required schedule extensions following PFA approval
- 82% of projects bid within estimated budget
- *Since the last report, projects that have reached substantial completion have increased from 89% to 100%*

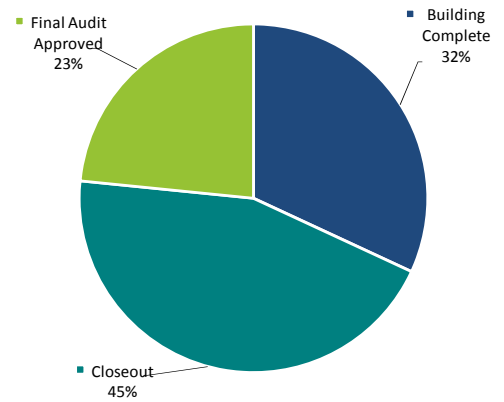

2013 ARP Status Chart

### 2012 Accelerated Repair Program

- Invitations – 27 districts, representing 39 projects
- SOI Removals – three districts, representing three projects
- Approved Project Funding Agreements – 24 districts, representing 36 projects
  - Scope includes 21 roofs, 11 windows/doors and seven boilers
- Total Project Budgets – \$63,009,653
- MSBA Total Facilities Grants – \$38,267,952
- Five districts, representing nine projects, required schedule extensions following PFA approval
- 86% of projects bid within estimated budget
- *78% of projects have completed Final Audit*

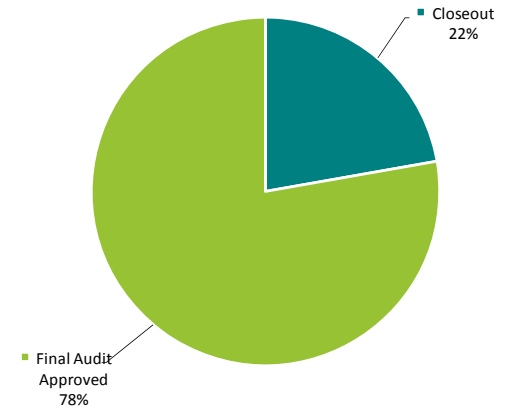

2012 ARP Status Chart

### Status of Green Repair Program

The Green Repair Program resulted in PFA authorizations totaling \$366,647,226 in Total Project Costs and \$222,889,218 in MSBA grants. Of the 189 projects, 180 have been approved for final grant payments. All projects that have not been previously approved for final grant payments (9) are substantially complete and require Final Audit.

**2014 Accelerated Repair Projects – Construction Estimate vs. 2015-2016 Bid Amount**

- Staff has reported previously on the shaded projects.
- As of this report, staff notes nine new projects have been added to the chart.
- 86% of the 37 reported projects came within the estimated budget.
- 10 additional projects are scheduled to be reported for the March 30, 2016 Board of Directors meeting.
- Bidding of remaining projects will be complete in February 2016.

				Total	\$69,417,752	\$52,697,079	\$16,720,673	-	\$11,887,007
District	School	Scope	Project Type	Bid Date	Construction Estimate **	Bid Amount **	Variance from Construction Estimate	Reimbursement Rate	Potential Grant Variance *
Quincy	Francis W. Parker MS	Windows/Doors	DBB	Jan-15	\$1,077,920	\$987,000	\$90,920	71.16%	\$64,699
Quincy	Lincoln-Hancock Community School	Windows/Doors	DBB	Jan-15	\$2,075,113	\$1,479,000	\$596,113	71.16%	\$424,194
Sudbury	General Nixon ES	Partial Roof/ Partial Windows/Doors	DBB	Feb-15	\$915,204	\$817,466	\$97,738	36.89%	\$36,056
Lynn	William P. Connery ES	Roof	DBB	Feb-15	\$859,532	\$604,000	\$255,532	78.95%	\$201,743
Lynn	E. J. Harrington ES	Roof	DBB	Feb-15	\$1,505,681	\$1,217,700	\$287,981	78.95%	\$227,361
Worcester	Goodard School of Science and Technology	Windows/Doors	DBB	Feb-15	\$4,634,609	\$3,053,000	\$1,581,609	78.95%	\$1,248,680
Worcester	West Tatnuck School	Windows/Doors	DBB	Feb-15	\$1,997,979	\$1,162,019	\$835,960	78.95%	\$659,990
Worcester	Clark Street Community	Windows/Doors	DBB	Feb-15	\$2,095,791	\$1,465,163	\$630,628	78.95%	\$497,881
Worcester	Union Hill School	Windows/Doors	DBB	Feb-15	\$2,096,895	\$1,618,818	\$478,077	78.95%	\$377,442
Dartmouth	George H. Potter ES	Roof	DBB	Feb-15	\$1,548,538	\$1,283,000	\$265,538	51.84%	\$137,655
Medway	John D. McGovern ES	Windows/Doors	DBB	Feb-15	\$894,675	\$561,886	\$332,789	50.16%	\$166,927
Norwood	Cornelius M. Callahan ES	Boiler	DBB	Mar-15	\$356,939	\$224,171	\$132,768	50.58%	\$67,154
Greenfield	Green River	Roof, Windows/Doors	DBB	Mar-15	\$1,739,286	\$1,005,890	\$733,396	77.47%	\$568,162
Springfield	Kensington Avenue	Windows/Doors	DBB	Mar-15	\$779,500	\$832,500	-\$53,000	80.00%	\$0
Wellesley	Wellesley MS	Windows/Doors	DBB	Mar-15	\$3,827,871	\$2,752,500	\$1,075,371	31.00%	\$333,365
Tyngsborough	Tyngsborough HS	Roof, Boiler	DBB	Mar-15	\$3,282,118	\$1,964,300	\$1,317,818	52.89%	\$696,994
Middleton	Fuller Meadow ES	Partial Roof	DBB	Apr-15	\$1,257,849	\$906,800	\$351,049	46.37%	\$162,781
Northampton	Leeds ES	Partial Roof	DBB	Apr-15	\$540,900	\$401,550	\$139,350	56.26%	\$78,398
Northampton	R. K. Finn Ryan Road School	Partial Roof	DBB	Apr-15	\$851,639	\$501,520	\$350,119	56.26%	\$196,977
North Attleborough	Roosevelt Avenue ES	Boiler	DBB	Apr-15	\$303,623	\$265,667	\$37,956	53.53%	\$20,318
Southern Berkshire RSD	Mount Everett RHS	Roof, Boiler	DBB	Apr-15	\$6,376,974	\$4,806,662	\$1,570,312	39.21%	\$615,719
Leominster	Northwest ES	Roof	DBB	May-15	\$2,693,028	\$1,805,000	\$888,028	71.96%	\$639,025
Tri-County RSD	Tri-County RVTHS	Boiler	DBB	Jun-15	\$729,259	\$494,131	\$235,128	51.42%	\$120,903
Auburn	Auburn MS	Roof, Partial Boiler	DBB	Jun-15	\$1,757,394	\$1,371,393	\$386,001	54.16%	\$209,058
Auburn	Bryn Mawr ES	Roof	DBB	Jun-15	\$671,935	\$578,000	\$93,935	54.16%	\$50,875

District	School	Scope	Project Type	Bid Date	Construction Estimate **	Bid Amount **	Variance from Construction Estimate	Reimbursement Rate	Potential Grant Variance *
South Shore Voc-Tech RSD	South Shore Voc-Tech Regional HS	Boiler	DBB	Aug-15	\$519,808	\$354,200	\$165,608	54.16%	\$89,693
Stoughton	Joseph H Gibbons	Roof Window/Door	DBB	Sep-15	\$2,740,109	\$1,914,220	\$825,889	54.16%	\$447,301
Gardner	Elm Street School	Boiler Window/Door	DBB	Sep-15	\$3,509,176	\$2,599,000	\$910,176	78.95%	\$718,584
Brockton	Brookfield ES	Roof	DBB	Oct-15	\$3,167,788	\$1,838,297	\$1,329,491	78.95%	\$1,049,633
Orleans	Orleans ES	Partial Window/Door	DBB	Oct-15	\$872,628	\$969,480	-\$96,852	36.68%	\$0
Randolph	J F Kennedy ES	Windows/Doors	DBB	Nov-15	\$2,079,590	\$2,031,583	\$48,007	74.74%	\$35,880
Randolph	Randolph HS	Partial Window/Door	DBB	Nov-15	\$4,461,242	\$2,428,015	\$2,033,227	74.74%	\$1,519,634
Springfield	J F Kennedy MS	Windows/Doors	DBB	Nov-15	\$2,229,800	\$3,732,000	-\$1,502,200	80.00%	\$0
Franklin County RSD	Franklin County Tech HS	Windows/Doors	DBB	Nov-15	\$1,711,460	\$1,656,723	\$54,737	73.89%	\$40,445
Wayland	Claypit Hill School	Windows/Doors	DBB	Dec-15	\$1,299,997	\$1,355,000	-\$55,003	35.42%	\$0
Melrose	Herbert Clark Hoover	Windows/Doors	DBB	Dec-15	\$1,090,827	\$734,000	\$356,827	51.42%	\$183,480
Gill-Montague RSD	Sheffield ES	Partial Window/Door	DBB	Dec-15	\$865,075	\$925,425	-\$60,350	76.00%	\$0

\*These numbers are based on preliminary information received from the district and are subject to further review and calculation.

\*\*The construction estimate and bid amount do not include pre-construction services and alternatives.

### Accelerated Repair Projects – Schedule Extension Update

The MSBA has granted districts conditional extensions to their Project Funding Agreements pending compliance with the following stipulations:

- The district needed to submit a detailed, revised construction timeline showing how the work will be completed at each school; and
- Any costs that may result from the district's requested extension of the construction schedule will be the sole responsibility of the district and are categorically ineligible for reimbursement by the MSBA.

Schedule delays for these districts can be attributed to local funding issues, lead time for windows, and construction delays on site. In no event have the extended schedules resulted in an increase to the Estimated Maximum Total Facilities Grant as authorized by the Board.

Six of the 47 2014 Accelerated Repair Projects will not meet their anticipated construction completion dates in 2015. These projects have revised construction schedules and are scheduled to be completed in 2016. Staff has reported previously on the five shaded projects listed below.

As of this report, staff notes that there is no new activity.

District	School	Scope	Original Construction Completion Date	Updated Construction Completion Date	Reason for Schedule Extension
Orleans	Orleans ES	Partial Window/Door	8/25/2015	8/29/2016	The District and its consultants have determined that the estimated lead time for windows requires construction to be scheduled for 2016.
Springfield	John F. Kennedy MS	Window/Door	12/22/2015	10/28/2016	The District and its consultants have determined that the estimated lead time for windows requires construction to be scheduled for 2016.
Brockton	Ashfield MS	Roof/Boiler	8/31/2015	7/11/2016	The District and its consultants have determined that the bidding for construction in 2016 would better serve the project budget and existing facilities.
Brockton	Gilmore School	Roof/Boiler	8/31/2015	7/11/2016	The District and its consultants have determined that the bidding for construction in 2016 would better serve the project budget and existing facilities.
Medfield	Ralph Wheelock School	Boiler	1/6/2016	8/31/2016	The District and its consultants have determined that the bidding for construction in 2016 would better serve the project budget and existing facility.
Springfield	Kensington Avenue	Window/Door	11/2/15	8/19/16	The District and its consultants have determined that the estimated lead time for windows requires construction to be scheduled for 2016.



# PROJECT VARIANCES

## Core Program – Total Project Budget Update

Upon receiving the Board’s approval of the Project Scope and Budget, the MSBA and participating districts enter into a Project Funding Agreement that establishes the Total Project Budget and the Estimated Maximum Total Facilities Grant for an approved project. Staff has reported on budget increases for the 14 projects shaded below at previous Board meetings. In no event has the increase in budget resulted in an increase to the Estimated Maximum Total Facilities Grant as authorized by the Board.

Since the last report, staff notes that no projects have increased its Total Project Budget.

District	School	Scope	Project Funding Agreement		PFA Bid Amendment/ Final Audit		Reason for Increase to Total Project Budget
			Total Project Budget	Total Maximum Facilities Grant	Total Project Budget	Total Maximum Facilities Grant	
Andover	Bancroft ES	New	\$44,659,837	\$16,773,753	\$50,374,837	\$16,575,965	The District has appropriated additional funds to cover the costs associated with increased construction costs and additional contingencies for litigation/settlement costs and other ineligible costs.
Burlington	Marshall Simonds MS	Add/Reno	\$32,865,272	\$17,143,365	\$34,221,929	\$15,362,127	The District appropriated at its May 2012 annual town meeting through Articles 18: 19, additional funds for the costs associated with the construction of the new field complex and field lighting replacement.
Essex North Shore Agricultural & Technical School District	Essex North Shore Agricultural & Technical High School	New	\$125,000,000	\$77,500,000	\$133,770,000	\$77,500,000	The Board was informed at the March 30, 2011 meeting that the Total Project Budget had increased due to additional ineligible scope that would be funded by DCAM.
Essex North Shore Agricultural & Technical School District	Essex North Shore Agricultural & Technical High School	New	\$125,000,000	\$77,500,000	\$134,501,368	\$77,500,000	The District has appropriated additional funds to cover the costs associated with increased construction costs for horse tack barn renovations.
Lexington	Estabrook ES	New	\$40,792,248	\$12,250,739	\$43,392,248	\$12,148,491	The District has executed a GMP that exceeds the Construction Budget of the PFA. The District has appropriated additional funds to cover the costs associated with increased construction costs and additional contingencies.
North Reading	North Reading MS/HS	Add/Reno	\$107,727,074	\$49,323,123	\$123,227,074	\$49,323,123	This is a CMR project. The estimated, reconciled construction costs tracked over budget at DD (\$9,746,655 over), 60% (\$4,655,965 over), and 90% (\$15,136,846 over). A Town override vote in March 2013 obtained an additional \$15,500,000 in local funding to proceed.
Revere	Staff Sergeant James J. Hill ES	New	\$45,402,396	\$29,551,048	45,402,396	\$29,551,048	At Project Scope and Budget, the Total Project Budget was approved at \$44,382,396. The City of Revere has increased the land acquisition budget. Therefore, the projected total project budget at PFA has increased to \$45,402,396. Note that the MSBA grant has not changed since the Project Scope and Budget Agreement.
Somerville	East Somerville Community School	Add/Reno	\$33,185,258	\$15,237,996	\$38,006,621	\$15,237,996	At the March 28, 2012 Board Meeting, the Board approved an amendment to the PFA and a \$6.25M District loan.
Uxbridge	Uxbridge HS	New	\$43,000,000	\$22,362,328	\$44,986,479	\$22,362,328	The District has appropriated additional funds to cover the costs associated with the construction of athletic fields originally included in the PFA but which were not included in the bid as the District’s construction contract would have exceeded the budget.
Norfolk County Agricultural	Norfolk County Agricultural HS	Add/Reno	\$28,552,385	\$15,369,712	30,589,078	13,867,050	The District has executed a Tender Agreement and Completion Agreement Contract, increasing its Total Project Budget, following the termination of its original construction contract.
Northborough	Lincoln Street ES	Add/Reno	\$25,530,553	\$10,407,408	TBD*	TBD*	The MSBA Board Approved Total Project Budget increased by \$60,400 from \$25,470,153 to \$25,530,553 due to the addition of an alternate, for a new ball field added at the District’s request.
Sutton	Sutton MS	Add/Reno	\$59,945,474	\$29,843,511	TBD*	TBD*	The District has executed a Tender Agreement and Completion Agreement Contract, increasing its Total Project Budget, following the termination of its original construction contract.
Weston	Field ES	New	\$31,504,146	\$8,310,510	TBD*	TBD*	District-approved Construction Change Orders exceeded available contingency amount.
Winthrop	Winthrop MS/HS	New	\$81,818,740	\$42,582,841	TBD*	TBD*	The MSBA Board Approved Total Project Budget increased due to revised FEMA flood plain requirements which necessitated the elevation of the new building to be raised. Note that the increased Total Project Budget will not increase the Maximum Total Facilities Grant.
Woburn**	Wyman-Hurld ES	New	\$33,705,396	\$14,387,427	TBD*	TBD*	The District had completed a project review with its Conservation Commission and an Order of conditions was issued on June 12, 2015. A neighborhood group has appealed this Order and it is now under review by DEP. The District has experienced delays in completing its City Council vote for its appropriation and incurred additional costs.

\*PFA Bid Amendment has not been developed to calculate a revised Total Facilities Grant amount. The Total Maximum Facilities Grant will not exceed the Board authorized amount in the PFA but, upon review, may decrease.

\*\*Pending an executed Project Funding Agreement.

# APPENDIX A PROJECT STATUS LIST

Date of Report: 1/8/2016

Total Projects: 306

MSBA ID	District	School	Project Phase	Project Type	Project Scope	Procurement Type	OPM	Designer	CM/GC	Commissioning Consultant
200800010405	Abington	Frolio Middle School	Construction	Core Program	New Construction	DBB	Knight, Bagge & Anderson Inc.	Ai3 Architects LLC	Brait Builders Corp.	Horizon Engineering Associates, LLP
201300080050	Amherst	Wildwood Elementary	Feasibility Study	Core Program			Joslin, Lesser + Associates Inc.	JCJ Architecture, PC	-	-
200800090003	Andover	Bancroft Elementary School	Closeout	Core Program	New Construction	CM@R	Dore & Whittier Management Partners, Inc.	Symmes Maini & McKee Associates, Inc.	Skanska USA Building, Inc.	Sebesta Blomberg & Associates, Inc.
201300140405	Ashland	Ashland Middle	Final Audit Approved	Accelerated Repair	Roof	DBB	Arcadis U.S., Inc.	Raymond Design Associates, Inc.	Gibson Roofs, Inc.	Gale Associates, Inc.
201300140010	Ashland	Henry E Warren Elem	Final Audit Approved	Accelerated Repair	Roof	DBB	Arcadis U.S., Inc.	Raymond Design Associates, Inc.	MDM Engineering	Gale Associates, Inc.
200908010605	Assabet Valley	Assabet Valley Regional Technical High School	Building Complete	Core Program	Repair	DBB	Colliers International	Design Partnership of Cambridge, Inc.	CTA Construction Co., Inc.	Symmes, Maini & McKee Associates
200906150020	Athol-Royalston	Riverbend School	Construction	Core Program	New Construction	DBB	Symmes Maini & McKee Associates	Mount Vernon Group Architects, Inc.	Fontaine Brothers, Inc.	Colliers International
201400160505	Attleboro	Attleboro High	OPM Selection	Core Program			-	-	-	-
200800170305	Auburn	Auburn Middle	Building Complete	Core Program	New Construction	CM@R	Skanska USA Building, Inc	Lamoureux Pagano & Associates, Inc.	Fontaine Brothers, Inc.	WSP USA
201400170305	Auburn	Auburn Middle	Building Complete	Accelerated Repair	Roof, Boiler		Skanska USA Building, Inc	Dietz & Company Architects, Inc.	-	Horizon Engineering Associates, LLP   Thompson & Lichtner Co., Inc.
201400170010	Auburn	Bryn Mawr	Building Complete	Accelerated Repair	Roof		Skanska USA Building, Inc	Dietz & Company Architects, Inc.	-	Thompson & Lichtner Co., Inc.
200806160505	Ayer-Shirley	Ayer-Shirley Regional Middle/High School	Building Complete	Core Program	Addition / Renovation	CM@R	Dore and Whittier Architects, Inc.	Symmes Maini & McKee Associates, Inc.	Consigli Construction Company, Inc.	WSP USA
201106160002G	Ayer-Shirley	Page Hilltop School		Green Repair		DBB	-	-	-	-
201300200010	Barnstable	Barnstable United Elementary School	Closeout	Accelerated Repair	Roof	DBB	exPERTcon, Inc.	Gale Associates, Inc.	Capeway Roofing Systems, Inc.	Russo Barr Associates, Inc.
201100200005G	Barnstable	West Barnstable Elem	Closeout	Green Repair	Windows / Doors	DBB	PMA Construction Services	-	Paul J. Rogan Co., Inc.	CBI Consulting Inc.
201200250009	Bellingham	Clara Macy Elementary		Core Program			-	-	-	-
201400250020	Bellingham	South Elem	Design Development	Accelerated Repair	Roof		Atlantic Construction and Management, Inc.	-	-	Building Enclosure Associates, LLC
201100260015G	Belmont	Daniel Butler		Green Repair		DBB	-	-	-	-
200800260035	Belmont	Roger Wellington Elementary School	Closeout	Core Program	New Construction	CM@R	PMA Construction Services	Jonathan Levi Architects LLC	Skanska USA Building, Inc.	Colliers International
200806200505	Berlin-Boylston	Tahanto Regional High School	Building Complete	Core Program	New Construction	DBB	PMA Construction Services	HMFH Architects, Inc.	CTA Construction Co., Inc.	Colliers International
200800300505	Beverly	Beverly High School	Final Audit Approved	Core Program	Addition / Renovation	DBB	HEERY	Mount Vernon Group Architects, Inc.	CTA Ventures	-
201300300305	Beverly	Briscoe Middle	Design Development	Core Program	New Construction		HEERY	Ai3 Architects LLC	-	Bard, Rao + Athanas Consulting Engineers, LLC
201300310505	Billerica	Billerica Memorial High School	Schematic Design	Core Program	New Construction		KV Associates, Inc.	Perkins+Will	-	-
201508050605	Blackstone Valley Reg	Blackstone Valley	Schematic Design	Accelerated Repair	Roof		Watermark Environmental, Inc.	Russo Barr Associates, Inc.	-	Gale Associates, Inc.
201206220505	Blackstone-Millville	Blackstone Millville RHS	Closeout	Accelerated Repair	Roof	DBB	Arcadis U.S., Inc.	DiMarinisi & Wolfe Architects Urban Designers	-	Gale Associates, Inc.
201306220010	Blackstone-Millville	Millville Elem	Building Complete	Accelerated Repair	Roof	DBB	Pinck & Co., Inc.	CBI Consulting Inc.	MDM Engineering	Simpson Gumpertz & Heger Inc.
201500350651	Boston	Dorchester Academy	OPM Selection	Accelerated Repair	Windows / Doors		-	-	-	-
201300350546	Boston	Boston Arts Academy	OPM Selection	Core Program			-	-	-	-

201500350052	Boston	Charles Sumner	OPM Selection	Accelerated Repair	Windows / Doors	-	-	-	-	-
201500350020	Boston	Curley K-8 School	OPM Selection	Accelerated Repair	Windows / Doors	-	-	-	-	-
201500350072	Boston	David A Ellis	OPM Selection	Accelerated Repair	Windows / Doors	-	-	-	-	-
201500350080	Boston	Donald Mckay	OPM Selection	Accelerated Repair	Windows / Doors	-	-	-	-	-
200800350415	Boston	Grover Cleveland		Core Program		-	-	-	-	-
201500350415	Boston	Grover Cleveland	OPM Selection	Accelerated Repair	Windows / Doors	-	-	-	-	-
201000350074	Boston	Henry Dearborn Middle School	Construction	Core Program	New Construction	CM@R	Daedalus Projects Inc	Jonathan Levi Architects LLC	Gilbane Building Company	Symmes, Maini & McKee Associates
201000350565	Boston	Quincy Upper School	Feasibility Study	Core Program			Skanska USA Building, Inc	HMFH Architects, Inc.	-	-
201500350380	Boston	Young Achievers	OPM Selection	Accelerated Repair	Windows / Doors	-	-	-	-	-
201400360010	Bourne	James F Peebles Elem	Feasibility Study	Core Program			Symmes Maini & McKee Associates, Inc.	Flansburgh Associates, Inc.	-	-
201300400305	Braintree	East Middle School	Feasibility Study	Core Program			Hill International Company	Miller Dyer Spears Inc.	-	-
201206250320	Bridgewater-Raynham	Bridgewater Middle School	Closeout	Accelerated Repair	Roof	DBB	Vertex Construction Services	-	-	CBI Consulting Inc.
201206250050	Bridgewater-Raynham	Laliberte Elementary School	Closeout	Accelerated Repair	Roof	DBB	Vertex Construction Services	Raymond Design Associates, Inc.	-	CBI Consulting Inc.
201206250020	Bridgewater-Raynham	Merrill Elementary School	Closeout	Accelerated Repair	Roof	DBB	Vertex Construction Services	Raymond Design Associates, Inc.	-	CBI Consulting Inc.
201409100705	Bristol County Agr	Bristol County Agr High	OPM Selection	Core Program			-	-	-	-
201400440421	Brockton	Ashfield Middle School	Construction	Accelerated Repair	Roof, Boiler		Architectural Consulting Group, LLC	Tighe & Bond, Inc.	-	Rist-Frost-Shumway Engineering, P.C.   Simpson Gumpertz & Heger Inc.
201400440080	Brockton	Barrett Russell School	Design Development	Accelerated Repair	Windows / Doors		Architectural Consulting Group, LLC	Tighe & Bond, Inc.	-	Simpson Gumpertz & Heger Inc.
201400440010	Brockton	Brookfield	Construction	Accelerated Repair	Roof		Architectural Consulting Group, LLC	Tighe & Bond, Inc.	-	Simpson Gumpertz & Heger Inc.
201400440035	Brockton	Gilmore	Construction	Accelerated Repair	Roof, Boiler		Architectural Consulting Group, LLC	Tighe & Bond, Inc.	-	Rist-Frost-Shumway Engineering, P.C.   Simpson Gumpertz & Heger Inc.
201100460015	Brookline	Edward Devotion	Design Development	Core Program	Addition / Renovation		Anthony Guigli Town Employee	HMFH Architects, Inc.	Shawmut Design and Construction	Consulting Engineering Services, LLC
201500490090	Cambridge	Fletcher/Maynard Academy	Schematic Design	Accelerated Repair	Boiler		-	-	-	Fitzemeyer & Tocci Associates, Inc.
201500490040	Cambridge	Kennedy-Longfellow	Schematic Design	Accelerated Repair	Roof		-	-	-	Thompson & Lichtner Co., Inc.
201200500012	Canton	Lt Peter M Hansen	Closeout	Accelerated Repair	Windows / Doors	DBB	Vertex Construction Services	CSS Architects Incorporated	Lockheed Window Corporations	Simpson Gumpertz & Heger Inc.
201200500305	Canton	Wm H Galvin Middle	Closeout	Accelerated Repair	Windows / Doors	DBB	Vertex Construction Services	CSS Architects Incorporated	Lockheed Window Corporations	Simpson Gumpertz & Heger Inc.
201408150605	Cape Cod Region Voc Tech	Cape Cod Region Voc Tech	OPM Selection	Core Program			-	-	-	-
201300520015	Carver	Carver Elementary School	Design Development	Core Program	New Construction		PMA Construction Services	HMFH Architects, Inc.	-	Symmes, Maini & McKee Associates
200800570050	Chelsea	Clark Avenue School	Construction	Core Program	New Construction	CM@R	Pinck & Co., Inc.	HMFH Architects, Inc.	W. T. Rich Company Inc.	Cannon Design
201500610010	Chicopee	Belcher	Schematic Design	Accelerated Repair	Roof		Joslin, Lesser + Associates Inc.	Kaestle Boos Associates, Inc.	-	Building Enclosure Associates, LLC
200900610021	Chicopee	Chicopee Academy	Building Complete	Core Program	Renovation	DBB	Arcadis U.S., Inc.	Caolo & Bieniek Associates, Inc.	Fontaine Brothers, Inc.	Symmes, Maini & McKee Associates
201500610310	Chicopee	Fairview Middle	Schematic Design	Accelerated Repair	Roof		-	Kaestle Boos Associates, Inc.	-	Building Enclosure Associates, LLC
201400630010	Clarksburg	Clarksburg Elementary	OPM Selection	Core Program			-	-	-	-
200906400505	Concord-Carlisle	Concord-Carlisle Regional High School	Building Complete	Core Program	New Construction	CM@R	KV Associates, Inc.	OMR Architects, Inc.	Turner Construction Company	Colliers International

200800710505	Danvers	Danvers High School	Closeout	Core Program	Addition / Renovation	DBB	Construction Monitoring Services, Inc.	DiNisco Design Partnership, Limited	Bacon Construction Co, Inc.	Turner Facilities Management Solutions
201400720030	Dartmouth	George H Potter	Construction	Accelerated Repair	Roof		Pinck & Co., Inc.	Russo Barr Associates, Inc.	Greenwood Industries, Inc.	Gale Associates, Inc.
201200730005	Dedham	Early Childhood Center	Schematic Design	Core Program	New Construction		Construction Monitoring Services, Inc.	Knight, Bagge & Anderson, Inc.	-	-
201500740015	Deerfield	Deerfield Elem	Schematic Design	Accelerated Repair	Roof		Pinck & Co., Inc.	Raymond Design Associates, Inc.	-	Russo Barr Associates, Inc.
201306500005	Dighton-Rehoboth	Dighton Elementary	Building Complete	Accelerated Repair	Roof	DBB	Arcadis U.S., Inc.	Dietz & Company Architects, Inc.	MDM Engineering	Gale Associates, Inc.
201306500305	Dighton-Rehoboth	Dighton Middle School	Building Complete	Accelerated Repair	Roof	DBB	Arcadis U.S., Inc.	Dietz & Company Architects, Inc.	MDM Engineering	Gale Associates, Inc.
201306500310	Dighton-Rehoboth	Dorothy L Beckwith	Building Complete	Accelerated Repair	Roof	DBB	Arcadis U.S., Inc.	Dietz & Company Architects, Inc.	Greenwood Industries, Inc.	Gale Associates, Inc.
201106500010G	Dighton-Rehoboth	Palmer River		Green Repair		DBB	-	-	-	-
200800770010	Douglas	Douglas Elementary	Closeout	Core Program	New Construction - Model School	DBB	HEERY	DiNisco Design Partnership, Limited	CTA Construction Co., Inc.	Consulting Engineering Services, LLC
200800770100G	Douglas	Douglas Intermediate Elementary School	Closeout	Green Repair	Roof, Windows / Doors, Boiler	DBB	HEERY	DiNisco Design Partnership, Limited	CTA Construction Co., Inc.	Consulting Engineering Services, LLC
200800790505	Dracut	Dracut Senior High School	Building Complete	Core Program	Addition / Renovation	DBB	Hill International Company	Mount Vernon Group Architects, Inc.	CTA Construction Co., Inc.	RDK Engineers
201000820505	Duxbury	Duxbury High School	Building Complete	Core Program	New Construction - Model School	CM@R	KV Associates, Inc.	Mount Vernon Group Architects, Inc.	Dimeo Construction Company	WSP USA
200900830505	East Bridgewater	East Bridgewater High School	Building Complete	Core Program	New Construction - Model School	DBB	Hill International Company	Ai3 Architects LLC	Fontaine Brothers, Inc.	Foreman Building Commissioning, LP
201400860010	Easthampton	Maple	OPM Selection	Core Program			-	-	-	-
201300880020	Easton	Moreau Hall	Closeout	Accelerated Repair	Roof	DBB	Skanska USA Building, Inc	Baker/Wohl Architects, Inc.	Capeway Roofing Systems, Inc.	Gale Associates, Inc.
200809130705	Essex Agr Tech	Essex Agricultural and Technical High School	Building Complete	Core Program	New Construction	CM@R	PMA Construction Services	Design Partnership of Cambridge, Inc.	Gilbane Building Company	Turner Facilities Management Solutions
201400930028	Everett	George Keverian School	Eligibility Period	Core Program			-	-	-	-
201500940305	Fairhaven	Hastings Middle	Schematic Design	Accelerated Repair	Roof		Potomac Capital Advisors	CGKV Architects, Inc.	-	Gale Associates, Inc.
201400950505	Fall River	B M C Durfee High	OPM Selection	Core Program			-	-	-	-
200900950315	Fall River	James Madison Morton Middle School	Closeout	Core Program	New Construction	DBB	Maguire Group Inc.	Mount Vernon Group Architects, Inc.	J & J Contractors, Inc.	Sebesta Blomberg & Associates, Inc.
201400960405	Falmouth	Lawrence	Design Development	Accelerated Repair	Windows / Doors		PMA Construction Services	Civitects PC	-	Gale Associates, Inc.
200800970016	Fitchburg	Crocker Elementary		Core Program			-	-	-	-
200901010505	Franklin	Franklin High School	Building Complete	Core Program	New Construction - Model School	DBB	Daedalus Projects Inc	Ai3 Architects LLC	Bacon-Agostini Construction Joint Venture	Consulting Engineering Services, LLC
201408180605	Franklin County	Franklin County Tech	Design Development	Accelerated Repair	Windows / Doors		Colliers International	Habeeb & Associates Architects, Inc.	-	CBI Consulting Inc.
201401030001	Gardner	Elm Street School	Construction	Accelerated Repair	Windows / Doors, Boiler		Hill International Company	ICON architecture, inc.	Thielsch Engineering, Inc.	Fitzmeyer & Tocci Associates, Inc.   Thompson & Lichtner Co., Inc.
201201030505	Gardner	Gardner High	Closeout	Science Lab Initiative	Addition / Renovation	DBB	Pinck & Co., Inc.	Lamoureux Pagano & Associates, Inc.	Five Star Building Corp.	Fitzmeyer & Tocci Associates, Inc.
201201030405	Gardner	Gardner Middle School	Final Audit Approved	Accelerated Repair	Boiler		Leftfield, LLC	Richard D. Kimball Company, Inc.	Royal Steam Heater Co.	Fitzmeyer & Tocci Associates, Inc.
200801050505	Georgetown	Georgetown Middle/High School	Building Complete	Core Program	Renovation	DBB	Municipal Building Consultants, Inc.	Drumme Rosane Anderson, Inc.	L.D. Russo, Inc.	WSP USA
200901050010	Georgetown	Penn Brook Elementary School	Building Complete	Core Program	New Construction	DBB	Municipal Building Consultants, Inc.	Drumme Rosane Anderson, Inc.	Brait Builders Corp.	Rist-Frost-Shumway Engineering, P.C.
201406740050	Gill-Montague	Sheffield Elementary	Design Development	Accelerated Repair	Windows / Doors, Boiler		NETCO Construction Project Managers, Inc.	The S/L/A/M Collaborative	-	CBI Consulting Inc.

200901070050	Gloucester	West Parish Elementary School	Construction	Core Program	New Construction	CM@R	Knight, Bagge & Anderson Inc.	Dore & Whittier Architects, Inc.	W. T. Rich Company Inc.	Fitzmeyer & Tocci Associates, Inc.
201201110010	Granby	West St	Schematic Design	Core Program			Colliers International	Jones Whitsett Architects, Inc.	-	-
201108230605	Greater Lawrence RVT	Gr Lawrence Reg Voc Tech	Building Complete	Core Program	Repair	DBB	Vertex Construction Services	Richard D. Kimball Company, Inc.	E. Amanti & Sons, Inc.	WSP USA
200908280605	Greater Lowell Voc Tec	Greater Lowell Regional Technical High School	Building Complete	Core Program	Addition / Renovation	CM@R	Joslin, Lesser + Associates Inc.	Knight, Bagge & Anderson, Inc.	Consigli Construction Company, Inc.	Horizon Engineering Associates, LLP
201008250605	Greater New Bedford	Greater New Bedford Vocational Technical High School	Building Complete	Core Program	Addition / Renovation	DBB	Construction Monitoring Services, Inc.	Drumey Rosane Anderson, Inc.	Agostini Construction Co., Inc.	Symmes, Maini & McKee Associates
201501140010	Greenfield	Federal	Schematic Design	Accelerated Repair	Roof, Windows / Doors, Boiler		-	-	-	Colliers International
201401140030	Greenfield	Green River	Construction	Accelerated Repair	Roof, Windows / Doors, Boiler		Arcadis U.S., Inc.	Baker/Wohl Architects, Inc.	RAC Builders, Inc.	CBI Consulting Inc.
200901140505	Greenfield	Greenfield High School	Building Complete	Core Program	New Construction	CM@R	Construction Monitoring Services, Inc.	Dore & Whittier Architects, Inc.	Shawmut Design and Construction	BVH Integrated Services, P.C.
201106730010G	Groton-Dunstable	Florence Roche School		Green Repair		DBB	-	-	-	-
201106730005G	Groton-Dunstable	Swallow/Union School		Green Repair		DBB	-	-	-	-
201306750007	Hamilton-Wenham	Bessie Buker Elementary	Final Audit Approved	Accelerated Repair	Boiler	DBB	NETCO Construction Project Managers, Inc.	Habeeb & Associates Architects, Inc.	Multitemp Mechanical Corporation	Colliers International
201306750015	Hamilton-Wenham	Winthrop School	Building Complete	Accelerated Repair	Windows / Doors, Boiler	DBB	NETCO Construction Project Managers, Inc.	Habeeb & Associates Architects, Inc.	E. Amanti & Sons, Inc.	CBI Consulting Inc.   Colliers International
201406800030	Hampden-Wilbraham	Soule Road		Accelerated Repair	Windows / Doors		exPERTcon, Inc.	The S/L/A/M Collaborative	-	-
201406800305	Hampden-Wilbraham	Thornton Burgess		Accelerated Repair	Windows / Doors		-	-	-	-
201406800310	Hampden-Wilbraham	Wilbraham Middle		Accelerated Repair	Roof		exPERTcon, Inc.	The S/L/A/M Collaborative	-	-
201301220015	Hanover	Sylvester	Feasibility Study	Core Program			P3 Inc.	Mount Vernon Group Architects, Inc.	-	-
201101250005G	Harvard	Harvard Elementary		Green Repair		DBB	-	-	-	-
201301270505	Hatfield	Smith Academy	Closeout	Accelerated Repair	Roof, Windows / Doors	DBB	Hill International Company	Civitects PC	Silktown Roofing	Building Enclosure Associates, LLC
201201280035	Haverhill	Caleb Dustin Hunking	Construction	Core Program	New Construction	CM@R	Joslin, Lesser + Associates Inc.	JCJ Architecture, PC	Shawmut Design and Construction	Colliers International
201101280100G	Haverhill	Consentino	Closeout	Green Repair	Windows / Doors	DBB	Vertex Construction Services	CSS Architects Incorporated	New England Builders & Contractors, Inc.	RDK Engineers   Russo Barr Associates, Inc.
201101280085G	Haverhill	John G Whittier	Closeout	Green Repair	Windows / Doors	DBB	Vertex Construction Services	CSS Architects Incorporated	New England Builders & Contractors, Inc.	Russo Barr Associates, Inc.
201101280075G	Haverhill	Tilton	Closeout	Green Repair	Roof	DBB	Vertex Construction Services	CSS Architects Incorporated	Titan Roofing, Inc.	Russo Barr Associates, Inc.
201101280080G	Haverhill	Walnut Square	Closeout	Green Repair	Roof, Windows / Doors	DBB	Vertex Construction Services	CSS Architects Incorporated	Titan Roofing, Inc.	RDK Engineers   Russo Barr Associates, Inc.
201001310410	Hingham	Hingham Middle School	Building Complete	Core Program	New Construction - Model School	DBB	Knight, Bagge & Anderson Inc.	Ai3 Architects LLC	Brait Builders Corp.	Foreman Building Commissioning, LP
200801330505	Holbrook	Holbrook Junior-Senior High School	Construction	Core Program	New Construction	CM@R	Symmes Maini & McKee Associates, Inc.	Flansburgh Associates, Inc.	Consigli Construction Company, Inc.	Consulting Engineering Services, LLC
201401370045	Holyoke	E N White Elem	Design Development	Accelerated Repair	Boiler		-	-	-	BVH Integrated Services, P.C.
201201370015	Holyoke	Lt Elmer J McMahon Elem	OPM Selection	Core Program			-	-	-	-
201401370025	Holyoke	Morgan Elem	Design Development	Accelerated Repair	Boiler		-	-	-	BVH Integrated Services, P.C.
201201370605	Holyoke	Wm J Dean Voc Tech High	Building Complete	Science Lab Initiative	Addition / Renovation	DBB	Skanska USA Building, Inc	Kaestle Boos Associates, Inc.	RAC Builders, Inc.	BVH Integrated Services, P.C.
201301380010	Hopedale	Memorial	Final Audit Approved	Accelerated Repair	Roof	DBB	Atlantic Construction and Management, Inc.	Civitects PC	MDM Engineering	Simpson Gumpertz & Heger Inc.

201301390005	Hopkinton	Center	Design Development	Core Program	New Construction		Compass Project Management, Inc.	Drumrey Rosane Anderson, Inc.	-	RDK Engineers
200801410410	Hudson	John F. Kennedy Middle School	Closeout	Core Program	New Construction	DBB	PMA Construction Services	OMR Architects, Inc.	Bacon-Agostini Construction Joint Venture	WSP USA
201401410007	Hudson	Mulready Elementary	Design Development	Accelerated Repair	Roof		Atlantic Construction and Management, Inc.	Raymond Design Associates, Inc.	-	CBI Consulting Inc.
201401440015	Ipswich	Winthrop	Feasibility Study	Core Program			-	-	-	-
201501510505	Leicester	Leicester High	Design Development	Accelerated Repair	Roof		Hill International Company	Gale Associates, Inc.	-	Russo Barr Associates, Inc.
201501530025	Leominster	Johnny Appleseed	Schematic Design	Accelerated Repair	Roof, Windows / Doors		-	Habeeb & Associates Architects, Inc.	-	Russo Barr Associates, Inc.
201401530030	Leominster	Northwest	Construction	Accelerated Repair	Roof		Architectural Consulting Group, LLC	Gale Associates, Inc.	Greenwood Industries, Inc.	Building Enclosure Associates, LLC
201101540005G	Leverett	Leverett Elementary	Final Audit Approved	Green Repair	Roof, Windows / Doors	DBB	Potomac Capital Advisors	DiMarinisi & Wolfe Architects Urban Designers	-	Russo Barr Associates, Inc.
201101550010E	Lexington	Joseph Estabrook	Closeout	Core Program	New Construction	CM@R	Hill International Company	DiNisco Design Partnership, Limited	Shawmut Design and Construction	BVH Integrated Services, P.C.
200801590505	Longmeadow	Longmeadow High School	Closeout	Core Program	New Construction	CM@R	Joslin, Lesser + Associates Inc.	OMR Architects, Inc.	Gilbane Building Company	Foreman Building Commissioning, LP
201401600505	Lowell	Lowell High	OPM Selection	Core Program			-	-	-	-
201501610010	Ludlow	East Street Elementary School	Feasibility Study	Accelerated Repair	Roof, Boiler		-	-	-	-
200801620505	Lunenburg	Lunenburg High School		Core Program			-	-	-	-
201001620505	Lunenburg	Lunenburg High School	Construction	Core Program	New Construction	CM@R	Joslin, Lesser + Associates Inc.	Tappe Associates, Inc.	Shawmut Design and Construction	Cannon Design
201201630405	Lynn	Breed Middle School	Final Audit Approved	Accelerated Repair	Windows / Doors	DBB	Diversified Project Management	Kaestle Boos Associates, Inc.	GVW, Inc.	CBI Consulting Inc.
201401630045	Lynn	E J Harrington	Construction	Accelerated Repair	Roof		NETCO Construction Project Managers, Inc.	Habeeb & Associates Architects, Inc.	Capeway Roofing Systems, Inc.	CBI Consulting Inc.
201201630605	Lynn	Lynn Voc Tech Institute	Final Audit Approved	Accelerated Repair	Roof	DBB	Diversified Project Management	Kaestle Boos Associates, Inc.	Gibson Roofs, Inc.	CBI Consulting Inc.
201401630420	Lynn	Pickering Middle	OPM Selection	Core Program			-	-	-	-
200901630305	Lynn	Thurgood Marshall Middle School	Construction	Core Program	New Construction	CM@R	Joslin, Lesser + Associates Inc.	Raymond Design Associates, Inc.	Walsh Brothers, Inc.	Rist-Frost-Shumway Engineering, P.C.
201401630040	Lynn	Wm P Connery	Construction	Accelerated Repair	Roof		NETCO Construction Project Managers, Inc.	Habeeb & Associates Architects, Inc.	Gibson Roofs, Inc.	CBI Consulting Inc.
200801680020	Marblehead	Glover School	Closeout	Core Program	New Construction	DBB	Municipal Building Consultants, Inc.	JCJ Architecture, PC	G & R Construction, Inc.	RDK Engineers
201101710505	Marshfield	Marshfield High	Building Complete	Core Program	New Construction - Model School	DBB	Compass Project Management, Inc.	Ai3 Architects LLC	Brait Builders Ventures	Sebesta Blomberg & Associates, Inc.
201101720035G	Mashpee	Quashnet School		Green Repair		DBB	-	-	-	-
200801740505	Maynard	Maynard High School	Final Audit Approved	Core Program	New Construction	DBB	Municipal Building Consultants, Inc.	Tappe Associates, Inc.	CTA Construction Co., Inc.	WSP USA
201401750007	Medfield	Ralph Wheelock School	Design Development	Accelerated Repair	Boiler		-	-	-	RDK Engineers
201201760505	Medford	Medford High	Building Complete	Science Lab Initiative	Addition / Renovation	DBB	Leftfield, LLC	DiNisco Design Partnership, Limited	G & R Construction, Inc.	Cannon Design
201301760505	Medford	Medford High	Closeout	Accelerated Repair	Windows / Doors, Boiler	DBB	Architectural Consulting Group, LLC	Dietz & Company Architects, Inc.	NB Kenney Company, Inc	Symmes, Maini & McKee Associates
201401770013	Medway	John D Mc Govern Elem	Building Complete	Accelerated Repair	Windows / Doors		Arcadis U.S., Inc.	CBI Consulting Inc.	-	Russo Barr Associates, Inc.
201401780017	Melrose	Herbert Clark Hoover	Design Development	Accelerated Repair	Windows / Doors		Colliers International	ICON architecture, inc.	-	Simpson Gumpertz & Heger Inc.
201201780505	Melrose	Melrose High	Final Audit Approved	Science Lab Initiative	Addition / Renovation	DBB	Hill International Company	Ai3 Architects LLC	G & R Construction, Inc.	WSP USA
201101780050	Melrose	Winthrop		Core Program			-	-	-	-
200801810505	Methuen	Methuen High School	Closeout	Core Program	Addition / Renovation	CM@R	KBA/Trident	Finegold Alexander and Associates Inc.	Consigli Construction Company, Inc.	Environmental Health and Engineering
201501820011	Middleborough	Memorial Early Childhood Center	Schematic Design	Accelerated Repair	Roof		Architectural Consulting Group, LLC	Knight, Bagge & Anderson, Inc.	-	Russo Barr Associates, Inc.

201401820505	Middleborough	Middleborough High	OPM Selection	Core Program							
201401840003	Middleton	Fuller Meadow	Building Complete	Accelerated Repair	Roof		Hill International Company	CBI Consulting Inc.	-		Building Enclosure Associates, LLC
201101850090	Milford	Woodland	Construction	Core Program	New Construction	CM@R	Joslin, Lesser + Associates Inc.	HMFH Architects, Inc.	Shawmut Design and Construction		Consulting Engineering Services, LLC
201401870005	Millis	Clyde F Brown	Feasibility Study	Core Program			Compass Project Management, Inc.	Tappe Associates, Inc.	-		
200908300605	Minuteman Voc Tech	Minuteman Regional High School	Schematic Design	Core Program			Skanska USA Building, Inc	Kaestle Boos Associates, Inc.	-		
201107129999	Monomoy	Monomoy Regional High School	Building Complete	Core Program	New Construction - Model School	DBB	Skanska USA Building, Inc	Mount Vernon Group Architects, Inc.	Fontaine Brothers, Inc.		Sebesta Blomberg & Associates, Inc.
201307150505	Mount Greylock	Mt Greylock Reg High	Schematic Design	Core Program	Addition / Renovation		Dore & Whittier Management Partners, Inc.	Design Partnership of Cambridge, Inc.	-		
200807200020	Narragansett	Templeton Center School	Design Development	Core Program			Colliers International	Symmes Maini & McKee Associates, Inc.	-		
201407250025	Nashoba	Florence Sawyer Sch	Closeout	Accelerated Repair	Boiler				-		
200807250015	Nashoba	Pompositicut Elementary School	Closeout	Core Program	Addition / Renovation	DBB	Construction Monitoring Services, Inc.	Symmes Maini & McKee Associates, Inc.	P.J. Stella Construction Corp.		Colliers International
201308520605	Nashoba Valley Tech	Nashoba Valley Tech H S	Closeout	Accelerated Repair	Roof	DBB	STV Incorporated	CGKV Architects, Inc.	Stanley Roofing Company, Inc.		CBI Consulting Inc.
201101980031G	Natick	Johnson	Green Repair			DBB			-		
201306600305	Nauset	Nauset Reg Middle	Final Audit Approved	Accelerated Repair	Roof	DBB	Colliers International	ICON architecture, inc.	Capeway Roofing Systems, Inc.		Russo Barr Associates, Inc.
201301990035	Needham	Hillside Elementary	Feasibility Study	Core Program			Steven H. Popper Town Employee	Dore & Whittier Architects, Inc.	-		
201502010063	New Bedford	Alfred J Gomes	Schematic Design	Accelerated Repair	Windows / Doors		Vertex Construction Services		-		CBI Consulting Inc.
201502010123	New Bedford	Casmir Pulaski	Schematic Design	Accelerated Repair	Windows / Doors, Boiler		Vertex Construction Services		-		CBI Consulting Inc.   WSP USA
201502010078	New Bedford	Hayden/McFadden	Schematic Design	Accelerated Repair	Windows / Doors, Boiler		Vertex Construction Services		-		CBI Consulting Inc.   WSP USA
201202010115	New Bedford	John Avery Parker		Core Program					-		
201502010115	New Bedford	John Avery Parker	Schematic Design	Accelerated Repair	Windows / Doors, Boiler		Vertex Construction Services		-		
200902010070	New Bedford	John Hannigan	Design Development	Core Program	New Construction		Daedalus Projects Inc	Turowski2 Architecture, Inc.	-		WSP USA
W201002010505P2	New Bedford	New Bedford High	Building Complete	Waitlist	Repair	DBB	Architectural Consulting Group, LLC	Mount Vernon Group Architects, Inc.	Sparks Company, Inc.		
201502010045	New Bedford	Sgt Wm H Carney Acad	Schematic Design	Accelerated Repair	Windows / Doors		Vertex Construction Services		-		CBI Consulting Inc.   WSP USA
W201002019999P2	New Bedford	Taylor School at the Sea Lab Marine Science Education Center	Construction	Waitlist	Addition / Renovation	DBB			-		
201102040005	Newburyport	Francis T Bresnahan Elem	Closeout	Core Program	New Construction - Model School	DBB	HEERY	HMFH Architects, Inc.	CTA Construction Co., Inc.		Fitzmeyer & Tocci Associates, Inc.
201002040305	Newburyport	Rupert A. Nock Middle School	Closeout	Core Program	Addition / Renovation	CM@R	HEERY	Miller Dyer Spears Inc.	Gilbane Building Company		Fitzmeyer & Tocci Associates, Inc.
201102070005	Newton	A E Angier	Building Complete	Core Program	New Construction	CM@R	Joslin, Lesser + Associates Inc.	DiNisco Design Partnership, Limited	W. T. Rich Company Inc.		Fitzmeyer & Tocci Associates, Inc.
201302070025	Newton	Cabot	Schematic Design	Core Program		CM@R	Joslin, Lesser + Associates Inc.	DiNisco Design Partnership, Limited	W. T. Rich Company Inc.		
200802079999	Newton	Carr School		Core Program					-		
200802079998	Newton	Newton Education Center		Core Program					-		
200802080005	Norfolk	Freeman-Kennedy Elementary School	Closeout	Core Program	New Construction	DBB	Joslin, Lesser + Associates Inc.	Flansburgh Associates, Inc.	Fontaine Brothers, Inc.		WSP USA
200909150705	Norfolk County Agriculture	Norfolk County Agr	Closeout	Core Program	Addition / Renovation	DBB	Compass Project Management, Inc.	Turowski2 Architecture, Inc.	Brait Builders Corp.		Rist-Frost-Shumway Engineering, P.C.
200802090305	North Adams	Silvio O Conte Middle School	Building Complete	Core Program	Addition / Renovation	DBB	Colliers International	Jones Whitsett Architects, Inc.	PDS Engineering and Construction, Inc.		Rist-Frost-Shumway Engineering, P.C.



201402120015	North Attleborough	Roosevelt Avenue	Building Complete	Accelerated Repair	Boiler		Pinck & Co., Inc.	Consulting Engineering Services, LLC	Falite Brothers Inc.	Bard, Rao + Athanas Consulting Engineers, LLC
201107350505	North Middlesex	North Middlesex Reg	Construction	Core Program	New Construction	DBB	HEERY	Symmes Maini & McKee Associates, Inc.	CTA Construction Co., Inc.	Horizon Engineering Associates, LLP
201502170003	North Reading	E Ethel Little School	Schematic Design	Accelerated Repair	Roof		Compass Project Management, Inc.	HAKS Engineers, P.C.	-	Thompson & Lichtner Co., Inc.
201002170505	North Reading	North Reading High School	Building Complete	Core Program	Addition / Renovation	CM@R	PMA Construction Services	Dore & Whittier Architects, Inc.	Gilbane Building Company	Cannon Design
201402100025	Northampton	Leeds	Building Complete	Accelerated Repair	Roof		STV Incorporated	Raymond Design Associates, Inc.	R & H Roofing, LLP	Russo Barr Associates, Inc.
201402100029	Northampton	R. K. Finn Ryan Road	Building Complete	Accelerated Repair	Roof		STV Incorporated	Raymond Design Associates, Inc.	R & H Roofing, LLP	Russo Barr Associates, Inc.
200904060705	Northampton-Smith	Smith Vocational and Agricultural High School		Core Program		DBB	-	-	-	-
201102130003	Northborough	Lincoln Street	Construction	Core Program	Addition / Renovation	DBB	Colliers International	Lamoureux Pagano & Associates, Inc.	Brait Builders Corp.	Fitzmeyer & Tocci Associates, Inc.
200908530605	Northeast Metro Voc	Northeast Metro Reg Voc		Core Program			-	-	-	-
200902180505	Norton	Norton High School	Building Complete	Core Program	Addition / Renovation	CM@R	Pinck & Co., Inc.	JCJ Architecture, PC	W. T. Rich Company Inc.	Rist-Frost-Shumway Engineering, P.C.
201402200010	Norwood	Cornelius M Callahan	Building Complete	Accelerated Repair	Boiler		PMA Construction Services	Consulting Engineering Services, LLC	George T. Wilkinson, Inc.	Symmes, Maini & McKee Associates
201102200075G	Norwood	George F. Willett		Green Repair		DBB	-	-	-	-
200802230010	Orange	Dexter Park		Core Program			-	-	-	-
201302230010	Orange	Dexter Park		Core Program			-	-	-	-
201402240005	Orleans	Orleans Elementary	Design Development	Accelerated Repair	Windows / Doors		Architectural Consulting Group, LLC	Tighe & Bond, Inc.	-	Gale Associates, Inc.
200802260405	Oxford	Oxford Middle School	Closeout	Core Program	Repair	DBB	Diversified Project Management	CGKV Architects, Inc.	J.J. Cardosi, Inc.	Cannon Design
201308600605	Pathfinder Voc Tech	Pathfinder Voc Tech	Building Complete	Accelerated Repair	Roof	DBB	exPERTcon, Inc.	Baker/Wohl Architects, Inc.	Allied Restoration Corporation	Building Enclosure Associates, LLC
200802290305	Peabody	Higgins Middle School	Construction	Core Program	New Construction	DBB	Daedalus Projects Inc	DiNisco Design Partnership, Limited	Bacon-Agostini Construction Joint Venture	BVH Integrated Services, P.C.
201102290007G	Peabody	John E Burke	Final Audit Approved	Green Repair	Roof, Windows / Doors, Boiler	DBB	Daedalus Projects Inc	LPBA/ Architects, Inc.	-	Sebesta Blomberg & Associates, Inc.
201402290016	Peabody	John E. McCarthy	Construction	Accelerated Repair	Roof, Windows / Doors		Hill International Company	Civitects PC	-	Thompson & Lichtner Co., Inc.
201502290510	Peabody	Peabody Veterans Memorial High	Designer Selection	Accelerated Repair	Roof		-	-	-	-
201102290027G	Peabody	William A Welch Sr	Final Audit Approved	Green Repair	Roof	DBB	Daedalus Projects Inc	LPBA/ Architects, Inc.	-	Sebesta Blomberg & Associates, Inc.
201302310010	Pembroke	Hobomock Elementary	Closeout	Accelerated Repair	Roof	DBB	Pinck & Co., Inc.	The S/L/A/M Collaborative	Greenwood Industries, Inc.	CBI Consulting Inc.
201302310015	Pembroke	North Pembroke Elem	Closeout	Accelerated Repair	Roof	DBB	Pinck & Co., Inc.	The S/L/A/M Collaborative	Paul J. Rogan Co., Inc.	CBI Consulting Inc.
201302310305	Pembroke	Pembroke Community Middle School	Closeout	Accelerated Repair	Roof	DBB	Pinck & Co., Inc.	The S/L/A/M Collaborative	Paul J. Rogan Co., Inc.	CBI Consulting Inc.
201302310505	Pembroke	Pembroke High School	Closeout	Accelerated Repair	Roof	DBB	Pinck & Co., Inc.	The S/L/A/M Collaborative	Greenwood Industries, Inc.	CBI Consulting Inc.
201307450405	Pentucket	Pentucket Reg Middle	Final Audit Approved	Accelerated Repair	Roof, Boiler	DBB	Arcadis U.S., Inc.	CGKV Architects, Inc.	Ambient Temperature Corporation	CBI Consulting Inc.   Colliers International
201107500007G	Pioneer Valley	Pearl E Rhodes Elem		Green Repair		DBB	-	-	-	-
201002360510	Pittsfield	Taconic High School	Design Development	Core Program	New Construction	CM@R	Skanska USA Building, Inc	Drumrey Rosane Anderson, Inc.	-	Colliers International
201202390515	Plymouth	Plymouth South High	Construction	Core Program	New Construction	DBB	Ted Gentry Associates, Inc	Ai3 Architects LLC	Bacon-Agostini Construction Joint Venture	Rist-Frost-Shumway Engineering, P.C.
201302420505	Provincetown	Provincetown High	Design Development	Core Program	Repair		Atlantic Construction and Management, Inc.	Raymond Design Associates, Inc.	-	BVH Integrated Services, P.C.

201502430020	Quincy	Beechwood Knoll Elem	Schematic Design	Accelerated Repair	Roof, Windows / Doors		Atlantic Construction and Management, Inc.	-	-	CBI Consulting Inc.
200802430315	Quincy	Central Middle School	Final Audit Approved	Core Program	New Construction - Model School	DBB	Tishman Construction Corporation of MA	Ai3 Architects LLC	H.V. Collins Co., Inc.	Sebesta Blomberg & Associates, Inc.
201402430075	Quincy	Francis W Parker	Building Complete	Accelerated Repair	Windows / Doors		PMA Construction Services	Russo Barr Associates, Inc.	Lockheed Window Corporations	Simpson Gumpertz & Heger Inc.
201402430035	Quincy	Lincoln-Hancock Comm Sch	Building Complete	Accelerated Repair	Windows / Doors		PMA Construction Services	Russo Barr Associates, Inc.	Lockheed Window Corporations	Simpson Gumpertz & Heger Inc.
201302430060	Quincy	Merrymount	Building Complete	Accelerated Repair	Windows / Doors	DBB	Skanska USA Building, Inc	Habeeb & Associates Architects, Inc.	Alpha Contracting Associates, Inc.	Simpson Gumpertz & Heger Inc.
201502430060	Quincy	Merrymount	Schematic Design	Accelerated Repair	Roof		Atlantic Construction and Management, Inc.	-	-	CBI Consulting Inc.
201302430510	Quincy	North Quincy High	Building Complete	Accelerated Repair	Windows / Doors	DBB	Skanska USA Building, Inc	Habeeb & Associates Architects, Inc.	GVW, Inc.	Simpson Gumpertz & Heger Inc.
201302430320	Quincy	Reay E Sterling Middle	Schematic Design	Core Program			Joslin, Lesser + Associates Inc.	Ai3 Architects LLC	-	-
201302430110	Quincy	Wollaston School	Building Complete	Accelerated Repair	Windows / Doors	DBB	Skanska USA Building, Inc	Habeeb & Associates Architects, Inc.	Northeast Energy Control Systems	Simpson Gumpertz & Heger Inc.
201402440018	Randolph	J F Kennedy Elem	Design Development	Accelerated Repair	Windows / Doors		STV Incorporated	Taylor & Burns, Inc.	-	Gale Associates, Inc.
201302440410	Randolph	Randolph Community Middle	Closeout	Accelerated Repair	Boiler	DBB	NETCO Construction Project Managers, Inc.	Taylor & Burns, Inc.	AAlanco Service Corporation	Consulting Engineering Services, LLC
201302440505	Randolph	Randolph High	Closeout	Accelerated Repair	Roof	DBB	NETCO Construction Project Managers, Inc.	Taylor & Burns, Inc.	John F. Shea Company, Inc.	Gale Associates, Inc.
201402440505	Randolph	Randolph High	Design Development	Accelerated Repair	Windows / Doors		STV Incorporated	Taylor & Burns, Inc.	-	Gale Associates, Inc.
201502480056	Revere	Garfield Elementary School	OPM Selection	Accelerated Repair	Roof		-	-	-	-
201002480035	Revere	Staff Sergeant James J. Hill School	Building Complete	Core Program	New Construction	DBB	Hill International Company	Drumrey Rosane Anderson, Inc.	CTA Construction Co., Inc.	Rist-Frost-Shumway Engineering, P.C.
200802510305	Rockland	John W. Rogers Middle School	Final Audit Approved	Core Program	New Construction	CM@R	Daedalus Projects Inc	Dore & Whittier Architects, Inc.	Agostini Construction Co., Inc.	Consulting Engineering Services, LLC
201202530005	Rowe	Rowe Elem		Core Program			-	-	-	-
200902580305G	Salem	Collins Middle School	Building Complete	Green Repair	Roof, Windows / Doors, Boiler, Building Envelope	CM@R	KV Associates, Inc.	Reinhardt Associates, Inc.	Gilbane Building Company	Rist-Frost-Shumway Engineering, P.C.
201002580050G	Salem	Saltonstall School	Closeout	Green Repair	Roof, Windows / Doors, Boiler, Building Envelope	CM@R	KV Associates, Inc.	Reinhardt Associates, Inc.	Gilbane Building Company	Rist-Frost-Shumway Engineering, P.C.
201002620305	Saugus	Belmonte Middle School	Closeout	Core Program	Repair	CM@R	Skanska USA Building, Inc	Fletcher Thompson Architecture Engineering, LLC	Consigli Construction Company, Inc.	Consulting Engineering Services, LLC
201202620505	Saugus	Saugus High		Science Lab Initiative			-	-	-	-
201402620505	Saugus	Saugus High	Designer Selection	Core Program			-	-	-	-
201202640305	Scituate	Gates Intermediate School	Construction	Core Program	New Construction		Daedalus Projects Inc	Dore & Whittier Architects, Inc.	Bacon-Agostini Construction Joint Venture	WSP USA
201208710605	Shawsheen Valley Voc Tech	Shawsheen Valley Voc Tech High School	Closeout	Accelerated Repair	Boiler	DBB	Diversified Project Management	Shekar & Associates, Inc.	NB Kenney Company, Inc	Fitzemeyer & Tocci Associates, Inc.
201102690010G	Sherborn	Pine Hill		Green Repair		DBB	-	-	-	-
201302710005	Shrewsbury	Beal School		Core Program			-	-	-	-
200802710305	Shrewsbury	Sherwood Middle School	Closeout	Core Program	New Construction	CM@R	PMA Construction Services	Lamoureux Pagano & Associates, Inc.	Gilbane Building Company	RDK Engineers
201308290605	So Middlesex Voc Tech Reg	Joseph P Keefe Tech HS	Final Audit Approved	Accelerated Repair	Roof	DBB	PMA Construction Services	Raymond Design Associates, Inc.	Greenwood Industries, Inc.	Russo Barr Associates, Inc.
20081119999	Somerset-Berkley	Somerset-Berkley High	Building Complete	Core Program	New Construction - Model School	DBB	Skanska USA Building, Inc	Ai3 Architects LLC	Bacon-Agostini Construction Joint Venture	Horizon Engineering Associates, LLP

200902740111E	Somerville	East Somerville Community School at Cummings	Closeout	Core Program	Renovation	CM@R	PMA Construction Services	Maguire Group Inc.	Gilbane Building Company	Foreman Building Commissioning, LP
201302740505	Somerville	Somerville High	Feasibility Study	Core Program			PMA Construction Services	Symmes Maini & McKee Associates, Inc.	-	-
200902780015	South Hadley	Plains School	Building Complete	Core Program	New Construction	DBB	Arcadis U.S., Inc.	Jones Whitsett Architects, Inc.	Fontaine Brothers, Inc.	Colliers International
201408730605	South Shore Reg Voc Tech	So Shore Voc Tech High	Construction	Accelerated Repair	Boiler		exPERTcon, Inc.	Richard D. Kimball Company, Inc.	-	Consulting Engineering Services, LLC
201407650505	Southern Berkshire	Mt Everett Regional	Construction	Accelerated Repair	Roof, Boiler		NETCO Construction Project Managers, Inc.	Dietz & Company Architects, Inc.	Titan Roofing, Inc.	Colliers International
200908760605	Southern Worcester Cty VT	Bay Path Regional Vocational Technical High School	Building Complete	Core Program	Addition / Renovation	CM@R	HEERY	Kaestle Boos Associates, Inc.	Consigli Construction Company, Inc.	RDK Engineers
201107660305	Southwick-Tolland	Powder Mill	Building Complete	Core Program	Repair	DBB	Colliers International	JCJ Architecture, PC	PDS Engineering and Construction, Inc.	BVH Integrated Services, P.C.
201107660505	Southwick-Tolland	Southwick-Tolland Regional High	Building Complete	Core Program	Addition / Renovation	DBB	Colliers International	JCJ Architecture, PC	Fontaine Brothers, Inc.	BVH Integrated Services, P.C.
200807660010	Southwick-Tolland	Woodland Elementary School	Building Complete	Core Program	Addition / Renovation	DBB	Colliers International	JCJ Architecture, PC	PDS Engineering and Construction, Inc.	BVH Integrated Services, P.C.
200807670505	Spencer-E Brookfield	David Prouty High School		Core Program			Dore and Whittier Architects, Inc.	Design Partnership of Cambridge, Inc.	-	-
201502810350	Springfield	STEM Middle Academy	Schematic Design	Accelerated Repair	Roof		-	-	-	Building Enclosure Associates, LLC
201302810310	Springfield	Chestnut Accelerated Middle School	Closeout	Accelerated Repair	Roof	DBB	Atlantic Construction and Management, Inc.	CBI Consulting Inc.	J.D. Rivet & Co., Inc.	Building Enclosure Associates, LLC
201502810035	Springfield	Daniel B Brunton	Schematic Design	Accelerated Repair	Windows / Doors		-	-	-	Building Enclosure Associates, LLC
201102810125E	Springfield	Dryden Memorial	Closeout	Core Program	Addition / Renovation	CM@R	Arcadis U.S., Inc.	Drumrey Rosane Anderson, Inc.	Morganti/Aquadro & Cerruti	BVH Integrated Services, P.C.
201102810030E	Springfield	Elias Brookings	Building Complete	Core Program	New Construction	CM@R	Arcadis U.S., Inc.	Drumrey Rosane Anderson, Inc.	Morganti/Aquadro & Cerruti	BVH Integrated Services, P.C.
W20014137	Springfield	Forest Park Middle School	Final Audit Approved	Waitlist	Addition / Renovation	CM@R	Arcadis U.S., Inc.	Perkins Eastman	Consigli Construction Company, Inc.	Foreman Building Commissioning, LP
201302810530	Springfield	High School/Science-Tech	Closeout	Accelerated Repair	Roof	DBB	Atlantic Construction and Management, Inc.	CBI Consulting Inc.	Kronenberger & Sons Restoration, INC.	Building Enclosure Associates, LLC
201402810328	Springfield	John F Kennedy Middle	Construction	Accelerated Repair	Windows / Doors		Arcadis U.S., Inc.	Gale Associates, Inc.	-	Building Enclosure Associates, LLC
201402810110	Springfield	Kensington Avenue	Construction	Accelerated Repair	Windows / Doors		Arcadis U.S., Inc.	Gale Associates, Inc.	Alpha Contracting Associates, Inc.	Building Enclosure Associates, LLC
201302810060	Springfield	Margaret C Ells	Closeout	Accelerated Repair	Roof	DBB	Atlantic Construction and Management, Inc.	CBI Consulting Inc.	Allied Restoration Corporation	Building Enclosure Associates, LLC
201502810155	Springfield	Mary M Walsh	Schematic Design	Accelerated Repair	Windows / Doors		-	-	-	Building Enclosure Associates, LLC
201302810355	Springfield	South End Middle School	Closeout	Accelerated Repair	Roof	DBB	Atlantic Construction and Management, Inc.	CBI Consulting Inc.	Titan Roofing, Inc.	Building Enclosure Associates, LLC
200902810500G	Springfield	Springfield Central High		Green Repair		DBB	-	-	-	-
201202810500	Springfield	Springfield Central High	Closeout	Science Lab Initiative	Addition / Renovation	CM@R	Leftfield, LLC	DiNisco Design Partnership, Limited	Morganti/Aquadro & Cerruti	Horizon Engineering Associates, LLP
200802819999	Springfield	Springfield Public Day High School		Core Program			-	-	-	-
201302810550	Springfield	Springfield Public Day High School	Closeout	Accelerated Repair	Roof	DBB	Atlantic Construction and Management, Inc.	CBI Consulting Inc.	-	Building Enclosure Associates, LLC
201502810550	Springfield	Springfield Public Day High School	Schematic Design	Accelerated Repair	Windows / Doors		-	-	-	Building Enclosure Associates, LLC
200902840405	Stoneham	Stoneham Middle School	Closeout	Core Program	Addition / Renovation	CM@R	Joslin, Lesser + Associates Inc.	Tappe Associates, Inc.	Shawmut Design and Construction	RDK Engineers
201302850010	Stoughton	Helen Hansen Elementary	Closeout	Accelerated Repair	Windows / Doors	DBB	Hill International Company	Russo Barr Associates, Inc.	Lockheed Window Corporations	Building Enclosure Associates, LLC
201402850025	Stoughton	Joseph H Gibbons	Construction	Accelerated Repair	Roof, Windows / Doors		Atlantic Construction and Management, Inc.	CGKV Architects, Inc.	A&A Window Products, Inc.	Building Enclosure Associates, LLC

201302850014	Stoughton	Joseph R Dawe Jr Elem	Closeout	Accelerated Repair	Windows / Doors	DBB	Hill International Company	Russo Barr Associates, Inc.	Lockheed Window Corporations	Building Enclosure Associates, LLC
201302850505	Stoughton	Stoughton High	Feasibility Study	Core Program			Compass Project Management, Inc.	Drumme Rosane Anderson, Inc.	-	-
201302850020	Stoughton	West Elementary	Closeout	Accelerated Repair	Roof	DBB	Compass Project Management, Inc.	Russo Barr Associates, Inc.	Titan Roofing, Inc.	Building Enclosure Associates, LLC
201502850020	Stoughton	West Elementary	Feasibility Study	Accelerated Repair	Windows / Doors		Compass Project Management, Inc.	-	-	-
200802870005	Sturbridge	Burgess Elementary School	Final Audit Approved	Core Program	Addition / Renovation	DBB	Lamoureux Pagano & Associates, Inc.	Drumme Rosane Anderson, Inc.	Fontaine Brothers, Inc.	Horizon Engineering Associates, LLP
201402880025	Sudbury	General John Nixon Elem	Building Complete	Accelerated Repair	Roof, Windows / Doors		Skanska USA Building, Inc	Baker/Wohl Architects, Inc.	Silktown Roofing	Building Enclosure Associates, LLC
200802900305	Sutton	Sutton Middle School	Building Complete	Core Program	Addition / Renovation	DBB	Colliers International	Flansburgh Associates, Inc.	Brait Builders Corp.	RDK Engineers
201102910010	Swampscott	Hadley	Closeout	Core Program	New Construction	DBB	Hill International Company	Mount Vernon Group Architects, Inc.	-	-
201202920505	Swansea	Joseph Case High		Science Lab Initiative			-	-	-	-
201202920305	Swansea	Joseph Case Jr High		Core Program			-	-	-	-
201502930007	Taunton	Edmund Hatch Bennett	OPM Selection	Accelerated Repair	Roof, Windows / Doors		Arcadis U.S., Inc.	CSS Architects Incorporated	-	-
201502930042	Taunton	Joseph H Martin	Schematic Design	Accelerated Repair	Roof, Windows / Doors		Arcadis U.S., Inc.	CSS Architects Incorporated	-	-
201402930015	Taunton	Mulcahey Elementary School	OPM Selection	Core Program			-	-	-	-
200802950505	Tewksbury	Tewksbury Memorial High School	Closeout	Core Program	New Construction - Model School	DBB	HEERY	Symmes Maini & McKee Associates, Inc.	CTA Ventures	Sebesta Blomberg & Associates, Inc.
201408780605	Tri County	Tri County Reg Voc Tech	Construction	Accelerated Repair	Boiler		Colliers International	Shekar & Associates, Inc.	-	Fitzemeyer & Tocci Associates, Inc.
201403010505	Tyngsborough	Tyngsborough High School	Building Complete	Accelerated Repair	Roof, Boiler		Municipal Building Consultants, Inc.	CSS Architects Incorporated	Greenwood Industries, Inc.	Colliers International
200803040505	Uxbridge	Uxbridge High	Final Audit Approved	Core Program	New Construction	CM@R	Joslin, Lesser + Associates Inc.	Raymond Design Associates, Inc.	Shawmut Design and Construction	Turner Facilities Management Solutions
200907750305	Wachusett	Mountview Middle School	Construction	Core Program	New Construction	DBB	Gary Kaczmarek Town Employee	Lamoureux Pagano & Associates, Inc.	CTA Construction Co., Inc.	Fitzemeyer & Tocci Associates, Inc.
201003050310	Wakefield	Galvin Middle School	Closeout	Core Program	New Construction	CM@R	Joslin, Lesser + Associates Inc.	Tappe Associates, Inc.	Bond Brothers, Inc.	B2Q Associates, Inc.
201303070015	Walpole	Fisher	Final Audit Approved	Accelerated Repair	Roof	DBB	NETCO Construction Project Managers, Inc.	ICON architecture, inc.	Rockwell Roofing, Inc.	Gale Associates, Inc.
201103080505G	Waltham	Waltham High School		Green Repair		DBB	-	-	-	-
201403080505	Waltham	Waltham High School	OPM Selection	Core Program			-	-	-	-
201503100003	Wareham	John W. Decas Elementary School	Schematic Design	Accelerated Repair	Roof, Boiler		-	-	-	-
201103100017	Wareham	Minot Forest		Core Program			-	-	-	-
201303100505	Wareham	Wareham Senior High	Closeout	Accelerated Repair	Roof	DBB	Hill International Company	Tighe & Bond, Inc.	Capeway Roofing Systems, Inc.	Russo Barr Associates, Inc.
201503140305	Watertown	Watertown Middle	Feasibility Study	Accelerated Repair	Windows / Doors		-	-	-	-
201403150005	Wayland	Claypit Hill School	Design Development	Accelerated Repair	Windows / Doors		Pinck & Co., Inc.	CGKV Architects, Inc.	-	Russo Barr Associates, Inc.
200903160015	Webster	Park Avenue Elementary School	Building Complete	Core Program	New Construction	DBB	Hill International Company	Dore & Whittier Architects, Inc.	CTA Construction Co., Inc.	Cannon Design
201403170305	Wellesley	Wellesley Middle	Construction	Accelerated Repair	Windows / Doors		Arcadis U.S., Inc.	CSS Architects Incorporated	Paul J. Rogan Co., Inc.	Gale Associates, Inc.
200803170505	Wellesley	Wellesley Senior School	Closeout	Core Program	New Construction	CM@R	-	Symmes Maini & McKee Associates, Inc.	-	Rist-Frost-Shumway Engineering, P.C.
201303180005	Wellfleet	Wellfleet Elementary	Closeout	Accelerated Repair	Roof	DBB	Architectural Consulting Group, LLC	CSS Architects Incorporated	DDC Construction Inc.	Russo Barr Associates, Inc.
201103220005G	West Boylston	Major Edwards Elementary	Closeout	Green Repair	Windows / Doors	DBB	URS Corporation	Reinhardt Associates, Inc.	-	Cannon Design
201103220505G	West Boylston	West Boylston Jr-Sr High		Green Repair		DBB	-	-	-	-

201503230005	West Bridgewater	Spring Street School	Schematic Design	Accelerated Repair	Roof		Potomac Capital Advisors	Tai Soo Kim Partners, LLC	-	Thompson & Lichtner Co., Inc.
201003230505	West Bridgewater	West Bridgewater Middle-Senior High School	Building Complete	Core Program	New Construction	DBB	Colliers International	Flansburgh Associates, Inc.	CTA Construction Co., Inc.	Cannon Design
200903320505	West Springfield	West Springfield High School	Building Complete	Core Program	New Construction - Model School	DBB	Colliers International	Symmes Maini & McKee Associates, Inc.	Fontaine Brothers, Inc.	Turner Facilities Management Solutions
200903210305	Westborough	Gibbons Middle School	Design Development	Core Program	Repair		HEERY	Habeeb & Associates Architects, Inc.	-	BVH Integrated Services, P.C.
200903250020	Westfield	Abner Gibbs Elementary School	Construction	Core Program	New Construction - Model School	DBB	Skanska USA Building, Inc	Jones Whitsett Architects, Inc.	Fontaine Brothers, Inc.	Horizon Engineering Associates, LLP
201303260025	Westford	Col John Robinson	Building Complete	Accelerated Repair	Windows / Doors	DBB	Colliers International	Gale Associates, Inc.	GTC Construction Management	CBI Consulting Inc.
201303260007	Westford	Day Elementary	Building Complete	Accelerated Repair	Windows / Doors	DBB	Colliers International	Gale Associates, Inc.	J.J. Cardosi, Inc.	CBI Consulting Inc.
201303270005	Westhampton	Westhampton Elem School	Final Audit Approved	Accelerated Repair	Roof, Windows / Doors, Boiler	DBB	Atlantic Construction and Management, Inc.	CSS Architects Incorporated	Independent Roofing Co. Inc.	Building Enclosure Associates, LLC
200903300012	Weston	Field Elementary School	Closeout	Core Program	New Construction	DBB	Compass Project Management, Inc.	Jonathan Levi Architects LLC	Colantonio, Inc.	Foreman Building Commissioning, LP
201103310305G	Westport	Westport Middle		Green Repair		DBB	-	-	-	-
201403310305	Westport	Westport Middle	OPM Selection	Core Program			-	-	-	-
201103360080G	Weymouth	William Seach		Green Repair		DBB	KBA Architects	-	-	-
200803400005	Williamsburg	Anne T. Dunphy School	Closeout	Core Program	Addition / Renovation	DBB	Arcadis U.S., Inc.	Drumme Rosane Anderson, Inc.	Enfield Builders, Inc.	B2Q Associates, Inc.
201203420060	Wilmington	North Intermediate	Closeout	Accelerated Repair	Windows / Doors	DBB	Diversified Project Management	-	-	CBI Consulting Inc.
200903420505	Wilmington	Wilmington High School	Building Complete	Core Program	New Construction	CM@R	Joslin, Lesser + Associates Inc.	Dore & Whittier Architects, Inc.	Gilbane Building Company	Symmes, Maini & McKee Associates
200803449999	Winchester	Parkhurst Elementary School		Core Program			-	-	-	-
201003440505	Winchester	Winchester High School	Construction	Core Program	Addition / Renovation	CM@R	Skanska USA Building, Inc	Symmes Maini & McKee Associates, Inc.	Consigli Construction Company, Inc.	RDK Engineers
200803460505	Winthrop	Winthrop High School	Construction	Core Program	New Construction	CM@R	Skanska USA Building, Inc	HMFH Architects, Inc.	Gilbane Building Company	WSP USA
201203470060	Woburn	Wyman	Design Development	Core Program	New Construction		Municipal Building Consultants, Inc.	DiNisco Design Partnership, Limited	-	Fitzmeyer & Tocci Associates, Inc.
201203480052	Worcester	Chandler Magnet	Final Audit Approved	Accelerated Repair	Windows / Doors	DBB	Tishman Construction Corporation of MA	Turowski2 Architecture, Inc.	J.J. Cardosi, Inc.	Russo Barr Associates, Inc.
201403480055	Worcester	Clark St Community	Construction	Accelerated Repair	Windows / Doors		Architectural Consulting Group, LLC	ICON architecture, inc.	J.J. Cardosi, Inc.	Russo Barr Associates, Inc.
201303480060	Worcester	Columbus Park	Building Complete	Accelerated Repair	Windows / Doors, Boiler	DBB	Architectural Consulting Group, LLC	The S/L/A/M Collaborative	Contractor's Network, Inc.	RDK Engineers   Russo Barr Associates, Inc.
201203488099	Worcester	Dr. James Caradonio Center	Final Audit Approved	Accelerated Repair	Boiler	DBB	Tishman Construction Corporation of MA	Turowski2 Architecture, Inc.	CAM HVAC & Construction, Inc.	RDK Engineers   Russo Barr Associates, Inc.
201503480090	Worcester	Flagg Street	Schematic Design	Accelerated Repair	Windows / Doors		Arcadis U.S., Inc.	CSS Architects Incorporated	-	Russo Barr Associates, Inc.
201503480177	Worcester	Francis J McGrath Elem	Schematic Design	Accelerated Repair	Windows / Doors		Arcadis U.S., Inc.	CSS Architects Incorporated	-	Russo Barr Associates, Inc.
201403480100	Worcester	Goddard Sch/Science Tech	Construction	Accelerated Repair	Windows / Doors		Architectural Consulting Group, LLC	ICON architecture, inc.	Lambrian Construction Corp.	Russo Barr Associates, Inc.
201503480115	Worcester	Grafton Street	Schematic Design	Accelerated Repair	Windows / Doors, Boiler		Arcadis U.S., Inc.	CSS Architects Incorporated	-	Russo Barr Associates, Inc.
201203480140	Worcester	Jacob Hiatt Magnet	Final Audit Approved	Accelerated Repair	Boiler	DBB	Tishman Construction Corporation of MA	Turowski2 Architecture, Inc.	CAM HVAC & Construction, Inc.	RDK Engineers
201503480140	Worcester	Jacob Hiatt Magnet	Schematic Design	Accelerated Repair	Windows / Doors		Arcadis U.S., Inc.	CSS Architects Incorporated	-	Russo Barr Associates, Inc.
201203480145	Worcester	Lake View	Final Audit Approved	Accelerated Repair	Windows / Doors	DBB	Tishman Construction Corporation of MA	Turowski2 Architecture, Inc.	J.J. Cardosi, Inc.	Russo Barr Associates, Inc.
201203480175	Worcester	May Street	Final Audit Approved	Accelerated Repair	Windows / Doors	DBB	Tishman Construction Corporation of MA	Turowski2 Architecture, Inc.	J.J. Cardosi, Inc.	Russo Barr Associates, Inc.



201203480200	Worcester	Nelson Place	Construction	Core Program	New Construction	CM@R	Tishman Construction Corporation of MA	Lamoureux Pagano & Associates, Inc.	Fontaine Brothers, Inc.	Bard, Rao + Athanas Consulting Engineers, LLC
201403480520	Worcester	South High Community	OPM Selection	Core Program			-	-	-	-
201303480230	Worcester	Tatnuck	Building Complete	Accelerated Repair	Windows / Doors	DBB	Architectural Consulting Group, LLC	The S/L/A/M Collaborative	GVW, Inc.	Russo Barr Associates, Inc.
201403480240	Worcester	Union Hill School	Construction	Accelerated Repair	Windows / Doors		Architectural Consulting Group, LLC	ICON architecture, inc.	J.J. Cardosi, Inc.	Russo Barr Associates, Inc.
201403480260	Worcester	West Tatnuck	Construction	Accelerated Repair	Windows / Doors		Architectural Consulting Group, LLC	ICON architecture, inc.	J.J. Cardosi, Inc.	Russo Barr Associates, Inc.
201303480225	Worcester	Worcester Arts Magnet Sch	Building Complete	Accelerated Repair	Windows / Doors	DBB	Architectural Consulting Group, LLC	The S/L/A/M Collaborative	GVW, Inc.	Russo Barr Associates, Inc.
201303480420	Worcester	Worcester East Middle	Building Complete	Accelerated Repair	Boiler	DBB	Architectural Consulting Group, LLC	The S/L/A/M Collaborative	Contractor's Network, Inc.	RDK Engineers
201503500003	Wrentham	Delaney	OPM Selection	Accelerated Repair	Roof		P3 Inc.	Turowski2 Architecture, Inc.	-	-

**APPENDIX B**  
**2016 ESTIMATED BID DATES**

## 2016 ESTIMATED BID DATES

Note bid dates are Estimates ONLY. Please contact Districts for exact information.


Total Project Budget denotes total District costs and does not denote the basis of the MSBA Total Facilities Grant.

District	Enrollment	Project Budget	Start	Finish	Construct Budget	Notes																				
							Nov '15	Dec '15	Jan '16	Feb '16	Mar '16	Apr '16	May '16	Jun '16	Jul '16	Aug '16	Sep '16	Oct '16	Nov '16	Dec '16	Jan '17	Feb '17				
Worcester	600	\$ 58.2	Wed 12/16/15	Tue 4/5/16	\$ 46.5	GMP targeted: April				Worcester - Nelson Place School																
Westborough	550	\$ 26.8	Wed 1/13/16	Thu 2/18/16	\$ 21.6	GMP targeted: February			Westborough - Sarah W. Gibbons MS																	
Woburn	410	\$ 31.8	Wed 5/4/16	Thu 6/30/16	\$ 26.2	NTP targeted: July								Woburn - Wyman Elementary School												
Brookline	830	\$ 113.4	Fri 5/13/16	Thu 6/23/16	\$ 92.2	GMP targeted: August									Brookline - Edward Devotion School											
New Bedford	400	\$ 35.6	Fri 5/20/16	Mon 6/27/16	\$ 35.1	NTP targeted: July									New Bedford - John Hannigan Elementary School											
Pittsfield	920	\$ 116.1	Thu 6/16/16	Fri 7/29/16	\$ 97.7	GMP targeted: August										Pittsfield - Taconic High School										
Carver	750	\$ 51.9	Mon 8/22/16	Fri 9/30/16	\$ 39.4	NTP targeted: October																				
Narragansett RSD	580	\$ 47.6	Fri 9/30/16	Tue 11/22/16	\$ 36.5	NTP targeted: December																				
Hopkinton	395	\$ 43.8	Tue 11/1/16	Tue 12/13/16	\$ 35.1	GMP targeted: December 2016																				
Beverly	1395	\$ 106.8	Wed 11/2/16	Thu 2/2/17	\$ 90.1	GMP targeted: February 2017																				
Provincetown	n/a	\$ 7.3	Tue 12/13/16	Thu 2/2/17	\$ 5.7	NTP targeted: February 2016																				
<b>Total</b>	<b>5500</b>	<b>\$ 639.3</b>			<b>\$ 526.1</b>																					

Note: Budget values are in millions.

The project start date represents the Filed-Sub bid solicitation date, gray diamond Filed-Sub bid date, and the black diamond GC Bids / GMP Execution.

01/08/2016





APPENDIX C  
CONSTRUCTION STATUS REPORT

**Projects in Construction  
MSBA Grant Basis and Maximum Grant Amount  
Data Reported as of January 8, 2016**

Core Program and Waitlist Totals			\$2,877,041,023															*Includes Alternates	\$1,794,143,069
Project	Grade	Contractor	Total Construction Cost*	Projected Enrollment	PFA or Bid Data	Proposed Sq.Ft.	Construction Cost/Sq.Ft.	Building Cost	Building Cost/Sq.Ft.	Procurement Type	Construction Start Date	Substantial Completion	Schedule Variance (days)	Physical Progress	Change Orders	Change Orders %	Construction Status	Est Max Total Facilities Grant	
<b>CAPITAL PIPELINE PROJECTS IN CONSTRUCTION</b>																			
<b>Core Program Totals</b>			<b>\$2,866,396,448</b>															<b>\$1,778,548,318</b>	
Abington Frolio Jr Hs	Junior High School	Brait Builders Corp.	\$78,465,366	1,115	PFA	235,370	\$333	\$56,420,036	\$240	Design/Bid/Build	03-Dec-15	18-Jul-17	0	4%	\$0	0.000%	The contractor has mobilized to the site and site preparation has commenced.	\$48,528,486	
Assabet Valley Assabet Valley Voc H S	Vocational / Technical	CTA Construction Co., Inc.	\$46,764,740	1,000	Bid	367,565	\$127	\$41,523,764	\$113	Design/Bid/Build	01-Apr-13	23-Aug-15	0	100%	\$3,397,467	7.265%	The 10-phase project is mostly complete. Work remaining includes minor punch list items, final commissioning and close out.	\$28,790,301	
Athol-Royalston Riverbend	Elementary School	Fontaine Brothers, Inc.	\$31,594,000	545	Bid	95,726	\$330	\$24,859,000	\$260	Design/Bid/Build	08-Dec-14	14-Jun-16	0	63%	\$184,501	0.584%	Work to export excess site materials is complete. Steel erection is nearing completion. Masonry work ongoing and temporary power installed.	\$26,011,620	
Berlin-Boylston Tahanto Reg High	Junior High School	CTA Construction Co., Inc.	\$32,162,000	560	Bid	126,100	\$255	\$24,629,999	\$195	Design/Bid/Build	10-May-11	01-Jul-13	0	100%	\$1,026,723	3.282%	The new school building is in service. The District is working to resolve issues associated with final change orders and rain screen repairs.	\$18,733,021	
Chicopee Chicopee Academy	Middle School	Fontaine Brothers, Inc.	\$31,487,000	825	Bid	176,425	\$178	\$25,639,000	\$145	Design/Bid/Build	01-Jul-14	11-Aug-15	0	99%	\$2,041,535	6.484%	Punch list work is ongoing.	\$28,813,458	
Dracut Dracut Senior High	High School	CTA Construction Co., Inc.	\$45,900,000	1,160	Bid	226,844	\$202	\$38,377,028	\$169	Design/Bid/Build	27-Aug-12	29-Aug-14	0	99%	\$2,235,746	4.871%	The project team is working to resolve a site drainage issue and additional work associated with rooftop downpipe. Punch list work is ongoing.	\$34,137,202	
East Bridgewater East Bridgewater High	High School	Fontaine Brothers, Inc.	\$65,409,000	950	Bid	213,544	\$306	\$47,684,117	\$223	Design/Bid/Build	10-Aug-11	25-Jun-13	0	99%	\$2,398,294	3.928%	One remaining item to be addressed to complete Commissioning.	\$40,164,584	
Franklin Franklin High	High School	Bacon-Agostini Construction Joint Venture	\$86,778,700	1,650	Bid	306,543	\$283	\$73,191,801	\$239	Design/Bid/Build	16-Oct-12	25-Jul-14	0	99%	\$1,108,661	1.278%	The new building and parking areas are complete. Site related punch list work continues.	\$54,558,408	
Georgetown Georgetown Middle/High	Junior High School	L.D. Russo, Inc.	\$5,279,622	720	Bid	128,670	\$41	\$4,265,936	\$33	Design/Bid/Build	15-Apr-15	21-Dec-15	0	95%	\$545,998	10.342%	Minor punch list work remains to be completed.	\$3,377,260	
Georgetown Penn Brook	Elementary School	Brait Builders Corp.	\$32,875,975	770	Bid	98,000	\$335	\$26,976,145	\$275	Design/Bid/Build	26-Sep-13	20-May-15	0	99%	\$3,840,126	11.681%	Site work continues weather permitting. Commissioning and punch list work are ongoing.	\$18,864,538	
Greater Lawrence RVT Gr Lawrence Reg Voc Tech	Vocational / Technical	E. Amanti & Sons, Inc.	\$3,484,000	1,400	Bid	360,000	\$10	\$2,889,100	\$8	Design/Bid/Build	04-Jun-14	12-Dec-14	0	100%	\$260,493	7.477%	This project includes the replacement of cooling towers, chiller plant, HVAC pumps, HVAC controls, domestic hot water heaters, roof top mechanical units, and ventilation throughout the shop areas. The only items that remain are minor punch list items, final commissioning and close out.	\$2,627,875	
Greater New Bedford Gr New Bedford Voc Tech	Vocational / Technical	Agostini Construction Co., Inc.	\$12,181,500	2,060	Bid	487,530	\$25	\$10,757,696	\$22	Design/Bid/Build	13-Sep-13	19-Dec-14	0	100%	\$1,273,194	10.452%	The building is complete and in service. Replacement of the cooling tower has been completed and is operational. Miscellaneous punch list work is remaining.	\$11,573,133	
Hingham Hingham Middle School	Middle School	Brait Builders Corp.	\$48,436,000	1,020	Bid	176,385	\$275	\$41,227,552	\$234	Design/Bid/Build	07-Jun-12	01-May-14	0	99%	\$714,526	1.492%	Landscaping and field installation is complete. Grass stabilization scheduled for Spring of 2016.	\$23,653,420	
Marshfield Marshfield High	High School	Brait Builders Ventures	\$84,980,000	1,310	Bid	267,469	\$318	\$64,604,850	\$242	Design/Bid/Build	16-Aug-12	01-Jun-14	0	99%	\$2,200,718	2.765%	Remaining work consists of punch list items. Phase III site restoration will be completed in the Spring of 2016.	\$46,550,599	
Monomoy Monomoy Regional High School	High School	Fontaine Brothers, Inc.	\$49,374,000	700	Bid	168,000	\$294	\$41,433,695	\$247	Design/Bid/Build	11-Feb-13	02-Sep-14	0	100%	\$1,088,517	2.267%	Remaining change order work and punch list items are being addressed.	\$27,654,507	
North Adams Silvio O Conte Middle	Middle School	PDS Engineering and Construction, Inc.	\$21,877,496	310	Bid	78,119	\$280	\$17,831,491	\$228	Design/Bid/Build	28-Apr-14	03-Dec-15	0	99%	\$1,837,212	8.398%	Site work is complete including paving, landscaping, and playground equipment. Interior work is complete except finishes and punch list items. Furniture has been moved into classrooms and offices. Teachers have begun setting up their classrooms. Opening of school to students scheduled for early January 2016.	\$20,508,670	
North Middlesex North Middlesex Reg	High School	CTA Construction Co., Inc.	\$68,829,726	870	PFA	180,530	\$381	\$44,223,062	\$245	Design/Bid/Build	25-May-15	14-Jul-17	0	13%	\$0	0.000%	Excavation of site and installation of utilities and structural steel placement continue.	39373276	
Northborough Lincoln Street	Elementary School	Brait Builders Corp.	\$18,450,000	270	PFA	52,920	\$349	\$14,514,966	\$274	Design/Bid/Build	27-Apr-15	01-Sep-16	0	58%	\$17,754	0.096%	Interior finishes are nearing completion in the Phase I spaces.	\$9,925,570	
Peabody J Henry Higgins Middle	Middle School	Bacon-Agostini Construction Joint Venture	\$70,679,700	1,340	Bid	227,314	\$311	\$52,186,177	\$230	Design/Bid/Build	10-Mar-14	01-Jul-16	0	62%	(\$391,815)	-0.554%	Academic west is near completion. Gym and cafeteria's rough-in finishes are in progress. Exterior panels are mostly installed. Sunshades are waiting to be installed. Glazing is near completion. MEP's in the overhead of the Auditorium is in progress. The District has started furniture purchase arrangements.	\$38,652,137	
Plymouth Plymouth South High	High School	Bacon-Agostini Construction Joint Venture	\$88,163,542	1,005	PFA	248,081	\$355	\$60,612,309	\$244	Design/Bid/Build	06-Jul-15	05-May-17	0	11%	\$0	0.000%	Bulk excavation has been completed in all 7 areas. Foundations excavated in Areas 1 through 5, backfilled in Areas 1 through 3 and underground plumbing complete in Area 1. Structural steel erected in Areas 1 & 2.	\$46,241,232	
Revere Staff Sergeant James J. Hill School	Elementary School	CTA Construction Co., Inc.	\$31,975,839	690	Bid	103,650	\$308	\$27,439,789	\$265	Design/Bid/Build	25-Mar-14	17-Aug-15	0	92%	\$1,110,455	3.473%	The contractor is in the process of completing work to close out the project including punch list items.	\$28,099,048	
Scituate Gates Intermediate School	Middle School	Agostini Bacon Construction	\$61,980,444	710	PFA	164,803	\$376	\$43,653,890	\$265	Design/Bid/Build	08-Dec-15	26-Jul-17	0	0%	\$0	0.000%	The contractor has mobilized to site and early site construction is in process.	\$20,603,507	
Somerset-Berkley Somerset-Berkley High	High School	Bacon-Agostini Construction Joint Venture	\$69,407,000	1,000	Bid	222,826	\$311	\$52,553,676	\$236	Design/Bid/Build	16-Jul-12	20-Jun-14	0	100%	\$844,154	1.282%	Remaining work consists of punch list items. Phase III site restoration will be completed in the Spring of 2016.	\$46,722,150	
South Hadley Plains Elementary	Elementary School	Fontaine Brothers, Inc.	\$21,391,144	270	Bid	63,377	\$338	\$17,380,907	\$274	Design/Bid/Build	08-May-14	04-Sep-15	0	95%	\$1,620,017	7.573%	Civil and site work continue (exterior play equipment, landscape plantings, etc.) as well as installation of solar shade brackets, safety signage, hazardous material abatement and selective demolition efforts.	\$13,676,432	
Southwick-Tolland Powder Mill	Middle School	PDS Engineering and Construction, Inc.	\$13,556,194	545	Bid	95,775	\$142	\$11,289,029	\$118	Design/Bid/Build	07-Jun-13	24-Aug-15	0	99%	\$955,184	7.046%	All five phases are complete. Punch list work is ongoing.	\$8,437,002	
Southwick-Tolland Southwick-Tolland Regional High	High School	Fontaine Brothers, Inc.	\$25,307,990	790	Bid	165,995	\$152	\$19,838,420	\$120	Design/Bid/Build	05-Aug-13	03-Sep-15	0	99%	\$2,075,841	8.375%	All five phases are complete. Punch list work is ongoing.	\$19,572,669	
Southwick-Tolland Woodland Elementary	Elementary School	PDS Engineering and Construction, Inc.	\$7,172,052	400	Bid	67,800	\$106	\$6,077,790	\$90	Design/Bid/Build	07-Jun-13	24-Aug-15	0	99%	\$755,026	10.527%	All four phases are complete. Punch list work is ongoing.	\$4,620,410	
Sutton Sutton Middle School	Junior High School	Brait Builders Corp.	\$41,230,800	840	PFA	179,040	\$230	\$32,998,403	\$184	Design/Bid/Build	01-Jul-11	05-Mar-15	0	99%	\$1,754,737	4.368%	Remaining punch list and commissioning items are being addressed.	\$26,120,512	
Wachusett Mountview Middle	Middle School	CTA Construction Co., Inc.	\$43,122,257	800	Bid	126,200	\$342	\$28,959,805	\$229	Design/Bid/Build	21-May-14	19-Apr-16	0	79%	\$429,165	0.995%	Site work has continued with grading and spreading loam, fence and guardrail installation, and installation of an infiltration basin. Finish installations continued in the academic building with casework, painting, tile, and electrical finish work. Drywall installation progressed in the gym/cafeeteria lobby area.	\$24,279,591	
Webster Park Avenue Elementary	Elementary School	CTA Construction Co., Inc.	\$32,370,001	720	Bid	109,597	\$295	\$24,190,915	\$221	Design/Bid/Build	08-Jul-13	06-Feb-15	0	99%	\$947,366	2.993%	Remaining work to be completed includes miscellaneous punch list items.	\$28,102,666	
West Bridgewater West Bridgewater Jr-Sr	Junior High School	CTA Construction Co., Inc.	\$46,267,000	625	Bid	141,250	\$328	\$34,404,274	\$244	Design/Bid/Build	01-Oct-13	09-Jul-15	0	88%	\$307,797	0.678%	Work continues on the punch list as well as completion of sound, security and fire alarm systems. Demolition and abatement of the existing school is complete.	\$26,385,058	
West Springfield West Springfield High	High School	Fontaine Brothers, Inc.	\$85,006,020	1,270	Bid	257,525	\$330	\$56,875,181	\$221	Design/Bid/Build	22-Nov-11	31-Dec-13	0	100%	\$3,055,746	4.337%	Change order work remains to be completed as well as resolution of warranty items.	\$60,722,795	
Westfield Abner Gibbs	Elementary School	Fontaine Brothers, Inc.	\$25,578,000	600	Bid	95,573	\$268	\$21,444,000	\$224	Design/Bid/Build	24-Aug-12	01-Jun-16	0	7%	\$0	0.000%	Work stoppage due to preliminary injunction based upon project site status as Article 97 "Protected Land". Preliminary Injunction vacated but city awaiting National Park Service approval for use of site. The General Contractor has demobilized from the site. The project team is working on closing out the General Contractor's contract.	\$21,281,639	
Auburn Auburn Middle	Middle School	Fontaine Brothers, Inc.	\$36,412,806	560	Bid	100,395	\$363	\$23,350,958	\$233	CM-at-Risk	27-Feb-14	07-Jul-15	0	99%	(\$194,889)	-0.549%	The project is complete except for minor punch list work and seasonal commissioning to be completed in the Spring of 2016.	\$19,761,870	

**Projects in Construction  
MSBA Grant Basis and Maximum Grant Amount  
Data Reported as of January 8, 2016**

Core Program and Waitlist Totals			\$2,877,041,023															*Includes Alternates	\$1,794,143,069
Project	Grade	Contractor	Total Construction Cost*	Projected Enrollment	PFA or Bid Data	Proposed Sq.Ft.	Construction Cost/Sq.Ft.	Building Cost	Building Cost/Sq.Ft.	Procurement Type	Construction Start Date	Substantial Completion	Schedule Variance (days)	Physical Progress	Change Orders	Change Orders %	Construction Status	Est Max Total Facilities Grant	
<b>CAPITAL PIPELINE PROJECTS IN CONSTRUCTION</b>																			
<b>Core Program Totals</b>			<b>\$2,866,396,448</b>																<b>\$1,778,548,318</b>
Ayer-Shirley Ayer-Shirley Regional Middle/High School	High School	Consigli Construction Company, Inc.	\$44,516,576	495	Bid	144,072	\$309	\$32,082,505	\$223	CM-at-Risk	19-Feb-13	31-Aug-15	0	99%	\$1,204,931	2.715%	This is a 6-phase Addition/Renovation project which is mostly complete. Items remaining include minor punch list items, final commissioning and close out.	\$34,704,031	
Boston Dearborn	Middle School	Gilbane Building Company	\$60,245,740	600	PFA	128,304	\$470	\$36,655,002	\$286	CM-at-Risk	08-Sep-15	28-Jun-17	0	2%	\$0	0.000%	Asbestos removal is well underway with about 30 workers on site daily. The first three floors have been abated and the contractor is working on the window caulking. In addition, wood and metal are being removed from the interior of the school in preparation for bulk demolition. Cutting and capping of utilities in underway.	\$36,615,390	
Chelsea Clark Avenue School	Middle School	W. T. Rich Company Inc.	\$46,046,367	670	PFA	115,235	\$400	\$29,311,076	\$254	CM-at-Risk	23-Feb-15	29-Jun-18	0	11%	\$0	0.000%	The contractor is erecting steel for Phase 1.	\$36,093,628	
Concord-Carlisle Concord Carlisle High	High School	Turner Construction Company	\$76,143,704	1,225	Bid	219,871	\$346	\$53,607,000	\$244	CM-at-Risk	20-Feb-13	13-Feb-15	0	99%	\$3,060,467	4.019%	The original building was abated and demolished by December 15, 2015. In the Spring of 2016, the outdoor classroom amphitheater will be completed as well as installation of plantings that could not be installed in 2015. Commissioning work continues.	\$26,795,748	
Duxbury Duxbury High	Junior High School	Dimeo Construction Company	\$105,475,520	1,735	Bid	322,105	\$327	\$73,368,123	\$228	CM-at-Risk	12-Sep-12	09-Jun-14	0	99%	\$6,123,067	6.149%	Site and landscaping work continues on both former school sites.	\$48,141,830	
Essex Agr Tech Essex Agr and Tech Inst	Vocational / Technical	Gilbane Building Company	\$110,217,451	1,440	Bid	337,000	\$327	\$79,334,889	\$235	CM-at-Risk	07-May-12	27-Aug-14	0	99%	\$2,885,921	2.618%	Punch list work is ongoing and is forecast to be completed in the very near future.	\$72,471,233	
Gloucester West Parish	Elementary School	W. T. Rich Company Inc.	\$29,995,466	355	Bid	65,679	\$457	\$18,591,872	\$283	CM-at-Risk	07-Jul-14	12-May-16	0	76%	\$115,992	0.387%	Academic Wing: Classroom/hallway wall painting, ceiling grid, and tile installations are ongoing. Gym/Cafe/Arts Wing: Interior framing and exterior envelope is progressing along with mechanical/electrical/plumbing work. Site: Play field drainage and curbs commenced installation. Binder course pavement has been installed around the site.	\$14,673,132	
Greater Lowell Voc Tec Gr Lowell Reg Voc Tech	Vocational / Technical	Consigli Construction Company, Inc.	\$52,472,010	1,990	Bid	505,766	\$104	\$38,997,643	\$77	CM-at-Risk	04-Nov-13	31-Aug-15	0	99%	\$2,830,688	5.395%	All work that was included in the original 3-phase project scope is complete other than punch list items, commissioning and close out. The District has elected to use some of the savings to renovate the original school kitchen which was not part of the original scope. This space will be repurposed to expand the culinary arts program. Work is scheduled to be completed in early Spring of 2016.	\$45,839,013	
Greenfield Greenfield High	High School	Shawmut Design and Construction	\$53,507,787	585	Bid	160,650	\$333	\$37,812,150	\$235	CM-at-Risk	27-Mar-13	31-Oct-15	0	100%	\$1,103,326	2.062%	The new school building and renovated Auditorium are in service. Final site work is scheduled for final acceptance inspection in the Spring of 2016.	\$42,146,257	
Haverhill Caleb Dustin Hunking	Middle School	Shawmut Design and Construction	\$49,544,769	1,005	PFA	147,996	\$335	\$35,181,852	\$238	CM-at-Risk	20-Apr-15	30-Dec-16	0	30%	\$4,596	0.009%	The new school building is forecast to be weather tight in mid-January. Exterior masonry work is nearly complete. roofing is complete for the A Building and nearly complete for C Building. Slab-on-grade placement is complete. Window installations are ongoing. Maintenance building design has been revised as well as the location.	\$39,639,497	
Holbrook Holbrook Jr Sr High	High School	Consigli Construction Company, Inc.	\$79,835,240	1,095	PFA	217,353	\$367	\$50,611,105	\$233	CM-at-Risk	24-Jun-15	05-Jun-17	0	7%	\$101,941	0.128%	Foundations are nearly complete and prep work has started for slabs-on-grade. CMU wall construction is ongoing for Building B. Site drainage is being installed.	\$54,644,960	
Lunenburg Lunenburg High	Junior High School	Shawmut Design and Construction	\$57,994,017	820	Bid	169,018	\$343	\$41,982,415	\$248	CM-at-Risk	15-Aug-14	30-Jun-16	0	70%	\$171,133	0.295%	Exterior masonry veneer installation is complete. Floor and metal panel installations are underway. Painting, wall tile and MEP installations are ongoing. Interior masonry installation is nearing completion.	\$34,122,826	
Lynn Thurgood Marshall Mid	Middle School	Walsh Brothers, Inc.	\$71,225,244	1,100	Bid	181,847	\$392	\$56,105,148	\$309	CM-at-Risk	27-Jun-14	06-Jun-16	47 ahead	79%	\$0	0.000%	Site work includes front entrance/side walk preparation and courtyard work. All roof work is complete. Punch list work remains ongoing. Flooring finish, painting, and cleaning are underway in Building A (95% complete), with VCT, tile work, and finish work underway in Building B (85% complete), and gym work, stage work, and finishes underway in Building C (80% complete).	\$49,541,568	
Milford Woodland	Elementary School	Shawmut Design and Construction	\$48,375,101	985	Bid	132,539	\$365	\$34,861,130	\$263	CM-at-Risk	01-Apr-15	28-Jul-16	0	50%	\$484,825	1.002%	In the gym and academic wings, exterior brick and interior CMU are complete and interior framing and drywall are ongoing. In the Admin/Cafe/Arts Wing, installation of the main roof and concrete slabs are complete. Exterior sheathing and exterior/interior framing are ongoing. Underground installation of utilities has been completed in all buildings and rough-in work is ongoing. Installation of new gas and electrical services have been completed. Asphalt base pavement and curbs at parking lots are complete.	\$27,418,234	
Newton A E Angier	Elementary School	W. T. Rich Company Inc.	\$30,158,875	465	Bid	74,960	\$402	\$19,837,027	\$265	CM-at-Risk	22-Aug-14	5-Jan-16	0	90%	\$299,664	1.143%	Furniture deliveries and millwork are in progress. Gym and cafeteria are to be finished last. The media center is almost complete but needs to be cleared for the furniture. Glazing is in progress. Landscaping is ongoing including pouring concrete for sidewalks.	\$10,687,077	
North Reading North Reading High	Junior High School	Gilbane Building Company	\$101,328,353	1,370	Bid	267,939	\$378	\$66,726,592	\$249	CM-at-Risk	01-May-12	21-Aug-15	0	98%	\$3,528,190	3.482%	Demolition of the existing high school is complete. Punch list items remain. Field restoration to be completed in the Spring 2016.	\$47,071,882	
Norton Norton High	High School	W. T. Rich Company Inc.	\$27,023,541	700	Bid	162,000	\$167	\$20,590,559	\$127	CM-at-Risk	12-Mar-12	31-Jan-14	0	100%	\$1,448,865	5.440%	The project is complete except for final commissioning and close out.	\$20,634,829	
Southern Worcester Cty VT Bay Path Reg Voc Tech H S	Vocational / Technical	Consigli Construction Company, Inc.	\$57,024,455	1,110	Bid	249,521	\$229	\$41,468,049	\$166	CM-at-Risk	02-Aug-13	01-Sep-15	0	99%	\$3,876,729	6.844%	Phase 10 of a 10-phase project has been completed. Items remaining include minor punch list items, final commissioning and close out.	\$44,420,530	
Springfield Elias Brookings	Elementary School	Morganti/Aquadro & Cerruti	\$22,733,394	320	Bid	64,800	\$351	\$18,337,328	\$283	CM-at-Risk	01-Jul-13	12-Feb-15	0	100%	\$243,295	1.070%	Remaining punch list and warranty issues are being addressed.	\$25,563,992	
Wilmington Wilmington High	High School	Gilbane Building Company	\$67,558,835	960	Bid	192,443	\$351	\$48,060,314	\$250	CM-at-Risk	30-Apr-13	12-Feb-15	0	97%	\$2,682,874	4.152%	Completing remaining punch list and warranty work	\$35,674,893	
Winchester Winchester High School	High School	Consigli Construction Company, Inc.	\$100,935,610	1,370	Bid	278,925	\$362	\$60,656,324	\$217	CM-at-Risk	23-Apr-14	31-Aug-17	0	64%	\$1,533,373	1.519%	Phase 1 construction of a new main entrance, administration offices, music wing, kitchen, cafeteria, and media center is complete and in service. Completion of renovations to the auditorium has been delayed from September 1, 2015 to September 1, 2016. Phase 2 renovations are in process and are scheduled for completion in August of 2016. Phase 3 renovations are scheduled for completion in August of 2017.	\$41,246,371	
Winthrop Winthrop Sr High	Junior High School	Gilbane Building Company	\$63,542,179	970	PFA	187,917	\$338	\$42,616,843	\$227	CM-at-Risk	01-Jul-14	30-Jun-16	0	65%	\$200,031	0.315%	Structural steel and concrete work have been completed. Roofing, framing, fireproofing and window installations are complete. The exterior façade is complete. The building was made weather tight at the end of October. Interior finish work is in progress.	\$39,559,238	
Worcester Nelson Place	Elementary School	Fontaine Brothers, Inc.	\$46,546,300	600	PFA	111,256	\$418	\$29,503,564	\$265	CM-at-Risk	01-Jul-15	01-Jun-17	0	13%	\$0	0.000%	Site work is ongoing including excavation and grading. Blasting and hauling extra material off site to the landfill are complete. The early concrete package will start next spring as early as weather allows in March/April and structural steel in May.	\$33,717,513	
<b>Waitlist Totals</b>			<b>\$10,644,575</b>																<b>\$15,594,751</b>
New Bedford New Bedford High	High School	Sparks Company, Inc.	\$1,875,567	4,000	Bid	454,028	\$4	\$1,762,320	\$4	Design/Bid/Build	27-Aug-14	06-Mar-15	0	99%	\$126,269	6.732%	All work is complete except change order work to install a new intrusion alarm system.	\$5,462,945	
New Bedford Taylor School at the Sea Lab Marine Science Education Center	Elementary School	M.O'Connor Contracting, Inc.	\$8,769,008	284	PFA	64,533	\$136	\$6,908,790	\$107	Design/Bid/Build	28-Nov-15	15-Aug-16	0	10%	\$0	0.000%	The contractor has mobilized to the site and is setting up office trailers. Excavation has begun for the new building wing.	\$10,131,806	
