

Massachusetts School Building Authority

CAPITAL PLANNING PROJECT OVERVIEW REPORT

April 19, 2017


TABLE OF CONTENTS

Capital Pipeline Overview	2-3
Statements of Interest (SOIs)	4
Core Program	5-16
Eligibility Period	5-6
Consultant Selection	7-8
Feasibility Study	9
Schematic Design	10
Commissioning	11-12
Design Development	13
Summary of Bid Data	14
Construction	15-16
Accelerated Repair Program	17-21
Project Variances	22-23
<i>Appendices</i>	
(A) <i>Project Status List</i>	
(B) <i>2016 and 2017 Estimated Bid Dates</i>	
(C) <i>Construction Status Report</i>	
(D) <i>MSBA funding limit for construction cost per square foot</i>	

CAPITAL PIPELINE OVERVIEW

Status of Current Projects

A total of 348 projects that have received invitations from the Board of Directors (“Board”) to collaborate with the Massachusetts School Building Authority (“MSBA”) are currently in the MSBA’s Eligibility Period and Capital Pipeline. The summary chart provides the number of projects in Eligibility Period and each phase of the Capital Pipeline. For a detailed look at the Capital Pipeline projects, please go to www.massschoolbuildings.org/building and select “Capital Pipeline Status Chart”.

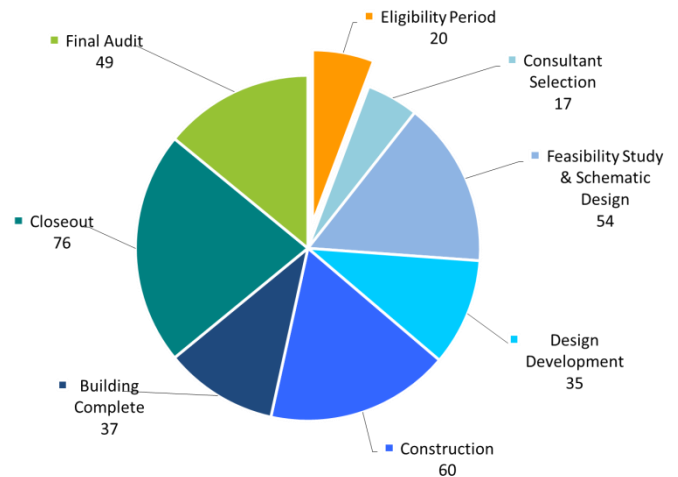

Capital Planning Updates:

The following FY 17 objectives have been completed and approved by the Board:

- 11/9/16 – The Removal of the incentive points for use of the Construction Manager at Risk.
- 11/9/16 - Revisions to the MSBA policy that would allow auditorium and gymnasium spaces above MSBA guidelines at the district’s sole expense for districts that are approved to proceed into Schematic Design on or after January 1, 2017.
- 11/9/16 – Removal of the previously approved Model School designs from the Model School Program.
- 2/15/17 – Update to the MSBA’s sustainability policies in relation to the 9th building code.

The following objectives are a forecast of topics that the MSBA staff anticipates sharing at the May 2017 and June 2017 Board meetings:

- Staff recommendation for information to be observed during school visits for a Post Occupancy Review Pilot Program and the best approach to conduct school visits for this review is anticipated at the May 12, 2017 Board meeting.
- 2017 SOIs for ARP and Core programs have been received and are under review by staff. Staff recommendations for ARP invitations will be prepared for the May 2017 and June 2017 Board meetings. Also, staff recommendations for senior study visits for Core Program SOIs is anticipated at the June 2017 Board meeting.
- 2016 school survey visits to 1432 schools are complete, as of January 31, 2017. The data is under review and districts will be offered the opportunity to validate the information in May. Staff anticipates sharing initial survey findings at the June 28, 2017 Board meeting.
- Staff is reviewing and assessing the process and procedures for the Eligibility Period, established in 2012. Staff anticipates sharing these findings at the June 28, 2017 Board meeting.
- Staff is reviewing the MSBA’s Green Schools Incentive Points in relation to the 9th Edition of the Massachusetts Building Code. Staff anticipates sharing a recommendation at the June 2017 or August 2017 Board meeting.

- Staff is reviewing the MSBA’s funding limit for construction costs per square foot for the June 28, 2017 Board meeting. (Additional information is included in Attachment D)

2017 Progress Report


- Statement of Interest (“SOI”) 2017
 - The 2017 SOI submittal period opened on January 6, 2017. The deadline to file SOIs for consideration in the Accelerated Repair Program (“ARP”) ended on February 17, 2017. The deadline to file SOIs for consideration in the Core Program ended on April 7, 2017. The current status for both programs is as follows:
 - 73 submittals were received for the ARP. Recommendations for invitation to the ARP will be presented at the May 2017 and June 2017 Board meetings; and
 - 83 submittals were received for the Core Program. Recommendations for Senior Study Visits are anticipated to be presented at the June 28, 2017 Board meeting.
- Eligibility Period
 - There are 20 districts in the Eligibility Period, with three of those districts anticipating invitation to Feasibility Study at the May 12, 2017 Board Meeting.
- Feasibility Study/Schematic Design
 - Seven districts received MSBA approval for selection of an Owner’s Project Manager (“OPM”).
 - One district completed Designer Selection.
 - 14 districts are anticipating submittals for the preferred schematic solutions between May 2017 and October 2017.
 - 12 districts are anticipating submittals for Project Funding Agreements between February 2017 and August 2017.
- Accelerated Repair Program (“ARP”)
 - MSBA staff anticipates recommendations for seven Project Funding Agreements at the May 12, 2017 Board Meeting. These recommendations will complete the Project Funding Agreements for the 2016 ARP.
- Construction Costs – Core Program
 - MSBA staff anticipates 11 projects will bid in 2017.
 - Of the 11 bids and/or executions of a GMP projected to bid in 2017, one project has completed the bidding process and its bids were within the estimated budget.
- Substantial Completion
 - Ten projects are projected to reach substantial completion in 2017.

STATEMENTS OF INTEREST (SOIs)

2017 SOI Process

The 2017 SOI submittal period opened on January 6, 2017. The deadline to file SOIs for consideration in the ARP, which is primarily for the repair and/or replacement of roofs, windows/doors, and/or boilers in an otherwise structurally sound facility ended on Friday, February 17, 2017. Currently, staff is performing a due diligence review on the 73 submittals. Staff anticipates issuing recommendations at the May 12, 2017 Board meeting.

The deadline to file SOIs for consideration in the Core Program, which is primarily for projects beyond the scope of ARP, including extensive repairs, renovations, addition/renovations, and new school construction opened on January 6, 2017 and ended on Friday, April 7, 2017. Currently, staff is performing a due diligence review on the 83 submittals. Staff anticipates issuing recommendations for Senior Study visits at the June 7, 2017 Facilities Assessment Subcommittee and June 28, 2017 Board meeting.

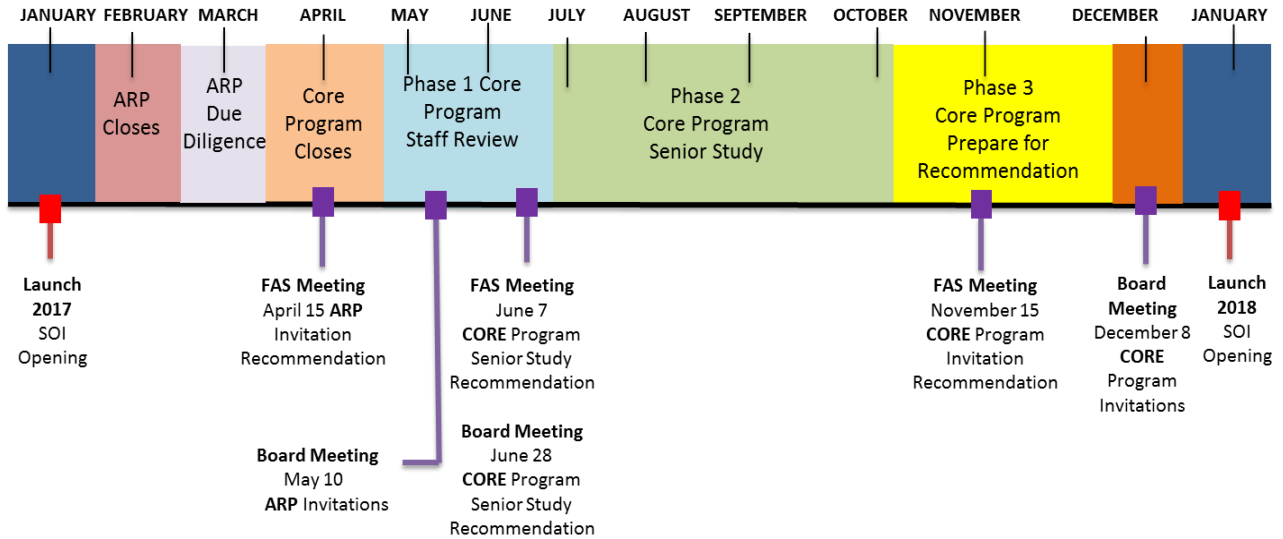

CORE PROGRAM

ELIGIBILITY PERIOD

There are 20 districts in Eligibility Period, with four districts having secured their funding.

An agreed-upon enrollment is a key pre-requisite for the MSBA to commence a Feasibility Study with a district. To begin the enrollment projection process, a district must file enrollment information utilizing the MSBA's online enrollment projection tool. Three of the 20 districts currently in Eligibility Period have completed their online enrollment projection information. Of the 20 districts, three districts have signed their enrollment certifications.

Based upon the schedules anticipated by the districts for completion of Eligibility Period requirements, MSBA staff anticipates recommending three districts, in Eligibility Period, for an Invitation to Feasibility Study at the May 12, 2017 Board Meeting.

District	School	Eligibility Period Commencement Date	30 days	60 days	90 days		180 days		270 days	Date of Invitation to Feasibility Study (Estimated)
			ICC	SBC	Online Enrollment Projection Info	Ed Profile Questionnaire	Maintenance Documents	Enrollment Certification	Local Authorization	
Amesbury	Amesbury ES	7/20/2016	X	X	X	X	X	X	X	5/10/17
Central Berkshire	Wahconah Regional HS	7/20/2016	X	X	X	X	X	X	X	5/10/17
West Springfield	Colburn ES	7/20/2016	X	X	X	X	X	X	X	5/10/17
Bridgewater-Raynham	Mitchell ES	3/1/2017	X							TBD
Leicester	Leicester Middle School	3/1/2017	X							TBD
Millbury	Raymond E. Shaw ES	3/1/2017	X							TBD
Westborough	Annie E. Fales ES	3/1/2017	X	X					X	TBD
Acton-Boxborough	CT Douglas ES	4/3/2017								TBD
Easton	Center School	4/3/2017								TBD
Gloucester	East Gloucester ES	4/3/2017								TBD
Rockland	Jefferson ES	4/3/2017								TBD
Sharon	Sharon HS	4/3/2017								TBD
Fitchburg	Crocker ES	5/1/2017								TBD
Gardner	Waterford Street ES	5/1/2017								TBD
Lawrence	Oliver Partnership School	5/1/2017								TBD
Orange	Dexter Park School	5/1/2017								TBD

District	School	Eligibility Period Commencement Date	30 days	60 days	90 days		180 days		270 days	Date of Invitation to Feasibility Study (Estimated)
			ICC	SBC	Online Enrollment Projection Info	Ed Profile Questionnaire	Maintenance Documents	Enrollment Certification	Local Authorization	
Braintree	South MS	6/1/2017	X							TBD
Nauset RSD	Nauset Regional HS	6/1/2017								TBD
Springfield	Deberry ES	6/1/2017								TBD
Worcester	Doherty Memorial HS	6/1/2017								TBD

CONSULTANT SELECTION

Owner's Project Manager ("OPM") Selection

After the district has completed all Eligibility Period requirements and has received a Board Invitation to Feasibility Study, the district procures an OPM. Since the last report, seven districts have completed their OPM selection (shaded in the table below). Currently, there are ten districts in the Capital Pipeline that are in the process of procuring an OPM.

District	School	Anticipated Selection
Foxborough	Mabelle ES	February 2017
Dennis-Yarmouth	Mattacheese MS	March 2017
Ludlow	Chapin Street ES	March 2017
Manchester Essex RSD	Manchester Memorial Elementary	March 2017
Weymouth	Chapman MS	March 2017
Belmont	Belmont HS	April 2017
Northbridge	W. Edward Balmer ES	April 2017
Pentucket	Pentucket RHS	May 2017
Marblehead	Elbridge Gerry ES	May 2017
Shrewsbury	Beal ECC	May 2017
Framingham	Fuller Middle School	June 2017
Danvers	Ivan G. Smith ES	June 2017
Springfield	Brightwood ES	June 2017
Tewksbury	Louise Davy Trahan ES	June 2017
Arlington	Arlington HS	July 2017
Wareham	Minot Forest ES	July 2017
Holyoke	Lt. Elmer J. McMahon ES	TBD

Designer Selection

After a district has selected and executed a contract with an OPM, the district selects a Designer by utilizing either a local designer selection process for projects under \$5 million or the MSBA’s Designer Selection Panel (“DSP”) for projects over \$5 million. Since the last report, one district has completed their Designer selection (shaded in the table below). There are currently seven districts in the Capital Pipeline that are in the process of procuring a Designer.

District	School	Anticipated Selection
Natick	John F. Kennedy MS	March 2017
Dennis-Yarmouth RSD	Mattacheese MS	May 2017
Foxborough	Mabelle M. Burrell ES	May 2017
Ludlow	Chapin Street ES	May 2017
Weymouth	Maria Weston Chapman MS	May 2017
Belmont	Belmont HS	June 2017
Manchester Essex RSD	Manchester Memorial ES	June 2017
Northbridge	W. Edward Balmer ES	June 2017

For additional information on the selected consultant teams, see Appendix A.

FEASIBILITY STUDY

Once a district has procured an OPM and Designer and prior to Board consideration to advance to Schematic Design, the district and the district's consultants must complete two Feasibility Study submittals, the Preliminary Design Program, and the Preferred Schematic Report. Based on the most recent data and schedules provided to the MSBA by districts, the MSBA anticipates that 14 districts will appear before the Board for their Preferred Schematic Designs authorizations at the May, June, August, and October 2017 Board Meetings.

District	School	Anticipated PS Board Date
Clarksburg	Clarksburg ES	May 2017
Middleborough	Middleborough HS	May 2017
Boston	Boston Arts Academy	June 2017
Easthampton	Maple ES	June 2017
Lowell	Lowell HS	June 2017
Worcester	South High Community School	June 2017
Tisbury	Tisbury ES	June 2017
Attleboro	Attleboro HS	August 2017
Fall River	Durfee HS	August 2017
Harvard	Harvard ES	August 2017
Taunton	Mulcahey ES	August 2017
Bristol County	Bristol County Agriculture HS	October 2017
Marlborough	Richer ES	October 2017
Everett	Keverian K-8	TBD

SCHEMATIC DESIGN

Prior to consideration by the Board for Project Scope and Budget Agreement authorization, a district must submit a Schematic Design to the MSBA for review. Based on the most recent data and schedules provided to the MSBA by districts, the MSBA anticipates that 12 districts will appear before the Board for Project Scope and Budget Agreement authorization at the upcoming May, June, August and October 2017 Board Meetings.

District	School	Anticipated PS&B Board Date
Millis	Clyde F. Brown ES	May 2017
Braintree	East MS	June 2017
Ipswich	Winthrop ES	June 2017
Triton	Pine Grove ES	June 2017
Saugus	Saugus HS	June 2017
Blue Hills	Blue Hills Regional Technical HS	August 2017
Cape Cod Regional Vocational Technical	Cape Cod Regional Technical HS	August 2017
Clarksburg	Clarksburg ES	August 2017
Lexington	Maria Hastings ES	August 2017
Middleboro	Middleboro HS	October 2017
Westport	Westport MS	October 2017
Everett	Keverian K-8	TBD

COMMISSIONING

The MSBA assigns a Commissioning Consultant after a district has secured local funding for the Board approved project. Since the last report, the MSBA has assigned Commissioning Consultants to 22 additional projects presented in the table below.

District	School	Program	Estimated Const. Cost (million)	Commissioning Consultant	Contract Amount
Agawam	Doering MS Boiler	2016 ARP	\$0.69	BVH Integrated Services	\$15,535
Worcester	Worcester 2 Schools Boilers	2016 ARP	\$0.79	BVH Integrated Services	\$31,070
Lawrence	Lawrence HS Learning Center Boiler	2016 ARP	\$1.18	Fitzemeyer & Tocci Associates	\$13,500
Boston	Boston 3 Schools Boilers	2016 ARP	\$3.10	Rist-Frost-Shumway Engineering	\$51,000
Cambridge	Fletcher/Maynard Roof	2016 ARP	\$0.81	Gale Associates	\$41,910
Springfield	Springfield Roofs & Windows 4 Schools	2016 ARP	\$13.91	Building Enclosure Associates	\$95,000
North Brookfield	North Brookfield ES Roof	2016 ARP	\$3.31	Simpson Gumpertz & Heger	\$32,000
Sharon	Heights ES roofing	2016 ARP	\$1.86	Simpson Gumpertz & Heger	\$32,000
Canton	Hansen MS roof	2016 ARP	\$1.42	Simpson Gumpertz & Heger	\$28,000
Boston	Boston 2 Schools Roofs	2016 ARP	\$5.12	Simpson Gumpertz & Heger	\$60,000
Swansea	Brown ES Windows	2016 ARP	\$1.13	Simpson Gumpertz & Heger	\$28,000
Marshfield	Furnace Brook MS Roof	2016 ARP	\$7.02	Russo Barr Associates	\$61,300
Quincy	Quincy 4 Schools Boilers	2016 ARP	\$2.50	Consulting Engineering Services	\$62,640
Worcester	Worcester 4 Schools Windows	2016 ARP	\$8.66	Russo Barr Associates	\$94,830
Boxford	Spofford Pond Roof & Windows	2016 ARP	\$3.91	CBI Consulting	\$63,000
Dartmouth	Middle School Roof	2016 ARP	\$4.82	CBI Consulting	\$44,800
Gloucester	High School Roof	2016 ARP	\$4.23	CBI Consulting	\$40,400
Northampton	Northampton 2 Schools Roofs	2016 ARP	\$2.43	CBI Consulting	\$44,310
Auburn	Pakachoag ES Roof	2016 ARP	\$0.62	Thompson & Lichtner	\$29,000
Chicopee	Chicopee 2 Schools Roof & Windows	2016 ARP	\$3.66	Thompson & Lichtner	\$50,950
Halifax	Halifax ES Roof Windows	2016 ARP	\$6.21	Russo Barr Associates	\$58,660
Revere	Garfield MS Boiler	2016 ARP	\$1.08	Fitzemeyer & Tocci Associates	\$11,900

To date, the MSBA has executed 398 Commissioning Consultant contracts, totaling \$28.0 million. To date, 260 contracts have been completed.

The table below represents the status of commissioning assignments sorted by the fiscal year in which the commissioning work orders were issued.

Fiscal Year	No. Work Orders Issued	Value of Work Orders Issued	Total Invoiced*	Percent Complete
FY10	31	\$4,231,376	\$4,273,277	100%
FY11	95	\$6,132,890	\$6,058,460	99%
FY12	52	\$4,450,761	\$4,385,280	99%
FY13	55	\$3,364,697	\$3,364,040	99%
FY14	47	\$2,604,062	\$2,428,986	93%
FY15	44	\$2,277,711	\$1,629,855	72%
FY16	44	\$3,385,137	\$1,140,150	34%
FY17	30	\$1,580,601	\$75,343	5%
Total	398	\$28,027,235	\$23,355,390	

**Includes approved additional services over value of Work Order*

DESIGN DEVELOPMENT

After a district has secured local funding and has entered into a Project Funding Agreement (“PFA”) with the MSBA, the district enters into the Design Development Phase. Currently, there are 31 projects in the Design Development Phase with a total estimated construction cost of approximately \$846.4 million. Of those 31 projects, 20 are ARP Projects and 11 are Core Program Projects. The 11 Core Program Projects in Design Development have a total estimated construction cost of approximately \$806.6 million and are listed below.

Elementary School Districts	Middle School Districts	High School Districts	Other Grade Configurations
Bourne (3-5) Dedham (PK-K) Hanover (2-4) Narragansett RSD (PK-5)* Needham (K-5) Newton (K-5)	Quincy (5-8)	Billerica (9-12) Minuteman RSD (9-12) Stoughton (9-12) Somerville (9-12)	

**Town is currently under Audit Review for Fiscal Year 2015 and 2016. Bids have been delayed pending outcome of financial support for the project.*

District Design Submittals

During Design Development, districts submit three design submittals (Design Development, 60% Construction Documents, and 90% Construction Documents) for MSBA review. MSBA staff reviews documents to ensure the project is still in compliance with the PFA. The chart below indicates the number of submittals received by the MSBA to date by type and by fiscal year.

Fiscal Year	DD Reviews	60% Reviews	90% Reviews	Total Reviews
2010	5	0	0	5
2011	21	24	20	65
2012	12	24	28	64
2013	20	20	19	59
2014	15	13	14	42
2015	6	12	13	31
2016	10	10	8	28
2017	11	10	9	30
Totals	100	113	111	324

SUMMARY OF BID DATA

Based on the most recent data and schedules provided by the districts, 11 projects are scheduled to bid in 2017, and one project is scheduled to bid in 2018.

Year	Number of Projects	Design Basis for Enrollment	Project Budget	Construction Budget
2017	11	6,828	\$822.01 million	\$647.42 million
2018	1	1,590	\$255.98 million	\$199.05 million
Grand Total	12	8,418	\$1.08 billion	\$0.85 billion

Note: These numbers are based on preliminary information received from the District and are subject to further review and calculation.

CONSTRUCTION

When a district issues a Notice to Proceed, the project is advanced to the Construction Phase. Currently, there are 64 projects in the Construction Phase with a total estimated construction cost of \$1.24 billion. Of those 64 projects, 44 are ARP Projects and 20 are Core Program Projects. This does not include the 37 projects that have reached substantial completion and are currently in the Building Complete Phase. The 20 Core Program Projects have a total estimated construction cost of \$1.15 billion and are listed below.

Elementary School Districts	Middle and Middle/High School Districts	High School Districts	Other Grade Configurations
Carver (PK-5) Granby (PK-3) Hopkinton (PK-1) New Bedford (PK-5) Woburn (K-5) Westfield* (K-5)	<u>Middle School Districts</u> Beverly (5-8) Chelsea (5-8) Scituate (6-8) Westborough (7-8) <u>Middle/High School Districts</u> Boston - Dearborn MS (6-12)	North Middlesex RSD (9-12) Mt. Greylock RSD (9-12) Pittsfield (9-12) Plymouth (9-12) Winchester (9-12)	Abington (PK; 5-12) Brookline (K-8) Holbrook (PK-12) Worcester (PK-6)

**Note: Westfield, Abner Gibbs Elementary School, stopped construction in December of 2012 due to a preliminary injunction based upon project site status as Article 97 "Protected Land".*

Amendment to the Project Funding Agreement (PFA)

Upon receipt of construction bids or the execution of a GMP, a district submits the Contractor's Schedule of Values to the MSBA. MSBA staff and the district collaborate to reconcile the actual construction costs against the estimated construction budget and an amendment to the PFA is executed to reflect bid costs. The chart, shown below, is the number of amendments to PFAs, listed by fiscal year.

Fiscal Year	Total Amendments
FY2012	30
FY2013	31
FY2014	31
FY2015	17
FY2016	22
FY2017	8

Substantial Completion

Ten projects are scheduled to reach Substantial Completion in 2017. They are listed in the table below. For additional information on the construction status for each of these projects, see Appendix C.

Project	Enrollment	Contractor	OPM	Designer	Est. Substantial Completion Date	Actual Substantial Completion Date	Est. Actual Difference (days)
Plymouth Plymouth South HS	1005	Bacon-Agostini	Ted Gentry	Ai3	5/5/17		
Worcester Nelson Place ES	600	Fontaine Brothers	Tishman	Lamoureux Pagano	5/31/17		
Abington Frolio Jr HS	870	Brait Builders	KBA	Ai3	6/1/17		
Holbrook PreK-12	1095	Consigli	SMMA	Flansburgh	6/5/17		
North Middlesex Reg. HS	1115	CTA Construction	Heery	SMMA	7/14/17		
Scituate Gates IS	710	Bacon-Agostini	Daedalus	Dore & Whittier	7/24/17		
New Bedford Hannigan ES	400	H.V. Collins	Daedalus	Turowski2 Architecture	8/7/17		
Westborough Sarah W. Gibbons MS	550	Gilbane	Heery	Habeeb & Associates Architects	8/25/17		
Winchester Winchester HS	1370	Consigli	Skanska	SMMA	8/31/17		
Boston Dearborn MS	600	Gilbane	Daedalus	Jonathan Levi	12/27/17		

ACCELERATED REPAIR PROGRAM


Currently, there are 219 projects, either active or completed in the ARP. The 219 projects are located in 96 districts and many of these districts have been invited in the ARP multiple times. All new information that has been updated since the last report is italicized.

Repair Program	Number of Districts	Number of Projects	Total Project Budgets	Maximum Facility Grants	Number of Projects Final Audit Approved
2016 Accelerated	28	48	<i>\$109,949,270*</i>	<i>\$63,314,661*</i>	0
2015 Accelerated	24	43	\$136,680,652	\$91,974,052	0
2014 Accelerated	34	47	\$108,410,084	\$65,388,035	13
2013 Accelerated	25	45	\$94,650,790	\$54,662,711	33
2012 Accelerated	24	36	\$63,009,653	\$38,267,952	36
Green	93	189	\$366,649,226	\$222,889,218	182

*Financial totals reflect projects approved for Project Funding Agreements as of the February 15, 2017 Board of Directors Meetings.

2016 Accelerated Repair Program


- *Invitations – 28 districts, representing 49 projects*
 - *Scope includes 25 roofs, 19 windows/doors, and 13 boilers*
- *SOI Removal - one project*
- *Approval for Project Funding Agreement - 22 districts, representing 37 projects*
- *Total Project Budgets - \$109,949,270*
- *MSBA Total Facilities Grant - \$63,314,661*
- *2 of 2 projects reporting bid within estimated budget*

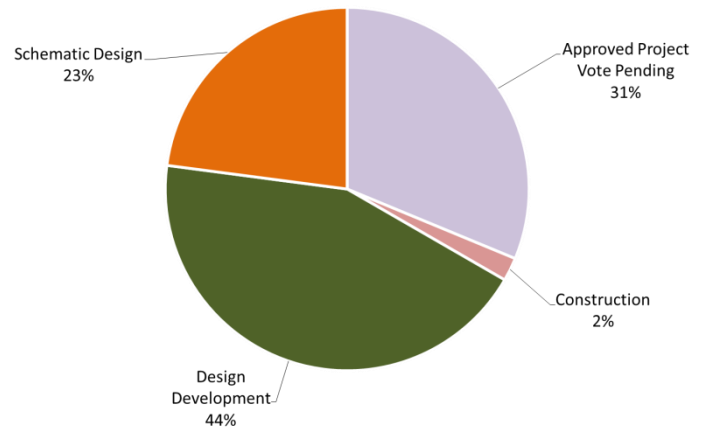

2016 ARP Status Chart

2015 Accelerated Repair Program


- Invitations – 24 districts, representing 44 projects
 - Scope includes 22 roofs, 26 windows/doors, and nine boilers
- SOI Removal – one project
- Approved for Project Funding Agreements – 24 districts, representing 43 projects
- Total Project Budgets - \$136,680,652
- MSBA Total Facilities Grants - \$91,974,052
- *One district, representing one project, required a schedule extension following PFA Approval*
- *81% of projects bid within estimated budgets*

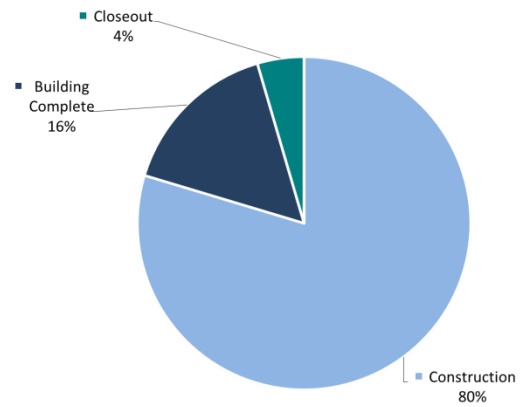

2015 ARP Status Chart

2014 Accelerated Repair Program


- Invitations – 36 districts, representing 51 projects
- SOI Removal – two districts, representing four projects
- Current 2014 ARP projects – 34 districts, representing 47 projects
 - Scope includes 20 roofs, 25 windows/doors, and 13 boilers
- Approved for Project Funding Agreements – 34 districts, representing 47 projects
- Total Project Budgets - \$108,410,084
- MSBA Total Facilities Grants - \$65,388,035
- Four districts, representing six projects, required schedule extensions following PFA approval
- 85% of projects bid within estimated budget
- *28% of projects have completed Final Audit*

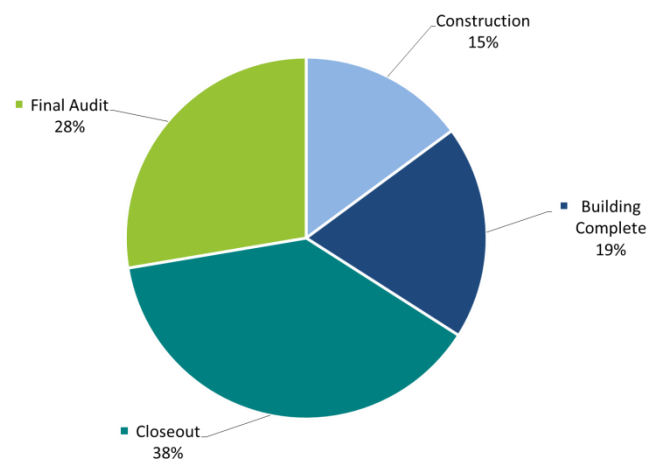

2014 ARP Status Chart

2013 Accelerated Repair Program


- Invitations – 28 districts, representing 50 projects
- SOI Removals – three districts, representing five projects
- Approved for Project Funding Agreements – 26 districts, representing 47 projects
- Active Projects – 25 districts, representing 45 projects
 - Scope includes 30 roofs, 13 windows/doors, and seven boilers
- Total Project Budgets – \$94,650,790
- MSBA Total Facilities Grants – \$54,662,711
- Four districts, representing seven projects, required schedule extensions following PFA approval
- 82% of projects bid within estimated budget
- *73% of projects have completed Final Audit*

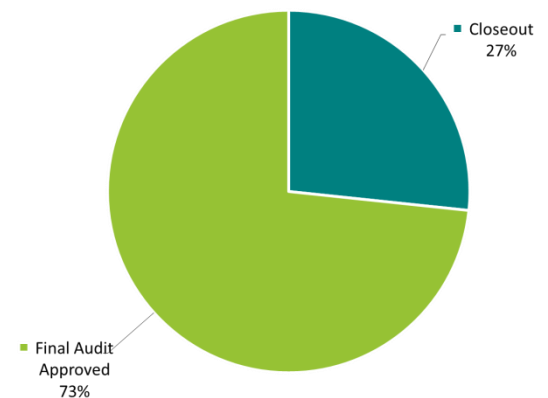

2013 ARP Status Chart

2012 Accelerated Repair Program

- Invitations – 27 districts, representing 39 projects
- SOI Removals – three districts, representing three projects
- Approved Project Funding Agreements – 24 districts, representing 36 projects
- Scope includes 21 roofs, 11 windows/doors, and seven boilers
- Total Project Budgets – \$63,009,653
- MSBA Total Facilities Grants – \$38,267,952
- Five districts, representing nine projects, required schedule extensions following PFA approval
- 86% of projects bid within estimated budget
- *100% of projects have completed Final Audit*
- *Final Costs Submitted: \$47,748,996*
- *Final MSBA Total Facilities Grant: \$28,518,764*



2012 ARP Status Chart

Status of Green Repair Program

The Green Repair Program resulted in PFA authorizations totaling \$366,647,226 in Total Project Costs and \$222,889,218 in MSBA grants. *Of the 189 projects, 182 have been approved for final grant payments. The seven projects that were not previously approved for final grant payments are substantially complete and require Final Audit.*

2016 Accelerated Repair Projects – Construction Estimate vs. 2017-2018

- *2 of 2 reported projects bid within the estimated budget*
- *19 of the remaining 46 projects will bid by the end of the May 2017 with an update anticipated at the June 2017 Board of Directors Meeting*

District	School	Scope	Project Type	Bid Date	Construction Estimate **	Bid Amount **	Variance from Construction Estimate	Reimbursement Rate	Potential Grant Variance *
Carver	Carver Middle/High School	Roof, Partial Windows/Doors Boiler	DBB	Mar-17	\$4,735,668	\$3,770,000	\$965,668	57.74%	\$557,577
Auburn	Pakachoag	Roof	DBB	Mar-17	\$619,654	\$566,000	\$53,654	54.16%	\$29,059
				Total	\$5,355,322	\$4,336,000	\$1,019,322		\$586,636

2015 Accelerated Repair Projects – Construction Estimate vs. 2016-2017

- Staff reported previously on the shaded projects below.
- *Staff added 12 new projects to the chart below. All projects are now reflected.*
- *81% of the 43 projects bid within the estimated budget.*

District	School	Scope	Project Type	Bid Date	Construction Estimate **	Bid Amount **	Variance from Construction Estimate	Reimbursement Rate	Potential Grant Variance *
Worcester	Grafton Street School	Windows/Doors Boiler	DBB	Mar-16	\$3,470,847	\$2,972,000	\$498,847	78.95%	\$393,840
Worcester	Francis J McGrath ES	Windows/Doors	DBB	Mar-16	\$1,211,628	\$941,640	\$269,988	78.95%	\$213,156
Worcester	Jacob Hiatt Magnet	Windows/Doors	DBB	Mar-16	\$1,647,516	\$1,300,360	\$347,156	78.95%	\$274,080
Worcester	Flagg Street	Windows/Doors	DBB	Mar-16	\$3,327,388	\$2,242,000	\$1,085,388	78.95%	\$856,914
New Bedford	Alfred J. Gomes School	Windows/Doors	DBB	Mar-16	\$3,794,672	\$2,718,100	\$1,076,572	80.00%	\$856,736
Blackstone Valley RSD	Blackstone Valley School	Roof – Partial	DBB	Mar-16	\$892,764	\$717,000	\$175,764	53.53%	\$94,086
New Bedford	Casmir Pulaski School	Windows/Doors / Boiler	DBB	April-16	\$2,274,474	\$1,926,000	\$348,474	79.58%	\$277,316
New Bedford	Hayden/McFadden School	Windows/Doors / Boiler	DBB	April-16	\$4,636,946	\$4,202,028	\$434,918	79.58%	\$346,108
New Bedford	Sgt. Williams H. Carney Academy	Windows/Doors / Boiler	DBB	April-16	\$4,078,525	\$4,208,704	-\$130,179	79.58%	\$0
Deerfield	Deerfield ES	Roof	DBB	April-16	\$2,341,276	\$1,589,000	\$752,276	52.06%	\$391,635
Cambridge	Kennedy-Longfellow School	Roof	DBB	April-16	\$2,804,463	\$1,137,000	\$1,667,463	47.03%	\$784,208
Ludlow	East Street ES	Roof / Partial Boiler	DBB	April-16	\$2,566,953	\$1,792,829	\$774,124	58.37%	\$451,856
North Reading	E. Ethel Little School	Roof-Partial	DBB	April-16	\$1,414,932	\$1,290,000	\$124,932	46.58%	\$58,193
Cambridge	Fletcher/Maynard Academy	Boiler	DBB	April-16	\$600,661	\$624,737	-\$24,076	47.03%	\$0
West Bridgewater	Spring Street School	Roof	DBB	April-16	\$1,107,449	\$638,000	\$469,449	52.69%	\$247,353
Quincy	Merrymount	Roof	DBB	May-16	\$1,472,686	\$1,078,975	\$393,711	68.96%	\$271,503
Chicopee	Belcher	Roof	DBB	May-16	\$724,660	\$452,185	\$272,475	78.95%	\$215,119
Chicopee	Fairview Middle	Roof	DBB	May-16	\$2,403,119	\$1,318,815	\$1,084,304	78.95%	\$856,085
Middleborough	Memorial ECC	Roof-Partial	DBB	Jun-16	\$891,117	\$640,000	\$251,117	56.26%	\$141,278
Revere	Garfield ES	Roof	DBB	Jul-16	\$6,527,919	\$6,124,000	\$403,319	77.47%	\$312,916
Fairhaven	Hastings Middle	Roof-Partial	DBB	Jul-16	\$633,861	\$481,300	\$152,561	54.79%	\$83,588
Springfield	Mary M Walsh	Windows/Doors	DBB	Aug-16	\$2,218,786	\$1,479,159	\$739,627	54.79%	\$405,242
Springfield	Springfield Public Day High School	Windows/Doors	DBB	Aug-16	\$1,313,487	\$1,105,221	\$208,266	80.00%	\$166,613
Springfield	STEM Middle Academy	Roof-Partial	DBB	Aug-16	\$1,666,499	\$963,321	\$703,178	80.00%	\$562,542
Wareham	John W. Decas Elementary School	Roof- Partial Boiler	DBB	Aug-16	\$2,019,034	\$1,165,300	\$853,734	70.10%	\$598,468
Springfield	Daniel B Brunton	Windows/Doors	DBB	Sept-16	\$2,233,738	\$1,834,000	\$399,738	80.00%	\$319,790
Leicester	Leicester High	Roof	DBB	Oct-16	\$2,097,427	\$1,321,689	\$775,738	59.21%	\$459,314
Taunton	Edmund Hatch Bennet	Roof/Windows	DBB	Oct-16	\$3,750,583	\$2,049,987	\$1,700,596	73.95%	\$1,257,591
Taunton	Joseph H Martin	Roof/Windows	DBB	Oct-16	\$5,407,623	\$3,474,593	\$1,933,030	73.95%	\$1,429,476
Greenfield	Federal	Boilers, Roof, Windows	DBB	Nov-16	\$4,698,376	\$2,566,916	\$2,131,460	77.47%	\$1,651,242
Leominster	Johnny Appleseed	Roof/Windows	DBB	Nov-16	\$3,168,446	\$1,523,600	\$1,644,846	72.59%	\$1,193,994
Quincy	Beechwood Knoll Elem	Roof Windows/Doors	DBB	Oct-16	\$3,635,778	\$2,849,000	\$786,778	68.96%	\$271,503

District	School	Scope	Project Type	Bid Date	Construction Estimate **	Bid Amount **	Variance from Construction Estimate	Reimbursement Rate	Potential Grant Variance *
Watertown	Watertown Middle School	Windows/Doors - Partial	DBB	Dec-16	\$2,813,525	\$1,693,000	\$1,120,525	48.47%	\$543,118
Stoughton	West Elementary	Windows/Doors - Partial	DBB	Feb-17	\$1,511,428	\$950,150	\$561,278	54.79%	\$307,524
Boston	Charles Sumner	Windows/Doors	DBB	Feb-17	\$1,981,779	\$2,010,500	-\$28,701	65.47%	\$0
Boston	Curley K-8 School	Windows/Doors	DBB	Feb-17	\$3,648,625	\$4,429,317	-\$780,692	65.47%	\$0
Boston	David A. Ellis	Windows/Doors	DBB	Feb-17	\$3,188,544	\$3,350,542	-\$161,998	65.47%	\$0
Boston	Dorchester Academy	Windows/Doors	DBB	Feb-17	\$4,524,620	\$4,432,500	\$92,120	65.47%	\$60,311
Boston	Grover Cleveland	Windows/Doors	DBB	Feb-17	\$1,895,564	\$2,404,871	-\$509,307	65.47%	\$0
Boston	Donald McKay	Windows/Doors - Partial	DBB	Feb-17	\$2,652,148	\$2,982,754	-\$330,606	65.47%	\$0
Boston	Young Achievers	Windows/Doors	DBB	Feb-17	\$3,597,623	\$4,597,000	-\$999,377	65.47%	\$0
Wrentham	Delaney	Roof-Partial	DBB	Feb-17	\$1,454,199	\$968,000	\$486,199	46.58%	\$226,471
Peabody	Peabody Veterans Memorial High	Roof-Partial	DBB	Feb-17	\$2,579,192	\$1,257,000	\$1,332,192	54.79%	\$724,429
				Total	\$108,985,316	\$87,803,093	\$23,087,207		\$15,170,242

*These numbers are based on preliminary information received from the district and are subject to further review and calculation.

Accelerated Repair Projects – Schedule Extension Update

The MSBA has granted districts conditional extensions to their PFAs pending compliance with the following stipulations:

- The district must submit a detailed, revised, construction timeline that explains how the work will be completed at each school; and
- Any costs that are related to a district requesting an extension to the construction schedule will be the sole responsibility of the district and those costs are categorically ineligible for reimbursement by the MSBA.

Schedule delays for these districts can be attributed to local funding issues, lead time for windows, and construction delays on site. In no event have the extended schedules resulted in an increase to the Estimated Maximum Total Facilities Grant, as authorized by the Board.

One of the 43 2015 ARP Projects did not meet its construction completion date in 2016. This Project revised its construction schedule and is scheduled to be completed in 2017. Staff has reported previously on the shaded projects listed below. (There is no new activity to report on.)

District	School	Scope	Original Construction Completion Date	Updated Construction Completion Date	Reason for Schedule Extension
Quincy	Beechwood Knoll Elementary	Roof Windows/Doors	8/23/2016	8/28/2017	The District and its consultants have determined that bidding for construction in 2017 would better serve the project budget and existing facilities.

PROJECT VARIANCES

Core Program – Total Project Budget Update

Upon receiving the Board’s approval of the Project Scope and Budget, the MSBA and participating districts enter into a Project Funding Agreement, which establishes the Total Project Budget and the Estimated Maximum Total Facilities Grant for an approved project. Staff has reported on budget increases for the 16 projects shaded below at previous Board Meetings. Project information that is new or updated from the last Board Meeting is un-shaded. In no event has the increase in budget resulted in an increase to the Estimated Maximum Total Facilities Grant, as authorized by the Board.

District	School	Scope	Project Funding Agreement		PFA Bid Amendment/ Final Audit		Reason for Increase to Total Project Budget
			Total Project Budget	Total Maximum Facilities Grant	Total Project Budget	Total Maximum Facilities Grant	
Andover	Bancroft ES	New	\$44,659,837	\$16,773,753	\$50,299,859	\$16,575,965	The District has appropriated additional funds to cover the costs associated with increased construction costs and additional contingencies for litigation/settlement costs and other ineligible costs.
Berlin-Boylston	Tahanto Regional HS	New	\$43,954,901	\$21,148,751	TBD	TBD	District submitted final project costs that exceeded the total project budget established at bid. Final Costs did not exceed the original total project budget established at Project Funding Agreement.
Burlington	Marshall Simonds MS	Add/Reno	\$32,865,272	\$17,143,365	\$34,221,929	\$15,362,127	The District appropriated at its May 2012 annual town meeting through Articles 18: 19, additional funds for the costs associated with the construction of the new field complex and field lighting replacement.
Essex North Shore Agricultural & Technical School District	Essex North Shore Agricultural & Technical HS	New	\$125,000,000	\$77,500,000	\$133,770,000	\$77,500,000	The Board was informed at the March 30, 2011 meeting that the Total Project Budget had increased due to additional ineligible scope that would be funded by DCAM.
			\$125,000,000	\$77,500,000	\$134,501,368	\$77,500,000	The District has appropriated additional funds to cover the costs associated with increased construction costs for horse tack barn renovations.
Greater New Bedford	Greater New Bedford Vocational and Technical High School	Add/Reno	\$17,099,808	\$13,543,920	\$16,396,429	\$12,258,642	District submitted final project costs that exceeded the total project budget established at bid. Final Costs did not exceed the original total project budget established at Project Funding Agreement.
Lexington	Joseph Estabrook ES	New	\$40,792,248	\$12,250,739	\$43,392,248	\$12,148,491	The District has executed a GMP that exceeds the Construction Budget of the PFA. The District has appropriated additional funds to cover the costs associated with increased construction costs and additional contingencies.
Newburyport	Nock/Molin MS	Add/Reno	\$26,997,326	\$13,697,934	\$28,170,749	\$12,520,326	The District has received additional funding to cover additional construction change order costs.
North Reading	North Reading MS/HS	Add/Reno	\$107,727,074	\$49,323,123	\$123,227,074	\$49,323,123	This is a CMR project. The estimated, reconciled construction costs tracked over budget at DD (\$9,746,655 over), 60% (\$4,655,965 over), and 90% (\$15,136,846 over). A Town override vote in March 2013 obtained an additional \$15,500,000 in local funding to proceed.
Norfolk County Agricultural	Norfolk County Agricultural HS	Add/Reno	\$28,552,385	\$15,369,712	\$30,589,078	\$13,867,050	The District has executed a Tender Agreement and Completion Agreement Contract, increasing its Total Project Budget, following the termination of its original construction contract.
Northborough	Lincoln Street ES	Add/Reno	\$25,530,553	\$10,407,408	\$25,530,553	\$10,407,408	The MSBA Board Approved Total Project Budget increased by \$60,400 from \$25,470,153 to \$25,530,553 due to the addition of an alternate, for a new ball field added at the District’s request.
Revere	Staff Sergeant James J. Hill ES	New	\$45,402,396	\$29,551,048	45,402,396	\$29,551,048	At Project Scope and Budget, the Total Project Budget was approved at \$44,382,396. The City of Revere has increased the land acquisition budget. Therefore, the projected total project budget at PFA has increased to \$45,402,396. Note that the MSBA grant has not changed since the Project Scope and Budget Agreement.
Somerville	East Somerville Community School	Add/Reno	\$33,185,258	\$15,237,996	\$38,006,621	\$15,237,996	At the March 28, 2012 Board Meeting, the Board approved an amendment to the PFA and a \$6.25M District loan.
Uxbridge	Uxbridge HS	New	\$43,000,000	\$22,362,328	\$44,986,479	\$22,362,328	The District has appropriated additional funds to cover the costs associated with the construction of athletic fields originally included in the PFA but which were not included in the bid as the District’s construction contract would have exceeded the budget.
Sutton	Sutton MS	Add/Reno	\$59,945,474	\$29,843,511	\$60,130,536	\$27,002,506	The District has executed a Tender Agreement and Completion Agreement Contract, increasing its Total Project Budget, following the termination of its original construction contract.
Weston	Field ES	New	\$31,504,146	\$8,310,510	\$32,654,146	\$8,105,549	District-approved Construction Change Orders exceeded available contingency amount.
Winchester	Winchester HS	Add/Reno	\$129,923,146	\$44,493,270	\$131,513,741	\$43,100,458	The MSBA Board Approved total Project Budget increased due to a construction change order for additional soil abatements at Skillings Field. Note that the increased Total Project Budget will not increase the Maximum Total Facilities Grant.
Winthrop	Winthrop MS/HS	New	\$81,818,740	\$42,582,841	\$81,432,986	\$41,249,005	The MSBA Board Approved Total Project Budget increased due to revised FEMA flood plain requirements which necessitated the elevation of the new building to be raised. Note that the increased Total Project Budget will not increase the Maximum Total Facilities Grant.

Woburn	Wyman-Hurld ES	New	\$33,705,396	\$14,387,427	TBD*	TBD*	The District had completed a project review with its Conservation Commission and an Order of Conditions was issued on June 12, 2015. A neighborhood group has appealed this Order and it is now under review by DEP. The District has experienced delays in completing its City Council vote for its appropriation and incurred additional costs.
--------	----------------	-----	--------------	--------------	------	------	---

**PFA Bid Amendment has not been developed to calculate a revised Total Facilities Grant amount. The Total Maximum Facilities Grant will not exceed the Board authorized amount in the PFA but, upon review, may decrease.*

Date of Report: 4/19/2017

Total Projects: 348

MSBA ID	District	School	Project Phase	Project Type	Project Scope	Procurement Type	OPM	Designer	CM/GC	Commissioning Consultant
200800010405	Abington	Frolio Middle School	Construction	Core Program	New Construction	DBB	Knight, Bagge & Anderson Inc.	Ai3 Architects LLC	Brait Builders Corp.	Horizon Engineering Associates, LLP
201606000020	Acton-Boxborough	Douglas	Eligibility Period				-	-	-	-
201600050303	Agawam	Agawam Middle School	Design Development	Accelerated Repair	Boiler		STV DPM (fka STV Inc.)	Hesnor Engineering Company	-	BVH Integrated Services, P.C.
201500070005	Amesbury	Amesbury Elementary	Eligibility Period	Core Program			-	-	-	-
201300080050	Amherst	Wildwood Elementary	Approved Project Vote Pending	Core Program	New Construction	CM@R	NV5 (fka Joslin, Lesser + Associates Inc.)	JCJ Architecture, PC	Fontaine Brothers, Inc.	-
200800090003	Andover	Bancroft Elementary School	Closeout	Core Program	New Construction	CM@R	Dore & Whittier Management Partners, Inc.	Symmes Maini & McKee Associates, Inc.	Skanska USA Building, Inc.	Sebesta Blomberg & Associates, Inc.
201500100505	Arlington	Arlington High	OPM Selection	Core Program			-	-	-	-
200908010605	Assabet Valley	Assabet Valley Regional Technical High School	Closeout	Core Program	Repair	DBB	Colliers International	Perkins Eastman/DPC	CTA Construction Co., Inc.	Symmes, Maini & McKee Associates
200906150020	Athol-Royalston	Riverbend School	Building Complete	Core Program	New Construction	DBB	Symmes Maini & McKee Associates	Mount Vernon Group Architects, Inc.	Fontaine Brothers, Inc.	Colliers International
201400160505	Attleboro	Attleboro High	Feasibility Study	Core Program			Skanska USA Building, Inc	Kaestle Boos Associates, Inc.	-	-
200800170305	Auburn	Auburn Middle	Closeout	Core Program	New Construction	CM@R	Skanska USA Building, Inc	Lamoureux Pagano & Associates, Inc.	Fontaine Brothers, Inc.	WSP USA
201400170305	Auburn	Auburn Middle	Closeout	Accelerated Repair	Roof, Boiler		Skanska USA Building, Inc	Dietz & Company Architects, Inc.	-	Horizon Engineering Associates, LLP Thompson & Lichtner Co., Inc.
201400170010	Auburn	Bryn Mawr	Closeout	Accelerated Repair	Roof		Skanska USA Building, Inc	Dietz & Company Architects, Inc.	-	Thompson & Lichtner Co., Inc.
201600170015	Auburn	Pakachoag	Design Development	Accelerated Repair	Roof		Hill International Company	CGKV Architects, Inc.	-	Thompson & Lichtner Co., Inc.
200806160505	Ayer-Shirley	Ayer-Shirley Regional Middle/High School	Closeout	Core Program	Addition / Renovation	CM@R	Dore and Whittier Architects, Inc.	Symmes Maini & McKee Associates, Inc.	Consigli Construction Company, Inc.	WSP USA
201400250020	Bellingham	South Elem	Closeout	Accelerated Repair	Roof		Atlantic Construction and Management, Inc.	Taylor & Burns, Inc.	Silktown Roofing	Building Enclosure Associates, LLC
201500260505	Belmont	Belmont High	Designer Selection	Core Program			Daedalus Projects Inc	-	-	-
200806200505	Berlin-Boylston	Tahanto Regional High School	Closeout	Core Program	New Construction	DBB	PMA Construction Services	HMFH Architects, Inc.	CTA Construction Co., Inc.	Colliers International
201300300305	Beverly	Briscoe Middle	Construction	Core Program	New Construction	CM@R	HEERY	Ai3 Architects LLC	Bacon-Agostini Construction Joint Venture	Bard, Rao + Athanas Consulting Engineers, LLC
201300310505	Billerica	Billerica Memorial High School	Design Development	Core Program	New Construction	CM@R	Leftfield, LLC	Perkins+Will	Shawmut Design and Construction	RDK Engineers
201508050605	Blackstone Valley Reg	Blackstone Valley	Construction	Accelerated Repair	Roof		Watermark Environmental, Inc.	Russo Barr Associates, Inc.	Silktown Roofing	Gale Associates, Inc.
201206220505	Blackstone-Millville	Blackstone Millville RHS	Final Audit Approved	Accelerated Repair	Roof	DBB	Arcadis U.S., Inc.	DiMarinisi & Wolfe Architects Urban Designers	-	Gale Associates, Inc.
201306220010	Blackstone-Millville	Millville Elem	Closeout	Accelerated Repair	Roof	DBB	Pinck & Co., Inc.	CBI Consulting Inc.	MDM Engineering	Simpson Gumpertz & Heger Inc.
201508060605	Blue Hills Voc	Blue Hills Reg Voc Tech	Schematic Design	Core Program	Addition / Renovation		Dore & Whittier Management Partners, Inc.	Drumrey Rosane Anderson, Inc.	-	-
201300350546	Boston	Boston Arts Academy	Feasibility Study	Core Program			PMA Construction Services	Perkins Eastman/DPC	-	-
201600350560	Boston	Boston Latin	Approved Project Vote Pending	Accelerated Repair	Boiler		NV5 (fka Joslin, Lesser + Associates Inc.)	ICON architecture, inc.	-	Rist-Frost-Shumway Engineering, P.C.
201500350052	Boston	Charles Sumner	Construction	Accelerated Repair	Windows / Doors		P3 Inc.	Dietz & Company Architects, Inc.	-	Simpson Gumpertz & Heger Inc.

201500350020	Boston	Curley K-8 School	Construction	Accelerated Repair	Windows / Doors		P3 Inc.	Dietz & Company Architects, Inc.	-	Simpson Gumpertz & Heger Inc.
201500350072	Boston	David A Ellis	Construction	Accelerated Repair	Windows / Doors		P3 Inc.	Dietz & Company Architects, Inc.	-	Simpson Gumpertz & Heger Inc.
201500350080	Boston	Donald Mckay	Construction	Accelerated Repair	Windows / Doors		P3 Inc.	Dietz & Company Architects, Inc.	-	Simpson Gumpertz & Heger Inc.
201500350651	Boston	Dorchester Academy	Construction	Accelerated Repair	Windows / Doors		P3 Inc.	Dietz & Company Architects, Inc.	-	Simpson Gumpertz & Heger Inc.
201500350415	Boston	Grover Cleveland	Construction	Accelerated Repair	Windows / Doors		P3 Inc.	Dietz & Company Architects, Inc.	-	Simpson Gumpertz & Heger Inc.
201000350074	Boston	Henry Dearborn Middle School	Construction	Core Program	New Construction	CM@R	Daedalus Projects Inc	Jonathan Levi Architects LLC	Gilbane Building Company	Symmes, Maini & McKee Associates
201600350146	Boston	James Condon Elem	Approved Project Vote Pending	Accelerated Repair	Boiler		NV5 (fka Joslin, Lesser + Associates Inc.)	ICON architecture, inc.	-	Rist-Frost-Shumway Engineering, P.C.
201600350179	Boston	John W McCormack	Approved Project Vote Pending	Accelerated Repair	Roof		NV5 (fka Joslin, Lesser + Associates Inc.)	ICON architecture, inc.	-	Simpson Gumpertz & Heger Inc.
201600350268	Boston	Paul A Dever	Approved Project Vote Pending	Accelerated Repair	Roof		NV5 (fka Joslin, Lesser + Associates Inc.)	ICON architecture, inc.	-	Simpson Gumpertz & Heger Inc.
201000350565	Boston	Quincy Upper School	Schematic Design	Core Program			Skanska USA Building, Inc	HMFH Architects, Inc.	-	-
201600350360	Boston	William Ellery Channing	Approved Project Vote Pending	Accelerated Repair	Boiler		NV5 (fka Joslin, Lesser + Associates Inc.)	ICON architecture, inc.	-	Rist-Frost-Shumway Engineering, P.C.
201500350380	Boston	Young Achievers	Construction	Accelerated Repair	Windows / Doors		P3 Inc.	Dietz & Company Architects, Inc.	-	Simpson Gumpertz & Heger Inc.
201400360010	Bourne	James F Peebles Elem	Design Development	Core Program	New Construction		Symmes Maini & McKee Associates, Inc.	Flansburgh Associates, Inc.	-	BVH Integrated Services, P.C.
201600380013	Boxford	Spofford Pond	Schematic Design	Accelerated Repair	Roof, Windows / Doors		NETCO Construction Project Managers, Inc.	Russo Barr Associates, Inc.	-	CBI Consulting Inc.
201300400305	Braintree	East Middle School	Schematic Design	Core Program			Hill International Company	Miller Dyer Spears Inc.	-	-
201600400310	Braintree	South Middle School	Eligibility Period	Core Program			-	-	-	-
201206250320	Bridgewater-Raynham	Bridgewater Middle School	Final Audit Approved	Accelerated Repair	Roof	DBB	Vertex Construction Services	-	-	CBI Consulting Inc.
201206250050	Bridgewater-Raynham	Laliberte Elementary School	Final Audit Approved	Accelerated Repair	Roof	DBB	Vertex Construction Services	Raymond Design Associates, Inc.	-	CBI Consulting Inc.
201206250020	Bridgewater-Raynham	Merrill Elementary School	Final Audit Approved	Accelerated Repair	Roof	DBB	Vertex Construction Services	Raymond Design Associates, Inc.	-	CBI Consulting Inc.
201606250002	Bridgewater-Raynham	Mitchell Elementary School	Eligibility Period	Core Program			-	-	-	-
201409100705	Bristol County Agr	Bristol County Agr High	Feasibility Study	Core Program			Colliers International	HMFH Architects, Inc.	-	-
201400440421	Brockton	Ashfield Middle School	Construction	Accelerated Repair	Roof, Boiler		Architectural Consulting Group, LLC	Tighe & Bond, Inc.	-	Rist-Frost-Shumway Engineering, P.C. Simpson Gumpertz & Heger Inc.
201400440080	Brockton	Barrett Russell School	Building Complete	Accelerated Repair	Windows / Doors		Architectural Consulting Group, LLC	Tighe & Bond, Inc.	Reliable Roofing and Sheet Metal, LLC	Simpson Gumpertz & Heger Inc.
201400440010	Brockton	Brookfield	Construction	Accelerated Repair	Roof		Architectural Consulting Group, LLC	Tighe & Bond, Inc.	-	Simpson Gumpertz & Heger Inc.
201400440035	Brockton	Gilmore	Construction	Accelerated Repair	Roof, Boiler		Architectural Consulting Group, LLC	Tighe & Bond, Inc.	-	Rist-Frost-Shumway Engineering, P.C. Simpson Gumpertz & Heger Inc.
201100460015	Brookline	Edward Devotion	Construction	Core Program	Addition / Renovation	CM@R	Town Employee	HMFH Architects, Inc.	Shawmut Design and Construction	Consulting Engineering Services, LLC
201500490090	Cambridge	Fletcher/Maynard Academy	Building Complete	Accelerated Repair	Boiler		Skanska USA Building, Inc	Tai Soo Kim Partners, LLC	CAM HVAC & Construction, Inc.	Fitzemeyer & Tocci Associates, Inc.
201600490090	Cambridge	Fletcher/Maynard Academy	Design Development	Accelerated Repair	Roof		Arcadis U.S., Inc.	HAKS Engineers, P.C.	-	Gale Associates, Inc.
201500490040	Cambridge	Kennedy-Longfellow	Building Complete	Accelerated Repair	Roof		Skanska USA Building, Inc	Tai Soo Kim Partners, LLC	Greenwood Industries, Inc.	Thompson & Lichtner Co., Inc.
201200500012	Canton	Lt Peter M Hansen	Final Audit Approved	Accelerated Repair	Windows / Doors	DBB	Vertex Construction Services	CSS Architects Incorporated	Lockheed Window Corporations	Simpson Gumpertz & Heger Inc.

201600500012	Canton	Lt Peter M Hansen	Approved Project Vote Pending	Accelerated Repair	Roof		Watermark Environmental, Inc.	Kaestle Boos Associates, Inc.	-	Simpson Gumpertz & Heger Inc.
201200500305	Canton	Wm H Galvin Middle	Final Audit Approved	Accelerated Repair	Windows / Doors	DBB	Vertex Construction Services	CSS Architects Incorporated	Lockheed Window Corporations	Simpson Gumpertz & Heger Inc.
201408150605	Cape Cod Region Voc Tech	Cape Cod Region Voc Tech	Schematic Design	Core Program			Colliers International	Drummeys Rosane Anderson, Inc.	-	-
201300520015	Carver	Carver Elementary School	Construction	Core Program	New Construction		PMA Construction Services	HMFH Architects, Inc.	CTA Construction Co., Inc.	Symmes, Maini & McKee Associates
201600520405	Carver	Carver Middle/High School	Construction	Accelerated Repair	Roof, Windows / Doors, Boiler		Leftfield, LLC	Johnson Roberts Associates, Inc.	-	Symmes, Maini & McKee Associates
201506350505	Central Berkshire	Wahconah Regional High	Eligibility Period	Core Program			-	-	-	-
200800570050	Chelsea	Clark Avenue School	Construction	Core Program	New Construction	CM@R	Pinck & Co., Inc.	HMFH Architects, Inc.	W. T. Rich Company Inc.	Cannon Design
201500610010	Chicopee	Belcher	Construction	Accelerated Repair	Roof		NV5 (fka Joslin, Lesser + Associates Inc.)	Kaestle Boos Associates, Inc.	J.D. Rivet & Co., Inc.	Building Enclosure Associates, LLC
201600610015	Chicopee	Bowe	Design Development	Accelerated Repair	Windows / Doors		Compass Project Management, Inc.	Turowski2 Architecture, Inc.	-	Thompson & Lichtner Co., Inc.
200900610021	Chicopee	Chicopee Academy	Building Complete	Core Program	Renovation	DBB	Arcadis U.S., Inc.	Caolo & Bieniek Associates, Inc.	Fontaine Brothers, Inc.	Symmes, Maini & McKee Associates
201500610310	Chicopee	Fairview Middle	Construction	Accelerated Repair	Roof		NV5 (fka Joslin, Lesser + Associates Inc.)	Kaestle Boos Associates, Inc.	J.D. Rivet & Co., Inc.	Building Enclosure Associates, LLC
201600610050	Chicopee	Selser	Design Development	Accelerated Repair	Roof		Compass Project Management, Inc.	Turowski2 Architecture, Inc.	-	Thompson & Lichtner Co., Inc.
201400630010	Clarksburg	Clarksburg Elementary	Feasibility Study	Core Program			Potomac Capital Advisors	Jones Whitsett Architects, Inc.	-	-
200906400505	Concord-Carlisle	Concord-Carlisle Regional High School	Closeout	Core Program	New Construction	CM@R	KV Associates, Inc.	OMR Architects, Inc.	Turner Construction Company	Colliers International
200800710505	Danvers	Danvers High School	Final Audit Approved	Core Program	Addition / Renovation	DBB	Construction Monitoring Services, Inc.	DiNisco Design, Inc.	Bacon Construction Co, Inc.	Turner Facilities Management Solutions
201500710032	Danvers	Ivan G Smith	OPM Selection	Core Program			-	-	-	-
201600720050	Dartmouth	Dartmouth Middle	Design Development	Accelerated Repair	Roof		Atlantic Construction and Management, Inc.	CSS Architects Incorporated	-	CBI Consulting Inc.
201400720030	Dartmouth	George H Potter	Final Audit Approved	Accelerated Repair	Roof		Pinck & Co., Inc.	Russo Barr Associates, Inc.	Greenwood Industries, Inc.	Gale Associates, Inc.
201200730005	Dedham	Early Childhood Center	Design Development	Core Program	New Construction	DBB	Construction Monitoring Services, Inc.	Knight, Bagge & Anderson, Inc.	C.J. Marbardy, Inc.	Symmes, Maini & McKee Associates
201500740015	Deerfield	Deerfield Elem	Building Complete	Accelerated Repair	Roof		Pinck & Co., Inc.	Raymond Design Associates, Inc.	MDM Engineering	Russo Barr Associates, Inc.
201506450305	Dennis-Yarmouth	Mattacheese Middle Sch	Designer Selection	Core Program			-	-	-	-
201306500305	Dighton-Rehoboth	Dighton Middle School	Final Audit Approved	Accelerated Repair	Roof	DBB	Arcadis U.S., Inc.	Dietz & Company Architects, Inc.	MDM Engineering	Gale Associates, Inc.
200800770010	Douglas	Douglas Elementary	Final Audit Approved	Core Program	New Construction - Model School	DBB	HEERY	DiNisco Design, Inc.	CTA Construction Co., Inc.	Consulting Engineering Services, LLC
200800770100G	Douglas	Douglas Intermediate Elementary School	Final Audit Approved	Green Repair	Roof, Windows / Doors, Boiler	DBB	HEERY	DiNisco Design, Inc.	CTA Construction Co., Inc.	Consulting Engineering Services, LLC
200800790505	Dracut	Dracut Senior High School	Building Complete	Core Program	Addition / Renovation	DBB	Hill International Company	Mount Vernon Group Architects, Inc.	CTA Construction Co., Inc.	RDk Engineers
201000820505	Duxbury	Duxbury High School	Closeout	Core Program	New Construction - Model School	CM@R	KV Associates, Inc.	Mount Vernon Group Architects, Inc.	Dimeo Construction Company	WSP USA
200900830505	East Bridgewater	East Bridgewater High School	Final Audit Approved	Core Program	New Construction - Model School	DBB	Hill International Company	Ai3 Architects LLC	Fontaine Brothers, Inc.	Foreman Building Commissioning, LP
201400860010	Easthampton	Maple	Feasibility Study	Core Program			Colliers International	Caolo & Bieniek Associates, Inc.	-	-
201600880003	Easton	Center School	Eligibility Period				-	-	-	-
201300880020	Easton	Moreau Hall	Final Audit Approved	Accelerated Repair	Roof	DBB	Skanska USA Building, Inc	Baker/Wohl Architects, Inc.	Capeway Roofing Systems, Inc.	Gale Associates, Inc.
200809130705	Essex Agr Tech	Essex Agricultural and Technical High School	Closeout	Core Program	New Construction	CM@R	PMA Construction Services	Perkins Eastman/DPC	Gilbane Building Company	Turner Facilities Management Solutions

201400930028	Everett	George Keverian School	Feasibility Study	Core Program			Symmes Maini & McKee Associates, Inc.	Mount Vernon Group Architects, Inc.	-	-
201500940305	Fairhaven	Hastings Middle	Construction	Accelerated Repair	Roof		Potomac Capital Advisors	CGKV Architects, Inc.	Capeway Roofing Systems, Inc.	Gale Associates, Inc.
201400950505	Fall River	B M C Durfee High	Feasibility Study	Core Program			Leftfield, LLC	Ai3 Architects LLC	-	-
201400960405	Falmouth	Lawrence	Closeout	Accelerated Repair	Windows / Doors		PMA Construction Services	Civitects PC	GVW, Inc.	Gale Associates, Inc.
201600970016	Fitchburg	Crocker Elementary	Eligibility Period	Core Program			-	-	-	-
201500990015	Foxborough	Mabelle M Burrell	Designer Selection	Core Program			Colliers International	-	-	-
201501000305	Framingham	Fuller Middle	OPM Selection	Core Program			-	-	-	-
200901010505	Franklin	Franklin High School	Closeout	Core Program	New Construction - Model School	DBB	Daedalus Projects Inc	Ai3 Architects LLC	Bacon-Agostini Construction Joint Venture	Consulting Engineering Services, LLC
201408180605	Franklin County	Franklin County Tech	Building Complete	Accelerated Repair	Windows / Doors		Colliers International	Habeeb & Associates Architects, Inc.	Gardner Construction & Industrial Services	CBI Consulting Inc.
201401030001	Gardner	Elm Street School	Closeout	Accelerated Repair	Windows / Doors, Boiler		Hill International Company	ICON architecture, inc.	Lockheed Window Corporations	Fitzemeyer & Tocci Associates, Inc. Thompson & Lichtner Co., Inc.
201601030020	Gardner	Waterford Street	Eligibility Period	Core Program			-	-	-	-
200801050505	Georgetown	Georgetown Middle/High School	Closeout	Core Program	Renovation	DBB	Municipal Building Consultants, Inc.	Drumme Rosane Anderson, Inc.	L.D. Russo, Inc.	WSP USA
200901050010	Georgetown	Penn Brook Elementary School	Building Complete	Core Program	New Construction	DBB	Municipal Building Consultants, Inc.	Drumme Rosane Anderson, Inc.	Brait Builders Corp.	Rist-Frost-Shumway Engineering, P.C.
201406740050	Gill-Montague	Sheffield Elementary	Closeout	Accelerated Repair	Windows / Doors, Boiler		NETCO Construction Project Managers, Inc.	The S/L/A/M Collaborative	Gardner Construction & Industrial Services	CBI Consulting Inc.
201601070020	Gloucester	East Gloucester Elem	Eligibility Period				-	-	-	-
201601070505	Gloucester	Gloucester High	Design Development	Accelerated Repair	Roof		P3 Inc.	Baker/Wohl Architects, Inc.	-	CBI Consulting Inc.
200901070050	Gloucester	West Parish Elementary School	Building Complete	Core Program	New Construction	CM@R	Knight, Bagge & Anderson Inc.	Dore & Whittier Architects, Inc.	W. T. Rich Company Inc.	Fitzemeyer & Tocci Associates, Inc.
201201110010	Granby	West St	Construction	Core Program	Addition / Renovation		Colliers International	Jones Whitsett Architects, Inc.	Fontaine Brothers, Inc.	Rist-Frost-Shumway Engineering, P.C.
201108230605	Greater Lawrence RVT	Gr Lawrence Reg Voc Tech	Final Audit Approved	Core Program	Repair	DBB	Vertex Construction Services	Richard D. Kimball Company, Inc.	E. Amanti & Sons, Inc.	WSP USA
200908280605	Greater Lowell Voc Tec	Greater Lowell Regional Technical High School	Closeout	Core Program	Addition / Renovation	CM@R	NV5 (fka Joslin, Lesser + Associates Inc.)	Knight, Bagge & Anderson, Inc.	Consigli Construction Company, Inc.	Horizon Engineering Associates, LLP
201008250605	Greater New Bedford	Greater New Bedford Vocational Technical High School	Final Audit Approved	Core Program	Addition / Renovation	DBB	Construction Monitoring Services, Inc.	Drumme Rosane Anderson, Inc.	Agostini Construction Co., Inc.	Symmes, Maini & McKee Associates
201501140010	Greenfield	Federal	Construction	Accelerated Repair	Roof, Windows / Doors, Boiler		-	-	-	Colliers International
201401140030	Greenfield	Green River	Closeout	Accelerated Repair	Roof, Windows / Doors, Boiler		Arcadis U.S., Inc.	Baker/Wohl Architects, Inc.	RAC Builders, Inc.	CBI Consulting Inc.
200901140505	Greenfield	Greenfield High School	Closeout	Core Program	New Construction	CM@R	Construction Monitoring Services, Inc.	Dore & Whittier Architects, Inc.	Shawmut Design and Construction	BVH Integrated Services, P.C.
201601180005	Halifax	Halifax Elementary	Approved Project Vote Pending	Accelerated Repair	Roof, Windows / Doors		Vertex Construction Services	Habeeb & Associates Architects, Inc.	-	Russo Barr Associates, Inc.
201306750015	Hamilton-Wenham	Winthrop School	Final Audit Approved	Accelerated Repair	Windows / Doors, Boiler	DBB	NETCO Construction Project Managers, Inc.	Habeeb & Associates Architects, Inc.	E. Amanti & Sons, Inc.	CBI Consulting Inc. Colliers International
201406800030	Hampden-Wilbraham	Soule Road	Final Audit Approved	Accelerated Repair	Windows / Doors		exPERTcon, Inc.	The S/L/A/M Collaborative	-	-
201301220015	Hanover	Sylvester	Design Development	Core Program	Addition / Renovation		P3 Inc.	Mount Vernon Group Architects, Inc.	-	Horizon Engineering Associates, LLP
201501250005	Harvard	Harvard Elementary	Feasibility Study	Core Program			NV5 (fka Joslin, Lesser + Associates Inc.)	Arrowstreet Inc.	-	-
201201280035	Haverhill	Caleb Dustin Hunking	Building Complete	Core Program	New Construction	CM@R	NV5 (fka Joslin, Lesser + Associates Inc.)	JCJ Architecture, PC	Shawmut Design and Construction	Colliers International
201101280100G	Haverhill	Consentino	Closeout	Green Repair	Windows / Doors	DBB	Vertex Construction Services	CSS Architects Incorporated	New England Builders & Contractors, Inc.	RDK Engineers Russo Barr Associates, Inc.



201101280085G	Haverhill	John G Whittier	Closeout	Green Repair	Windows / Doors	DBB	Vertex Construction Services	CSS Architects Incorporated	New England Builders & Contractors, Inc.	Russo Barr Associates, Inc.
201101280075G	Haverhill	Tilton	Closeout	Green Repair	Roof	DBB	Vertex Construction Services	CSS Architects Incorporated	Titan Roofing, Inc.	Russo Barr Associates, Inc.
201101280080G	Haverhill	Walnut Square	Closeout	Green Repair	Roof, Windows / Doors	DBB	Vertex Construction Services	CSS Architects Incorporated	Titan Roofing, Inc.	RDK Engineers Russo Barr Associates, Inc.
201001310410	Hingham	Hingham Middle School	Closeout	Core Program	New Construction - Model School	DBB	Knight, Bagge & Anderson Inc.	Ai3 Architects LLC	Brait Builders Corp.	Foreman Building Commissioning, LP
200801330505	Holbrook	Holbrook Junior-Senior High School	Construction	Core Program	New Construction	CM@R	Symmes Maini & McKee Associates, Inc.	Flansburgh Associates, Inc.	Consigli Construction Company, Inc.	Consulting Engineering Services, LLC
201401370045	Holyoke	E N White Elem	Building Complete	Accelerated Repair	Boiler		STV DPM (fka STV Inc.)	Richard D. Kimball Company, Inc.	Adams Plumbing and Heating, Inc.	BVH Integrated Services, P.C.
201201370015	Holyoke	Lt Elmer J McMahon Elem	OPM Selection	Core Program			-	-	-	-
201401370025	Holyoke	Morgan Elem	Building Complete	Accelerated Repair	Boiler		STV DPM (fka STV Inc.)	Richard D. Kimball Company, Inc.	Adams Plumbing and Heating, Inc.	BVH Integrated Services, P.C.
201201370605	Holyoke	Wm J Dean Voc Tech High	Closeout	Science Lab Initiative	Addition / Renovation	DBB	Skanska USA Building, Inc	Kaestle Boos Associates, Inc.	RAC Builders, Inc.	BVH Integrated Services, P.C.
201301390005	Hopkinton	Center	Construction	Core Program	New Construction	CM@R	Compass Project Management, Inc.	Drumrey Rosane Anderson, Inc.	Colantonio, Inc.	RDK Engineers
200801410410	Hudson	John F. Kennedy Middle School	Closeout	Core Program	New Construction	DBB	PMA Construction Services	OMR Architects, Inc.	Bacon-Agostini Construction Joint Venture	WSP USA
201401410007	Hudson	Mulready Elementary	Closeout	Accelerated Repair	Roof		Atlantic Construction and Management, Inc.	Raymond Design Associates, Inc.	Capeway Roofing Systems, Inc.	CBI Consulting Inc.
201401440015	Ipswich	Winthrop	Schematic Design	Core Program			PMA Construction Services	Perkins Eastman/DPC	-	-
201601490050	Lawrence	Henry K Oliver	Eligibility Period				-	-	-	-
201601490536	Lawrence	High School Learning Center	Design Development	Accelerated Repair	Boiler		Pinck & Co., Inc.	Shekar & Associates, Inc.	-	Fitzmeyer & Tocci Associates, Inc.
201501510505	Leicester	Leicester High	Construction	Accelerated Repair	Roof		Hill International Company	Gale Associates, Inc.	Greenwood Industries, Inc.	Russo Barr Associates, Inc.
201601510015	Leicester	Leicester Middle	Eligibility Period	Core Program			-	-	-	-
201501530025	Leominster	Johnny Appleseed	Construction	Accelerated Repair	Roof, Windows / Doors		NETCO Construction Project Managers, Inc.	Habeeb & Associates Architects, Inc.	Greenwood Industries, Inc.	Russo Barr Associates, Inc.
201401530030	Leominster	Northwest	Closeout	Accelerated Repair	Roof		Architectural Consulting Group, LLC	Gale Associates, Inc.	Greenwood Industries, Inc.	Building Enclosure Associates, LLC
201501550035	Lexington	Maria Hastings	Schematic Design	Core Program	New Construction		Dore & Whittier Management Partners, Inc.	DiNisco Design, Inc.	-	-
201401600505	Lowell	Lowell High	Feasibility Study	Core Program			Skanska USA Building, Inc	Perkins Eastman/DPC	-	-
201501610020	Ludlow	Chapin Street Elementary School	Designer Selection	Core Program			-	-	-	-
201501610010	Ludlow	East Street Elementary School	Building Complete	Accelerated Repair	Roof, Boiler		STV DPM (fka STV Inc.)	Johnson Roberts Associates, Inc.	Westfield Construction Co., Inc.	Colliers International
201001620505	Lunenburg	Lunenburg High School	Building Complete	Core Program	New Construction	CM@R	NV5 (fka Joslin, Lesser + Associates Inc.)	Tappe Associates, Inc.	Shawmut Design and Construction	Cannon Design
201401630045	Lynn	E J Harrington	Closeout	Accelerated Repair	Roof		NETCO Construction Project Managers, Inc.	Habeeb & Associates Architects, Inc.	Capeway Roofing Systems, Inc.	CBI Consulting Inc.
201401630420	Lynn	Pickering Middle	Approved Project Vote Pending	Core Program			Leftfield, LLC	Raymond Design Associates, Inc.	-	-
200901630305	Lynn	Thurgood Marshall Middle School	Closeout	Core Program	New Construction	CM@R	NV5 (fka Joslin, Lesser + Associates Inc.)	Raymond Design Associates, Inc.	Walsh Brothers, Inc.	Rist-Frost-Shumway Engineering, P.C.
201401630040	Lynn	Wm P Connery	Final Audit Approved	Accelerated Repair	Roof		NETCO Construction Project Managers, Inc.	Habeeb & Associates Architects, Inc.	Gibson Roofs, Inc.	CBI Consulting Inc.
201506980010	Manchester Essex Regional	Manchester Memorial Elementary	Designer Selection	Core Program			-	-	-	-
201501680015	Marblehead	Elbridge Gerry	OPM Selection	Core Program			-	-	-	-

201501700025	Marlborough	Richer	Feasibility Study	Core Program			Daedalus Projects Inc	Lamoureux Pagano & Associates, Inc.	-	-
201601710310	Marshfield	Furnace Brook Middle	Approved Project Vote Pending	Accelerated Repair	Roof		Potomac Capital Advisors	Civitects PC	-	Russo Barr Associates, Inc.
201101710505	Marshfield	Marshfield High	Closeout	Core Program	New Construction - Model School	DBB	Compass Project Management, Inc.	Ai3 Architects LLC	Brait Builders Ventures	Sebesta Blomberg & Associates, Inc.
201601720035	Mashpee	Quashnet School	Schematic Design	Accelerated Repair	Windows / Doors		exPERTcon, Inc.	Raymond Design Associates, Inc.	-	CBI Consulting Inc.
201401750007	Medfield	Ralph Wheelock School	Building Complete	Accelerated Repair	Boiler		-	-	Performance Plumbing and Heating	RDK Engineers
201301760505	Medford	Medford High	Closeout	Accelerated Repair	Windows / Doors, Boiler	DBB	Architectural Consulting Group, LLC	Dietz & Company Architects, Inc.	NB Kenney Company, Inc	Symmes, Maini & McKee Associates
201401770013	Medway	John D Mc Govern Elem	Final Audit Approved	Accelerated Repair	Windows / Doors		Arcadis U.S., Inc.	CBI Consulting Inc.	-	Russo Barr Associates, Inc.
201401780017	Melrose	Herbert Clark Hoover	Construction	Accelerated Repair	Windows / Doors		Colliers International	ICON architecture, inc.	GVW, Inc.	Simpson Gumpertz & Heger Inc.
200801810505	Methuen	Methuen High School	Closeout	Core Program	Addition / Renovation	CM@R	KBA/Trident	Finegold Alexander and Associates Inc.	Consigli Construction Company, Inc.	Environmental Health and Engineering
201501820011	Middleborough	Memorial Early Childhood Center	Construction	Accelerated Repair	Roof		Architectural Consulting Group, LLC	Knight, Bagge & Anderson, Inc.	MDM Engineering	Russo Barr Associates, Inc.
201401820505	Middleborough	Middleborough High	Feasibility Study	Core Program			Compass Project Management, Inc.	Drumrey Rosane Anderson, Inc.	-	-
201401840003	Middleton	Fuller Meadow	Closeout	Accelerated Repair	Roof		Hill International Company	CBI Consulting Inc.	-	Building Enclosure Associates, LLC
201101850090	Milford	Woodland	Building Complete	Core Program	New Construction	CM@R	NV5 (fka Joslin, Lesser + Associates Inc.)	HMFH Architects, Inc.	Shawmut Design and Construction	Consulting Engineering Services, LLC
201601860025	Millbury	Raymond E. Shaw Elementary	Eligibility Period	Core Program			-	-	-	-
201401870005	Millis	Clyde F Brown	Schematic Design	Core Program	New Construction		Compass Project Management, Inc.	Tappe Associates, Inc.	-	-
200908300605	Minuteman Voc Tech	Minuteman Regional High School	Design Development	Core Program	New Construction		Skanska USA Building, Inc	Kaestle Boos Associates, Inc.	-	Bard, Rao + Athanas Consulting Engineers, LLC
201107129999	Monomoy	Monomoy Regional High School	Closeout	Core Program	New Construction - Model School	DBB	Skanska USA Building, Inc	Mount Vernon Group Architects, Inc.	Fontaine Brothers, Inc.	Sebesta Blomberg & Associates, Inc.
201307150505	Mount Greylock	Mt Greylock Reg High	Construction	Core Program	Addition / Renovation	CM@R	Dore & Whittier Management Partners, Inc.	Perkins Eastman/DPC	Turner Construction Company	BVH Integrated Services, P.C.
200807200020	Narragansett	Templeton Center School	Design Development	Core Program			Colliers International	Symmes Maini & McKee Associates, Inc.	-	Fitzmeyer & Tocci Associates, Inc.
200807250015	Nashoba	Pompositticut Elementary School	Final Audit Approved	Core Program	Addition / Renovation	DBB	Construction Monitoring Services, Inc.	Symmes Maini & McKee Associates, Inc.	P.J. Stella Construction Corp.	Colliers International
201501980305	Natick	J F Kennedy Middle Sch	Feasibility Study	Core Program			Compass Project Management, Inc.	-	-	-
201606600505	Nauset	Nauset Regional High	Eligibility Period	Core Program			-	-	-	-
201301990035	Needham	Hillside Elementary	Design Development	Core Program	New Construction	DBB	Town Employee	Dore & Whittier Architects, Inc.	-	Rist-Frost-Shumway Engineering, P.C.
201502010063	New Bedford	Alfred J Gomes	Construction	Accelerated Repair	Windows / Doors		Vertex Construction Services	-	-	CBI Consulting Inc.
201502010123	New Bedford	Casmir Pulaski	Construction	Accelerated Repair	Windows / Doors, Boiler		Vertex Construction Services	-	-	CBI Consulting Inc. WSP USA
201502010078	New Bedford	Hayden/McFadden	Construction	Accelerated Repair	Windows / Doors, Boiler		Vertex Construction Services	-	-	CBI Consulting Inc. WSP USA
201502010115	New Bedford	John Avery Parker	Closeout	Accelerated Repair	Windows / Doors, Boiler		Vertex Construction Services	-	-	-
201602010115	New Bedford	John Avery Parker	Approved Project Vote Pending	Accelerated Repair	Windows / Doors		Architectural Consulting Group, LLC	CBI Consulting Inc.	-	WSP USA
200902010070	New Bedford	John Hannigan	Construction	Core Program	New Construction	DBB	Daedalus Projects Inc	Turowski2 Architecture, Inc.	H.V. Collins Co., Inc.	WSP USA
201502010045	New Bedford	Sgt Wm H Carney Acad	Construction	Accelerated Repair	Windows / Doors		Vertex Construction Services	-	-	CBI Consulting Inc. WSP USA

W20100201999P2	New Bedford	Taylor School at the Sea Lab Marine Science Education Center	Building Complete	Waitlist	Addition / Renovation	DBB	Architectural Consulting Group, LLC	Mount Vernon Group Architects, Inc.	M. O'Connor Contracting, Inc.	WSP USA
201102040005	Newburyport	Francis T Bresnahan Elem	Final Audit Approved	Core Program	New Construction - Model School	DBB	HEERY	HMFH Architects, Inc.	CTA Construction Co., Inc.	Fitzemeyer & Tocci Associates, Inc.
201002040305	Newburyport	Rupert A. Nock Middle School	Closeout	Core Program	Addition / Renovation	CM@R	HEERY	Miller Dyer Spears Inc.	Gilbane Building Company	Fitzemeyer & Tocci Associates, Inc.
201102070005	Newton	A E Angier	Building Complete	Core Program	New Construction	CM@R	NV5 (fka Joslin, Lesser + Associates Inc.)	DiNisco Design, Inc.	W. T. Rich Company Inc.	Fitzemeyer & Tocci Associates, Inc.
201302070025	Newton	Cabot	Design Development	Core Program		CM@R	NV5 (fka Joslin, Lesser + Associates Inc.)	DiNisco Design, Inc.	W. T. Rich Company Inc.	Colliers International
200802080005	Norfolk	Freeman-Kennedy Elementary School	Closeout	Core Program	New Construction	DBB	NV5 (fka Joslin, Lesser + Associates Inc.)	Flansburgh Associates, Inc.	Fontaine Brothers, Inc.	WSP USA
200909150705	Norfolk County Agriculture	Norfolk County Agr	Final Audit Approved	Core Program	Addition / Renovation	DBB	Compass Project Management, Inc.	Turowski2 Architecture, Inc.	Brait Builders Corp.	Rist-Frost-Shumway Engineering, P.C.
200802090305	North Adams	Silvio O Conte Middle School	Closeout	Core Program	Addition / Renovation	DBB	Colliers International	Jones Whitsett Architects, Inc.	PDS Engineering and Construction, Inc.	Rist-Frost-Shumway Engineering, P.C.
201402120015	North Attleborough	Roosevelt Avenue	Final Audit Approved	Accelerated Repair	Boiler		Pinck & Co., Inc.	Consulting Engineering Services, LLC	Falite Brothers Inc.	Bard, Rao + Athanas Consulting Engineers, LLC
201602150015	North Brookfield	North Brookfield Elem	Approved Project Vote Pending	Accelerated Repair	Roof		Skanska USA Building, Inc	Dietz & Company Architects, Inc.	-	Simpson Gumpertz & Heger Inc.
201607350030	North Middlesex	Hawthorne Brook	Schematic Design	Accelerated Repair			Atlantic Construction and Management, Inc.	Habeeb & Associates Architects, Inc.	-	-
201107350505	North Middlesex	North Middlesex Reg	Construction	Core Program	New Construction	DBB	HEERY	Symmes Maini & McKee Associates, Inc.	CTA Construction Co., Inc.	Horizon Engineering Associates, LLP
201607350020	North Middlesex	Squannacook	Schematic Design	Accelerated Repair			Atlantic Construction and Management, Inc.	Habeeb & Associates Architects, Inc.	-	-
201607350035	North Middlesex	Varnum Brook	Schematic Design	Accelerated Repair			Atlantic Construction and Management, Inc.	Habeeb & Associates Architects, Inc.	-	-
201502170003	North Reading	E Ethel Little School	Building Complete	Accelerated Repair	Roof		Compass Project Management, Inc.	HAKS Engineers, P.C.	Stanley Roofing Company, Inc.	Thompson & Lichtner Co., Inc.
201002170505	North Reading	North Reading High School	Building Complete	Core Program	Addition / Renovation	CM@R	PMA Construction Services	Dore & Whittier Architects, Inc.	Gilbane Building Company	Cannon Design
201602100005	Northampton	Bridge Street	Approved Project Vote Pending	Accelerated Repair	Roof		Colliers International	The S/L/A/M Collaborative	-	CBI Consulting Inc.
201402100025	Northampton	Leeds	Final Audit Approved	Accelerated Repair	Roof		STV DPM (fka STV Inc.)	Raymond Design Associates, Inc.	R & H Roofing, LLP	Russo Barr Associates, Inc.
201602100025	Northampton	Leeds	Approved Project Vote Pending	Accelerated Repair	Roof		Colliers International	The S/L/A/M Collaborative	-	CBI Consulting Inc.
201402100029	Northampton	R. K. Finn Ryan Road	Final Audit Approved	Accelerated Repair	Roof		STV DPM (fka STV Inc.)	Raymond Design Associates, Inc.	R & H Roofing, LLP	Russo Barr Associates, Inc.
201102130003	Northborough	Lincoln Street	Building Complete	Core Program	Addition / Renovation	DBB	Colliers International	Lamoureux Pagano & Associates, Inc.	Brait Builders Corp.	Fitzemeyer & Tocci Associates, Inc.
201502140001	Northbridge	W Edward Balmer	OPM Selection	Core Program			-	-	-	-
200902180505	Norton	Norton High School	Final Audit Approved	Core Program	Addition / Renovation	CM@R	Pinck & Co., Inc.	JCJ Architecture, PC	W. T. Rich Company Inc.	Rist-Frost-Shumway Engineering, P.C.
201402200010	Norwood	Cornelius M Callahan	Final Audit Approved	Accelerated Repair	Boiler		PMA Construction Services	Consulting Engineering Services, LLC	George T. Wilkinson, Inc.	Symmes, Maini & McKee Associates
201602230010	Orange	Dexter Park	Eligibility Period				-	-	-	-
201402240005	Orleans	Orleans Elementary	Construction	Accelerated Repair	Windows / Doors		Architectural Consulting Group, LLC	Tighe & Bond, Inc.	RAC Builders, Inc.	Gale Associates, Inc.
200802260405	Oxford	Oxford Middle School	Closeout	Core Program	Repair	DBB	Diversified Project Management	CGKV Architects, Inc.	J.J. Cardosi, Inc.	Cannon Design
201308600605	Pathfinder Voc Tech	Pathfinder Voc Tech	Final Audit Approved	Accelerated Repair	Roof	DBB	exPERTcon, Inc.	Baker/Wohl Architects, Inc.	Allied Restoration Corporation	Building Enclosure Associates, LLC
200802290305	Peabody	Higgins Middle School	Building Complete	Core Program	New Construction	DBB	Daedalus Projects Inc	DiNisco Design, Inc.	Bacon-Agostini Construction Joint Venture	BVH Integrated Services, P.C.
201402290016	Peabody	John E. McCarthy	Building Complete	Accelerated Repair	Roof, Windows / Doors		Hill International Company	Civitects PC	-	Thompson & Lichtner Co., Inc.

201502290510	Peabody	Peabody Veterans Memorial High	Design Development	Accelerated Repair	Roof		Municipal Building Consultants, Inc.	Civitects PC	-		Thompson & Lichtner Co., Inc.
201302310010	Pembroke	Hobomock Elementary	Closeout	Accelerated Repair	Roof	DBB	Pinck & Co., Inc.	The S/L/A/M Collaborative	Greenwood Industries, Inc.		CBI Consulting Inc.
201302310015	Pembroke	North Pembroke Elem	Closeout	Accelerated Repair	Roof	DBB	Pinck & Co., Inc.	The S/L/A/M Collaborative	Paul J. Rogan Co., Inc.		CBI Consulting Inc.
201302310305	Pembroke	Pembroke Community Middle School	Closeout	Accelerated Repair	Roof	DBB	Pinck & Co., Inc.	The S/L/A/M Collaborative	Paul J. Rogan Co., Inc.		CBI Consulting Inc.
201302310505	Pembroke	Pembroke High School	Closeout	Accelerated Repair	Roof	DBB	Pinck & Co., Inc.	The S/L/A/M Collaborative	Greenwood Industries, Inc.		CBI Consulting Inc.
201507450505	Pentucket	Pentucket Reg Sr High	OPM Selection	Core Program			-	-	-		-
201002360510	Pittsfield	Taconic High School	Construction	Core Program	New Construction	CM@R	Skanska USA Building, Inc	Drumme Rosane Anderson, Inc.	Gilbane Building Company		Colliers International
201202390515	Plymouth	Plymouth South High	Construction	Core Program	New Construction	DBB	Ted Gentry Associates, Inc	Ai3 Architects LLC	Bacon-Agostini Construction Joint Venture		Rist-Frost-Shumway Engineering, P.C.
201302420505	Provincetown	Provincetown High	Building Complete	Core Program	Repair	DBB	Atlantic Construction and Management, Inc.	Raymond Design Associates, Inc.	E. Amanti & Sons, Inc.		BVH Integrated Services, P.C.
201607780505	Quaboag Regional	Quaboag Regional High	Closeout	Accelerated Repair	Boiler		NETCO Construction Project Managers, Inc.	-	-		-
201607780005	Quaboag Regional	Warren Elementary	Schematic Design	Accelerated Repair	Windows / Doors		NETCO Construction Project Managers, Inc.	-	-		-
201602430040	Quincy	Atherton Hough	Design Development	Accelerated Repair	Boiler		Hill International Company	Architectural Engineers, Inc.	-		Consulting Engineering Services, LLC
201502430020	Quincy	Beechwood Knoll Elem	Construction	Accelerated Repair	Roof, Windows / Doors		Atlantic Construction and Management, Inc.	Baker/Wohl Architects, Inc.	Alpha Contracting Associates, Inc.		CBI Consulting Inc.
201602430020	Quincy	Beechwood Knoll Elem	Design Development	Accelerated Repair	Boiler		Hill International Company	Architectural Engineers, Inc.	-		Consulting Engineering Services, LLC
201402430075	Quincy	Francis W Parker	Final Audit Approved	Accelerated Repair	Windows / Doors		PMA Construction Services	Russo Barr Associates, Inc.	Lockheed Window Corporations		Simpson Gumpertz & Heger Inc.
201402430035	Quincy	Lincoln-Hancock Comm Sch	Final Audit Approved	Accelerated Repair	Windows / Doors		PMA Construction Services	Russo Barr Associates, Inc.	Lockheed Window Corporations		Simpson Gumpertz & Heger Inc.
201302430060	Quincy	Merrymount	Final Audit Approved	Accelerated Repair	Windows / Doors	DBB	Skanska USA Building, Inc	Habeeb & Associates Architects, Inc.	Alpha Contracting Associates, Inc.		Simpson Gumpertz & Heger Inc.
201502430060	Quincy	Merrymount	Building Complete	Accelerated Repair	Roof		Atlantic Construction and Management, Inc.	Baker/Wohl Architects, Inc.	Gibson Roofs, Inc.		CBI Consulting Inc.
201602430060	Quincy	Merrymount	Design Development	Accelerated Repair	Boiler		Hill International Company	Architectural Engineers, Inc.	-		Consulting Engineering Services, LLC
201302430510	Quincy	North Quincy High	Final Audit Approved	Accelerated Repair	Windows / Doors	DBB	Skanska USA Building, Inc	Habeeb & Associates Architects, Inc.	GVW, Inc.		Simpson Gumpertz & Heger Inc.
201302430320	Quincy	Reay E Sterling Middle	Design Development	Core Program	New Construction		Potomac Capital Advisors	Ai3 Architects LLC	-		Symmes, Maini & McKee Associates
201302430110	Quincy	Wollaston School	Final Audit Approved	Accelerated Repair	Windows / Doors	DBB	Skanska USA Building, Inc	Habeeb & Associates Architects, Inc.	Northeast Energy Control Systems		Simpson Gumpertz & Heger Inc.
201602430110	Quincy	Wollaston School	Design Development	Accelerated Repair	Boiler		Hill International Company	Architectural Engineers, Inc.	-		Consulting Engineering Services, LLC
201402440018	Randolph	J F Kennedy Elem	Construction	Accelerated Repair	Windows / Doors		STV DPM (fka STV Inc.)	Taylor & Burns, Inc.	Modern Glass & Aluminum, Inc.		Gale Associates, Inc.
201402440505	Randolph	Randolph High	Construction	Accelerated Repair	Windows / Doors		STV DPM (fka STV Inc.)	Taylor & Burns, Inc.	A&A Window Products, Inc.		Gale Associates, Inc.
201502480056	Revere	Garfield Elementary School	Construction	Accelerated Repair	Roof		Leftfield, LLC	Turowski2 Architecture, Inc.	Greenwood Industries, Inc.		Thompson & Lichtner Co., Inc.
201602480057	Revere	Garfield Middle School	Design Development	Accelerated Repair	Boiler		-	-	-		Fitzemeyer & Tocci Associates, Inc.
201002480035	Revere	Staff Sergeant James J. Hill School	Building Complete	Core Program	New Construction	DBB	Hill International Company	Drumme Rosane Anderson, Inc.	CTA Construction Co., Inc.		Rist-Frost-Shumway Engineering, P.C.
201602510060	Rockland	Jefferson Elementary School	Eligibility Period	Core Program			-	-	-		-

200902580305G	Salem	Collins Middle School	Closeout	Green Repair	Roof, Windows / Doors, Boiler, Building Envelope	CM@R	KV Associates, Inc.	Reinhardt Associates, Inc.	Gilbane Building Company	Rist-Frost-Shumway Engineering, P.C.
201002580050G	Salem	Saltonstall School	Closeout	Green Repair	Roof, Windows / Doors, Boiler, Building Envelope	CM@R	KV Associates, Inc.	Reinhardt Associates, Inc.	Gilbane Building Company	Rist-Frost-Shumway Engineering, P.C.
201002620305	Saugus	Belmonte Middle School	Final Audit Approved	Core Program	Repair	CM@R	Skanska USA Building, Inc	Fletcher Thompson Architecture Engineering, LLC	Consigli Construction Company, Inc.	Consulting Engineering Services, LLC
201402620505	Saugus	Saugus High	Schematic Design	Core Program	New Construction		PMA Construction Services	HMFH Architects, Inc.	-	-
201202640305	Scituate	Gates Intermediate School	Construction	Core Program	New Construction	DBB	Daedalus Projects Inc	Dore & Whittier Architects, Inc.	Bacon-Agostini Construction Joint Venture	WSP USA
201602660015	Sharon	Heights Elementary	Approved Project Vote Pending	Accelerated Repair	Roof		Potomac Capital Advisors	Knight, Bagge & Anderson, Inc.	-	Simpson Gumpertz & Heger Inc.
201602660505	Sharon	Sharon High	Eligibility Period	Core Program			-	-	-	-
201502710005	Shrewsbury	Beal School	OPM Selection	Core Program			-	-	-	-
200802710305	Shrewsbury	Sherwood Middle School	Closeout	Core Program	New Construction	CM@R	PMA Construction Services	Lamoureux Pagano & Associates, Inc.	Gilbane Building Company	RDK Engineers
200811119999	Somerset-Berkley	Somerset-Berkley High	Closeout	Core Program	New Construction - Model School	DBB	Skanska USA Building, Inc	Ai3 Architects LLC	Bacon-Agostini Construction Joint Venture	Horizon Engineering Associates, LLP
200902740111E	Somerville	East Somerville Community School at Cummings	Closeout	Core Program	Renovation	CM@R	PMA Construction Services	Maguire Group Inc.	Gilbane Building Company	Foreman Building Commissioning, LP
201302740505	Somerville	Somerville High	Design Development	Core Program	Addition / Renovation		PMA Construction Services	Symmes Maini & McKee Associates, Inc.	-	-
201602740120	Somerville	Winter Hill Community	Schematic Design	Accelerated Repair	Roof, Windows / Doors		Municipal Building Consultants, Inc.	Tai Soo Kim Partners, LLC	-	-
200902780015	South Hadley	Plains School	Building Complete	Core Program	New Construction	DBB	Arcadis U.S., Inc.	Jones Whitsett Architects, Inc.	Fontaine Brothers, Inc.	Colliers International
201408730605	South Shore Reg Voc Tech	So Shore Voc Tech High	Final Audit Approved	Accelerated Repair	Boiler		exPERTcon, Inc.	Richard D. Kimball Company, Inc.	-	Consulting Engineering Services, LLC
201407650505	Southern Berkshire	Mt Everett Regional	Closeout	Accelerated Repair	Roof, Boiler		NETCO Construction Project Managers, Inc.	Dietz & Company Architects, Inc.	Titan Roofing, Inc.	Colliers International
200908760605	Southern Worcester Cty VT	Bay Path Regional Vocational Technical High School	Building Complete	Core Program	Addition / Renovation	CM@R	HEERY	Kaestle Boos Associates, Inc.	Consigli Construction Company, Inc.	RDK Engineers
201107660305	Southwick-Tolland	Powder Mill	Closeout	Core Program	Repair	DBB	Colliers International	JCJ Architecture, PC	PDS Engineering and Construction, Inc.	BVH Integrated Services, P.C.
201107660505	Southwick-Tolland	Southwick-Tolland Regional High	Closeout	Core Program	Addition / Renovation	DBB	Colliers International	JCJ Architecture, PC	Fontaine Brothers, Inc.	BVH Integrated Services, P.C.
200807660010	Southwick-Tolland	Woodland Elementary School	Closeout	Core Program	Addition / Renovation	DBB	Colliers International	JCJ Architecture, PC	PDS Engineering and Construction, Inc.	BVH Integrated Services, P.C.
201602810095	Springfield	Alfred G Zanetti	Design Development	Accelerated Repair	Windows / Doors		Leftfield, LLC	Gale Associates, Inc.	-	Building Enclosure Associates, LLC
201602810015	Springfield	Balliet Elementary School	Schematic Design	Accelerated Repair	Roof		Leftfield, LLC	Gale Associates, Inc.	-	-
201602810360	Springfield	Balliet Middle School	Schematic Design	Accelerated Repair	Windows / Doors		Leftfield, LLC	Gale Associates, Inc.	-	-
201502810025	Springfield	Brightwood	OPM Selection	Core Program			-	-	-	-
201302810310	Springfield	Chestnut Accelerated Middle School	Final Audit Approved	Accelerated Repair	Roof	DBB	Atlantic Construction and Management, Inc.	CBI Consulting Inc.	J.D. Rivet & Co., Inc.	Building Enclosure Associates, LLC
201502810035	Springfield	Daniel B Brunton	Construction	Accelerated Repair	Windows / Doors		Skanska USA Building, Inc	CBI Consulting Inc.	Five Star Building Corp.	Building Enclosure Associates, LLC
201102810030E	Springfield	Elias Brookings	Closeout	Core Program	New Construction	CM@R	Arcadis U.S., Inc.	Drumrey Rosane Anderson, Inc.	Morganti/Aquadro & Cerruti	BVH Integrated Services, P.C.
201302810530	Springfield	High School/Science-Tech	Final Audit Approved	Accelerated Repair	Roof	DBB	Atlantic Construction and Management, Inc.	CBI Consulting Inc.	Kronenberger & Sons Restoration, INC.	Building Enclosure Associates, LLC
201402810328	Springfield	John F Kennedy Middle	Closeout	Accelerated Repair	Windows / Doors		Arcadis U.S., Inc.	Gale Associates, Inc.	Lambrian Construction Corp.	Building Enclosure Associates, LLC

201402810110	Springfield	Kensington Avenue	Closeout	Accelerated Repair	Windows / Doors		Arcadis U.S., Inc.	Gale Associates, Inc.	Alpha Contracting Associates, Inc.	Building Enclosure Associates, LLC
201602810110	Springfield	Kensington Avenue	Design Development	Accelerated Repair	Roof		Leftfield, LLC	Gale Associates, Inc.	-	Building Enclosure Associates, LLC
201602810330	Springfield	M Marcus Kiley Middle	Design Development	Accelerated Repair	Windows / Doors		Leftfield, LLC	Gale Associates, Inc.	-	Building Enclosure Associates, LLC
201302810060	Springfield	Margaret C Ells	Final Audit Approved	Accelerated Repair	Roof	DBB	Atlantic Construction and Management, Inc.	CBI Consulting Inc.	Allied Restoration Corporation	Building Enclosure Associates, LLC
201602810140	Springfield	Mary M Lynch	Design Development	Accelerated Repair	Roof		Leftfield, LLC	Gale Associates, Inc.	-	Building Enclosure Associates, LLC
201502810155	Springfield	Mary M Walsh	Construction	Accelerated Repair	Windows / Doors		Skanska USA Building, Inc	CBI Consulting Inc.	PDS Engineering and Construction, Inc.	Building Enclosure Associates, LLC
201302810355	Springfield	South End Middle School	Final Audit Approved	Accelerated Repair	Roof	DBB	Atlantic Construction and Management, Inc.	CBI Consulting Inc.	Titan Roofing, Inc.	Building Enclosure Associates, LLC
201202810500	Springfield	Springfield Central High	Closeout	Science Lab Initiative	Addition / Renovation	CM@R	Leftfield, LLC	DiNisco Design, Inc.	Morganti/Aquadro & Cerruti	Horizon Engineering Associates, LLP
201302810550	Springfield	Springfield Public Day High School	Final Audit Approved	Accelerated Repair	Roof	DBB	Atlantic Construction and Management, Inc.	CBI Consulting Inc.	-	Building Enclosure Associates, LLC
201502810550	Springfield	Springfield Public Day High School	Construction	Accelerated Repair	Windows / Doors		Skanska USA Building, Inc	CBI Consulting Inc.	Westfield Construction Co., Inc.	Building Enclosure Associates, LLC
201502810350	Springfield	STEM Middle Academy	Construction	Accelerated Repair	Roof		Skanska USA Building, Inc	CBI Consulting Inc.	Westfield Construction Co., Inc.	Building Enclosure Associates, LLC
201602810045	Springfield	William N Deberry	Eligibility Period				-	-	-	-
200902840405	Stoneham	Stoneham Middle School	Final Audit Approved	Core Program	Addition / Renovation	CM@R	NV5 (fka Joslin, Lesser + Associates Inc.)	Tappe Associates, Inc.	Shawmut Design and Construction	RDK Engineers
201302850010	Stoughton	Helen Hansen Elementary	Final Audit Approved	Accelerated Repair	Windows / Doors	DBB	Hill International Company	Russo Barr Associates, Inc.	Lockheed Window Corporations	Building Enclosure Associates, LLC
201402850025	Stoughton	Joseph H Gibbons	Building Complete	Accelerated Repair	Roof, Windows / Doors		Atlantic Construction and Management, Inc.	CGKV Architects, Inc.	A&A Window Products, Inc.	Building Enclosure Associates, LLC
201302850014	Stoughton	Joseph R Dawe Jr Elem	Final Audit Approved	Accelerated Repair	Windows / Doors	DBB	Hill International Company	Russo Barr Associates, Inc.	Lockheed Window Corporations	Building Enclosure Associates, LLC
201302850505	Stoughton	Stoughton High	Design Development	Core Program	New Construction	CM@R	Compass Project Management, Inc.	Drumrey Rosane Anderson, Inc.	Consigli Construction Company, Inc.	Fitzmeyer & Tocci Associates, Inc.
201502850020	Stoughton	West Elementary	Construction	Accelerated Repair	Windows / Doors		Compass Project Management, Inc.	CBI Consulting Inc.	-	Building Enclosure Associates, LLC
200802900305	Sutton	Sutton Middle School	Final Audit Approved	Core Program	Addition / Renovation	DBB	Colliers International	Flansburgh Associates, Inc.	Brait Builders Corp.	RDK Engineers
201602920006	Swansea	Elizabeth S Brown	Approved Project Vote Pending	Accelerated Repair	Windows / Doors		Skanska USA Building, Inc	Tighe & Bond, Inc.	-	Simpson Gumpertz & Heger Inc.
201502930007	Taunton	Edmund Hatch Bennett	Construction	Accelerated Repair	Roof, Windows / Doors		Arcadis U.S., Inc.	CSS Architects Incorporated	TRAC Builders, Inc.	Gale Associates, Inc.
201502930042	Taunton	Joseph H Martin	Construction	Accelerated Repair	Roof, Windows / Doors		Arcadis U.S., Inc.	CSS Architects Incorporated	TRAC Builders, Inc.	Gale Associates, Inc.
201402930015	Taunton	Mulcahey Elementary School	Feasibility Study	Core Program			CGA Project Management	Dore & Whittier Architects, Inc.	-	-
201502950025	Tewksbury	Louise Davy Trahan	OPM Selection	Core Program			-	-	-	-
200802950505	Tewksbury	Tewksbury Memorial High School	Closeout	Core Program	New Construction - Model School	DBB	HEERY	Symmes Maini & McKee Associates, Inc.	CTA Ventures	Sebesta Blomberg & Associates, Inc.
201502960005	Tisbury	Tisbury Elementary	Feasibility Study	Core Program			Daedalus Projects Inc	Turowski2 Architecture, Inc.	-	-
201602980005	Topsfield	Proctor Elementary	Schematic Design	Accelerated Repair	Roof		Compass Project Management, Inc.	The S/L/A/M Collaborative	-	-
201602980010	Topsfield	Steward Elementary	Schematic Design	Accelerated Repair	Roof		Compass Project Management, Inc.	The S/L/A/M Collaborative	-	-
201408780605	Tri County	Tri County Reg Voc Tech	Final Audit Approved	Accelerated Repair	Boiler		Colliers International	Shekar & Associates, Inc.	-	Fitzmeyer & Tocci Associates, Inc.
201507730025	Triton	Pine Grove	Schematic Design	Core Program	Addition / Renovation		Pinck & Co., Inc.	Dore & Whittier Architects, Inc.	-	-
201403010505	Tyngsborough	Tyngsborough High School	Closeout	Accelerated Repair	Roof, Boiler		Municipal Building Consultants, Inc.	CSS Architects Incorporated	Greenwood Industries, Inc.	Colliers International
200907750305	Wachusett	Mountview Middle School	Building Complete	Core Program	New Construction	DBB	Town Employee	Lamoureux Pagano & Associates, Inc.	CTA Construction Co., Inc.	Fitzmeyer & Tocci Associates, Inc.

201003050310	Wakefield	Galvin Middle School	Closeout	Core Program	New Construction	CM@R	NV5 (fka Joslin, Lesser + Associates Inc.)	Tappe Associates, Inc.	Bond Brothers, Inc.	B2Q Associates, Inc.
201403080505	Waltham	Waltham High School	Feasibility Study	Core Program			NV5 (fka Joslin, Lesser + Associates Inc.)	Symmes Maini & McKee Associates, Inc.	-	-
201503100003	Wareham	John W. Decas Elementary School	Construction	Accelerated Repair	Roof, Boiler		Colliers International	ICON architecture, inc.	Nadeau Corporation	Bard, Rao + Athanas Consulting Engineers, LLC Gale Associates, Inc.
201503100017	Wareham	Minot Forest	OPM Selection	Core Program			-	-	-	-
201503140305	Watertown	Watertown Middle	Design Development	Accelerated Repair	Windows / Doors		exPERTcon, Inc.	Gale Associates, Inc.	-	Thompson & Lichtner Co., Inc.
201403150005	Wayland	Claypit Hill School	Building Complete	Accelerated Repair	Windows / Doors		Pinck & Co., Inc.	CGKV Architects, Inc.	Lockheed Window Corporations	Russo Barr Associates, Inc.
201603150020	Wayland	Loker School	Schematic Design	Accelerated Repair	Windows / Doors		Colliers International	CBI Consulting Inc.	-	-
200903160015	Webster	Park Avenue Elementary School	Closeout	Core Program	New Construction	DBB	Hill International Company	Dore & Whittier Architects, Inc.	CTA Construction Co., Inc.	Cannon Design
201403170305	Wellesley	Wellesley Middle	Building Complete	Accelerated Repair	Windows / Doors		Arcadis U.S., Inc.	CSS Architects Incorporated	Paul J. Rogan Co., Inc.	Gale Associates, Inc.
200803170505	Wellesley	Wellesley Senior School	Final Audit Approved	Core Program	New Construction	CM@R	-	Symmes Maini & McKee Associates, Inc.	-	Rist-Frost-Shumway Engineering, P.C.
201303180005	Wellfleet	Wellfleet Elementary	Final Audit Approved	Accelerated Repair	Roof	DBB	Architectural Consulting Group, LLC	CSS Architects Incorporated	DDC Construction Inc.	Russo Barr Associates, Inc.
201103220005G	West Boylston	Major Edwards Elementary	Closeout	Green Repair	Windows / Doors	DBB	URS Corporation	Reinhardt Associates, Inc.	-	Cannon Design
201503230005	West Bridgewater	Spring Street School	Closeout	Accelerated Repair	Roof		Potomac Capital Advisors	Tai Soo Kim Partners, LLC	Capeway Roofing Systems, Inc.	Thompson & Lichtner Co., Inc.
201003230505	West Bridgewater	West Bridgewater Middle-Senior High School	Building Complete	Core Program	New Construction	DBB	Colliers International	Flansburgh Associates, Inc.	CTA Construction Co., Inc.	Cannon Design
201503320007	West Springfield	Philip G Coburn	Eligibility Period	Core Program			-	-	-	-
200903320505	West Springfield	West Springfield High School	Closeout	Core Program	New Construction - Model School	DBB	Colliers International	Symmes Maini & McKee Associates, Inc.	Fontaine Brothers, Inc.	Turner Facilities Management Solutions
201603210010	Westborough	Annie E Fales	Eligibility Period	Core Program			-	-	-	-
200903210305	Westborough	Gibbons Middle School	Construction	Core Program	Repair	CM@R	HEERY	Habeeb & Associates Architects, Inc.	Gilbane Building Company	BVH Integrated Services, P.C.
200903250020	Westfield	Abner Gibbs Elementary School	Construction	Core Program	New Construction - Model School	DBB	Skanska USA Building, Inc	Jones Whitsett Architects, Inc.	Fontaine Brothers, Inc.	Horizon Engineering Associates, LLP
201303260025	Westford	Col John Robinson	Closeout	Accelerated Repair	Windows / Doors	DBB	Colliers International	Gale Associates, Inc.	GTC Construction Management	CBI Consulting Inc.
201303260007	Westford	Day Elementary	Closeout	Accelerated Repair	Windows / Doors	DBB	Colliers International	Gale Associates, Inc.	J.J. Cardosi, Inc.	CBI Consulting Inc.
200903300012	Weston	Field Elementary School	Final Audit Approved	Core Program	New Construction	DBB	Compass Project Management, Inc.	Jonathan Levi Architects LLC	Colantonio, Inc.	Foreman Building Commissioning, LP
201403310305	Westport	Westport Middle	Schematic Design	Core Program	New Construction		Daedalus Projects Inc	Jonathan Levi Architects LLC	-	-
201503360020	Weymouth	Maria Weston Chapman Middle School	Designer Selection	Core Program			Hill International Company	-	-	-
200803400005	Williamsburg	Anne T. Dunphy School	Final Audit Approved	Core Program	Addition / Renovation	DBB	Arcadis U.S., Inc.	Drumrey Rosane Anderson, Inc.	Enfield Builders, Inc.	B2Q Associates, Inc.
200903420505	Wilmington	Wilmington High School	Building Complete	Core Program	New Construction	CM@R	NV5 (fka Joslin, Lesser + Associates Inc.)	Dore & Whittier Architects, Inc.	Gilbane Building Company	Symmes, Maini & McKee Associates
201003440505	Winchester	Winchester High School	Construction	Core Program	Addition / Renovation	CM@R	Skanska USA Building, Inc	Symmes Maini & McKee Associates, Inc.	Consigli Construction Company, Inc.	RDK Engineers
200803460505	Winthrop	Winthrop High School	Building Complete	Core Program	New Construction	CM@R	Skanska USA Building, Inc	HMFH Architects, Inc.	Gilbane Building Company	WSP USA
201203470060	Woburn	Wyman	Construction	Core Program	New Construction		Municipal Building Consultants, Inc.	DiNisco Design, Inc.	CTA Construction Co., Inc.	Fitzmeyer & Tocci Associates, Inc.
201603480020	Worcester	Belmont Street Community	Design Development	Accelerated Repair	Windows / Doors		Watermark Environmental, Inc.	Tighe & Bond, Inc.	-	Russo Barr Associates, Inc.
201603480050	Worcester	Chandler Elem Community	Design Development	Accelerated Repair	Windows / Doors, Boiler		Watermark Environmental, Inc.	Tighe & Bond, Inc.	-	BVH Integrated Services, P.C. Russo Barr Associates, Inc.

201403480055	Worcester	Clark St Community	Closeout	Accelerated Repair	Windows / Doors		Architectural Consulting Group, LLC	ICON architecture, inc.	J.J. Cardosi, Inc.	Russo Barr Associates, Inc.
201303480060	Worcester	Columbus Park	Closeout	Accelerated Repair	Windows / Doors, Boiler	DBB	Architectural Consulting Group, LLC	The S/L/A/M Collaborative	Contractor's Network, Inc.	RDK Engineers Russo Barr Associates, Inc.
201603480512	Worcester	Doherty Memorial High	Eligibility Period	Core Program			-	-	-	-
201503480090	Worcester	Flagg Street	Construction	Accelerated Repair	Windows / Doors		Arcadis U.S., Inc.	CSS Architects Incorporated	J.J. Cardosi, Inc.	Russo Barr Associates, Inc.
201503480177	Worcester	Francis J McGrath Elem	Construction	Accelerated Repair	Windows / Doors		Arcadis U.S., Inc.	CSS Architects Incorporated	J.J. Cardosi, Inc.	Russo Barr Associates, Inc.
201603481004	Worcester	Gerald Creamer Center	Design Development	Accelerated Repair	Windows / Doors, Boiler		Watermark Environmental, Inc.	Tighe & Bond, Inc.	-	BVH Integrated Services, P.C. Russo Barr Associates, Inc.
201403480100	Worcester	Goddard Sch/Science Tech	Closeout	Accelerated Repair	Windows / Doors		Architectural Consulting Group, LLC	ICON architecture, inc.	Lambrian Construction Corp.	Russo Barr Associates, Inc.
201503480115	Worcester	Grafton Street	Building Complete	Accelerated Repair	Windows / Doors, Boiler		Arcadis U.S., Inc.	CSS Architects Incorporated	J.J. Cardosi, Inc.	Rist-Frost-Shumway Engineering, P.C. Russo Barr Associates, Inc.
201503480140	Worcester	Jacob Hiatt Magnet	Construction	Accelerated Repair	Windows / Doors		Arcadis U.S., Inc.	CSS Architects Incorporated	J.J. Cardosi, Inc.	Russo Barr Associates, Inc.
201203480200	Worcester	Nelson Place	Construction	Core Program	New Construction	CM@R	Tishman Construction Corporation of MA	Lamoureux Pagano & Associates, Inc.	Fontaine Brothers, Inc.	Bard, Rao + Athanas Consulting Engineers, LLC
201403480520	Worcester	South High Community	Feasibility Study	Core Program			HEERY	Lamoureux Pagano & Associates, Inc.	-	-
201303480230	Worcester	Tatnuck	Closeout	Accelerated Repair	Windows / Doors	DBB	Architectural Consulting Group, LLC	The S/L/A/M Collaborative	GVW, Inc.	Russo Barr Associates, Inc.
201403480240	Worcester	Union Hill School	Closeout	Accelerated Repair	Windows / Doors		Architectural Consulting Group, LLC	ICON architecture, inc.	J.J. Cardosi, Inc.	Russo Barr Associates, Inc.
201603480026	Worcester	Wawecus Road School	Design Development	Accelerated Repair	Windows / Doors		Watermark Environmental, Inc.	Tighe & Bond, Inc.	-	Russo Barr Associates, Inc.
201403480260	Worcester	West Tatnuck	Closeout	Accelerated Repair	Windows / Doors		Architectural Consulting Group, LLC	ICON architecture, inc.	J.J. Cardosi, Inc.	Russo Barr Associates, Inc.
201303480225	Worcester	Worcester Arts Magnet Sch	Closeout	Accelerated Repair	Windows / Doors	DBB	Architectural Consulting Group, LLC	The S/L/A/M Collaborative	GVW, Inc.	Russo Barr Associates, Inc.
201303480420	Worcester	Worcester East Middle	Closeout	Accelerated Repair	Boiler	DBB	Architectural Consulting Group, LLC	The S/L/A/M Collaborative	Contractor's Network, Inc.	RDK Engineers
201503500003	Wrentham	Delaney	Design Development	Accelerated Repair	Roof		P3 Inc.	Turowski2 Architecture, Inc.	-	Gale Associates, Inc.

2017 ESTIMATED BID DATES

Note bid dates are Estimates ONLY. Please contact Districts for exact information.


Total Project Budget denotes total District costs and does not denote the basis of the MSBA Total Facilities Grant.

District	Enrollment	Project Budget	Start	Finish	Construct Budget	Notes	Jan '17	Feb '17	Mar '17	Apr '17	May '17	Jun '17	Jul '17	Aug '17	Sep '17	Oct '17	Nov '17	Dec '17	Jan '18	Feb '18					
Granby	430	\$ 34.2	Mon 11/7/16	Thu 1/26/17	\$ 26.5	NTP issued: January 2017																			
Mount Greylock	535	\$ 64.7	Mon 2/20/17	Thu 5/4/17	\$ 52.3	GMP targeted: June 2017																			
Quincy	430	\$ 58.3	Fri 3/17/17	Fri 6/9/17	\$ 46.6	GMP targeted: June 2017																			
Hanover	560	\$ 32.4	Tue 5/9/17	Tue 6/20/17	\$ 26.1	NTP targeted: July 2017																			
Stoughton	1065	\$ 123.5	Wed 5/24/17	Wed 7/26/17	\$ 97.2	GMP targeted: July 2017																			
Billerica	1610	\$ 175.9	Mon 6/5/17	Fri 8/25/17	\$ 140.7	GMP targeted: August 2017																			
Needham	430	\$ 65.9	Wed 7/5/17	Wed 9/13/17	\$ 45.5	NTP targeted: October 2017																			
Dedham	200	\$ 33.2	Fri 7/21/17	Fri 9/8/17	\$ 26.2	NTP targeted: September 2017																			
Bourne	460	\$ 39.9	Wed 10/4/17	Tue 11/21/17	\$ 30.9	NTP targeted: November 2017																			
Newton	480	\$ 49.0	Wed 10/4/17	Tue 11/28/17	\$ 36.2	GMP targeted: November 2017																			
Minuteman Reg. School District	628	\$ 144.9	Wed 10/25/17	Mon 2/5/18	\$ 119.2	GMP targeted: February 2018																			
Total	6828	\$ 822.0			\$ 647.4																				

Note: Budget values are in millions.

The project start date represents the Filed-Sub bid solicitation date, gray diamond Filed-Sub bid date, and the black diamond GC Bids / GMP Execution.

4/19/17



2018 ESTIMATED BID DATES

Note bid dates are Estimates ONLY. Please contact Districts for exact information.


Total Project Budget denotes total District costs and does not denote the basis of the MSBA Total Facilities Grant.

District	Enrollment	Project Budget	Start	Finish	Construct Budget	Notes	Predecessors																
								Jan '18	Feb '18	Mar '18	Apr '18	May '18	Jun '18	Jul '18	Aug '18	Sep '18	Oct '18	Nov '18	Dec '18				
Somerville	1590	\$ 256.0	Mon 3/12/18	Mon 7/2/18	\$ 199.0	GMP targeted: July 2018					3/12	Somerville High School				6/4	7/2						
Total	1590	\$ 256.0			\$ 199.0																		

Note: Budget values are in millions.

The project start date represents the Filed-Sub bid solicitation date, gray diamond Filed-Sub bid date, and the black diamond GC Bids / GMP Execution.

04/19/2017




**Projects in Construction
MSBA Grant Basis and Maximum Grant Amount
Data Reported as of April 07, 2017**

Core Program and Waitlist Totals			\$2,000,098,685														*Includes Alternates	\$1,212,408,732
Project	Grade	Contractor	Total Construction Cost*	Projected Enrollment	PFA or Bid Data	Proposed Sq.Ft.	Construction Cost/Sq.Ft.	Building Cost	Building Cost/Sq.Ft.	Procurement Type	Construction Start Date	Substantial Completion	Schedule Variance (days)	Physical Progress	Change Orders	Change Orders %	Construction Status	Est Max Total Facilities Grant
CAPITAL PIPELINE PROJECTS IN CONSTRUCTION																		
Core Program Totals			\$1,991,133,685															\$1,202,276,926
Abington Frolio Jr Hs	Junior High School	Brait Builders Corp.	\$78,791,215	1,115	Bid	235,370	\$335	\$61,468,040	\$261	Design/Bid/Build	03-Dec-15	18-Jul-17	45 ahead	80%	\$879,301	1.142%	Finishes being installed throughout the building. Project team working on the punch list. Furniture, furnishing and equipment to be delivered May 2017.	\$48,528,486
Athol-Royalston Riverbend	Elementary School	Fontaine Brothers, Inc.	\$31,594,000	545	Bid	95,726	\$330	\$24,859,000	\$260	Design/Bid/Build	08-Dec-14	14-Jun-16	0	99%	\$1,926,763	6.099%	Final site work completed. Commissioning and punch list work is ongoing.	\$26,011,620
Chicopee Chicopee Academy	Middle School	Fontaine Brothers, Inc.	\$31,487,000	825	Bid	176,425	\$178	\$25,639,000	\$145	Design/Bid/Build	01-Jul-14	11-Aug-15	0	100%	\$2,063,322	6.553%	The punch list work is complete. Two items remain on the Commissioning log. Designer to submit LEED documentation to the USGBCI following completion of commissioning activities.	\$28,813,458
Dracut Dracut Senior High	High School	CTA Construction Co., Inc.	\$45,900,000	1,160	Bid	226,844	\$202	\$38,377,028	\$169	Design/Bid/Build	27-Aug-12	29-Aug-14	0	100%	\$2,651,850	5.778%	Minor punch list items related to dunnage work remain. Project team is preparing for closeout.	\$34,137,202
Georgetown Penn Brook	Elementary School	Brait Builders Corp.	\$32,875,975	770	Bid	98,000	\$335	\$26,976,145	\$275	Design/Bid/Build	26-Sep-13	20-May-15	0	100%	\$3,897,226	11.854%	Final landscaping completed. Commissioning complete and punch list work ongoing.	\$18,864,538
New Bedford John Hannigan	Elementary School	H.V. Collins Co., Inc.	\$29,792,732	400	PFA	74,056	\$402	\$20,536,621	\$277	Design/Bid/Build	11-Aug-16	07-Aug-17	14 behind	45%	\$51,016	0.171%	A delay in manufacturing of steel recovered through overtime work by the steel contractor has reduced a 20 days delay in the project to 14 days. Elevated slabs, light-gauge metal and roof work are ongoing. Ductwork and fire protection are complete throughout the building. Electrical is underway on third floor. Window blocking is complete and window installation to commence early May 2017. Site work includes retaining wall prep work. The City and OPM have verbally agreed to execute a construction change directive (CCD) for acceleration in order to meet the August completion date.	\$22,428,240
North Middlesex North Middlesex Reg	High School	CTA Construction Co., Inc.	\$64,995,000	870	Bid	180,530	\$360	\$49,909,000	\$276	Design/Bid/Build	25-May-15	14-Jul-17	0	78%	\$283,077	0.436%	Roof detailing underway. Finishes being installed throughout the building. Furniture, furnishing and equipment to be delivered June 2017.	\$38,471,881
Northborough Lincoln Street	Elementary School	Brait Builders Corp.	\$18,450,000	270	Bid	52,920	\$349	\$14,514,966	\$274	Design/Bid/Build	27-Apr-15	31-Aug-16	0	99%	\$188,487	1.022%	Items remaining include minor punch list items, final commissioning and close out.	\$9,925,570
Peabody J Henry Higgins Middle	Middle School	Bacon-Agostini Construction Joint Venture	\$70,679,700	1,340	Bid	227,314	\$311	\$52,186,177	\$230	Design/Bid/Build	10-Mar-14	05-Aug-16	0	98%	\$1,002,230	1.418%	Playfield construction in progress.	\$38,652,137
Plymouth Plymouth South High	High School	Bacon-Agostini Construction Joint Venture	\$90,266,700	1,005	Bid	248,081	\$364	\$66,744,766	\$269	Design/Bid/Build	06-Jul-15	05-May-17	0	87%	\$397,045	0.468%	Building is weather tight and receiving temp heat. Finishes remain ongoing including drywall with some areas receiving paint and millwork. Monumental stair is nearing completion. The contractor continues with the flow of work from areas 1-7 on all floors, all trades. Finish lighting in classrooms and technology infrastructure continues in areas 1,2,&3. Binder course and granite curbs have been installed.	\$45,733,725
Provincetown Provincetown High	High School	E. Amanti & Sons, Inc.	\$5,709,882	111	Bid	62,645	\$91	\$3,671,169	\$59	Design/Bid/Build	14-Mar-16	07-Dec-16	0	99%	\$704,693	12.342%	Auditorium related lighting and finish items as well as site related items are ongoing and expected to be complete by mid-May 2017. Further exploration of existing envelope leaks in the Principal's office and the building's electrical entry point may need to be addressed during Summer of 2017.	\$3,258,431
Revere Staff Sergeant James J. Hill School	Elementary School	CTA Construction Co., Inc.	\$31,975,839	690	Bid	103,650	\$308	\$27,439,789	\$265	Design/Bid/Build	25-Mar-14	17-Aug-15	0	99%	\$1,110,455	3.473%	The contractor/City is in the process of completing work to close out the project including punch list items.	\$28,099,048
Scituate Gates Intermediate School	Middle School	Bacon-Agostini Construction Joint Venture	\$52,596,801	710	Bid	164,803	\$319	\$42,947,412	\$261	Design/Bid/Build	08-Dec-15	24-Jul-17	0	87%	\$1,538,986	2.926%	High school auditorium nears completion. Middle School interior finishes, carpentry, millwork, mechanical, electrical and plumbing are in progress. Masonry, and roofing contractors finishing exterior work and roof edge. Glazing is in progress. The Site Contractor remobilized and began grading and installing light pole bases and curbing.	\$20,436,585
South Hadley Plains Elementary	Elementary School	Fontaine Brothers, Inc.	\$21,391,144	270	Bid	63,377	\$338	\$17,380,907	\$274	Design/Bid/Build	08-May-14	04-Sep-15	0	100%	\$1,676,719	7.838%	Building project is complete. District working towards submitting final payment and project closeout.	\$13,676,432
Wachusett Mountview Middle	Middle School	CTA Construction Co., Inc.	\$43,122,257	800	Bid	126,200	\$342	\$28,959,805	\$229	Design/Bid/Build	21-May-14	11-Apr-16	0	99%	\$967,266	2.243%	Incomplete commissioning items and warranty work remain for completion and moving this project into the closeout phase.	\$24,279,591
West Bridgewater West Bridgewater Jr-Sr	Junior High School	CTA Construction Co., Inc.	\$46,267,914	625	Bid	141,250	\$328	\$35,071,188	\$248	Design/Bid/Build	01-Oct-13	09-Jul-15	0	99%	\$622,152	1.345%	Work continues on the punch list as well as completion of sound, security and fire alarm systems. Commissioning of the building is ongoing.	\$26,385,058
Westfield Abner Gibbs	Elementary School	Fontaine Brothers, Inc.	\$25,578,000	600	Bid	95,573	\$268	\$21,444,000	\$224	Design/Bid/Build	24-Aug-12	01-Jun-19	0	2%	\$0	0.000%	Work stoppage due to preliminary injunction based upon project site status as Article 97 "Protected Land". Preliminary Injunction vacated but city awaiting National Park Service approval for use of site. The General Contractor has demobilized from the site. The project team is working on closing out the General Contractor's contract.	\$20,004,463
Beverly Briscoe Middle	Middle School	Bacon-Agostini Construction Joint Venture	\$90,129,432	1,395	PFA	231,509	\$389	\$62,790,920	\$271	CM-at-Risk	24-Dec-15	30-Mar-18	0	30%	\$0	0.000%	Steel erection in the area of auditorium and gym is nearing completion. Installation of the roof at the classroom wings has begun. Underground plumbing work is underway. Light gauge framing work continues.	\$48,018,498
Boston Dearborn	Middle School	Gilbane Building Company	\$60,245,740	600	Bid	128,304	\$470	\$36,655,002	\$286	CM-at-Risk	08-Sep-15	27-Dec-17	0	52%	\$0	0.000%	HVAC, plumbing, and drywall work continues in the interior of the building. Duct work on floors 2 and 3 is complete and floor 4 duct work installation is underway. Window and air vapor barrier installation is ongoing. Masonry work has begun. Atrium skylight installation to commence late Spring 2017.	\$36,033,391
Brookline Edward Devotion	Elementary School	Shawmut Design and Construction	\$92,237,854	1,010	PFA	227,087	\$406	\$57,910,095	\$255	CM-at-Risk	11-Jul-16	31-Jul-18	0	15%	\$131,946	0.143%	Structural steel is complete in the building wings (Areas A & B). Exterior framing, roof installation, spray fireproofing and mechanical hangers are underway in Area A wing. In the portion of the original 1913 building, added shoring, masonry repairs and rough carpentry work continues.	\$25,910,852
Chelsea Clark Avenue School	Middle School	W. T. Rich Company Inc.	\$46,046,367	670	Bid	115,235	\$400	\$29,311,076	\$254	CM-at-Risk	23-Feb-15	29-Jun-18	0	63%	\$215,923	0.469%	The first half (Phase 1) of the new school remains occupied with students and staff. Minor punch list and commissioning items remain for completion of Phase 1. Abatement of the remaining building under Phase 2 has been completed, and demolition is underway. Concrete foundation placement will progress through April with structural steel erection in May.	\$36,163,680
Gloucester West Parish	Elementary School	W. T. Rich Company Inc.	\$29,995,466	355	Bid	65,679	\$457	\$18,591,872	\$283	CM-at-Risk	07-Jul-14	15-Jul-16	0	0%	\$573,387	1.912%	Minor punch list and administrative activities are ongoing.	\$14,673,132
Haverhill Caleb Dustin Hunking	Middle School	Shawmut Design and Construction	\$49,544,769	1,005	Bid	147,996	\$335	\$35,181,852	\$238	CM-at-Risk	20-Apr-15	16-Dec-16	0	97%	\$1,599,990	3.229%	The upper school portion of the new building is in use. The lower school portion of the building will be occupied in September. Punch list work continues on the new building. Training sessions on new equipment are ongoing. MEP work continues on the new maintenance building. Demolition and site work continue.	\$39,518,874
Holbrook Holbrook Jr Sr High	High School	Consigli Construction Company, Inc.	\$78,135,643	1,095	Bid	217,353	\$359	\$52,399,810	\$241	CM-at-Risk	24-Jun-15	05-Jun-17	0	76%	\$1,364,085	1.756%	Finish work continues including prime and finish painting, metal hand railings, ceiling grids and tiles, ceramic tiles, floor tiles, lab casework, wooden door and hardware installations, gym flooring, and stairway wooden hand rails.	\$53,832,918
Hopkinton Center	Elementary School	Colantonio, Inc.	\$35,140,982	395	PFA	83,256	\$422	\$21,864,684	\$263	CM-at-Risk	03-Oct-16	31-Jul-18	0	18%	\$148,521	0.423%	Building foundation is complete. Structural steel is completed at the Cafeterium and Gymnasium and is in progress in academic buildings. Building underground utilities and site work are in progress.	\$13,763,197
Lunenburg Lunenburg High	Junior High School	Shawmut Design and Construction	\$57,994,017	820	Bid	169,018	\$343	\$41,982,415	\$248	CM-at-Risk	15-Aug-14	30-Jun-16	0	99%	\$1,188,726	2.050%	Final site work to be completed. Commissioning and punch list work ongoing.	\$34,122,826
Milford Woodland	Elementary School	Shawmut Design and Construction	\$48,375,101	985	Bid	132,539	\$365	\$34,861,130	\$263	CM-at-Risk	01-Apr-15	28-Jul-16	0	96%	\$1,172,259	2.423%	Testing and balancing of building systems are ongoing. Site work ongoing. Punch list and additional owner requested changes/work are in progress.	\$27,418,234
Mount Greylock Mt Greylock Reg High	High School	Turner Construction Company	\$52,475,706	535	PFA	132,800	\$395	\$30,982,991	\$233	CM-at-Risk	30-Mar-17	25-Apr-18	0	15%	\$0	0.000%	Foundations have continued to be poured with the warmer weather. Steel has begun to be erected and is to be completed by the end of April. Decking, slab on grade and elevated slabs to follow steel installation. Filed Sub-Bids have been received and GMP Execution is targeted for mid-June.	\$32,491,074
Newton A E Angier	Elementary School	W. T. Rich Company Inc.	\$30,158,875	465	Bid	74,960	\$402	\$19,837,027	\$265	CM-at-Risk	22-Aug-14	04-Jan-16	0	99%	\$366,791	1.399%	The punch list has been completed. Contractor is working on O&M manuals. Asphalt patch open warranty item is being addressed. Issue at sliding glass doors at main reception is under investigation.	\$10,687,077
North Reading North Reading High	Junior High School	Gilbane Building Company	\$101,328,353	1,370	Bid	267,939	\$378	\$66,726,592	\$249	CM-at-Risk	01-May-12	21-Aug-15	0	99%	\$3,512,026	3.466%	Punch list items including site work, warranty items, and commissioning closeout items remain for completion. OPM report indicates that drain line corrective work and final landscaping will be scheduled for Spring 2017.	\$47,071,882

**Projects in Construction
MSBA Grant Basis and Maximum Grant Amount
Data Reported as of April 07, 2017**

Core Program and Waitlist Totals			\$2,000,098,685														*Includes Alternates	\$1,212,408,732
Project	Grade	Contractor	Total Construction Cost*	Projected Enrollment	PFA or Bid Data	Proposed Sq.Ft.	Construction Cost/Sq.Ft.	Building Cost	Building Cost/Sq.Ft.	Procurement Type	Construction Start Date	Substantial Completion	Schedule Variance (days)	Physical Progress	Change Orders	Change Orders %	Construction Status	Est Max Total Facilities Grant
CAPITAL PIPELINE PROJECTS IN CONSTRUCTION																		
Core Program Totals			\$1,991,133,685															\$1,202,276,926
Pittsfield Taconic High	High School	Gilbane Building Company	\$97,757,373	920	PFA	246,520	\$397	\$56,984,184	\$231	CM-at-Risk	21-Mar-16	29-Jun-18	0	26%	\$1,038,291	1.062%	Mechanical and electrical rough-in work has progressed through the A and B Building sections (gym, auditorium, and cafeteria and some classroom spaces). Slab on grade is in progress and the elevated slabs are complete. Interior masonry, spray fireproofing, and drywall installation is also underway. The temporary enclosure and temporary heat for A and B has been maintained through the winter in support of this work. Roof installation is nearing completion for the A and B Buildings.	\$72,491,194
Southern Worcester Cty VT Bay Path Reg Voc Tech HS	Vocational / Technical	Consigli Construction Company, Inc.	\$57,024,455	1,110	Bid	249,521	\$229	\$41,468,049	\$166	CM-at-Risk	02-Aug-13	01-Sep-15	0	100%	\$4,402,328	7.772%	Project team is awaiting planting season to complete landscaping. The CM contract will be closed following the completion of remaining planting work.	\$44,420,530
Westborough Sarah W Gibbons Middle	Middle School	Gilbane Building Company	\$21,595,600	550	Bid	110,000	\$196	\$12,693,993	\$115	CM-at-Risk	22-Jun-16	25-Aug-17	0	70%	\$525,087	2.432%	Phase 3 of 7 achieved certificate of occupancy. Phase 4 work commenced and includes auditorium, stage and boiler room selective demo work. Scaffolding above auditorium seating installed to allow new installation of sprinkler system. Owner requested library lighting upgrade is complete except for 2 long lead lighting fixtures.	\$11,113,998
Wilmington Wilmington High	High School	Gilbane Building Company	\$67,558,835	960	Bid	192,443	\$351	\$48,060,314	\$250	CM-at-Risk	30-Apr-13	12-Feb-15	0	99%	\$2,881,004	4.458%	The project team is working to resolve an issue with the gym floor.	\$35,674,893
Winchester Winchester High School	High School	Consigli Construction Company, Inc.	\$101,404,577	1,370	Bid	278,925	\$364	\$70,862,283	\$254	CM-at-Risk	23-Apr-14	31-Aug-17	0	92%	\$5,646,571	5.568%	Phase 3 of 3 is nearing completion. The exterior facade has been completed and interior finishes are on going. B Wing is receiving tile, paint, finish floor and ceiling grids. A Wing is just behind B Wing with plaster work being completed and paint, tile and other finishes beginning. Casework has also begun to be installed. Early summer 2017 work to include disassemble walls and finishes will be connected to Phase 2, modular-trailers will be disassembled and removed and site work will be completed over the summer.	\$42,187,027
Winthrop Winthrop Sr High	Junior High School	Gilbane Building Company	\$63,542,179	970	Bid	187,917	\$338	\$49,608,610	\$264	CM-at-Risk	01-Jul-14	30-Jun-16	0	100%	\$1,646,932	2.592%	The new building opened for the Fall 2016 school year. Miscellaneous punch list items are remaining to be completed.	\$38,996,995
Worcester Nelson Place	Elementary School	Fontaine Brothers, Inc.	\$46,546,300	600	Bid	111,256	\$418	\$29,503,564	\$265	CM-at-Risk	01-Jul-15	31-May-17	0	68%	(\$147,809)	-0.318%	Worcester has had seven (7) snow day cancellations. This is impacting the planned start of the abatement and demolition of the existing building, but not the completion and opening of the new school. The team is evaluating different ways to mitigate the impact. Finishes, mechanical, electrical, plumbing and exterior work are ongoing. The site work subcontractor has remobilized and is continuing with earthmoving, setting curbs and erosion control.	\$33,324,289
Carver Carver Elementary School	Elementary School	CTA Construction Co., Inc.	\$41,426,767	750	PFA	112,350	\$369	\$26,491,831	\$236	Undetermined	27-Sep-16	22-Jun-18	0	11%	\$37,882	0.096%	Site drainage work continues to progress. Mock-up panel has been installed. Erection of steel continues at 'C' building, detail and decking at 'B' building continues. Stud welding at 'B' building continues. Placing of slab on deck at 'A' building continues. Underground sanitary at 'B' building continues and other utility work remains ongoing in coordination with other trades.	\$25,814,682
Granby West St	Elementary School	Fontaine Brothers, Inc.	\$26,453,000	430	PFA	68,760	\$385	\$16,570,000	\$241	Undetermined	07-Feb-17	17-Aug-18	0	1%	\$0	0.000%	The contractor has mobilized on site, installed erosion protections, installed field office trailers, installed site fencing, stripped and stockpiled topsoil, removed existing asphalt parking from the construction area and installed a temporary parking area for school staff.	\$16,867,064
Woburn Wyman	Elementary School	CTA Construction Co., Inc.	\$27,017,841	410	PFA	70,701	\$382	\$18,251,786	\$258	Undetermined	10-Jan-17	11-Jul-18	0	15%	\$51,107	0.189%	Foundations and footings are near completion. Underground utilities, drainage and water services are ongoing. Steel erection to commence mid-May 2017.	\$13,974,154
Waitlist Totals			\$8,965,000				\$139		\$108									\$10,131,806
New Bedford Taylor School at the Sea Lab Marine Science Education Center	N/A	M. O'Connor Contracting, Inc.	\$8,965,000	284	Bid	64,533	\$139	\$6,967,355	\$108	Design/Bid/Build	28-Nov-15	01-Nov-16	0	99%	\$457,938	5.108%	Work continues on punch list items as well as training school staff on equipment and systems.	\$10,131,806

MSBA Construction Costs Compared to Common Economic Indicators

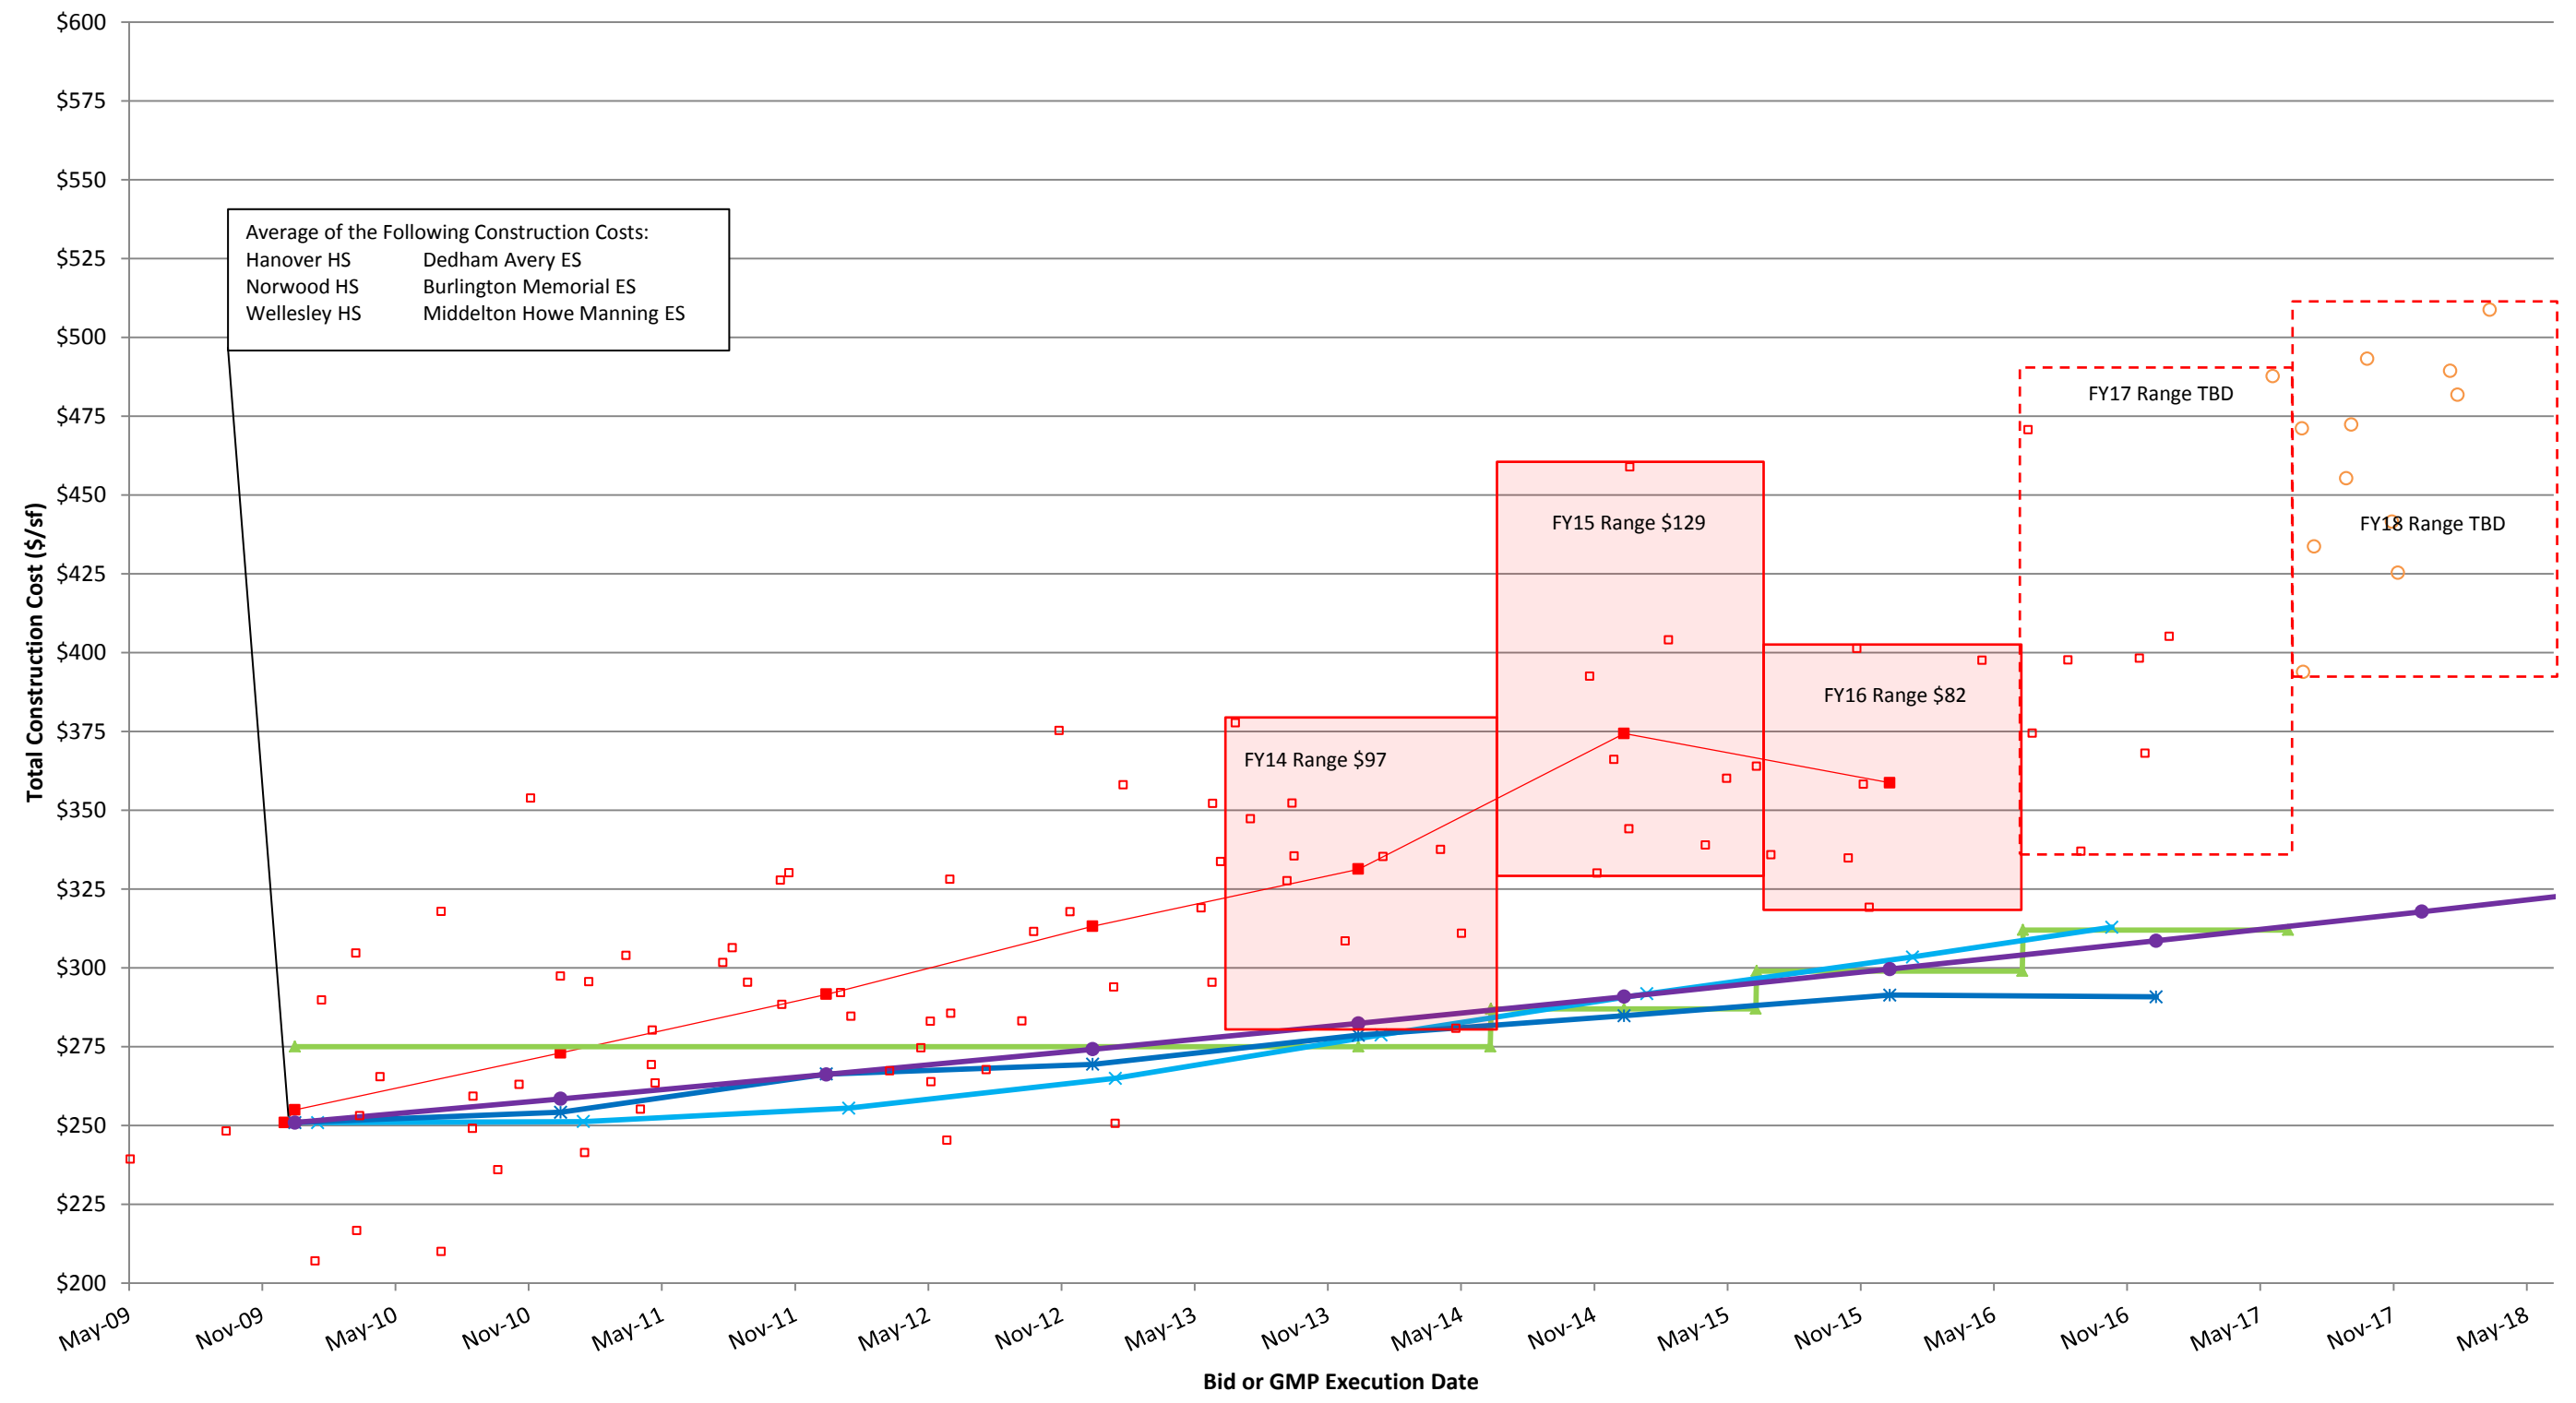

- Total Construction Cost
- Average Total Construction Cost by FY
- MSBA Construction Funding
- RLB USA Report Comparative Cost Index - Boston
- ✱ BLS New Schools PPI
- 3% Escalation
- Total Construction Cost- SD DATA
- FY Boundaries
