

Massachusetts School Building Authority

CAPITAL PLANNING PROJECT OVERVIEW REPORT

June 3, 2020

TABLE OF CONTENTS

Capital Pipeline Overview	2-3
Statements of Interest (SOIs)	4
Core Program	5-15
Eligibility Period	5
Consultant Selection	6-7
Feasibility Study	8
Schematic Design	9
Commissioning	10
Design Development	11
Summary of Bid Data	12
Construction	13-14
Closeout	15
Accelerated Repair Program	16-24
Project Variances	25-26

Appendices

(A) Project Status List

(B) 2018-21 Estimated Bid Dates


(C) School Construction Costs compared to Common Economic Indicators

(D) Construction Status Report

CAPITAL PIPELINE OVERVIEW

Status of Current Projects

A total of 321 projects that have received invitations from the Board of Directors (“Board”) to collaborate with the Massachusetts School Building Authority (“MSBA”) are currently in the MSBA’s Eligibility Period and Capital Pipeline. The summary chart provides the number of projects in Eligibility Period and each phase of the Capital Pipeline. For a detailed look at the Capital Pipeline projects, please go to www.massschoolbuildings.org/building and select “Capital Pipeline Status Chart”.

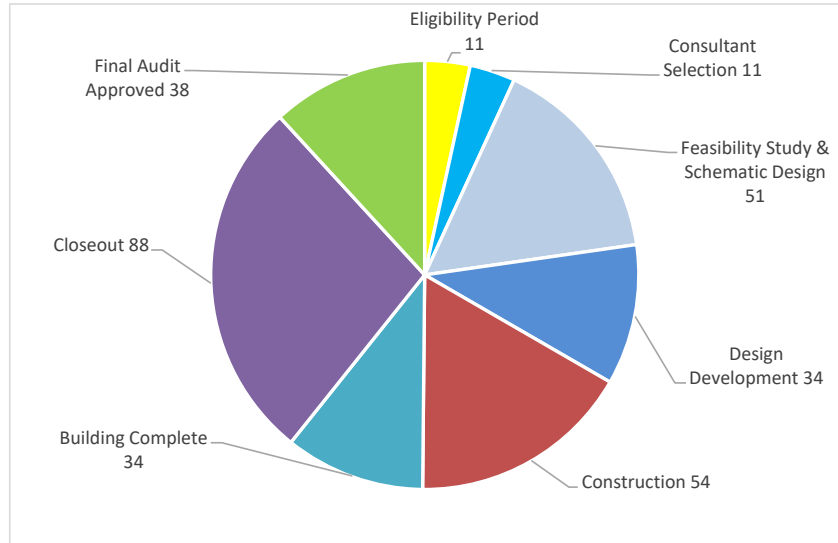

Capital Planning Updates:

The following activities are scheduled for FY 2020:

- Model School Program – Five responses were received on October 31, 2019. Site visits occurred at two of the schools prior to school closures. Staff anticipates completing the site visits upon return to work.
- The RFS for commissioning services was advertised in March 2020 with responses due on April 30, 2020. Staff anticipates recommending their selections for approval at the June 2020 Board meeting.
- Due to staff transitions, the procurement for services to assist the MSBA with the School Survey has been postponed until at least 2021.
- The 2020 SOI submittal period opened on January 8, 2020 with a deadline of February 14, 2020 for districts to submit SOIs for the Accelerated Repair Program. The closing deadline for Core Program SOIs was extended from April 8, 2020 to May 6, 2020.
 - Due to ongoing public health issues, the MSBA’s due diligence for the Accelerated Repair Program which includes a site visit to the school for the 30 qualifying schools has been postponed. Districts who submitted for the 2020 ARP program have been notified if their SOI is being further considered. Unlike prior years in which project invitations were approved at the June Board meeting, invitations to the 2020 Accelerated Repair Program are anticipated, at this time, at the October 28, 2020 Board meeting.
- The Consultant hired to review construction cost and the Consultant hired to review the MSBA’s enrollment methodology are drafting final reports for MSBA acceptance..
- MSBA Roundtables – Upcoming dates for 2020 are listed below:
 - Contractor Roundtable including invitations to superintendents and OPMS is scheduled for June 11, 2020 – Topic: *Best Safety Practices during COVID-19*
 - Commissioning Roundtable was held April 2020 – Topic: *MSBA Post-Occupancy Evaluation Program*
 - Superintendent Roundtable is scheduled for June 18, 2020 – Topic: *Facility Considerations for Superintendents: Before, During and after a Building Project*

2020 Progress Report

- * Statements of Interest (“SOIs”) 2020
 - The 2020 SOI submittal period opened on Wednesday, January 8, 2020. The deadline to file for consideration in the Accelerated Repair Program (“ARP”) was Friday, February 14, 2020. The MSBA received 90 ARP SOIs for consideration. The deadline to file for consideration in the Core Program was extended from April 8, 2020 to May 6, 2020. The MSBA received 71 Core Program SOIs for consideration.
- * Eligibility Period – Core Program
 - There are 11 districts currently in the Eligibility Period for the Core Program.
 - All 2018 SOIs received recommendations for Invitations to Feasibility Study as of the April 2020 Board meeting.
- * Feasibility Study/Schematic Design – Core Program
 - Eight districts are tentatively scheduled to receive MSBA approval for selection of their OPM.
 - One district completed their Designer Selection Process and three districts are in the process of procuring a Designer.
 - Nine districts are anticipating submittals for their Preferred Schematic Solutions between June 2020 and October 2020.
 - Five districts are anticipating submittals for their Project Funding Agreements between June 2020 and October 2020.
- * Accelerated Repair Program
 - All 25 active districts from the 2019 ARP invitations have received consultant assignments. Two districts have requested and received authorization for their removal from the ARP.
- * Construction Costs – Core Program
 - In 2019, MSBA staff anticipated DBB bids or GMP executions for 22 projects. All 22 projects have received sub-bids and 19 of those projects have proceeded to DBB bids or GMP execution. The remaining three projects revised their DBB bids or GMP executions to 2020.
 - In 2020, MSBA staff anticipates sub-bids as well as DBB bids or GMP executions for an additional 16 projects, of which one has received DBB bids.
- * Substantial Completion – Core Program
 - Nine projects are scheduled to reach substantial completion in 2020.

STATEMENTS OF INTEREST (SOIs)

2020 SOI Process

The 2020 SOI submittal period opened on January 8, 2020. The deadline to file SOIs for consideration into the Accelerated Repair Program, which is primarily for the replacement of roofs, windows/doors, and/or boilers in an otherwise structurally sound facility was Friday, February 14, 2020. The MSBA received 90 ARP SOIs for consideration. The deadline to file SOIs for consideration into the Core Program, which is primarily for projects beyond the scope of ARP, including extensive repairs, renovations, additions/renovations, and new school construction, was Wednesday, May 6, 2020. The MSBA received 71 Core Program SOIs for consideration.

Due to ongoing public health issues, the MSBA’s due diligence for the Accelerated Repair Program which includes a site visit to the school for the 30 qualifying schools has been postponed. Districts who submitted for the 2020 ARP program have been notified if their SOI is being further considered. Unlike prior years in which project invitations were approved at the June Board meeting, invitations to the 2020 Accelerated Repair Program are anticipated, at this time, at the October 28, 2020 Board meeting. If invited, districts would then need to approve funding for the Feasibility Study/Schematic Design portion of potential projects within 60 calendar days of the date of invitation into the ARP.

Due diligence for the 2020 SOIs received for the Core Program is underway with discussions ahead related to the possible impact of the ongoing public health issues.

The table below lists the number of SOIs received and Invitations granted for the calendar years 2008 through 2020.

Year	Total Number of SOIs Submitted	Number of CORE Program SOIs Submitted	Number of CORE Program Invitations	Number of Green Repair or Accelerated Repair Program SOIs Submitted	Number of Green Repair or Accelerated Program Repair Invitations	Number of SCILAB SOIs Submitted	Number of SCILAB Program Invitations
2008	431	425	104	6	6		
2009	237	206	41	31	31		
2010	224	202	19	22	22		
2011	371	184	18	187	149		
2012	280	198	11	69	36	13	11
2013	201	123	17	78	47		
2014	229	110	18	119	51		
2015	158	97	26	61	44		
2016	156	89	17	67	49		
2017	156	83	15	73	36		
2018	130	70	12	60	34		
2019	144	61	11	83	42		
2020	161	71	TBD	90	TBD		

2008: The MSBA launched the annual filing period.

2011: The MSBA opened the annual filing period twice, which included a dedicated opening for interest in the

Green Repair Program and the annual opening.

2012: The MSBA's annual filing period captures interest in the newly created Accelerated Repair Program, the 2012 Science Laboratory Initiative and the Core Program.

CORE PROGRAM

ELIGIBILITY PERIOD

There are 11 districts in the Eligibility Period and one of those districts has secured their local funding. Three of the 11 districts have requested extensions to commence Eligibility Period: East Longmeadow, Nashoba and North Adams.

An agreed-upon enrollment is a key pre-requisite for the MSBA to commence a Feasibility Study with a district. To begin the enrollment projection process, a district must file enrollment information utilizing the MSBA's online enrollment projection tool.

District	School	Eligibility Period Commencement Date	30 days	60 days	90 days		180 days		270 days	Date of Invitation to Feasibility Study (Estimated)
			ICC	SBC	Online Enrollment Projection Info	Ed Profile Questionnaire	Maintenance Documents	Enrollment Certification	Local Authorization	
Amherst	Fort River ES	5/1/20	X							TBD
East Longmeadow	East Longmeadow HS	10/1/20								TBD
Hingham	Foster ES	4/1/20	X	X					X	TBD
Maynard	Green Meadow ES	5/1/20	X							TBD
Nashoba	Nashoba RHS	8/1/20								TBD
North Adams	Greylock ES	9/1/20								TBD
Tri-County RVTSD	Tri-County RVTHS	7/1/20								TBD
Wakefield	Memorial HS	4/1/20	X	X						TBD
Whitman-Hanson	Whitman MS	6/1/20								TBD
Whittier RVTSD	Whittier RVTHS	7/1/20								TBD
Winchester	Lynch ES	4/1/20	X	X						TBD

CONSULTANT SELECTION

Owner's Project Manager ("OPM") Selection

After the district has completed all Eligibility Period requirements and has received a Board Invitation to Feasibility Study, the district procures an OPM. Since the last report, Peabody and Westfield have completed their OPM selections. Currently, there are eight districts in the Capital Pipeline that are in the process of procuring an OPM.

District	School	Anticipated Selection
Norwood	Coakley MS	July 2020
Tyngsborough	Tyngsborough MS	July 2020
Brookline	John R. Pierce School	August 2020
Webster	Bartlett HS	August 2020
Hull	Memorial MS	September 2020
Revere	Revere HS	September 2020
Haverhill	Consentino MS	October 2020
Spencer-East Brookfield	David Prouty HS	October 2020

Designer Selection

After a district has selected and executed a contract with an OPM, the district selects a Designer by utilizing either a local designer selection process for projects under \$5 million or the MSBA’s Designer Selection Panel (“DSP”) for projects over \$5 million. Since the last report, one district has completed its Designer selection (shaded in the table below). There are currently three districts in the Capital Pipeline that are in the process of procuring a Designer.

District	School	Anticipated Selection
Walpole	Bird MS	May 2020
Stoneham	Stoneham HS	June 2020
Peabody	William A. Welch ES	July / August 2020
Westfield	Franklin Ave ES	July 2020

For additional information on the selected consultant teams, see Appendix A.

FEASIBILITY STUDY

Once a district has procured an OPM and a Designer, the district and the district’s consultants must complete two Feasibility Study submittals, the Preliminary Design Program and the Preferred Schematic Report, prior to Board consideration to proceed into Schematic Design. Based on the most recent data and schedules provided to the MSBA by districts, the MSBA anticipates that nine districts will appear before the Board for their Preferred Schematic Design authorizations at the June, August, and October 2020 Board meetings.

District	School	Anticipated PS Board Date
Ashland	David Mindess ES	June 2020
Groton-Dunstable	Florence Roche ES	June 2020
Lawrence	Oliver Partnership	June 2020
Somerset	Somerset MS	June 2020
Andover	West ES	August 2020
Westwood	Hanlon ES	August 2020
Fitchburg	Crocker ES	October 2020
Medfield	Dale Street ES	October 2020
Wellesley	Upham ES	October 2020

SCHEMATIC DESIGN

Prior to consideration by the Board for Project Scope and Budget Agreement authorization, a district must submit a Schematic Design to the MSBA for review. Based on the most recent data and schedules provided to the MSBA by districts, the MSBA anticipates that five districts will appear before the Board for Project Scope and Budget Agreement authorizations at the June, August and October 2020 Board meetings.

District	School	Anticipated PS&B Board Date
Springfield	DeBerry ES	June 2020
Gloucester	East Gloucester ES	August 2020
Worcester	Doherty Memorial HS	August 2020
Boston	Josiah Quincy Upper School	October 2020
Somerset	Somerset MS	October 2020

COMMISSIONING

The MSBA assigns a Commissioning Consultant after a district has secured local funding for the Board approved project. Since the last report, the MSBA has assigned Commissioning Consultants for one additional project which is presented in the table below.

District	School	Program	Estimated Const. Cost (million)	Commissioning Consultant	Contract Amount
Essex North Shore	Essex North Shore Roof	2019 ARP	\$1.26	CBI Consulting	\$45,915

To date, the MSBA has executed 517 commissioning Consultant contracts, totaling \$38.8 million in commissioning fees. To date, 364 work orders have been completed.

The table below represents the status of commissioning assignments sorted by the fiscal year in which the commissioning work orders were issued.

Fiscal Year	No. Work Orders Issued	Value of Work Orders Issued	Total Invoiced*	Percent Complete
FY10	31	\$4,231,376	\$4,273,277	100%
FY11	95	\$6,132,890	\$6,058,460	99%
FY12	52	\$4,373,944	\$4,386,520	100%
FY13	55	\$3,364,697	\$3,408,897	100%
FY14	47	\$2,604,062	\$2,541,165	98%
FY15	44	\$2,277,711	\$2,271,979	100%
FY16	44	\$3,385,137	\$3,214,399	95%
FY17	37	\$2,290,661	\$2,041,736	89%
FY 18	44	\$4,137,550	\$2,326,740	56%
FY 19	39	\$3,604,720	\$858,225	24%
FY 20	26	\$2,381,013	\$101,784	4%
Total	517	\$38,783,761	\$31,483,180	

*Includes approved additional services over value of Work Order

DESIGN DEVELOPMENT

After a district has secured local funding and has entered into a Project Funding Agreement (“PFA”) with the MSBA, the district enters into the Design Development Phase. Currently, there are 34 projects in the Design Development Phase with a total estimated construction cost of approximately \$1.49 billion. Of those 34 projects, 20 are ARP Projects and 14 are Core Program Projects. The 14 Core Program Projects in Design Development have a total estimated construction cost of approximately \$1.45 billion and are listed below.

Elementary School Districts	Middle School Districts	High School Districts	Other Grade Configurations
Acton-Boxborough (PK-6) Amesbury (PK-2) Bridgewater-Raynham (PK-2) Easton (K-2) Gardner (PK-1) Rockland (1-4) Tewksbury (2-4) West Springfield (K-5) Westborough (K-3)	Dennis-Yarmouth (4-7) Weymouth (6-8)	Arlington (9-12) Lowell (9-12) Sharon (9-12)	

District Design Submittals

During the Design Development phase, districts will submit three design submittals (Design Development, 60% Construction Documents, and 90% Construction Documents) for the MSBA to review. MSBA staff reviews the documents to ensure the project is still in compliance with the PFA. The chart below indicates the number of submittals received and reviewed by the MSBA in each fiscal year.

Fiscal Year	DD Reviews	60% Reviews	90% Reviews	Total Reviews
FY2010	5	0	0	5
FY2011	21	24	20	65
FY2012	12	24	28	64
FY2013	20	20	19	59
FY2014	15	13	14	42
FY2015	6	12	13	31
FY2016	10	10	8	28
FY2017	11	10	12	33
FY2018	10	11	9	30
FY2019	17	16	10	43
FY2020	12	14	18	44
Totals	139	154	151	444

SUMMARY OF BID DATA

Based on the most recent data and schedules provided by districts, 16 projects are scheduled to receive sub-bids in 2020, eight projects are scheduled to receive sub-bids in 2021, and one project is scheduled to receive sub-bids in 2022. In 2019, MSBA staff anticipated DBB bids or GMP executions for 22 projects. All 22 projects have received sub-bids and 19 have proceeded to DBB bids or GMP execution. The remaining three projects revised their GMP executions to 2020.

Year	Number of Projects	Design Basis for Enrollment	Project Budget	Construction Budget
2019	22	20,170	\$2.55 billion	\$2.07 billion
2020	16	15,240	\$1.94 billion	\$1.55 billion
2021	8	9,785	\$1.27 billion	\$1.01 billion
2022	1	930	\$91 million	\$72 million
Grand Total	47	46,125	\$5.85 billion	\$4.70 billion

Note: These numbers are based on preliminary information received from the District and are subject to further review and calculation. Data is shown only for projects which have Project Scope and Budget Agreement approval by the Board. For additional information on the bid schedules of these projects, please see Appendix B.

The New Construction graph which plots Schematic Design Estimates, Construction Estimates, and Construction Bid Results from 2016 to present is not available for this Project Overview Report. The graph would have included seven new construction projects that received bids in FY 2017, nine new construction projects that received bids in FY 2018, nine new construction projects that received bids in FY 2019, and ten new construction projects that received bids in FY 2020. Danvers has received its bids, which were within its estimated construction budget, since the last report prepared for the April 15, 2020 Board meeting. The project will be reflected in future graphs.

A fully interactive version of the New Construction graph is available on the MSBA website, here:

<http://info.massschoolbuildings.org/TabPub/TableauCostData.aspx>.

The Addition/Renovation graph which plots Schematic Design Estimates, Construction Estimates, and Construction Bid Results from 2016 to present is not available for this Project Overview Report. The graph would have included three addition/renovation construction projects that received bids in FY 2017, five addition/renovation construction projects that received bids in FY 2018, and three addition/renovation project that has received bids in FY 2020. Fall River has finalized its Guaranteed Maximum Price, which is within its estimated construction budget, since the last report prepared for the April 15, 2020 Board meeting. The project will be reflected in future graphs.

A fully interactive version of the Addition/Renovation graph is available on the MSBA website, here:

<http://info.massschoolbuildings.org/TabPub/TableauCostData.aspx>

CONSTRUCTION

When a district with a Design-Bid-Build Construction project issues a Notice to Proceed, or when a Construction Manager At-Risk project has received bids for the concrete foundation package, the project is advanced to the Construction Phase. Currently, there are 54 projects in the Construction Phase with a total estimated construction cost of \$2.76 billion. Of those 54 projects, 25 are ARP Projects and 29 are Core Program Projects; however, this does not include the 34 projects that have reached substantial completion and are currently in the Building Complete Phase. The 29 Core Program Projects have a total estimated construction cost of \$2.71 billion and are listed below.

Elementary School Districts	Middle and Middle/High School Districts	High School Districts	Other Grade Configurations
Danvers (K-5)	Belmont (7-12)	Attleboro (9-12)	Braintree (5-8)
Foxborough (PK-4)	Framingham (6-8)	Boston (9-12)	Easthampton (K-8)
Harvard (PK-5)	Saugus (6-12)	Bristol County Agr. (9-12)	Natick (5-8)
Ludlow (2-5)		Cape Cod Reg. Vo Tech (9-12)	Pentucket (7-12)
Manchester Essex Reg. (K-5)		Central Berkshire (9-12)	Westport (5-12)
Marblehead (PK-3)		Fall River (9-12)	
Marlborough (K-5)		Middleborough (9-12)	
Northbridge (PK-5)		Somerville (9-12)	
Shrewsbury (K-4)		Worcester (9-12)	
Springfield (PK-5)			
Taunton (PK-6)			
Wareham (PK-4)			

Amendment to the Project Funding Agreement (PFA)

Upon receipt of construction bids or the execution of a GMP, a district submits the Contractor’s Schedule of Values to the MSBA. MSBA staff will collaborate with the district to reconcile the construction costs from the schedule of values against the estimated construction budget. Afterwards, an amendment to the PFA is executed to reflect the bids received for those projects. The chart, shown below, is the number of amendments to PFAs listed by fiscal year.

Fiscal Year	Total Amendments
FY2012	30
FY2013	31
FY2014	31
FY2015	17
FY2016	22
FY2017	8
FY2018	15
FY2019	13
FY2020	10

Substantial Completion

Nine projects are scheduled to reach Substantial Completion in 2020. They are listed in the table below.

Project	Enrollment	Contractor	OPM	Designer	Substantial Completion Date*	Building Construction Completion Date**	Variance (days)
Lexington Maria Hastings	645	Walsh Brothers	Dore & Whittier	DiNisco	2/10/20	2/13/20	3 behind
Marlborough Richer Elementary	610	Fontaine Brothers	Daedalus	Mount Vernon	4/8/20		
Somerville HS	1590	Suffolk	PMA	Symmes Maini & McKee	5/15/20		
Taunton Mulcahey	735	Agostini	CGA	Dore & Whittier	6/26/20		
Braintree East Middle School	1180	Shawmut	Hill International	Miller Dyer Spears	7/1/20		
Saugus Middle/High School	1360	Suffolk	PMA	HMFH	7/1/20		
Middleborough High School	720	Fontaine Brothers	Compass	Drummey Rosane Anderson	11/13/20		
Natick J F Kennedy Middle School	1000	Brait Builders	Compass	Ai3	11/16/20		
Cape Cod RVTHS	650	Brait Builders	Colliers	Drummey Rosane Anderson	12/4/20		

*As defined in the executed Construction Contract, once provided to the MSBA

**Date on the Certificate of Substantial Completion, once provided to the MSBA

CLOSEOUT

After the district’s contractor finishes all project work including, demolishing the old building, completing site work, and finalizing commissioning, the project proceeds to the Closeout Phase. Once all the project costs have been paid by the District, the District submits its Final Request for Payment Reimbursement via the MSBA’s Pro-Pay system. After the District submits all the items identified on the MSBA’s Index of Final Closeout, including the Final Request for Payment Reimbursement, the MSBA initiates the Draft Audit Report and sends it to the District for its consideration. The MSBA performs the final audit to determine final total grant amounts. Final payment to the District requires the MSBA Board’s approval of the final Total Facilities Grant for the project.

Currently, there are 88 projects in the Closeout Phase including 65 ARP Projects and 23 Core Program Projects. The chart, shown below, lists the Core Program Projects by year of achieved Substantial Completion:

Year	All Project Phases	Final Audit Approved	Closeout	Building Complete
Failed to Approve Local Appropriation for Total Project Budget	1	0	1	0
2012	22	22	0	0
2013	24	24	0	0
2014	19	19	0	0
2015	27	23	4	0
2016	12	10	2	0
2017	8	2	4	2
2018	11	1	9	1
2019	13	0	3	10
2020	1	0	0	1
Total	138	101	23	14

ACCELERATED REPAIR PROGRAM




The photos above depict the before and after of the roof at Marshfield's Furnace Brook Middle School, serving 904 students. The project replaced the existing roof with a modified Bituminous Membrane Roof, thus extending the useful life of the 61-year-old building. The project reached Substantial Completion in September 2018 and is going to the June 2020 Board of Directors meeting for Final Audit Approval.

Currently, there are 323 projects that are either active or completed in the ARP. The 323 projects are located in 127 districts, many of whom have been invited to the ARP multiple times. All the new information that has been updated since the last report is ***italicized and bolded***.

Repair Program	Number of Districts	Number of Projects	Total Project Budgets	Maximum Facilities Grants	Number of Projects Final Audit Approved
2019 Accelerated	25	40	<i>\$59,441,967</i>	<i>\$36,399,559</i>	
2018 Accelerated	20	30	\$83,172,480	\$47,018,557	-
2017 Accelerated	19	34	\$117,020,597	\$73,280,673	1
2016 Accelerated	28	48	\$156,598,234	\$83,007,586	<i>14</i>
2015 Accelerated	24	43	\$136,680,652	\$91,974,052	<i>31</i>
2014 Accelerated	34	47	\$108,410,084	\$65,388,035	<i>44</i>
2013 Accelerated	25	45	\$94,650,790	\$54,662,711	45
2012 Accelerated	24	36	\$63,009,653	\$38,267,952	36

2019 Accelerated Repair Program


- Invitations – 27 districts, representing 42 projects
 - Scope includes 24 roofs and 21 boilers
- SOI Removal – two districts; two projects (one roof, one boiler)
- **Approved for Project Funding Agreement – 17 districts, representing 27 projects**
- **Total Project Budgets - \$59,441,967**
- **MSBA Total Facilities Grant - \$36,399,559**
- **5 of 5 projects reporting bids within estimated budget**

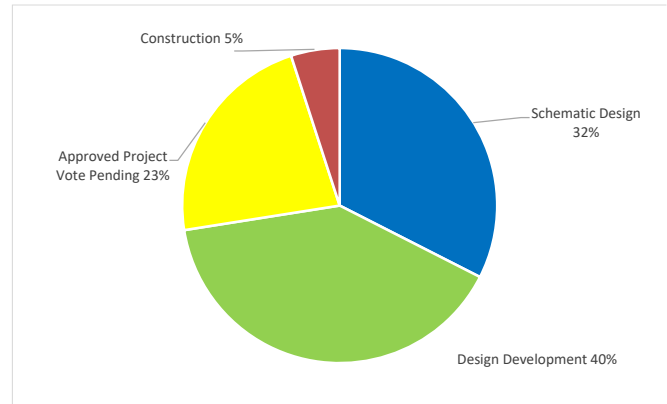

2019 ARP Status Chart

2018 Accelerated Repair Program


- Invitations – 23 districts, representing 34 projects
 - Scope includes 17 roofs, 11 windows/doors, and 14 boilers
- SOI Removal – three districts; four projects (two roofs, two windows, one boiler)
- Approved for Project Funding Agreement – 20 districts, representing 30 projects
- Total Project Budgets - \$83,172,480
- MSBA Total Facilities Grant - \$47,018,557
- **25 of 28 projects reporting bids within estimated budget**

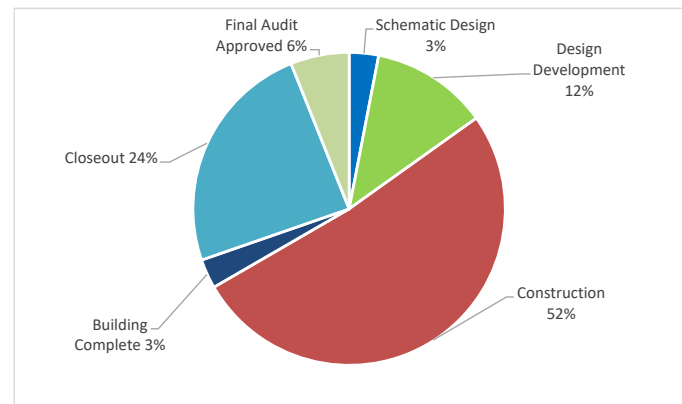

2018 ARP Status Chart

2017 Accelerated Repair Program

- Invitations – 20 districts, representing 36 projects
 - Scope includes nine roofs, 23 windows/doors, and 15 boilers
- SOI Removal - one district; two projects (one boiler; one windows/doors)
- Approved for Project Funding Agreement - 19 districts, representing 34 projects
- Total Project Budgets - \$117,020,597
- MSBA Total Facilities Grant - \$73,280,673
- Three districts, representing six projects, required a schedule extension following PFA approval
- 27 of 34 projects (79%) report bid within estimated budget

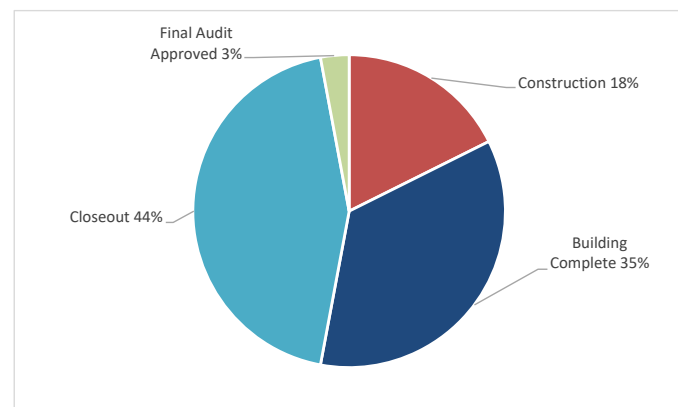


2017 ARP Status Chart

- 1 project has completed Final Audit

2016 Accelerated Repair Program


- Invitations – 28 districts, representing 49 projects
 - Scope includes 25 roofs, 19 windows/doors, and 13 boilers
- SOI Removal - one project (one boiler)
- Approved for Project Funding Agreements - 28 districts, representing 48 projects
- Total Project Budgets - \$156,598,234
- MSBA Total Facilities Grant - \$83,007,586
- Four districts, representing four projects, required a schedule extension following PFA approval
- 73% of projects bid within estimated budget
- **14 projects have completed Final Audit**

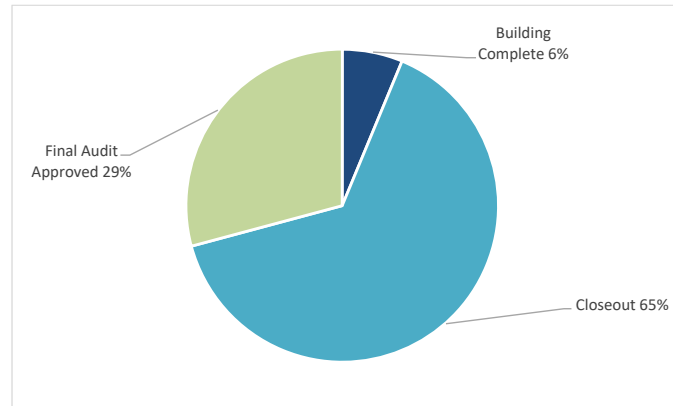

2016 ARP Status Chart

2015 Accelerated Repair Program


- Invitations – 24 districts, representing 44 projects
 - Scope includes 22 roofs, 26 windows/doors, and nine boilers
- SOI Removal – one project
- Approved for Project Funding Agreements – 24 districts, representing 43 projects
- Total Project Budgets - \$136,680,652
- MSBA Total Facilities Grants - \$91,974,052
- One district, representing one project, required two schedule extensions following PFA Approval
- 81% of projects bid within estimated budgets
- **31 projects have completed Final Audit**

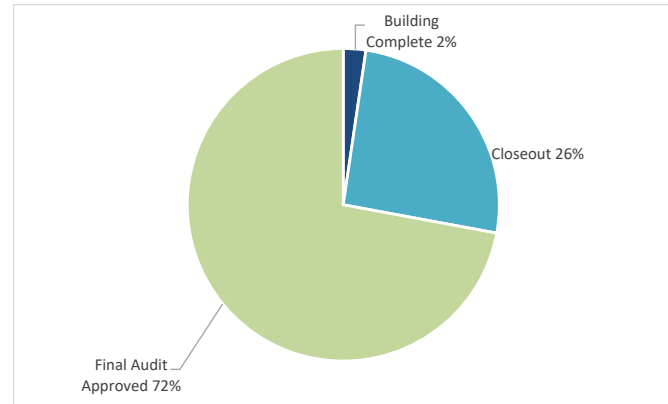

2015 ARP Status Chart

2014 Accelerated Repair Program

- Invitations – 36 districts, representing 51 projects
- SOI Removal – two districts, representing four projects
- Current 2014 ARP projects – 34 districts, representing 47 projects
 - Scope includes 20 roofs, 25 windows/doors, and 13 boilers
- Approved for Project Funding Agreements – 34 districts, representing 47 projects
- Total Project Budgets - \$108,410,084
- MSBA Total Facilities Grants - \$65,388,035
- Four districts, representing six projects, required schedule extensions following PFA approval
- 85% of projects bid within estimated budget
- 94% of projects have completed Final Audit

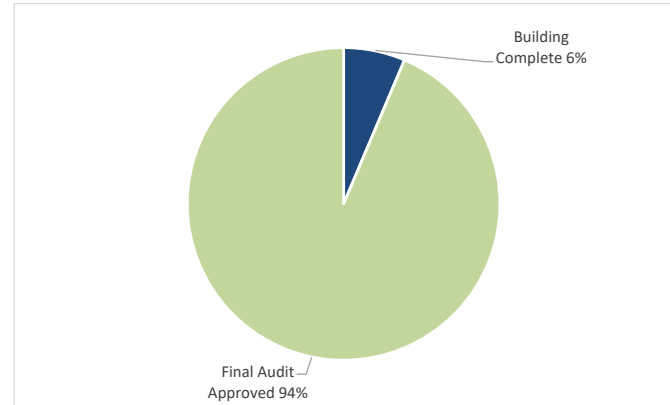

2014 ARP Status Chart

2013 Accelerated Repair Program

- Approved and completed Project Funding Agreements
 - 25 districts, representing 45 projects
- Scope included 30 roofs, 13 windows/doors, and seven boilers
- 100% of projects have completed Final Audit
 - Final Costs Submitted - \$70,489,512
 - Final MSBA Total Facilities Grants - \$37,769,94

2012 Accelerated Repair Program

- Approved and Completed Project Funding Agreements
 - 24 districts, representing 36 projects
- Scope included 21 roofs, 11 windows/doors, and seven boilers
- 100% of projects have completed Final Audit
 - Final Costs Submitted: \$47,748,996
 - Final MSBA Total Facilities Grant: \$28,518,764

Status of Green Repair Program

The Green Repair Program resulted in PFA authorizations totaling \$366,647,226 in Total Project Costs and \$222,889,218 in MSBA grants. All 189 projects from 93 districts have been approved for final grant payments.

2019 Accelerated Repair Projects – Construction Estimate vs. 2020-2021

- 5 of 5 projects reported bids within estimated budget.
- An additional 17 projects are anticipated to be reported by the August Board of Directors meeting.

District	School	Scope	Project Type	Bid Date	Construction Estimate*	Bid Amount*	Variance from Construction Estimate	Reimbursement Rate	Potential Grant Variance**
Chelmsford	South Row	Partial Roof	DBB	Feb-20	\$367,991	\$348,000	\$19,991	50.16%	\$10,027
Southborough	Mary E Finn School	Boiler	DBB	Mar-20	\$736,495	\$714,900	\$21,595	36.89%	\$7,966
Fitchburg	South Street Elementary	Partial Roof, Partial Boiler	DBB	Mar-20	\$2,592,075	\$1,765,000	\$827,075	80.00%	\$661,660
Blackstone Valley Reg	Blackstone Valley	Partial Roof	DBB	Apr-20	\$1,129,684	\$823,900	\$305,784	55.00%	\$168,181
Agawam	Agawam Junior High	Boiler	DBB	Apr-20	\$897,291	\$472,000	\$425,291	58.37%	\$248,242
				Total	\$5,723,536	\$4,123,800	\$1,599,736		\$1,096,077

2018 Accelerated Repair Projects – Construction Estimate vs. 2019-2020

- 25 of 28 projects reported bids within estimated budget.
- Remaining 2 projects are anticipated to be reported by the December Board of Directors meeting.

District	School	Scope	Project Type	Bid Date	Construction Estimate*	Bid Amount*	Variance from Construction Estimate	Reimbursement Rate	Potential Grant Variance**
Norfolk	H Olive Day	Roof	DBB	Apr-19	\$2,471,557	\$3,043,000	-\$571,443	51.63%	\$0
Nashoba Valley Tech	Nashoba Valley Tech HS	Partial Roof, Partial Windows/Doors	DBB	Apr-19	\$2,545,929	\$2,870,100	-\$324,171	55.00%	\$0
New Bedford	Trinity Day Academy	Boiler	DBB	Apr-19	\$532,049	\$496,000	\$36,049	80.00%	\$28,839
Cambridge	Graham and Parks	Partial Roof	DBB	Apr-19	\$3,310,795	\$2,236,000	\$1,074,795	44.08%	\$473,770
Danvers	Highlands	Roof	DBB	May-19	\$2,774,225	\$2,216,100	\$558,125	50.58%	\$282,300
New Bedford	John Avery Parker	Roof	DBB	May-19	\$1,067,014	\$754,400	\$312,614	80.00%	\$250,091
Newton	Bigelow Middle	Boiler	DBB	May-19	\$1,009,826	\$850,830	\$158,996	32.47%	\$51,626
Ware	Stanley M Koziol Elem	Boiler	DBB	May-19	\$561,341	\$398,810	\$162,531	78.95%	\$128,318
Lynn	Lynn Vo Tech Institute	Partial Roof	DBB	Jun-19	\$3,526,624	\$2,003,000	\$1,523,624	79.58%	\$1,212,500
Springfield	Milton Bradley School	Partial Roof	DBB	Jun-19	\$2,785,783	\$1,548,500	\$1,237,283	80.00%	\$1,212,500
East Longmeadow	Meadow Brook	Roof	DBB	Jun-19	\$2,548,488	\$1,131,000	\$1,417,488	55.00%	\$779,618
West Bridgewater	Howard School	Partial Roof	DBB	Jun-19	\$311,438	\$248,000	\$63,438	52.69%	\$33,425
Tantasqua	Tantasqua Reg Jr High	Windows/Doors	DBB	Jun-19	\$1,542,752	\$1,306,000	\$236,752	55.63%	\$131,705
Springfield	High School/Science-Tech	Boiler	DBB	Oct-19	\$4,271,083	\$2,972,000	\$1,299,083	80.00%	\$1,039,266
Bourne	Bourne High	Roof	DBB	Nov-19	\$1,771,122	\$1,358,122	\$412,194	46.79%	\$192,866
Boston	Donald McKay	Boiler	DBB	Nov-19	\$1,260,188	\$1,028,925	\$231,263	61.89%	\$143,129
Boston	Lyndon	Boiler	DBB	Nov-19	\$1,482,480	\$1,614,633	-\$132,153	61.89%	\$0
Boston	Josiah Quincy (Lower)	Boiler	DBB	Nov-19	\$1,637,122	\$1,489,755	\$147,367	61.89%	\$91,205
Boston	James Otis	Windows / Doors	DBB	Nov-19	\$2,183,743	\$1,816,122	\$367,621	61.89%	\$227,521
Boston	O'Bryant School Math/Science	Windows / Doors	DBB	Nov-19	\$1,519,283	\$1,118,313	\$400,970	61.89%	\$248,160
Boston	Rafael Hernandez	Boiler	DBB	Nov-19	\$1,070,887	\$994,242	\$76,645	61.89%	\$47,435
Ware	Ware Middle School	Windows / Doors	DBB	Jan-20	\$2,652,601	\$1,878,829	\$773,772	78.95%	\$610,893
Worcester	Challenge and Reach Academy	Roof, Windows / Doors, Boiler	DBB	Jan-20	\$4,988,468	\$3,785,000	\$1,203,468	78.95%	\$950,138
Fall River	Resiliency Preparatory School	Roof, Boiler	DBB	Feb-20	\$5,065,796	\$4,281,000	\$784,796	80.00%	\$627,837
Fall River	Westall	Partial Roof, Boiler	DBB	Feb-20	\$1,329,587	\$1,103,000	\$226,587	80.00%	\$181,270
New Salem-Wendell	Swift River	Windows / Doors	DBB	Mar-20	\$784,404	\$498,768	\$285,636	76.00%	\$217,083
Blackstone-Millville	Millville Elem	Boiler	DBB	Mar-20	\$1,271,000	\$1,197,000	\$74,000	59.21%	\$43,815
Newton	F A Day Middle	Boiler	DBB	Apr-20	\$818,254	\$606,218	\$212,036	32.47%	\$68,848
				Total	\$57,093,839	\$44,844,473	\$12,249,366		\$9,064,706

2017 Accelerated Repair Projects – Construction Estimate vs. 2018-2020

- 27 of 34 projects reported bids within estimated budget.
- All 2017 projects have reported bids.

District	School	Scope	Project Type	Bid Date	Construction Estimate*	Bid mount*	Variance for Construction Estimate	Reimbursement Rate	Potential Grant Variance**
Westford	Abbot Elementary School	Partial Roof	DBB	Mar-18	\$2,399,102	\$1,987,000	\$412,102	44.48%	\$183,303
Weymouth	Wessagusset	Boiler	DBB	Apr-18	\$747,558	\$544,111	\$203,447	54.16%	\$29,059
Weymouth	Thomas W. Hamilton Primary School	Boiler	DBB	Apr-18	\$754,474	\$578,691	\$175,783	55.63%	\$97,788
East Longmeadow	Meadow Brook	Windows/ Doors	DBB	Apr-18	\$2,228,280	\$1,770,877	\$457,403	55.00%	\$251,572
Quincy	North Quincy High	Partial Roof	DBB	May-18	\$1,266,623	\$1,346,000	-\$79,377	68.33%	\$0
Lawrence	Arlington Elementary School	Roof, Boiler	DBB	May-18	\$2,541,724	\$2,048,000	\$493,724	80.00%	\$394,979
Boston	William E. Russell	Roof	DBB	May-18	\$1,598,728	\$1,576,700	\$22,028	65.47%	\$14,422
Worcester	Thorndyke Road	Partial Windows/ Doors	DBB	Jun-18	\$2,010,580	\$2,468,151	-\$457,571	78.95%	\$0
Worcester	Lincoln Street	Partial Roof, Windows/ Doors	DBB	Jun-18	\$3,082,067	\$2,540,513	\$541,554	78.95%	\$427,557
Worcester	Elm Park Community	Windows/ Doors	DBB	Jun-18	\$2,623,542	\$2,623,336	\$206	78.95%	\$163
Athol-Royalston	Athol High	Roof, Windows/ Doors, Boiler	DBB	Oct-18	\$8,103,411	\$6,277,000	\$1,826,411	79.58%	\$1,453,458
Norton	J C Solmonese	Windows /Doors	DBB	Oct-18	\$1,876,411	\$2,005,257	-\$126,846	55.63%	\$0
Norton	Henri A. Yelle	Windows/ Doors	DBB	Oct-18	\$3,116,095	\$3,182,481	-\$66,386	55.63%	\$0
Norton	L G Nourse Elementary	Windows/ Doors	DBB	Oct-18	\$1,709,260	\$1,747,262	-\$38,002	55.63%	\$0
Holyoke	Morgan Elem	Windows/ Doors	DBB	Nov-18	\$1,960,881	\$1,962,810	-\$1,929	80.00%	\$0
Holyoke	Lt Clayre Sullivan Elem	Windows/ Doors	DBB	Nov-18	\$4,167,411	\$3,973,625	\$193,786	80.00%	\$155,029
Seekonk	Mildred Aitken School	Partial Windows/ Doors	DBB	Dec-18	\$926,745	\$965,500	-\$38,755	52.69%	\$0
Mansfield	Mansfield High	Partial Windows/ Doors	DBB	Dec-18	\$1,562,260	\$1,347,000	\$215,260	50.79%	\$109,331
Randolph	Martin E Young Elem	Windows/ Doors	DBB	Jan-19	\$1,828,630	\$1,393,298	\$435,332	76.84%	\$334,509
Springfield	South End Middle School	Windows/ Doors	DBB	Oct-18	\$1,934,908	\$1,198,000	\$736,908	80.00%	\$589,526
Lynn	Hood	Roof, Windows/ Doors	DBB	Dec-18	\$4,439,681	\$3,546,000	\$893,681	79.58%	\$711,191
Holyoke	Kelly Elem	Windows/ Doors, Boiler	DBB	Apr-18/Nov-18	\$5,286,531	\$4,391,000	\$895,531	80.00%	\$716,425
Randolph	Margaret L Donovan	Windows/ Doors, Boiler	DBB	Aug-18/Dec-18	\$3,843,498	\$3,225,498	\$618,254	76.84%	\$475,066
Boston	John Marshall	Windows/ Doors	DBB	Jan-19	\$4,458,029	\$3,969,000	\$489,029	65.47%	\$320,167
Boston	Hugh Roe O'Donnell	Boiler	DBB	Dec-18	\$911,516	\$892,621	\$18,895	65.47%	\$12,371

District	School	Scope	Project Type	Bid Date	Construction Estimate*	Bid amount*	Variance for Construction Estimate	Reimbursement Rate	Potential Grant Variance**
Boston	Charles Sumner	Boiler	DBB	Dec-18	\$1,013,960	\$910,700	\$103,260	65.47%	\$67,604
Boston	Maurice J Tobin	Boiler	DBB	Dec-18	\$1,463,372	\$1,032,808	\$430,564	65.47%	\$281,890
East Bridgewater	Central	Boiler	DBB	Feb-19	\$1,223,611	\$759,619	\$463,992	56.26%	\$261,042
Blackstone-Millville	John F Kennedy Elem	Windows/ Doors, Boiler	DBB	Mar-19	\$3,828,470	\$2,105,900	\$1,722,570	57.74%	\$994,612
Lawrence	School for Exceptional Studies	Roof	DBB	Mar-19	\$3,782,209	\$3,161,000	\$621,209	80.00%	\$496,967
Fall River	Samuel Watson	Roof, Windows / Doors, Boiler	DBB	May-20	\$6,048,869	\$4,390,285	\$1,658,584	79.58%	\$1,319,901
				Total	\$90,612,523	\$77,483,393	\$13,129,130		\$10,230,222

Accelerated Repair Projects – Schedule Extension Update

The MSBA has granted districts conditional extensions to their PFAs pending compliance with the following stipulations:

- The district must submit a detailed, revised, construction timeline that explains how the work will be completed at each school; and
- Any costs that are related to a district requesting an extension to the construction schedule will be the sole responsibility of the district, and those costs are categorically ineligible for reimbursement by the MSBA.

Schedule delays for these districts can be attributed to local funding issues, lead time for windows, and construction delays on site. In no event have the extended schedules resulted in an increase to the Estimated Maximum Total Facilities Grant, as authorized by the Board.

Six of the 34 2017 ARP Projects revised their construction schedules to reflect substantial completion in 2019 or beyond. Staff has reported previously on the shaded projects listed below, which remain in Construction or Design Development.

District	School	Scope	Original Construction Completion Date	Updated Construction Completion Date	Reason for Schedule Extension
Fall River	Samuel Watson	Roof, Windows/Doors, Boiler	31-Dec-19	31-Aug-21	The District and its consultants sought and received a MAAB variance prior to proceeding with its appropriation vote, which delayed the development of construction documents.

One of the 30 2018 ARP Projects revised their construction schedules to reflect substantial completion in 2019 or beyond. Staff has reported previously on the shaded projects listed below, which remain in Construction or Design Development.

District	School	Scope	Original Construction Completion Date	Updated Construction Completion Date	Reason for Schedule Extension
Norfolk County Agricultural	Norfolk County Agricultural High School	Partial Roof, Partial Windows/Doors,	20-Aug-20	24-Aug-21	The District and its consultants have determined that bidding for construction in 2021 would better serve the project budget following appropriation of the project funds.

PROJECT VARIANCES

Core Program – Total Project Budget Update

Upon receiving the Board’s approval of the Project Scope and Budget, the MSBA and participating districts enter into a Project Funding Agreement, which establishes the Total Project Budget and the Estimated Maximum Total Facilities Grant for an approved project. Staff has reported on budget increases for the 23 projects shaded below at previous Board Meetings. No shading appears where project information is new or updated since the previous Board Meeting. In no event has the increase in a budget resulted in an increase to the Estimated Maximum Total Facilities Grant, as authorized by the Board.

District	School	Scope	Project Funding Agreement		PFA Bid Amendment/ Final Audit		Reason for Increase to Total Project Budget
			Total Project Budget	Total Maximum Facilities Grant	Total Project Budget	Total Maximum Facilities Grant	
Andover	Bancroft ES	New	\$44,659,837	\$16,773,753	\$50,299,859	\$16,575,965	The District has appropriated additional funds to cover the costs associated with increased construction costs and additional contingencies for litigation/settlement costs and other ineligible costs.
Berlin-Boylston	Tahanto Regional HS	New	\$43,954,901	\$21,148,751	\$43,519,302	\$18,972,041	District submitted final project costs that exceeded the total project budget established at bid. Final Costs did not exceed the original total project budget established at Project Funding Agreement.
Blue Hills	Blue Hills Regional Technical School	Add/Reno	\$84,862,768	\$44,210,180	\$87,221,616	\$43,784,558	The District has appropriated additional funds to cover the costs associated with increased construction costs.
Burlington	Marshall Simonds MS	Add/Reno	\$32,865,272	\$17,143,365	\$34,221,929	\$15,362,127	The District appropriated at its May 2012 annual town meeting through Articles 18: 19, additional funds for the costs associated with the construction of the new field complex and field lighting replacement.
Essex North Shore Agricultural & Technical School District	Essex North Shore Agricultural & Technical HS	New	\$125,000,000	\$77,500,000	\$133,770,000	\$77,500,000	The Board was informed at the March 30, 2011 meeting that the Total Project Budget had increased due to additional ineligible scope that would be funded by DCAM.
			\$125,000,000	\$77,500,000	\$134,501,368	\$77,500,000	The District has appropriated additional funds to cover the costs associated with increased construction costs for horse tack barn renovations.
Greater New Bedford	Greater New Bedford Vocational and Technical High School	Add/Reno	\$17,099,808	\$13,543,920	\$16,396,429	\$12,258,642	District submitted final project costs that exceeded the total project budget established at bid. Final Costs did not exceed the original total project budget established at Project Funding Agreement.
Hopkinton	Center ES	New	\$45,629,373	\$14,058,455	\$47,129,373	\$14,058,455	The District has appropriated \$1,500,000 of additional funds to cover the costs associated with the construction of a building addition due to an unanticipated increase in enrollment.
Lexington	Joseph Estabrook ES	New	\$40,792,248	\$12,250,739	\$43,392,248	\$12,148,491	The District has executed a GMP that exceeds the Construction Budget of the PFA. The District has appropriated additional funds to cover the costs associated with increased construction costs and additional contingencies.
Newburyport	Nock/Molin MS	Add/Reno	\$26,997,326	\$13,697,934	\$28,170,749	\$12,520,326	The District has received additional funding to cover additional construction change order costs.
North Reading	North Reading MS/HS	Add/Reno	\$107,727,074	\$49,323,123	\$123,227,074	\$49,323,123	This is a CMR project. The estimated, reconciled construction costs tracked over budget at DD (\$9,746,655 over), 60% (\$4,655,965 over), and 90% (\$15,136,846 over). A Town override vote in March 2013 obtained an additional \$15,500,000 in local funding to proceed.
Norfolk County Agricultural	Norfolk County Agricultural HS	Add/Reno	\$28,552,385	\$15,369,712	\$30,589,078	\$13,867,050	The District has executed a Tender Agreement and Completion Agreement Contract, increasing its Total Project Budget, following the termination of its original construction contract.
Northborough	Lincoln Street ES	Add/Reno	\$25,530,553	\$10,407,408	\$25,530,553	\$10,407,408	The MSBA Board Approved Total Project Budget increased by \$60,400 from \$25,470,153 to \$25,530,553 due to the addition of an alternate, for a new ball field added at the District’s request.
Plymouth	South HS	New	\$107,800,000	\$46,867,514	\$111,063,271	\$46,328,160	The District appropriated \$3,263,371 of additional funding to fund change order work to incorporate scope previously identified in the construction bid documents as Alternate 4 (synthetic turf field) and a portion of Alternate 5 (electrical infrastructure to support future lights at synthetic turf field). Note that the increased Total Project Budget will not increase the Maximum Facilities Grant.
Revere	Staff Sergeant James J. Hill ES	New	\$45,402,396	\$29,551,048	\$45,402,396	\$29,551,048	At Project Scope and Budget, the Total Project Budget was approved at \$44,382,396. The City of Revere has increased the land acquisition budget. Therefore, the projected total project budget at PFA has increased to \$45,402,396. Note that the MSBA grant has not changed since the Project Scope and Budget Agreement.
Salem	Saltonstall ES	Repair	\$15,503,406	\$11,794,492	\$15,752,033	\$10,709,091	The District has executed a GMP that exceeds the Construction Budget of the PFA. The District has appropriated additional funds to cover the costs associated with increased construction costs and additional contingencies.
Somerville	East Somerville Community School	Add/Reno	\$33,185,258	\$15,237,996	\$38,006,621	\$15,237,996	At the March 28, 2012 Board Meeting, the Board approved an amendment to the PFA and a \$6.25M District loan.

District	School	Scope	Project Funding Agreement		PFA Bid Amendment/ Final Audit		Reason for Increase to Total Project Budget
			Total Project Budget	Total Maximum Facilities Grant	Total Project Budget	Total Maximum Facilities Grant	
Sutton	Sutton MS	Add/Reno	\$59,945,474	\$29,843,511	\$60,130,536	\$27,002,506	The District has executed a Tender Agreement and Completion Agreement Contract, increasing its Total Project Budget, following the termination of its original construction contract.
Uxbridge	Uxbridge HS	New	\$43,000,000	\$22,362,328	\$44,986,479	\$22,362,328	The District has appropriated additional funds to cover the costs associated with the construction of athletic fields originally included in the PFA but which were not included in the bid as the District's construction contract would have exceeded the budget.
Weston	Field ES	New	\$31,504,146	\$8,310,510	\$32,654,146	\$8,105,549	District-approved Construction Change Orders exceeded available contingency amount.
Winchester	Winchester HS	Add/Reno	\$129,923,146	\$44,493,270	\$131,513,741	\$43,100,458	The MSBA Board Approved total Project Budget increased due to a construction change order for additional soil abatements at Skillings Field. Note that the increased Total Project Budget will not increase the Maximum Total Facilities Grant.
Winthrop	Winthrop MS/HS	New	\$81,818,740	\$42,582,841	\$81,432,986	\$41,249,005	The MSBA Board Approved Total Project Budget increased due to revised FEMA flood plain requirements which necessitated the elevation of the new building to be raised. Note that the increased Total Project Budget will not increase the Maximum Total Facilities Grant.
Woburn	Wyman-Hurld ES	New	\$33,705,396	\$14,387,427	\$39,647,723	\$14,387,427	The District had completed a project review with its Conservation Commission and an Order of Conditions was issued on June 12, 2015. A neighborhood group appealed this Order and was reviewed by The DEP. The District experienced delays in completing its City Council vote for its appropriation and incurred additional costs.
Oxford	Oxford MS	Add/Reno	\$6,128,870	\$3,483,589	\$7,340,000	\$3,359,171	The District received additional funding to cover additional construction costs including accessibility upgrades. District submitted final project costs that exceeded the total project budget established at bid. Final Costs did not exceed the original total project budget established at Project Funding Agreement.
Tewksbury	Tewksbury HS	New	\$84,173,174	\$44,194,627	\$67,710,158	\$36,219,487	District submitted final project costs that exceeded the total project budget established at bid. Final Costs did not exceed the original total project budget established at Project Funding Agreement.

APPENDIX A PROJECT STATUS LIST

Date of Report: 6/2/2020
 Total Projects: 367

SOI	MSBA ID	District	School	Project Phase	Project Type	Project Scope	Procurement Type	OPM	Designer	CM/GC	Commissioning Consultant
2008	200800010405	Abington	Frolio Middle School	Closeout	Core Program	New Construction	DBB	Knight, Bagge & Anderson Inc.	Ai3 Architects LLC	Brait Builders Corp.	Horizon Engineering Associates, LLP
2016	201606000020	Acton-Boxborough	C.T. Douglas Elementary School	Design Development	Core Program	New Construction	CM@R	Skanska USA Building, Inc	Arrowstreet Inc.	-	Colliers Project Leaders NE, LLC
2019	201900030025	Acushnet	Acushnet Elementary School	Schematic Design	Accelerated Repair	Roof		Arcadis U.S., Inc.	Next Phase Studios, Inc.	-	-
2019	201900050405	Agawam	Agawam Junior High	Construction	Accelerated Repair	Boiler	DBB	-	-	-	BVH Integrated Services, P.C.
2015	201500070005	Amesbury	Amesbury Elementary	Design Development	Core Program	New Construction		NV5 (fka Joslin, Lesser + Associates Inc.)	DiNisco Design, Inc.	-	BVH Integrated Services, P.C.
2019	201900080020	Amherst	Fort River Elementary	Eligibility Period	Core Program			-	-	-	-
2017	201700090025	Andover	West Elementary	Feasibility Study	Core Program			PMA Consultants, LLC	Symmes Maini & McKee Associates, Inc.	-	-
2015	201500100505	Arlington	Arlington High	Design Development	Core Program	New Construction	CM@R	Skanska USA Building, Inc	HMFH Architects, Inc.	Consigli Construction Company, Inc.	Rist-Frost-Shumway Engineering, P.C.
2017	201700140015	Ashland	David Mindess	Feasibility Study	Core Program			Compass Project Management, Inc.	Flansburgh Associates, Inc.	-	-
2017	201706150505	Athol-Royalston	Athol High	Closeout	Accelerated Repair	Roof, Windows / Doors, Boiler	DBB	NETCO Construction Project Managers, Inc.	CSS Architects Incorporated	J.D. Rivet & Co., Inc.	Colliers Project Leaders NE, LLC
2014	201400160505	Attleboro	Attleboro High	Construction	Core Program	New Construction	CM@R	Skanska USA Building, Inc	Kaestle Boos Associates, Inc.	Consigli Construction Company, Inc.	Cadmus Group LLC
2015	201500260505	Belmont	Belmont High	Construction	Core Program	Addition / Renovation	CM@R	CHA Consulting, Inc.	Perkins+Will	Skanska USA Building, Inc.	Bard, Rao + Athanas Consulting Engineers, LLC
2013	201300300305	Beverly	Briscoe Middle	Closeout	Core Program	New Construction	CM@R	CBRE/HEERY	Ai3 Architects LLC	Bacon-Agostini Construction Joint Venture	Thompson & Lichtner Co., Inc.
2019	201908050605	Blackstone Valley Regional Voc Tech	Blackstone Valley	Construction	Accelerated Repair	Roof	DBB	Hill International Company	Mount Vernon Group Architects, Inc.	-	Colliers Project Leaders NE, LLC
2017	201706220008	Blackstone-Millville	John F Kennedy Elementary	Closeout	Accelerated Repair	Windows / Doors, Boiler	DBB	Skanska USA Building, Inc	TSKP Studio, LLC	Homer Contracting	Colliers Project Leaders NE, LLC
2018	201806220010	Blackstone-Millville	Millville Elementary	Design Development	Accelerated Repair	Boiler	DBB	PCA 360	NV5	-	Symmes, Maini & McKee Associates
2013	201300350546	Boston	Boston Arts Academy	Construction	Core Program	New Construction	CM@R	PMA Consultants, LLC	Perkins Eastman/DPC	Lee Kennedy Co., Inc.	-
2017	201700350036	Boston	Carter School	Feasibility Study	Core Program			Hill International Company	Perkins+Will	-	-
2015	201500350052	Boston	Charles Sumner	Closeout	Accelerated Repair	Windows / Doors	DBB	P3 Inc.	Dietz & Company Architects, Inc.	Lambrian Construction Corp.	Simpson Gumpertz & Heger Inc.
2015	201500350020	Boston	Curley K-8 School	Closeout	Accelerated Repair	Windows / Doors	DBB	P3 Inc.	Dietz & Company Architects, Inc.	GVW, Inc.	Simpson Gumpertz & Heger Inc.
2019	201900350020	Boston	Curley K-8 School	Schematic Design	Accelerated Repair	Roof		NETCO Construction Project Managers, Inc.	Raymond Design Associates, Inc.	-	-
2015	201500350072	Boston	David A Ellis	Closeout	Accelerated Repair	Windows / Doors	DBB	P3 Inc.	Dietz & Company Architects, Inc.	GVW, Inc.	Simpson Gumpertz & Heger Inc.
2015	201500350080	Boston	Donald Mckay	Closeout	Accelerated Repair	Windows / Doors	DBB	P3 Inc.	Dietz & Company Architects, Inc.	Paul J. Rogan Co., Inc.	Simpson Gumpertz & Heger Inc.
2018	201800350080	Boston	Donald Mckay	Construction	Accelerated Repair	Boiler	DBB	NV5 (fka Joslin, Lesser + Associates Inc.)	CSS Architects Incorporated	Enterprise Equipment Co., Inc.	Fitzmeyer & Tocci Associates, Inc.
2015	201500350651	Boston	Dorchester Academy	Closeout	Accelerated Repair	Windows / Doors	DBB	P3 Inc.	Dietz & Company Architects, Inc.	Lambrian Construction Corp.	Simpson Gumpertz & Heger Inc.
2015	201500350415	Boston	Grover Cleveland	Closeout	Accelerated Repair	Windows / Doors	DBB	P3 Inc.	Dietz & Company Architects, Inc.	Paul J. Rogan Co., Inc.	Simpson Gumpertz & Heger Inc.
2010	201000350074	Boston	Henry Dearborn Middle School	Closeout	Core Program	New Construction	CM@R	CHA Consulting, Inc.	Jonathan Levi Architects LLC	Gilbane Building Company	Symmes, Maini & McKee Associates
2018	201800350156	Boston	James Otis	Construction	Accelerated Repair	Windows / Doors	DBB	NV5 (fka Joslin, Lesser + Associates Inc.)	CSS Architects Incorporated	GVW, Inc.	Simpson Gumpertz & Heger Inc.
2017	201700350178	Boston	John Marshall	Construction	Accelerated Repair	Windows / Doors	DBB	Vertex Construction Services	The S/L/A/M Collaborative	WCI Corp.	Simpson Gumpertz & Heger Inc.
2016	201600350179	Boston	John W McCormack	Closeout	Accelerated Repair	Roof	DBB	NV5 (fka Joslin, Lesser + Associates Inc.)	ICON architecture, inc.	Gibson Roofs, Inc.	Simpson Gumpertz & Heger Inc.
2018	201800350286	Boston	Josiah Quincy	Construction	Accelerated Repair	Boiler	DBB	NV5 (fka Joslin, Lesser + Associates Inc.)	CSS Architects Incorporated	Enterprise Equipment Co., Inc.	Fitzmeyer & Tocci Associates, Inc.

2018	201800350262	Boston	Lyndon	Construction	Accelerated Repair	Boiler	DBB	NV5 (fka Joslin, Lesser + Associates Inc.)	CSS Architects Incorporated	Enterprise Equipment Co., Inc.	Fitzmeyer & Tocci Associates, Inc.
2019	201900350655	Boston	Lyon Upper 9-12	Schematic Design	Accelerated Repair	Boiler		NETCO Construction Project Managers, Inc.	Raymond Design Associates, Inc.	-	-
2017	201700350229	Boston	Maurice J Tobin O'Bryant School Math/Science	Construction	Accelerated Repair	Boiler	DBB	Vertex Construction Services	The S/L/A/M Collaborative	Enterprise Equipment Co., Inc.	Rist-Frost-Shumway Engineering, P.C.
2018	201800350575	Boston	Rafael Hernandez	Construction	Accelerated Repair	Windows / Doors	DBB	NV5 (fka Joslin, Lesser + Associates Inc.)	CSS Architects Incorporated	GVW, Inc.	Simpson Gumpertz & Heger Inc.
2016	201600350268	Boston	Paul A Dever	Closeout	Accelerated Repair	Roof	DBB	NV5 (fka Joslin, Lesser + Associates Inc.)	ICON architecture, inc.	Gibson Roofs, Inc.	Simpson Gumpertz & Heger Inc.
2010	201000350565	Boston	Quincy Upper School	Schematic Design	Core Program			Skanska USA Building, Inc	HMFH Architects, Inc.	-	-
2018	201800350691	Boston	Rafael Hernandez	Construction	Accelerated Repair	Boiler	DBB	NV5 (fka Joslin, Lesser + Associates Inc.)	CSS Architects Incorporated	Enterprise Equipment Co., Inc.	Fitzmeyer & Tocci Associates, Inc.
2019	201900350363	Boston	William McKinley	Schematic Design	Accelerated Repair	Roof		NETCO Construction Project Managers, Inc.	Raymond Design Associates, Inc.	-	-
2015	201500350380	Boston	Young Achievers	Closeout	Accelerated Repair	Windows / Doors	DBB	P3 Inc.	Dietz & Company Architects, Inc.	Lockheed Window Corporations	Simpson Gumpertz & Heger Inc.
2018	201800360505	Bourne	Bourne High School	Construction	Accelerated Repair	Roof	DBB	P3 Inc.	CIVITECTS PC	Larochelle Construction Co., Inc.	Russo Barr Associates, Inc.
2014	201400360010	Bourne	Peebles Elementary School	Closeout	Core Program	New Construction	DBB	Symmes Maini & McKee Associates, Inc.	Flansburgh Associates, Inc.	Brait Builders Corp.	BVH Integrated Services, P.C.
2016	201600380013	Boxford	Spofford Pond	Closeout	Accelerated Repair	Roof, Windows / Doors	DBB	NETCO Construction Project Managers, Inc.	Russo Barr Associates, Inc.	Homer Contracting	CBI Consulting LLC
2013	201300400305	Braintree	East Middle School	Construction	Core Program	Addition / Renovation	CM@R	Hill International Company	Miller Dyer Spears Inc.	Shawmut Design and Construction	Fitzmeyer & Tocci Associates, Inc.
2016	201600400310	Braintree	South Middle School	Approved Project Vote Pending	Core Program	New Construction		Hill International Company	Miller Dyer Spears Inc.	-	Rist-Frost-Shumway Engineering, P.C.
2016	201606250002	Bridgewater-Raynham	Mitchell Elementary School	Design Development	Core Program	New Construction	DBB	CHA Consulting, Inc.	Raymond Design Associates, Inc.	-	Consulting Engineering Services, LLC
2014	201409100705	Bristol County Agricultural	Bristol County Agricultural High	Construction	Core Program	Addition / Renovation	CM@R	Colliers Project Leaders NE, LLC	HMFH Architects, Inc.	Gilbane Building Company	NV5
2017	201708100605	Bristol-Plymouth Regional Voc Tech	Bristol-Plymouth Vocational Technical	Feasibility Study	Core Program			-	-	-	-
2019	201900440055	Brockton	Huntington	Schematic Design	Accelerated Repair	Roof		PCA 360	TSKP Studio, LLC	-	-
2018	201800460040	Brookline	Pierce	OPM Selection	Core Program			-	-	-	-
2016	201600490090	Cambridge	Fletcher/Maynard Academy	Closeout	Accelerated Repair	Roof	DBB	Arcadis U.S., Inc.	Atane Engineers, P.C.	John F. Shea Company, Inc.	Gale Associates, Inc.
2018	201800490080	Cambridge	Graham and Parks	Closeout	Accelerated Repair	Roof	DBB	exPERTcon, Inc.	The S/L/A/M Collaborative	-	Thompson & Lichtner Co., Inc.
2014	201408150605	Cape Cod Regional Voc Tech	Cape Cod Region Vocational Technical	Construction	Core Program	New Construction	DBB	Colliers Project Leaders NE, LLC	Drumme Rosane Anderson, Inc.	Brait Builders Corp.	NV5
2013	201300520015	Carver	Carver Elementary School	Final Audit Approved	Core Program	New Construction	DBB	PMA Consultants, LLC	HMFH Architects, Inc.	CTA Construction Co., Inc.	Symmes, Maini & McKee Associates
2016	201600520405	Carver	Carver Middle/High School	Final Audit Approved	Accelerated Repair	Roof, Windows / Doors, Boiler	DBB	Leftfield, LLC	Johnson Roberts Associates, Inc.	J.J. Cardosi, Inc.	Symmes, Maini & McKee Associates
2015	201506350505	Central Berkshire	Wahconah Regional High	Construction	Core Program	New Construction	CM@R	Skanska USA Building, Inc	Drumme Rosane Anderson, Inc.	Barr & Barr Inc.	Horizon Engineering Associates, LLP
2019	201900560015	Chelmsford	South Row	Approved Project Vote Pending	Accelerated Repair	Roof	DBB	JACOBS Project Management Co.	Russo Barr Associates, Inc.	-	Simpson Gumpertz & Heger Inc.
2008	200800570050	Chelsea	Clark Avenue School	Closeout	Core Program	New Construction	CM@R	Pinck & Co., Inc.	HMFH Architects, Inc.	W. T. Rich Company Inc.	Cannon Design
2015	201500610010	Chicopee	Belcher	Final Audit Approved	Accelerated Repair	Roof	DBB	NV5 (fka Joslin, Lesser + Associates Inc.)	Kaestle Boos Associates, Inc.	J.D. Rivet & Co., Inc.	Building Enclosure Associates, LLC
2016	201600610015	Chicopee	Bowe	Closeout	Accelerated Repair	Windows / Doors	DBB	Compass Project Management, Inc.	Turowski2 Architecture, Inc.	W.J. Mountford Company	Thompson & Lichtner Co., Inc.
2016	201600610050	Chicopee	Chicopee Academy	Closeout	Accelerated Repair	Roof	DBB	Compass Project Management, Inc.	Turowski2 Architecture, Inc.	W.J. Mountford Company	Thompson & Lichtner Co., Inc.
2009	200900610021	Chicopee	Dupont Middle	Closeout	Core Program	Renovation	DBB	Arcadis U.S., Inc.	Caolo & Bieniek Associates, Inc.	Fontaine Brothers, Inc.	Symmes, Maini & McKee Associates
2015	201500610310	Chicopee	Fairview Elementary	Final Audit Approved	Accelerated Repair	Roof	DBB	NV5 (fka Joslin, Lesser + Associates Inc.)	Kaestle Boos Associates, Inc.	J.D. Rivet & Co., Inc.	Building Enclosure Associates, LLC
2018	201800710010	Danvers	Highlands	Closeout	Accelerated Repair	Roof	DBB	JACOBS Project Management Co.	ICON architecture, inc.	Northern Contracting	R.J. Kenney Associates, Inc.
2015	201500710032	Danvers	Ivan G Smith	Construction	Core Program	New Construction	CM@R	PMA Consultants, LLC	Tappe Architects, Inc.	W. T. Rich Company Inc.	Colliers Project Leaders NE, LLC

2016	201600720050	Dartmouth	Dartmouth Middle	Final Audit Approved	Accelerated Repair	Roof	DBB	Atlantic Construction and Management, Inc.	CSS Architects Incorporated	Greenwood Industries, Inc.	CBI Consulting LLC
2012	201200730005	Dedham	Early Childhood Center	Closeout	Core Program	New Construction	DBB	Construction Monitoring Services, Inc.	Knight, Bagge & Anderson, Inc.	H.V. Collins Co., Inc.	Symmes, Maini & McKee Associates
2015	201506450305	Dennis-Yarmouth	Mattacheese Middle School	Design Development	Core Program	New Construction	DBB	PMA Consultants, LLC	Perkins Eastman/DPC	-	Consulting Engineering Services, LLC
2019	201900790035	Dracut	Brookside Elementary	Approved Project Vote Pending	Accelerated Repair	Roof	DBB	Vertex Construction Services	CIVITECTS PC	-	Russo Barr Associates, Inc.
2019	201900790045	Dracut	George H. Englesby Elementary School	Approved Project Vote Pending	Accelerated Repair	Roof	DBB	Vertex Construction Services	CIVITECTS PC	-	Russo Barr Associates, Inc.
2017	201700830005	East Bridgewater	Central	Closeout	Accelerated Repair	Boiler	DBB	PMA Consultants, LLC	Architectural Engineers, Inc.	George T. Wilkinson, Inc.	Bard, Rao + Athanas Consulting Engineers, LLC
2019	201900830005	East Bridgewater	Central	Approved Project Vote Pending	Accelerated Repair	Roof	DBB	PMA Consultants, LLC	Kaestle Boos Associates, Inc.	-	CBI Consulting LLC
2019	201900870505	East Longmeadow	East Longmeadow High	Eligibility Period	Core Program			-	-	-	-
2017	201700870013	East Longmeadow	Meadow Brook	Closeout	Accelerated Repair	Windows / Doors	DBB	Vertex Construction Services	Kaestle Boos Associates, Inc.	Lizotte Glass	Building Enclosure Associates, LLC
2018	201800870013	East Longmeadow	Meadow Brook	Construction	Accelerated Repair	Roof	DBB	Pinck & Co., Inc.	Turowski2 Architecture, Inc.	Titan Roofing, Inc.	CBI Consulting LLC
2014	201400860010	Easthampton	Maple	Construction	Core Program	New Construction	DBB	Colliers Project Leaders NE, LLC	Caolo & Bieniek Associates, Inc.	Fontaine Brothers, Inc.	Horizon Engineering Associates, LLP
2016	201600880003	Easton	Center School	Design Development	Core Program	New Construction		PMA Consultants, LLC	Perkins Eastman/DPC	-	Symmes, Maini & McKee Associates
2019	201908170505	Essex North Shore Agricultural and Technical	Essex Technical High School	Design Development	Accelerated Repair	Roof		Atlantic Construction and Management, Inc.	ICON architecture, inc.	-	-
2014	201400950505	Fall River	B M C Durfee High	Construction	Core Program	Addition / Renovation	CM@R	Leftfield, LLC	Ai3 Architects LLC	Suffolk Construction Company	Jacobs Engineering Group Inc.
2017	201700950140	Fall River	James Tansey	Construction	Accelerated Repair	Windows / Doors, Boiler	DBB	exPERTcon, Inc.	Tighe & Bond, Inc.	Collins Construction Co., Inc.	Fitzmeyer & Tocci Associates, Inc. Thompson & Lichtner Co., Inc.
2018	201800950325	Fall River	Resiliency Preparatory School	Construction	Accelerated Repair	Roof, Boiler	DBB	P3 Inc.	edm Services, Inc.	-	Symmes, Maini & McKee Associates
2017	201700950145	Fall River	Samuel Watson	Construction	Accelerated Repair	Roof, Windows / Doors, Boiler	DBB	exPERTcon, Inc.	Tighe & Bond, Inc.	-	Fitzmeyer & Tocci Associates, Inc. Thompson & Lichtner Co., Inc.
2018	201800950150	Fall River	Westall	Construction	Accelerated Repair	Roof, Boiler	DBB	P3 Inc.	edm Services, Inc.	-	Symmes, Maini & McKee Associates
2016	201600970016	Fitchburg	Crocker Elementary	Feasibility Study	Core Program			Colliers Project Leaders NE, LLC	saam architecture	-	-
2019	201900970060	Fitchburg	South Street Elementary	Approved Project Vote Pending	Accelerated Repair	Roof, Boiler	DBB	P3 Inc.	edm Services, Inc.	-	Colliers Project Leaders NE, LLC
2015	201500990015	Foxborough	Mabelle M Burrell	Construction	Core Program	Addition / Renovation	DBB	Colliers Project Leaders NE, LLC	Kaestle Boos Associates, Inc.	CTA Construction Co., Inc.	Cadmus Group LLC
2015	201501000305	Framingham	Fuller Middle	Construction	Core Program	New Construction	CM@R	Symmes Maini & McKee Associates, Inc.	Jonathan Levi Architects LLC	Consigli Construction Company, Inc.	Jacobs Engineering Group Inc.
2016	201601030020	Gardner	Waterford Street	Design Development	Core Program	New Construction		Colliers Project Leaders NE, LLC	Jones Whitsett Architects, Inc.	-	Fitzmeyer & Tocci Associates, Inc.
2016	201601070020	Gloucester	East Gloucester Elementary	Schematic Design	Core Program			CBRE/HEERY	Dore & Whittier Architects, Inc.	-	-
2016	201601070505	Gloucester	Gloucester High	Final Audit Approved	Accelerated Repair	Roof	DBB	P3 Inc.	Baker/Wohl Architects, Inc.	Stanley Roofing Company, Inc.	CBI Consulting LLC
2012	201201110010	Granby	West Street	Closeout	Core Program	Addition / Renovation	DBB	Colliers Project Leaders NE, LLC	Jones Whitsett Architects, Inc.	Fontaine Brothers, Inc.	Rist-Frost-Shumway Engineering, P.C.
2017	201708210605	Greater Fall River Regional Voc Tech	Diman Regional Vocational Technical High	Feasibility Study	Core Program			Colliers Project Leaders NE, LLC	Kaestle Boos Associates, Inc.	-	-
2009	200908280605	Greater Lowell Regional Voc Tech	Gr Lowell Regional Vocational Technical	Final Audit Approved	Core Program	Addition / Renovation	CM@R	NV5 (fka Joslin, Lesser + Associates Inc.)	Knight, Bagge & Anderson, Inc.	Consigli Construction Company, Inc.	Horizon Engineering Associates, LLP
2017	201706730010	Groton-Dunstable	Florence Roche School	Feasibility Study	Core Program			Leftfield, LLC	Studio G. Architects, Inc.	-	-
2016	201601180005	Halifax	Halifax Elementary	Closeout	Accelerated Repair	Roof, Windows / Doors	DBB	Vertex Construction Services	Habeeb & Associates Architects, Inc.	Lambrian Construction Corp.	Russo Barr Associates, Inc.

2019	201906800310	Hampden-Wilbraham	Wilbraham Middle	Design Development	Accelerated Repair	Roof	DBB	Leftfield, LLC	Dietz & Company Architects, Inc.	-	Thompson & Lichtner Co., Inc.
2013	201301220015	Hanover	Sylvester	Closeout	Core Program	Addition / Renovation	DBB	P3 Inc.	Mount Vernon Group Architects, Inc.	Brait Builders Corp.	Horizon Engineering Associates, LLP
2015	201501250005	Harvard	Hildreth Elementary School	Construction	Core Program	New Construction	CM@R	NV5 (fka Joslin, Lesser + Associates Inc.)	Arrowstreet Inc.	Shawmut Design and Construction	Bard, Rao + Athanas Consulting Engineers, LLC
2012	201201280035	Haverhill	Caleb Dustin Hunking	Closeout	Core Program	New Construction	CM@R	NV5 (fka Joslin, Lesser + Associates Inc.)	JCJ Architecture, PC	Shawmut Design and Construction	Colliers Project Leaders NE, LLC
2018	201801280100	Haverhill	Consentino Middle School	OPM Selection	Core Program			-	-	-	-
2019	201901310010	Hingham	Wm L Foster Elementary	Eligibility Period	Core Program			-	-	-	-
2008	200801330505	Holbrook	Holbrook Junior-Senior High School	Closeout	Core Program	New Construction	CM@R	Symmes Maini & McKee Associates, Inc.	Flansburgh Associates, Inc.	Consigli Construction Company, Inc.	Consulting Engineering Services, LLC
2014	201401370045	Holyoke	E N White Elementary	Final Audit Approved	Accelerated Repair	Boiler	DBB	STV DPM (fka STV Inc.)	Richard D. Kimball Co., Inc. (d/b/a NV5)	Adams Plumbing and Heating, Inc.	BVH Integrated Services, P.C.
2017	201701370010	Holyoke	H.B. Lawrence School	Closeout	Core Program	New Construction		Pinck & Co., Inc.	Jones Whitsett Architects, Inc.	-	-
2014	201401370025	Holyoke	William G. Morgan	Final Audit Approved	Accelerated Repair	Boiler	DBB	STV DPM (fka STV Inc.)	Richard D. Kimball Co., Inc. (d/b/a NV5)	Adams Plumbing and Heating, Inc.	BVH Integrated Services, P.C.
2013	201301390005	Hopkinton	Center	Closeout	Core Program	New Construction	CM@R	Compass Project Management, Inc.	Drumrey Rosane Anderson, Inc.	Colantonio, Inc.	NV5
2018	201801420305	Hull	Memorial Middle	OPM Selection	Core Program			-	-	-	-
2014	201401440015	Ipswich	Winthrop	Final Audit Approved	Core Program	New Construction		PMA Consultants, LLC	Perkins Eastman/DPC	-	-
2019	201901450005	Kingston	Kingston Elementary	Approved Project Vote Pending	Accelerated Repair	Boiler		exPERTcon, Inc.	Architectural Engineers, Inc.	-	-
2017	201701490040	Lawrence	Francis M Leahy	Feasibility Study	Core Program			Atlantic Construction and Management, Inc.	Mount Vernon Group Architects, Inc.	-	-
2016	201601490050	Lawrence	Henry K Oliver	Feasibility Study	Core Program			Pinck & Co., Inc.	Symmes Maini & McKee Associates, Inc.	-	-
2017	201701490537	Lawrence	School for Exceptional Studies	Construction	Accelerated Repair	Roof	DBB	Pinck & Co., Inc.	Johnson Roberts Associates, Inc.	Greenwood Industries, Inc.	Symmes, Maini & McKee Associates
2016	201601510015	Leicester	Leicester Middle	Approved Project Vote Pending	Core Program			NV5 (fka Joslin, Lesser + Associates Inc.)	Finegold Alexander Architects	-	-
2019	201901600002	Lowell	Dr Gertrude Bailey	Design Development	Accelerated Repair	Roof, Boiler		Leftfield, LLC	CGKV Architects, Inc.	-	Symmes, Maini & McKee Associates
2019	201901600015	Lowell	Greenhalge	Design Development	Accelerated Repair	Boiler	DBB	Leftfield, LLC	CGKV Architects, Inc.	-	Symmes, Maini & McKee Associates
2019	201901600315	Lowell	James S Daley Middle School	Design Development	Accelerated Repair	Boiler	DBB	Leftfield, LLC	CGKV Architects, Inc.	-	Symmes, Maini & McKee Associates
2019	201901600340	Lowell	James Sullivan Middle School	Design Development	Accelerated Repair	Roof, Boiler		Leftfield, LLC	CGKV Architects, Inc.	-	Symmes, Maini & McKee Associates
2014	201401600505	Lowell	Lowell High	Design Development	Core Program	Addition / Renovation	CM@R	Skanska USA Building, Inc	Perkins Eastman/DPC	Suffolk Construction Company	Bard, Rao + Athanas Consulting Engineers, LLC
2019	201901600005	Lowell	Rogers Early Learning Center	Design Development	Accelerated Repair	Boiler	DBB	Leftfield, LLC	CGKV Architects, Inc.	-	Symmes, Maini & McKee Associates
2019	201901600075	Lowell	S Christa McAuliffe Elementary	Design Development	Accelerated Repair	Boiler	DBB	Leftfield, LLC	CGKV Architects, Inc.	-	Symmes, Maini & McKee Associates
2015	201501610020	Ludlow	Chapin Street Elementary School	Construction	Core Program	New Construction	DBB	STV DPM (fka STV Inc.)	Mount Vernon Group Architects, Inc.	Fontaine Brothers, Inc.	Horizon Engineering Associates, LLP
2010	201001620505	Lunenburg	Lunenburg High	Final Audit Approved	Core Program	New Construction	CM@R	NV5 (fka Joslin, Lesser + Associates Inc.)	Tappe Architects, Inc.	Shawmut Design and Construction	Cannon Design
2018	201801630605	Lynn	Lynn Vocational Technical Institute	Design Development	Accelerated Repair	Roof	DBB	-	-	Stanley Roofing Company, Inc.	CBI Consulting LLC
2015	201506980010	Manchester Essex Regional	Manchester Memorial Elementary	Construction	Core Program	New Construction	CM@R	Dore & Whittier Management Partners, Inc.	JCJ Architecture, PC	W. T. Rich Company Inc.	Symmes, Maini & McKee Associates
2017	201701670505	Mansfield	Mansfield High	Closeout	Accelerated Repair	Windows / Doors	DBB	Watermark Environmental, Inc.	Baker/Wohl Architects, Inc.	J.J. Cardosi, Inc.	CBI Consulting LLC
2015	201501680015	Marblehead	Elbridge Gerry	Construction	Core Program	New Construction	CM@R	Leftfield, LLC	Raymond Design Associates, Inc.	Gilbane Building Company	NV5
2015	201501700025	Marlborough	Richer	Construction	Core Program	New Construction - Model School	DBB	CHA Consulting, Inc.	Mount Vernon Group Architects, Inc.	Fontaine Brothers, Inc.	WSP USA
2016	201601710310	Marshfield	Furnace Brook Middle	Closeout	Accelerated Repair	Roof	DBB	PCA 360	CIVITECTS PC	Colantonio, Inc.	Russo Barr Associates, Inc.

2016	201601720035	Mashpee	Quashnet School	Closeout	Accelerated Repair	Windows / Doors	DBB	exPERTcon, Inc.	Raymond Design Associates, Inc.	J.J. Cardosi, Inc.	CBI Consulting LLC
2019	201901740010	Maynard	Green Meadow	Eligibility Period	Core Program			-	-	-	-
2017	201701750005	Medfield	Dale Street	Feasibility Study	Core Program			Leftfield, LLC	Arrowstreet Inc.	-	-
2014	201401820505	Middleborough	Middleborough High	Construction	Core Program	New Construction	DBB	Compass Project Management, Inc.	Drumme Rosane Anderson, Inc.	Fontaine Brothers, Inc.	Colliers Project Leaders NE, LLC
2011	201101850090	Milford	Woodland	Final Audit Approved	Core Program	New Construction	CM@R	NV5 (fka Joslin, Lesser + Associates Inc.)	HMFH Architects, Inc.	Shawmut Design and Construction	Consulting Engineering Services, LLC
2016	201601860025	Milbury	Raymond E. Shaw Elementary	Approved Project Vote Pending	Core Program	New Construction		Hill International Company	Turowski2 Architecture, Inc.	-	Consulting Engineering Services, LLC
2019	201901910025	Monson	Quarry Hill Community School	Schematic Design	Accelerated Repair	Roof		P3 Inc.	Simpson Gumpertz & Heger Inc.	-	-
2013	201307150505	Mount Greylock	Mt Greylock Regional High	Closeout	Core Program	Addition / Renovation	CM@R	Dore & Whittier Management Partners, Inc.	Perkins Eastman/DPC	Turner Construction Company	BVH Integrated Services, P.C.
2019	201907250505	Nashoba	Nashoba Regional	Eligibility Period	Core Program			-	-	-	-
2018	201808520605	Nashoba Valley Regional Voc Tech	Nashoba Valley Technical High School	Closeout	Accelerated Repair	Roof, Windows / Doors	DBB	Leftfield, LLC	Robinson Green Beretta (RGB) Architects	Capeway Roofing Systems, Inc.	Simpson Gumpertz & Heger Inc.
2015	201501980305	Natick	J F Kennedy Middle School	Construction	Core Program	New Construction	DBB	Compass Project Management, Inc.	Ai3 Architects LLC	Brait Builders Corp.	Rist-Frost-Shumway Engineering, P.C.
2016	201606600505	Nauset	Nauset Regional High	Approved Project Vote Pending	Core Program			CHA Consulting, Inc.	Flansburgh Associates, Inc.	-	-
2017	201702010015	New Bedford	Elizabeth Carter Brooks	Construction	Accelerated Repair	Windows / Doors, Boiler	DBB	NV5 (fka Joslin, Lesser + Associates Inc.)	Johnson Roberts Associates, Inc.	-	WSP USA
2016	201602010115	New Bedford	John Avery Parker	Closeout	Accelerated Repair	Windows / Doors	DBB	Architectural Consulting Group, LLC	CBI Consulting LLC	-	WSP USA
2018	201802010115	New Bedford	John Avery Parker	Closeout	Accelerated Repair	Roof	DBB	Vertex Construction Services	Habeeb & Associates Architects, Inc.	Capeway Roofing Systems, Inc.	Thompson & Lichtner Co., Inc.
2009	200902010070	New Bedford	John Hannigan	Closeout	Core Program	New Construction	DBB	CHA Consulting, Inc.	Turowski2 Architecture, Inc.	H.V. Collins Co., Inc.	WSP USA
2018	201802010510	New Bedford	Trinity Day Academy	Closeout	Accelerated Repair	Boiler	DBB	Vertex Construction Services	Habeeb & Associates Architects, Inc.	Araujo Brothers Plumbing & Heating	WSP USA
2018	201807280015	New Salem-Wendell	Swift River	Construction	Accelerated Repair	Windows / Doors	DBB	Colliers Project Leaders NE, LLC	TSKP Studio, LLC	-	Russo Barr Associates, Inc.
2018	201802070305	Newton	Bigelow Middle	Closeout	Accelerated Repair	Boiler	DBB	NETCO Construction Project Managers, Inc.	Tighe & Bond, Inc.	Veterans Development Corporation, Inc.	NV5
2018	201802070315	Newton	F A Day Middle	Construction	Accelerated Repair	Boiler	DBB	NETCO Construction Project Managers, Inc.	Tighe & Bond, Inc.	-	NV5
2018	201802080015	Norfolk	H Olive Day	Closeout	Accelerated Repair	Roof	DBB	PMA Consultants, LLC	Gale Associates, Inc.	Greenwood Industries, Inc.	R.J. Kenney Associates, Inc.
2018	201809150705	Norfolk County Agricultural	Norfolk County Agricultural	Design Development	Accelerated Repair	Roof, Windows / Doors, Boiler	DBB	Atlantic Construction and Management, Inc.	Raymond Design Associates, Inc.	-	Gale Associates, Inc.
2019	201902090015	North Adams	Greylock	Eligibility Period	Core Program			-	-	-	-
2016	201602150015	North Brookfield	North Brookfield Elementary	Final Audit Approved	Accelerated Repair	Roof	DBB	Skanska USA Building, Inc	Dietz & Company Architects, Inc.	MDM Engineering	Simpson Gumpertz & Heger Inc.
2016	201607350030	North Middlesex	Hawthorne Brook	Closeout	Accelerated Repair	Windows / Doors	DBB	Atlantic Construction and Management, Inc.	Habeeb & Associates Architects, Inc.	E. Amanti & Sons, Inc.	Gale Associates, Inc.
2016	201607350020	North Middlesex	Squannacook	Closeout	Accelerated Repair	Roof	DBB	Atlantic Construction and Management, Inc.	Habeeb & Associates Architects, Inc.	Vanguard Construction Company, Inc.	Gale Associates, Inc.
2016	201607350035	North Middlesex	Varnum Brook	Closeout	Accelerated Repair	Roof, Windows / Doors	DBB	Atlantic Construction and Management, Inc.	Habeeb & Associates Architects, Inc.	E. Amanti & Sons, Inc.	Gale Associates, Inc.
2010	201002170505	North Reading	North Reading High	Closeout	Core Program	Addition / Renovation	CM@R	PMA Consultants, LLC	Dore & Whittier Architects, Inc.	Gilbane Building Company	Cannon Design
2016	201602100005	Northampton	Bridge Street	Final Audit Approved	Accelerated Repair	Roof	DBB	Colliers Project Leaders NE, LLC	The S/L/A/M Collaborative	D.A. Sullivan & Sons, Inc.	CBI Consulting LLC
2016	201602100025	Northampton	Leeds	Final Audit Approved	Accelerated Repair	Roof	DBB	Colliers Project Leaders NE, LLC	The S/L/A/M Collaborative	D.A. Sullivan & Sons, Inc.	CBI Consulting LLC
2019	201902140305	Northbridge	Northbridge Middle	Approved Project Vote Pending	Accelerated Repair	Boiler		Architectural Consulting Group, LLC	Habeeb & Associates Architects, Inc.	-	-
2015	201502140001	Northbridge	W Edward Balmer	Construction	Core Program	New Construction	CM@R	Symmes Maini & McKee Associates, Inc.	Dore & Whittier Architects, Inc.	Fontaine Brothers, Inc.	Fitzmeyer & Tocci Associates, Inc.
2017	201708530605	Northeast Metropolitan Regional Voc Tech	Northeast Metro Regional Vocational	Feasibility Study	Core Program			PMA Consultants, LLC	Drumme Rosane Anderson, Inc.	-	-
2018	201802200305	Norwood	Dr. Philip O. Coakley Middle School	OPM Selection	Core Program			-	-	-	-

2016	201602230010	Orange	Dexter Park	Approved Project Vote Pending	Core Program	Addition / Renovation		Hill International Company	Raymond Design Associates, Inc.	-	-
2008	200802290305	Peabody	J Henry Higgins Middle	Closeout	Core Program	New Construction	DBB	CHA Consulting, Inc.	DiNisco Design, Inc.	Bacon-Agostini Construction Joint Venture	BVH Integrated Services, P.C.
2018	201802290027	Peabody	William A Welch Sr	Designer Selection	Core Program			-	-	-	-
2015	201507450505	Pentucket	Pentucket Regional Sr High	Construction	Core Program	New Construction	CM@R	Vertex Construction Services	Dore & Whittier Architects, Inc.	Rich-KBE Pentucket School Joint Venture	Jacobs Engineering Group Inc.
2010	201002360510	Pittsfield	Taconic High	Closeout	Core Program	New Construction	CM@R	Skanska USA Building, Inc	Drumrey Rosane Anderson, Inc.	Gilbane Building Company	Colliers Project Leaders NE, LLC
2012	201202390515	Plymouth	Plymouth South High	Final Audit Approved	Core Program	New Construction	DBB	Ted Gentry Associates, Inc	Ai3 Architects LLC	Bacon-Agostini Construction Joint Venture	Rist-Frost-Shumway Engineering, P.C.
2013	201302420505	Provincetown	Provincetown High	Final Audit Approved	Core Program	Repair	DBB	Atlantic Construction and Management, Inc.	Raymond Design Associates, Inc.	E. Amanti & Sons, Inc.	BVH Integrated Services, P.C.
2019	201907530010	Quabbin	Hubbardston Center	Schematic Design	Accelerated Repair	Roof		Pinck & Co., Inc.	CSS Architects Incorporated	-	-
2016	201607780005	Quabog Regional	Warren Elementary	Final Audit Approved	Accelerated Repair	Windows / Doors	DBB	NETCO Construction Project Managers, Inc.	TSKP Studio, LLC	Lockheed Window Corporations	Colliers Project Leaders NE, LLC
2018	201807780010	Quabog Regional	West Brookfield Elementary	Final Audit Approved	Accelerated Repair	Windows / Doors		Arcadis U.S., Inc.	Baker/Wohl Architects, Inc.	-	-
2016	201602430040	Quincy	Atherton Hough	Closeout	Accelerated Repair	Boiler	DBB	Hill International Company	Architectural Engineers, Inc.	E. Amanti & Sons, Inc.	Consulting Engineering Services, LLC
2016	201602430020	Quincy	Beechwood Knoll Elementary	Closeout	Accelerated Repair	Boiler	DBB	Hill International Company	Architectural Engineers, Inc.	E. Amanti & Sons, Inc.	Consulting Engineering Services, LLC
2015	201502430060	Quincy	Merrymount	Final Audit Approved	Accelerated Repair	Roof	DBB	Atlantic Construction and Management, Inc.	Baker/Wohl Architects, Inc.	Gibson Roofs, Inc.	CBI Consulting LLC
2016	201602430060	Quincy	Merrymount	Closeout	Accelerated Repair	Boiler	DBB	Hill International Company	Architectural Engineers, Inc.	E. Amanti & Sons, Inc.	Consulting Engineering Services, LLC
2017	201702430510	Quincy	North Quincy High	Closeout	Accelerated Repair	Roof	DBB	STV DPM (fka STV Inc.)	CBI Consulting LLC	Greenwood Industries, Inc.	Gale Associates, Inc.
2016	201602430110	Quincy	Wollaston School	Closeout	Accelerated Repair	Boiler	DBB	Hill International Company	Architectural Engineers, Inc.	E. Amanti & Sons, Inc.	Consulting Engineering Services, LLC
2017	201702440020	Randolph	Elizabeth G Lyons Elementary	Feasibility Study	Core Program			CHA Consulting, Inc.	TSKP Studio, LLC	-	-
2017	201702440015	Randolph	Margaret L Donovan	Closeout	Accelerated Repair	Windows / Doors, Boiler	DBB	Atlantic Construction and Management, Inc.	TSKP Studio, LLC	A&A Window Products, Inc.	Consulting Engineering Services, LLC Gale Associates, Inc.
2017	201702440040	Randolph	Martin E Young Elementary	Closeout	Accelerated Repair	Windows / Doors	DBB	Atlantic Construction and Management, Inc.	TSKP Studio, LLC	Modern Glass & Aluminum, Inc.	Gale Associates, Inc.
2015	201502480056	Revere	Garfield Elementary School	Final Audit Approved	Accelerated Repair	Roof	DBB	Leftfield, LLC	Turowski2 Architecture, Inc.	Greenwood Industries, Inc.	Thompson & Lichtner Co., Inc.
2016	201602480057	Revere	Garfield Middle School	Final Audit Approved	Accelerated Repair	Boiler	DBB	NV5 (fka Joslin, Lesser + Associates Inc.)	BLW Engineers, Inc.	Enterprise Equipment Co., Inc.	Fitzmeyer & Tocci Associates, Inc.
2018	201802480505	Revere	Revere High	OPM Selection	Core Program			-	-	-	-
2010	201002480035	Revere	Staff Sargent James J. Hill Elementary School	Closeout	Core Program	New Construction	DBB	Hill International Company	Drumrey Rosane Anderson, Inc.	CTA Construction Co., Inc.	Rist-Frost-Shumway Engineering, P.C.
2016	201602510060	Rockland	Jefferson Elementary School	Design Development	Core Program	New Construction	DBB	PMA Consultants, LLC	Symmes Maini & McKee Associates, Inc.	-	NV5
2019	201902580005	Salem	Bentley	Design Development	Accelerated Repair	Boiler		NETCO Construction Project Managers, Inc.	Johnson Roberts Associates, Inc.	-	-
2019	201902610002	Sandwich	Forestdale School	Schematic Design	Accelerated Repair	Boiler		Atlantic Construction and Management, Inc.	The S/L/A/M Collaborative	-	-
2019	201902610025	Sandwich	Oak Ridge	Schematic Design	Accelerated Repair	Boiler		Atlantic Construction and Management, Inc.	The S/L/A/M Collaborative	-	-
2014	201402620505	Saugus	Saugus High	Construction	Core Program	New Construction	CM@R	PMA Consultants, LLC	HMFH Architects, Inc.	Suffolk Construction Company	Consulting Engineering Services, LLC
2017	201702650015	Seekonk	Mildred Aitken School	Closeout	Accelerated Repair	Windows / Doors	DBB	Colliers Project Leaders NE, LLC	Gale Associates, Inc.	Lizotte Glass	Thompson & Lichtner Co., Inc.
2016	201602660505	Sharon	Sharon High	Design Development	Core Program	New Construction		PMA Consultants, LLC	Tappe Architects, Inc.	-	Fitzmeyer & Tocci Associates, Inc.
2015	201502710005	Shrewsbury	Beal School	Construction	Core Program	New Construction	CM@R	PMA Consultants, LLC	Lamoureux Pagano Associates Architects, Inc.	Fontaine Brothers, Inc.	Bard, Rao + Athanas Consulting Engineers, LLC
2017	201702730305	Somerset	Somerset Middle School	Feasibility Study	Core Program			CGA Project Management	Ai3 Architects LLC	-	-
2013	201302740505	Somerville	Somerville High	Construction	Core Program	Addition / Renovation	CM@R	PMA Consultants, LLC	Symmes Maini & McKee Associates, Inc.	Suffolk Construction Company	WSP USA
2016	201602740120	Somerville	Winter Hill Community	Closeout	Accelerated Repair	Roof, Windows / Doors	DBB	Municipal Building Consultants, Inc.	TSKP Studio, LLC	Lockheed Window Corporations	Thompson & Lichtner Co., Inc.

2019	201902760008	Southborough	Mary E Finn School	Approved Project Vote Pending	Accelerated Repair	Boiler	DBB	Hill International Company	CSS Architects Incorporated	-	Consulting Engineering Services, LLC
2018	201807670505	Spencer-E Brookfield	David Prouty High	OPM Selection	Core Program			-	-	-	-
2016	201602810095	Springfield	Alfred G. Zanetti Montessori Magnet School	Closeout	Accelerated Repair	Windows / Doors	DBB	Leftfield, LLC	Gale Associates, Inc.	D.A. Sullivan & Sons, Inc.	Building Enclosure Associates, LLC
2016	201602810360	Springfield	Balliet Middle School	Closeout	Accelerated Repair	Windows / Doors	DBB	Leftfield, LLC	Gale Associates, Inc.	W.J. Mountford Company	Building Enclosure Associates, LLC
2015	201502810025	Springfield	Brightwood	Construction	Core Program	New Construction	CM@R	Skanska USA Building, Inc	DiNisco Design, Inc.	Daniel O'Connell's Sons, Inc.	WSP USA
2015	201502810035	Springfield	Daniel B Brunton	Final Audit Approved	Accelerated Repair	Windows / Doors	DBB	Skanska USA Building, Inc	CBI Consulting LLC	Five Star Building Corp.	Building Enclosure Associates, LLC
2019	201902810080	Springfield	Frederick Harris	Schematic Design	Accelerated Repair	Boiler		PCA 360	Raymond Design Associates, Inc.	-	-
2018	201802810530	Springfield	High School/Science-Tech	Construction	Accelerated Repair	Boiler	DBB	Architectural Consulting Group, LLC	Shekar & Associates, Inc.	Adams Plumbing and Heating, Inc.	Colliers Project Leaders NE, LLC
2019	201902810100	Springfield	Indian Orchard Elementary	Schematic Design	Accelerated Repair	Boiler		PCA 360	Raymond Design Associates, Inc.	-	-
2016	201602810110	Springfield	Kensington International School	Closeout	Accelerated Repair	Roof	DBB	Leftfield, LLC	Gale Associates, Inc.	Greenwood Industries, Inc.	Building Enclosure Associates, LLC
2016	201602810330	Springfield	M Marcus Kiley Middle	Closeout	Accelerated Repair	Windows / Doors	DBB	Leftfield, LLC	Gale Associates, Inc.	D.A. Sullivan & Sons, Inc.	Building Enclosure Associates, LLC
2016	201602810140	Springfield	Mary M Lynch	Closeout	Accelerated Repair	Roof	DBB	Leftfield, LLC	Gale Associates, Inc.	Greenwood Industries, Inc.	Building Enclosure Associates, LLC
2015	201502810155	Springfield	Mary M Walsh	Final Audit Approved	Accelerated Repair	Windows / Doors	DBB	Skanska USA Building, Inc	CBI Consulting LLC	PDS Engineering and Construction, Inc.	Building Enclosure Associates, LLC
2018	201802810023	Springfield	Milton Bradley School	Design Development	Accelerated Repair	Roof	DBB	Architectural Consulting Group, LLC	Kaestle Boos Associates, Inc.	J.D. Rivet & Co., Inc.	Building Enclosure Associates, LLC
2017	201702810355	Springfield	South End Middle School	Closeout	Accelerated Repair	Windows / Doors	DBB	P3 Inc.	CGKV Architects, Inc.	W.J. Mountford Company	Building Enclosure Associates, LLC
2015	201502810550	Springfield	Springfield Public Day High School	Final Audit Approved	Accelerated Repair	Windows / Doors	DBB	Skanska USA Building, Inc	CBI Consulting LLC	Wesfield Construction Co., Inc.	Building Enclosure Associates, LLC
2015	201502810350	Springfield	STEM Middle Academy	Final Audit Approved	Accelerated Repair	Roof	DBB	Skanska USA Building, Inc	CBI Consulting LLC	Wesfield Construction Co., Inc.	Building Enclosure Associates, LLC
2019	201902810160	Springfield	Sumner Avenue	Schematic Design	Accelerated Repair	Boiler		PCA 360	Raymond Design Associates, Inc.	-	-
2016	201602810015	Springfield	Thomas M Balliet	Closeout	Accelerated Repair	Roof	DBB	Leftfield, LLC	Gale Associates, Inc.	W.J. Mountford Company	Building Enclosure Associates, LLC
2016	201602810045	Springfield	William N. DeBerry	Schematic Design	Core Program	New Construction		Skanska USA Building, Inc	DiNisco Design, Inc.	-	-
2018	201802840505	Stoneham	Stoneham High	Designer Selection	Core Program			-	-	-	-
2014	201402850025	Stoughton	Joseph H Gibbons	Final Audit Approved	Accelerated Repair	Roof, Windows / Doors	DBB	Atlantic Construction and Management, Inc.	CGKV Architects, Inc.	A&A Window Products, Inc.	Building Enclosure Associates, LLC
2015	201502850020	Stoughton	West Elementary School	Closeout	Accelerated Repair	Windows / Doors	DBB	Compass Project Management, Inc.	CBI Consulting LLC	Alpha Contracting Associates, Inc.	Building Enclosure Associates, LLC
2017	201702910010	Swampscott	Hadley	Feasibility Study	Core Program			-	-	-	-
2018	201802920505	Swansea	Joseph Case High	Schematic Design	Accelerated Repair	Boiler		Vertex Construction Services	Architectural Engineers, Inc.	-	-
2018	201807700405	Tantasqua	Tantasqua Regional Jr High	Construction	Accelerated Repair	Windows / Doors	DBB	Architectural Consulting Group, LLC	Next Phase Studios, Inc.	-	R.J. Kenney Associates, Inc.
2015	201502930007	Taunton	Edmund Hatch Bennett	Closeout	Accelerated Repair	Roof, Windows / Doors	DBB	Arcadis U.S., Inc.	CSS Architects Incorporated	TRAC Builders, Inc.	Gale Associates, Inc.
2015	201502930042	Taunton	Joseph H Martin	Closeout	Accelerated Repair	Roof, Windows / Doors	DBB	Arcadis U.S., Inc.	CSS Architects Incorporated	TRAC Builders, Inc.	Gale Associates, Inc.
2014	201402930015	Taunton	Mulcahey Elementary School	Construction	Core Program	New Construction	DBB	CGA Project Management	Dore & Whittier Architects, Inc.	Agostini Construction Co., Inc.	Consulting Engineering Services, LLC
2018	201802930525	Taunton	Taunton Alternative High School	Construction	Accelerated Repair	Roof, Windows / Doors	DBB	NETCO Construction Project Managers, Inc.	Simpson Gumpertz & Heger Inc.	-	Building Enclosure Associates, LLC
2015	201502950025	Tewksbury	Louise Davy Trahan	Design Development	Core Program	New Construction		CBRE/HEERY	Flansburgh Associates, Inc.	-	Consulting Engineering Services, LLC
2016	201602980005	Topsfield	Proctor Elementary	Closeout	Accelerated Repair	Roof	DBB	Compass Project Management, Inc.	The S/L/A/M Collaborative	Northern Contracting	Gale Associates, Inc.
2016	201602980010	Topsfield	Steward Elementary	Closeout	Accelerated Repair	Roof	DBB	Compass Project Management, Inc.	The S/L/A/M Collaborative	Northern Contracting	Gale Associates, Inc.
2019	201908780605	Tri County	Tri-County Regional Vocational Technical	Eligibility Period	Core Program			-	-	-	-
2018	201803010305	Tyngsborough	Tyngsborough Middle	OPM Selection	Core Program			-	-	-	-

2009	200907750305	Wachusett	Mountview Middle	Final Audit Approved	Core Program	New Construction	DBB	-	Lamoureux Pagano Associates Architects, Inc.	CTA Construction Co., Inc.	Fitzmeyer & Tocci Associates, Inc.
2019	201903050020	Wakefield	Greenwood	Design Development	Accelerated Repair	Roof	DBB	PMA Consultants, LLC	Gale Associates, Inc.	-	Building Enclosure Associates, LLC
2019	201903050505	Wakefield	Wakefield Memorial High	Eligibility Period	Core Program			-	-	-	-
2018	201803070305	Walpole	Bird Middle	Feasibility Study	Core Program			Compass Project Management, Inc.	-	-	-
2014	201403080505	Waltham	Waltham Sr High	Approved Project Vote Pending	Core Program	New Construction		NV5 (fka Joslin, Lesser + Associates Inc.)	Symmes Maini & McKee Associates, Inc.	-	-
2018	201803090305	Ware	Ware Middle School	Construction	Accelerated Repair	Windows / Doors	DBB	Hill International Company	CGKV Architects, Inc.	Wesfield Construction Co., Inc.	CBI Consulting LLC
2015	201503100003	Wareham	John William Decas	Closeout	Accelerated Repair	Roof, Boiler	DBB	Colliers Project Leaders NE, LLC	ICON architecture, inc.	Nadeau Corporation	Bard, Rao + Athanas Consulting Engineers, LLC Gale Associates, Inc.
2015	201503100017	Wareham	Minot Forest	Construction	Core Program	New Construction		PMA Consultants, LLC	Mount Vernon Group Architects, Inc.	Bacon Construction Co, Inc.	Symmes, Maini & McKee Associates
2017	201703140505	Watertown	Watertown High	Feasibility Study	Core Program			Compass Project Management, Inc.	Ai3 Architects LLC	-	-
2015	201503140305	Watertown	Watertown Middle	Final Audit Approved	Accelerated Repair	Windows / Doors	DBB	exPERTcon, Inc.	Gale Associates, Inc.	Homer Contracting	Thompson & Lichtner Co., Inc.
2014	201403150005	Wayland	Claypit Hill School	Final Audit Approved	Accelerated Repair	Windows / Doors	DBB	Pinck & Co., Inc.	CGKV Architects, Inc.	Lockheed Window Corporations	Russo Barr Associates, Inc.
2016	201603150020	Wayland	Loker School	Closeout	Accelerated Repair	Windows / Doors	DBB	Colliers Project Leaders NE, LLC	CBI Consulting LLC	GVW, Inc.	Thompson & Lichtner Co., Inc.
2019	201903150020	Wayland	Loker School	Approved Project Vote Pending	Accelerated Repair	Roof	DBB	Architectural Consulting Group, LLC	Tighe & Bond, Inc.	-	Gale Associates, Inc.
2018	201803160505	Webster	Bartlett Jr Sr High Sch	OPM Selection	Core Program			-	-	-	-
2017	201703170050	Wellesley	Ernest F Upham	Feasibility Study	Core Program			Compass Project Management, Inc.	Symmes Maini & McKee Associates, Inc.	-	-
2018	201803230305	West Bridgewater	Howard School	Closeout	Accelerated Repair	Roof	DBB	JACOBS Project Management Co.	Mount Vernon Group Architects, Inc.	MDM Engineering	Russo Barr Associates, Inc.
2010	201003230505	West Bridgewater	West Bridgewater Junior/Senior	Final Audit Approved	Core Program	New Construction	DBB	Colliers Project Leaders NE, LLC	Flansburgh Associates, Inc.	CTA Construction Co., Inc.	Cannon Design
2015	201503320007	West Springfield	Philip G Coburn	Design Development	Core Program	New Construction		NV5 (fka Joslin, Lesser + Associates Inc.)	TSKP Studio, LLC	-	Horizon Engineering Associates, LLP
2016	201603210010	Westborough	Annie E Fales	Design Development	Core Program	New Construction	CM@R	Vertex Construction Services	HMFH Architects, Inc.	Gilbane Building Company	Fitzmeyer & Tocci Associates, Inc.
2018	201803210025	Westborough	Elsie A Hastings Elementary	Final Audit Approved	Accelerated Repair	Roof, Windows / Doors, Boiler		Leftfield, LLC	Dietz & Company Architects, Inc.	-	-
2009	200903210305	Westborough	Sarah W Gibbons Middle	Closeout	Core Program	Repair	CM@R	CBRE/HEERY	Habeeb & Associates Architects, Inc.	Gilbane Building Company	BVH Integrated Services, P.C.
2018	201803250015	Westfield	Franklin Ave	Designer Selection	Core Program			-	-	-	-
2017	201703260004	Westford	Abbot Elementary	Final Audit Approved	Accelerated Repair	Roof	DBB	Leftfield, LLC	Raymond Design Associates, Inc.	Titan Roofing, Inc.	CBI Consulting LLC
2019	201903310030	Westport	Westport Elementary	Design Development	Accelerated Repair	Roof		Vertex Construction Services	The S/L/A/M Collaborative	-	-
2014	201403310305	Westport	Westport Junior/Senior High School	Construction	Core Program	New Construction	CM@R	CHA Consulting, Inc.	Jonathan Levi Architects LLC	Agostini Construction Co., Inc.	BVH Integrated Services, P.C.
2017	201703350015	Westwood	Paul Hanlon	Feasibility Study	Core Program			Compass Project Management, Inc.	Dore & Whittier Architects, Inc.	-	-
2015	201503360020	Weymouth	Maria Weston Chapman Middle School	Design Development	Core Program	Addition / Renovation	CM@R	Hill International Company	HMFH Architects, Inc.	Bond Brothers, Inc.	WSP USA
2019	201903360085	Weymouth	Ralph Talbot	Schematic Design	Accelerated Repair	Boiler		Colliers Project Leaders NE, LLC	Shekar & Associates, Inc.	-	-
2017	201703360105	Weymouth	Thomas W. Hamilton Primary School	Closeout	Accelerated Repair	Boiler	DBB	Atlantic Construction and Management, Inc.	BLW Engineers, Inc.	AAIanco Service Corporation	Fitzmeyer & Tocci Associates, Inc.
2017	201703360110	Weymouth	Wessagusset	Closeout	Accelerated Repair	Boiler	DBB	Atlantic Construction and Management, Inc.	BLW Engineers, Inc.	AAIanco Service Corporation	Fitzmeyer & Tocci Associates, Inc.
2019	201907800310	Whitman-Hanson	Whitman Middle	Eligibility Period	Core Program			-	-	-	-
2019	201908850605	Whittier Voc	Whittier Regional Vocational	Eligibility Period	Core Program			-	-	-	-
2009	200903420505	Wilmington	Wilmington High	Closeout	Core Program	New Construction	CM@R	NV5 (fka Joslin, Lesser + Associates Inc.)	Dore & Whittier Architects, Inc.	Gilbane Building Company	Symmes, Maini & McKee Associates
2019	201903440020	Winchester	Lynch Elementary	Eligibility Period	Core Program			-	-	-	-

2010	201003440505	Winchester	Winchester High School	Closeout	Core Program	Addition / Renovation	CM@R	Skanska USA Building, Inc	Symmes Maini & McKee Associates, Inc.	Consigli Construction Company, Inc.	NV5
2012	201203470060	Woburn	Wyman	Closeout	Core Program	New Construction	DBB	Municipal Building Consultants, Inc.	DiNisco Design, Inc.	CTA Construction Co., Inc.	Fitzmeyer & Tocci Associates, Inc.
2016	201603480020	Worcester	Belmont Street Community	Closeout	Accelerated Repair	Windows / Doors	DBB	Watermark Environmental, Inc.	Tighe & Bond, Inc.	Stutman Contracting, Inc.	Russo Barr Associates, Inc.
2019	201903480035	Worcester	Burncoat Street	Design Development	Accelerated Repair	Roof	DBB	exPERTcon, Inc.	Habeeb & Associates Architects, Inc.	-	Russo Barr Associates, Inc.
2018	201803481008	Worcester	Challenge and Reach Academy	Construction	Accelerated Repair	Roof, Windows / Doors, Boiler	DBB	Arcadis U.S., Inc.	Johnson Roberts Associates, Inc.	-	Colliers Project Leaders NE, LLC
2016	201603480050	Worcester	Chandler Elementary Community	Closeout	Accelerated Repair	Windows / Doors, Boiler	DBB	Watermark Environmental, Inc.	Tighe & Bond, Inc.	Stutman Contracting, Inc.	BVH Integrated Services, P.C. Russo Barr Associates, Inc.
2016	201603480512	Worcester	Doherty Memorial High	Schematic Design	Core Program	New Construction		Tishman Construction Corporation of MA	Lamoureux Pagano Associates Architects, Inc.	-	-
2017	201703480095	Worcester	Elm Park Community	Closeout	Accelerated Repair	Windows / Doors	DBB	NV5 (fka Joslin, Lesser + Associates Inc.)	Atane Engineers, P.C.	Fontaine Brothers, Inc.	Russo Barr Associates, Inc.
2015	201503480090	Worcester	Flagg Street	Final Audit Approved	Accelerated Repair	Windows / Doors	DBB	Arcadis U.S., Inc.	CSS Architects Incorporated	J.J. Cardosi, Inc.	Russo Barr Associates, Inc.
2015	201503480177	Worcester	Francis J McGrath Elementary	Final Audit Approved	Accelerated Repair	Windows / Doors	DBB	Arcadis U.S., Inc.	CSS Architects Incorporated	J.J. Cardosi, Inc.	Russo Barr Associates, Inc.
2016	201603481004	Worcester	Gerald Creamer Center	Closeout	Accelerated Repair	Windows / Doors, Boiler	DBB	Watermark Environmental, Inc.	Tighe & Bond, Inc.	Stutman Contracting, Inc.	BVH Integrated Services, P.C. Russo Barr Associates, Inc.
2015	201503480115	Worcester	Grafton Street	Final Audit Approved	Accelerated Repair	Windows / Doors, Boiler	DBB	Arcadis U.S., Inc.	CSS Architects Incorporated	J.J. Cardosi, Inc.	Rist-Frost-Shumway Engineering, P.C. Russo Barr Associates, Inc.
2015	201503480140	Worcester	Jacob Hiatt Magnet	Final Audit Approved	Accelerated Repair	Windows / Doors	DBB	Arcadis U.S., Inc.	CSS Architects Incorporated	J.J. Cardosi, Inc.	Russo Barr Associates, Inc.
2017	201703480160	Worcester	Lincoln Street	Closeout	Accelerated Repair	Roof, Windows / Doors	DBB	NV5 (fka Joslin, Lesser + Associates Inc.)	Atane Engineers, P.C.	Fontaine Brothers, Inc.	Russo Barr Associates, Inc.
2019	201903480160	Worcester	Lincoln Street	Design Development	Accelerated Repair	Boiler	DBB	exPERTcon, Inc.	Habeeb & Associates Architects, Inc.	-	Rist-Frost-Shumway Engineering, P.C.
2012	201203480200	Worcester	Nelson Place	Final Audit Approved	Core Program	New Construction	CM@R	Tishman Construction Corporation of MA	Lamoureux Pagano Associates Architects, Inc.	Fontaine Brothers, Inc.	Bard, Rao + Athanas Consulting Engineers, LLC
2014	201403480520	Worcester	South High Community	Construction	Core Program	New Construction	CM@R	CBRE/HEERY	Lamoureux Pagano Associates Architects, Inc.	Fontaine Brothers, Inc.	Horizon Engineering Associates, LLP
2019	201903480230	Worcester	Tatnuck	Design Development	Accelerated Repair	Roof	DBB	exPERTcon, Inc.	Habeeb & Associates Architects, Inc.	-	Russo Barr Associates, Inc.
2017	201703480235	Worcester	Thorndyke Road	Closeout	Accelerated Repair	Windows / Doors	DBB	NV5 (fka Joslin, Lesser + Associates Inc.)	Atane Engineers, P.C.	Fontaine Brothers, Inc.	Russo Barr Associates, Inc.
2019	201903480280	Worcester	Vernon Hill School	Design Development	Accelerated Repair	Roof	DBB	exPERTcon, Inc.	Habeeb & Associates Architects, Inc.	-	Russo Barr Associates, Inc.
2016	201603480026	Worcester	Wawecus Road School	Closeout	Accelerated Repair	Windows / Doors	DBB	Watermark Environmental, Inc.	Tighe & Bond, Inc.	Stutman Contracting, Inc.	Russo Barr Associates, Inc.
2019	201903480420	Worcester	Worcester East Middle	Design Development	Accelerated Repair	Roof	DBB	exPERTcon, Inc.	Habeeb & Associates Architects, Inc.	-	Russo Barr Associates, Inc.

APPENDIX B
2020-21 ESTIMATED BID DATES

SUMMARY OF BID DATA

The 2020-21 Estimated Bid Dates schedule is not available for this Project Overview Report. Based on the most recent data and schedules provided by districts, 16 projects are scheduled to receive sub-bids in 2020, eight projects are scheduled to receive sub-bids in 2021, and one project is scheduled to receive sub-bids in 2022. In 2019, MSBA staff anticipated DBB bids or GMP executions for 22 projects. All 22 projects have received sub-bids and 19 have proceeded to DBB bids or GMP execution. The remaining three projects revised their GMP executions to 2020.

Year	Number of Projects	Design Basis for Enrollment	Project Budget	Construction Budget
2019	22	20,170	\$2.55 billion	\$2.07 billion
2020	16	15,240	\$1.94 billion	\$1.55 billion
2021	8	9,785	\$1.27 billion	\$1.01 billion
2022	1	930	\$91 million	\$72 million
Grand Total	47	46,125	\$5.85 billion	\$4.70 billion

Note: These numbers are based on preliminary information received from the District and are subject to further review and calculation. Data is shown only for projects which have Project Scope and Budget Agreement approval by the Board. For additional information on the bid schedules of these projects, please see Appendix B.

APPENDIX C
SCHOOL CONSTRUCTION COSTS COMPARED
TO COMMON ECONOMIC INDICATORS

School Construction Costs

The New Construction Costs Compared to Common Economic Indicators graph which plots Schematic Design Estimates, Construction Estimates, and Construction Bid Results from 2009 to present is not available for this Project Overview Report. The graph would have included Springfield which is scheduled for Project Scope and Budget Agreement authorization at the June 2020 Board meeting. Northbridge, Shrewsbury, Framingham, Wareham, and now Danvers have received bids since the last graphic could be prepared for the February 2020 Board meeting. Danvers has received its bids, which were within its estimated construction budget, since the April 15, 2020 Board Meeting. All the projects will be reflected in future graphs.

A fully interactive version of the New Construction graph is available on the MSBA website, here: <http://info.massschoolbuildings.org/TabPub/TableauCostData.aspx> .

The Addition/Renovation Costs Compared to Common Economic Indicators graph which plots Schematic Design Estimates, Construction Estimates, and Construction Bid Results from 2009 to present is not available for this Project Overview Report. There are no Addition/Renovation projects scheduled for Project Scope and Budget Authorization at the June 2020 Board meeting. Somerville and now Fall River have received bids since the last graphic could be prepared for the February 2020 Board meeting. Fall River has received its bids, which were within its estimated construction budget, since the April 15, 2020 Board meeting. Both projects will be reflected in future graphs.

A fully interactive version of the Addition/Renovation graph is available on the MSBA website, here: <http://info.massschoolbuildings.org/TabPub/TableauCostData.aspx>

APPENDIX D
CONSTRUCTION STATUS REPORT

**Projects in Construction
MSBA Grant Basis and Maximum Grant Amount
Data Reported as of June 3, 2020**

Core Program and Waitlist Totals			\$3,439,522,793																Includes Alternates	\$1,759,795,360
Project	Grade	Contractor	Total Construction Cost*	Projected Enrollment	PFA or Bid Data	Proposed Sq.Ft.	Construction Cost/Sq.Ft.	Building Cost	Building Cost/Sq.Ft.	Procurement Type	Construction Start Date	Substantial Completion Date *	Building Construction Complete **	Schedule Variance (days) ***	Physical Progress	Change Orders	Change Orders %	Construction Status	Est Max Total Facilities Grant	
CAPITAL PIPELINE PROJECTS IN CONSTRUCTION																				
Core Program Totals			\$3,439,522,793																\$1,759,795,360	
Cape Cod Regional Voc Tech Cape Cod Region Voc Tech	Vocational/Technical	Brait Builders Corp.	\$104,223,800	650	Bid	220,880	\$472	\$65,139,000	\$295	Design/Bid/Build	01-Dec-18	04-Dec-20		0	84%	\$1,423,172	1.366%	Building exterior activities include storefronts, curtain wall and zinc shingles installations. Building interior activities at the core spaces include drywall and framing. At the classroom wings activities include Intumescent spray fireproofing, terrazzo installation, linoleum flooring, finish painting, ceiling grids, lockers, bathroom partitions, and wood door installation. Mechanical equipment is being connected and plumbing fixtures are being installed. Site work activities include site lighting. The OPM reported a reduced workforce from April 1, 2020 to April 27, 2020.	\$45,721,370	
Easthampton Maple	Elementary School	Fontaine Brothers, Inc.	\$90,122,000	1,010	PFA	177,370	\$508	\$57,752,000	\$326	Design/Bid/Build	04-Dec-19	01-Sep-21		0	5%	\$39,156	0.043%	Site work activities include underground drainage, footings and foundations. Building construction activity includes steel erection. The OPM reported the project stopped activities from April 8, 2020 to April 22, 2020 due to an order of the local jurisdiction.	\$49,432,097	
Foxborough Mabelle M Burrell	Elementary School	CTA Construction Co., Inc.	\$27,057,700	270	PFA	61,455	\$440	\$17,853,000	\$291	Design/Bid/Build	14-Nov-19	26-Jul-21		0	20%	\$86,832	0.321%	Construction activities include concrete slab pours at the gymnasium and emergency generator pad. Steel work, roofing, and general site work are ongoing.	\$14,689,542	
Ludlow Chapin Street Elementary School	Elementary School	Fontaine Brothers, Inc.	\$45,754,614	630	Bid	106,250	\$431	\$30,234,697	\$285	Design/Bid/Build	21-May-19	15-Apr-21		0	36%	\$325,451	0.711%	Building exterior activities include exterior framing, roof installation and roof drain connections. Concrete masonry units and dense glass are also in progress. Building interior activities include concrete masonry unit installation at the kitchen, elevators and stairs, framing and spray fireproofing. Mechanical, electrical, plumbing and fire protection installation continues. Site work activities include electrical underground installation.	\$27,081,076	
Marlborough Richer	Elementary School	Fontaine Brothers, Inc.	\$47,831,946	610	Bid	111,437	\$429	\$31,031,124	\$278	Design/Bid/Build	02-Jul-18	08-Apr-20		0	96%	\$569,495	1.191%	Site work activities include courtyard plantings and sub-grading, sidewalks, additional paving, and foyer tile at the front entrance. Punch list work is ongoing.	\$27,295,076	
Middleborough Middleborough High	High School	Fontaine Brothers, Inc.	\$83,582,398	720	PFA	166,650	\$502	\$50,541,889	\$303	Design/Bid/Build	19-Feb-19	13-Nov-20		0	57%	\$284,543	0.344%	Building construction activities include miscellaneous metals, roofing, mechanical, electrical, plumbing rough-in work, fireproofing, rough carpentry, and masonry. Steel punch list activities are in progress. Site work activities include general site development, preparation for concrete paving at concessions, and bleacher installation.	\$42,541,652	
Narragansett Templeton Center	Elementary School	Fontaine Brothers, Inc.	\$36,522,000	580	Bid	92,735	\$394	\$24,888,000	\$268	Design/Bid/Build	06-Dec-17	15-May-19	18-Jun-19	34 behind	99%	\$784,346	2.148%	Final punch list work is ongoing.	\$22,250,143	
Natick J F Kennedy Middle	Middle School	Brait Builders Corp.	\$87,559,890	1,000	Bid	182,195	\$481	\$58,353,861	\$320	Design/Bid/Build	19-Mar-19	07-Oct-21		0	58%	\$1,059,452	1.210%	Building exterior activities include facade and window installations. Building interior activities include finishes as well as mechanical, electrical, and plumbing work. The OPM reported a reduced workforce from April 6, 2020 to April 21, 2020.	\$36,501,996	
Needham Hillside Elementary	Elementary School	Bacon Construction Co., Inc.	\$45,465,414	430	Bid	90,975	\$500	\$32,250,467	\$354	Design/Bid/Build	17-Oct-17	14-Jun-19	05-Jul-19	21 behind	99%	\$1,141,567	2.511%	Site work activities include balance of landscape punch list work. The OPM reported the the school building is closed to contractors as of March 17, 2020.	\$12,931,741	
North Middlesex North Middlesex Regional	High School	CTA Construction Co., Inc.	\$64,995,000	870	Bid	180,530	\$360	\$49,909,000	\$276	Design/Bid/Build	25-May-15	23-Aug-17	23-Aug-17	0	99%	\$3,911,821	6.019%	Building exterior activities include work on the maintenance garage.	\$38,471,881	
Scituate Gates Intermediate School	Middle School	Bacon-Agostini Construction Joint Venture	\$52,596,801	710	Bid	164,803	\$319	\$42,947,412	\$261	Design/Bid/Build	08-Dec-15	14-Aug-17	14-Aug-17	0	99%	\$2,388,406	4.541%	Concrete deterioration at the exterior walks and plazas remains unresolved.	\$20,436,585	
Taunton Mulcahey Elementary School	Elementary School	Agostini Construction Co., Inc.	\$50,074,205	735	Bid	119,693	\$418	\$34,127,642	\$285	Design/Bid/Build	11-Feb-19	26-Jun-20		0	74%	\$272,909	0.545%	Building interior activities include finishes and storefront glazing installation. Building exterior activities include curbs, sidewalks, and site lighting. The OPM reported a reduced workforce from March 20, 2020 to April 21, 2020.	\$39,248,729	
Wareham Minot Forest	Elementary School	Bacon Construction Co., Inc.	\$72,066,378	1,020	PFA	159,989	\$450	\$46,771,033	\$292	Design/Bid/Build	01-Mar-20	21-Jun-21		0	5%	\$0	0.000%	Building exterior activities includes work on concrete footings, foundations, and walls. Site work activities include infiltration and drainage systems.	\$50,841,225	
Attleboro Attleboro High	High School	Consigli Construction Company, Inc.	\$223,088,312	1,725	PFA	476,425	\$468	\$134,982,665	\$283	CM-at-Risk	13-May-19	13-May-22		0	17%	\$183,794	0.082%	Building exterior activities include steel installation, roof and roof blocking. Building interior activities include under slab plumbing and electrical. Slab on deck work is ongoing. Site work activities include miscellaneous grading, excavation and back fill.	\$124,276,563	
Belmont Belmont High	High School	Skanska USA Building, Inc.	\$236,647,607	2,215	PFA	455,100	\$520	\$151,271,445	\$332	CM-at-Risk	10-Jun-19	21-Jul-23		0	17%	\$0	0.000%	Site work activities include civil site work as well as geothermal wells drilling and installing of loops. Building interior activities include steel erection, metal decking and steel detailing. Concrete foundations, mechanical, electrical and plumbing installations are also ongoing. Trenching for under slab mechanical, electrical and plumbing rough-in has commenced. Radiant in-slab tubing is being installed throughout available areas of the building. The OPM reported a reduced workforce from April 6, 2020 to April 24, 2020.	\$77,906,660	
Billerica Billerica Memorial High School	K-12	Shawmut Design and Construction	\$140,773,848	1,610	Bid	325,191	\$433	\$79,526,376	\$245	CM-at-Risk	13-Feb-17	29-Mar-19	06-Jun-19	69 behind	95%	\$539,556	0.383%	Demolition of existing school is ongoing. Site preparation for field and stadium construction is ongoing.	\$71,262,413	
Blue Hills Voc Blue Hills Regional Voc Tech	Vocational/Technical	Consigli Construction Company, Inc.	\$70,509,857	900	Bid	292,400	\$241	\$46,789,510	\$160	CM-at-Risk	28-May-18	30-Nov-19	30-Nov-19	0	99%	\$7,205,295	10.219%	Punch list work is ongoing. Site work activities include spreading dirt pile to repair trailer site and starting bleacher modifications at the athletic field. Commissioning testing continues.	\$42,982,084	
Boston Boston Arts Academy	High School	Lee Kennedy Co., Inc.	\$95,976,807	500	PFA	153,476	\$625	\$64,448,394	\$420	CM-at-Risk	17-Dec-18	20-Oct-21		0	25%	\$0	0.000%	The OPM reported the project was closed from March 16, 2020 to May 18, 2020 due to an order of the local jurisdiction.	\$47,675,093	
Braintree East Middle School	Middle School	Shawmut Design and Construction	\$67,736,699	1,180	Bid	184,425	\$367	\$44,090,239	\$239	CM-at-Risk	01-May-18	01-Jul-20		0	90%	\$1,864,325	2.752%	Building construction activities in the fourth and final phase include build-out of health and bathroom spaces, final finishes in existing academic wing, ceiling tiles, millwork and doors, and hardware installations. Site work activities include playgrounds, east and west parking lots and parent drop-off area repairs. Commissioning and startup activities are in progress. The OPM reported a reduced workforce from April 6, 2020 to April 22, 2020.	\$40,346,375	
Bristol County Agricultural Bristol County Agricultural High	Agricultural	Gilbane Building Company	\$83,953,900	640	PFA	196,081	\$428	\$51,232,400	\$261	CM-at-Risk	15-Jun-19	26-Nov-21		0	22%	\$0	0.000%	Construction progress continues at the north campus buildings. Building exterior activities include site enabling work as well as concrete footings and foundations. Building interior activities include mechanical, electrical, and plumbing rough-in work as well as interior framing. The OPM reported a reduced workforce from March 25, 2020 to April 13, 2020.	\$51,428,124	
Brookline Edward Devotion	Elementary School	Shawmut Design and Construction	\$92,237,854	1,010	Bid	227,087	\$406	\$57,910,095	\$255	CM-at-Risk	11-Jul-16	31-Jul-18	06-Sep-18	37 behind	98%	\$2,272,157	2.463%	Remedial flooring repair and punch list work are ongoing throughout the building.	\$25,197,463	
Central Berkshire Wahconah Regional High	High School	Barr & Barr Inc.	\$59,585,032	460	PFA	122,760	\$485	\$45,210,600	\$368	CM-at-Risk	18-Mar-20	26-Jul-21		0	3%	\$0	0.000%	Site work activities include removal of topsoil, excavation for footings, and concrete pours.	\$30,540,668	
Danvers Ivan G Smith	Elementary School	W. T. Rich Company Inc.	\$42,074,273	465	PFA	82,728	\$509	\$26,619,276	\$322	CM-at-Risk	27-Jun-19	31-May-21		0	17%	\$0	0.000%	Building construction activities include structural steel erection, slab on deck pours, and install of housekeeping pads. Building exterior activities include roof decking, roof blocking, roof drain installation and oil separator installation. The OPM reported a reduced workforce from April 6, 2020 to April 22, 2020.	\$19,842,384	
Fall River B M C Durfee High	High School	Suffolk Construction Company	\$217,839,610	2,570	PFA	501,330	\$435	\$138,754,022	\$277	CM-at-Risk	14-Aug-18	05-May-21		0	31%	\$0	0.000%	Building exterior activities include brick veneer wall and window installation. Renovations to existing field house continue. Building interior activities include spray-foam and sound insulation, rough fire suppression, plumbing, electrical and heating ventilation and air conditioning installations. The OPM reported a reduced workforce from April 3, 2020 to April 21, 2020.	\$165,084,900	
Frammingham Fuller Middle	Middle School	Consigli Construction Company, Inc.	\$77,935,429	630	PFA	136,790	\$570	\$47,232,742	\$345	CM-at-Risk	13-Sep-19	01-Dec-21		0	22%	\$183,564	0.236%	Building exterior activities include steel detailing. Building interior activities include structural masonry and masonry work for the concrete masonry unit wall in the auditorium. Underground plumbing and electrical are also ongoing. Site work activities include miscellaneous grading, excavation and back fill as well as retaining wall work.	\$37,997,085	
Harvard Hildreth Elementary School	Elementary School	Shawmut Design and Construction	\$42,999,041	445	PFA	85,214	\$505	\$26,771,866	\$314	CM-at-Risk	16-Apr-19	12-Apr-21		0	34%	\$811,115	1.886%	Building interior activities include exterior and interior framing, spray fireproofing, roofing, mechanical, electrical, plumbing ductwork, and elevator shaft masonry.	\$18,327,080	
Lexington Maria Hastings	Elementary School	Walsh Brothers, Inc.	\$52,973,417	645	Bid	110,000	\$482	\$34,033,179	\$309	CM-at-Risk	25-Jun-18	10-Feb-20	13-Feb-20	3 behind	92%	\$859,800	1.623%	Punch list work is ongoing. Abatement and demolition of the existing school is ongoing.	\$16,513,723	
Manchester Essex Regional Manchester Memorial Elementary	Elementary School	W. T. Rich Company Inc.	\$41,142,104	335	PFA	77,102	\$534	\$23,969,899	\$311	CM-at-Risk	29-Jul-19	29-Jun-21		0	36%	\$7,499	0.018%	Classroom Building exterior activities include washing down the exterior masonry, roof metal edge measurements, installation of the windows and storefronts and window testing. Building interior activities includes acoustical ceiling tiles, ceramic tiles, painting, mechanical systems, light fixtures and elevator. Site work activities include ramp and helical piles. The OPM reported a reduced workforce from April 6, 2020 to April 27, 2020.	\$12,279,466	
Marblehead Elbridge Gerry	Elementary School	Gilbane Building Company	\$43,786,426	450	PFA	81,935	\$534	\$26,553,310	\$324	CM-at-Risk	04-Apr-20	04-Apr-22		0	1%	\$0	0.000%	Site work activities include site enabling work.	\$13,997,188	
Mills Clyde F Brown	Elementary School	Bacon-Agostini Construction Joint Venture	\$42,591,393	515	Bid	89,852	\$474	\$26,297,583	\$293	CM-at-Risk	15-Feb-18	25-May-19	07-Jun-19	21 behind	94%	\$495,622	1.164%	Site work activities include final landscaping. Building interior activities include completing the punch list.	\$20,951,650	
Minuteman Voc Tech Minuteman Regional High	High School	Gilbane Building Company	\$119,200,892	628	Bid	257,745	\$462	\$71,673,473	\$278	CM-at-Risk	06-Jun-17	25-Sep-19		0	98%	\$2,369,385	1.988%	Punch list work is ongoing. Abatement and demolition of the existing school is ongoing.	\$43,902,613	
Newton Cabot	Elementary School	W. T. Rich Company Inc.	\$36,690,618	480	Bid	84,262	\$435	\$26,978,824	\$320	CM-at-Risk	11-Jul-17	30-Jun-19	09-Aug-19	40 behind	99%	\$357,098	0.985%	Building interior activities include commissioning punch list.	\$13,636,546	

**Projects in Construction
MSBA Grant Basis and Maximum Grant Amount
Data Reported as of June 3, 2020**

Northbridge W Edward Balmer	Elementary School	Fontaine Brothers, Inc.	\$79,492,662	1,030	PFA	167,352	\$475	\$47,191,266	\$282	CM-at-Risk	28-Aug-19	15-Jun-21		0	24%	\$123,151	0.155%	Building exterior activities include structural steel installation and roof drains. Building interior activities include slab on deck work and underground plumbing, as well as electrical work. Site work activities include miscellaneous grading, excavation and back filling as well as miscellaneous landscaping at residential homes abutting the project site.	\$46,043,257
Pentucket Pentucket Regional Sr High	High School	Rich-KBE Pentucket School Joint Venture	\$118,540,836	965	PFA	211,700	\$560	\$70,483,358	\$333	CM-at-Risk	22-Apr-20	29-Aug-22		0	1%	\$0	0.000%	Building interior activities include abatement in the existing building in preparation for boiler room demolition and installation of a temporary boiler and hot water heater. Site work activities include civil site work and fencing.	\$52,752,304
Quincy Reay E Sterling Middle	Middle School	Bond Brothers, Inc.	\$46,550,994	430	Bid	95,732	\$486	\$29,569,323	\$309	CM-at-Risk	20-Jun-17	20-May-19	20-May-19	0	98%	\$1,488,554	3.198%	Punch list and commissioning work is ongoing.	\$28,022,957
Saugus Saugus High	High School	Suffolk Construction Company	\$128,085,356	1,360	Bid	269,070	\$476	\$77,121,412	\$287	CM-at-Risk	25-Jun-18	01-Jul-20		0	82%	\$387,809	0.303%	Building interior activities include punch list work. Site work activities include landscaping and punch list work with demolition of existing school to follow.	\$62,758,835
Shrewsbury Beal School	Elementary School	Fontaine Brothers, Inc.	\$74,111,830	790	PFA	142,113	\$521	\$43,382,405	\$305	CM-at-Risk	02-Sep-19	28-May-21		0	26%	\$0	0.000%	Building exterior activities include forming and pouring of canopy piers as well as installation of roof and air vapor barrier at the roof edge. Building interior activities include installation of underground plumbing, water and sewer pipes, stairs, and concrete masonry units at elevator machine room.	\$33,222,716
Somerville Somerville High	High School	Suffolk Construction Company	\$199,051,710	1,590	PFA	369,496	\$539	\$111,565,951	\$302	CM-at-Risk	12-Jun-17	15-May-20		0	56%	\$1,649,812	0.829%	Exterior building activities include phase 1 and 2 envelope work. The OPM reported an "essential only" reduced workforce starting on March 24, 2020 and then reported a "construction activity shutdown" on April 25, 2020 through May 18, 2020.	\$119,706,988
Springfield Brightwood	Elementary School	Daniel O'Connell's Sons, Inc.	\$66,941,200	800	PFA	150,500	\$445	\$44,037,500	\$293	CM-at-Risk	20-Aug-19	30-Jun-21		0	22%	\$0	0.000%	Building exterior construction activities include installation of stair towers numbers 1 and 2, exterior sheathing, brick veneer and curtain wall. Building interior construction activities include mechanical, electrical, plumbing and fire protection trades working to install overhead and in-wall equipment. Site work activities include catch basin installation and soil density testing. The OPM reported a reduced workforce from April 6, 2020 to April 21, 2020.	\$49,147,673
Stoughton Stoughton High	High School	Consigli Construction Company, Inc.	\$100,961,191	1,065	Bid	214,860	\$470	\$58,510,773	\$272	CM-at-Risk	12-Jun-17	11-Jul-19	11-Jul-19	0	94%	\$3,340,513	3.436%	Site work activities include final landscaping. Building interior activities include the punch list. The OPM reported a reduced workforce from April 6, 2020 to April 27, 2020.	\$50,285,284
Triton Pine Grove	K-8	W. T. Rich Company Inc.	\$30,191,749	415	Bid	87,674	\$344	\$17,111,184	\$195	CM-at-Risk	09-Apr-18	26-Aug-19	23-Aug-19	3 ahead	98%	\$1,095,713	3.629%	Building punch list is ongoing.	\$16,264,155
Westport Westport Junior/Senior High School	Middle/High School	Agostini Construction Co., Inc.	\$79,880,726	860	PFA	187,100	\$427	\$46,662,684	\$249	CM-at-Risk	15-Oct-18	31-Mar-21		0	24%	\$83,928	0.105%	Building exterior activities include steel erection and detailing as well as sheathing. Building interior activities include spray fireproofing, concrete slab placement, and metal framing. Site work activities include site utilities, retaining wall installation, and tennis court construction.	\$37,418,778
Worcester South High Community	High School	Fontaine Brothers, Inc.	\$172,861,181	1,420	Bid	359,994	\$480	\$105,012,370	\$292	CM-at-Risk	11-Oct-18	16-Jun-21		0	49%	\$219,193	0.127%	Site work activities include underground utilities south of the existing school. Building exterior finishes include masonry veneer, fiber cement panels, metal panels, windows, curtain wall and roof metal trim at the Academic and Kitchen buildings. Building interior activities include interior finishes including framing, painting, taping, acoustical ceiling, tiling, mechanical rough-in and electrical. The OPM reported the project was closed from April 7, 2020 to May 11, 2020 due to an order of the local jurisdiction.	\$111,788,053

Substantial Completion Date *

* Contract Substantial Completion Date. Field will remain blank until a contract/GMP has been executed.

Building Construction Complete **

** Field represents actual Substantial Completion date (date of Certificate of Completion).

Variance***

*** Variance is the difference between "Building Construction Completion" date and "Substantial Completion" Date. The number zero (0) will appear in this column until actual certificate of Substantial Completion is achieved.
