

Massachusetts School Building Authority

# CAPITAL PLANNING PROJECT OVERVIEW REPORT

October 28, 2015


# TABLE OF CONTENTS

<b>Capital Pipeline Overview .....</b>	<b>2</b>
<b>Statements of Interest (SOIs) .....</b>	<b>3</b>
<b>Core Program .....</b>	<b>4-10</b>
Eligibility Period .....	4
Consultant Selection .....	5
Feasibility Study .....	6
Schematic Design .....	7
Commissioning .....	8
Design Development .....	9
Summary of Bid Data.....	9
Construction .....	10
<b>Accelerated Repair Program .....</b>	<b>11-13</b>
<b>Project Variances .....</b>	<b>14-15</b>
<i>Appendix</i>	
(A) <i>Project Status List</i>	
(B) <i>2015 &amp; 2016 Estimated Bid Dates</i>	
(C) <i>Construction Status Report</i>	

# CAPITAL PIPELINE OVERVIEW

## Current Projects Status

A total of 306 projects that have received invitations from the Board of Directors (“Board”) to collaborate with the MSBA are currently in the MSBA’s Eligibility Period and Capital Pipeline. The summary chart provides the number of projects in Eligibility Period and each phase of the Capital Pipeline. For a detailed look at the Capital Pipeline projects, please go to [www.massschoolbuildings.org/building](http://www.massschoolbuildings.org/building) and select “Capital Pipeline Status Chart”.

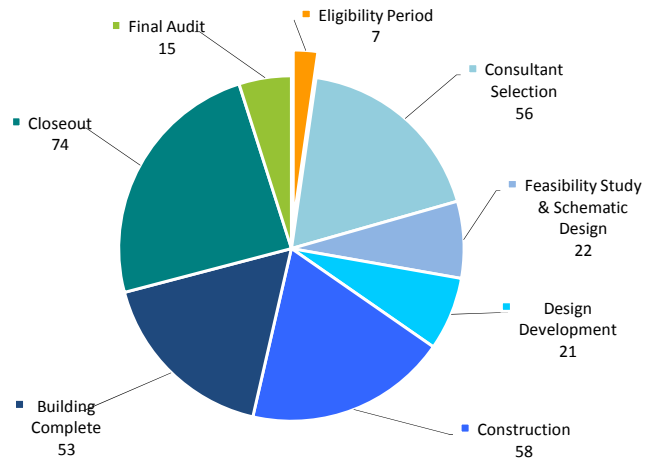

## 2015 Progress Report

- SOI 2015
  - 97 Core Program SOIs were received; due diligence is underway.
  - 2015 ARP SOIs were finalized with recommendations for invitation issued for 24 districts representing 44 projects at the June 3, 2015 Board meeting.
- SOI 2016
  - Preparing to open the SOI System for January 2016.
- Eligibility Period
  - Six of the seven districts in Eligibility Period are being recommended for an invitation to Feasibility Study at the November Board Meeting. The remaining district is anticipated in January.
- Feasibility Study/Schematic Design
  - One district received MSBA approval for selection of an OPM.
  - One district completed designer selection.
- Accelerated Repair Program
  - From the 2015 SOI opening, 23 of 24 districts have completed preliminary requirements and have been assigned consultants. The final consultant assignment will be made following the MSBA’s receipt of the district’s funding authorization vote. Project funding agreements are expected in the winter/spring for all districts.
- Construction Costs
  - Of the 14 bids and/or executions of a GMP in 2015, ten have been reported to date.
  - Of the ten, seven bids came in within the estimated budget.
- Substantial Completion
  - Of the 24 districts anticipating substantial completion in 2015, 21 have declared substantial completion as of this report.

# STATEMENTS OF INTEREST (SOIs)

## **2015 SOI Process**

The 2015 Statement of Interest ("SOI") process opened on Friday, January 9, 2015. The deadline to file a SOI for consideration in the Accelerated Repair Program ("ARP") was Friday, February 13, 2015. Due to inclement weather, the MSBA extended the deadline for ARP printed SOI materials and related vote information to Friday, February 17, 2015. As of the deadline, the MSBA received 61 SOIs, submitted by 24 districts, for consideration into the Program. Invites into the ARP were concluded at the June 3, 2015 Board of Directors meeting; and 24 districts, representing 44 projects, were invited into the Program.

The deadline to file a SOI for consideration in the Core Program, which is primarily for projects beyond the scope of Accelerated Repair, including extensive repairs, renovations, additions/renovations and new school construction, was Friday, April 10, 2015. As of the deadline, the MSBA received 97 Core Program SOIs. The review process for these SOIs continues with Senior Studies underway and invites into Eligibility Period anticipated at the winter of 2016 Board of Directors meetings.

# CORE PROGRAM

## Eligibility Period

There are seven districts in Eligibility Period. All seven districts have secured funding.

An agreed-upon enrollment is a key pre-requisite for the MSBA to commence a Feasibility Study with a district. To begin the enrollment projection process, a district must file enrollment information utilizing the MSBA’s online enrollment projection tool. All seven districts have completed their online enrollment projection information. Of the seven districts, six districts have signed their enrollment certifications and one enrollment certification is pending.

Based upon the schedules anticipated by the districts for completion of Eligibility Period requirements, staff anticipates recommending six districts in Eligibility Period for an Invitation to Feasibility Study at the November Board meeting and the remaining district in January 2016.

District	School	Date of Invitation to Eligibility Period	30 days	60 days	90 days		180 days		270 days	Date of Invitation to Feasibility Study (Estimated)
			ICC	SBC	Online Enrollment Projection Info	Ed Profile Questionnaire	Maintenance Documents	Enrollment Certification	Local Authorization	
Attleboro	Attleboro HS	01/14/15	x	x	x	x	x	x	x	11/18/15
Bristol County Agricultural RSD	Bristol County Agricultural HS	01/14/15	x	x	x	x	x	x	x	11/18/15
Clarksburg	Clarksburg ES	01/14/15	x	x	x	x	x	x	x	11/18/15
Fall River	B.M.C. Durfee HS	01/14/15	x	x	x	x	x	x	x	11/18/15
Lowell	Lowell HS	3/25/15	x	x	x	x	x	x	x	11/18/15
Middleborough	Middleborough HS	01/14/15	x	x	x	x	x	x	x	11/18/15
Everett	George Keverian School	3/25/15	x	x	x	x	x		x	1/27/16

**Consultant Selection**

**OPM Selection**

After the district has completed all Eligibility Period requirements and has received a Board Invitation to Feasibility Study, the district procures an Owner’s Project Manager (“OPM”). Since the last report, one district has completed its OPM selection as shown shaded in the table below. Currently, there are 10 districts in the Capital Pipeline that are in the process of procuring an OPM.

District	School	Anticipated Selection
Ipswich	Winthrop ES	September 2015
Saugus	Saugus HS	December 2015
Westport	Westport MS	December 2015
Lynn	Pickering MS	January 2016
Waltham	Waltham HS	January 2016
Boston	Boston Arts Academy	February 2016
Cape Cod RVTSD	Cape Cod RTHS	February 2016
Easthampton	Maple ES	February 2016
Taunton	Mulcahey ES	March 2016
Holyoke	Lt. Elmer J. McMahan ES	TBD
Worcester	South High Community School	TBD

**Designer Selection**

After a district has selected and executed a contract with an OPM, it selects a Designer utilizing either a local designer selection process for projects under \$5 million or the MSBA’s Designer Selection Panel (“DSP”) for projects over \$5 million. Since the last report, one district has completed their Designer selection as shown shaded in the table below. There are currently two districts in the Capital Pipeline that are in the process of procuring a Designer.

District	School	Anticipated Selection
Bourne	James F. Peebles ES	September 2015
Millis	Clyde F. Brown ES	November 2015
Ipswich	Winthrop ES	December 2015

For additional information on the selected consultant teams, see Appendix A.

**Feasibility Study**

Once a district has procured an OPM and Designer, the district and its consultants must complete two Feasibility Study submittals, the Preliminary Design Program and the Preferred Schematic Report, prior to Board consideration to proceed into Schematic Design. Based on the most recent data and schedules provided to the MSBA by districts, the MSBA anticipates that seven districts will present their preferred schematic designs to the Board at the upcoming November, January, and March Board meetings.

District	School	Anticipated PS Board Date
Quincy	Sterling MS	November 18, 2015
Hanover	Sylvester ES	January 27, 2016
Needham	Hillside ES	January 27, 2016
Stoughton	Stoughton HS	January 27, 2016
Amherst	Wildwood ES	March 30, 2016
Boston	Quincy Upper School	March 30, 2016
Braintree	East MS	March 30, 2016

## Schematic Design

Prior to consideration by the Board for Project Scope and Budget authorization, a district must submit a Schematic Design to the MSBA for review. Based on the most recent data and schedules provided to the MSBA by districts, the MSBA anticipates that eight districts will appear before the Board for Project Scope and Budget Agreement authorization at the upcoming November, January, and March Board meetings.

District	School	Anticipated PS&B Board Date
Carver	Carver ES	November 18, 2015
Narragansett RSD	Templeton Center ES	November 18, 2015
Billerica	Memorial HS	January 27, 2016
Granby	West Street ES	January 27, 2016
Minuteman RVTSD	Minuteman Career and Technical HS	January 27, 2016
Mount Greylock RSD	Mount Greylock RHS	January 27, 2016
Dedham	Early Childhood Center	March 30, 2016
Newton	Cabot ES	March 30, 2016



## **Commissioning**

The MSBA assigns a Commissioning Consultant once a district has secured local funding for the Board approved project. Since the last report, the MSBA has assigned additional Commissioning Consultants to three projects presented in the table below.

District	School	Program	Estimated Const. Cost (million)	Commissioning Consultant	Contract Amount
Beverly	Briscoe MS	Core	\$90.10	Bard, Rao + Athanas Consulting Engineers, LLC	\$180,587
Holyoke	2 Schools (Boilers)	2014 ARP	\$0.66	BVH Integrated Services, PC	\$29,320
New Bedford	John Hannigan ES	Core	\$29.80	WSP USA	\$85,905

To date, the MSBA has executed 331 Commissioning Consultant contracts, totaling \$23.9 million. To date, 176 contracts have been completed.

The table below represents the status of commissioning assignments sorted by the fiscal year in which the commissioning work orders were issued.

Fiscal Year	No. Work Orders Issued	Value of Work Orders Issued	Total Invoiced	Percent Complete
FY10	31	\$4,231,376	\$4,273,277	100%
FY11	95	\$6,132,890	\$6,043,905	99%
FY12	52	\$4,450,761	\$4,181,045	94%
FY13	55	\$3,364,697	\$2,747,258	82%
FY14	47	\$2,604,062	\$1,520,078	58%
FY15	44	\$2,277,711	\$601,837	26%
FY16	7	\$826,592	\$4,900	1%

**Design Development**

Once a district has secured local funding and has entered into a Project Funding Agreement with the MSBA, it enters into the Design Development phase. Currently, there are 21 projects in the Design Development phase with a total estimated construction cost of approximately \$501.6 million: 13 Accelerated Repair projects, one waitlist project, and seven Core Program projects. The seven Core Program projects in Design Development have a total estimated construction cost of approximately \$470.7 million and are listed below.

Elementary School Districts	Middle and Middle/High School Districts	High School Districts	Other Grade Configurations
New Bedford	<p><b><u>Middle School Districts</u></b></p> <p>Beverly Scituate Westborough</p> <p><b><u>Middle/High School Districts</u></b></p> <p>Abington</p>	Pittsfield	Brookline (K-8)

**Summary of Bid Data**

Based on the most recent data and schedules provided by the districts, the MSBA anticipates 14 projects will bid in 2015.

Year	Number of Projects	Design Basis for Enrollment	Project Budget	Construction Budget
2015	14	10,654	\$887.9 M	\$700.9 M
2016	9	5,500	\$539.4 M	\$444.9 M
<b>Totals</b>	<b>23</b>	<b>16,154</b>	<b>\$1.43 B</b>	<b>\$1.15 B</b>

*Note: These numbers are based on preliminary information received from the District and are subject to further review and calculation.*

**Anticipated Bids in 2015:**

- November – Chelsea (CMR), Holbrook (CMR)
- December – Boston (CMR ), Scituate (DBB)

**Anticipated Bids in 2016:**

- January – N/A
- February – Westborough (CMR)

For additional information on each of these projects, see Appendix B.

**Construction**

When a district issues a Notice to Proceed, the project is advanced to the Construction phase. Currently, there are 58 projects in the Construction phase with a total estimated construction cost of \$1.16 billion: 35 Accelerated Repair projects and 23 Core Program projects. This does not include the 53 projects that have reached substantial completion and are currently in the Building Complete phase. The 23 Core Program projects have a total estimated construction cost of \$1.11 billion and are listed below.

Elementary School Districts	Middle and Middle/High School Districts	High School Districts	Other Grade Configurations
Athol-Royalston Regional Gloucester Milford Newton Northborough South Hadley Westfield*	<p><b><u>Middle School Districts</u></b></p> Chelsea Lynn Peabody Wachusett Regional	North Middlesex Regional Plymouth Winchester	Haverhill (K-8) Holbrook (PK-12) North Adams (K-7) Worcester (PK-6)
	<p><b><u>Middle/High School Districts</u></b></p> Boston ( <i>Dearborn MS</i> ) Georgetown Greenfield Lunenburg Winthrop		

*\*Note: Westfield, Abner Gibbs Elementary School, stopped construction in December of 2012 due to a preliminary injunction based upon project site status as Article 97 "Protected Land".*

For additional information on the construction status for each of these projects, see Appendix C.

# ACCELERATED REPAIR PROGRAM

Currently there are a total of 83 districts, representing 172 projects, either active or completed in the Accelerated Repair Program.

Repair Program	Number of Districts	Number of Projects	Total Project Budgets	Maximum Facility Grants	Number of Projects Final Audit Approved
2015 Accelerated*	24	44	-	-	0
2014 Accelerated**	34	47	\$108,410,084	\$65,388,035	0
2013 Accelerated	25	45	\$94,349,037	\$54,509,127	7
2012 Accelerated	24	36	\$63,009,653	\$38,267,952	22
Green	93	189	\$366,647,226	\$222,889,214	180

\*Totals reflect projects invited into the Accelerated Repair Program as of the September 30, 2015 Board of Directors' Meeting.


\*\*Totals reflect projects approved for Project Funding Agreements as of the September 30, 2015 Board of Directors' Meeting.

## 2015 Accelerated Repair Program

- Invitations – 24 districts, representing 44 projects
  - Scope includes 22 roofs, 26 windows/doors and nine boilers
- Consultants assigned following submission of pre-requisite documents
- One district, representing one project, is seeking PFA approval at the November 18, 2015 Board of Director's Meeting

## 2014 Accelerated Repair Program


- Invitations – 36 districts, representing 51 projects
- SOI Removal – two districts, representing four projects
- Current 2014 ARP projects – 34 districts, representing 47 projects
  - Scope includes 20 roofs, 25 windows/doors and 13 boilers
- Approved for Project Funding Agreements – 34 districts, representing 47 projects
- Total Project Budgets - \$108,410,084
- MSBA Total Facilities Grants - \$65,388,035
- Four districts, representing six projects, required schedule extensions following PFA approval
- 93% of reporting projects bid within estimated budget

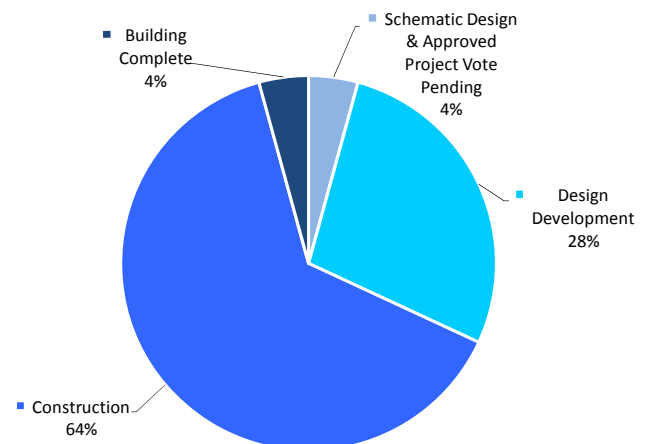

2014 ARP Status Chart

### 2013 Accelerated Repair Program


- Invitations – 28 districts, representing 50 projects
- SOI Removals – four districts, representing five projects
- Approved for Project Funding Agreements – 26 districts, representing 47 projects
- Active Projects – 25 districts, representing 45 projects
  - Scope includes 30 roofs, 13 windows/doors and seven boilers
- Total Project Budgets – \$94,349,037
- MSBA Total Facilities Grants – \$54,509,127
- Four districts, representing seven projects, required schedule extensions following PFA approval
- 82% of projects bid within estimated budget
- Since the last report, projects that have reached substantial completion have increased from 80.8% to 89%

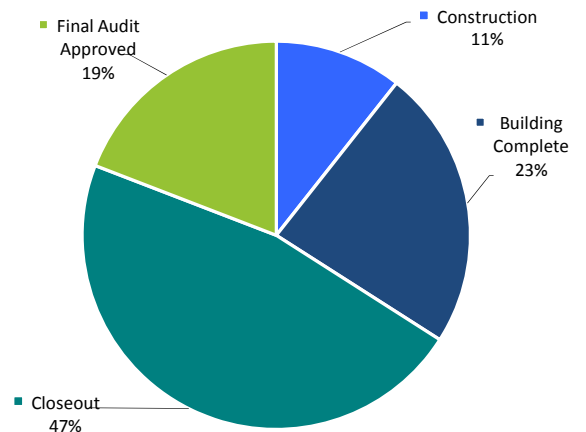

2013 ARP Status Chart

### 2012 Accelerated Repair Program

- Invitations – 27 districts, representing 39 projects
- SOI Removals – three districts, representing three projects
- Approved Project Funding Agreements – 24 districts, representing 36 projects
  - Scope includes 21 roofs, 11 windows/doors and seven boilers
- Total Project Budgets – \$63,009,653
- MSBA Total Facilities Grants – \$38,267,952
- Five districts, representing nine projects, required schedule extensions following PFA approval
- 86% of projects bid within estimated budget
- 61.1% of projects have completed final audit

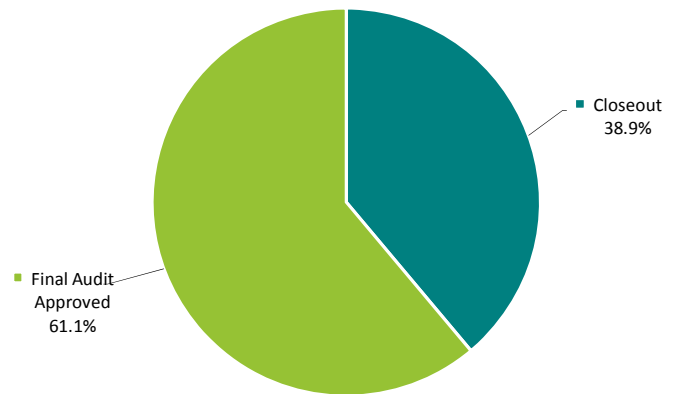

2012 ARP Status Chart

### Status of Green Repair Program

The Green Repair Program resulted in PFA authorizations totaling \$366,647,226 in Total Project Costs and \$222,889,214 in MSBA grants. Of the 189 projects, 180 have been approved for final grant payments. All projects that have not been previously approved for final grant payments (9) are substantially complete and require Final Audit.

## 2014 Accelerated Repair Projects – Construction Estimate vs. 2015-2016 Bid Amount

- Staff has reported previously on the shaded projects .
- As of this report, staff notes two new projects have been out to bid.
- 93% of the 28 reported projects came within the estimated budget.
- 16 additional projects are scheduled to be reported prior to the January 27, 2016 Board of Directors meeting.
- After the January 27, 2016 Board of Directors meeting, the final two projects will be bid in February 2016.

				Total	\$49,430,476	\$35,321,113	\$14,109,363	-	\$8,941,683
District	School	Scope	Project Type	Bid Date	Construction Estimate **	Bid Amount **	Variance from Construction Estimate	Reimbursement Rate	Potential Grant Variance *
Quincy	Francis W. Parker MS	Windows/Doors	DBB	Jan-15	\$1,077,920	\$987,000	\$90,920	71.16%	\$64,699
Quincy	Lincoln-Hancock Community School	Windows/Doors	DBB	Jan-15	\$2,075,113	\$1,479,000	\$596,113	71.16%	\$424,194
Sudbury	General Nixon ES	Partial Roof/ Partial Windows/Doors	DBB	Feb-15	\$915,204	\$817,466	\$97,738	36.89%	\$36,056
Lynn	William P. Connery ES	Roof	DBB	Feb-15	\$859,532	\$604,000	\$255,532	78.95%	\$201,743
Lynn	E. J. Harrington ES	Roof	DBB	Feb-15	\$1,505,681	\$1,217,700	\$287,981	78.95%	\$227,361
Worcester	Goodard School of Science and Technology	Windows/Doors	DBB	Feb-15	\$4,634,609	\$3,053,000	\$1,581,609	78.95%	\$1,248,680
Worcester	West Tatnuck School	Windows/Doors	DBB	Feb-15	\$1,997,979	\$1,162,019	\$835,960	78.95%	\$659,990
Worcester	Clark Street Community	Windows/Doors	DBB	Feb-15	\$2,095,791	\$1,465,163	\$630,628	78.95%	\$497,881
Worcester	Union Hill School	Windows/Doors	DBB	Feb-15	\$2,096,895	\$1,618,818	\$478,077	78.95%	\$377,442
Dartmouth	George H. Potter ES	Roof	DBB	Feb-15	\$1,548,538	\$1,283,000	\$265,538	51.84%	\$137,655
Medway	John D. McGovern ES	Windows/Doors	DBB	Feb-15	\$894,675	\$561,886	\$332,789	50.16%	\$166,927
Norwood	Cornelius M. Callahan ES	Boiler	DBB	Mar-15	\$356,939	\$224,171	\$132,768	50.58%	\$67,154
Greenfield	Green River	Roof, Windows/Doors	DBB	Mar-15	\$1,739,286	\$1,005,890	\$733,396	77.47%	\$568,162
Springfield	Kensington Avenue	Windows/Doors	DBB	Mar-15	\$779,500	\$832,500	-\$53,000	80.00%	\$0
Wellesley	Wellesley MS	Windows/Doors	DBB	Mar-15	\$3,827,871	\$2,752,500	\$1,075,371	31.00%	\$333,365
Tyngsborough	Tyngsborough HS	Roof, Boiler	DBB	Mar-15	\$3,282,118	\$1,964,300	\$1,317,818	52.89%	\$696,994
Middleton	Fuller Meadow ES	Partial Roof	DBB	Apr-15	\$1,257,849	\$906,800	\$351,049	46.37%	\$162,781
Northampton	Leeds ES	Partial Roof	DBB	Apr-15	\$540,900	\$401,550	\$139,350	56.26%	\$78,398
Northampton	R. K. Finn Ryan Road School	Partial Roof	DBB	Apr-15	\$851,639	\$501,520	\$350,119	56.26%	\$196,977
North Attleborough	Roosevelt Avenue ES	Boiler	DBB	Apr-15	\$303,623	\$265,667	\$37,956	53.53%	\$20,318
Southern Berkshire RSD	Mount Everett RHS	Roof, Boiler	DBB	Apr-15	\$6,376,974	\$4,806,662	\$1,570,312	39.21%	\$615,719
Leominster	Northwest ES	Roof	DBB	May-15	\$2,693,028	\$1,805,000	\$888,028	71.96%	\$639,025
Tri-County Regional	Tri-County RVTHS	Boiler	DBB	Jun-15	\$729,259	\$494,131	\$235,128	51.42%	\$120,903
Auburn	Auburn MS	Roof, Partial Boiler	DBB	Jun-15	\$1,757,394	\$1,371,393	\$386,001	54.16%	\$209,058
Auburn	Bryn Mawr ES	Roof	DBB	Jun-15	\$671,935	\$578,000	\$93,935	54.16%	\$50,875
South Shore Voc-Tech Regional	South Shore Voc-Tech Regional HS	Boiler	DBB	Aug-15	\$519,808	\$354,200	\$165,608	54.16%	\$89,693
Orleans	Orleans ES	Partial Window/Door	DBB	Oct-15	\$872,628	\$969,480	-\$96,852	36.68%	\$0
Brockton	Brookfield ES	Roof	DBB	Oct-15	\$3,167,788	\$1,838,297	\$1,329,491	78.95%	\$1,049,633

\*These numbers are based on preliminary information received from the district and are subject to further review and calculation.

\*\*The construction estimate and bid amount do not include pre-construction services and alternatives.

# PROJECT VARIANCES

## Core Program – Total Project Budget Update

Upon receiving the Board’s approval of the Project Scope and Budget, the MSBA and participating districts enter into a Project Funding Agreement that establishes the Total Project Budget and the Estimated Maximum Total Facilities Grant for an approved project. Staff has reported on budget increases for the 13 projects shaded below at previous Board meetings. In no event has the increase in budget resulted in an increase to the Estimated Maximum Total Facilities Grant as authorized by the Board.

Since the last report, staff notes that one project has increased its Total Project Budget.

District	School	Scope	Project Funding Agreement		PFA Bid Amendment/ Final Audit		Reason for Increase to Total Project Budget
			Total Project Budget	Total Maximum Facilities Grant	Total Project Budget	Total Maximum Facilities Grant	
Andover	Bancroft ES	New	\$44,659,837	\$16,773,753	\$50,374,837	\$16,575,965	The District has appropriated additional funds to cover the costs associated with increased construction costs and additional contingencies for litigation/settlement costs and other ineligible costs.
Burlington	Marshall Simonds MS	Add/Reno	\$32,865,272	\$17,143,365	\$34,221,929	\$15,362,127	The District appropriated at its May 2012 annual town meeting through Articles 18: 19, additional funds for the costs associated with the construction of the new field complex and field lighting replacement.
Essex North Shore Agricultural & Technical School District	Essex North Shore Agricultural & Technical High School	New	\$125,000,000	\$77,500,000	\$133,770,000	\$77,500,000	The Board was informed at the March 30, 2011 meeting that the Total Project Budget had increased due to additional ineligible scope that would be funded by DCAM.
Essex North Shore Agricultural & Technical School District	Essex North Shore Agricultural & Technical High School	New	\$125,000,000	\$77,500,000	\$134,501,368	\$77,500,000	The District has appropriated additional funds to cover the costs associated with increased construction costs for horse tack barn renovations.
Lexington	Estabrook ES	New	\$40,792,248	\$12,250,739	\$43,392,248	\$12,148,491	The District has executed a GMP that exceeds the Construction Budget of the PFA. The District has appropriated additional funds to cover the costs associated with increased construction costs and additional contingencies.
North Reading	North Reading MS/HS	Add/Reno	\$107,727,074	\$49,323,123	\$123,227,074	\$49,323,123	This is a CMR project. The estimated, reconciled construction costs tracked over budget at DD (\$9,746,655 over), 60% (\$4,655,965 over), and 90% (\$15,136,846 over). A Town override vote in March 2013 obtained an additional \$15,500,000 in local funding to proceed.
Revere	Staff Sergeant James J. Hill ES	New	\$45,402,396	\$29,551,048	45,402,396	\$29,551,048	At Project Scope and Budget, the Total Project Budget was approved at \$44,382,396. The City of Revere has increased the land acquisition budget. Therefore, the projected total project budget at PFA has increased to \$45,402,396. Note that the MSBA grant has not changed since the Project Scope and Budget Agreement.
Somerville	East Somerville Community School	Add/Reno	\$33,185,258	\$15,237,996	\$38,006,621	\$15,237,996	At the March 28, 2012 Board Meeting, the Board approved an amendment to the PFA and a \$6.25M District loan.
Uxbridge	Uxbridge HS	New	\$43,000,000	\$22,362,328	\$44,986,479	\$22,362,328	The District has appropriated additional funds to cover the costs associated with the construction of athletic fields originally included in the PFA but which were not included in the bid as the District’s construction contract would have exceeded the budget.
Norfolk County Agricultural	Norfolk County Agricultural HS	Add/Reno	\$28,552,385	\$15,369,712	30,589,078	13,867,050	The District has executed a Tender Agreement and Completion Agreement Contract, increasing its Total Project Budget, following the termination of its original construction contract.
Northborough	Lincoln Street ES	Add/Reno	\$25,530,553	\$10,407,408	TBD*	TBD*	The MSBA Board Approved Total Project Budget increased by \$60,400 from \$25,470,153 to \$25,530,553 due to the addition of an alternate, for a new ball field added at the District’s request.
Sutton	Sutton MS	Add/Reno	\$59,945,474	\$29,843,511	TBD*	TBD*	The District has executed a Tender Agreement and Completion Agreement Contract, increasing its Total Project Budget, following the termination of its original construction contract.
Weston	Field ES	New	\$31,504,146	\$8,310,510	TBD*	TBD*	District-approved Construction Change Orders exceeded available contingency amount.
Winthrop	Winthrop MS/HS	New	\$81,818,740	\$42,582,841	TBD*	TBD*	The MSBA Board Approved Total Project Budget increased due to revised FEMA flood plain requirements which necessitated the elevation of the new building to be raised. Note that the increased Total Project Budget will not increase the Maximum Total Facilities Grant.
Woburn**	Wyman-Hurld ES	New	\$33,705,396	\$14,387,427	TBD*	TBD*	The District had completed a project review with its Conservation Commission and an Order of conditions was issued on June 12, 2015. A neighborhood group has appealed this Order and it is now under review by DEP. The District has experienced delays in completing its City Council vote for its appropriation and incurred additional costs.

\*PFA Bid Amendment has not been developed to calculate a revised Total Facilities Grant amount. The Total Maximum Facilities Grant will not exceed the Board authorized amount in the PFA but, upon review, may decrease.

\*\*Pending an executed Project Funding Agreement.

### Accelerated Repair Projects – Schedule Extension Update

The MSBA has granted districts conditional extensions to their Project Funding Agreements pending compliance with the following stipulations:

- The district needed to submit a detailed, revised construction timeline showing how the work will be completed at each school; and
- Any costs that may result from the district’s requested extension of the construction schedule will be the sole responsibility of the district and are categorically ineligible for reimbursement by the MSBA.

Schedule delays for these districts can be attributed to local funding issues, lead time for windows, and construction delays on site. In no event have the extended schedules resulted in an increase to the Estimated Maximum Total Facilities Grant as authorized by the Board.

Seven of the 45 2013 Accelerated Repair Projects did not meet their anticipated construction completion dates in 2014. These projects have revised construction schedules and are scheduled to be completed in 2015.

As of this report, staff notes that there is no new activity.

District	School	Scope	Original Construction Completion Date	Updated Construction Completion Date	Reason for Schedule Extension
Hamilton-Wenham RSD	Winthrop ES	Windows	9/15/2014	8/13/2015	The District and its consultants have determined that the estimated lead time for windows requires construction to be scheduled for 2015.
Pathfinder RVTSD	Pathfinder RVTHS	Roof	9/22/2014	8/28/2015	The District fell behind schedule due to local funding issues.
Quincy	Merrymount ES	Windows	9/22/2014	8/28/2015	The District and its consultants have elected to re-bid the project and complete construction in 2015.
Quincy	North Quincy HS	Windows	9/22/2014	8/28/2015	The District and its consultants have elected to re-bid the project and complete construction in 2015.
Quincy	Wollaston ES	Windows	9/22/2014	8/28/2015	The District and its consultants have elected to re-bid the project and complete construction in 2015.
Dighton-Rehoboth RSD	Dighton ES	Roof	8/29/2014	7/31/2015	The District requested that spray-foam insulation be applied during Summer 2015. The spray-foam created an odor that was disruptive to students and staff.
Dighton-Rehoboth RSD	Dighton MS	Roof	8/29/2014	7/31/2015	The District requested that spray-foam insulation be applied during Summer 2015. The spray-foam created an odor that was disruptive to students and staff.

Six of the 47 2014 Accelerated Repair Projects will not meet their anticipated construction completion dates in 2015. These projects have revised construction schedules and are scheduled to be completed in 2016. Staff has reported previously on the five shaded projects listed below.

As of this report, staff notes one project has extended its Construction Completion date.


District	School	Scope	Original Construction Completion Date	Updated Construction Completion Date	Reason for Schedule Extension
Orleans	Orleans ES	Partial Window/Door	8/25/2015	8/29/2016	The District and its consultants have determined that the estimated lead time for windows requires construction to be scheduled for 2016.
Springfield	John F. Kennedy MS	Window/Door	12/22/2015	10/28/2016	The District and its consultants have determined that the estimated lead time for windows requires construction to be scheduled for 2016.
Brockton	Ashfield MS	Roof/Boiler	8/31/2015	7/11/2016	The District and its consultants have determined that the bidding for construction in 2016 would better serve the project budget and existing facilities.
Brockton	Gilmore School	Roof/Boiler	8/31/2015	7/11/2016	The District and its consultants have determined that the bidding for construction in 2016 would better serve the project budget and existing facilities.
Medfield	Ralph Wheelock School	Boiler	1/6/2016	8/31/2016	The District and its consultants have determined that the bidding for construction in 2016 would better serve the project budget and existing facility.
Springfield	Kensington Avenue	Window/Door	11/2/15	8/19/16	The District and its consultants have determined that the estimated lead time for windows requires construction to be scheduled for 2016.



# PROJECT STATUS

Total Number of Projects: 299

Wednesday, October 28, 2015

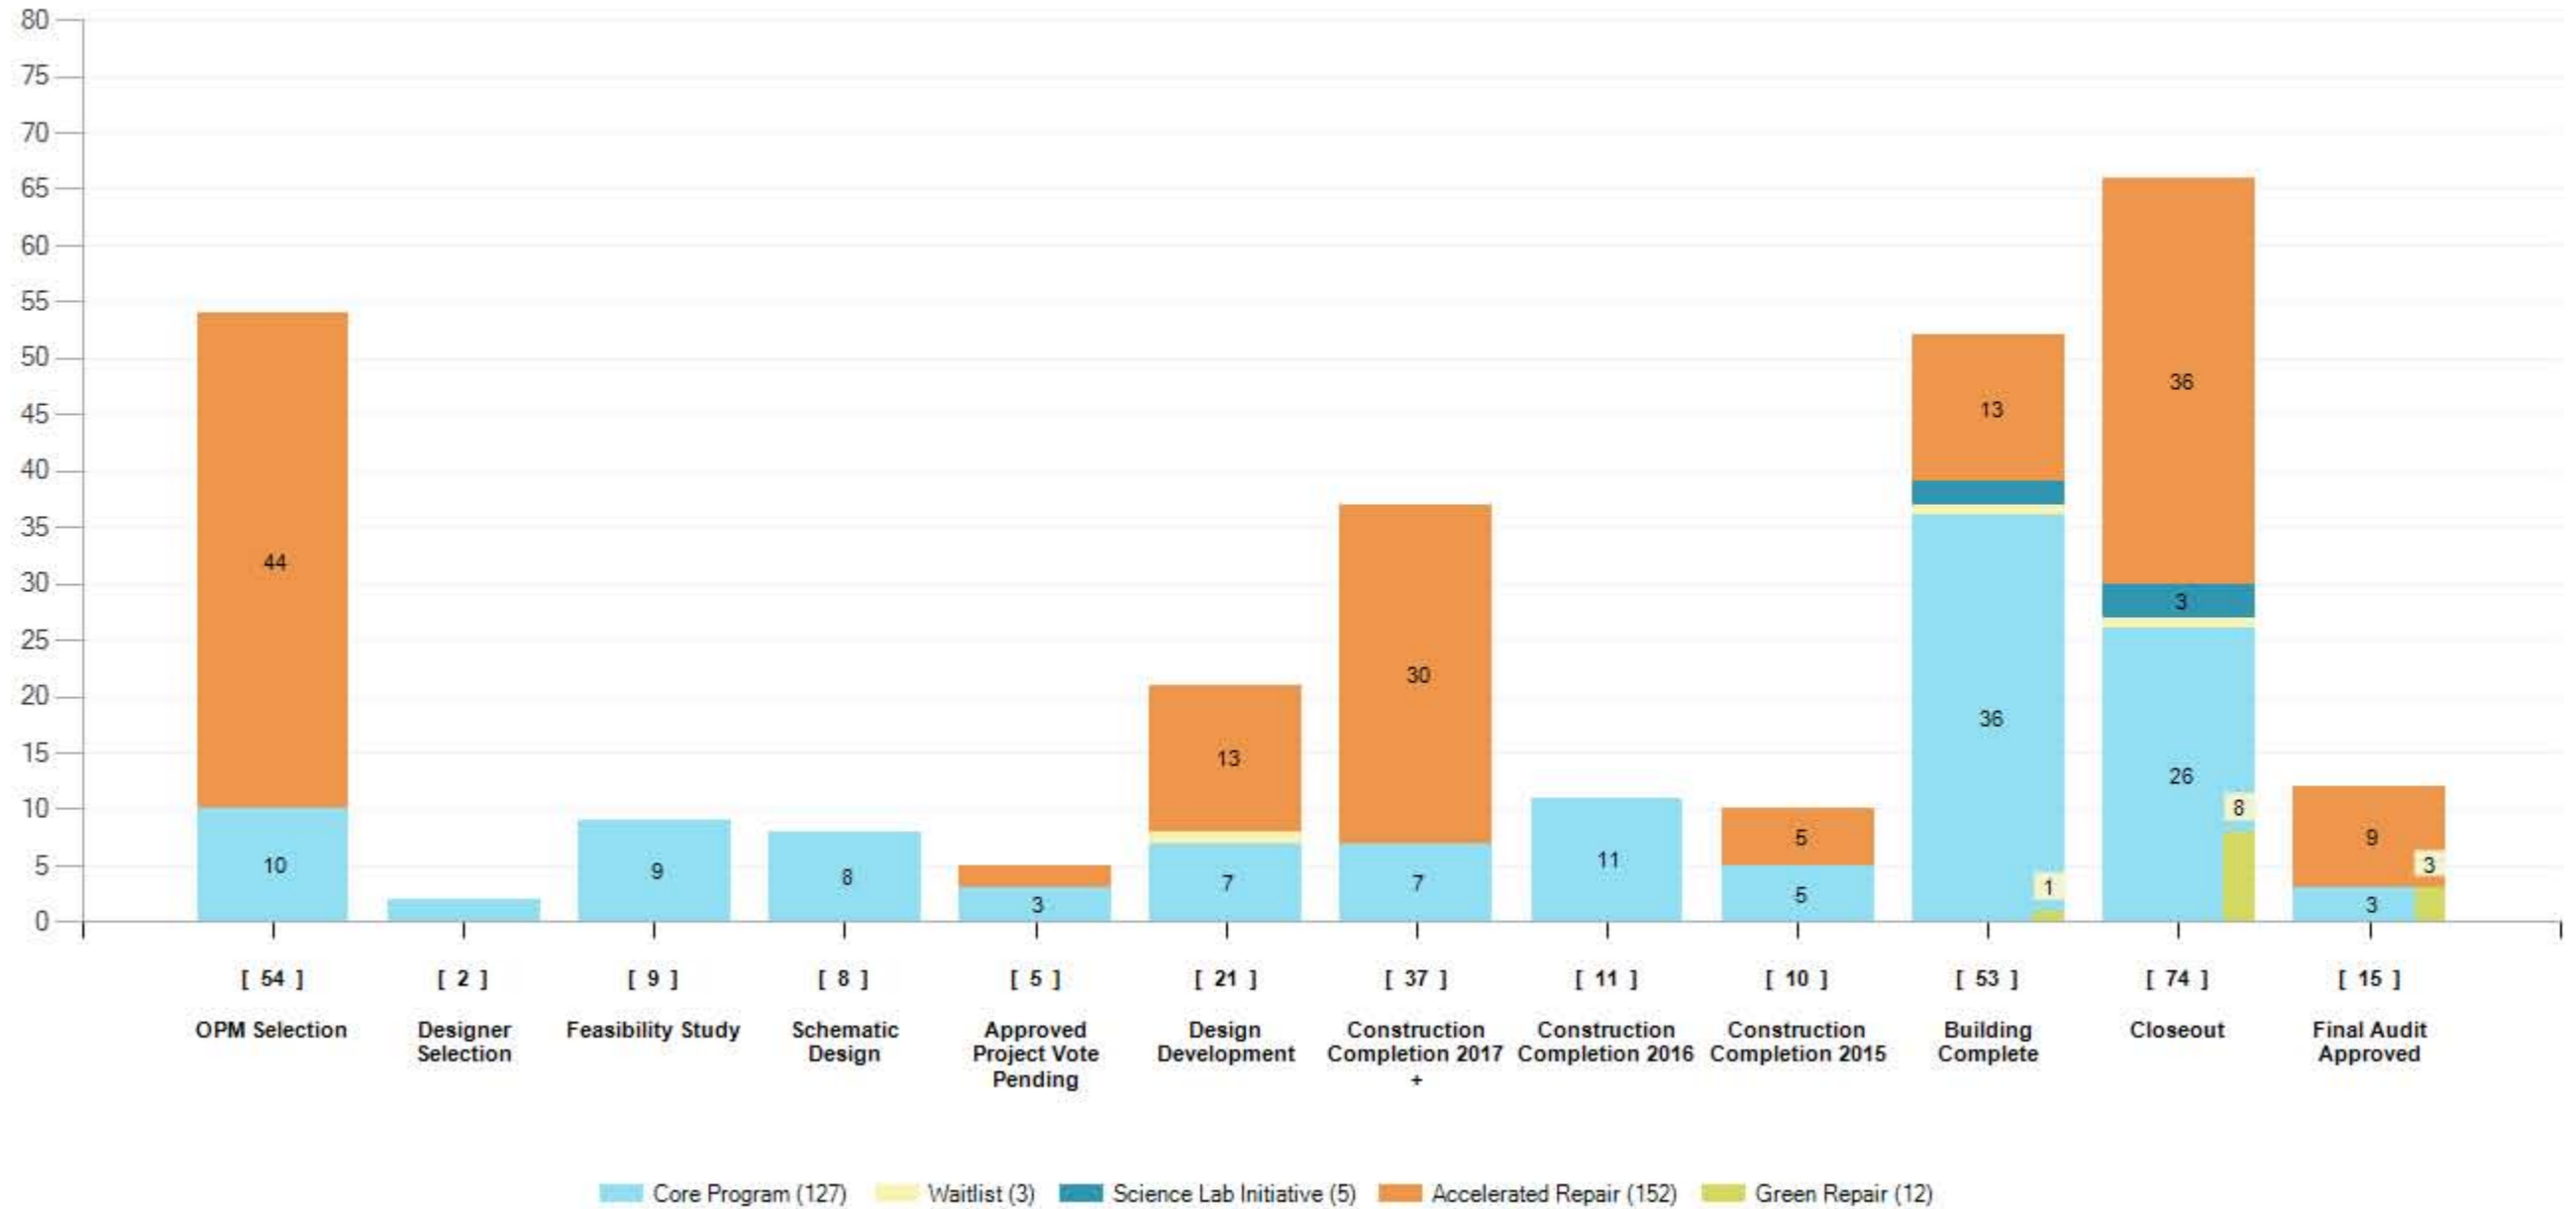

Number less than 3 is not shown in the chart.

# PROJECT INDEX

Wednesday, October 28, 2015

## OPM Selection

Blackstone Valley Reg	Blackstone Valley	OPM Selection	Accelerated Repair
Boston	Dorchester Academy	OPM Selection	Accelerated Repair
Boston	Charles Sumner	OPM Selection	Accelerated Repair
Boston	Curley K-8 School	OPM Selection	Accelerated Repair
Boston	David A Ellis	OPM Selection	Accelerated Repair
Boston	Donald Mckay	OPM Selection	Accelerated Repair
Boston	Grover Cleveland	OPM Selection	Accelerated Repair
Boston	Young Achievers	OPM Selection	Accelerated Repair
Cambridge	Fletcher/Maynard Academy	OPM Selection	Accelerated Repair
Cambridge	Kennedy-Longfellow	OPM Selection	Accelerated Repair
Chicopee	Belcher	OPM Selection	Accelerated Repair
Chicopee	Fairview Middle	OPM Selection	Accelerated Repair
Deerfield	Deerfield Elem	OPM Selection	Accelerated Repair
Fairhaven	Hastings Middle	OPM Selection	Accelerated Repair
Greenfield	Federal	OPM Selection	Accelerated Repair
Leicester	Leicester High	OPM Selection	Accelerated Repair
Leominster	Johnny Appleseed	OPM Selection	Accelerated Repair
Ludlow	East Street Elementary School	OPM Selection	Accelerated Repair
Middleborough	Memorial Early Childhood Center	OPM Selection	Accelerated Repair
New Bedford	Alfred J Gomes	OPM Selection	Accelerated Repair
New Bedford	Casmir Pulaski	OPM Selection	Accelerated Repair
New Bedford	Hayden/McFadden	OPM Selection	Accelerated Repair
New Bedford	John Avery Parker	OPM Selection	Accelerated Repair
New Bedford	Sgt Wm H Carney Acad	OPM Selection	Accelerated Repair
North Reading	E Ethel Little School	OPM Selection	Accelerated Repair
Peabody	Peabody Veterans Memorial High	OPM Selection	Accelerated Repair
Quincy	Beechwood Knoll Elem	OPM Selection	Accelerated Repair
Quincy	Merrymount	OPM Selection	Accelerated Repair
Revere	Garfield Elementary School	OPM Selection	Accelerated Repair
Springfield	STEM Middle Academy	OPM Selection	Accelerated Repair
Springfield	Daniel B Brunton	OPM Selection	Accelerated Repair
Springfield	Mary M Walsh	OPM Selection	Accelerated Repair
Springfield	Springfield Public Day High School	OPM Selection	Accelerated Repair
Stoughton	West Elementary	OPM Selection	Accelerated Repair
Taunton	Edmund Hatch Bennett	OPM Selection	Accelerated Repair
Taunton	Joseph H Martin	OPM Selection	Accelerated Repair
Wareham	John W. Decas Elementary School	OPM Selection	Accelerated Repair
Watertown	Watertown Middle	OPM Selection	Accelerated Repair
West Bridgewater	Spring Street School	OPM Selection	Accelerated Repair
Worcester	Flagg Street	OPM Selection	Accelerated Repair
Worcester	Francis J McGrath Elem	OPM Selection	Accelerated Repair
Worcester	Grafton Street	OPM Selection	Accelerated Repair
Worcester	Jacob Hiatt Magnet	OPM Selection	Accelerated Repair
Wrentham	Delaney	OPM Selection	Accelerated Repair
Boston	Boston Arts Academy	OPM Selection	Core Program
Cape Cod Region Voc Tech	Cape Cod Region Voc Tech	OPM Selection	Core Program
Easthampton	Maple	OPM Selection	Core Program
Holyoke	Lt Elmer J McMahon Elem	OPM Selection	Core Program
Lynn	Pickering Middle	OPM Selection	Core Program
Saugus	Saugus High	OPM Selection	Core Program
Taunton	Mulcahey Elementary School	OPM Selection	Core Program
Waltham	Waltham High School	OPM Selection	Core Program
Westport	Westport Middle	OPM Selection	Core Program
Worcester	South High Community	OPM Selection	Core Program

## Designer Selection

Ipswich	Winthrop	Designer Selection	Core Program
Millis	Clyde F Brown	Designer Selection	Core Program

**Feasibility Study**

Amherst	Wildwood Elementary	Feasibility Study	Core Program
Boston	Quincy Upper School	Feasibility Study	Core Program
Bourne	James F Peebles Elem	Feasibility Study	Core Program
Braintree	East Middle School	Feasibility Study	Core Program
Hanover	Sylvester	Feasibility Study	Core Program
Needham	Hillside Elementary	Feasibility Study	Core Program
Quincy	Reay E Sterling Middle	Feasibility Study	Core Program
Somerville	Somerville High	Feasibility Study	Core Program
Stoughton	Stoughton High	Feasibility Study	Core Program

**Schematic Design**

Billerica	Billerica Memorial High School	Schematic Design	Core Program
Carver	Carver Elementary School	Schematic Design	Core Program
Dedham	Early Childhood Center	Schematic Design	Core Program
Granby	West St	Schematic Design	Core Program
Minuteman Voc Tech	Minuteman Regional High	Schematic Design	Core Program
Mount Greylock	Mt Greylock Reg High	Schematic Design	Core Program
Narragansett	Templeton Center	Schematic Design	Core Program
Newton	Cabot	Schematic Design	Core Program

**Approved Project Vote Pending**

Holyoke	E N White Elem	Approved Project Vote Pending	Accelerated Repair
Holyoke	Morgan Elem	Approved Project Vote Pending	Accelerated Repair
Hopkinton	Center	Approved Project Vote Pending	Core Program
Provincetown	Provincetown High	Approved Project Vote Pending	Core Program
Woburn	Wyman	Approved Project Vote Pending	Core Program

**Design Development**

Bellingham	South Elem	Design Development	Accelerated Repair
Brockton	Barrett Russell School	Design Development	Accelerated Repair
Falmouth	Lawrence	Design Development	Accelerated Repair
Franklin County	Franklin County Tech	Design Development	Accelerated Repair
Gill-Montague	Sheffield Elementary	Design Development	Accelerated Repair
Hudson	Mulready Elementary	Design Development	Accelerated Repair
Medfield	Ralph Wheelock School	Design Development	Accelerated Repair
Melrose	Herbert Clark Hoover	Design Development	Accelerated Repair
Orleans	Orleans Elementary	Design Development	Accelerated Repair
Randolph	J F Kennedy Elem	Design Development	Accelerated Repair
Randolph	Randolph High	Design Development	Accelerated Repair
Springfield	John F Kennedy Middle	Design Development	Accelerated Repair
Wayland	Claypit Hill School	Design Development	Accelerated Repair
New Bedford	Taylor School at the Sea Lab Marine Science Education Center	Design Development	Waitlist
Abington	Frolio Jr Hs	Design Development	Core Program
Beverly	Briscoe Middle	Design Development	Core Program
Brookline	Edward Devotion	Design Development	Core Program
New Bedford	John Hannigan	Design Development	Core Program
Pittsfield	Taconic High	Design Development	Core Program
Scituate	Gates Intermediate School	Design Development	Core Program
Westborough	Sarah W Gibbons Middle	Design Development	Core Program

**Construction Completion 2017 +**

Auburn	Auburn Middle	Construction Completion 2017 +	Accelerated Repair
Auburn	Bryn Mawr	Construction Completion 2017 +	Accelerated Repair
Brockton	Ashfield Middle School	Construction Completion 2017 +	Accelerated Repair
Brockton	Brookfield	Construction Completion 2017 +	Accelerated Repair
Brockton	Gilmore	Construction Completion 2017 +	Accelerated Repair
Dartmouth	George H Potter	Construction Completion 2017 +	Accelerated Repair
Gardner	Elm Street School	Construction Completion 2017 +	Accelerated Repair
Greenfield	Green River	Construction Completion 2017 +	Accelerated Repair
Leominster	Northwest	Construction Completion 2017 +	Accelerated Repair
Lynn	E J Harrington	Construction Completion 2017 +	Accelerated Repair
Lynn	Wm P Connery	Construction Completion 2017 +	Accelerated Repair

Medway	John D Mc Govern Elem	Construction Completion 2017 +	Accelerated Repair
Middleton	Fuller Meadow	Construction Completion 2017 +	Accelerated Repair
North Attleborough	Roosevelt Avenue	Construction Completion 2017 +	Accelerated Repair
Northampton	Leeds	Construction Completion 2017 +	Accelerated Repair
Northampton	R. K. Finn Ryan Road	Construction Completion 2017 +	Accelerated Repair
Peabody	John E. McCarthy	Construction Completion 2017 +	Accelerated Repair
South Shore Reg Voc Tech	So Shore Voc Tech High	Construction Completion 2017 +	Accelerated Repair
Southern Berkshire	Mt Everett Regional	Construction Completion 2017 +	Accelerated Repair
Springfield	Kensington Avenue	Construction Completion 2017 +	Accelerated Repair
Stoughton	Joseph H Gibbons	Construction Completion 2017 +	Accelerated Repair
Tri County	Tri County Reg Voc Tech	Construction Completion 2017 +	Accelerated Repair
Tyngsborough	Tyngsborough High School	Construction Completion 2017 +	Accelerated Repair
Wellesley	Wellesley Middle	Construction Completion 2017 +	Accelerated Repair
Westford	Col John Robinson	Construction Completion 2017 +	Accelerated Repair
Westford	Day Elementary	Construction Completion 2017 +	Accelerated Repair
Worcester	Clark St Community	Construction Completion 2017 +	Accelerated Repair
Worcester	Goddard Sch/Science Tech	Construction Completion 2017 +	Accelerated Repair
Worcester	Union Hill School	Construction Completion 2017 +	Accelerated Repair
Worcester	West Tatnuck	Construction Completion 2017 +	Accelerated Repair
Boston	Dearborn	Construction Completion 2017 +	Core Program
Chelsea	Clark Avenue School	Construction Completion 2017 +	Core Program
Holbrook	Holbrook Jr Sr High	Construction Completion 2017 +	Core Program
North Middlesex	North Middlesex Reg	Construction Completion 2017 +	Core Program
Plymouth	Plymouth South High	Construction Completion 2017 +	Core Program
Winchester	Winchester High School	Construction Completion 2017 +	Core Program
Worcester	Nelson Place	Construction Completion 2017 +	Core Program

**Construction Completion 2016**

Athol-Royalston	Riverbend	Construction Completion 2016	Core Program
Gloucester	West Parish	Construction Completion 2016	Core Program
Haverhill	Caleb Dustin Hunking	Construction Completion 2016	Core Program
Lunenburg	Lunenburg High	Construction Completion 2016	Core Program
Lynn	Thurgood Marshall Mid	Construction Completion 2016	Core Program
Milford	Woodland	Construction Completion 2016	Core Program
Northborough	Lincoln Street	Construction Completion 2016	Core Program
Peabody	J Henry Higgins Middle	Construction Completion 2016	Core Program
Wachusett	Mountview Middle	Construction Completion 2016	Core Program
Westfield	Abner Gibbs	Construction Completion 2016	Core Program
Winthrop	Winthrop Sr High	Construction Completion 2016	Core Program

**Construction Completion 2015**

Quincy	Francis W Parker	Construction Completion 2015	Accelerated Repair
Quincy	Lincoln-Hancock Comm Sch	Construction Completion 2015	Accelerated Repair
Quincy	Merrymount	Construction Completion 2015	Accelerated Repair
Quincy	North Quincy High	Construction Completion 2015	Accelerated Repair
Quincy	Wollaston School	Construction Completion 2015	Accelerated Repair
Georgetown	Georgetown Middle/High	Construction Completion 2015	Core Program
Greenfield	Greenfield High	Construction Completion 2015	Core Program
Newton	A E Angier	Construction Completion 2015	Core Program
North Adams	Silvio O Conte Middle	Construction Completion 2015	Core Program
South Hadley	Plains Elementary	Construction Completion 2015	Core Program

**Building Complete**

Blackstone-Millville	Millville Elem	Building Complete	Accelerated Repair
Dighton-Rehoboth	Dighton Elementary	Building Complete	Accelerated Repair
Dighton-Rehoboth	Dighton Middle School	Building Complete	Accelerated Repair
Dighton-Rehoboth	Dorothy L Beckwith	Building Complete	Accelerated Repair
Hamilton-Wenham	Winthrop School	Building Complete	Accelerated Repair
Medford	Medford High	Building Complete	Accelerated Repair
Norwood	Cornelius M Callahan	Building Complete	Accelerated Repair
Pathfinder Voc Tech	Pathfinder Voc Tech	Building Complete	Accelerated Repair
Sudbury	General John Nixon Elem	Building Complete	Accelerated Repair
Worcester	Columbus Park	Building Complete	Accelerated Repair
Worcester	Tatnuck	Building Complete	Accelerated Repair

Worcester	Worcester Arts Magnet Sch	Building Complete	Accelerated Repair
Worcester	Worcester East Middle	Building Complete	Accelerated Repair
Salem	Collins Middle	Building Complete	Green Repair
Holyoke	Wm J Dean Voc Tech High	Building Complete	Science Lab Initiative
Medford	Medford High	Building Complete	Science Lab Initiative
New Bedford	New Bedford High	Building Complete	Waitlist
Assabet Valley	Assabet Valley Voc H S	Building Complete	Core Program
Auburn	Auburn Middle	Building Complete	Core Program
Ayer-Shirley	Ayer-Shirley Regional Middle/High School	Building Complete	Core Program
Berlin-Boylston	Tahanto Reg High	Building Complete	Core Program
Chicopee	Chicopee Academy	Building Complete	Core Program
Concord-Carlisle	Concord Carlisle High	Building Complete	Core Program
Dracut	Dracut Senior High	Building Complete	Core Program
Duxbury	Duxbury High	Building Complete	Core Program
East Bridgewater	East Bridgewater High	Building Complete	Core Program
Essex Agr Tech	Essex Agr and Tech Inst	Building Complete	Core Program
Franklin	Franklin High	Building Complete	Core Program
Georgetown	Penn Brook	Building Complete	Core Program
Greater Lawrence RVT	Gr Lawrence Reg Voc Tech	Building Complete	Core Program
Greater Lowell Voc Tec	Gr Lowell Reg Voc Tech	Building Complete	Core Program
Greater New Bedford	Gr New Bedford Voc Tech	Building Complete	Core Program
Hingham	Hingham Middle School	Building Complete	Core Program
Marshfield	Marshfield High	Building Complete	Core Program
Monomoy	Monomoy Regional High School	Building Complete	Core Program
Newburyport	Francis T Bresnahan Elem	Building Complete	Core Program
Newburyport	Rupert A Nock Middle	Building Complete	Core Program
North Reading	North Reading High	Building Complete	Core Program
Norton	Norton High	Building Complete	Core Program
Revere	Staff Sergeant James J. Hill School	Building Complete	Core Program
Somerset-Berkley	Somerset-Berkley High	Building Complete	Core Program
Southern Worcester Cty VT	Bay Path Reg Voc Tech H S	Building Complete	Core Program
Southwick-Tolland	Powder Mill	Building Complete	Core Program
Southwick-Tolland	Southwick-Tolland Regional High	Building Complete	Core Program
Southwick-Tolland	Woodland Elementary	Building Complete	Core Program
Springfield	Elias Brookings	Building Complete	Core Program
Sutton	Sutton Middle School	Building Complete	Core Program
Webster	Park Avenue Elementary	Building Complete	Core Program
West Bridgewater	West Bridgewater Jr-Sr	Building Complete	Core Program
West Springfield	West Springfield High	Building Complete	Core Program
Weston	Field Elem School	Building Complete	Core Program
Williamsburg	Anne T Dunphy	Building Complete	Core Program
Wilmington	Wilmington High	Building Complete	Core Program

**Closeout**

Ashland	Ashland Middle	Closeout	Accelerated Repair
Ashland	Henry E Warren Elem	Closeout	Accelerated Repair
Barnstable	Barnstable United Elementary School	Closeout	Accelerated Repair
Blackstone-Millville	Blackstone Millville RHS	Closeout	Accelerated Repair
Bridgewater-Raynham	Bridgewater Middle School	Closeout	Accelerated Repair
Bridgewater-Raynham	Laliberte Elementary School	Closeout	Accelerated Repair
Bridgewater-Raynham	Merrill Elementary School	Closeout	Accelerated Repair
Canton	Lt Peter M Hansen	Closeout	Accelerated Repair
Canton	Wm H Galvin Middle	Closeout	Accelerated Repair
Easton	Moreau Hall	Closeout	Accelerated Repair
Gardner	Gardner Middle School	Closeout	Accelerated Repair
Hatfield	Smith Academy	Closeout	Accelerated Repair
Nashoba Valley Tech	Nashoba Valley Tech H S	Closeout	Accelerated Repair
Pembroke	Hobomock Elementary	Closeout	Accelerated Repair
Pembroke	North Pembroke Elem	Closeout	Accelerated Repair
Pembroke	Pembroke Community Middle School	Closeout	Accelerated Repair
Pembroke	Pembroke High School	Closeout	Accelerated Repair
Randolph	Randolph Community Middle	Closeout	Accelerated Repair
Randolph	Randolph High	Closeout	Accelerated Repair
Shawsheen Valley Voc Tech	Shawsheen Valley Voc Tech High School	Closeout	Accelerated Repair

Springfield	Chestnut Accelerated Middle School	Closeout	Accelerated Repair
Springfield	High School/Science-Tech	Closeout	Accelerated Repair
Springfield	Margaret C Ells	Closeout	Accelerated Repair
Springfield	South End Middle School	Closeout	Accelerated Repair
Springfield	Springfield Public Day High School	Closeout	Accelerated Repair
Stoughton	Helen Hansen Elementary	Closeout	Accelerated Repair
Stoughton	Joseph R Dawe Jr Elem	Closeout	Accelerated Repair
Stoughton	West Elementary	Closeout	Accelerated Repair
Wareham	Wareham Senior High	Closeout	Accelerated Repair
Wellfleet	Wellfleet Elementary	Closeout	Accelerated Repair
Wilmington	North Intermediate	Closeout	Accelerated Repair
Worcester	Chandler Magnet	Closeout	Accelerated Repair
Worcester	Dr. James Caradonio Center	Closeout	Accelerated Repair
Worcester	Jacob Hiatt Magnet	Closeout	Accelerated Repair
Worcester	Lake View	Closeout	Accelerated Repair
Worcester	May Street	Closeout	Accelerated Repair
Barnstable	West Barnstable Elem	Closeout	Green Repair
Douglas	Douglas Intermediate School	Closeout	Green Repair
Haverhill	Consentino	Closeout	Green Repair
Haverhill	John G Whittier	Closeout	Green Repair
Haverhill	Tilton	Closeout	Green Repair
Haverhill	Walnut Square	Closeout	Green Repair
Salem	Saltonstall School	Closeout	Green Repair
West Boylston	Major Edwards Elementary	Closeout	Green Repair
Gardner	Gardner High	Closeout	Science Lab Initiative
Melrose	Melrose High	Closeout	Science Lab Initiative
Springfield	Springfield Central High	Closeout	Science Lab Initiative
Springfield	Forest Park Middle	Closeout	Waitlist
Andover	Bancroft Elementary	Closeout	Core Program
Belmont	Roger Wellington	Closeout	Core Program
Beverly	Beverly High	Closeout	Core Program
Danvers	Danvers High	Closeout	Core Program
Douglas	Douglas Elementary	Closeout	Core Program
Fall River	Morton Middle	Closeout	Core Program
Hudson	John F Kennedy	Closeout	Core Program
Lexington	Joseph Estabrook	Closeout	Core Program
Longmeadow	Longmeadow High	Closeout	Core Program
Marblehead	Glover	Closeout	Core Program
Methuen	Methuen High	Closeout	Core Program
Nashoba	Pompositicut	Closeout	Core Program
Norfolk	Freeman-Kennedy Elementary	Closeout	Core Program
Norfolk County Agriculture	Norfolk County Agr	Closeout	Core Program
Oxford	Oxford Middle	Closeout	Core Program
Quincy	Central Middle	Closeout	Core Program
Rockland	John W Rogers Middle	Closeout	Core Program
Saugus	Belmonte Saugus Middle	Closeout	Core Program
Shrewsbury	Sherwood Middle School	Closeout	Core Program
Somerville	E Somerville Community	Closeout	Core Program
Springfield	Dryden Memorial	Closeout	Core Program
Stoneham	Stoneham Middle School	Closeout	Core Program
Swampscott	Hadley	Closeout	Core Program
Tewksbury	Tewksbury Memorial High	Closeout	Core Program
Wakefield	Galvin Middle School	Closeout	Core Program
Wellesley	Wellesley Sr High	Closeout	Core Program

**Final Audit Approved**

Hamilton-Wenham	Bessie Buker Elementary	Final Audit Approved	Accelerated Repair
Hopedale	Memorial	Final Audit Approved	Accelerated Repair
Lynn	Breed Middle School	Final Audit Approved	Accelerated Repair
Lynn	Lynn Voc Tech Institute	Final Audit Approved	Accelerated Repair
Nauset	Nauset Reg Middle	Final Audit Approved	Accelerated Repair
Pentucket	Pentucket Reg Middle	Final Audit Approved	Accelerated Repair
So Middlesex Voc Tech Reg	Joseph P Keefe Tech HS	Final Audit Approved	Accelerated Repair
Walpole	Fisher	Final Audit Approved	Accelerated Repair
Westhampton	Westhampton Elem School	Final Audit Approved	Accelerated Repair
Leverett	Leverett Elementary	Final Audit Approved	Green Repair

Peabody	John E Burke	Final Audit Approved	Green Repair
Peabody	William A Welch Sr	Final Audit Approved	Green Repair
Maynard	Maynard High	Final Audit Approved	Core Program
Sturbridge	Burgess Elementary	Final Audit Approved	Core Program
Uxbridge	Uxbridge High	Final Audit Approved	Core Program

Date of Report: 10/28/2015

Total Projects: 306

MSBA ID	District	School	Project Phase	Project Type	Project Scope	Procurement Type	OPM	Designer	CM/GC	Commissioning Consultant
200800010405	Abington	Frolio Middle School	Design Development	Core Program	New Construction	DBB	Knight, Bagge & Anderson Inc.	Ai3 Architects LLC	-	Horizon Engineering Associates, LLP
201300080050	Amherst	Wildwood Elementary	Feasibility Study	Core Program			Joslin, Lesser + Associates Inc.	JCJ Architecture, PC	-	-
200800090003	Andover	Bancroft Elementary School	Closeout	Core Program	New Construction	CM@R	Dore & Whittier Management Partners, Inc.	Symmes Maini & McKee Associates, Inc.	Skanska USA Building, Inc.	Sebesta Blomberg & Associates, Inc.
201300140405	Ashland	Ashland Middle	Closeout	Accelerated Repair	Roof	DBB	Arcadis U.S., Inc.	Raymond Design Associates, Inc.	Gibson Roofs, Inc.	Gale Associates, Inc.
201300140010	Ashland	Henry E Warren Elem	Closeout	Accelerated Repair	Roof	DBB	Arcadis U.S., Inc.	Raymond Design Associates, Inc.	MDM Engineering	Gale Associates, Inc.
200908010605	Assabet Valley	Assabet Valley Regional Technical High School	Building Complete	Core Program	Repair	DBB	Strategic Building Solutions, LLC	Design Partnership of Cambridge, Inc.	CTA Construction Co., Inc.	Symmes, Maini & McKee Associates
200906150020	Athol-Royalston	Riverbend School	Construction	Core Program	New Construction	DBB	Symmes Maini & McKee Associates	Mount Vernon Group Architects, Inc.	Fontaine Brothers, Inc.	Strategic Building Solutions, LLC
201400160505	Attleboro	Attleboro High	Eligibility Period	Core Program			-	-	-	-
200800170305	Auburn	Auburn Middle	Building Complete	Core Program	New Construction	CM@R	Skanska USA Building, Inc	Lamoureux Pagano & Associates, Inc.	Fontaine Brothers, Inc.	WSP USA
201400170305	Auburn	Auburn Middle	Construction	Accelerated Repair	Roof, Boiler		Skanska USA Building, Inc	Dietz & Company Architects, Inc.	-	Horizon Engineering Associates, LLP   Thompson & Lichtner Co., Inc.
201400170010	Auburn	Bryn Mawr	Construction	Accelerated Repair	Roof		Skanska USA Building, Inc	Dietz & Company Architects, Inc.	-	Thompson & Lichtner Co., Inc.
200806160505	Ayer-Shirley	Ayer-Shirley Regional Middle/High School	Building Complete	Core Program	Addition / Renovation	CM@R	Dore and Whittier Architects, Inc.	Symmes Maini & McKee Associates, Inc.	Consigli Construction Company, Inc.	WSP USA
201300200010	Barnstable	Barnstable United Elementary School	Closeout	Accelerated Repair	Roof	DBB	exPERTcon, Inc.	Gale Associates, Inc.	Capeway Roofing Systems, Inc.	Russo Barr Associates, Inc.
201100200005G	Barnstable	West Barnstable Elem	Closeout	Green Repair	Windows / Doors	DBB	PMA Construction Services	-	Paul J. Rogan Co., Inc.	CBI Consulting Inc.
201400250020	Bellingham	South Elem	Design Development	Accelerated Repair	Roof		Atlantic Construction and Management, Inc.	-	-	Building Enclosure Associates, LLC
200800260035	Belmont	Roger Wellington Elementary School	Closeout	Core Program	New Construction	CM@R	PMA Construction Services	Jonathan Levi Architects LLC	Skanska USA Building, Inc.	Strategic Building Solutions, LLC
200806200505	Berlin-Boylston	Tahanto Regional High School	Building Complete	Core Program	New Construction	DBB	PMA Construction Services	HMFH Architects, Inc.	CTA Construction Co., Inc.	Strategic Building Solutions, LLC
200800300505	Beverly	Beverly High School	Closeout	Core Program	Addition / Renovation	DBB	HEERY	Mount Vernon Group Architects, Inc.	CTA Ventures	-
201300300305	Beverly	Briscoe Middle	Design Development	Core Program	New Construction		HEERY	Ai3 Architects LLC	-	Bard, Rao + Athanas Consulting Engineers, LLC
201300310505	Billerica	Billerica Memorial High School	Schematic Design	Core Program	New Construction		KV Associates, Inc.	Perkins+Will	-	-
201508050605	Blackstone Valley Reg	Blackstone Valley	OPM Selection	Accelerated Repair	Roof		-	-	-	-
201206220505	Blackstone-Millville	Blackstone Millville RHS	Closeout	Accelerated Repair	Roof	DBB	Arcadis U.S., Inc.	DiMarinisi & Wolfe Architects Urban Designers	-	Gale Associates, Inc.
201306220010	Blackstone-Millville	Millville Elem	Building Complete	Accelerated Repair	Roof	DBB	Pinck & Co., Inc.	CBI Consulting Inc.	MDM Engineering	Simpson Gumpertz & Heger Inc.
201500350651	Boston	Dorchester Academy	OPM Selection	Accelerated Repair	Windows / Doors		-	-	-	-
201300350546	Boston	Boston Arts Academy	OPM Selection	Core Program			-	-	-	-
201500350052	Boston	Charles Sumner	OPM Selection	Accelerated Repair	Windows / Doors		-	-	-	-
201500350020	Boston	Curley K-8 School	OPM Selection	Accelerated Repair	Windows / Doors		-	-	-	-
201500350072	Boston	David A Ellis	OPM Selection	Accelerated Repair	Windows / Doors		-	-	-	-



201500350080	Boston	Donald Mckay	OPM Selection	Accelerated Repair	Windows / Doors	-	-	-	-	-
201500350415	Boston	Grover Cleveland	OPM Selection	Accelerated Repair	Windows / Doors	-	-	-	-	-
201000350074	Boston	Henry Dearborn Middle School	Construction	Core Program	New Construction	CM@R	Daedalus Projects Inc	Jonathan Levi Architects LLC	Gilbane Building Company	Symmes, Maini & McKee Associates
201000350565	Boston	Quincy Upper School	Feasibility Study	Core Program			Skanska USA Building, Inc	HMFH Architects, Inc.	-	-
201500350380	Boston	Young Achievers	OPM Selection	Accelerated Repair	Windows / Doors					
201400360010	Bourne	James F Peebles Elem	Feasibility Study	Core Program			Symmes Maini & McKee Associates, Inc.	Flansburgh Associates, Inc.	-	-
201300400305	Braintree	East Middle School	Feasibility Study	Core Program			Hill International Company	Miller Dyer Spears Inc.	-	-
201206250320	Bridgewater-Raynham	Bridgewater Middle School	Closeout	Accelerated Repair	Roof	DBB	Vertex Construction Services	-	-	CBI Consulting Inc.
201206250050	Bridgewater-Raynham	Laliberte Elementary School	Closeout	Accelerated Repair	Roof	DBB	Vertex Construction Services	Raymond Design Associates, Inc.	-	CBI Consulting Inc.
201206250020	Bridgewater-Raynham	Merrill Elementary School	Closeout	Accelerated Repair	Roof	DBB	Vertex Construction Services	Raymond Design Associates, Inc.	-	CBI Consulting Inc.
201409100705	Bristol County Agr	Bristol County Agr High	Eligibility Period	Core Program			-	-	-	-
201400440421	Brockton	Ashfield Middle School	Construction	Accelerated Repair	Roof, Boiler		Architectural Consulting Group, LLC	Tighe & Bond, Inc.	-	Rist-Frost-Shumway Engineering, P.C.   Simpson Gumpertz & Heger Inc.
201400440080	Brockton	Barrett Russell School	Design Development	Accelerated Repair	Windows / Doors		Architectural Consulting Group, LLC	Tighe & Bond, Inc.	-	Simpson Gumpertz & Heger Inc.
201400440010	Brockton	Brookfield	Construction	Accelerated Repair	Roof		Architectural Consulting Group, LLC	Tighe & Bond, Inc.	-	Simpson Gumpertz & Heger Inc.
201400440035	Brockton	Gilmore	Construction	Accelerated Repair	Roof, Boiler		Architectural Consulting Group, LLC	Tighe & Bond, Inc.	-	Rist-Frost-Shumway Engineering, P.C.   Simpson Gumpertz & Heger Inc.
201100460015	Brookline	Edward Devotion	Design Development	Core Program	Addition / Renovation		Anthony Guigli Town Employee	HMFH Architects, Inc.	Shawmut Design and Construction	Consulting Engineering Services, LLC
201500490090	Cambridge	Fletcher/Maynard Academy	OPM Selection	Accelerated Repair	Boiler		-	-	-	-
201500490040	Cambridge	Kennedy-Longfellow	OPM Selection	Accelerated Repair	Roof		-	-	-	-
201200500012	Canton	Lt Peter M Hansen	Closeout	Accelerated Repair	Windows / Doors	DBB	Vertex Construction Services	CSS Architects Incorporated	Lockheed Window Corporations	Simpson Gumpertz & Heger Inc.
201200500305	Canton	Wm H Galvin Middle	Closeout	Accelerated Repair	Windows / Doors	DBB	Vertex Construction Services	CSS Architects Incorporated	Lockheed Window Corporations	Simpson Gumpertz & Heger Inc.
201408150605	Cape Cod Region Voc Tech	Cape Cod Region Voc Tech	OPM Selection	Core Program			-	-	-	-
201300520015	Carver	Carver Elementary School	Schematic Design	Core Program	New Construction		PMA Construction Services	HMFH Architects, Inc.	-	-
200800570050	Chelsea	Clark Avenue School	Construction	Core Program	New Construction	CM@R	Pinck & Co., Inc.	HMFH Architects, Inc.	W. T. Rich Company Inc.	Cannon Design
201500610010	Chicopee	Belcher	OPM Selection	Accelerated Repair	Roof		-	-	-	-
200900610021	Chicopee	Chicopee Academy	Building Complete	Core Program	Renovation	DBB	Arcadis U.S., Inc.	Caolo & Bieniek Associates, Inc.	Fontaine Brothers, Inc.	Symmes, Maini & McKee Associates
201500610310	Chicopee	Fairview Middle	OPM Selection	Accelerated Repair	Roof		-	-	-	-
201400630010	Clarksburg	Clarksburg Elementary	Eligibility Period	Core Program			-	-	-	-
200906400505	Concord-Carlisle	Concord-Carlisle Regional High School	Building Complete	Core Program	New Construction	CM@R	KV Associates, Inc.	OMR Architects, Inc.	Turner Construction Company	Strategic Building Solutions, LLC
200800710505	Danvers	Danvers High School	Closeout	Core Program	Addition / Renovation	DBB	Construction Monitoring Services, Inc.	DiNisco Design Partnership, Limited	Bacon Construction Co, Inc.	Turner Facilities Management Solutions
201400720030	Dartmouth	George H Potter	Construction	Accelerated Repair	Roof		Pinck & Co., Inc.	Russo Barr Associates, Inc.	Greenwood Industries, Inc.	Gale Associates, Inc.
201200730005	Dedham	Early Childhood Center	Schematic Design	Core Program	New Construction		Construction Monitoring Services, Inc.	Knight, Bagge & Anderson, Inc.	-	-
201500740015	Deerfield	Deerfield Elem	OPM Selection	Accelerated Repair	Roof		-	-	-	-

201306500005	Dighton-Rehoboth	Dighton Elementary	Building Complete	Accelerated Repair	Roof	DBB	Arcadis U.S., Inc.	Dietz & Company Architects, Inc.	MDM Engineering	Gale Associates, Inc.
201306500305	Dighton-Rehoboth	Dighton Middle School	Building Complete	Accelerated Repair	Roof	DBB	Arcadis U.S., Inc.	Dietz & Company Architects, Inc.	MDM Engineering	Gale Associates, Inc.
201306500310	Dighton-Rehoboth	Dorothy L Beckwith	Building Complete	Accelerated Repair	Roof	DBB	Arcadis U.S., Inc.	Dietz & Company Architects, Inc.	Greenwood Industries, Inc.	Gale Associates, Inc.
200800770010	Douglas	Douglas Elementary	Closeout	Core Program	New Construction - Model School	DBB	HEERY	DiNisco Design Partnership, Limited	CTA Construction Co., Inc.	Consulting Engineering Services, LLC
200800770100G	Douglas	Douglas Intermediate Elementary School	Closeout	Green Repair	Roof, Windows / Doors, Boiler	DBB	HEERY	DiNisco Design Partnership, Limited	CTA Construction Co., Inc.	Consulting Engineering Services, LLC
200800790505	Dracut	Dracut Senior High School	Building Complete	Core Program	Addition / Renovation	DBB	Hill International Company	Mount Vernon Group Architects, Inc.	CTA Construction Co., Inc.	RDk Engineers
201000820505	Duxbury	Duxbury High School	Building Complete	Core Program	New Construction - Model School	CM@R	KV Associates, Inc.	Mount Vernon Group Architects, Inc.	Dimeo Construction Company	WSP USA
200900830505	East Bridgewater	East Bridgewater High School	Building Complete	Core Program	New Construction - Model School	DBB	Hill International Company	Ai3 Architects LLC	Fontaine Brothers, Inc.	Foreman Building Commissioning, LP
201400860010	Easthampton	Maple	OPM Selection	Core Program			-	-	-	-
201300880020	Easton	Moreau Hall	Closeout	Accelerated Repair	Roof	DBB	Skanska USA Building, Inc	Baker/Wohl Architects, Inc.	Capeway Roofing Systems, Inc.	Gale Associates, Inc.
200809130705	Essex Agr Tech	Essex Agricultural and Technical High School	Building Complete	Core Program	New Construction	CM@R	PMA Construction Services	Design Partnership of Cambridge, Inc.	Gilbane Building Company	Turner Facilities Management Solutions
201400930028	Everett	George Keverian School	Eligibility Period	Core Program			-	-	-	-
201500940305	Fairhaven	Hastings Middle	OPM Selection	Accelerated Repair	Roof		-	-	-	-
201400950505	Fall River	B M C Durfee High	Eligibility Period	Core Program			-	-	-	-
200900950315	Fall River	James Madison Morton Middle School	Closeout	Core Program	New Construction	DBB	Maguire Group Inc.	Mount Vernon Group Architects, Inc.	J & J Contractors, Inc.	Sebesta Blomberg & Associates, Inc.
201400960405	Falmouth	Lawrence	Design Development	Accelerated Repair	Windows / Doors		PMA Construction Services	Civitects PC	-	Gale Associates, Inc.
200901010505	Franklin	Franklin High School	Building Complete	Core Program	New Construction - Model School	DBB	Daedalus Projects Inc	Ai3 Architects LLC	Bacon-Agostini Construction Joint Venture	Consulting Engineering Services, LLC
201408180605	Franklin County	Franklin County Tech	Design Development	Accelerated Repair	Windows / Doors		Strategic Building Solutions, LLC	Habeeb & Associates Architects, Inc.	-	CBI Consulting Inc.
201401030001	Gardner	Elm Street School	Construction	Accelerated Repair	Windows / Doors, Boiler		Hill International Company	ICON architecture, inc.	-	Fitzmeyer & Tocci Associates, Inc.   Thompson & Lichtner Co., Inc.
201201030505	Gardner	Gardner High	Closeout	Science Lab Initiative	Addition / Renovation	DBB	Pinck & Co., Inc.	Lamoureux Pagano & Associates, Inc.	Five Star Building Corp.	Fitzmeyer & Tocci Associates, Inc.
201201030405	Gardner	Gardner Middle School	Closeout	Accelerated Repair	Boiler		Leftfield, LLC	Richard D. Kimball Company, Inc.	Royal Steam Heater Co.	Fitzmeyer & Tocci Associates, Inc.
200801050505	Georgetown	Georgetown Middle/High School	Construction	Core Program	Renovation	DBB	Municipal Building Consultants, Inc.	Drumme Rosane Anderson, Inc.	L.D. Russo, Inc.	WSP USA
200901050010	Georgetown	Penn Brook Elementary School	Building Complete	Core Program	New Construction	DBB	Municipal Building Consultants, Inc.	Drumme Rosane Anderson, Inc.	Brait Builders Corp.	Rist-Frost-Shumway Engineering, P.C.
201406740050	Gill-Montague	Sheffield Elementary	Design Development	Accelerated Repair	Windows / Doors, Boiler		NETCO Construction Project Managers, Inc.	The S/L/A/M Collaborative	-	CBI Consulting Inc.
200901070050	Gloucester	West Parish Elementary School	Construction	Core Program	New Construction	CM@R	Knight, Bagge & Anderson Inc.	Dore & Whittier Architects, Inc.	W. T. Rich Company Inc.	Fitzmeyer & Tocci Associates, Inc.
201201110010	Granby	West St	Schematic Design	Core Program			Strategic Building Solutions, LLC	Jones Whitsett Architects, Inc.	-	-
201108230605	Greater Lawrence RVT	Gr Lawrence Reg Voc Tech	Building Complete	Core Program	Repair	DBB	Vertex Construction Services	Richard D. Kimball Company, Inc.	E. Amanti & Sons, Inc.	WSP USA
200908280605	Greater Lowell Voc Tec	Greater Lowell Regional Technical High School	Building Complete	Core Program	Addition / Renovation	CM@R	Joslin, Lesser + Associates Inc.	Knight, Bagge & Anderson, Inc.	Consigli Construction Company, Inc.	Horizon Engineering Associates, LLP
201008250605	Greater New Bedford	Greater New Bedford Vocational Technical High School	Building Complete	Core Program	Addition / Renovation	DBB	Construction Monitoring Services, Inc.	Drumme Rosane Anderson, Inc.	Agostini Construction Co., Inc.	Symmes, Maini & McKee Associates

201501140010	Greenfield	Federal	OPM Selection	Accelerated Repair	Roof, Windows / Doors, Boiler	-	-	-	-	
201401140030	Greenfield	Green River	Construction	Accelerated Repair	Roof, Windows / Doors, Boiler	Arcadis U.S., Inc.	Baker/Wohl Architects, Inc.	RAC Builders, Inc.	CBI Consulting Inc.	
200901140505	Greenfield	Greenfield High School	Construction	Core Program	New Construction	CM@R	Construction Monitoring Services, Inc.	Dore & Whittier Architects, Inc.	Shawmut Design and Construction	BVH Integrated Services, P.C.
201306750007	Hamilton-Wenham	Bessie Buker Elementary	Final Audit Approved	Accelerated Repair	Boiler	DBB	NETCO Construction Project Managers, Inc.	Habeeb & Associates Architects, Inc.	Multitemp Mechanical Corporation	Strategic Building Solutions, LLC
201306750015	Hamilton-Wenham	Winthrop School	Building Complete	Accelerated Repair	Windows / Doors, Boiler	DBB	NETCO Construction Project Managers, Inc.	Habeeb & Associates Architects, Inc.	E. Amanti & Sons, Inc.	CBI Consulting Inc.   Strategic Building Solutions, LLC
201301220015	Hanover	Sylvester	Feasibility Study	Core Program			P3 Inc.	Mount Vernon Group Architects, Inc.	-	-
201301270505	Hatfield	Smith Academy	Closeout	Accelerated Repair	Roof, Windows / Doors	DBB	Hill International Company	Civitects PC	Silktown Roofing	Building Enclosure Associates, LLC
201201280035	Haverhill	Caleb Dustin Hunking	Construction	Core Program	New Construction	CM@R	Joslin, Lesser + Associates Inc.	JCJ Architecture, PC	Shawmut Design and Construction	Strategic Building Solutions, LLC
201101280100G	Haverhill	Consentino	Closeout	Green Repair	Windows / Doors	DBB	Vertex Construction Services	CSS Architects Incorporated	New England Builders & Contractors, Inc.	RDK Engineers   Russo Barr Associates, Inc.
201101280085G	Haverhill	John G Whittier	Closeout	Green Repair	Windows / Doors	DBB	Vertex Construction Services	CSS Architects Incorporated	New England Builders & Contractors, Inc.	Russo Barr Associates, Inc.
201101280075G	Haverhill	Tilton	Closeout	Green Repair	Roof	DBB	Vertex Construction Services	CSS Architects Incorporated	Titan Roofing, Inc.	Russo Barr Associates, Inc.
201101280080G	Haverhill	Walnut Square	Closeout	Green Repair	Roof, Windows / Doors	DBB	Vertex Construction Services	CSS Architects Incorporated	Titan Roofing, Inc.	RDK Engineers   Russo Barr Associates, Inc.
201001310410	Hingham	Hingham Middle School	Building Complete	Core Program	New Construction - Model School	DBB	Knight, Bagge & Anderson Inc.	Ai3 Architects LLC	Brait Builders Corp.	Foreman Building Commissioning, LP
200801330505	Holbrook	Holbrook Junior-Senior High School	Construction Approved Project Vote Pending	Core Program	New Construction	CM@R	Symmes Maini & McKee Associates, Inc.	Flansburgh Associates, Inc.	Consigli Construction Company, Inc.	Consulting Engineering Services, LLC
201401370045	Holyoke	E N White Elem	Construction Approved Project Vote Pending	Accelerated Repair	Boiler		-	-	-	BVH Integrated Services, P.C.
201201370015	Holyoke	Lt Elmer J McMahon Elem	OPM Selection	Core Program			-	-	-	-
201401370025	Holyoke	Morgan Elem	Construction Approved Project Vote Pending	Accelerated Repair	Boiler		-	-	-	BVH Integrated Services, P.C.
201201370605	Holyoke	Wm J Dean Voc Tech High	Building Complete	Science Lab Initiative	Addition / Renovation	DBB	Skanska USA Building, Inc	Kaestle Boos Associates, Inc.	RAC Builders, Inc.	BVH Integrated Services, P.C.
201301380010	Hopedale	Memorial	Final Audit Approved	Accelerated Repair	Roof	DBB	Atlantic Construction and Management, Inc.	Civitects PC	MDM Engineering	Simpson Gumpertz & Heger Inc.
201301390005	Hopkinton	Center	Construction Approved Project Vote Pending	Core Program	New Construction		Compass Project Management, Inc.	Drumney Rosane Anderson, Inc.	-	-
200801410410	Hudson	John F. Kennedy Middle School	Closeout	Core Program	New Construction	DBB	PMA Construction Services	OMR Architects, Inc.	Bacon-Agostini Construction Joint Venture	WSP USA
201401410007	Hudson	Mulready Elementary	Design Development	Accelerated Repair	Roof		Atlantic Construction and Management, Inc.	-	-	CBI Consulting Inc.
201401440015	Ipswich	Winthrop	Designer Selection	Core Program			-	-	-	-
201501510505	Leicester	Leicester High	OPM Selection	Accelerated Repair	Roof		Hill International Company	Gale Associates, Inc.	-	-
201501530025	Leominster	Johnny Appleseed	OPM Selection	Accelerated Repair	Roof, Windows / Doors		-	-	-	-
201401530030	Leominster	Northwest	Construction	Accelerated Repair	Roof		Architectural Consulting Group, LLC	Gale Associates, Inc.	-	Building Enclosure Associates, LLC
201101540005G	Leverett	Leverett Elementary	Final Audit Approved	Green Repair	Roof, Windows / Doors	DBB	Potomac Capital Advisors	DiMarinisi & Wolfe Architects Urban Designers	-	Russo Barr Associates, Inc.
201101550010E	Lexington	Joseph Estabrook	Closeout	Core Program	New Construction	CM@R	Hill International Company	DiNisco Design Partnership, Limited	Shawmut Design and Construction	BVH Integrated Services, P.C.
200801590505	Longmeadow	Longmeadow High School	Closeout	Core Program	New Construction	CM@R	Joslin, Lesser + Associates Inc.	OMR Architects, Inc.	Gilbane Building Company	Foreman Building Commissioning, LP

201401600505	Lowell	Lowell High	Eligibility Period	Core Program			-	-	-	-
201501610010	Ludlow	East Street Elementary School	OPM Selection	Accelerated Repair	Roof, Boiler		-	-	-	-
201001620505	Lunenburg	Lunenburg High School	Construction	Core Program	New Construction	CM@R	Joslin, Lesser + Associates Inc.	Tappe Associates, Inc.	Shawmut Design and Construction	Cannon Design
201201630405	Lynn	Breed Middle School	Final Audit Approved	Accelerated Repair	Windows / Doors	DBB	Diversified Project Management	Kaestle Boos Associates, Inc.	GVW, Inc.	CBI Consulting Inc.
201401630045	Lynn	E J Harrington	Construction	Accelerated Repair	Roof		NETCO Construction Project Managers, Inc.	Habeeb & Associates Architects, Inc.	Capeway Roofing Systems, Inc.	CBI Consulting Inc.
201201630605	Lynn	Lynn Voc Tech Institute	Final Audit Approved	Accelerated Repair	Roof	DBB	Diversified Project Management	Kaestle Boos Associates, Inc.	Gibson Roofs, Inc.	CBI Consulting Inc.
201401630420	Lynn	Pickering Middle	OPM Selection	Core Program			-	-	-	-
200901630305	Lynn	Thurgood Marshall Middle School	Construction	Core Program	New Construction	CM@R	Joslin, Lesser + Associates Inc.	Raymond Design Associates, Inc.	Walsh Brothers, Inc.	Rist-Frost-Shumway Engineering, P.C.
201401630040	Lynn	Wm P Connery	Construction	Accelerated Repair	Roof		NETCO Construction Project Managers, Inc.	Habeeb & Associates Architects, Inc.	Gibson Roofs, Inc.	CBI Consulting Inc.
200801680020	Marblehead	Glover School	Closeout	Core Program	New Construction	DBB	Municipal Building Consultants, Inc.	JCJ Architecture, PC	G & R Construction, Inc.	RDK Engineers
201101710505	Marshfield	Marshfield High	Building Complete	Core Program	New Construction - Model School	DBB	Compass Project Management, Inc.	Ai3 Architects LLC	Brait Builders Ventures	Sebesta Blomberg & Associates, Inc.
200801740505	Maynard	Maynard High School	Final Audit Approved	Core Program	New Construction	DBB	Municipal Building Consultants, Inc.	Tappe Associates, Inc.	CTA Construction Co., Inc.	WSP USA
201401750007	Medfield	Ralph Wheelock School	Design Development	Accelerated Repair	Boiler		-	-	-	RDK Engineers
201201760505	Medford	Medford High	Building Complete	Science Lab Initiative	Addition / Renovation	DBB	Leftfield, LLC	DiNisco Design Partnership, Limited	G & R Construction, Inc.	Cannon Design
201301760505	Medford	Medford High	Building Complete	Accelerated Repair	Windows / Doors, Boiler	DBB	Architectural Consulting Group, LLC	Dietz & Company Architects, Inc.	NB Kenney Company, Inc	Symmes, Maini & McKee Associates
201401770013	Medway	John D Mc Govern Elem	Construction	Accelerated Repair	Windows / Doors		Arcadis U.S., Inc.	CBI Consulting Inc.	-	Russo Barr Associates, Inc.
201401780017	Melrose	Herbert Clark Hoover	Design Development	Accelerated Repair	Windows / Doors		Strategic Building Solutions, LLC	ICON architecture, inc.	-	Simpson Gumpertz & Heger Inc.
201201780505	Melrose	Melrose High	Closeout	Science Lab Initiative	Addition / Renovation	DBB	Hill International Company	Ai3 Architects LLC	G & R Construction, Inc.	WSP USA
200801810505	Methuen	Methuen High School	Closeout	Core Program	Addition / Renovation	CM@R	KBA/Trident	Finegold Alexander and Associates Inc.	Consigli Construction Company, Inc.	Environmental Health and Engineering
201501820011	Middleborough	Memorial Early Childhood Center	OPM Selection	Accelerated Repair	Roof		-	-	-	-
201401820505	Middleborough	Middleborough High	Eligibility Period	Core Program			-	-	-	-
201401840003	Middleton	Fuller Meadow	Construction	Accelerated Repair	Roof		Hill International Company	CBI Consulting Inc.	-	Building Enclosure Associates, LLC
201101850090	Milford	Woodland	Construction	Core Program	New Construction	CM@R	Joslin, Lesser + Associates Inc.	HMFH Architects, Inc.	Shawmut Design and Construction	Consulting Engineering Services, LLC
201401870005	Millis	Clyde F Brown	Designer Selection	Core Program			Compass Project Management, Inc.	-	-	-
200908300605	Minuteman Voc Tech	Minuteman Regional High School	Schematic Design	Core Program			Skanska USA Building, Inc	Kaestle Boos Associates, Inc.	-	-
201107129999	Monomoy	Monomoy Regional High School	Building Complete	Core Program	New Construction - Model School	DBB	Skanska USA Building, Inc	Mount Vernon Group Architects, Inc.	Fontaine Brothers, Inc.	Sebesta Blomberg & Associates, Inc.
201307150505	Mount Greylock	Mt Greylock Reg High	Schematic Design	Core Program	Addition / Renovation		Dore & Whittier Management Partners, Inc.	Design Partnership of Cambridge, Inc.	-	-
200807200020	Narragansett	Templeton Center School	Schematic Design	Core Program			Strategic Building Solutions, LLC	Symmes Maini & McKee Associates, Inc.	-	-
200807250015	Nashoba	Pompositticut Elementary School	Closeout	Core Program	Addition / Renovation	DBB	Construction Monitoring Services, Inc.	Symmes Maini & McKee Associates, Inc.	P.J. Stella Construction Corp.	Strategic Building Solutions, LLC
201308520605	Nashoba Valley Tech	Nashoba Valley Tech H S	Closeout	Accelerated Repair	Roof	DBB	STV Incorporated	CGKV Architects, Inc.	Stanley Roofing Company, Inc.	CBI Consulting Inc.
201306600305	Nauset	Nauset Reg Middle	Final Audit Approved	Accelerated Repair	Roof	DBB	Strategic Building Solutions, LLC	ICON architecture, inc.	Capeway Roofing Systems, Inc.	Russo Barr Associates, Inc.

201301990035	Needham	Hillside Elementary	Feasibility Study	Core Program			Steven H. Popper Town Employee	Dore & Whittier Architects, Inc.	-	-	
201502010063	New Bedford	Alfred J Gomes	OPM Selection	Accelerated Repair	Windows / Doors		-	-	-	-	
201502010123	New Bedford	Casmir Pulaski	OPM Selection	Accelerated Repair	Windows / Doors, Boiler		-	-	-	-	
201502010078	New Bedford	Hayden/McFadden	OPM Selection	Accelerated Repair	Windows / Doors, Boiler		-	-	-	-	
201502010115	New Bedford	John Avery Parker	OPM Selection	Accelerated Repair	Windows / Doors, Boiler		-	-	-	-	
200902010070	New Bedford	John Hannigan	Design Development	Core Program	New Construction		Daedalus Projects Inc	Turowski2 Architecture, Inc.	-	-	WSP USA
W201002010505P2	New Bedford	New Bedford High	Building Complete	Waitlist	Repair	DBB	Architectural Consulting Group, LLC	Mount Vernon Group Architects, Inc.	Sparks Company, Inc.	-	
201502010045	New Bedford	Sgt Wm H Carney Acad	OPM Selection	Accelerated Repair	Windows / Doors		-	-	-	-	
W201002019999	New Bedford	Taylor School at the Sea Lab Marine Science Education Center	Design Development	Waitlist			Architectural Consulting Group, LLC	Mount Vernon Group Architects, Inc.	-	-	WSP USA
201102040005	Newburyport	Francis T Bresnahan Elem	Building Complete	Core Program	New Construction - Model School	DBB	HEERY	HMFH Architects, Inc.	CTA Construction Co., Inc.	-	Fitzmeyer & Tocci Associates, Inc.
201002040305	Newburyport	Rupert A. Nock Middle School	Building Complete	Core Program	Addition / Renovation	CM@R	HEERY	Miller Dyer Spears Inc.	Gilbane Building Company	-	Fitzmeyer & Tocci Associates, Inc.
201102070005	Newton	A E Angier	Construction	Core Program	New Construction	CM@R	Joslin, Lesser + Associates Inc.	DiNisco Design Partnership, Limited	W. T. Rich Company Inc.	-	Fitzmeyer & Tocci Associates, Inc.
201302070025	Newton	Cabot	Schematic Design	Core Program		CM@R	Joslin, Lesser + Associates Inc.	DiNisco Design Partnership, Limited	W. T. Rich Company Inc.	-	
200802080005	Norfolk	Freeman-Kennedy Elementary School	Closeout	Core Program	New Construction	DBB	Joslin, Lesser + Associates Inc.	Flansburgh Associates, Inc.	Fontaine Brothers, Inc.	-	WSP USA
200909150705	Norfolk County Agriculture	Norfolk County Agr	Closeout	Core Program	Addition / Renovation	DBB	Compass Project Management, Inc.	Turowski2 Architecture, Inc.	Brait Builders Corp.	-	Rist-Frost-Shumway Engineering, P.C.
200802090305	North Adams	Silvio O Conte Middle School	Construction	Core Program	Addition / Renovation	DBB	Strategic Building Solutions, LLC	Jones Whitsett Architects, Inc.	PDS Engineering and Construction, Inc.	-	Rist-Frost-Shumway Engineering, P.C.
201402120015	North Attleborough	Roosevelt Avenue	Construction	Accelerated Repair	Boiler		Pinck & Co., Inc.	Consulting Engineering Services, LLC	Falite Brothers Inc.	-	Bard, Rao + Athanas Consulting Engineers, LLC
201107350505	North Middlesex	North Middlesex Reg	Construction	Core Program	New Construction	DBB	HEERY	Symmes Maini & McKee Associates, Inc.	CTA Construction Co., Inc.	-	Horizon Engineering Associates, LLP
201502170003	North Reading	E Ethel Little School	OPM Selection	Accelerated Repair	Roof		Compass Project Management, Inc.	HAKS Engineers, P.C.	-	-	
201002170505	North Reading	North Reading High School	Building Complete	Core Program	Addition / Renovation	CM@R	PMA Construction Services	Dore & Whittier Architects, Inc.	Gilbane Building Company	-	Cannon Design
201402100025	Northampton	Leeds	Construction	Accelerated Repair	Roof		STV Incorporated	Raymond Design Associates, Inc.	R & H Roofing, LLP	-	Russo Barr Associates, Inc.
201402100029	Northampton	R. K. Finn Ryan Road	Construction	Accelerated Repair	Roof		STV Incorporated	Raymond Design Associates, Inc.	R & H Roofing, LLP	-	Russo Barr Associates, Inc.
201102130003	Northborough	Lincoln Street	Construction	Core Program	Addition / Renovation	DBB	Strategic Building Solutions, LLC	Lamoureux Pagano & Associates, Inc.	Brait Builders Corp.	-	Fitzmeyer & Tocci Associates, Inc.
200902180505	Norton	Norton High School	Building Complete	Core Program	Addition / Renovation	CM@R	Pinck & Co., Inc.	JCJ Architecture, PC	W. T. Rich Company Inc.	-	Rist-Frost-Shumway Engineering, P.C.
201402200010	Norwood	Cornelius M Callahan	Building Complete	Accelerated Repair	Boiler		PMA Construction Services	Consulting Engineering Services, LLC	George T. Wilkinson, Inc.	-	Symmes, Maini & McKee Associates
201402240005	Orleans	Orleans Elementary	Design Development	Accelerated Repair	Windows / Doors		Architectural Consulting Group, LLC	Tighe & Bond, Inc.	-	-	Gale Associates, Inc.
200802260405	Oxford	Oxford Middle School	Closeout	Core Program	Repair	DBB	Diversified Project Management	CGKV Architects, Inc.	J.J. Cardosi, Inc.	-	Cannon Design
201308600605	Pathfinder Voc Tech	Pathfinder Voc Tech	Building Complete	Accelerated Repair	Roof	DBB	exPERTcon, Inc.	Baker/Wohl Architects, Inc.	Allied Restoration Corporation	-	Building Enclosure Associates, LLC
200802290305	Peabody	Higgins Middle School	Construction	Core Program	New Construction	DBB	Daedalus Projects Inc	DiNisco Design Partnership, Limited	Bacon-Agostini Construction Joint Venture	-	BVH Integrated Services, P.C.
201102290007G	Peabody	John E Burke	Final Audit Approved	Green Repair	Roof, Windows / Doors, Boiler	DBB	Daedalus Projects Inc	LPBA/ Architects, Inc.	-	-	Sebesta Blomberg & Associates, Inc.

201402290016	Peabody	John E. McCarthy	Construction	Accelerated Repair	Roof, Windows / Doors		Hill International Company	Civitects PC	-		Thompson & Lichtner Co., Inc.
201502290510	Peabody	Peabody Veterans Memorial High	OPM Selection	Accelerated Repair	Roof		-	-	-		-
201102290027G	Peabody	William A Welch Sr	Final Audit Approved	Green Repair	Roof	DBB	Daedalus Projects Inc	LPBA/ Architects, Inc.	-		Sebesta Blomberg & Associates, Inc.
201302310010	Pembroke	Hobomock Elementary	Closeout	Accelerated Repair	Roof	DBB	Pinck & Co., Inc.	The S/L/A/M Collaborative		Greenwood Industries, Inc.	CBI Consulting Inc.
201302310015	Pembroke	North Pembroke Elem	Closeout	Accelerated Repair	Roof	DBB	Pinck & Co., Inc.	The S/L/A/M Collaborative		Paul J. Rogan Co., Inc.	CBI Consulting Inc.
201302310305	Pembroke	Pembroke Community Middle School	Closeout	Accelerated Repair	Roof	DBB	Pinck & Co., Inc.	The S/L/A/M Collaborative		Paul J. Rogan Co., Inc.	CBI Consulting Inc.
201302310505	Pembroke	Pembroke High School	Closeout	Accelerated Repair	Roof	DBB	Pinck & Co., Inc.	The S/L/A/M Collaborative		Greenwood Industries, Inc.	CBI Consulting Inc.
201307450405	Pentucket	Pentucket Reg Middle	Final Audit Approved	Accelerated Repair	Roof, Boiler	DBB	Arcadis U.S., Inc.	CGKV Architects, Inc.		Ambient Temperature Corporation	CBI Consulting Inc.   Strategic Building Solutions, LLC
201002360510	Pittsfield	Taconic High School	Design Development	Core Program	New Construction	CM@R	Skanska USA Building, Inc	Drumme Rosane Anderson, Inc.	-		Strategic Building Solutions, LLC
201202390515	Plymouth	Plymouth South High	Construction	Core Program	New Construction		Ted Gentry Associates, Inc	Ai3 Architects LLC		Bacon-Agostini Construction Joint Venture	Rist-Frost-Shumway Engineering, P.C.
201302420505	Provincetown	Provincetown High	Approved Project Vote Pending	Core Program	Repair		Atlantic Construction and Management, Inc.	Raymond Design Associates, Inc.	-		-
201502430020	Quincy	Beechwood Knoll Elem	OPM Selection	Accelerated Repair	Roof, Windows / Doors		-	-	-		-
200802430315	Quincy	Central Middle School	Closeout	Core Program	New Construction - Model School	DBB	Tishman Construction Corporation of MA	Ai3 Architects LLC		H.V. Collins Co., Inc.	Sebesta Blomberg & Associates, Inc.
201402430075	Quincy	Francis W Parker	Construction	Accelerated Repair	Windows / Doors		PMA Construction Services	Russo Barr Associates, Inc.		Lockheed Window Corporations	Simpson Gumpertz & Heger Inc.
201402430035	Quincy	Lincoln-Hancock Comm Sch	Construction	Accelerated Repair	Windows / Doors		PMA Construction Services	Russo Barr Associates, Inc.		Lockheed Window Corporations	Simpson Gumpertz & Heger Inc.
201302430060	Quincy	Merrymount	Construction	Accelerated Repair	Windows / Doors	DBB	Skanska USA Building, Inc	Habeeb & Associates Architects, Inc.		Alpha Contracting Associates, Inc.	Simpson Gumpertz & Heger Inc.
201502430060	Quincy	Merrymount	OPM Selection	Accelerated Repair	Roof		-	-	-		-
201302430510	Quincy	North Quincy High	Construction	Accelerated Repair	Windows / Doors	DBB	Skanska USA Building, Inc	Habeeb & Associates Architects, Inc.		GVW, Inc.	Simpson Gumpertz & Heger Inc.
201302430320	Quincy	Reay E Sterling Middle	Feasibility Study	Core Program			Joslin, Lesser + Associates Inc.	Ai3 Architects LLC	-		-
201302430110	Quincy	Wollaston School	Construction	Accelerated Repair	Windows / Doors	DBB	Skanska USA Building, Inc	Habeeb & Associates Architects, Inc.		Northeast Energy Control Systems	Simpson Gumpertz & Heger Inc.
201402440018	Randolph	J F Kennedy Elem	Design Development	Accelerated Repair	Windows / Doors		STV Incorporated	Taylor & Burns, Inc.	-		Gale Associates, Inc.
201302440410	Randolph	Randolph Community Middle	Closeout	Accelerated Repair	Boiler	DBB	NETCO Construction Project Managers, Inc.	Taylor & Burns, Inc.		AAlanco Service Corporation	Consulting Engineering Services, LLC
201302440505	Randolph	Randolph High	Closeout	Accelerated Repair	Roof	DBB	NETCO Construction Project Managers, Inc.	Taylor & Burns, Inc.		John F. Shea Company, Inc.	Gale Associates, Inc.
201402440505	Randolph	Randolph High	Design Development	Accelerated Repair	Windows / Doors		STV Incorporated	Taylor & Burns, Inc.	-		Gale Associates, Inc.
201502480056	Revere	Garfield Elementary School	OPM Selection	Accelerated Repair	Roof		-	-	-		-
201002480035	Revere	Staff Sergeant James J. Hill School	Building Complete	Core Program	New Construction	DBB	Hill International Company	Drumme Rosane Anderson, Inc.		CTA Construction Co., Inc.	Rist-Frost-Shumway Engineering, P.C.
200802510305	Rockland	John W. Rogers Middle School	Closeout	Core Program	New Construction	CM@R	Daedalus Projects Inc	Dore & Whittier Architects, Inc.		Agostini Construction Co., Inc.	Consulting Engineering Services, LLC
200902580305G	Salem	Collins Middle School	Building Complete	Green Repair	Roof, Windows / Doors, Boiler, Building Envelope	CM@R	KV Associates, Inc.	Reinhardt Associates, Inc.		Gilbane Building Company	Rist-Frost-Shumway Engineering, P.C.
201002580050G	Salem	Saltonstall School	Closeout	Green Repair	Roof, Windows / Doors, Boiler, Building Envelope	CM@R	KV Associates, Inc.	Reinhardt Associates, Inc.		Gilbane Building Company	Rist-Frost-Shumway Engineering, P.C.



201002620305	Saugus	Belmonte Middle School	Closeout	Core Program	Repair	CM@R	Skanska USA Building, Inc	Fletcher Thompson Architecture Engineering, LLC	Consigli Construction Company, Inc.	Consulting Engineering Services, LLC
201402620505	Saugus	Saugus High	OPM Selection	Core Program			-	-	-	-
201202640305	Scituate	Gates Intermediate School	Design Development	Core Program	New Construction		Daedalus Projects Inc	Dore & Whittier Architects, Inc.	-	WSP USA
201208710605	Shawshen Valley Voc Tech	Shawshen Valley Voc Tech High School	Closeout	Accelerated Repair	Boiler	DBB	Diversified Project Management	Shekar & Associates, Inc.	NB Kenney Company, Inc	Fitzmeyer & Tocci Associates, Inc.
200802710305	Shrewsbury	Sherwood Middle School	Closeout	Core Program	New Construction	CM@R	PMA Construction Services	Lamoureux Pagano & Associates, Inc.	Gilbane Building Company	RDK Engineers
201308290605	So Middlesex Voc Tech Reg	Joseph P Keefe Tech HS	Final Audit Approved	Accelerated Repair	Roof	DBB	PMA Construction Services	Raymond Design Associates, Inc.	Greenwood Industries, Inc.	Russo Barr Associates, Inc.
200811119999	Somerset-Berkley	Somerset-Berkley High	Building Complete	Core Program	New Construction - Model School	DBB	Skanska USA Building, Inc	Ai3 Architects LLC	Bacon-Agostini Construction Joint Venture	Horizon Engineering Associates, LLP
200902740111E	Somerville	East Somerville Community School at Cummings	Closeout	Core Program	Renovation	CM@R	PMA Construction Services	Maguire Group Inc.	Gilbane Building Company	Foreman Building Commissioning, LP
201302740505	Somerville	Somerville High	Feasibility Study	Core Program			PMA Construction Services	Symmes Maini & McKee Associates, Inc.	-	-
200902780015	South Hadley	Plains School	Construction	Core Program	New Construction	DBB	Arcadis U.S., Inc.	Jones Whitsett Architects, Inc.	Fontaine Brothers, Inc.	Strategic Building Solutions, LLC
201408730605	South Shore Reg Voc Tech	So Shore Voc Tech High	Construction	Accelerated Repair	Boiler		exPERTcon, Inc.	Richard D. Kimball Company, Inc.	-	Consulting Engineering Services, LLC
201407650505	Southern Berkshire	Mt Everett Regional School	Construction	Accelerated Repair	Roof, Boiler		NETCO Construction Project Managers, Inc.	Dietz & Company Architects, Inc.	Titan Roofing, Inc.	Strategic Building Solutions, LLC
200908760605	Southern Worcester Cty VT	Bay Path Regional Vocational Technical High School	Building Complete	Core Program	Addition / Renovation	CM@R	HEERY	Kaestle Boos Associates, Inc.	Consigli Construction Company, Inc.	RDK Engineers
201107660305	Southwick-Tolland	Powder Mill	Building Complete	Core Program	Repair	DBB	Strategic Building Solutions, LLC	JCJ Architecture, PC	PDS Engineering and Construction, Inc.	BVH Integrated Services, P.C.
201107660505	Southwick-Tolland	Southwick-Tolland Regional High	Building Complete	Core Program	Addition / Renovation	DBB	Strategic Building Solutions, LLC	JCJ Architecture, PC	Fontaine Brothers, Inc.	BVH Integrated Services, P.C.
200807660010	Southwick-Tolland	Woodland Elementary School	Building Complete	Core Program	Addition / Renovation	DBB	Strategic Building Solutions, LLC	JCJ Architecture, PC	PDS Engineering and Construction, Inc.	BVH Integrated Services, P.C.
201502810350	Springfield	STEM Middle Academy	OPM Selection	Accelerated Repair	Roof		-	-	-	-
201302810310	Springfield	Chestnut Accelerated Middle School	Closeout	Accelerated Repair	Roof	DBB	Atlantic Construction and Management, Inc.	CBI Consulting Inc.	J.D. Rivet & Co., Inc.	Building Enclosure Associates, LLC
201502810035	Springfield	Daniel B Brunton	OPM Selection	Accelerated Repair	Windows / Doors		-	-	-	-
201102810125E	Springfield	Dryden Memorial	Closeout	Core Program	Addition / Renovation	CM@R	Arcadis U.S., Inc.	Drumme Rosane Anderson, Inc.	Morganti/Aquadro & Cerruti	BVH Integrated Services, P.C.
201102810030E	Springfield	Elias Brookings	Building Complete	Core Program	New Construction	CM@R	Arcadis U.S., Inc.	Drumme Rosane Anderson, Inc.	Morganti/Aquadro & Cerruti	BVH Integrated Services, P.C.
W20014137	Springfield	Forest Park Middle School	Closeout	Waitlist	Addition / Renovation	CM@R	Arcadis U.S., Inc.	Perkins Eastman	Consigli Construction Company, Inc.	Foreman Building Commissioning, LP
201302810530	Springfield	High School/Science-Tech	Closeout	Accelerated Repair	Roof	DBB	Atlantic Construction and Management, Inc.	CBI Consulting Inc.	Kronenberger & Sons Restoration, Inc.	Building Enclosure Associates, LLC
201402810328	Springfield	John F Kennedy Middle	Design Development	Accelerated Repair	Windows / Doors		Arcadis U.S., Inc.	Gale Associates, Inc.	-	Building Enclosure Associates, LLC
201402810110	Springfield	Kensington Avenue	Construction	Accelerated Repair	Windows / Doors		Arcadis U.S., Inc.	Gale Associates, Inc.	Alpha Contracting Associates, Inc.	Building Enclosure Associates, LLC
201302810060	Springfield	Margaret C Ells	Closeout	Accelerated Repair	Roof	DBB	Atlantic Construction and Management, Inc.	CBI Consulting Inc.	Allied Restoration Corporation	Building Enclosure Associates, LLC
201502810155	Springfield	Mary M Walsh	OPM Selection	Accelerated Repair	Windows / Doors		-	-	-	-
201302810355	Springfield	South End Middle School	Closeout	Accelerated Repair	Roof	DBB	Atlantic Construction and Management, Inc.	CBI Consulting Inc.	Titan Roofing, Inc.	Building Enclosure Associates, LLC
201202810500	Springfield	Springfield Central High	Closeout	Science Lab Initiative	Addition / Renovation	CM@R	Leftfield, LLC	DiNisco Design Partnership, Limited	Morganti/Aquadro & Cerruti	Horizon Engineering Associates, LLP
201302810550	Springfield	Springfield Public Day High School	Closeout	Accelerated Repair	Roof	DBB	Atlantic Construction and Management, Inc.	CBI Consulting Inc.	-	Building Enclosure Associates, LLC

201502810550	Springfield	Springfield Public Day High School	OPM Selection	Accelerated Repair	Windows / Doors	-	-	-	-	-
200902840405	Stoneham	Stoneham Middle School	Closeout	Core Program	Addition / Renovation	CM@R	Joslin, Lesser + Associates Inc.	Tappe Associates, Inc.	Shawmut Design and Construction	RDK Engineers
201302850010	Stoughton	Helen Hansen Elementary	Closeout	Accelerated Repair	Windows / Doors	DBB	Hill International Company	Russo Barr Associates, Inc.	Lockheed Window Corporations	Building Enclosure Associates, LLC
201402850025	Stoughton	Joseph H Gibbons	Construction	Accelerated Repair	Roof, Windows / Doors	-	Atlantic Construction and Management, Inc.	CGKV Architects, Inc.	Gibson Roofs, Inc.	Building Enclosure Associates, LLC
201302850014	Stoughton	Joseph R Dawe Jr Elem	Closeout	Accelerated Repair	Windows / Doors	DBB	Hill International Company	Russo Barr Associates, Inc.	Lockheed Window Corporations	Building Enclosure Associates, LLC
201302850505	Stoughton	Stoughton High	Feasibility Study	Core Program	-	-	Compass Project Management, Inc.	Drumme Rosane Anderson, Inc.	-	-
201302850020	Stoughton	West Elementary	Closeout	Accelerated Repair	Roof	DBB	Hill International Company	Russo Barr Associates, Inc.	Titan Roofing, Inc.	Building Enclosure Associates, LLC
201502850020	Stoughton	West Elementary	OPM Selection	Accelerated Repair	Windows / Doors	-	-	-	-	-
200802870005	Sturbridge	Burgess Elementary School	Final Audit Approved	Core Program	Addition / Renovation	DBB	Lamoureux Pagano & Associates, Inc.	Drumme Rosane Anderson, Inc.	Fontaine Brothers, Inc.	Horizon Engineering Associates, LLP
201402880025	Sudbury	General John Nixon Elem	Building Complete	Accelerated Repair	Roof, Windows / Doors	-	Skanska USA Building, Inc	Baker/Wohl Architects, Inc.	Silktown Roofing	Building Enclosure Associates, LLC
200802900305	Sutton	Sutton Middle School	Building Complete	Core Program	Addition / Renovation	DBB	Strategic Building Solutions, LLC	Flansburgh Associates, Inc.	Brait Builders Corp.	RDK Engineers
201102910010	Swampscott	Hadley	Closeout	Core Program	New Construction	DBB	Hill International Company	Mount Vernon Group Architects, Inc.	-	-
201502930007	Taunton	Edmund Hatch Bennett	OPM Selection	Accelerated Repair	Roof, Windows / Doors	-	-	-	-	-
201502930042	Taunton	Joseph H Martin	OPM Selection	Accelerated Repair	Roof, Windows / Doors	-	-	-	-	-
201402930015	Taunton	Mulcahey Elementary School	OPM Selection	Core Program	-	-	-	-	-	-
200802950505	Tewksbury	Tewksbury Memorial High School	Closeout	Core Program	New Construction - Model School	DBB	HEERY	Symmes Maini & McKee Associates, Inc.	CTA Ventures	Sebesta Blomberg & Associates, Inc.
201408780605	Tri County	Tri County Reg Voc Tech	Construction	Accelerated Repair	Boiler	-	Strategic Building Solutions, LLC	Shekar & Associates, Inc.	-	Fitzmeyer & Tocci Associates, Inc.
201403010505	Tyngsborough	Tyngsborough High School	Construction	Accelerated Repair	Roof, Boiler	-	Municipal Building Consultants, Inc.	CSS Architects Incorporated	Greenwood Industries, Inc.	Strategic Building Solutions, LLC
200803040505	Uxbridge	Uxbridge High	Final Audit Approved	Core Program	New Construction	CM@R	Joslin, Lesser + Associates Inc.	Raymond Design Associates, Inc.	Shawmut Design and Construction	Turner Facilities Management Solutions
200907750305	Wachusett	Mountview Middle School	Construction	Core Program	New Construction	DBB	Gary Kaczmarek Town Employee	Lamoureux Pagano & Associates, Inc.	CTA Construction Co., Inc.	Fitzmeyer & Tocci Associates, Inc.
201003050310	Wakefield	Galvin Middle School	Closeout	Core Program	New Construction	CM@R	Joslin, Lesser + Associates Inc.	Tappe Associates, Inc.	Bond Brothers, Inc.	B2Q Associates, Inc.
201303070015	Walpole	Fisher	Final Audit Approved	Accelerated Repair	Roof	DBB	NETCO Construction Project Managers, Inc.	ICON architecture, inc.	Rockwell Roofing, Inc.	Gale Associates, Inc.
201403080505	Waltham	Waltham High School	OPM Selection	Core Program	-	-	-	-	-	-
201503100003	Wareham	John W. Decas Elementary School	OPM Selection	Accelerated Repair	Roof, Boiler	-	-	-	-	-
201303100505	Wareham	Wareham Senior High	Closeout	Accelerated Repair	Roof	DBB	Hill International Company	Tighe & Bond, Inc.	Capeway Roofing Systems, Inc.	Russo Barr Associates, Inc.
201503140305	Watertown	Watertown Middle	OPM Selection	Accelerated Repair	Windows / Doors	-	-	-	-	-
201403150005	Wayland	Claypit Hill School	Design Development	Accelerated Repair	Windows / Doors	-	Pinck & Co., Inc.	CGKV Architects, Inc.	-	Russo Barr Associates, Inc.
200903160015	Webster	Park Avenue Elementary School	Building Complete	Core Program	New Construction	DBB	Hill International Company	Dore & Whittier Architects, Inc.	CTA Construction Co., Inc.	Cannon Design
201403170305	Wellesley	Wellesley Middle	Construction	Accelerated Repair	Windows / Doors	-	Arcadis U.S., Inc.	CSS Architects Incorporated	Paul J. Rogan Co., Inc.	Gale Associates, Inc.
200803170505	Wellesley	Wellesley Senior School	Closeout	Core Program	New Construction	CM@R	-	Symmes Maini & McKee Associates, Inc.	-	Rist-Frost-Shumway Engineering, P.C.
201303180005	Wellfleet	Wellfleet Elementary	Closeout	Accelerated Repair	Roof	DBB	Architectural Consulting Group, LLC	CSS Architects Incorporated	DDC Construction Inc.	Russo Barr Associates, Inc.
201103220005G	West Boylston	Major Edwards Elementary	Closeout	Green Repair	Windows / Doors	DBB	URS Corporation	Reinhardt Associates, Inc.	-	Cannon Design



201503230005	West Bridgewater	Spring Street School	OPM Selection	Accelerated Repair	Roof	-	-	-	-	-
201003230505	West Bridgewater	West Bridgewater Middle-Senior High School	Building Complete	Core Program	New Construction	DBB	Strategic Building Solutions, LLC	Flansburgh Associates, Inc.	CTA Construction Co., Inc.	Cannon Design
200903320505	West Springfield	West Springfield High School	Building Complete	Core Program	New Construction - Model School	DBB	Strategic Building Solutions, LLC	Symmes Maini & McKee Associates, Inc.	Fontaine Brothers, Inc.	Turner Facilities Management Solutions
200903210305	Westborough	Gibbons Middle School	Design Development	Core Program	Repair	-	HEERY	Habeeb & Associates Architects, Inc.	-	BVH Integrated Services, P.C.
200903250020	Westfield	Abner Gibbs Elementary School	Construction	Core Program	New Construction - Model School	DBB	Skanska USA Building, Inc	Jones Whitsett Architects, Inc.	Fontaine Brothers, Inc.	Horizon Engineering Associates, LLP
201303260025	Westford	Col John Robinson	Construction	Accelerated Repair	Windows / Doors	DBB	Strategic Building Solutions, LLC	Gale Associates, Inc.	GTC Construction Management	CBI Consulting Inc.
201303260007	Westford	Day Elementary	Construction	Accelerated Repair	Windows / Doors	DBB	Strategic Building Solutions, LLC	Gale Associates, Inc.	J.J. Cardosi, Inc.	CBI Consulting Inc.
201303270005	Westhampton	Westhampton Elem School	Final Audit Approved	Accelerated Repair	Roof, Windows / Doors, Boiler	DBB	Atlantic Construction and Management, Inc.	CSS Architects Incorporated	Independent Roofing Co. Inc.	Building Enclosure Associates, LLC
200903300012	Weston	Field Elementary School	Building Complete	Core Program	New Construction	DBB	Compass Project Management, Inc.	Jonathan Levi Architects LLC	Colantonio, Inc.	Foreman Building Commissioning, LP
201403310305	Westport	Westport Middle	OPM Selection	Core Program	-	-	-	-	-	-
200803400005	Williamsburg	Anne T. Dunphy School	Building Complete	Core Program	Addition / Renovation	DBB	Arcadis U.S., Inc.	Drumme Rosane Anderson, Inc.	Enfield Builders, Inc.	B2Q Associates, Inc.
201203420060	Wilmington	North Intermediate	Closeout	Accelerated Repair	Windows / Doors	DBB	Diversified Project Management	-	-	CBI Consulting Inc.
200903420505	Wilmington	Wilmington High School	Building Complete	Core Program	New Construction	CM@R	Joslin, Lesser + Associates Inc.	Dore & Whittier Architects, Inc.	Gilbane Building Company	Symmes, Maini & McKee Associates
201003440505	Winchester	Winchester High School	Construction	Core Program	Addition / Renovation	CM@R	Skanska USA Building, Inc	Symmes Maini & McKee Associates, Inc.	Consigli Construction Company, Inc.	RDK Engineers
200803460505	Winthrop	Winthrop High School	Construction	Core Program	New Construction	CM@R	Skanska USA Building, Inc	HMFH Architects, Inc.	Gilbane Building Company	WSP USA
201203470060	Woburn	Wyman	Approved Project Vote Pending	Core Program	New Construction	-	Municipal Building Consultants, Inc.	DiNisco Design Partnership, Limited	-	Fitzemeyer & Tocci Associates, Inc.
201203480052	Worcester	Chandler Magnet	Closeout	Accelerated Repair	Windows / Doors	DBB	Tishman Construction Corporation of MA	Turowski2 Architecture, Inc.	J.J. Cardosi, Inc.	Russo Barr Associates, Inc.
201403480055	Worcester	Clark St Community	Construction	Accelerated Repair	Windows / Doors	-	Architectural Consulting Group, LLC	ICON architecture, inc.	J.J. Cardosi, Inc.	Russo Barr Associates, Inc.
201303480060	Worcester	Columbus Park	Building Complete	Accelerated Repair	Windows / Doors, Boiler	DBB	Architectural Consulting Group, LLC	The S/L/A/M Collaborative	Contractor's Network, Inc.	RDK Engineers   Russo Barr Associates, Inc.
201203488099	Worcester	Dr. James Caradonio Center	Closeout	Accelerated Repair	Boiler	DBB	Tishman Construction Corporation of MA	Turowski2 Architecture, Inc.	CAM HVAC & Construction, Inc.	RDK Engineers   Russo Barr Associates, Inc.
201503480090	Worcester	Flagg Street	OPM Selection	Accelerated Repair	Windows / Doors	-	-	-	-	-
201503480177	Worcester	Francis J McGrath Elem	OPM Selection	Accelerated Repair	Windows / Doors	-	-	-	-	-
201403480100	Worcester	Goddard Sch/Science Tech	Construction	Accelerated Repair	Windows / Doors	-	Architectural Consulting Group, LLC	ICON architecture, inc.	Lambrian Construction Corp.	Russo Barr Associates, Inc.
201503480115	Worcester	Grafton Street	OPM Selection	Accelerated Repair	Windows / Doors, Boiler	-	-	-	-	-
201203480140	Worcester	Jacob Hiatt Magnet	Closeout	Accelerated Repair	Boiler	DBB	Tishman Construction Corporation of MA	Turowski2 Architecture, Inc.	CAM HVAC & Construction, Inc.	RDK Engineers
201503480140	Worcester	Jacob Hiatt Magnet	OPM Selection	Accelerated Repair	Windows / Doors	-	-	-	-	-
201203480145	Worcester	Lake View	Closeout	Accelerated Repair	Windows / Doors	DBB	Tishman Construction Corporation of MA	Turowski2 Architecture, Inc.	J.J. Cardosi, Inc.	Russo Barr Associates, Inc.
201203480175	Worcester	May Street	Closeout	Accelerated Repair	Windows / Doors	DBB	Tishman Construction Corporation of MA	Turowski2 Architecture, Inc.	J.J. Cardosi, Inc.	Russo Barr Associates, Inc.
201203480200	Worcester	Nelson Place	Construction	Core Program	New Construction	CM@R	Tishman Construction Corporation of MA	Lamoureux Pagano & Associates, Inc.	Fontaine Brothers, Inc.	Bard, Rao + Athanas Consulting Engineers, LLC
201403480520	Worcester	South High Community	OPM Selection	Core Program	-	-	-	-	-	-
201303480230	Worcester	Tatnuck	Building Complete	Accelerated Repair	Windows / Doors	DBB	Architectural Consulting Group, LLC	The S/L/A/M Collaborative	GVW, Inc.	Russo Barr Associates, Inc.
201403480240	Worcester	Union Hill School	Construction	Accelerated Repair	Windows / Doors	-	Architectural Consulting Group, LLC	ICON architecture, inc.	J.J. Cardosi, Inc.	Russo Barr Associates, Inc.



201403480260	Worcester	West Tatnuck	Construction	Accelerated Repair	Windows / Doors		Architectural Consulting Group, LLC	ICON architecture, inc.	J.J. Cardosi, Inc.	Russo Barr Associates, Inc.
201303480225	Worcester	Worcester Arts Magnet Sch	Building Complete	Accelerated Repair	Windows / Doors	DBB	Architectural Consulting Group, LLC	The S/L/A/M Collaborative	GVW, Inc.	Russo Barr Associates, Inc.
201303480420	Worcester	Worcester East Middle	Building Complete	Accelerated Repair	Boiler	DBB	Architectural Consulting Group, LLC	The S/L/A/M Collaborative	Contractor's Network, Inc.	RDK Engineers
201503500003	Wrentham	Delaney	OPM Selection	Accelerated Repair	Roof		-	-	-	-

## 2015 ESTIMATED BID DATES


Note bid dates are Estimates ONLY. Please contact Districts for exact information.

Total Project Budget denotes total District costs and does not denote the basis of the MSBA Total Facilities Grant.

District	Enrollment	Project Budget	Start	Finish	Constructio Budget	Oct '14	Nov '14	Dec '14	Jan '15	Feb '15	Mar '15	Apr '15	May '15	Jun '15	Jul '15	Aug '15	Sep '15	Oct '15	Nov '15	Dec '15	Jan '16					
<b>Gloucester</b>	355	\$ 39.6	Mon 10/20/14	Thu 1/8/15	\$ 30.0	<b>Gloucester - West Parish ES</b> 10/20 (DBB) — 1/8 (CMR)																				
<b>Milford</b>	985	\$ 60.9	Mon 11/3/14	Tue 1/20/15	\$ 48.4	<b>Milford - Woodland ES</b> 11/3 (DBB) — 1/20 (CMR)																				
<b>Winthrop</b>	970	\$ 80.2	Wed 2/4/15	Thu 4/16/15	\$ 61.9	<b>Winthrop - Winthrop MS/HS</b> 2/4 (DBB) — 4/16 (CMR)																				
<b>Northborough</b>	270	\$ 25.5	Mon 2/9/15	Fri 5/1/15	\$ 18.2	<b>Northborough - Lincoln Street ES</b> 2/9 (DBB) — 5/1 (CMR)																				
<b>Georgetown</b>	720	\$ 7.8	Mon 2/9/15	Thu 3/12/15	\$ 5.9	<b>Georgetown - Georgetown MS/HS</b> 2/9 (DBB) — 3/12 (CMR)																				
<b>North Middlesex RSD</b>	870	\$ 89.0	Wed 4/8/15	Thu 5/21/15	\$ 68.8	<b>North Middlesex RSD - North Middlesex RHS</b> 4/8 (DBB) — 5/21 (CMR)																				
<b>Haverhill</b>	1005	\$ 61.5	Tue 4/14/15	Mon 5/18/15	\$ 50.0	<b>Haverhill - Caleb Dustin Hunking MS</b> 4/14 (DBB) — 5/18 (CMR)																				
<b>Plymouth</b>	1005	\$ 107.8	Thu 5/21/15	Wed 7/1/15	\$ 83.8	<b>Plymouth - Plymouth South HS</b> 5/21 (DBB) — 7/1 (CMR)																				
<b>Chelsea</b>	670	\$ 57.3	Wed 7/22/15	Fri 11/20/15	\$ 46.0	<b>Clark Avenue MS</b> 7/22 (DBB) — 11/20 (CMR)																				
<b>Abington</b>	1115	\$ 96.4	Tue 9/1/15	Tue 10/20/15	\$ 77.2	<b>Abington - Frolio Jr/ High</b> 9/1 (DBB) — 10/20 (CMR)																				
<b>New Bedford</b>	284	\$ 12.5	Wed 9/23/15	Mon 10/26/15	\$ 8.8	<b>New Bedford - Taylor at Sea Lab</b> 9/23 (DBB) — 10/26 (CMR)																				
<b>Boston</b>	355	\$ 73.5	Mon 9/28/15	Fri 12/18/15	\$ 60.2	<b>Boston - Henry Dearborn MS</b> 9/28 (DBB) — 12/18 (CMR)																				
<b>Holbrook</b>	985	\$ 103.0	Tue 9/29/15	Mon 11/23/15	\$ 79.8	<b>Holbrook - Holbrook Junior-Senior HS</b> 9/29 (DBB) — 11/23 (CMR)																				

Note: Budget values are in millions.  
 The project start date represents the Filed-Sub bid solicitation date, gray diamond Filed-Sub bid date, and the black diamond GC Bids / GMP Execution.

10/28/2015




## 2015 ESTIMATED BID DATES

Note bid dates are Estimates ONLY. Please contact Districts for exact information.


Total Project Budget denotes total District costs and does not denote the basis of the MSBA Total Facilities Grant.

District	Enrollment	Project Budget	Start	Finish	Constructio Budget	Oct '14	Nov '14	Dec '14	Jan '15	Feb '15	Mar '15	Apr '15	May '15	Jun '15	Jul '15	Aug '15	Sep '15	Oct '15	Nov '15	Dec '15	Jan '16		
						<b>Scituate</b>	970	\$ 72.9	Wed 10/28/15	Wed 12/2/15	\$ 61.9												
<b>Total</b>	<b>10559</b>	<b>\$ 887.9</b>			<b>\$ 700.9</b>																		



Note: Budget values are in millions.  
The project start date represents the Filed-Sub bid solicitation date, gray diamond Filed-Sub bid date, and the black diamond GC Bids / GMP Execution.

10/28/2015




**2016 ESTIMATED BID DATES**

Note bid dates are Estimates ONLY. Please contact Districts for exact information.

Total Project Budget denotes total District costs and does not denote the basis of the MSBA Total Facilities Grant.

District	Enrollment	Project Budget	Start	Finish	Constructio Budget	Notes	Nov '15	Dec '15	Jan '16	Feb '16	Mar '16	Apr '16	May '16	Jun '16	Jul '16	Aug '16	Sep '16	Oct '16	Nov '16	Dec '16	Jan '17	Feb '17	
							Worcester	600	\$ 58.2	Wed 12/16/15	Tue 4/5/16	\$ 46.5	GMP targeted: April 2016		12/16	Worcester - Nelson Place School			4/5				
Westborough	550	\$ 26.8	Wed 1/13/16	Thu 2/18/16	\$ 21.6	GMP targeted: February			Westborough - Sarah W. Gibbons MS			2/18											
Woburn	410	\$ 31.8	Wed 5/4/16	Thu 6/30/16	\$ 26.2	NTP targeted: July 2016							Woburn - Wyman Elementary School		6/10								
Brookline	830	\$ 113.4	Fri 5/13/16	Thu 6/23/16	\$ 92.2	GMP targeted: August							Brookline - Edward Devotion School		6/2								
New Bedford	400	\$ 35.6	Fri 5/20/16	Mon 6/27/16	\$ 35.1	NTP targeted: July 2016							New Bedford - John Hannigan Elementary School		6/16								
Pittsfield	920	\$ 116.1	Thu 6/16/16	Fri 7/29/16	\$ 97.7	GMP targeted: August							Pittsfield - Taconic High School		7/22								
Hopkinton	395	\$ 43.8	Tue 11/1/16	Tue 12/13/16	\$ 35.1	GMP targeted: December													Hopkinton - Center Elementary School				
Beverly	1395	\$ 106.8	Wed 11/2/16	Thu 2/2/17	\$ 90.1	GMP targeted: February														Beverly - Briscoe Middle School			
Provincetown	n/a	\$ 7.3	Tue 12/13/16	Thu 2/2/17	\$ 5.7	NTP targeted: Februry														Provincetown - Provincetown Schools K-8			
<b>Total</b>	<b>5500</b>	<b>\$ 539.8</b>			<b>\$ 403.7</b>																		

Note: Budget values are in millions.  
The project start date represents the Filed-Sub bid solicitation date, gray diamond Filed-Sub bid date, and the black diamond GC Bids / GMP Execution.



**Projects in Construction  
MSBA Grant Basis and Maximum Grant Amount  
Data Reported as of October 28, 2015**

Core Program and Waitlist Totals			\$2,824,936,196															*Includes Alternates	\$1,759,223,077
Project	Grade	Contractor	Total Construction Cost*	Projected Enrollment	PFA or Bid Data	Proposed Sq.Ft.	Construction Cost/Sq.Ft.	Building Cost	Building Cost/Sq.Ft.	Procurement Type	Construction Start Date	Substantial Completion	Schedule Variance (days)	Physical Progress	Change Orders	Change Orders %	Construction Status	Est Max Total Facilities Grant	
<b>CAPITAL PIPELINE PROJECTS IN CONSTRUCTION</b>																			
<b>Core Program Totals</b>			<b>\$2,822,960,113</b>																<b>\$1,753,760,132</b>
Assabet Valley Assabet Valley Voc H S	Vocational / Technical	CTA Construction Co., Inc.	\$46,764,740	1,000	Bid	367,565	\$127	\$41,523,764	\$113	Design/Bid/Build	01-Apr-13	23-Aug-15	0	98%	\$3,308,224	7.074%	The 10-phase project is nearly complete. Interior work remaining includes punch list, café lighting, kitchen testing, minor work in 2 shops, door hardware, security and some owner directed work. Exterior work includes punch list, site and landscaping. Entire project is scheduled to be complete in December, 2015.	\$28,790,301	
Athol-Royalston Riverbend	Elementary School	Fontaine Brothers, Inc.	\$35,191,363	545	Bid	95,726	\$368	\$21,101,359	\$220	Design/Bid/Build	08-Dec-14	14-Jun-16	0	35%	\$66,235	0.188%	Site utilities and roadway work are ongoing. Work to export excess site materials is continuing. Foundations and steel erection are underway.	\$26,011,620	
Berlin-Boylston Tahanto Reg High	Junior High School	CTA Construction Co., Inc.	\$32,162,000	560	Bid	126,100	\$255	\$24,629,999	\$195	Design/Bid/Build	10-May-11	01-Jul-13	0	99%	\$1,026,723	3.282%	The new school building is in service. The District is working to resolve issues associated with final change orders and rain screen repairs.	\$18,733,021	
Chicopee Chicopee Academy	Middle School	Fontaine Brothers, Inc.	\$30,776,990	825	Bid	176,425	\$174	\$21,508,080	\$122	Design/Bid/Build	01-Jul-14	11-Aug-15	0	100%	\$1,921,883	6.245%	The new school building opened on August 31, 2015. Punch list work is ongoing.	\$28,813,458	
Dracut Dracut Senior High	High School	CTA Construction Co., Inc.	\$45,900,000	1,160	Bid	226,844	\$202	\$38,377,028	\$169	Design/Bid/Build	27-Aug-12	29-Aug-14	0	98%	\$2,224,148	4.846%	The project team is working to resolve a site drainage issue. Punch list work is ongoing.	\$34,137,202	
East Bridgewater East Bridgewater High	High School	Fontaine Brothers, Inc.	\$65,409,000	950	Bid	213,544	\$306	\$47,684,117	\$223	Design/Bid/Build	10-Aug-11	25-Jun-13	0	99%	\$2,398,294	3.928%	One remaining item to be addressed to complete Commissioning.	\$40,164,584	
Franklin Franklin High	High School	Bacon-Agostini Construction Joint Venture	\$86,778,700	1,650	Bid	306,543	\$283	\$73,191,801	\$239	Design/Bid/Build	16-Oct-12	25-Jul-14	0	99%	\$1,108,661	1.278%	The new building and parking areas are complete. Construction of the synthetic field as well as landscaping and installation of the sport light poles are near completion.	\$54,558,408	
Georgetown Georgetown Middle/High	Junior High School	L.D. Russo, Inc.	\$5,861,090	720	Bid	128,670	\$46	\$3,543,961	\$28	Design/Bid/Build	15-Apr-15	21-Dec-15	0	91%	\$439,157	7.493%	Demolition and abatement are completed. Interior improvements in classrooms, corridors, and gymnasium continue. Roofing and waterproofing completed.	\$3,377,260	
Georgetown Penn Brook	Elementary School	Brait Builders Corp.	\$32,875,975	770	Bid	98,000	\$335	\$26,976,145	\$275	Design/Bid/Build	26-Sep-13	20-May-15	0	97%	\$3,707,559	11.277%	Site work is being worked around the new building. Commissioning and punch list work are ongoing. FF&E delivery and installation is complete. Demolition of existing building is underway.	\$18,864,538	
Greater Lawrence RVT Gr Lawrence Reg Voc Tech	Vocational / Technical	E. Amanti & Sons, Inc.	\$4,361,641	1,400	Bid	360,000	\$12	\$3,551,593	\$10	Design/Bid/Build	04-Jun-14	12-Dec-14	0	100%	\$260,493	5.972%	Project includes the replacement of cooling towers, chiller plant, HVAC pumps, HVAC controls, domestic hot water heaters, roof top mechanical units, and ventilation throughout the shop areas. The only work remaining is the chiller and cooling tower start up, commissioning, training and closeout. The project team is currently investigating a noise level issue with the above ceiling unit heaters. This will be resolved as part of the final commissioning process.	\$2,627,875	
Greater New Bedford Gr New Bedford Voc Tech	Vocational / Technical	Agostini Construction Co., Inc.	\$12,181,500	2,060	Bid	487,530	\$25	\$10,757,696	\$22	Design/Bid/Build	13-Sep-13	19-Dec-14	0	100%	\$1,273,194	10.452%	The building is complete and in service. Replacement of the cooling tower has been completed and is operational. Miscellaneous punch list work remaining.	\$11,573,133	
Hingham Hingham Middle School	Middle School	Brait Builders Corp.	\$48,436,000	1,020	Bid	176,385	\$275	\$41,227,552	\$234	Design/Bid/Build	07-Jun-12	01-May-14	0	99%	\$714,526	1.492%	Demolition of the existing building is complete. Landscaping and field installation is complete. Commissioning of the building has been completed.	\$23,653,420	
Marshfield Marshfield High	High School	Brait Builders Ventures	\$84,980,000	1,310	Bid	267,469	\$318	\$64,604,850	\$242	Design/Bid/Build	16-Aug-12	01-Jun-14	0	99%	\$2,162,935	2.718%	Remaining work consists of punch list items, system checkouts, and technology interfacing. Demolition of the old high school is complete, Phase III site restoration is proceeding.	\$46,550,599	
Monomoy Monomoy Regional High School	High School	Fontaine Brothers, Inc.	\$49,374,000	700	Bid	168,000	\$294	\$41,433,695	\$247	Design/Bid/Build	11-Feb-13	02-Sep-14	0	100%	\$1,058,937	2.206%	Remaining punch list items and landscaping items are being addressed.	\$27,654,507	
Newburyport Francis T Bresnahan Elem	Elementary School	CTA Construction Co., Inc.	\$28,190,000	660	PFA	112,517	\$251	\$20,841,757	\$185	Design/Bid/Build	14-Mar-13	19-Aug-14	0	99%	\$1,086,168	3.963%	Punch list work is remaining. The commissioning consultant completed the 10-month walk through for the final commissioning.	\$15,676,427	
North Adams Silvio O Conte Middle	Middle School	PDS Engineering and Construction, Inc.	\$21,877,496	310	Bid	78,119	\$280	\$17,831,491	\$228	Design/Bid/Build	28-Apr-14	16-Nov-15	0	95%	\$1,352,478	6.182%	Increased contractor workforce has improved progress towards the November 2, 2015 date for delivery and move in of furniture, and the Substantial Completion date. Site work has progressed with top course of paving installed, fencing, guardrail, landscaping installation underway, and playground equipment installed in front of the school. Inside the school, the third floor is progressing towards final cleaning, and the second and first floor mechanical installations are complete with finish work progressing. Elevator installation is complete and will be available to facilitate furniture move in.	\$20,508,670	
North Middlesex North Middlesex Reg	High School	CTA Construction Co., Inc.	\$68,829,726	870	PFA	180,530	\$381	\$44,223,062	\$245	Design/Bid/Build	25-May-15	14-Jul-17	0	0%	\$0	0.000%	Contractor has mobilized. Site work and foundations have begun.	\$39,373,276	
Northborough Lincoln Street	Elementary School	Brait Builders Corp.	\$18,450,000	270	PFA	52,920	\$349	\$14,514,966	\$274	Design/Bid/Build	27-Apr-15	01-Sep-16	0	25%	\$0	0.000%	Brick veneer and curtain wall assemblies are underway at the new gym addition. Painting and ceramic tile installations have commenced in the Phase 1 bathroom and renovation spaces.	\$9,925,570	
Peabody J Henry Higgins Middle	Middle School	Bacon-Agostini Construction Joint Venture	\$70,679,700	1,340	Bid	227,314	\$338	\$47,562,204	\$209	Design/Bid/Build	10-Mar-14	01-Jul-16	0	53%	(\$391,815)	-0.554%	Over 100 construction workers are on site daily and a strong effort has been made in the past month to close in the building before winter starts. In the academic wing, the curtain walls have been installed and the windows are nearly complete. Finish work, including final painting, has started on the third floor of the academic wing.	\$38,652,137	
Plymouth Plymouth South High	High School	Agostini Construction Co., Inc.	\$88,163,542	1,005	PFA	248,081	\$355	\$60,612,309	\$244	Design/Bid/Build	06-Jul-15	05-May-17	0	2%	\$0	0.000%	Groundbreaking took place on September 24, 2015. Excavation and foundation work remain ongoing.	\$46,241,232	
Revere Staff Sergeant James J. Hill School	Elementary School	CTA Construction Co., Inc.	\$33,897,336	690	Bid	103,650	\$327	\$24,309,968	\$235	Design/Bid/Build	25-Mar-14	17-Aug-15	0	90%	\$1,050,055	3.098%	The contractor is in the process of completing work to close out the project including punch list items.	\$28,099,048	
Somerset-Berkley Somerset-Berkley High	High School	Bacon-Agostini Construction Joint Venture	\$69,407,000	1,000	Bid	222,826	\$311	\$52,553,676	\$236	Design/Bid/Build	16-Jul-12	20-Jun-14	0	98%	\$828,170	1.258%	Phase III work continues on site development and removal of demolition debris. Punch list and warranty items continue to be addressed.	\$46,722,150	
South Hadley Plains Elementary	Elementary School	Fontaine Brothers, Inc.	\$21,391,144	270	Bid	63,377	\$338	\$17,380,907	\$274	Design/Bid/Build	08-May-14	04-Sep-15	0	92%	\$1,128,992	5.278%	The school opened on September 8, 2015. Punch list items remain within the building. Site work and demolition of the existing building remain ongoing.	\$13,676,432	
Southwick-Tolland Powder Mill	Middle School	PDS Engineering and Construction, Inc.	\$13,556,194	545	Bid	95,775	\$142	\$11,289,029	\$118	Design/Bid/Build	07-Jun-13	24-Aug-15	0	99%	\$945,979	6.978%	All five phases are complete. Punch list work is ongoing.	\$8,437,002	
Southwick-Tolland Southwick-Tolland Regional High	High School	Fontaine Brothers, Inc.	\$25,307,990	790	Bid	165,995	\$152	\$19,838,420	\$120	Design/Bid/Build	05-Aug-13	03-Sep-15	0	99%	\$2,030,077	8.191%	This is a 5-phase project. All Phases are complete but for Phase 4A (Alternate Gym) where the wall padding has not yet been installed. Punch list work is ongoing.	\$19,572,669	
Southwick-Tolland Woodland Elementary	Elementary School	PDS Engineering and Construction, Inc.	\$7,172,052	400	Bid	67,800	\$106	\$6,077,790	\$90	Design/Bid/Build	07-Jun-13	24-Aug-15	0	99%	\$739,980	10.318%	All four phases are complete. Punch list work is ongoing.	\$4,620,410	
Sutton Sutton Middle School	Junior High School	Brait Builders Corp.	\$41,230,800	840	PFA	179,040	\$230	\$32,998,403	\$184	Design/Bid/Build	01-Jul-11	05-Mar-15	0	99%	\$1,754,737	4.368%	Remaining punch list items are being addressed.	\$26,120,512	
Wachusett Mountview Middle	Middle School	CTA Construction Co., Inc.	\$43,122,257	800	Bid	126,200	\$342	\$28,959,805	\$229	Design/Bid/Build	21-May-14	19-Apr-16	0	60%	\$429,164	0.995%	Interior finish work is most advanced on the academic building third floor which is ready for final above ceiling inspection followed by ceiling installation. Floor installation is pending concrete moisture test results. On the second and first floors, wall tile and mechanical and electrical finish work are underway. Gym/Auditorium and Cafeteria area drywall installation is nearing completion. The rooftop HVAC units have been installed along with the rooftop solar panel arrays and wiring. Boiler startup is pending and the boiler will be used for temporary heat during the upcoming winter. Site work continues with curbing installation complete, sidewalk installations prepared for concrete placement, and landscape plantings delivered and installed.	\$24,279,591	
Webster Park Avenue Elementary	Elementary School	CTA Construction Co., Inc.	\$32,370,001	720	Bid	109,597	\$295	\$24,190,915	\$221	Design/Bid/Build	08-Jul-13	06-Feb-15	0	99%	\$949,062	2.999%	Remaining work to be completed includes miscellaneous punch list items.	\$28,102,666	
West Bridgewater West Bridgewater Jr-Sr	Junior High School	CTA Construction Co., Inc.	\$46,267,000	625	Bid	141,250	\$328	\$34,404,274	\$244	Design/Bid/Build	01-Oct-13	09-Jul-15	0	88%	\$307,797	0.678%	Interior finishes are being completed and final cleaning has started. Work continues on the punch list as well as completion of sound, security and fire alarm systems. Demolition and abatement of the existing school is underway.	\$26,385,058	



**Projects in Construction  
MSBA Grant Basis and Maximum Grant Amount  
Data Reported as of October 28, 2015**

Core Program and Waitlist Totals			\$2,824,936,196														*Includes Alternates	\$1,759,223,077
Project	Grade	Contractor	Total Construction Cost*	Projected Enrollment	PFA or Bid Data	Proposed Sq.Ft.	Construction Cost/Sq.Ft.	Building Cost	Building Cost/Sq.Ft.	Procurement Type	Construction Start Date	Substantial Completion	Schedule Variance (days)	Physical Progress	Change Orders	Change Orders %	Construction Status	Est Max Total Facilities Grant
<b>CAPITAL PIPELINE PROJECTS IN CONSTRUCTION</b>																		
<b>Core Program Totals</b>			<b>\$2,822,960,113</b>															<b>\$1,753,760,132</b>
West Springfield West Springfield High	High School	Fontaine Brothers, Inc.	\$85,006,020	1,270	Bid	257,525	\$330	\$56,875,181	\$221	Design/Bid/Build	22-Nov-11	31-Dec-13	0	99%	\$3,050,109	4.329%	Warranty items are being tracked and resolved. Remaining change order work is being completed.	\$60,722,795
Westfield Abner Gibbs	Elementary School	Fontaine Brothers, Inc.	\$25,578,000	600	Bid	95,573	\$268	\$21,444,000	\$224	Design/Bid/Build	24-Aug-12	01-Jun-16	0	7%	\$0	0.000%	Work stoppage due to preliminary injunction based upon project site status as Article 97 "Protected Land". Preliminary Injunction vacated but city awaiting National Park Service approval for use of site. The General Contractor has demobilized from the site. The project team is working on closing out the General Contractor's contract.	\$21,281,639
Weston Field Elem School	Elementary School	Colantonio, Inc.	\$24,537,966	355	Bid	65,390	\$375	\$19,872,289	\$304	Design/Bid/Build	21-Dec-12	04-Aug-14	0	100%	\$2,222,124	9.056%	Remaining punch list items consist of mostly site work.	\$8,004,886
Williamsburg Anne T Dunphy	Elementary School	Enfield Builders, Inc.	\$8,990,457	170	Bid	37,859	\$237	\$7,625,327	\$201	Design/Bid/Build	05-Apr-13	29-Aug-14	0	100%	\$683,518	7.603%	Miscellaneous punch list work items remain to be completed.	\$6,808,088
Auburn Auburn Middle	Middle School	Fontaine Brothers, Inc.	\$36,412,806	560	Bid	100,395	\$363	\$23,350,958	\$233	CM-at-Risk	27-Feb-14	07-Jul-15	0	99%	\$139,506	0.393%	The project is complete except for minor punch list and seasonal commissioning to be completed in the Spring of 2016.	\$19,761,870
Ayer-Shirley Ayer-Shirley Regional Middle/High School	High School	Consigli Construction Company, Inc.	\$44,516,576	495	Bid	144,072	\$309	\$32,082,505	\$223	CM-at-Risk	19-Feb-13	31-Aug-15	0	96%	\$1,110,017	2.501%	This is a 6-phase Addition/Renovation project. Two general classroom sections (section C) were completed on time during the summer and turned over to the District on September 2, 2014. Phases 1a, 1b, 2a, 2b, 3a and 3c are complete and only minor punch list work remains. Phase 3b was done during the Summer of 2015 and included the new cafeteria, new front entry, all work in building F and site work. Phase 3b was completed on August 26, 2015. The project reached substantial completion on September 1, 2015	\$34,704,031
Boston Dearborn	Middle School	Gilbane Building Company	\$60,245,740	600	PFA	128,304	\$470	\$36,655,002	\$286	CM-at-Risk	8-Sep-15	31-Jan-18	0	0%	\$0	0	The contractor is mobilizing to the site to start construction.	\$36,615,390
Chelsea Clark Avenue School	Middle School	W. T. Rich Company Inc.	\$46,046,367	670	PFA	115,235	\$400	\$29,311,076	\$254	CM-at-Risk	23-Feb-15	29-Jun-18	0	6%	\$0	0.000%	Interior abatement work and building demolition have been completed (Phase 1).	\$36,093,628
Concord-Carlisle Concord Carlisle High	High School	Turner Construction Company	\$76,143,704	1,225	Bid	219,871	\$346	\$53,607,000	\$244	CM-at-Risk	20-Feb-13	13-Feb-15	0	96%	\$3,003,691	3.945%	All building systems have been successfully started up and commissioned. Demolition, site work and close out are ongoing. Although some time was lost due to unforeseen abatement scope, the project remains on schedule overall.	\$26,795,748
Duxbury Duxbury High	Junior High School	Dimeo Construction Company	\$105,475,520	1,735	Bid	322,105	\$327	\$73,368,123	\$228	CM-at-Risk	12-Sep-12	09-Jun-14	0	99%	\$6,143,967	6.170%	Site and landscaping work continues on both former school sites. Site work around the new building is nearly complete.	\$48,141,830
Essex Agr Tech Essex Agr and Tech Inst	Vocational / Technical	Gilbane Building Company	\$110,217,451	1,440	Bid	337,000	\$327	\$79,334,889	\$235	CM-at-Risk	07-May-12	27-Aug-14	0	99%	\$3,018,720	2.739%	Punch list work is ongoing and is expected to be complete by the end of the calendar year.	\$72,471,233
Gloucester West Parish	Elementary School	W. T. Rich Company Inc.	\$29,995,466	355	PFA	65,679	\$457	\$18,591,872	\$283	CM-at-Risk	07-Jul-14	12-May-16	0	64%	\$115,992	0.387%	Academic Wing: Classroom/hallway walls painting and ceiling grid installation are ongoing. Tile installation commenced on Levels 3 and 2 (working top down). Gym/Cafe/Arts Wing: Interior framing is ongoing. Curtain wall and KaWall installations are ongoing. Mechanical/Electrical/Plumbing work is ongoing. Art Room- special concrete slab is complete. Site: Play field drainage and curbs commenced installation. Bio-swale work is ongoing. Binder course pavement has been installed around site.	\$14,732,645
Greater Lowell Voc Tec Gr Lowell Reg Voc Tech	Vocational / Technical	Consigli Construction Company, Inc.	\$52,472,010	1,990	Bid	505,766	\$104	\$38,997,643	\$77	CM-at-Risk	04-Nov-13	31-Aug-15	0	95%	\$2,661,724	5.073%	The only work that remains on this 3-phase projects is punch list items, some site work and Commissioning. Commissioning is over 70% complete. All work is scheduled to be completed by the end of November 2015.	\$45,839,013
Greenfield Greenfield High	High School	Shawmut Design and Construction	\$53,507,787	585	Bid	160,650	\$333	\$37,812,150	\$235	CM-at-Risk	27-Mar-13	31-Oct-15	0	95%	\$926,377	1.731%	The new school building and renovated auditorium are in service. Final site work is scheduled for completion in late October 2015 and the final acceptance inspection is scheduled for the Spring of 2016.	\$42,146,257
Haverhill Caleb Dustin Hunking	Middle School	Shawmut Design and Construction	\$58,998,100	1,005	PFA	147,996	\$399	\$34,446,742	\$233	CM-at-Risk	20-Apr-15	30-Dec-16	0	19%	\$0	0.000%	Structural steel framing is nearly complete. Concrete slabs for the 3-story wing are complete. Spray-on fireproofing and plumbing/electrical rough-ins are ongoing. Exterior light gauge metal framing is underway in the 3-story wing. Site work is ongoing including earthwork, storm water detention systems, bus exit and utilities.	\$39,639,497
Holbrook Holbrook Jr Sr High	High School	Consigli Construction Company, Inc.	\$80,240,040	1,095	PFA	217,353	\$369	\$50,611,105	\$233	CM-at-Risk	24-Jun-15	05-Jun-17	0	5%	\$62,642	0.079%	Excavation for foundations is ongoing for Building A and foundation placement is ongoing for Building B.	\$54,644,960
Lunenburg Lunenburg High	Junior High School	Shawmut Design and Construction	\$59,570,728	820	Bid	169,018	\$352	\$39,057,924	\$231	CM-at-Risk	15-Aug-14	25-Mar-16	0	60%	\$137,977	0.232%	Slab-on-grade installation is complete. Air vapor barrier and spray fireproofing installations are underway throughout the building. Gym, auditorium and locker room area masonry installations are complete. Rough mechanical, electrical, plumbing and interior framing work is also underway. Flat roof installation is nearing completion.	\$34,122,826
Lynn Thurgood Marshall Mid	Middle School	Walsh Brothers, Inc.	\$67,725,244	1,100	PFA	181,847	\$372	\$49,913,764	\$274	CM-at-Risk	27-Jun-14	06-Jun-16	0	72%	\$0	0.000%	Site work includes front entrance/side walk preparation and utility preparation/pole relocation. All roof work is complete. VCT tile, mechanical work, and finish work are underway in Building A with drywall, painting, and ceiling work underway in Building B and exterior/interior CMU work and skylight installations underway in Building C. Elevator installation is complete.	\$49,690,902
Milford Woodland	Elementary School	Shawmut Design and Construction	\$48,381,844	985	Bid	132,539	\$365	\$31,853,445	\$240	CM-at-Risk	01-Apr-15	28-Jul-16	0	29%	\$238,089	0.492%	Gym Wing: Exterior brick and interior CMU are complete. Interior framing and drywall are ongoing. Academic Wing: Exterior framing, brick, and roof installations are complete. Interior framing and drywall are ongoing. Admin/Cafe/Arts Wing: The installation of the main roof is complete. Concrete slabs-on-deck and grade have been placed. Exterior sheathing and exterior/interior framing are ongoing. Mechanical/Electrical/Plumbing: Underground installation of utilities has been completed in all buildings. Rough-in work is ongoing in all buildings. Site: Installation of new gas and electrical services have been completed. The west subsurface detention system has been completed. Asphalt base pavement and curbs at parking lots are complete.	\$27,418,234
Newburyport Rupert A Nock Middle	Middle School	Gilbane Building Company	\$20,877,414	845	PFA	161,500	\$129	\$14,924,391	\$92	CM-at-Risk	18-Mar-13	10-Oct-14	0	99%	\$2,572,334	12.321%	Miscellaneous punch list items remain to be completed. The commissioning consultant completed the 10-month walk through for the final commissioning.	\$12,785,667
Newton A E Angier	Elementary School	W. T. Rich Company Inc.	\$30,179,957	465	Bid	74,960	\$403	\$16,758,548	\$224	CM-at-Risk	22-Aug-14	18-Dec-15	0	74%	\$12,733	0.049%	Mechanical system rough-ins are installed. Preparation for landscaping is ongoing. Steel and light bollards are being installed. Generator is installed. Rough grading, sub-drainage and stone veneer are ongoing. Masonry is nearly complete with a small section to be completed. Window and curtain wall system installations are ongoing. 3rd and 2nd floor lighting are ongoing. Specialties and finish millwork are ongoing. Elevator installation has commenced. Bathroom finishes and fixtures are being installed. Wall tile and flooring has started in corridors and classrooms as well as painting in the upper floors. Gym painting and MEPs are ongoing. Kitchen tile has started with equipment installation to follow. 1st floor ceiling grid and trim started.	\$10,687,077
North Reading North Reading High	Junior High School	Gilbane Building Company	\$101,328,353	1,370	Bid	267,939	\$378	\$66,726,592	\$249	CM-at-Risk	01-May-12	21-Aug-15	0	97%	\$3,337,425	3.294%	Delivery of furniture is ongoing. Landscaping and final paving are underway. Local inspections have been performed and deficiencies identified for correction. Abatement and demolition of the old high school is proceeding.	\$47,071,882
Norton Norton High	High School	W. T. Rich Company Inc.	\$27,023,541	700	Bid	162,000	\$167	\$20,590,559	\$127	CM-at-Risk	12-Mar-12	31-Jan-14	0	100%	\$136,653	0.513%	Roof top unit punch list issue is ongoing. The closeout process including the final change orders are pending resolution of a roof top unit noise and vibration issue.	\$20,634,829
Southern Worcester Cty VT Bay Path Reg Voc Tech H S	Vocational / Technical	Consigli Construction Company, Inc.	\$57,024,455	1,110	Bid	249,521	\$229	\$41,468,049	\$166	CM-at-Risk	02-Aug-13	01-Sep-15	0	96%	\$3,592,817	6.343%	Project just completed phase 10 of a 10 phase project. Interior scope that remains includes punch list for phase 10, door hardware, minor glazing, minor work to complete security upgrades, HVAC balancing and some miscellaneous metal work. Exterior work that remains includes punch list for site, landscaping and some sealant in joints. Additional commissioning is also required.	\$44,420,530
Springfield Elias Brookings	Elementary School	Morganti/Aquadro & Cerruti	\$22,733,394	320	Bid	64,800	\$351	\$18,337,328	\$283	CM-at-Risk	01-Jul-13	12-Feb-15	0	100%	(\$243,295)	-1.070%	Remaining punch list and warranty issues are being addressed.	\$25,563,992
Wilmington Wilmington High	High School	Gilbane Building Company	\$67,558,835	960	Bid	192,443	\$351	\$48,060,314	\$250	CM-at-Risk	30-Apr-13	12-Feb-15	0	96%	\$2,566,712	3.972%	Punch list and warranty items are being completed.	\$35,674,893

**Projects in Construction  
MSBA Grant Basis and Maximum Grant Amount  
Data Reported as of October 28, 2015**

Core Program and Waitlist Totals			\$2,824,936,196															*Includes Alternates	\$1,759,223,077
Project	Grade	Contractor	Total Construction Cost*	Projected Enrollment	PFA or Bid Data	Proposed Sq.Ft.	Construction Cost/Sq.Ft.	Building Cost	Building Cost/Sq.Ft.	Procurement Type	Construction Start Date	Substantial Completion	Schedule Variance (days)	Physical Progress	Change Orders	Change Orders %	Construction Status	Est Max Total Facilities Grant	
<b>CAPITAL PIPELINE PROJECTS IN CONSTRUCTION</b>																			
<b>Core Program Totals</b>			<b>\$2,822,960,113</b>																<b>\$1,753,760,132</b>
Winchester High School	High School	Consigli Construction Company, Inc.	\$101,118,622	1,370	PFA	278,925	\$363	\$60,656,324	\$217	CM-at-Risk	23-Apr-14	31-Aug-17	0	54%	\$1,264,651	1.253%	Phase 1 construction of a new main entrance, administration offices, music wing, kitchen, cafeteria, and media center is complete and in service. Completion of renovations to the Auditorium has been delayed from September 1, 2015 to September 1, 2016. Phase 2 renovations are in process and are scheduled for completion in August 2016. Phase 3 renovations are scheduled for completion in August 2017.	\$42,106,263	
Winthrop Winthrop Sr High	Junior High School	Gilbane Building Company	\$63,542,179	970	PFA	187,917	\$338	\$42,616,843	\$227	CM-at-Risk	01-Jul-14	30-Jun-16	0	61%	\$93,419	0.147%	Structural work has been completed in most of the building. Roofing, framing, fireproofing and window installations are complete. The exterior façade is complete. Interior finish work is in progress.	\$39,559,238	
Worcester Nelson Place	Elementary School	Fontaine Brothers, Inc.	\$46,546,300	600	PFA	111,256	\$418	\$29,503,564	\$265	CM-at-Risk	01-Jul-15	01-Jun-17	0	10%	\$0	0.000%	Removal of soil is ongoing from the Nelson Place site to the Greenwood Street landfill site. Blasting of ledge is also ongoing.	\$33,717,513	
<b>Waitlist Totals</b>			<b>\$1,976,083</b>				<b>\$4</b>		<b>\$4</b>										<b>\$5,462,945</b>
New Bedford New Bedford High	High School	Sparks Company, Inc.	\$1,976,083	4,000	Bid	454,028	\$4	\$1,669,516	\$4	Design/Bid/Build	27-Aug-14	06-Mar-15	0	99%	\$154,139	7.800%	Miscellaneous punch list items remain to be completed.	\$5,462,945	
